


Weekly Construction Progress Report

Work Period: 11/15/21 thru 11/19/21

**Northrop Grumman
Operable Unit 3
RW-21 Project Area
Bldg. 109 Treatment System
Bethpage, New York**

Project Work Performed:

- Performed Community Air Monitoring with no sustained exceedances.
- Performed noise monitoring with no sustained exceedances.
- Began installing building trench drains.
- Continued installing rebar for building floor slab.
- Completed installing forms and rebar for retaining wall on the west side of the site.
- Completed concrete pours for retaining wall on the west side of the site.
- Completed backfilling retaining wall on the west side of the site.
- Began installing building sub-grade conduits.
- Successfully pressure tested previously installed sections of 8-inch fire protection and 3-inch potable water pipes.

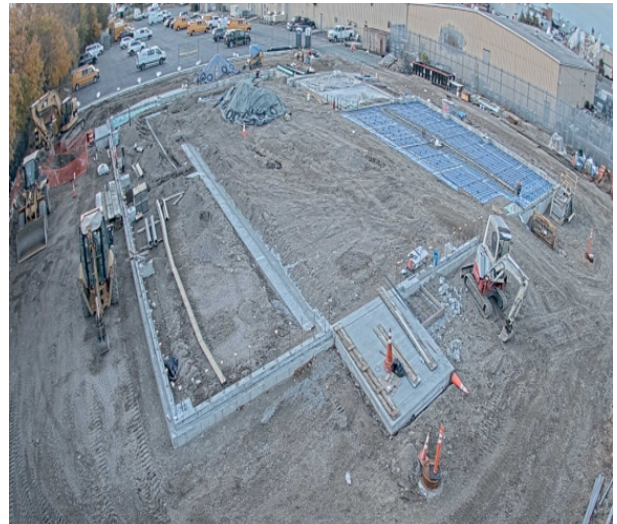

Aerial View from East Side of Site

Work Projected Next Period:

- Continue Community Air Monitoring.
- Continue noise monitoring.
- Continue installing building trench drains.
- Continue installing rebar for building floor slab.
- Continue pouring concrete for building floor slab.
- Continue installing building sub-grade conduits.
- Begin installing building grounding grid.



Rebar Installed in Building Northeast Corner

Site Visitors:

- None.



Retaining Wall on Site West Side with Future Conduit Openings
