

Weekly Construction Progress Report

Work Period: 3/14/22 thru 3/18/22

**Northrop Grumman
Operable Unit 3
RW-21 Project Area
Bldg. 109 Treatment System
Bethpage, New York**

Project Work Performed:

- Completed installing insulation and brick on building exterior walls.
- Completed installing roof insulation and panels.
- Completed installing precast concrete roof planks on interior rooms.
- Completed installing precast concrete caps on top of building exterior brick walls.
- Completed installing plumbing rough-in for bathroom.
- Continued installing building HVAC system.
- Received clarifier, clarifier tank and platform.
- Received two dewatering volutes.
- Began washing previously installed brick walls.
- Continued site cleanup following masonry work.




Aerial View from East Side of Site

Work Projected Next Period:

- Begin installing insulated building wall panels.
- Continue installing building HVAC system.
- Continue receiving equipment deliveries.
- Complete washing previously installed brick walls.
- Complete site cleanup following masonry work.



Building Metal Roof Installation

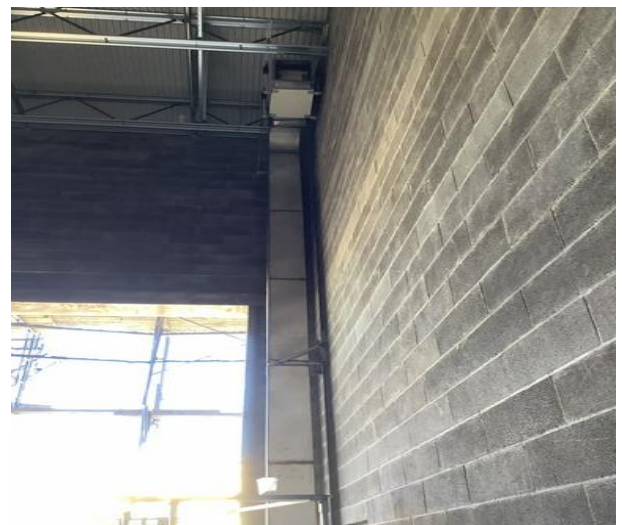

HVAC Ductwork in Chemical Rooms

Site Visitors:

- None.
