

TRANSMITTAL SLIP

TO


Heather Bishop

FROM

Walter Parish R-1

RE:

Liberty Industrial Farmingdale



Attached is a copy of the fuel oil tank removal report from NCOH who attended the work.

There was 600-700 yds³ of contaminated soil that was excavated & needs to be disposed of.

FOR ACTION AS INDICATED:

- ☐ Please Handle
- ☐ Prepare Reply
- ☐ Prepare Reply for _____
Signature
- ☒ Information
- ☐ Approval
- ☐ Prepare final/draft in _____ Copies

- ☐ Comments
- ☐ Signature
- ☐ File
- ☐ Return to me
- ☐ _____
- ☐ _____

Field Investigation
Article XI Facility
Nassau County Department of Health



- ☐ Initial System Test ☒ Tank Removal
☐ Tank Only ☐ Installation
☐ System Retest ☐ Abandonment
☐ Periodic Year ☐ Well Installed

Date of Job 7/20/05 8/3/05 Time 11/4/05

Facility ID# 58767

Date Received 1/14/05 Time

Confirmation # 214105 R02 + 215105 R01
0261105 R01

Contractor ERM - Rick - consultant (Rick)

DEC Spill #

Telephone # 631-756-8933 cell 516 903-7325

Establishment Name former Liberty Industrial Site

Address 55 Motor Avenue (North Side)


Town Farmingdale

Telephone #

No. Tanks 2 10' x 31' oil 10' x 34'

Type of Test

Tank #	#1	#2		
Size	15K	20K		
Product	#6F10	#4F10		
Test:				
System Test				
Tank Test				
Leak Rate				
Pass/Fail				
Fee				
Fee Paid				
Retest Needed				
Removal:				
Visible Holes	no	no		
# of Holes	none	none		
Size	15K	20K		
Location				
Photo	no	no		

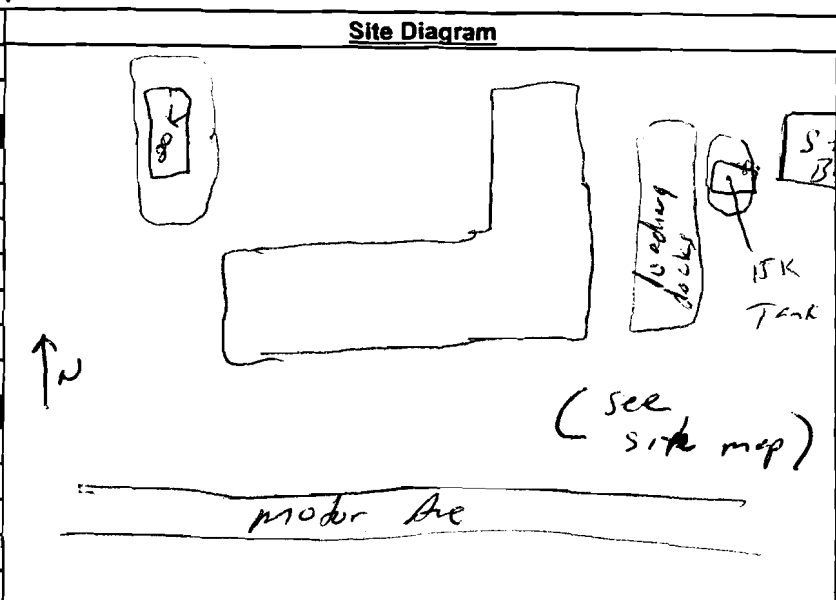

Excavation Clean Contaminated Soil Free Floating Product

Soil Removed Amount yds³

Installation Y N Gas Tank Size Approved plans: Yes No N/A


Notes: EPA - Lorenzo Thantia Project Coordinator - Region 2 290 Broadway
Record of Decision criteria
20K Tank removed - no holes not leaking
NY, NY 10001

Inspector A. Donohue Supervisor DEC DEC DEC DEC (see continuation sheets)

Employee Number 802 AD Date 8/1/05

- 1-Piping
3-Fitting
2-Tank
4-Other



Field Investigation.doc




- ☐ Continued on Reverse Side
☒ Computer Entry
☒ Data Book Entry

631 444-0241

Walter Parrish

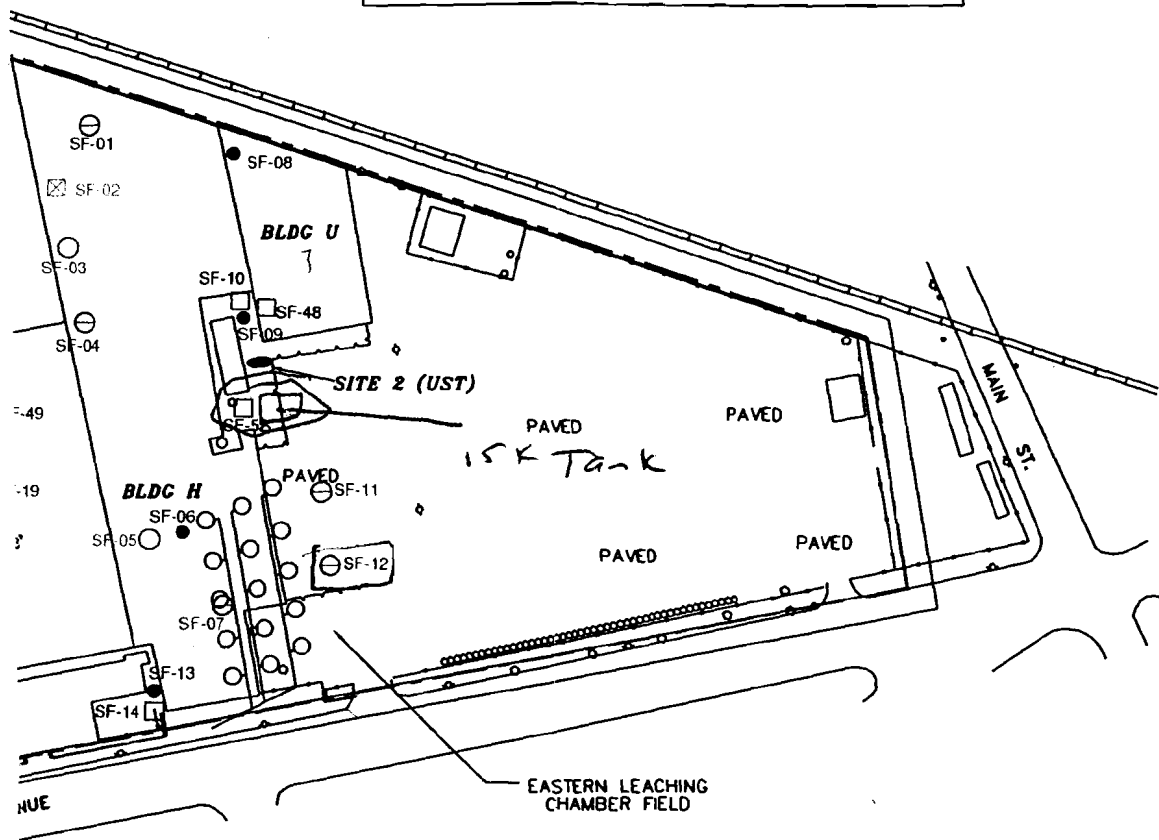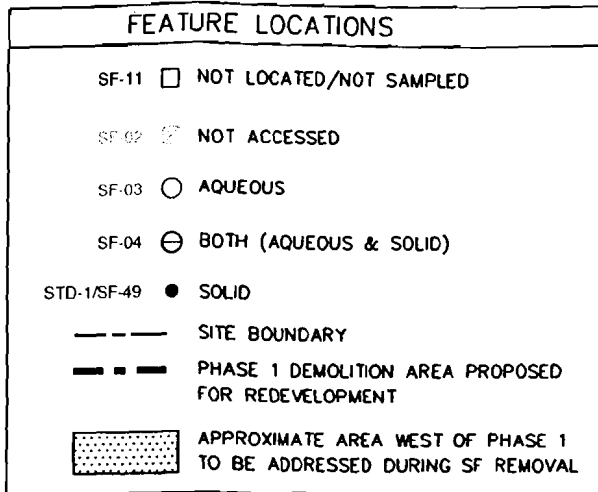

LDWG. DATED NOVEMBER 11, 1993 BY ROY F. WESTO OF NEW YORK, INC.
 4Y PRODUCED IN 1990 AND TOPOGRAPHIC
 FOR ROY F. WESTON OF NEW YORK, INC.



		DRAWN	DATE	SF LOCATIONS			SHEET NO.
		DESIGN ENGINEER					
		PROJECT ENGINEER					
		PROJECT MANAGER					
APPROVED		DATE	11/5/02	REVISION DATE			
APPROVED		SCALE	GRAPHIC	FILE NAME	FFB0200021		

NTAL

Owner or Agent: Liberty Dred Site

Inspector

ation Sheet
sau County Health Department

Address 55 Motor Ave
Farmersdale

802/AB

DATE	COMMENTS
8/13/05 Am	Called Walker at (DEC) 631-444-0241. He will get back to me concerning methods and if DEC to cover removals
	- RICK at ERM said today will only be removing E. 15K tank. Also removing 20K tank ^{from} site. They are not ready to do testing at this time. Looking for later in the week. They have removed more soil that was contaminated. They have to contact property owner and give him proposal for new work.
11:10 Am	I called Rick at ERM (on site). He will sample both excavations 5 samples each for methods 8270 & 8021
	- If a tank has w/o in it. Also sample for RCRA metals.
	- He will remove 15 K tank + leave on site
	- Both holes to be left open
	- NCHD will be contacted when samples to be taken
8/14/05 Am	Spoke to Dave Raymond at DEC. Stated Contractor can excavate Contam. Soil at De End Point Sampling. (see method above)
	- Reports to be sent to DEC (Dave Raymond) and ERM. Contact Dave Raymond after 8/15/05.

Farming date

COMMENTS

Side Inspection. 15 K Tank removed. no hole in tank. Tank cleaned to dry. Excavation open.

- Rick at ERM given permission to remove tank. Samples of both excavations have not yet been taken

- Rick to notify NCHD when he wants to sample


- DEC to be notified of all sample results.

- NCHD to be on site when sampling takes place

Soil Sampling

- 600 to 675 yds contam. soil stockpiled
- 2 sides, soil sampling done

West Site

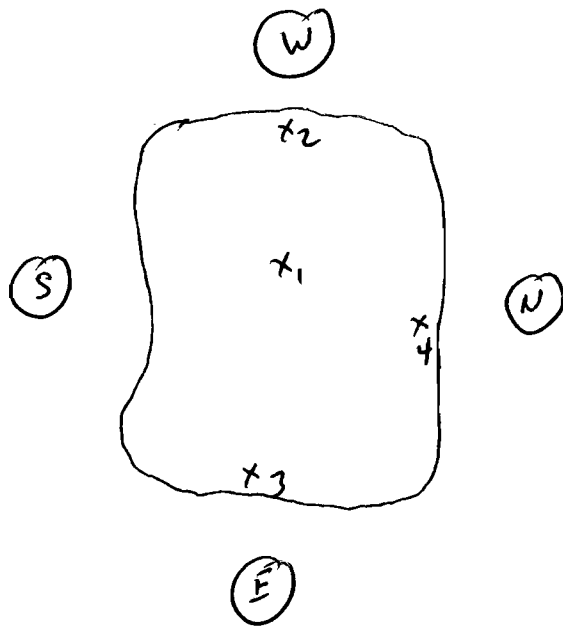


ERM #	NCHD #	ERM PID	NCHD PID
PRCB	x1	.2ppm	00
PRCW	x2	00	00
PRCE	x3	00	00
PRCN	x4	00	00
*			

* - S. Side not accessible

- excavation approx 20' deep

East Side

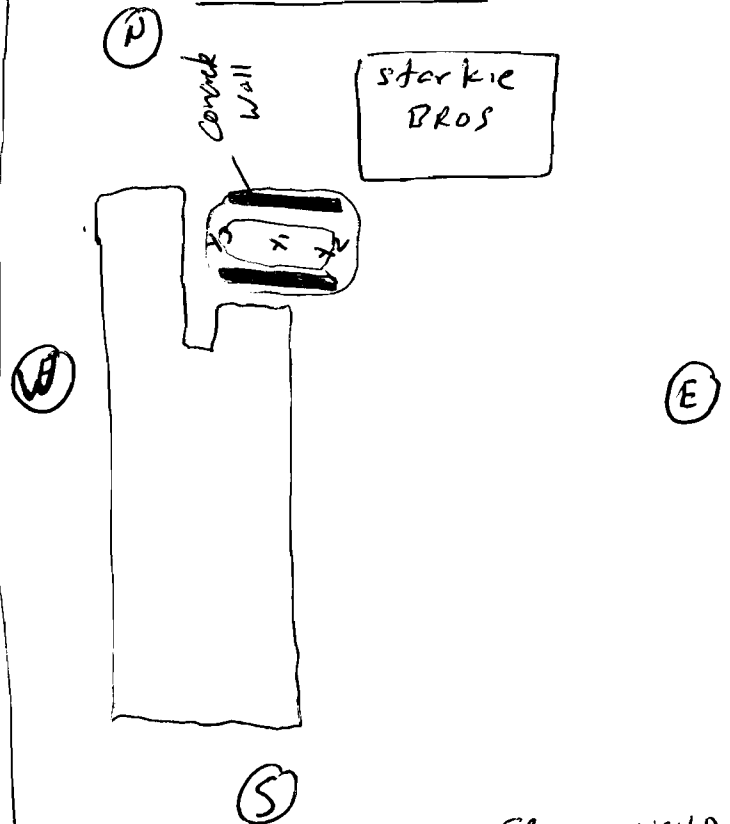

ERM #	NCHD #	ERM PID ppm	NCHD PID ppm
PRCB	y1	00	00
PRCE	y2	00	00
PRCW	y3	00	00

- N. + S. side of excavation limited by concrete wall

shelton- Rick from ERM called. NCHD gave permission to close 2 excavations on 2 tanks that were removed.
- Tank Contractor (ERM) to send end point sample results
