

New York State Department of Environmental Conservation
Division of Environmental Remediation
Central Office



DAILY INSPECTION REPORT

Site Code #: 1-30-009	Date: 10/29/2014	Report #: 57
------------------------------	-------------------------	---------------------

Site Name: Photo Circuits Site – Waste Characterization, Transportation & Disposal

Location: Glen Cove, Nassau County

DEC Proj. Mgr.: Michael Mason

Call Out Contractor: Environmental Assessment & Remediation (EAR)

Call Out Contractor Proj. Mgr.: Ian Hofmann

	AM	PM
Weather	Clear	Clear
Temperature	50	70
Wind Direction	West	West

Description of work performed by contractor this report period:

EAR (Prime):

- Removed solid waste from a 5700 gal tank located in the Waste Recovery Building. Personnel entered the tank in Level B PPE. Solids were shoveled into 5 gallon pales and transferred to 55 gallon poly drums just outside the tank.

PSC Environmental Services (Sub):

- Not on site

Discussions/comments regarding visitors, contractor and/or engineer:

Change Orders:

Sampling and Analyses:

Major Issues	Description & Reason

Health & Safety:

Level of protection: B (in tank), C (outside tank)

Is the level of protection in conformance with the approved Health & Safety Plan? Yes

List deviations: None

Are atmospheric monitoring results acceptable? Yes

Site Visitors	Representing	Entered Exclusion Zone

Contractor's Information:

Prime contractor worked from: 7:00am – 3:00pm (Estimate)

Subcontractor	Activity	Hours Worked
(1) Island Pump and Tank	Chemical Disposal	
(2) PSC	Chemical Disposal	

Equipment	P Hrs.	1 Hrs.	2	3	4	Personnel	P Hrs.	1 Hrs.	2 Hrs.	3	4
Pick up/Ford F150 w/300 gal poly tank	8					Super	8				
						(3)Laborers	8				
Decon Trailer	8					Chemists	8				
Generator	8					Laborer					
Utility Trailer	8					Technician					
Pick Up											
Pick up/Ford F250											
Box Truck											
Sampling Van	8										
Fork Lift/Doosan	8										

Site Representative: Kristopher Keenan**Date: 10/29/2014****Representative's Signature:**

Photo Log



Preparing to enter 5700 gal. tank




Transferring solid material to poly drum



Solid material in tank



Tanks for supplied air

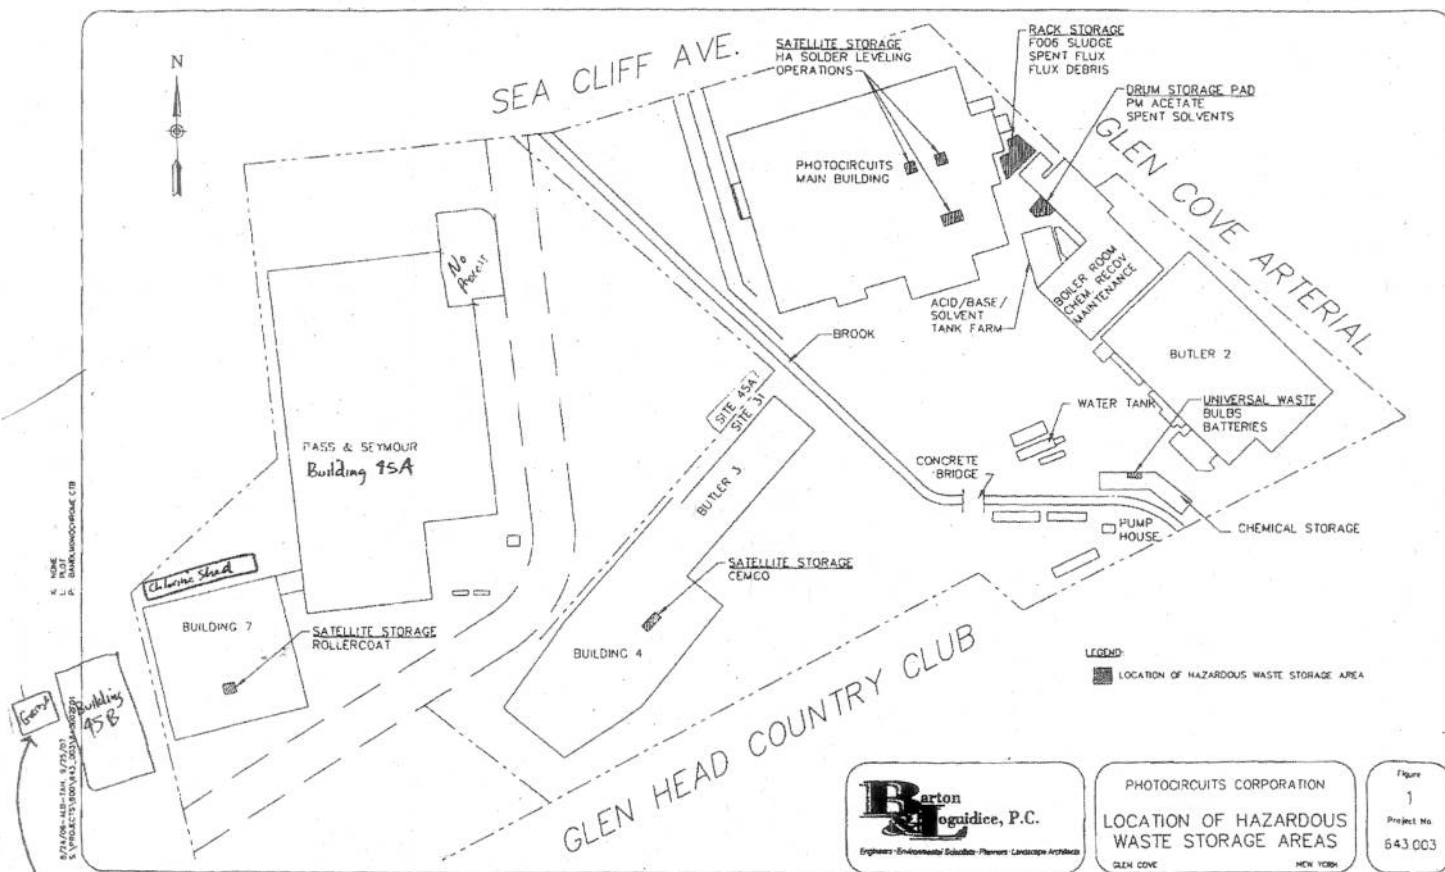

Currently occupied by Ted Dubik North Shore Contracting (516-676-2772)

Barton
Loguidice, P.C.
 Engineers • Environmental Scientists • Planners • Landscape Architects

PHOTOCIRCUITS CORPORATION
 LOCATION OF HAZARDOUS
 WASTE STORAGE AREAS
 GLEN COVE NEW YORK

Figure
 1
 Project No.
 643 003
