



**Department of  
Environmental  
Conservation**

**Division of Environmental Remediation  
Central Office**

**DAILY INSPECTION REPORT**

<b>Site Code #:</b> 1-30-009	<b>Date:</b> 03/23/2015	<b>Report #:</b> 61
------------------------------	-------------------------	---------------------

**Site Name:** Photo Circuits Site – Waste Characterization, Transportation & Disposal

**Location:** Glen Cove, Nassau County

**DEC Proj. Mgr.:** Michael Mason

**Contractor:** Environmental Assessment & Remediation (EAR)

	<b>AM</b>	<b>PM</b>
<b>Weather</b>	Clear	Clear
<b>Temperature</b>	20	35
<b>Wind Direction</b>	West	West

**Description of work performed by contractor this report period:**

EAR (Prime):

- Waste chemicals recovered from Building 7 on the Pass & Seymour property were staged at the west end of the building near the loading dock.
- Contractor entered Building 45B on the Pass & Seymour property to document and recover waste chemicals remaining in the building.

**Discussions/comments regarding visitors, contractor and/or engineer:**

**Summary of samples collected this report period:**

<b>Sample Number</b>	<b>Date Collected</b>	<b>Sample Type</b>	<b>Location</b>	<b>Parameter</b>	<b>Method Number</b>	<b>Turn Around</b>

**Health & Safety:**

Level of protection: C when entering buildings

Is the level of protection in conformance with the approved Health & Safety Plan? Yes

List deviations: None

Are atmospheric monitoring results acceptable? Yes

<b>Site Visitors</b>	<b>Representing</b>	<b>Entered Exclusion Zone</b>

**Contractor's Information:**

Prime contractor worked from: 6:30am – 3:00pm

Subcontractor	Activity	Hours Worked
(1) PSC	Chemical Disposal	

Equipment	P	1	2	3	4	Personnel	P	1	2	3	4
Pick up/Ford F150						Super	1				
Pick Up/Ford Ranger	1					Laborers	3				
Decon Trailer	1					Chemists	1				
Generator	1					Laborer					
Utility Trailer	1					Technician					
Tractor Trailer											
Pick up/Ford F250	1										
Box Truck											
Sampling Van	1										
Fork Lift/Doosan											

**Site Representative: Kristopher Keenan**

**Date: 03/23/2015**

**Representative's Signature:**




## Photo Log



**Waste chemicals staged at west end of Building 7**



**Building 7. Unknown substance on floor**

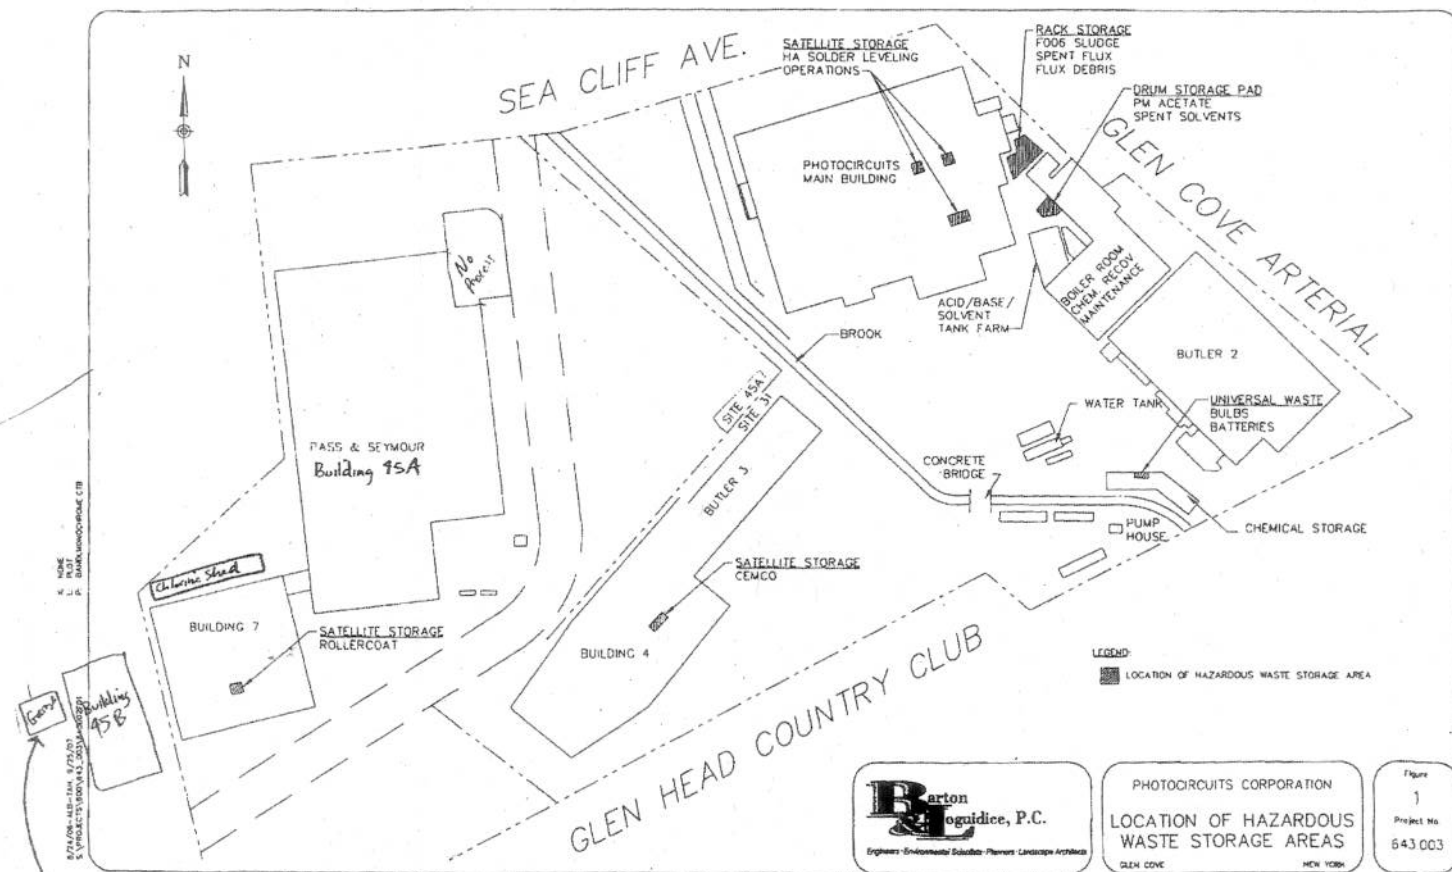

Currently occupied by Ted Dubilly North Shore Contracting (516-676-2772)

**Barton**  
Loguidice, P.C.  
Engineers-Environmental Scientists-Planners-Landscape Architects

PHOTOCIRCUITS CORPORATION  
LOCATION OF HAZARDOUS  
WASTE STORAGE AREAS  
GLEN COVE NEW YORK

Figure  
1  
Project No.  
643 003
