

Division of Environmental Remediation Central Office

DAILY INSPECTION REPORT

Site Name: Photo Circuits Site – Waste Characterization, Transportation & Disposal

Location: Glen Cove, Nassau County **DEC Proj. Mgr.:** Michael Mason

Call Out Contractor: Environmental Assessment & Remediation (EAR)

Call Out Contractor Proj. Mgr.: Ian Hofmann

	AM	PM
Weather	Rain	Rain
Temperature	50	60
Wind Direction	West	West

Description of work performed by contractor this report period:

EAR (Prime):

- Debris from a sump pit located at the west end of Building 4 was removed and power washed. After power washing, the debris was placed adjacent to the sump pit.

Mr. Pump (Sub):

- Storm water and rinse water was vacced out of a sump pit located at the west end of Building 4. Water was shipped to Clear Flo Technologies for disposal. Approximately 3000gal.

Discussions/comments regarding visito	ors, contractor and/or engin	neer:
Change Orders:		
Sampling and analysis this report perio	<u>od:</u>	
Health & Safety:		
Level of protection: C		
s the level of protection in conformance	with the approved Health &	Safety Plan? Yes
List deviations: None		
Are atmospheric monitoring results accep	ptable? Yes	
Site Visitors	Representing	Entered Exclusion Zone

Contractor's Information:

Prime contractor worked from: 6:30am – 3:00pm

Subcontractor	Activity	Hours Worked		
(1) Mr. Pump	Vac Truck	2		

Equipment	P	1	2	3	4	Personnel	P	1	2	3	4
Pick up/Ford F150	1					Super	1				
Pick Up/Ford Ranger	1					Laborer	3				
Decon Trailer	1					Chemists	1				
Generator	1					Technician					
Utility Trailer	1					Teamster		1			
20 ft storage container	1										
Pick up/Ford F250											
Vac Truck		1									
Sampling Van	1										
Fork Lift/Doosan											
Power Washer	1										


Site Representative: Kristopher Keenan Date: <u>04/20/2015</u>

Representative's Signature:

Photo Log



Removing water from sump

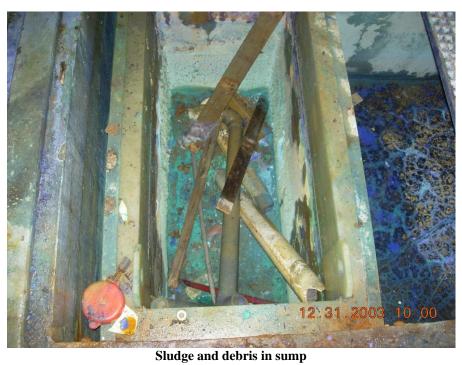



Sludge at bottom of sump

