

NYSDEC Division of Environmental Remediation				 Department of Environmental Conservation		Contract No. DEC Insp. DEC PM – Payson Long, P.E. GES PM. – Scott McDonald HRP Engineer PM – Tom Battles HRP PM – Derek Roy	
Site Location: NYSDEC Lawrence Aviation, Port Jefferson Station, NY							
Weather Conditions							
General Description	Showers, drizzle	AM	Cloudy	PM			
Temperature	46 F	AM	52 F	PM			
Wind	0-2 mph SE	AM	0-2 mph NW	PM			
Health & Safety If any box below is checked “Yes”, provide explanation under “Health & Safety Comments”.							
Were there any changes to the Health & Safety Plan?					*Yes	No	NA
Were there any exceedances of the perimeter air monitoring reported on this date?					*Yes	No	NA
Were there any nuisance issues reported/observed on this date?					*Yes	No	NA
Health & Safety Comments Conducted daily tailgate meeting, conduct drive around to check for trespassers, check for access issues.							
Summary of Work performed		Arrived at site:	0630		Departed Site:	1630	
0630 – Pawel Mecinski (GES) onsite. Unlocked Park Ave Gate. Highground Industrial (HGI) personnel onsite. Held H&S meeting 0700 – Carly Saindon (HRP), Matt Reppenhagen (GES) on site. -No CAMP in the AM hours due to rain showers and drizzle with fog. 0900 – Chris Labbe and Keith Gandarillas (HRP) onsite for GW treatment system maintenance. 1100 – Chris L. and Keith G. offsite. 1200-Set up CAMP stations and monitor ambient air for dust and VOCs. No abnormal readings noted during the work shift duration. 1150 – Jeff Hoffman on site to sample septic sludge and septic liquids waste streams. 1210 – Janet Gremli (SCDHS) on site to inspect excavated and backfilled structures. Oversee sampling of drywell structure DW-6 post remedial excavation. 1300 – Janet G. offsite 1415 – Jeff H. offsite. 1345 – Pace labs courier onsite for sample pickup. 1545 – Trespassers observed on dirt bikes coming from the greenway trail and were asked to leave the site. Work Completed by HGI: -Pump out remaining liquids from DW-6 -Excavate drywell DW-6 from 14ft below ground surface (bgs) to approximately 19ft bgs. -Process clean concrete into 6"- backfill material. -Decontaminate equipment used for remedial excavation. HRP collected a bottom sample from DW-6 from approx. 19-19.5 ft bgs. Imports/Exports: - None 1600- HGI crew offsite. 1630 – All personnel offsite. Locked gates, system shed.							

[illegible]

Equipment/Material Tracking Comments:

Visitors to Site

Name	Representing	Entered Exclusion/CRZ Zone	
None		Yes	No
		Yes	No
		Yes	No

Site Representatives




Janet Gremli	SCDHS

Project Schedule Comments

Issues Pending

Interaction with Public, Property Owners, Media, etc.

Include (insert) figures with markups showing location of work and job progress

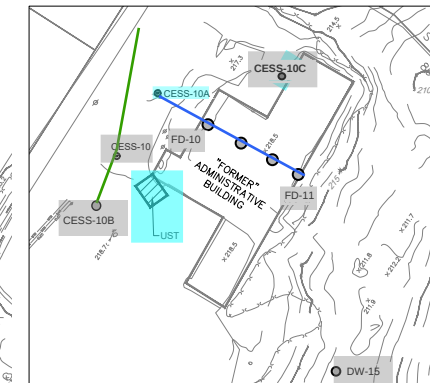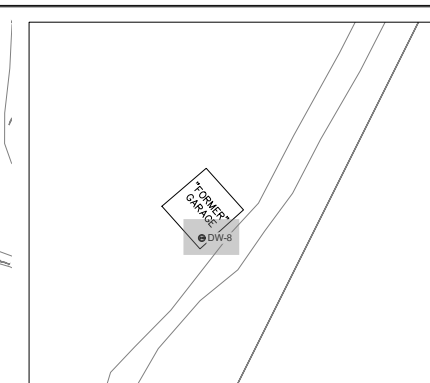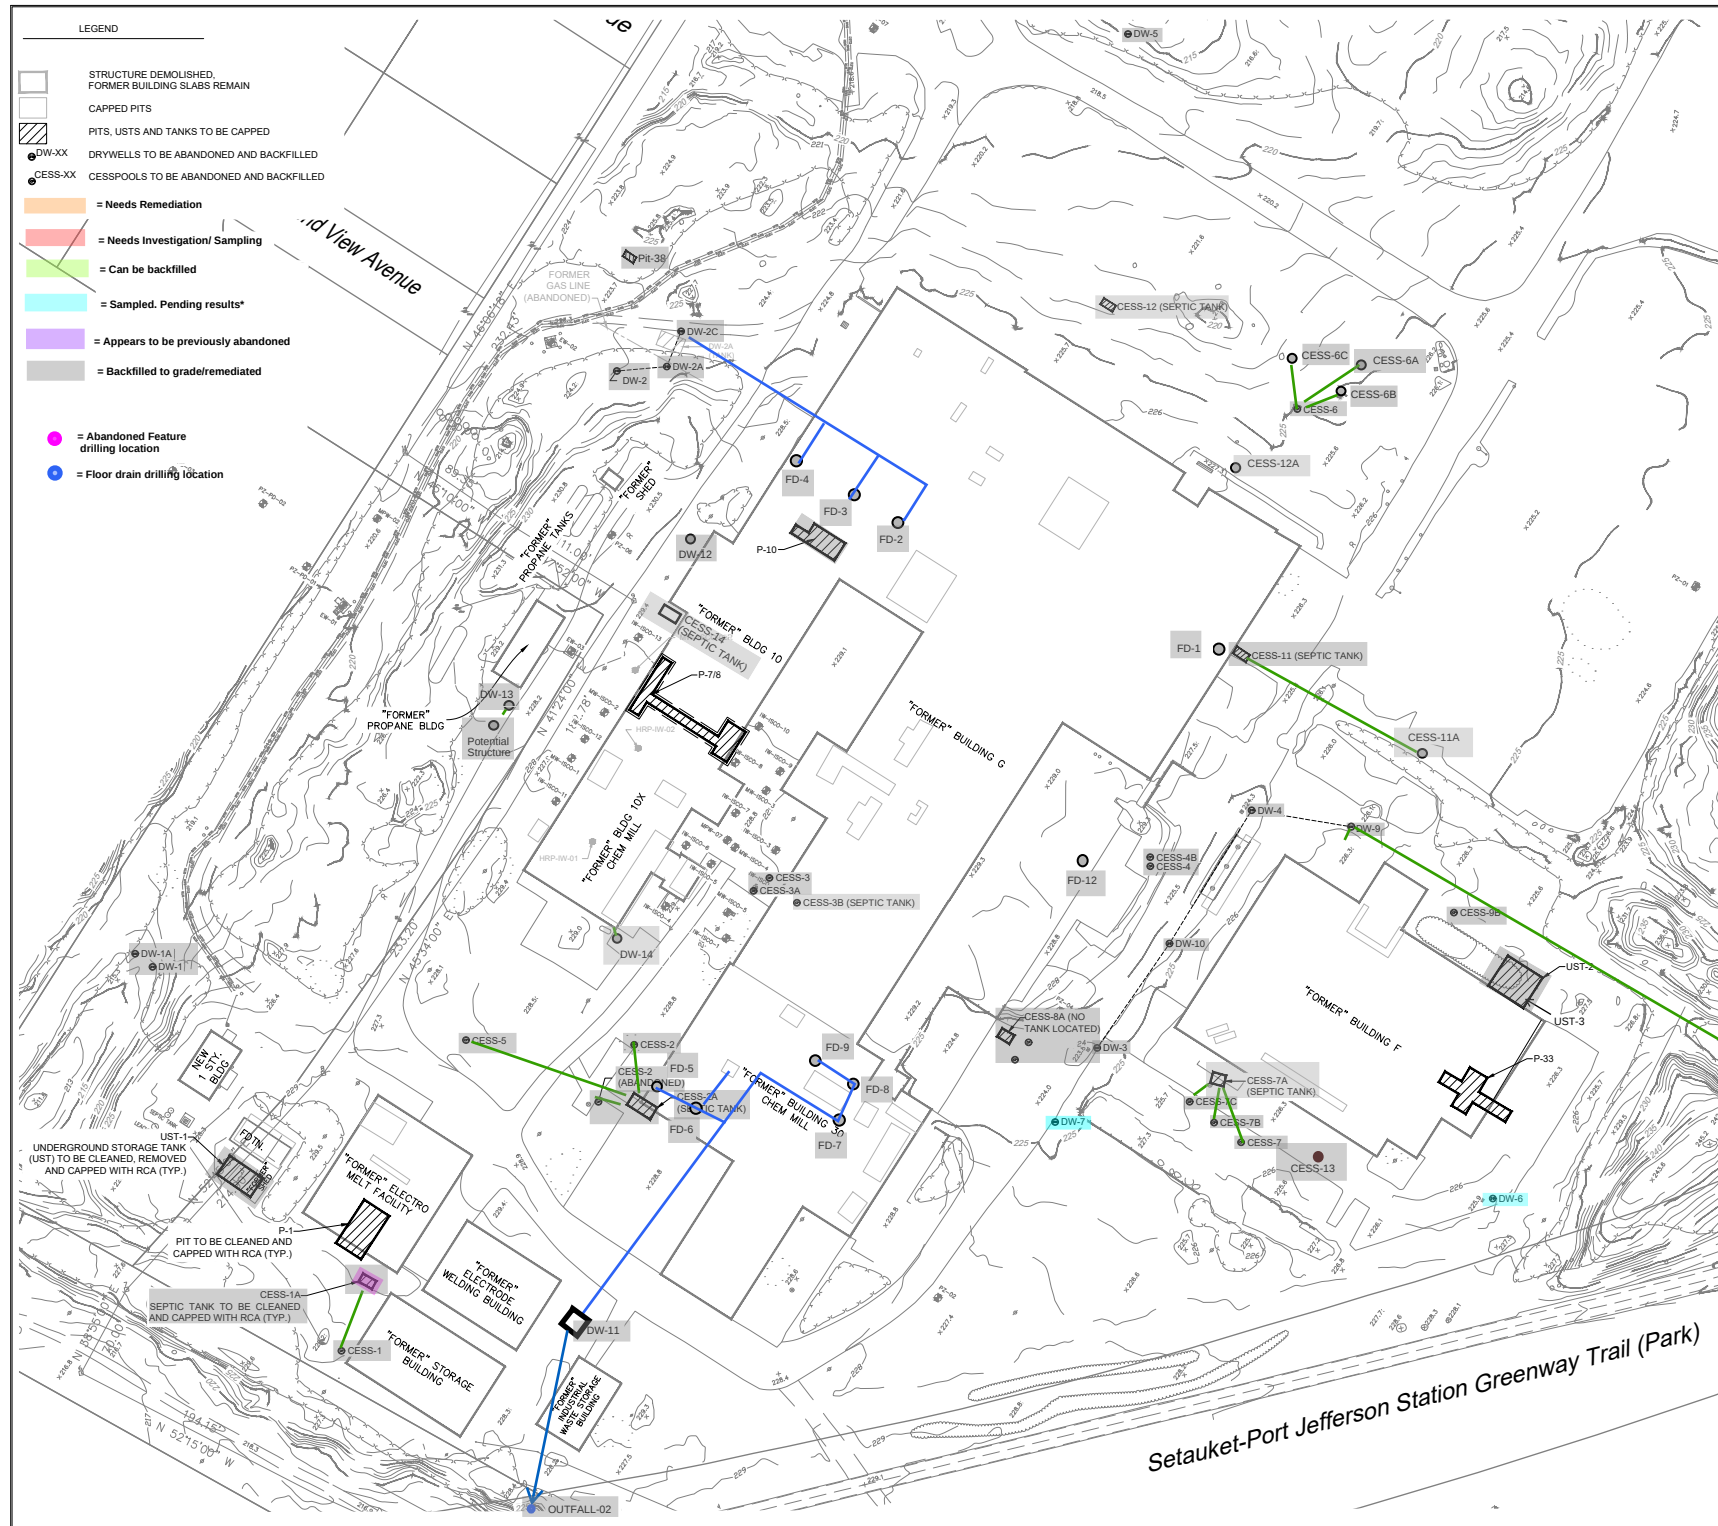

FORMER GARAGE LOCATED ON THE NORTHEAST CORNER OF THE
PROPERTY OFF OF SHEEP PASTURE ROAD

FORMER ADMINISTRATIVE BUILDING LOCATED ON THE
NORTHWEST CORNER OF THE PROPERTY OFF OF PARK AVENUE

GENERAL NOTES:

1. NOT ALL UTILITIES MAY BE SHOWN. ALL UTILITIES AND STRUCTURES MUST BE VERIFIED BY CONTRACTOR.
2. ALL WELLS WITHIN THE CONSTRUCTION SITE ARE TO BE PROTECTED AND MAINTAINED THROUGHOUT CONSTRUCTION ACTIVITIES.
3. SITE TO BE CLEARED AND GRUBBED AS NECESSARY TO PERFORM THE WORK.

SUGGESTED CONSTRUCTION SEQUENCE

4. INSTALL STOCKPILE/STAGING AREAS IN ACCORDANCE WITH SHEETS C2.0.
5. INSTALL FENCING IN ACCORDANCE WITH SHEET C2.0.
6. FOLLOWING COORDINATION WITH NYSDEC TO DEWATER AND CLEAN THE VARIOUS PITS, CONTRACTOR SHALL BACKFILL THE PITS, CESS POOLS, DRYWELLS AND USTS TO EXISTING GRADE.
7. REMOVE ALL TEMPORARY EROSION AND SEDIMENT CONTROL MEASURES AND TEMPORARY FENCING AFTER ALL AREAS HAVE BEEN WELL ESTABLISHED AND THE SITE HAS BEEN INSPECTED AND APPROVED BY THE OWNER AND/OR THE OWNER'S REPRESENTATIVE.



NORT

[illegible]

LAWRENCE AVIATION INDUSTRIES	NEW YORK STATE DEPARTMENT OF ENVIRONMENTAL CONSERVATION
100 SHEEP PASTURE ROAD	ROOST HILL, NEW YORK 10978

SITE DRAINAGE FEATURES 2025

SHEET NO.

Fig. 2

Site Photographs (Descriptions Below)	
	
Photo 1 – Excavation of the bottom sediments at DW-6 structure.	Photo 2- Excavation of muddy sludge from DW-6 drywell.
	
Photo 3 – DW-6 post remediation. Bottom of the structure excavated from 14ft down to 19ft below surface.	Photo 4 – Generated stockpile from DW-6 remediation
	
Photo 5 – Concrete processing activities.	

Comments	
Site Inspector(s): Carly Saindon and Pawel Mecinski	
Date: 03/20/2025	

Videos of discreet operations have been provided to the DEC Project Manager to facilitate understanding of the ongoing work? Yes ☐ No ☒ N/A ☐

REMEDIAL ACTIVITIES AT OTHER PROPERTIES
[Residential, Adjacent, AWS, non-Site Properties]
(Section may be deleted for ongoing remedial sites)

1. Does the Department and its Contractor(s) have permission to enter the property or properties for the day's work?	Yes ☒	No ☐
2. Does anyone at this location have any symptoms of a respiratory infection (e.g., cough, sore throat, fever, or shortness of breath)?	Yes ☐	No ☒
3. Has anyone at this location been tested and confirmed to have COVID-19?	Yes ☐	No ☒
4. If Yes to 1, 2 or 3, follow the latest NYSDOH COVID-19 guidance: https://coronavirus.health.ny.gov/home	Yes ☐	No ☐
<u>Comments:</u>		

ON-SITE WASTE STORAGE

Drums, roll offs and piles are staged in secure areas?	Yes ☒	No ☐	N/A ☐
Liners and berms have been installed if necessary to prevent cross contamination of clean areas?	Yes ☐	No ☐	N/A ☒
Containers are in good condition or properly overpacked?	Yes ☐	No ☐	N/A ☒
Waste materials are scheduled to be properly characterized and disposed of prior to demobilization?	Yes ☒	No ☐	N/A ☐
Complying with RCRA 90 day storage limitation for hazardous waste?	Yes ☒	No ☐	N/A ☐
Piles are securely covered when not in use?	Yes ☒	No ☐	N/A ☐
Containers are closed when not in use?	Yes ☒	No ☐	N/A ☐
Staging areas should be inspected periodically and any issues addressed immediately?	Yes ☒	No ☐	N/A ☐
Signage and labeling comply with RCRA requirements for all staging areas and containers?	Yes ☐	No ☐	N/A ☒
If any issues noted, has Contractor been notified?	Yes ☐	No ☐	N/A ☒
<u>Comments:</u>			

NUISANCE CHECKLIST

Were there any community complaints related to work on this date?	Yes ☐	No ☒	N/A ☐
Were there any odors detected on this date?	Yes ☐	No ☒	N/A ☐
Was noise outside specification and/or above background on this date?	Yes ☐	No ☒	N/A ☐
Were vibration readings outside specification and/or above background on this date?	Yes ☐	No ☒	N/A ☐
Any visible dust observed beyond the work perimeter on this date?	Yes ☐	No ☒	N/A ☐
Any visible contrast (turbidity) beyond engineering controls observed on this date?	Yes ☐	No ☒	N/A ☐
Was turbidity checked at the outfall(s)?	AM ☐	PM ☐	N/A ☒
Were any property owners NOT provided advance notice for work performed on this property on this date?	Yes ☐	No ☒	N/A ☐

Was the temporary fabric structure closed at the end of the day?	Yes ☐	No ☐	N/A ☒
Has Contractor failed to protect all foundations and structures adjacent to and adjoining the site which are affected by the excavations or other operations connected with performance of the Work?	Yes ☐	No ☐	N/A ☒
If yes, has Contractor been notified?	Yes ☐	No ☐	N/A ☒
<u>Comments:</u>			

RESILIENCE/GREEN REMEDIATION CHECKLIST

Is site power procured from renewable energy sources (e.g., solar, wind, geothermal, biomass and biogas)?	Yes ☐	No ☐	N/A ☒
Is the Contractor employing 2007 or newer or retrofitted (BART*) diesel on-road trucks and non-road equipment?	Yes ☐	No ☐	N/A ☒
Is vehicle idling adequately reduced per 6NYCRR Part 217-3?	Yes ☐	No ☐	N/A ☒
Have equipment operators been trained in the idling requirements of 6NYCRR Part 217-3?	Yes ☐	No ☐	N/A ☒
Is BART-equipped equipment properly maintained and working?	Yes ☐	No ☐	N/A ☒
Is work being sequenced to avoid double handling?	Yes ☒	No ☐	N/A ☐
Is there an onsite recycling program for CONTRACTOR-generated wastes and is it complied with?	Yes ☐	No ☐	N/A ☒
Are office trailer heating and cooling systems maintained at efficient set points, have programable thermostats been installed?	Yes ☐	No ☐	N/A ☒
Are products and materials used in performance of the work appropriately certified (e.g., LEED, Energy Star, Sustainable Forestry Initiative®, etc.)?	Yes ☐	No ☐	N/A ☒
Are resiliency features included in the design, or completed remedy properly installed and/or maintained (flood control, storm water controls, erosion measures, etc.)?	Yes ☐	No ☐	N/A ☒
Are green remediation elements included in the design, or completed remedy properly installed and/or maintained (e.g., porous pavement, geothermal, variable speed drives, native plantings, natural stream bank restoration, etc.)?	Yes ☐	No ☐	N/A ☒
Has Contractor been notified of any deficiencies?	Yes ☐	No ☐	N/A ☒
Are remote/call in job meetings being held in lieu of meeting in person where possible?	Yes ☐	No ☒	N/A ☐
<u>Comments:</u>			

* BART – Best Available Retrofit Technology
