

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	----------	---	---	----	---	---

 Date: 9-Mar-09
 REPORT No. 95
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		42/47			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction manager	1x8 hrs	J.Szymanski
EnviroTrac	Operator	1x8hrs	J.Byrnes
EnviroTrac	Technician	3x8 hrs	R.Gimbel, K.Davies, R.Maletta
Preferred Environmental Services	Technician	1x4hrs	B.Gammons

EQUIPMENT AT THE SITE

I = Idle W = Working

Daewoo 450 skidder - W	
Case 590 Backhoe - W	
Case 621D Front End Loader - W	
20' Storage Container - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in level D-PPE		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM	
Health and Safety Site Officer: N/A	
DESCRIPTION OF WORK PERFORMED AND OBSERVED	
1-Tailgate H&S meeting performed before the start of the work day. monitoring was not performed due to rain.	2- Air
2-Hazardous soil stockpile being loaded into 2 dump trucks (Gondul Trucking) and transported to the disposal facility, Clean Earth. Manifests being prepared by Spectrum Preferred Environmental Services. A total of 9 hazardous load were sent to Clean Earth, 7 on Friday and 2 today.	
3-Non-hazardous soil stockpile being loaded into 3 dump trucks (1 truck Rainbow Transportation and 2 trucks Greenwood 2 Trucking) and transported to the disposal facility, Soil Safe. Manifests being prepared by Spectrum Preferred Environmental Services.	
4-Daewoo skid steer deconned before going to Cabot St. to move RCA. Decon pad set over sump #2 (solid vault) with poly over the sump and going to the north to off the pad. The skid steer entered from the south, was steam cleaned then exited over clean poly to the north.	
5- AT 51 Cabot Street - sidewalk was repaired using RCA and then tamped down to make a level walkway. At 61 Cabot Street - parking lot hole was repaired using RCA and then tamped down level.	
6- EnviroTrac 20' storage container delivered to the site and set up next to the field trailer.	

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 03/9/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0087.jpg	3/9/2009	AM	Front end loader loading dump truck with hazardous soil
100_0093.jpg	3/9/2009	PM	20' storage container next to field trailer
100_0089.jpg	3/9/2009	AM	Deconning skid steer with steam cleaner
100_0090.jpg	3/9/2009	PM	Repaired parking lot using RCA at 61 Cabot Street
100_0091.jpg	3/9/2009	PM	Repaired sidewalk using RCA at 51 Cabot Street
100_0092.jpg	3/9/2009	PM	Panoramic photo of site after soil pile removal

PHOTOS - 3/09/09



100_0087.jpg - Front end loader loading hazardous soil into a dump truck.



100_0093.jpg - 20' storage container next to field trailer



100_0089.jpg - Deconning skid steerer with a steam cleaner.




100_0090.jpg - Repaired parking lot area with RCA at 61 Cabot Street.



100_0091.jpg - Repaired sidewalk with RCA at 51 Cabot Street.



100_0092.jpg - Panoramic view of site after soil pile removal.

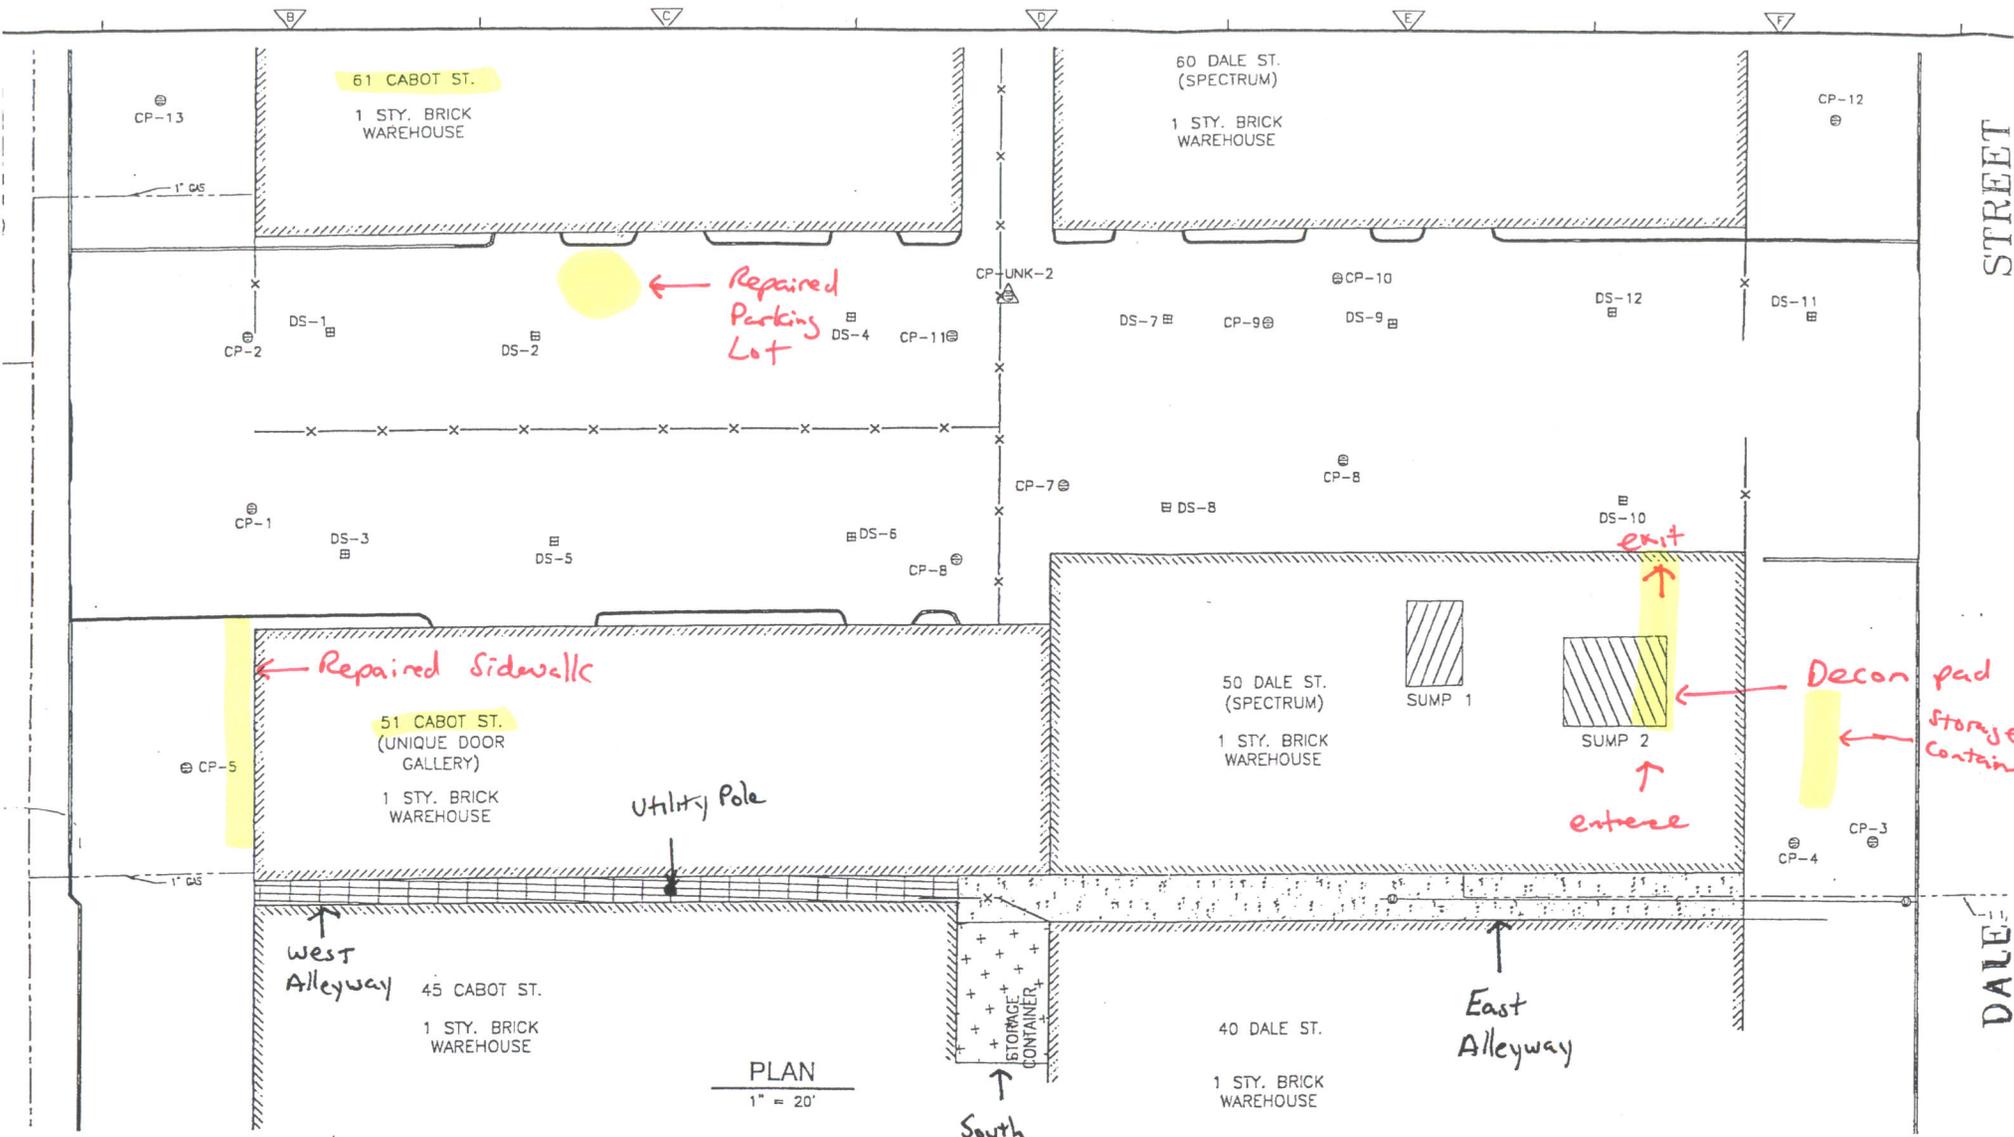

3/9/09

Work Areas
