

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 17-Mar-09
 REPORT No. 101
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		33/52			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	2x8 hrs	J. Szymanski', M.Rose
AARCO	Operator	2x8 hrs	C.Blumberg, B.Wyble

EQUIPMENT AT THE SITE

I = Idle W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in level D-PPE		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1-Tailgate H&S meeting performed before the start of the work day.
2-AARCO started to backfill the east alleyway using the front end loader to move the backfill material to the excavation and the excavator to place the backfill in the excavation. Backfill was done in 8" lifts and then compacted using a flat plate compactor.
3-Watral & Sons delivered 5 loads of backfill material (150 yd3).



x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 03/17/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0128.jpg	3/17/2009	AM	Compacting east alleyway, looking east.
100_130.jpg	3/17/2009	PM	Backfilling and compaction completed for the day (east alleyway, looking


PHOTOS 3-17-09



100_00128.jpg - Compacting east alleyway, looking east.



100_00130.jpg - Backfilling and compaction completed for the day at the east alleyway, looking east.

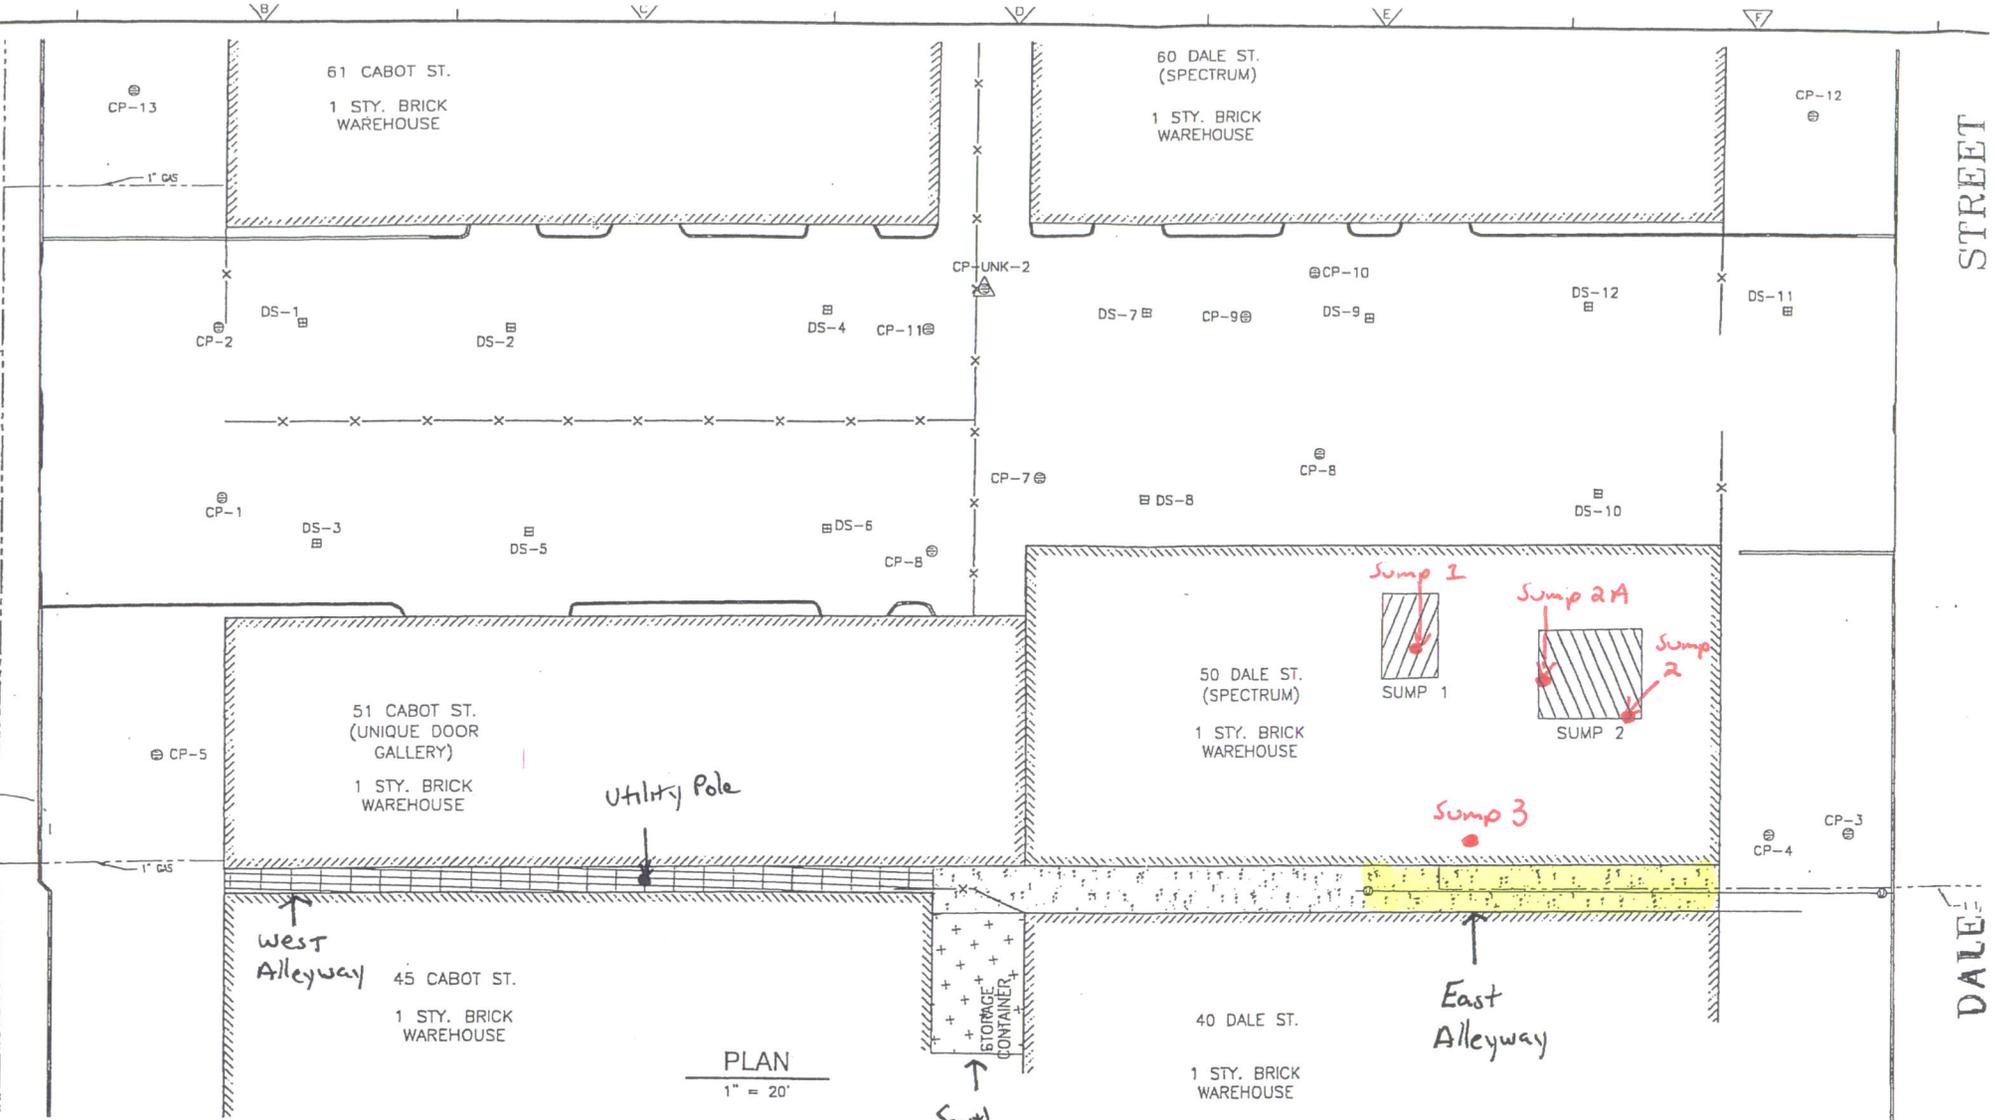

PLAN
1" = 20'

3/17/09

- Work Areas
Backfill and Compacting

