

Project: Spectrum Finishing - Remedial Action  
 Contractor: EnviroTrac Environmental Services  
 CDM Job No: D-006956 Site No. 1-52-029  
 CDM Project Manager: John Blaum

CDM  
 100 Crossways Park West  
 Woodbury, NY 11797  
 Telephone: 516.496.8400  
 Fax: 516.496.8864

### DAILY REPORT

Day: 

S	<b>M</b>	T	W	TH	F	S
---	----------	---	---	----	---	---

  
 Date: 23-Mar-09  
 REPORT No. 105  
 PAGE No. 1

<b>WEATHER</b>	Clear	Partly Cloudy	Overcast	Rain	Snow
<b>TEMP L/H</b>		29/36			
<b>HUMIDITY</b>	Dry	Moderate	High		
<b>WIND</b>	Calm	Light	Moderate	High	
<b>WIND DIR</b>	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

### AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	2x8 hrs	J. Szymanski', M.Rose
EnviroTrac	Operator	2x8 hrs	B.Byrnes, B.Gimbel
EnviroTrac	Technician	2x8 hrs	R.Maletta, K.Davies

### EQUIPMENT AT THE SITE

I = Idle      W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

### HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in modifies level D-PPE (tyvek and booties)		

### CONSTRUCTION ACTIVITIES

<b>Site Representative:</b> Frank Robinson - CDM
<b>Health and Safety Site Officer:</b> N/A
<b>DESCRIPTION OF WORK PERFORMED AND OBSERVED</b>
1-Tailgate H&S meeting performed before the start of the work day. <span style="float: right;">2-Air</span> monitoring for dust and VOC's (2 stations) were set up.
3-Started to chase the contamination around sump-3, started to remove the slab from the foundation wall towards sump-3 and found a lot of green concrete staining. An approximately 50x50 foot area of slab was removed (see drawing). Much of the concrete slab and foundation wall was red and green stained. The staining was more pronounced around sumps 2, 2A and 3.
4-Approximately 25' of the foundation wall was removed, most of the concrete was stained red and green. Some of the foundation was stained red completely through. The soil was also stained green and red from grade down to about 7' bgs along the foundation wall.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

**PHOTOGRAPHIC LOG**

**Date: 03/23/09**

**CDM Job No. D-006956**

**Spectrum Finishing Remedial Action**

**SITE No. 1-52-029**

<b>PHOTO</b>	<b>DATE</b>	<b>TIME</b>	<b>DESCRIPTION</b>
100_00144.jpg	3/23/2009	AM	Green stained concrete near sump-3
100_00149.jpg	3/23/2009	AM	Green stained concrete on south foundation wall
100_00155.jpg	3/23/2009	AM	Red stained concrete from around sump-2
100_00157.jpg	3/23/2009	AM	Red/purple stained concrete from around sump-2
100_00159.jpg	3/23/2009	PM	Green/red stained soil by foundation wall
100_00165.jpg	3/23/2009	PM	Red stained concrete foundation wall, stained completely through
100_00166.jpg	3/23/2009	PM	Excavation at the end of the day

# PHOTOS 3/23/09



100\_00144.jpg - Green stained concrete near sump-3.



100\_00149.jpg - Green staining on south foundation wall.



**100\_00155.jpg - Red stained concrete from around sump-2.**



**100\_00157.jpg - Red/purple stained concrete from around sump-2.**






**100\_00159.jpg - Green/red stained soil by foundation wall.**



**100\_00166.jpg - Red stained concrete foundation wall, stained completely through.**



100\_00167.jpg - Excavation at the end of the day.

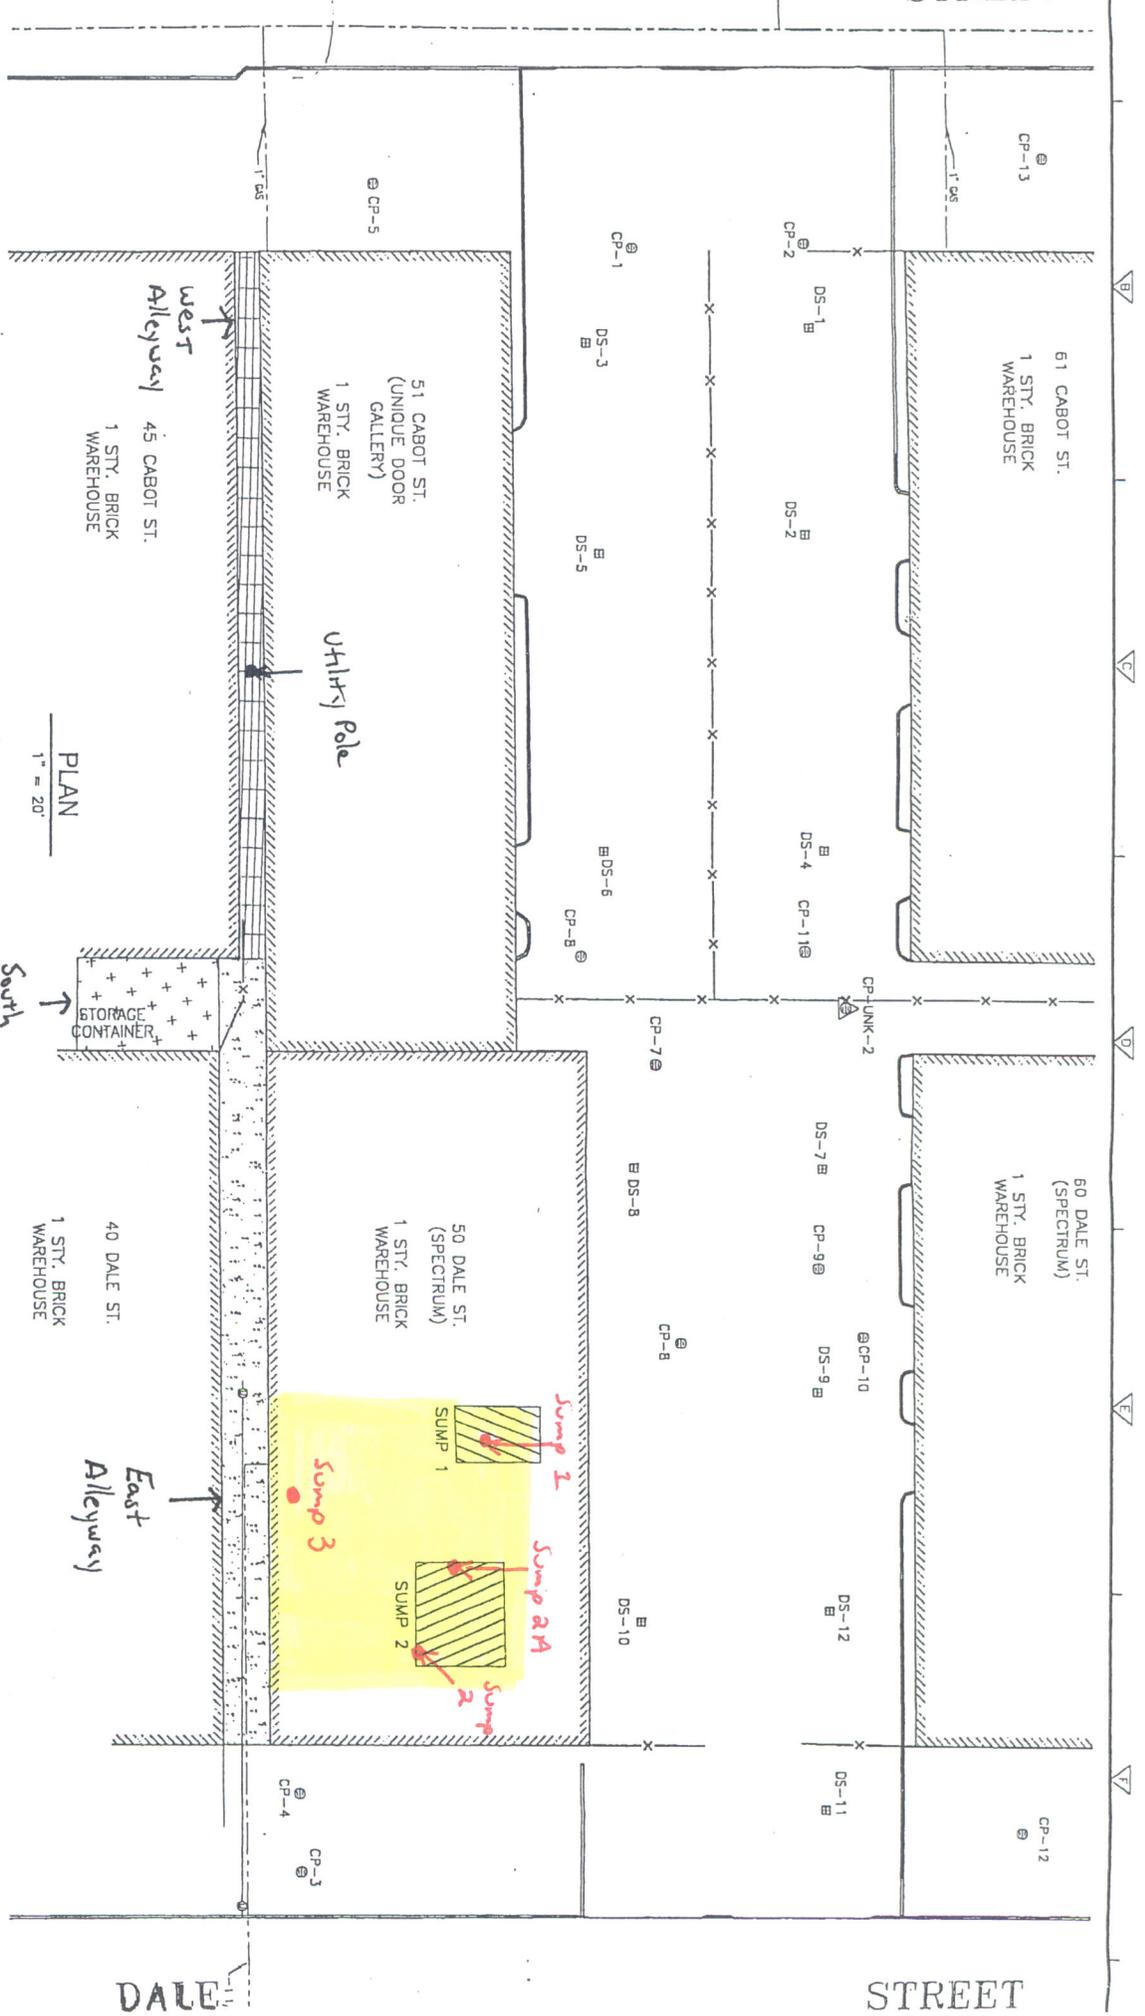

PLAN  
1" = 20'

3/23/09  
Work Area

DALE

STREET
