

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 25-Mar-09
 REPORT No. 107
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		31/52			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x8 hrs	M.Rose
EnviroTrac	Operator	2x8 hrs	B.Byrnes, B.Gimbel
EnviroTrac	Technician	2x8 hrs	R.Maletta, K.Davies, R.Bauer
Preferred Env. Services	Technician	1x8 hrs	B.Gammons

EQUIPMENT AT THE SITE I = Idle W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in modified level D-PPE (tyvek and booties)		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1-Tailgate H&S meeting performed before the start of the work day. 2-Air monitoring for dust and VOC's (2 stations) were set up.
3-14 trucks loads (10 wheel) of hazardous waste soil were transported to the disposal facility, Clean Earth, by ETGI Trucking.
4-Continue to excavate the area down to ~4 that was started yesterday. Excavating down to ~10 along where the foundation wall was and where sump-3 used to be. Found hard grayish clay layers with green veins of material going through it. Also hard chunks of green and red material, almost like concrete north of where sump-3 was.
5-Found 3 PVC pipes just below the slab with green soil and concrete soil around them. See drawing for location.
6-Sprayed water on slab for dust control.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG
25-Mar-09
CDM Job No. D-006956
Spectrum Finishing Remedial Action
SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_00190.jpg	3/25/2009	AM	3 PVC pipes found just under the slab. See drawing for location
100_00191.jpg	3/25/2009	AM	Green stained soil on east side of excavation
100_00192.jpg	3/25/2009	AM	Excavating soil from the excavation
100_00195.jpg	3/25/2009	AM	Green clay like material at SW corner of excavation
100_00201.jpg	3/25/2009	AM	Chunks of green/red hard material from north side of sump-3
100_00203.jpg	3/25/2009	AM	Green clay like material with red crust around, south side of excavation
100_00206.jpg	3/25/2009	PM	Excavation at the end of the day

PHOTOS 3/25/09



100_00190.jpg - 3 PVC pipes found just below the slab. See drawing for location.



100_00191.jpg - Green stained soil on east side of excavation



100_00192.jpg - Excavating soil from the excavation.



100_00195.jpg - Green clay like material at SW corner of excavation




100_00201.jpg - Chunks of green/red hard material from north side of sump-3



100_00203.jpg - Green clay like material with red crust around, south side of excavation.



100_00206.jpg - Excavation at the end of the day.

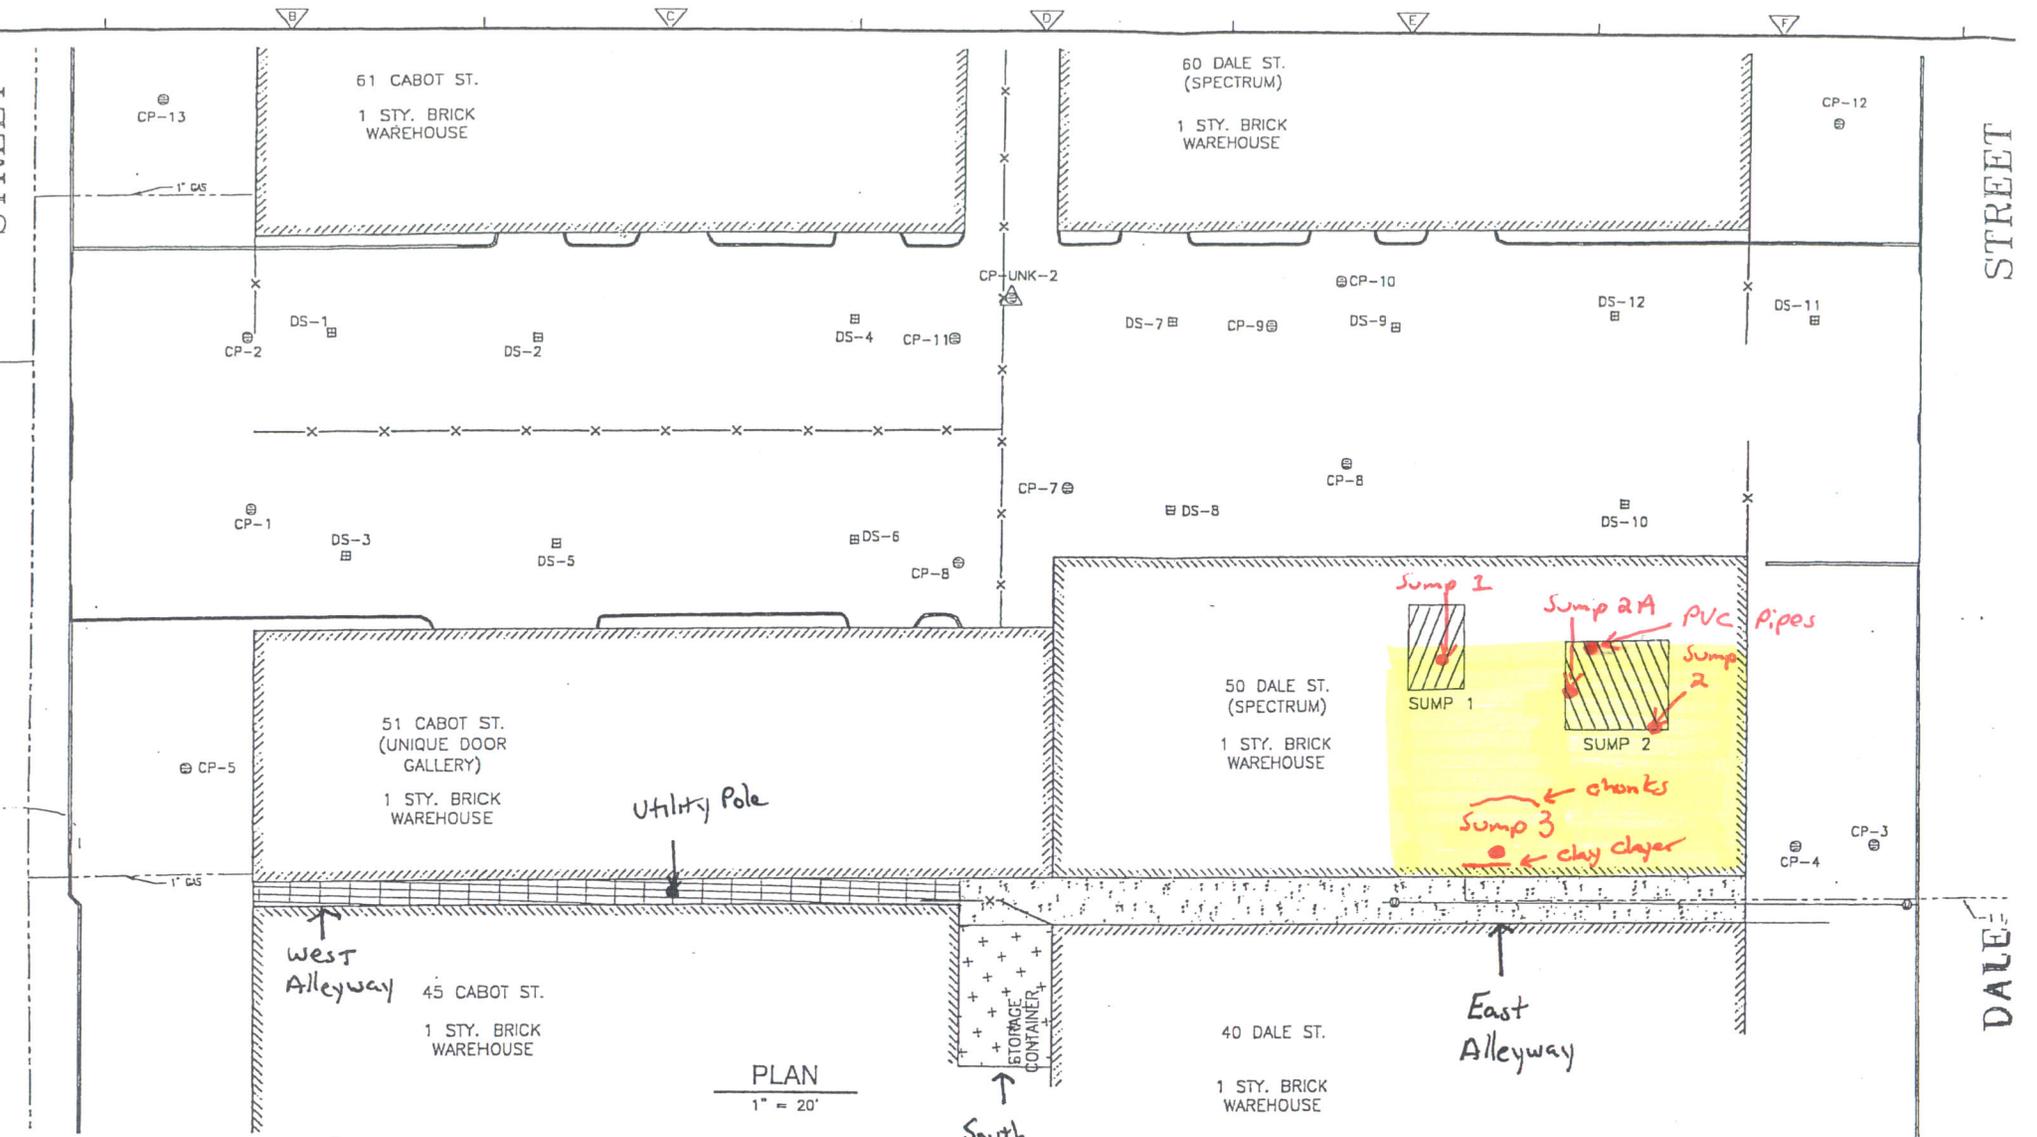

PLAN
1" = 20'

3/25/09

Work Areas

STREET

DALE

61 CABOT ST.
1 STY. BRICK WAREHOUSE

60 DALE ST.
(SPECTRUM)
1 STY. BRICK WAREHOUSE

51 CABOT ST.
(UNIQUE DOOR GALLERY)
1 STY. BRICK WAREHOUSE

50 DALE ST.
(SPECTRUM)
1 STY. BRICK WAREHOUSE

West Alleyway
45 CABOT ST.
1 STY. BRICK WAREHOUSE

40 DALE ST.
1 STY. BRICK WAREHOUSE

STORAGE CONTAINER

South Alleyway

East Alleyway

Utility Pole

Sump 1

Sump 2A

Sump 2

Sump 3

PVC Pipes

chunks

clay layer

CP-13

CP-2

DS-1

DS-2

DS-4

CP-11

CP-UNK-2

DS-7

CP-9

CP-10

DS-9

DS-12

DS-11

CP-12

CP-1

DS-3

DS-5

DS-5

CP-8

CP-7

DS-8

CP-8

DS-10

CP-5

CP-4

CP-3
