

Project: Spectrum Finishing - Remedial Action  
 Contractor: EnviroTrac Environmental Services  
 CDM Job No: D-006956 Site No. 1-52-029  
 CDM Project Manager: John Blaum

CDM  
 100 Crossways Park West  
 Woodbury, NY 11797  
 Telephone: 516.496.8400  
 Fax: 516.496.8864

### DAILY REPORT

Day: 

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

  
 Date: 30-Mar-09  
 REPORT No. 110  
 PAGE No. 1

<b>WEATHER</b>	Clear	Partly Cloudy	Overcast	Rain	Snow
<b>TEMP L/H</b>		47/52			
<b>HUMIDITY</b>	Dry	Moderate	High		
<b>WIND</b>	Calm	Light	Moderate	High	
<b>WIND DIR</b>	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

### AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	2x8 hrs	M.Rose, J.Szymanski
EnviroTrac	Operator	2x8 hrs	B.Byrnes, B.Gimbel
EnviroTrac	Technician	2x8 hrs	R.Maletta, K.Davies

### EQUIPMENT AT THE SITE

I = Idle      W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

### HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in modified level D-PPE (tyvek and booties)		

### CONSTRUCTION ACTIVITIES

<b>Site Representative:</b> Frank Robinson - CDM
<b>Health and Safety Site Officer:</b> N/A
<b>DESCRIPTION OF WORK PERFORMED AND OBSERVED</b>
1-Tailgate H&S meeting performed before the start of the work day. monitoring for dust and VOC's (2 stations) were set up. <span style="float: right;">2-Air</span>
3-Excavating at and around sump-1. Finding red and green contamination to the north, south, and directly under the sump. Excavated down to ~16' directly under sump-1 and cleaned out most of the red and green material. Squared up and excavated the ramps used for the excavator. Stopped excavating because EnviroTrac is estimating they are reaching the monetary limit.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson      Project Manager: John Blaum

**PHOTOGRAPHIC LOG**  
**30-Mar-09**  
**CDM Job No. D-006956**  
**Spectrum Finishing Remedial Action**  
**SITE No. 1-52-029**

<b>PHOTO</b>	<b>DATE</b>	<b>TIME</b>	<b>DESCRIPTION</b>
100_00276.jpg	3/30/2009	AM	Green chunks of material from the bottom of sump-1
100_00279.jpg	3/30/2009	AM	Green/red stained soil on side of sump-1 looking NE
100_00282.jpg	3/30/2009	AM	Green/red soil in pile removed from sump-1.
100_00283.jpg	3/30/2009	AM	Green/red soil in excavator bucket removed from the bottom of sump-1, ~16'.
100_00284.jpg	3/30/2009	PM	Excavation at the end of the day of sump-1 looking SW
100_00287.jpg	3/30/2009	PM	Excavation at the end of the day of sump-1, panoramic view looking SW

# PHOTOS 3/30/09



100\_00276.jpg - Green chunks of material from the bottom of sump-1.



100\_00279.jpg - Green/red stained soil on side of sump-1, looking NE.



**100\_00282.jpg - Green/red soil in pile removed from sump-1.**



**100\_00283.jpg - Green/red soil in excavator bucket from the bottom of sump-1, ~16'.**






**100\_00284.jpg - Excavation at the end of the day of sump-1 looking west.**



**100\_00287.jpg - Excavation at the end of the day, panoramic view looking NW.**

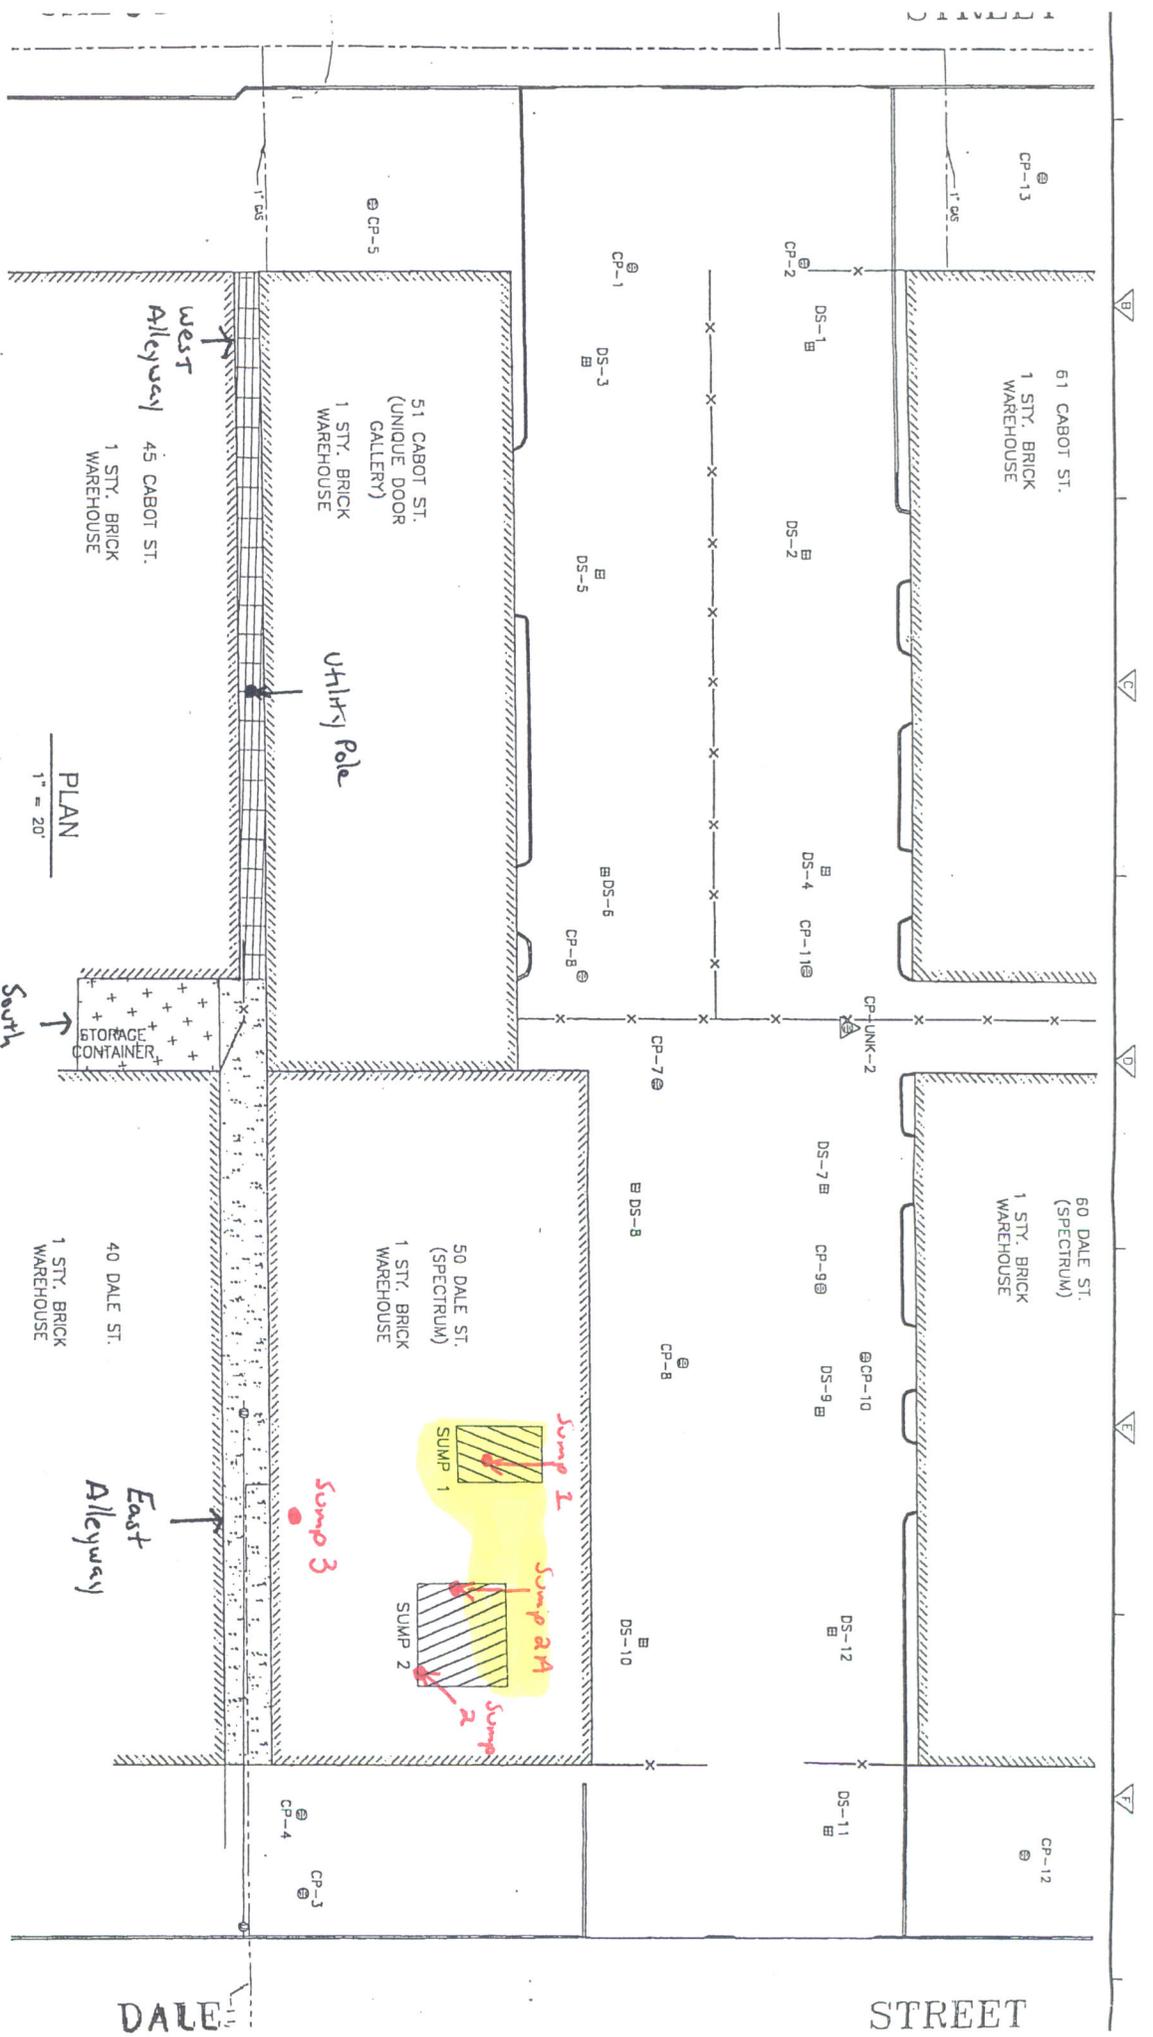

PLAN  
1" = 20'

3/30/09  
Work Areas

DALE

STREET
