

Project: Spectrum Finishing - Remedial Action  
 Contractor: EnviroTrac Environmental Services  
 CDM Job No: D-006956 Site No. 1-52-029  
 CDM Project Manager: John Blaum

CDM  
 100 Crossways Park West  
 Woodbury, NY 11797  
 Telephone: 516.496.8400  
 Fax: 516.496.8864

### DAILY REPORT

Day: 

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

  
 Date: 2-Apr-09  
 REPORT No. 113  
 PAGE No. 1

<b>WEATHER</b>	Clear	Partly Cloudy	Overcast Drizzle	Rain	Snow
<b>TEMP L/H</b>		45/59			
<b>HUMIDITY</b>	Dry	Moderate	High		
<b>WIND</b>	Calm	Light	Moderate	High	
<b>WIND DIR</b>	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

#### AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	2x8 hrs	J.Szymanski, M.Rose
EnviroTrac	Operator	2x8 hrs	B.Byrnes, B.Gimbel
EnviroTrac	Technician	2x8 hrs	R.Maletta, K.Davies

#### EQUIPMENT AT THE SITE

I = Idle      W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

#### HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in modified level D-PPE (tyvek and booties)		

#### CONSTRUCTION ACTIVITIES

<b>Site Representative:</b> Frank Robinson - CDM	
<b>Health and Safety Site Officer:</b> N/A	
<b>DESCRIPTION OF WORK PERFORMED AND OBSERVED</b>	
1-Tailgate H&S meeting performed before the start of the work day. monitoring for dust and VOC's was not performed today due to light rain/drizzle.	2-Air
3-Continued to excavate the green contaminated soil from the NE corner. Also removed 27' of the whole east foundation wall and an additional 18' of just the top 1' east foundation wall all of which was contaminated.	
4-The rest of the visibly contaminated soil and concrete foundation wall in the NE corner should be removed tomorrow.	



x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

**PHOTOGRAPHIC LOG**  
**2-Apr-09**  
**CDM Job No. D-006956**  
**Spectrum Finishing Remedial Action**  
**SITE No. 1-52-029**

<b>PHOTO</b>	<b>DATE</b>	<b>TIME</b>	<b>DESCRIPTION</b>
100_00314.jpg	4/2/2009	AM	Green contaminated concrete on east foundation wall, looking east
100_00315.jpg	4/2/2009	AM	Green contaminated soil/chunks taken from the NE corner
100_00316.jpg	4/2/2009	AM	Pile of contaminated soil/chunks taken from the NE corner
100_00318.jpg	4/2/2009	PM	Excavation at the end of the day, looking north
100_00320.jpg	4/2/2009	PM	Excavation at the end of the day, looking SE
100_00321.jpg	4/2/2009	PM	Mt. Spectrum at the end of the day

# PHOTOS 4/02/09



100\_00314.jpg - Green contaminated concrete on east foundation wall, looking east



100\_00315.jpg - Green contaminated soil/chunks taken from the NE corner



100\_00316.jpg - Pile of green contaminated soil/chunks taken from the NE corner




100\_00318.jpg - Excavation at the end of the day, looking north



100\_00320.jpg - Excavation at the end of the day looking SE




100\_00321.jpg - Mt. Spectrum at the end of the day.

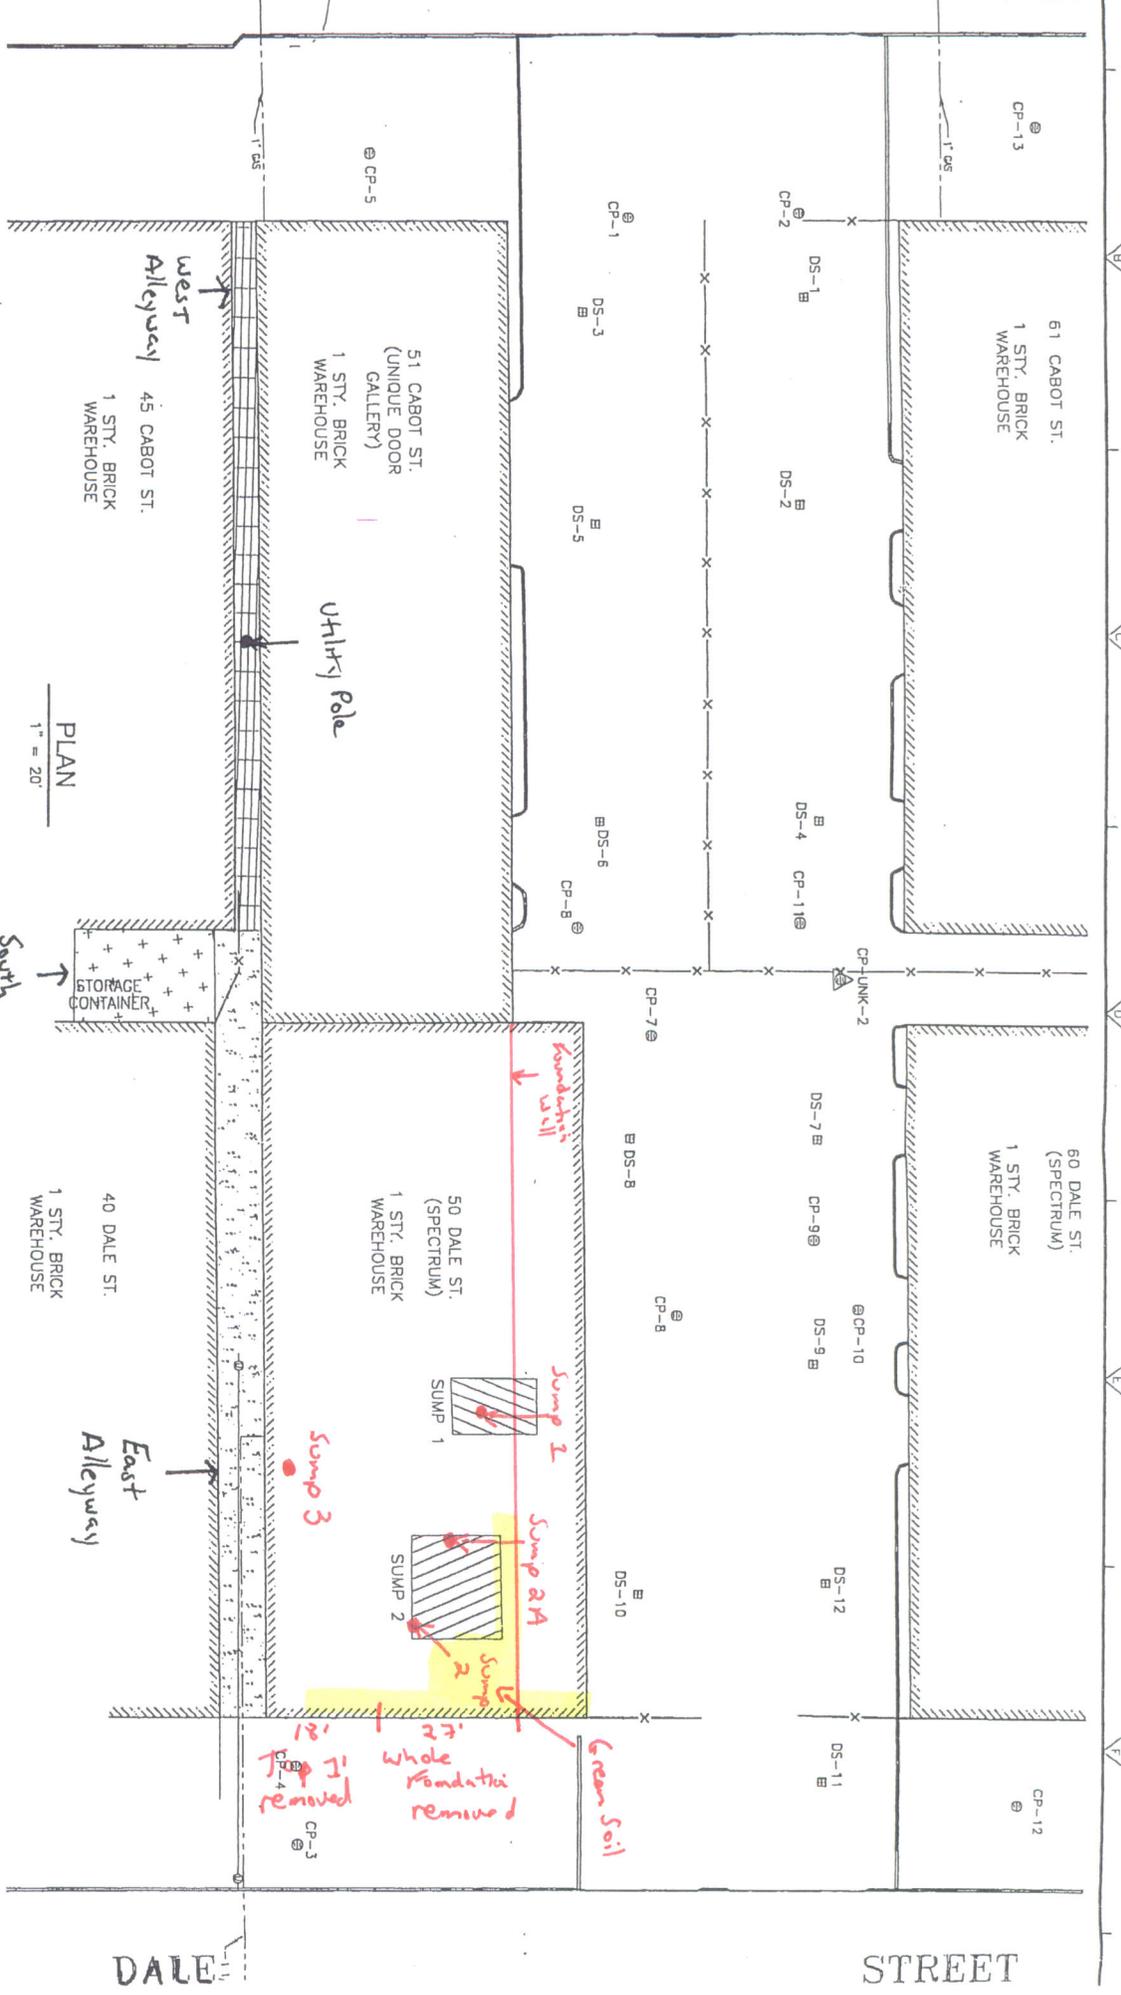

4/2/09  
Work Areas

DALE STREET

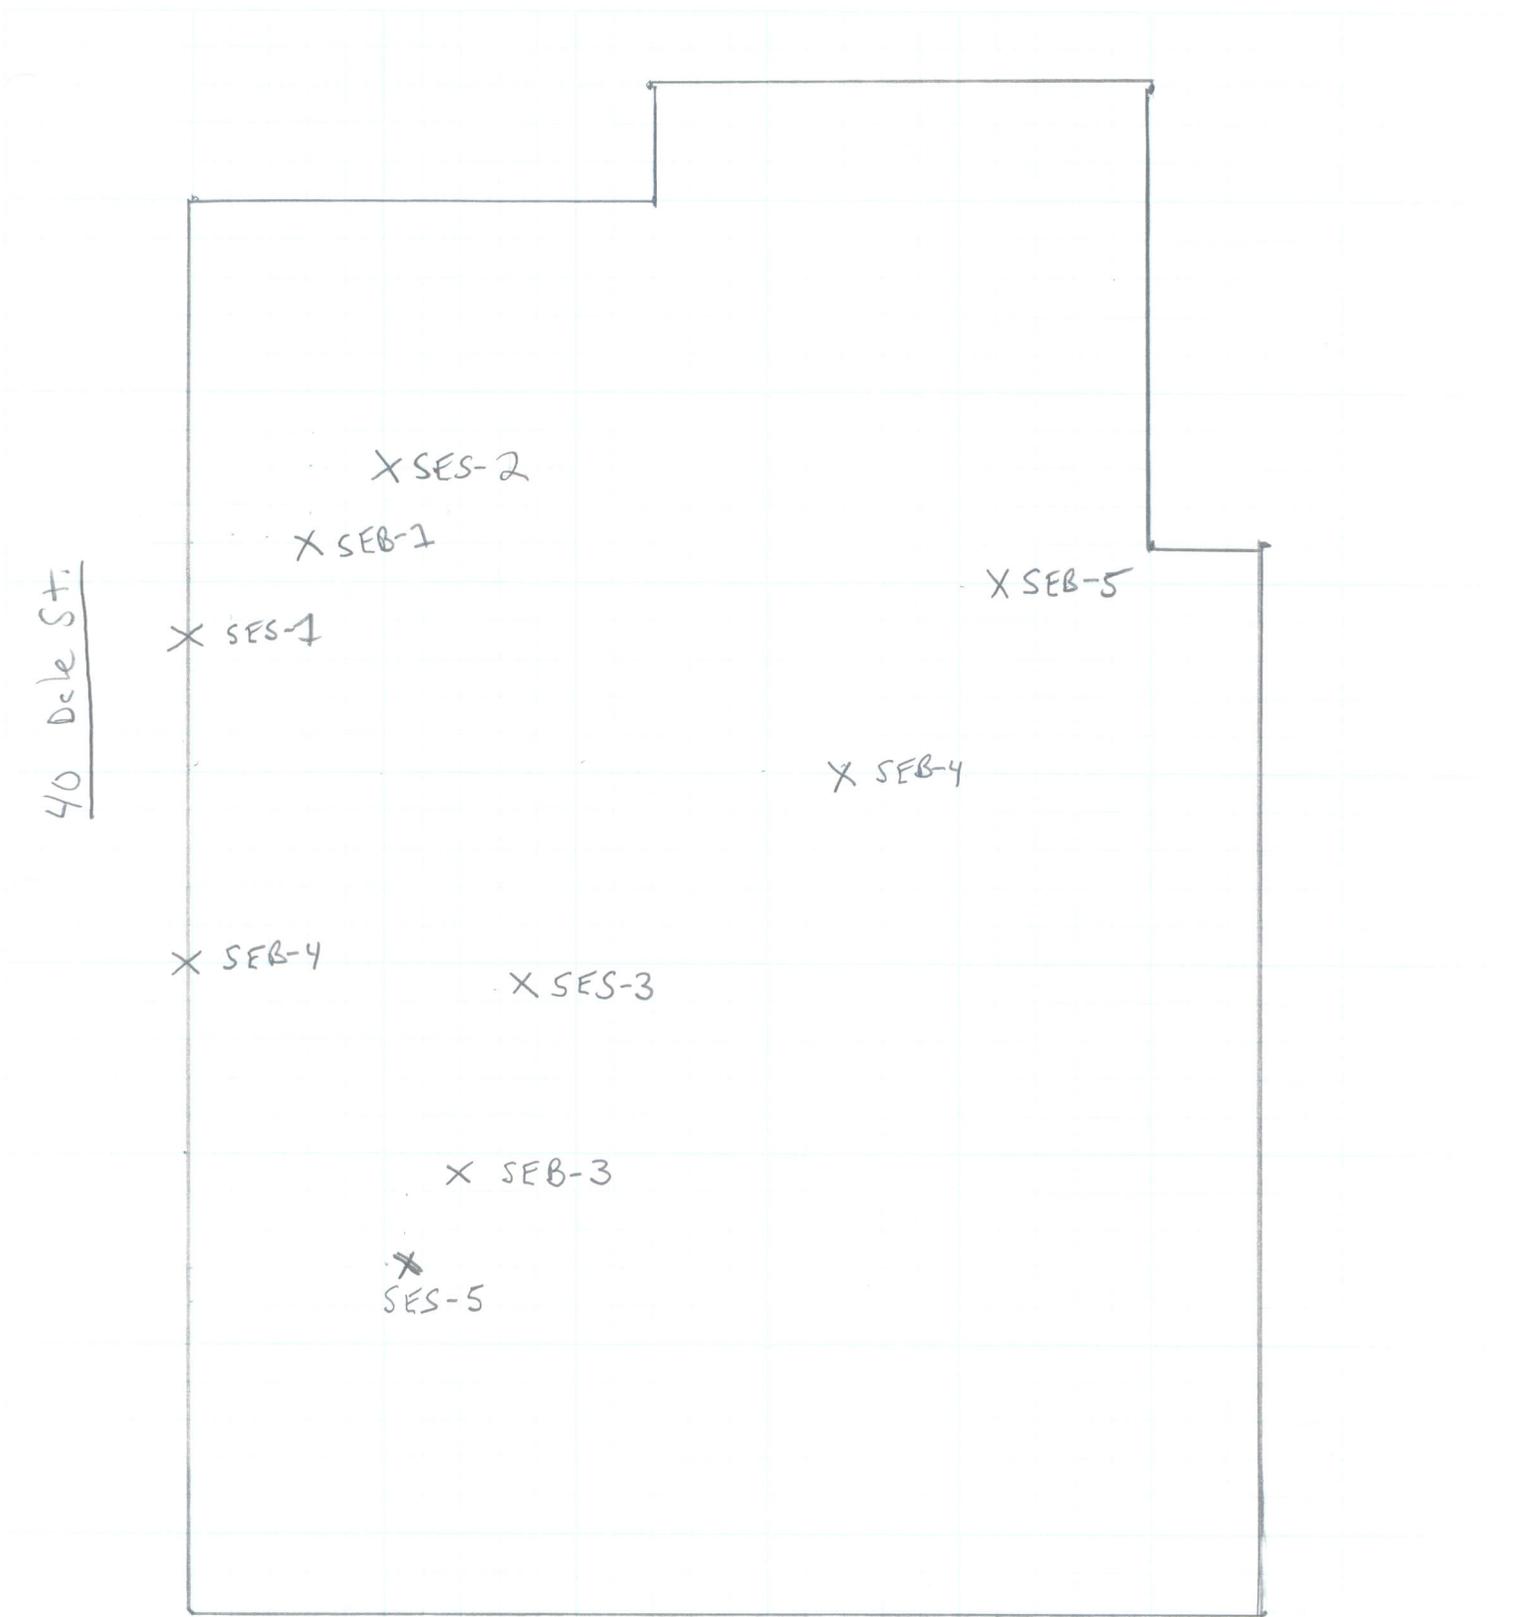

Notes

1 square = 2'  
SES = Sump Excavation  
SEB = Sump Excavation

Dale St.

Sidewalk Sample Location  
Bottom Sample Location.
