

Project: Spectrum Finishing - Remedial Action  
 Contractor: EnviroTrac Environmental Services  
 CDM Job No: D-006956 Site No. 1-52-029  
 CDM Project Manager: John Blaum

CDM  
 100 Crossways Park West  
 Woodbury, NY 11797  
 Telephone: 516.496.8400  
 Fax: 516.496.8864

### DAILY REPORT

Day: 

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

  
 Date: 3-Apr-09  
 REPORT No. 114  
 PAGE No. 1

<b>WEATHER</b>	Clear	Partly Cloudy	Overcast	Rain	Snow
<b>TEMP L/H</b>		52/54			
<b>HUMIDITY</b>	Dry	Moderate	High		
<b>WIND</b>	Calm	Light	Moderate	High	
<b>WIND DIR</b>	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

### AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x4 hrs	M.Rose
EnviroTrac	Operator	2x4 hrs	B.Byrnes, B.Gimbel
EnviroTrac	Technician	2x4 hrs	R.Maletta, K.Davies

### EQUIPMENT AT THE SITE

I = Idle      W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

### HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in modified level D-PPE (tyvek and booties)		

### CONSTRUCTION ACTIVITIES

<b>Site Representative:</b> Frank Robinson - CDM
<b>Health and Safety Site Officer:</b> N/A
<b>DESCRIPTION OF WORK PERFORMED AND OBSERVED</b>
1-Tailgate H&S meeting performed before the start of the work day. monitoring for dust and VOC's was not performed today due to rain <span style="float: right;">2-Air</span>
3-The last 30' of the north contaminated foundation wall was removed. Chased green contaminated soil from the NE corner of the slab, excavated ~10'x4' area and ~3' deep, removed all the visible contamination.
4-Collected sidewall samples, SES-10 + duplicate, SES-11 and SES-12 and bottom samples SEB-7 +MS/MSD and SEB-8. Samples will be analyzed for TAL metals + cyanide for 24 hour TAT.
5-EnviroTrac worked a half a day due to everyone taking a CPR course.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson      Project Manager: John Blaum

**PHOTOGRAPHIC LOG**  
**3-Apr-09**  
**CDM Job No. D-006956**  
**Spectrum Finishing Remedial Action**  
**SITE No. 1-52-029**

<b>PHOTO</b>	<b>DATE</b>	<b>TIME</b>	<b>DESCRIPTION</b>
100_00322.jpg	4/3/2009	AM	Green contaminated soil in NE corner of excavation
100_00323.jpg	4/3/2009	AM	North foundation wall down, looking NE
100_00324.jpg	4/3/2009	AM	Excavation at the end of the day, looking north
100_00325.jpg	4/3/2009	AM	Excavation at the end of the day, looking east
100_00326.jpg	4/3/2009	AM	Close-up view of fire main, looking north
100_00327.jpg	4/3/2009	AM	Close-up of water main (left) and sewer pipe (left) looking east

# PHOTOS 4/03/09



100\_00322.jpg - Green contaminated soil in NE corner of excavation



5-EnviroTra

100\_00323.jpg - North foundation wall down, looking NW



100\_00324.jpg - Excavation at the end of the day, looking north




100\_00325.jpg - Excavation at the end of the day, looking east



**100\_00326.jpg - Close-up of fire main, looking north**



**100\_00327.jpg - Close-up of water main (left) and sewer pipe (right) looking east**

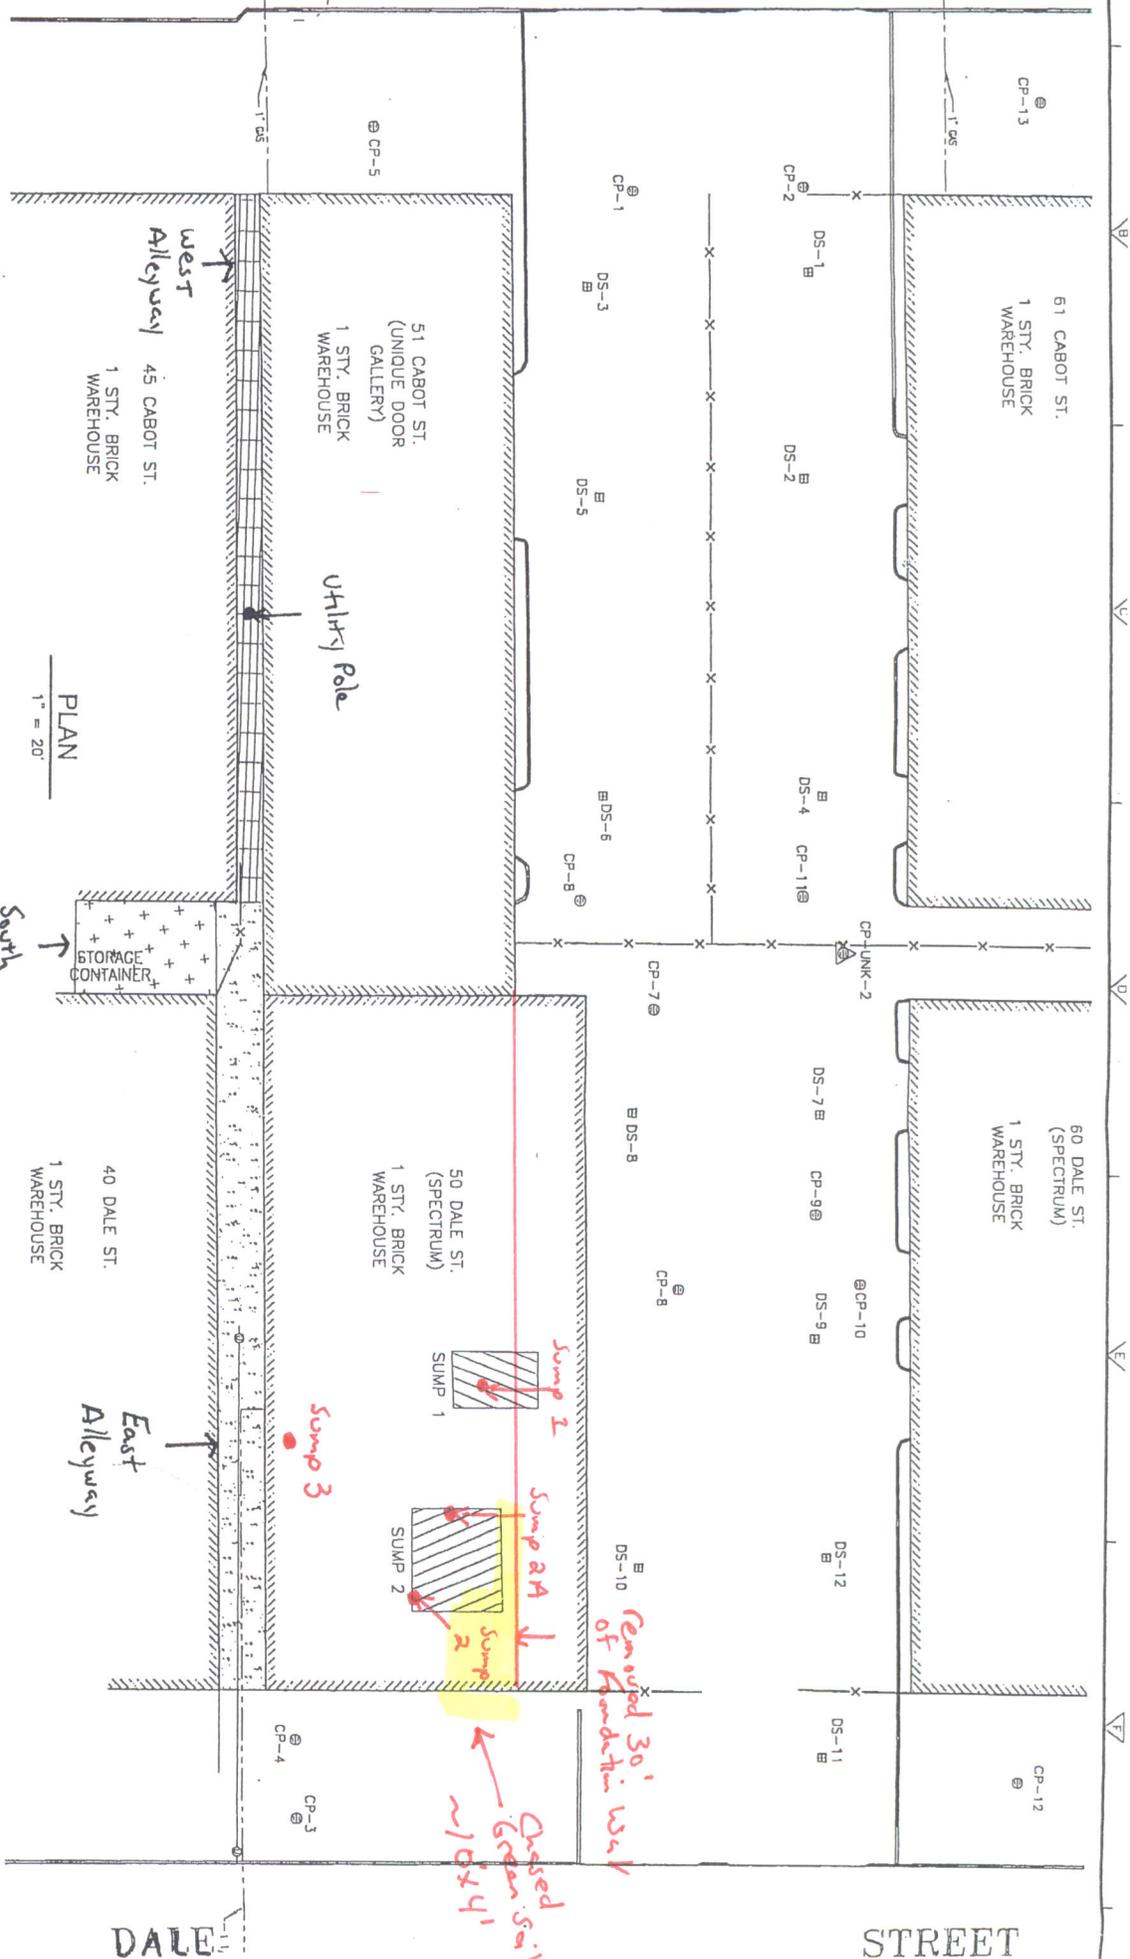

PLAN  
1" = 20'


Work Area

4/3/69

Sump 1  
Sump 2  
Sump 3  
Sump 2A  
Sump 2  
Removed 30' of Foundation W/S  
Graded soil  
~16x4'

DALE

STREET

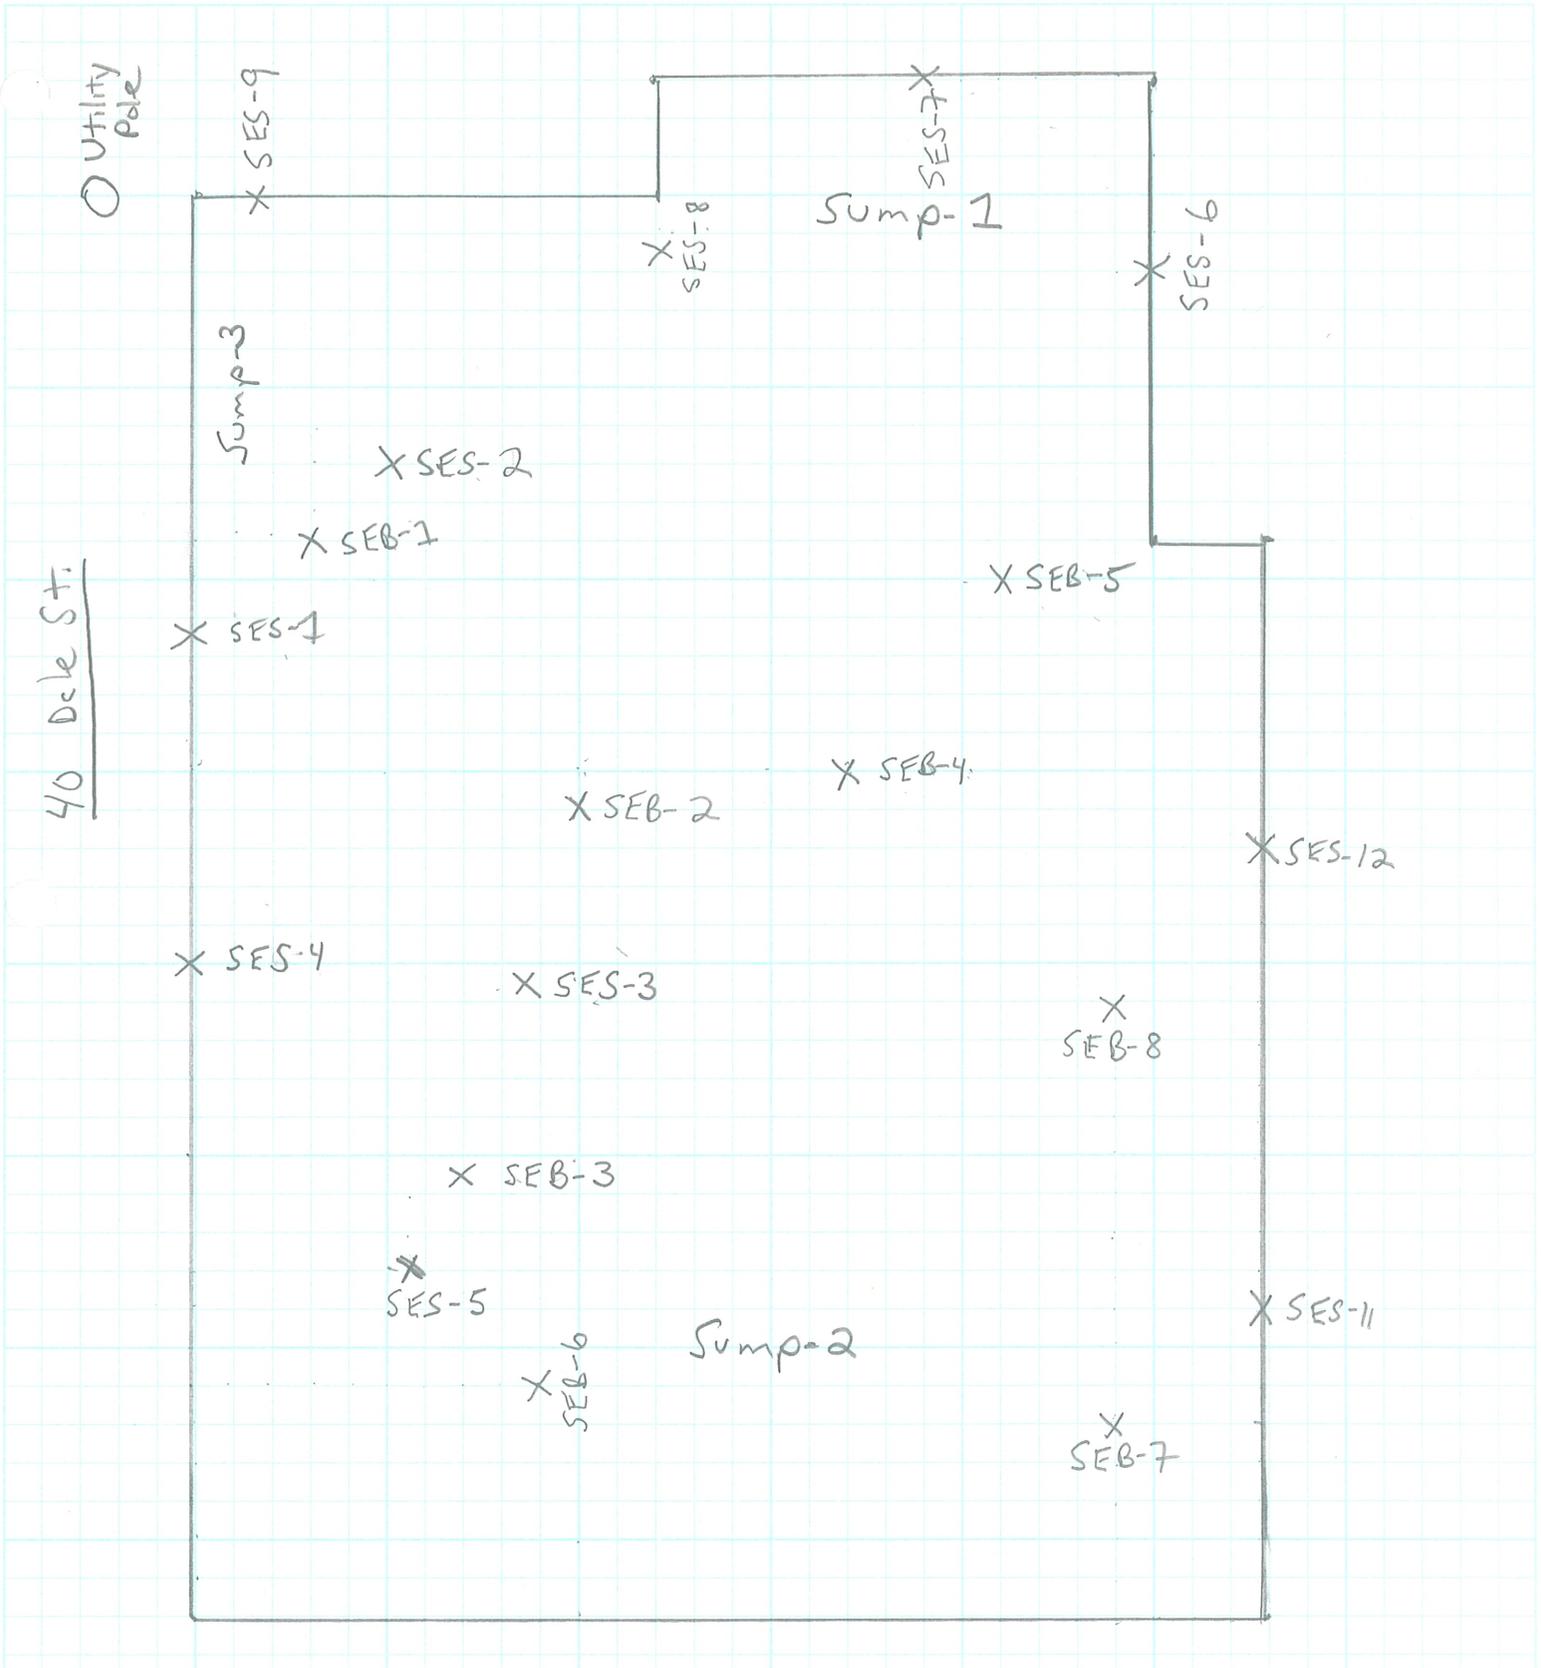

Notes

1 square = 2'  
 SES = Sump Excavation Sidewalk Sample Location  
 SEB = Sump Excavation Bottom Sample Location.

Date St.

X SES-10
