

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	----------	---	----	---	---

 Date: 7-Apr-09
 REPORT No. 116
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		41/47			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x8 hrs	M.Rose
EnviroTrac	Operator	2x8 hrs	B.Byrnes, B.Gimbel
EnviroTrac	Technician	2x8 hrs	R.Maletta, K.Davies
YEC, Inc.	Surveyor	2x2 hr	D. Stedje, J. Chen

EQUIPMENT AT THE SITE

I = Idle W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in modified level D-PPE (tyvek and booties)		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1-Tailgate H&S meeting performed before the start of the work day. 2-2 air monitoring stations for dust and VOC's were set up.
3-Finished excavating the area around SEB-3 and SES-5 and removed the ramp that was built to get to this area. Cleaned up and leveled the south side of the excavation. Removed any remaining concrete and contaminated soil/chunks.
4-Cleaned up around the entire excavation and secured Mt. Spectrum with poly.
5-YEC surveyors on site to survey the excavation. They will give us a rough idea of the size of the excavation and the depths of the deepest points. This will be for certification purposes(extent of contamination) and not for payment purposes.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG
7-Apr-09
CDM Job No. D-006956
Spectrum Finishing Remedial Action
SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0033.jpg	4/7/2009	AM	Excavator excavating ramp that was used to get to SEB-3/SES-5 area
100_00334.jpg	4/7/2009	AM	Finished excavation at the end of the day, looking north
100_00335.jpg	4/7/2009	AM	Finished excavation at the SEB-3/SES-5 area at the end of the day
100_00345.jpg	4/7/2009	AM	Mt. Spectrum at the end of the excavations, awaiting disposal

PHOTOS 4/07/09



100_00333.jpg - Excavator excavating ramp that was used to get to SEB-3/SES-5 area




100_00334.jpg - Finished excavation at the end of the day, looking north.



100_00335.jpg - Finished excavation at the SEB-3/SES-5 area, at the end of the day, looking SE



100_00345.jpg - Mt. Spectrum at the end of excavations, awaiting disposal.

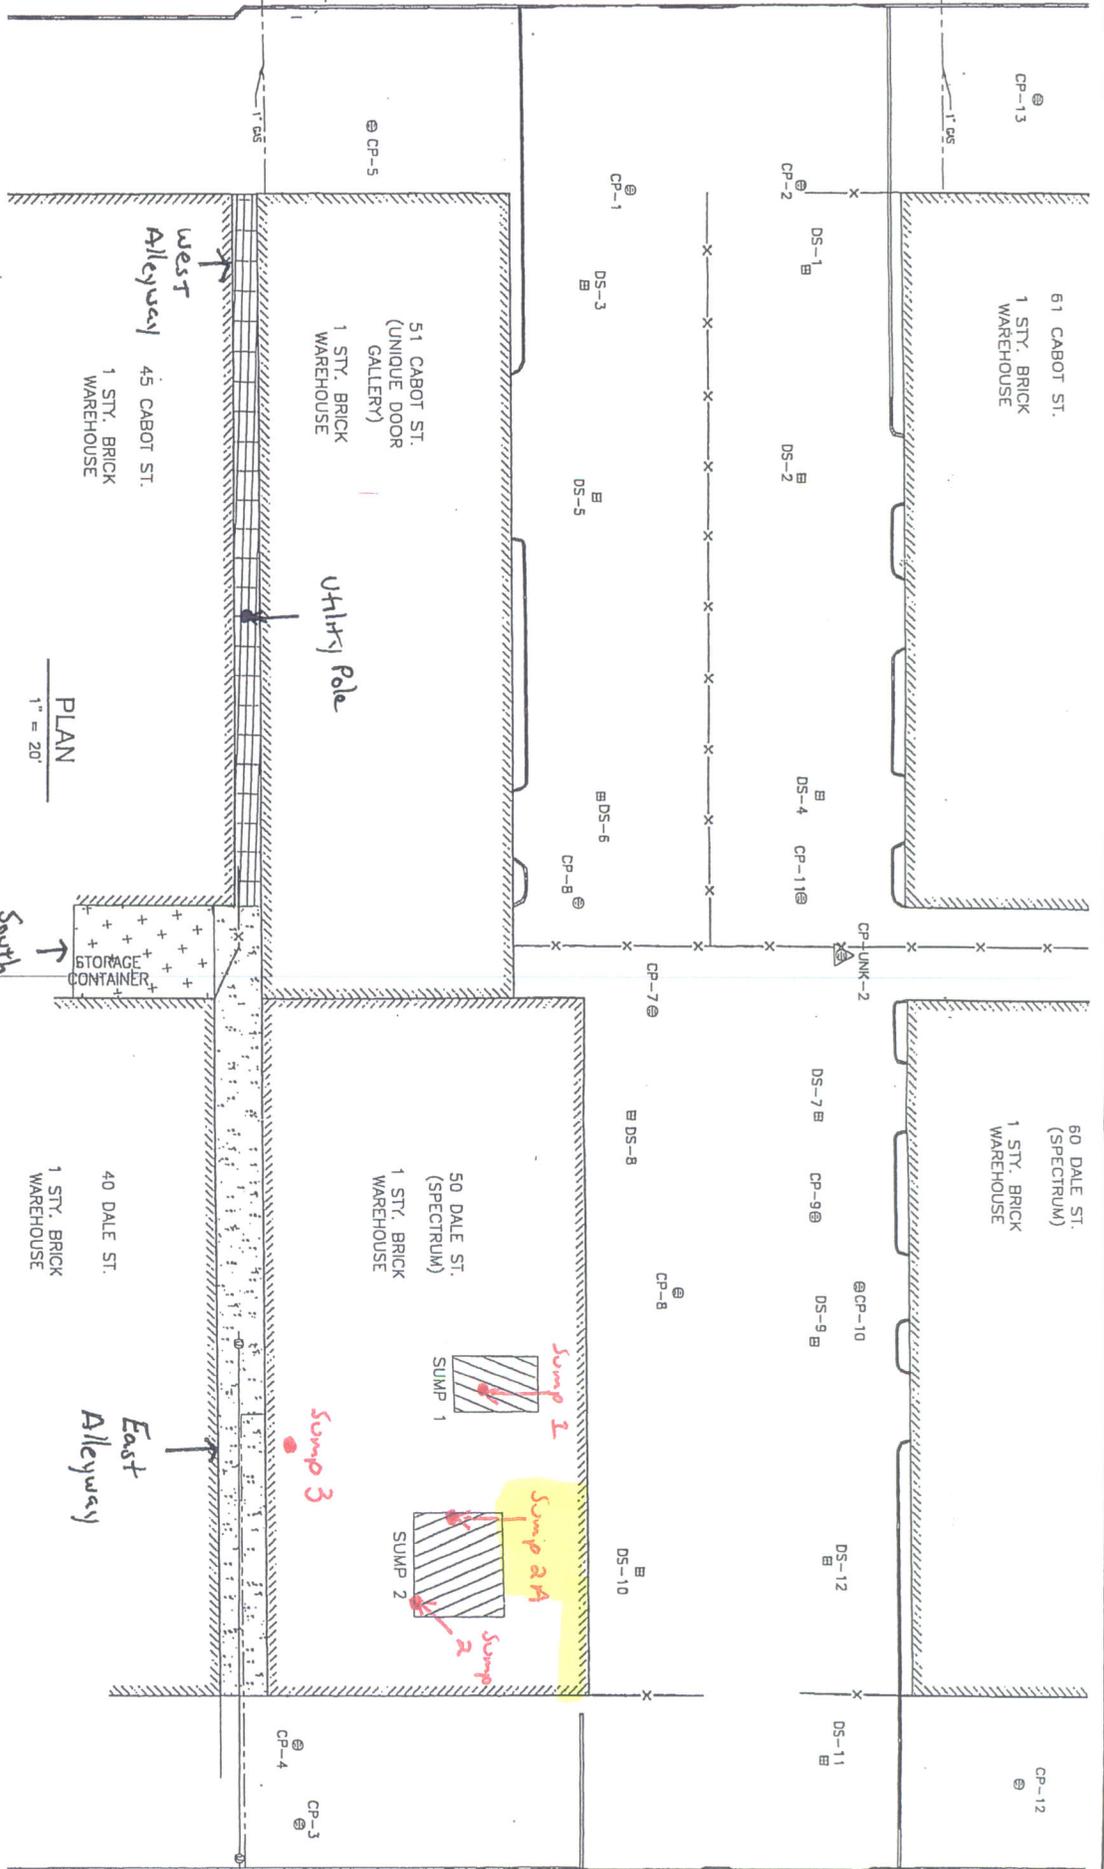

PLAN
1" = 20'

4/2/09

Work Areas

DALE

STREET
