

Project: Spectrum Finishing - Remedial Action  
 Contractor: EnviroTrac Environmental Services  
 CDM Job No: D-006956 Site No. 1-52-029  
 CDM Project Manager: John Blaum

CDM  
 100 Crossways Park West  
 Woodbury, NY 11797  
 Telephone: 516.496.8400  
 Fax: 516.496.8864

**DAILY REPORT**

Day: 

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

  
 Date: 13-May-09  
 REPORT No. 142  
 PAGE No. 1

<b>WEATHER</b>	Clear	Partly Cloudy	Overcast	Rain	Snow
<b>TEMP L/H</b>		46/65			
<b>HUMIDITY</b>	Dry	Moderate	High		
<b>WIND</b>	Calm	Light	Moderate	High	
<b>WIND DIR</b>	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

**AVERAGE FIELD FORCE**

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x8 hrs	M. Rose
EnviroTrac	Operator	1x8 hrs	B.Gimbel
AARCO	Technician	2x8 hrs	M. Bonislawski, A.Sanchez

**EQUIPMENT AT THE SITE** I = Idle W = Working

20" Storage Container - W	AARCO Guzzler Vac Truck - W
Daewoo 450 skidder - I	Earth Care Vac Truck - W
CAT 430E Backhoe -W	

**HEALTH AND SAFETY**

Name	Time (From - To)	Task/Level of PPE
		All workers onsite were in level D-PPE

**CONSTRUCTION ACTIVITIES**

<b>Site Representative:</b> Frank Robinson - CDM
<b>Health and Safety Site Officer:</b> N/A
<b>DESCRIPTION OF WORK PERFORMED AND OBSERVED</b>
1-Tailgate H&S meeting performed before the start of the work day.
2-AARCO cleaned out the following structures of sediment: 51 Cabot St.:DS-3 and 6 (haz soils); 61 Cabot St.: CP-11,
3-EnviroTrac conducted end point sampling on the following structures that were cleaned out:50 Dale St.: CP-3, 4 and 7; 51 Cabot St.:CP-6, DS 3 and 5; 61 Cabot St.:DS-1. Samples were collected with a hand auger, decontaminated between samples and sampled for metals EPA 6010 and 7470 and volatiles EPA 8260.
4-CP-7 (50 Dale St.) the inside of the concrete structure is visibly stained green (from yesterday's report with photo attached).
5-Janet Gremler (SCDHS) was on site to observe the end point sampling, but it was completed by the time she arrived. She was concerned about tracing piping that may go to unknown structures. I told her that it was not in our scope to do this and she will speak to Bryan Grogen about this and possibly send out an e-mail to resolve this.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

**PHOTOGRAPHIC LOG**  
**13-May-09**  
**CDM Job No. D-006956**  
**Spectrum Finishing Remedial Action**  
**SITE No. 1-52-029**

<b>PHOTO</b>	<b>DATE</b>	<b>TIME</b>	<b>DESCRIPTION</b>
100_00589.jpg	5/13/2009	AM	Inside of CP-7, green visibly stained concrete
100_00594.jpg	5/13/2009	AM	EnviroTrac conducting end point sampling of CP-7, 50 Dale St.
100_00600.jpg	5/13/2009	AM	AARCO cleaning out CP-11, 61 Cabot St.

# PHOTOS 5/13/09




100\_00595.jpg - Inside of CP-7, green visibly stained concrete.



100\_00599.jpg - EnviroTrac conducting end point sampling of CP-7 (50 Dale St.)



100\_00600.jpg - AARCO cleaning out CP-11 (61 Cabot St.)

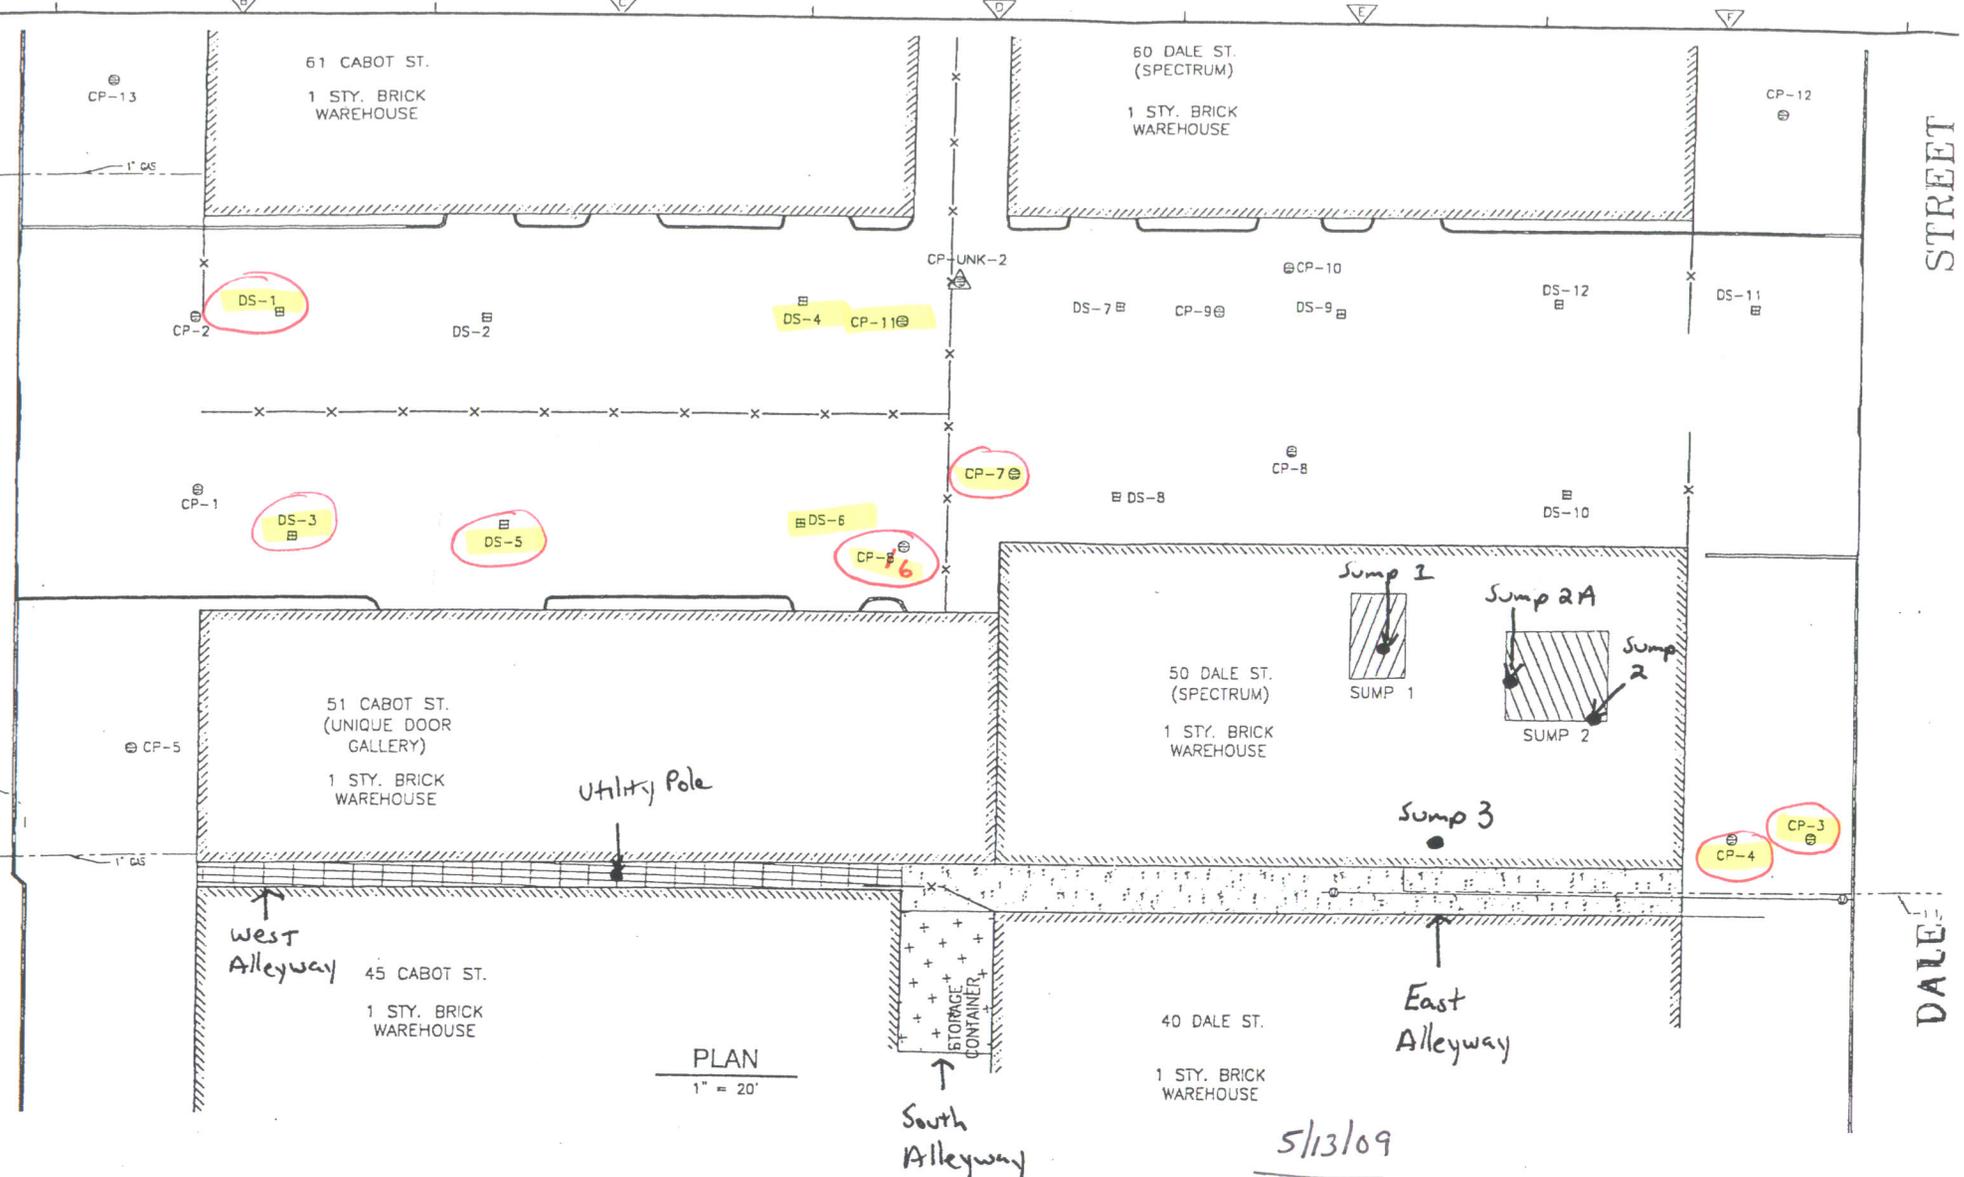

5/13/09

Work Areas

- end point sampling
