

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

| | | | | | | |
|---|---|---|---|----|---|---|
| S | M | T | W | TH | F | S |
|---|---|---|---|----|---|---|

 Date: 29-May-09
 REPORT No. 153
 PAGE No. 1

| | | | | | |
|-----------------|-------|---------------|----------|------|------|
| WEATHER | Clear | Partly Cloudy | Overcast | Rain | Snow |
| TEMP L/H | | 54/64 | | | |
| HUMIDITY | Dry | Moderate | High | | |
| WIND | Calm | Light | Moderate | High | |
| WIND DIR | N | E | S | W | |
| | NE | SE | SW | NW | |

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

| Name of Contractor | Title | Hours Worked | Remarks |
|--------------------|----------------------|--------------|---------------------|
| EnviroTrac | Construction Manager | 1x8 hrs | M.Rose |
| EnviroTrac | Operator | 2x8 hrs | B.Gimbel, J.Byrnes |
| EnviroTrac | Technician | 1x8 hrs | K.Davies |
| Cork and Sons | Operator | 1x3 hrs | G.Cork |
| Cork and Sons | Technician | 2x3 hrs | E.O'Connor, N.Cuomo |
| | | | |
| | | | |

EQUIPMENT AT THE SITE

I = Idle W = Working

| | |
|--------------------------------|--|
| 20" Storage Container - W | Cork and Sons: Mack Dump Truck - I |
| Daewoo 450 skidder - W | Cork and Sons Case 580 Backhoe - I |
| CAT 430E Backhoe -W | Cork and Sons Case CX225SR Excavator - I |
| Case 621C Front End Loader - I | |
| | |
| | |

HEALTH AND SAFETY

| Name | Time (From - To) | Task/Level of PPE |
|------|------------------|--|
| | | All workers onsite were in level D-PPE |

CONSTRUCTION ACTIVITIES

| |
|---|
| Site Representative: Frank Robinson - CDM |
| Health and Safety Site Officer: N/A |
| DESCRIPTION OF WORK PERFORMED AND OBSERVED |
| 1-Tailgate H&S meeting performed before the start of the work day. No air monitoring today due to rain/drizzle all day. |
| 2-Cork and Sons performed the following work at 51 and 61 Cabot St.: Laid out the roof drains where they come out of the building. Could not install the roof drains at 51 and 61 Cabot St. due to the heavy rains this morning. |
| 3-EnviroTrac abandoned the following structures by removing the dome top by dropping it down to the bottom of the structure then backfilling with clean material generated during structure installation: 51 Cabot St.: CP-6; 50 Dale St.:CP-3. |
| |
| |



x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

PHOTOGRAPHIC LOG
29-May-09
CDM Job No. D-006956
Spectrum Finishing Remedial Action
SITE No. 1-52-029

| PHOTO | DATE | TIME | DESCRIPTION |
|--------------|-------------|-------------|--|
| 100_0725.jpg | 5/29/2009 | AM | CP-6, 51 Cabot St., partially abandoned |
| 100_0727.jpg | 5/29/2009 | AM | CP-6, 51 Cabot St., completely abandoned |
| 100_0726.jpg | 5/29/2009 | AM | CP-3, 50 Dale St., partially abandoned |
| 100_0727.jpg | 5/29/2009 | PM | CP-3, 50 Dale St., completely abandoned |
| | | | |
| | | | |
| | | | |

PHOTOS 5/29/09



100_0725.jpg - CP-6, 51 Cabot St., partially abandoned




100_0727.jpg - CP-6, 51 Cabot St., completely abandoned



100_0726pg - CP-3, 50 Dale St., partially abandoned



100_0727.jpg - CP-3, 50 Dale St., completely abandoned

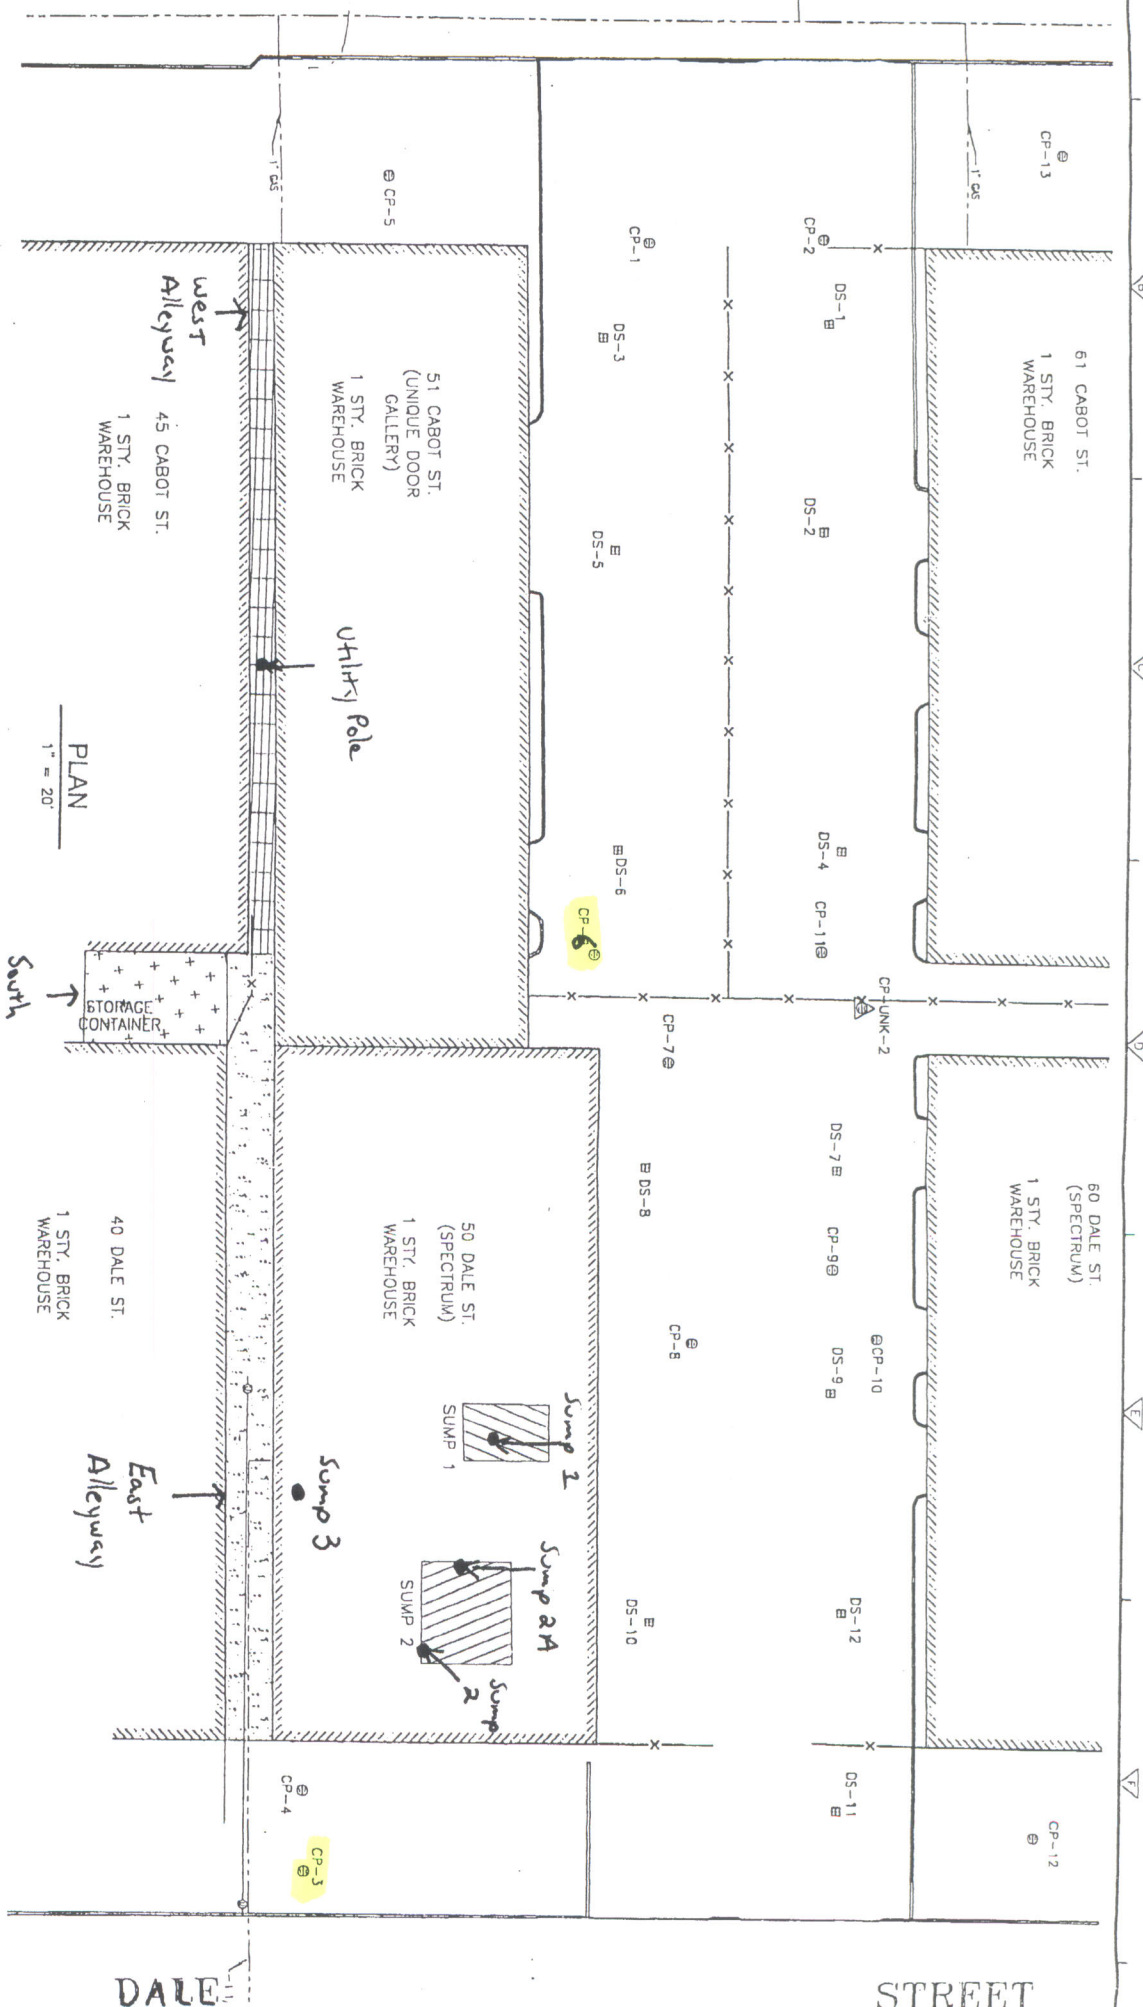


PLAN
1" = 20"

5/29/09

Work Areas

DALE

STREET

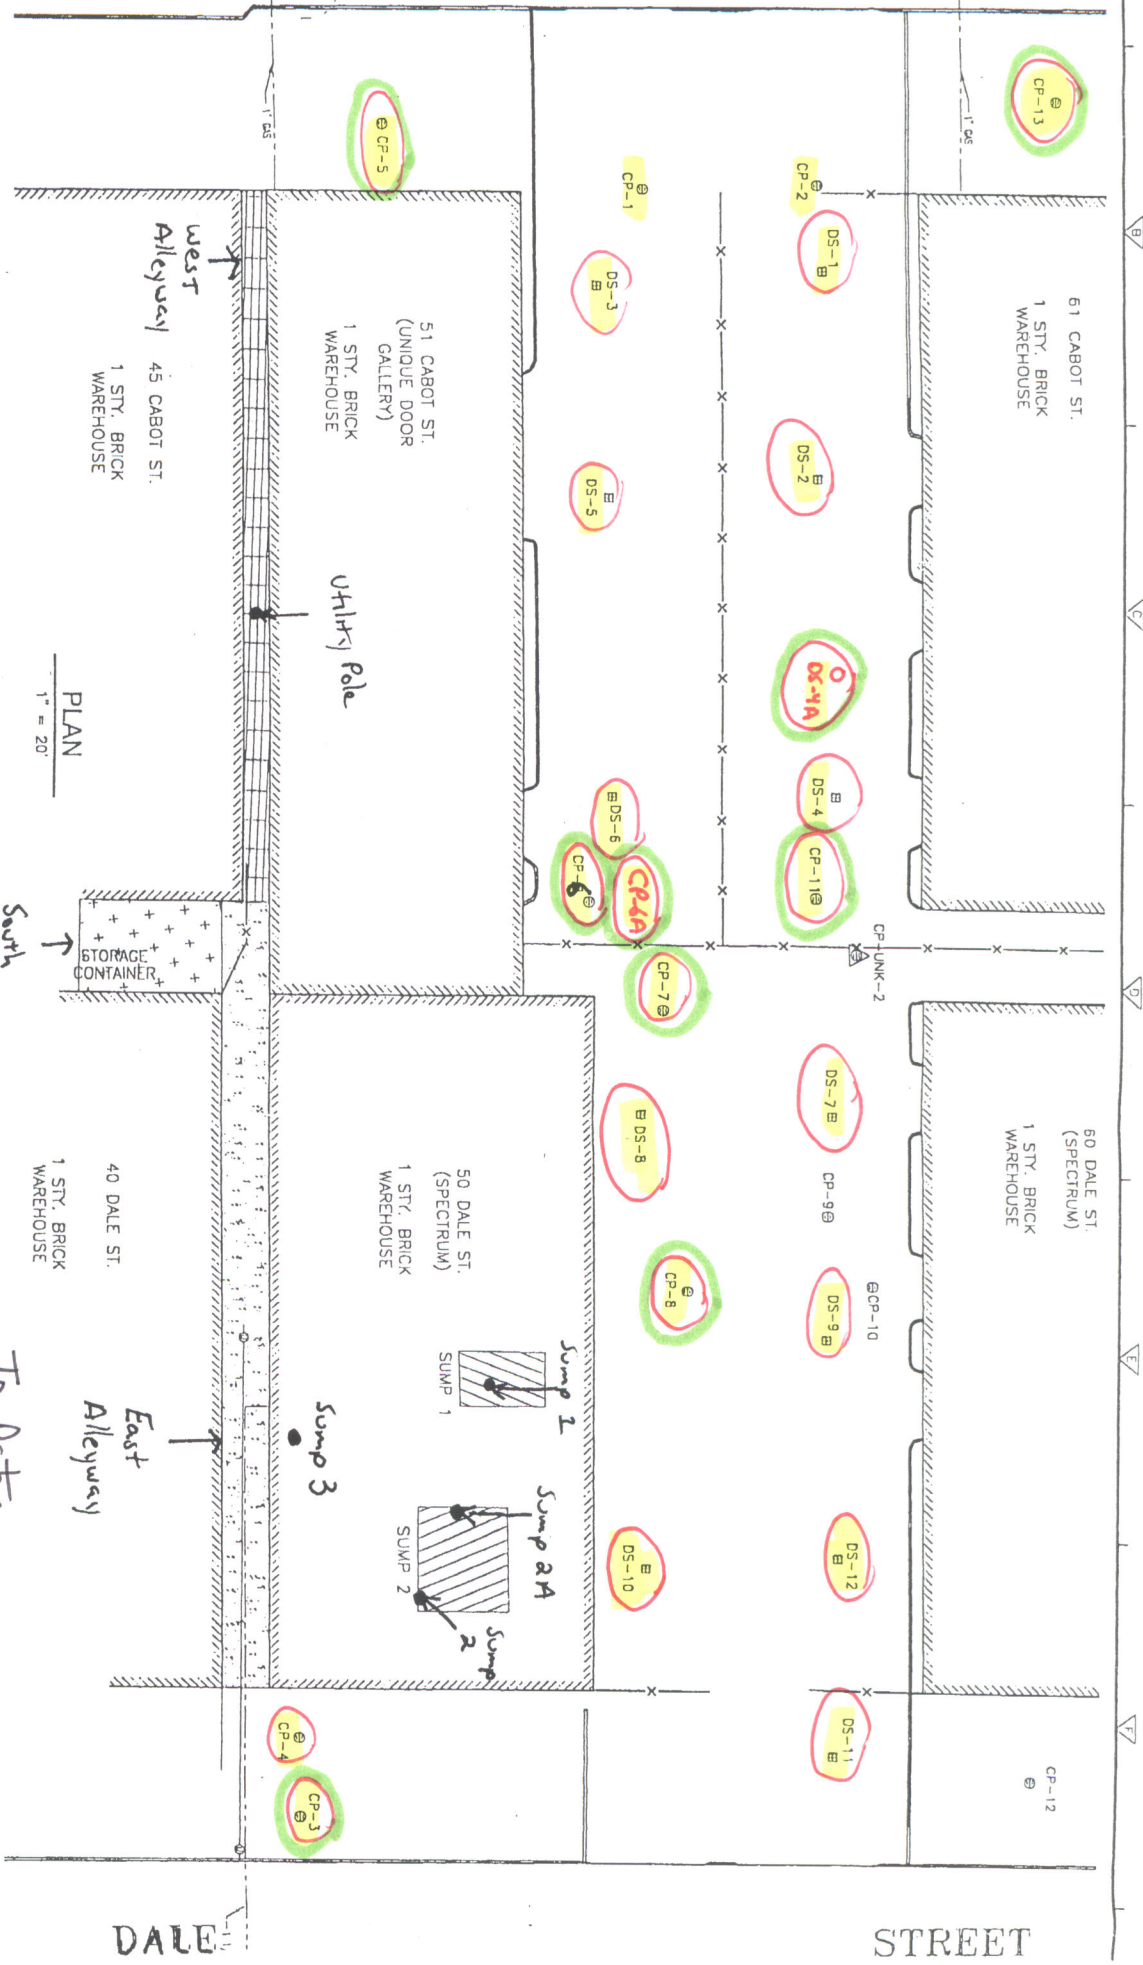

- To Date:**
- Structures cleaned out
 - end point sampled
 - Abandoned

DALE STREET
