

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

| | | | | | | |
|---|---|---|---|----|---|---|
| S | M | T | W | TH | F | S |
|---|---|---|---|----|---|---|

 Date: 11-Jun-09
 REPORT No. 162
 PAGE No. 1

| | | | | | |
|-----------------|-------|---------------|------------------|------|------|
| WEATHER | Clear | Partly Cloudy | Overcast/Drizzle | Rain | Snow |
| TEMP L/H | | 59/67 | | | |
| HUMIDITY | Dry | Moderate | High | | |
| WIND | Calm | Light | Moderate | High | |
| WIND DIR | N | E | S | W | |
| | NE | SE | SW | NW | |

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

| Name of Contractor | Title | Hours Worked | Remarks |
|--------------------|----------------------|--------------|----------|
| EnviroTrac | Construction Manager | 1x8 hrs | M.Rose |
| EnviroTrac | Operator | 1x8 hrs | J.Byrnes |
| EnviroTrac | Technician | 1x8 hrs | K.Davies |
| | | | |
| | | | |
| | | | |

EQUIPMENT AT THE SITE I = Idle W = Working

| | |
|--------------------------------|--|
| 20" Storage Container - W | |
| Case 621C Front End Loader - W | |
| CAT 430E Backhoe - W | |
| CAT 226B skidder - W | |
| | |
| | |
| | |

HEALTH AND SAFETY

| Name | Time (From - To) | Task/Level of PPE |
|------|------------------|--|
| | | All workers onsite were in level D-PPE |

CONSTRUCTION ACTIVITIES

| |
|---|
| Site Representative: Frank Robinson - CDM |
| Health and Safety Site Officer: N/A |
| DESCRIPTION OF WORK PERFORMED AND OBSERVED |
| 1- Tailgate H&S meeting performed before the start of the work day. |
| 2-EnviroTrac abandoned the following structures by breaking the dome top into the structure and backfilling with clean on-site material: 60 Dale St.: DS-7 and DS-12. This completes structure abandonment. |
| 3-EnviroTrac loaded 5 roll offs (provided by AARCO): 2 of concrete and 3 of asphalt as C&D for disposal at South Shore Materials. |
| 4-Olson Nursery delivered 1 truck load of backfill material and 1 truck load of RCA. |
| 5- Progress Meeting #18 was held in the site trailer |

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 06/11/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

| PHOTO | DATE | TIME | DESCRIPTION |
|--------------|-------------|-------------|---|
| 100_0806.jpg | 6/11/2009 | AM | Starting abandonment of DS-7, 60 Dale St. |
| 100_0807.jpg | 6/11/2009 | AM | Abandonment completed of DS-7, 60 Dale St. |
| 100_0809.jpg | 6/11/2009 | AM | Abandonment completed of DS-12, 60 Dale St. |
| | | | |
| | | | |
| | | | |
| | | | |

PHOTOS 6-11-09




100_0806.jpg - Starting abandonment of DS-7, 60 Dale St.




100_0807.jpg - Abandonment complete of DS-7, 60 Dale St.



100_0809.jpg - Abandonment complete at DS-12, 60 Dale St.

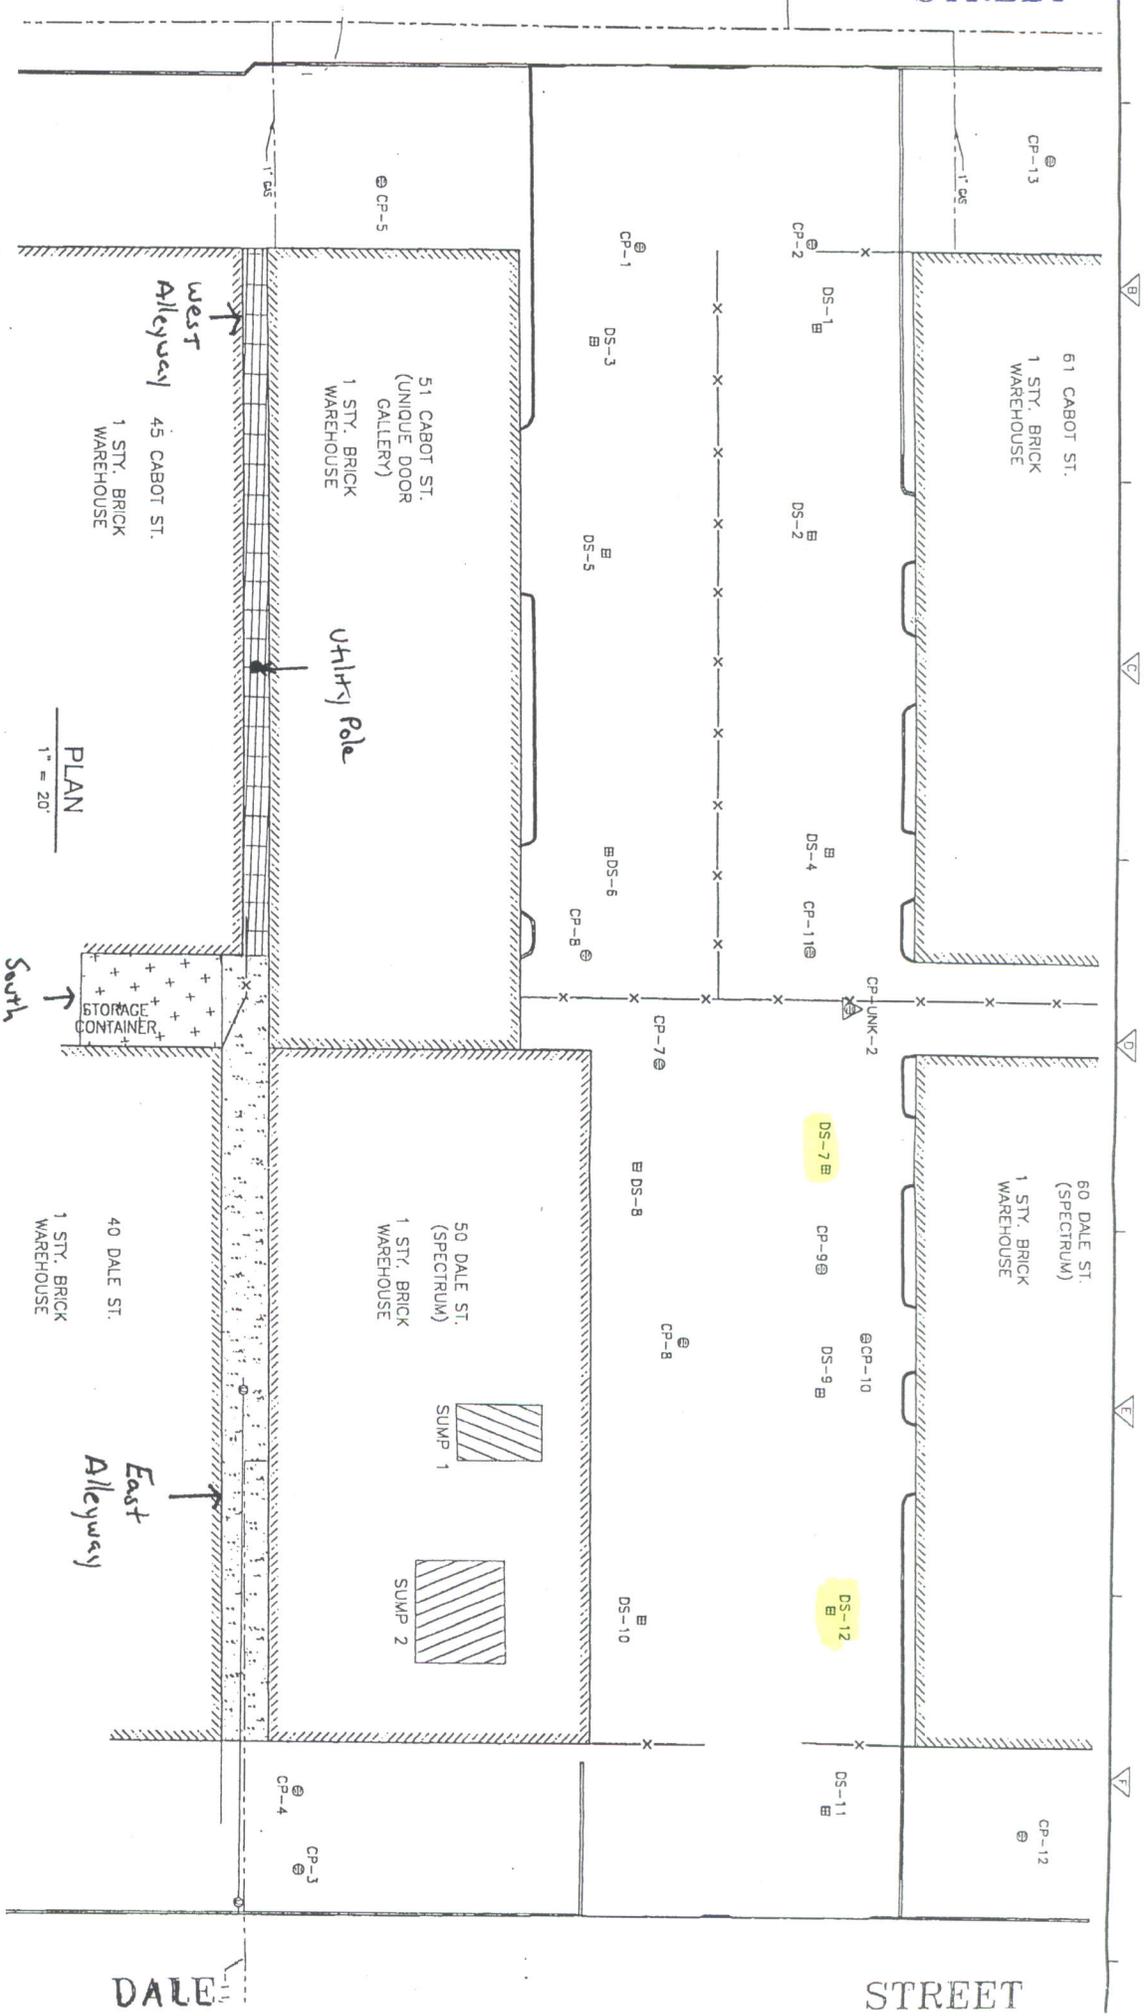

6/11/09
Work Areas

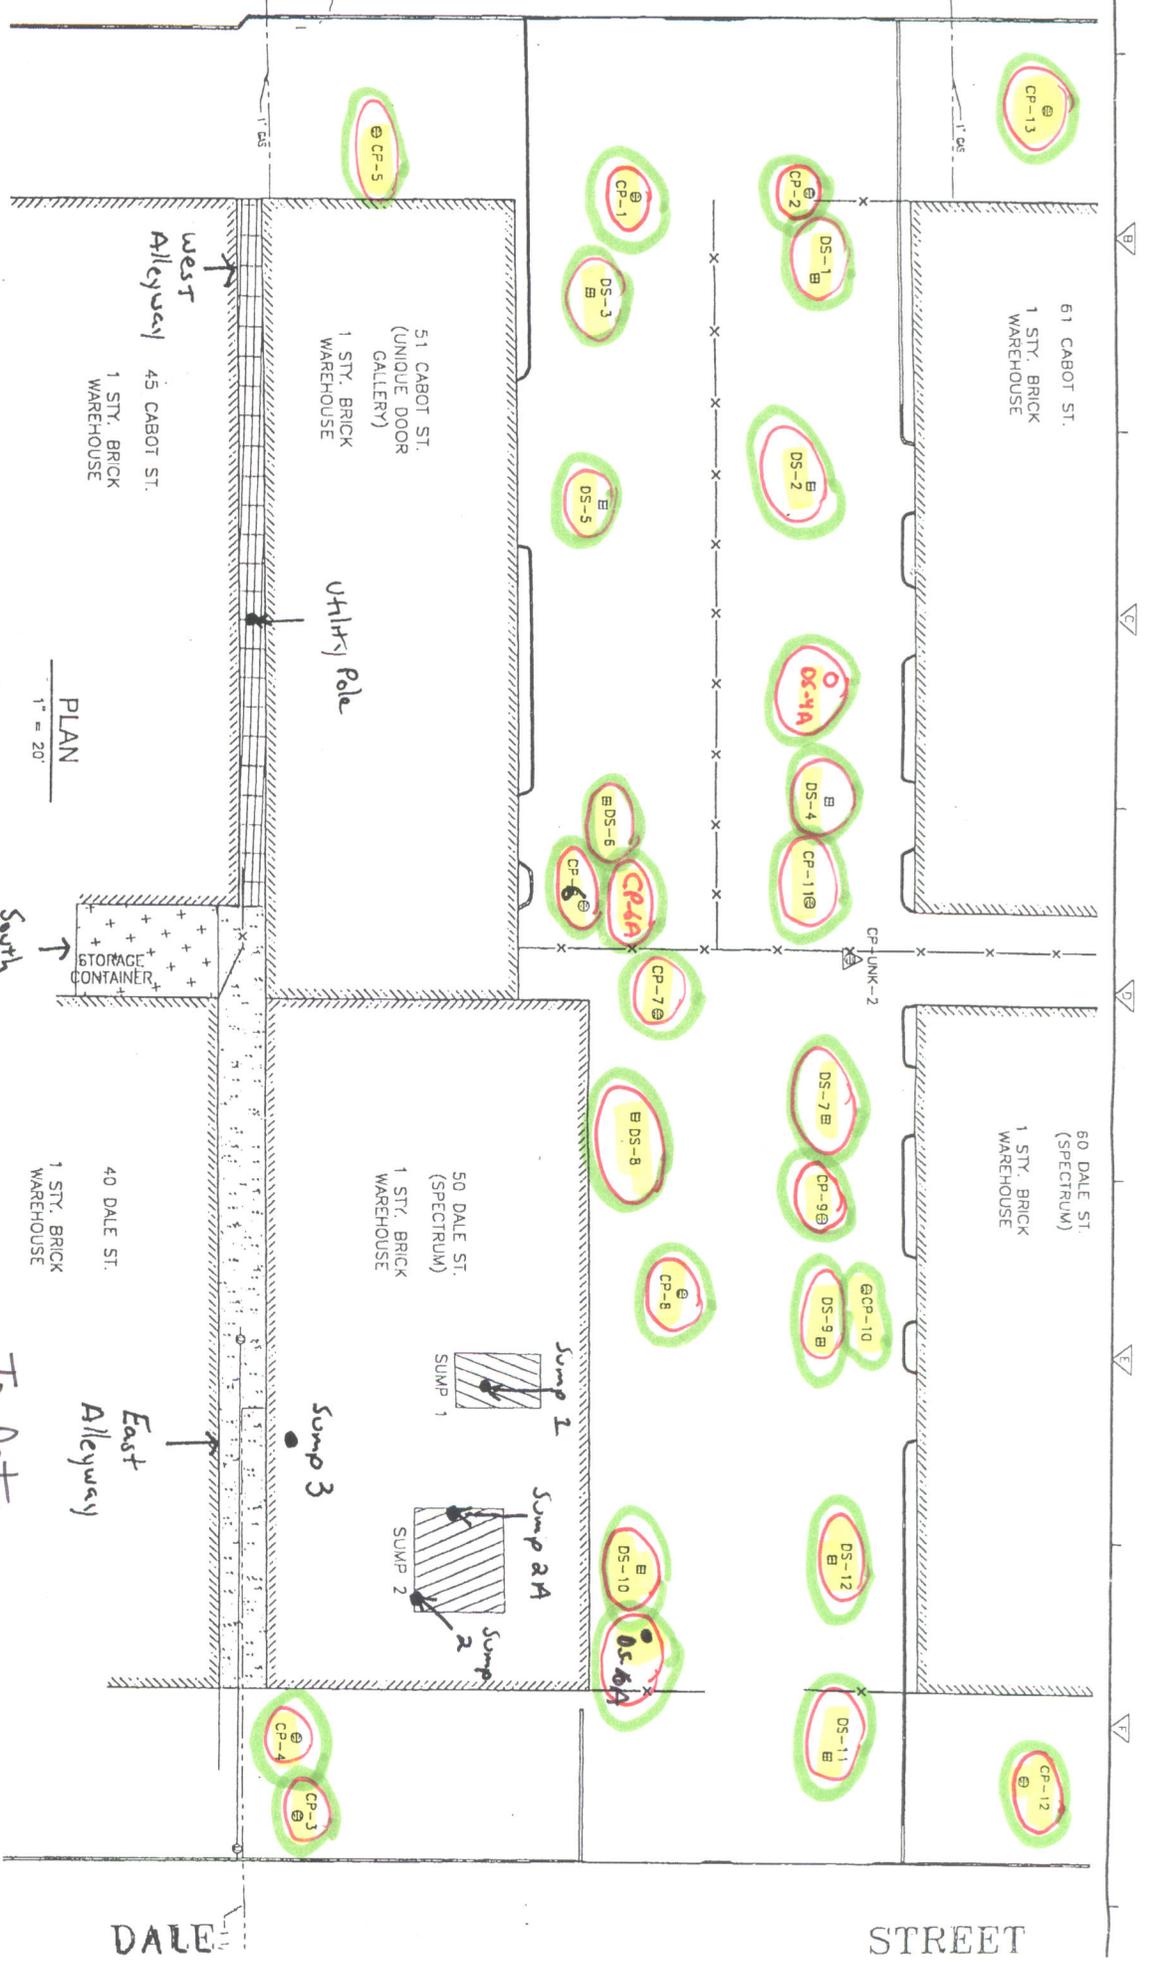

PLAN
1" = 20'

South Alleyway

East Alleyway

- To Date:**
- Structures cleaned out
 - end point sampled
 - Abandoned

NOTE

CP-10 not sampled, it was a tank

DALE

STREET
