

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 18-Jun-09
 REPORT No. 167
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		63/67			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x8 hrs	M.Rose
EnviroTrac	Operator	1x8 hrs	J.Byrnes
EnviroTrac	Technician	1x8 hrs	K.Davies
AARCO	Technician	3x1 hrs	C.Blumberg, M.Buskey, J.Ramos

EQUIPMENT AT THE SITE I = Idle W = Working

20" Storage Container - W	
Case 621C Front End Loader - I	
CAT 430E Backhoe - W	
CAT 226B skidder - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
		All workers onsite were in level D-PPE

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1- Tailgate H&S meeting performed before the start of the work day.
2-EnviroTrac lined the UST-5/9 excavation with filter fabric to delineate the excavation. The excavation was then backfilled and compacted. Watral Brothers delivered 2 truck loads of backfill material, 39.14 tons +41.77 tons = 80.91 tons. A final layer of 6" of RCA was installed and compacted.
3-EnviroTrac finished spreading 2-4" of topsoil to the front of 60 Dale St.
4-Mr.Michael Bavaro, Jr. of City & County Paving Corp. was on site to look over the site and to submit an estimate to grade and pave the site.
5-AARCO on site to pick up road plates and safety cones and barrels.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 06/18/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0844.jpg	6/18/2009	AM	Finished spreading topsoil in front of 60 Dale St.
100_0845.jpg	6/18/2009	AM	Starting to backfill and compact UST-5/9 excavation
100_0846.jpg	6/18/2009	AM	Almost completed backfilling and compacting excavation, needs more RCA

PHOTOS 6-18-09




100_0844.jpg - Finished spreading topsoil in front of 60 Dale St.



100_0845.jpg - Starting to backfill and compact UST-5/9 excavation



100_0846.jpg - Almost finished backfilling excavation, still need to add more
RCA

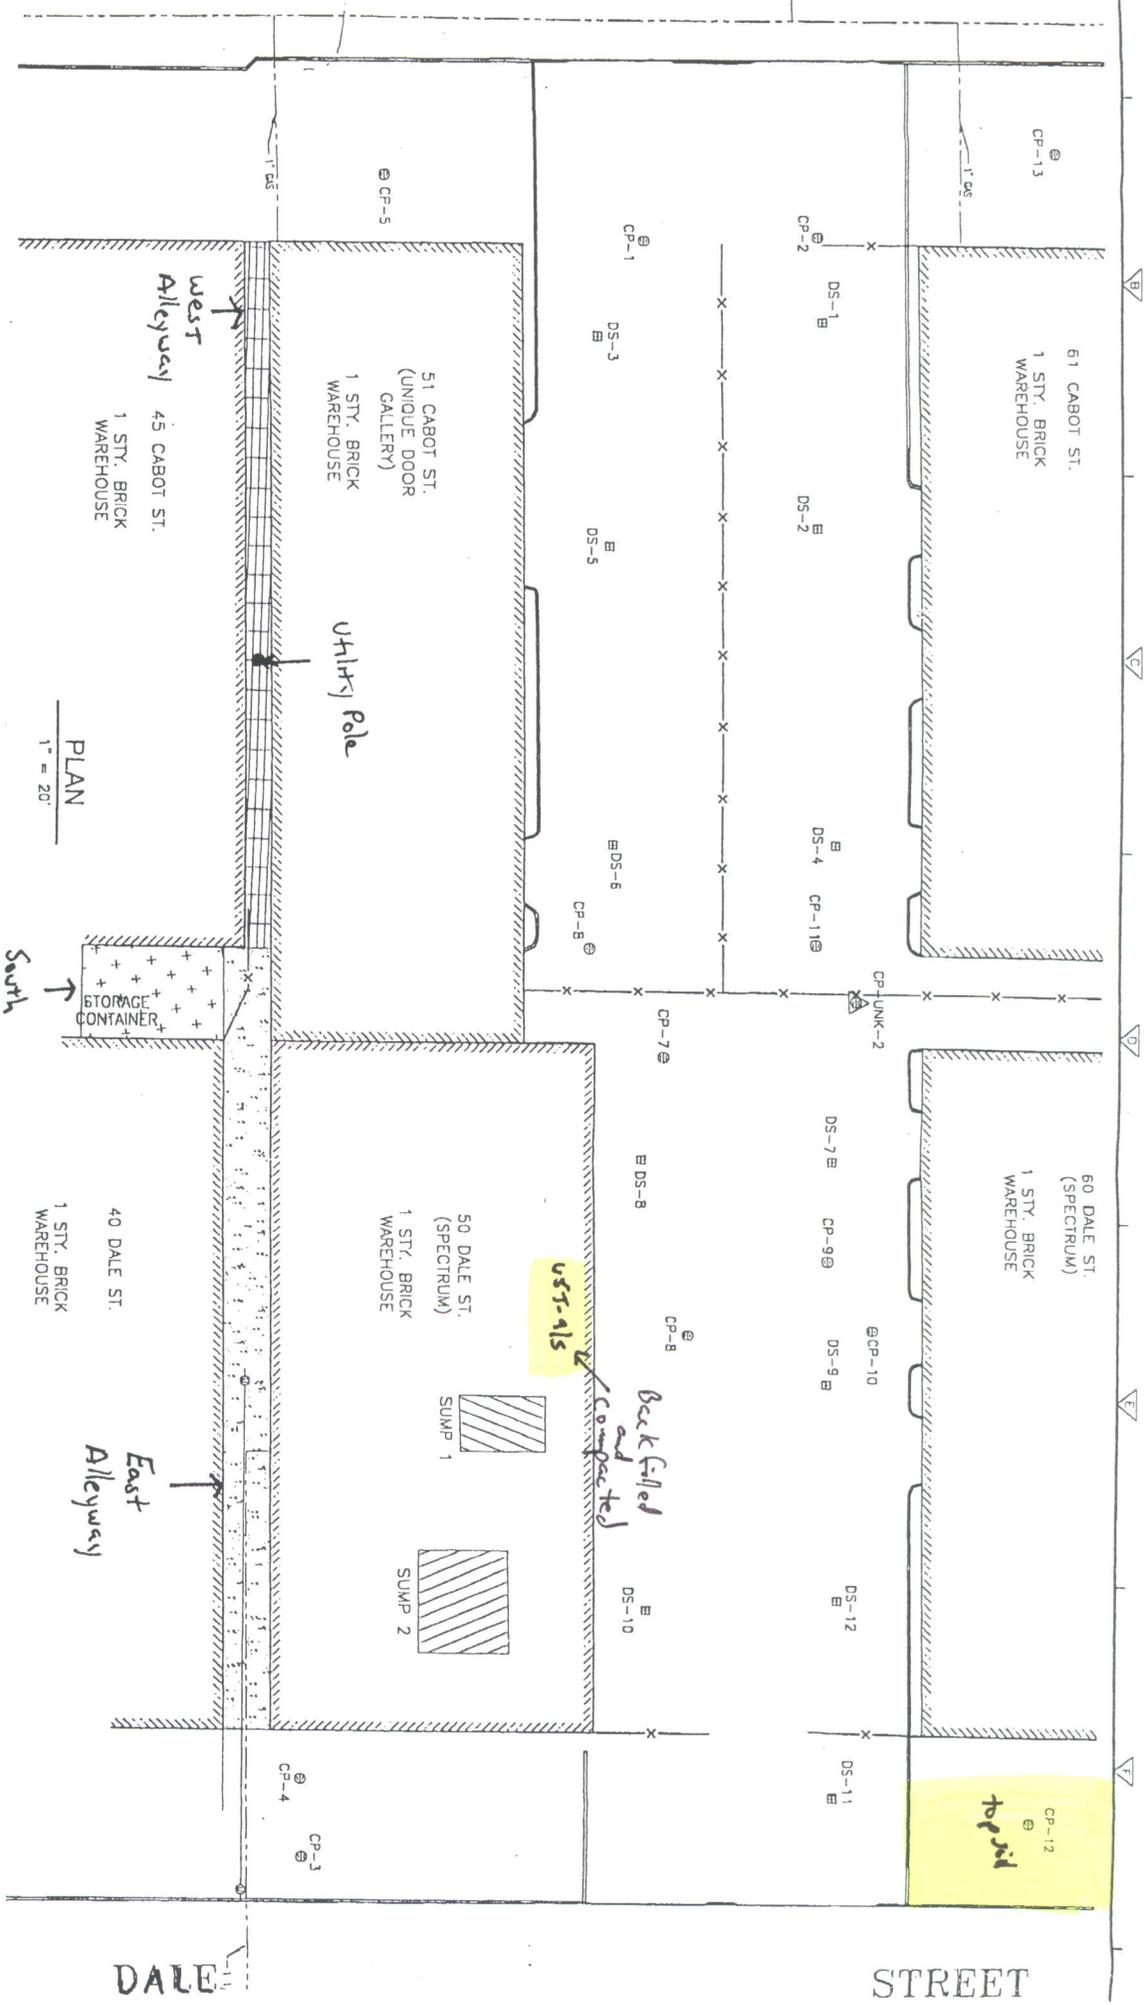

PLAN
1" = 20'

6/15/09
Work Areas

DALE

STREET

WATRAL BROTHERS INC
45 SOUTH 4th STREET
BAY SHORE, NY 11706

PHONE (631) 586-8300

FAX (631) 586-8335

78379 X


DATE 6/18/09

NAME Envior Truck

ADDRESS Dale St
Kermingdale #05

Screened Sand	
115940	
38280	
37 ^{GG} Tons	

CURB DELIVERIES ONLY
OTHERS AT CUSTOMER'S RISK

ACCEPTED BY 

WATRAL BROTHERS
45 S. 4TH STREET
BAY SHORE, NY
631-586-8300
07:35
06-18-2009
TRK ID: WB05
CN: 478
115940 G lb
37660 T lb Mem_Wt
78280 N lb

**WATRAL BROTHERS INC
45 SOUTH 4th STREET
BAY SHORE, NY 11706**

PHONE (631) 586-8300

FAX (631) 586-8335

78380 X

DATE 6/18/09

NAME Envior Trak

ADDRESS Dale St.

Farmingdale tw

Screened Sand

121200

37660

41 77 Tons

**CURB DELIVERIES ONLY
OTHERS AT CUSTOMER'S RISK**

ACCEPTED BY _____

WATRAL BROTHERS
45 S. 4TH STREET
BAY SHORE, NY
631-586-8300

08:42

06-18-2009

TRK ID: WB05

CN: 482

121200 G lb

37660 T lb Mem_Wt

83540 N lb
