

Project: Spectrum Finishing - Remedial Action  
 Contractor: EnviroTrac Environmental Services  
 CDM Job No: D-006956 Site No. 1-52-029  
 CDM Project Manager: John Blaum

CDM  
 100 Crossways Park West  
 Woodbury, NY 11797  
 Telephone: 516.496.8400  
 Fax: 516.496.8864

### DAILY REPORT

Day: 

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

  
 Date: 8-Jul-09  
 REPORT No. 180  
 PAGE No. 1

<b>WEATHER</b>	Clear	Partly Cloudy	Overcast	Rain	Snow
<b>TEMP L/H</b>		59/76			
<b>HUMIDITY</b>	Dry	Moderate	High		
<b>WIND</b>	Calm	Light	Moderate	High	
<b>WIND DIR</b>	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

#### AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction manager	1x8 hrs	M.Rose
Accurate Blacktop	Operator	2x8 hrs	D.Flores, T. Saladino
Accurate Blacktop	Laborer	4x8 hrs	R.Nolasco, M.Scioli, R.Jimenez, J.Castro
Accurate Blacktop	Laborer	3x8 hrs	R.Soto, M.Blanco, M.Andasol

#### EQUIPMENT AT THE SITE      I = Idle      W = Working

20" Storage Container - I	Accurate - Case 570 MXT Loader w/ Grading Box - W
Accurate - Mack Dump truck - W	
Accurate - Case 590 Backhoe - W	
Accurate-Dynapac Roller/Compactor-W	

#### HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
		All workers onsite were in level D-PPE

#### CONSTRUCTION ACTIVITIES

<b>Site Representative:</b> Frank Robinson - CDM
<b>Health and Safety Site Officer:</b> N/A
<b>DESCRIPTION OF WORK PERFORMED AND OBSERVED</b>
1- A H&S tailgate meeting was held before the start of work.
2-Accutate Blacktop removed the rest of the asphalt and re-graded and compacted the site with RCA in preparation for paving the 2" asphalt binder course tomorrow.
3-Manole covers for the drainage and septic structures were raised as needed to the required elevation.
4-Removed concrete apron by entrance to 51 and 61 Cabot St.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson      Project Manager: John Blaum

**PHOTOGRAPHIC LOG**

**Date: 07/08/09**

**CDM Job No. D-006956**

**Spectrum Finishing Remedial Action**


**SITE No. 1-52-029**

<b>PHOTO</b>	<b>DATE</b>	<b>TIME</b>	<b>DESCRIPTION</b>
100_0937.jpg	7/8/2009	AM	Accurate Blacktop removing the last of the asphalt, looking west
100_0938.jpg	7/8/2009	AM	Accurate Blacktop removing the 51 Cabot St. concrete apron
100_0939.jpg	7/8/2009	AM	Accurate Blacktop raising manhole covers by the side of 60 Dale St.
100_0940.jpg	7/8/2009	PM	Accurate Blacktop spreading RCA at 61 Cabot St.
100_0941.jpg	7/8/2009	PM	Accurate Blacktop grading and compacting RCA, looking east

# PHOTOS 7-08-09



100\_0937.jpg - Accurate Blacktop removing the last of the asphalt, looking west

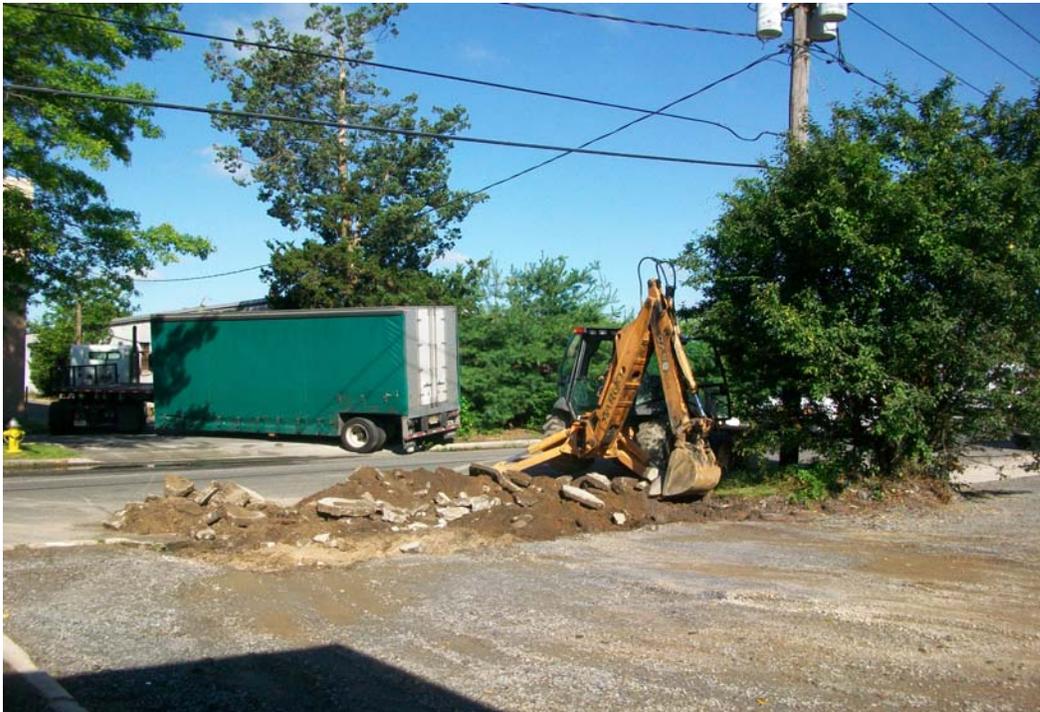

100\_0938.jpg - Accurate Blacktop removing the 51 Cabot St. concrete apron



**100\_0939.jpg - Accurate Blacktop raising the manhole covers by the side of 60 Dale St.**




**100\_0940.jpg - Accurate Blacktop spreading RCA at 61 Cabot St.**



**100\_0941 - Accurate Blacktop grading and compacting RCA, looking east**

B C D E F

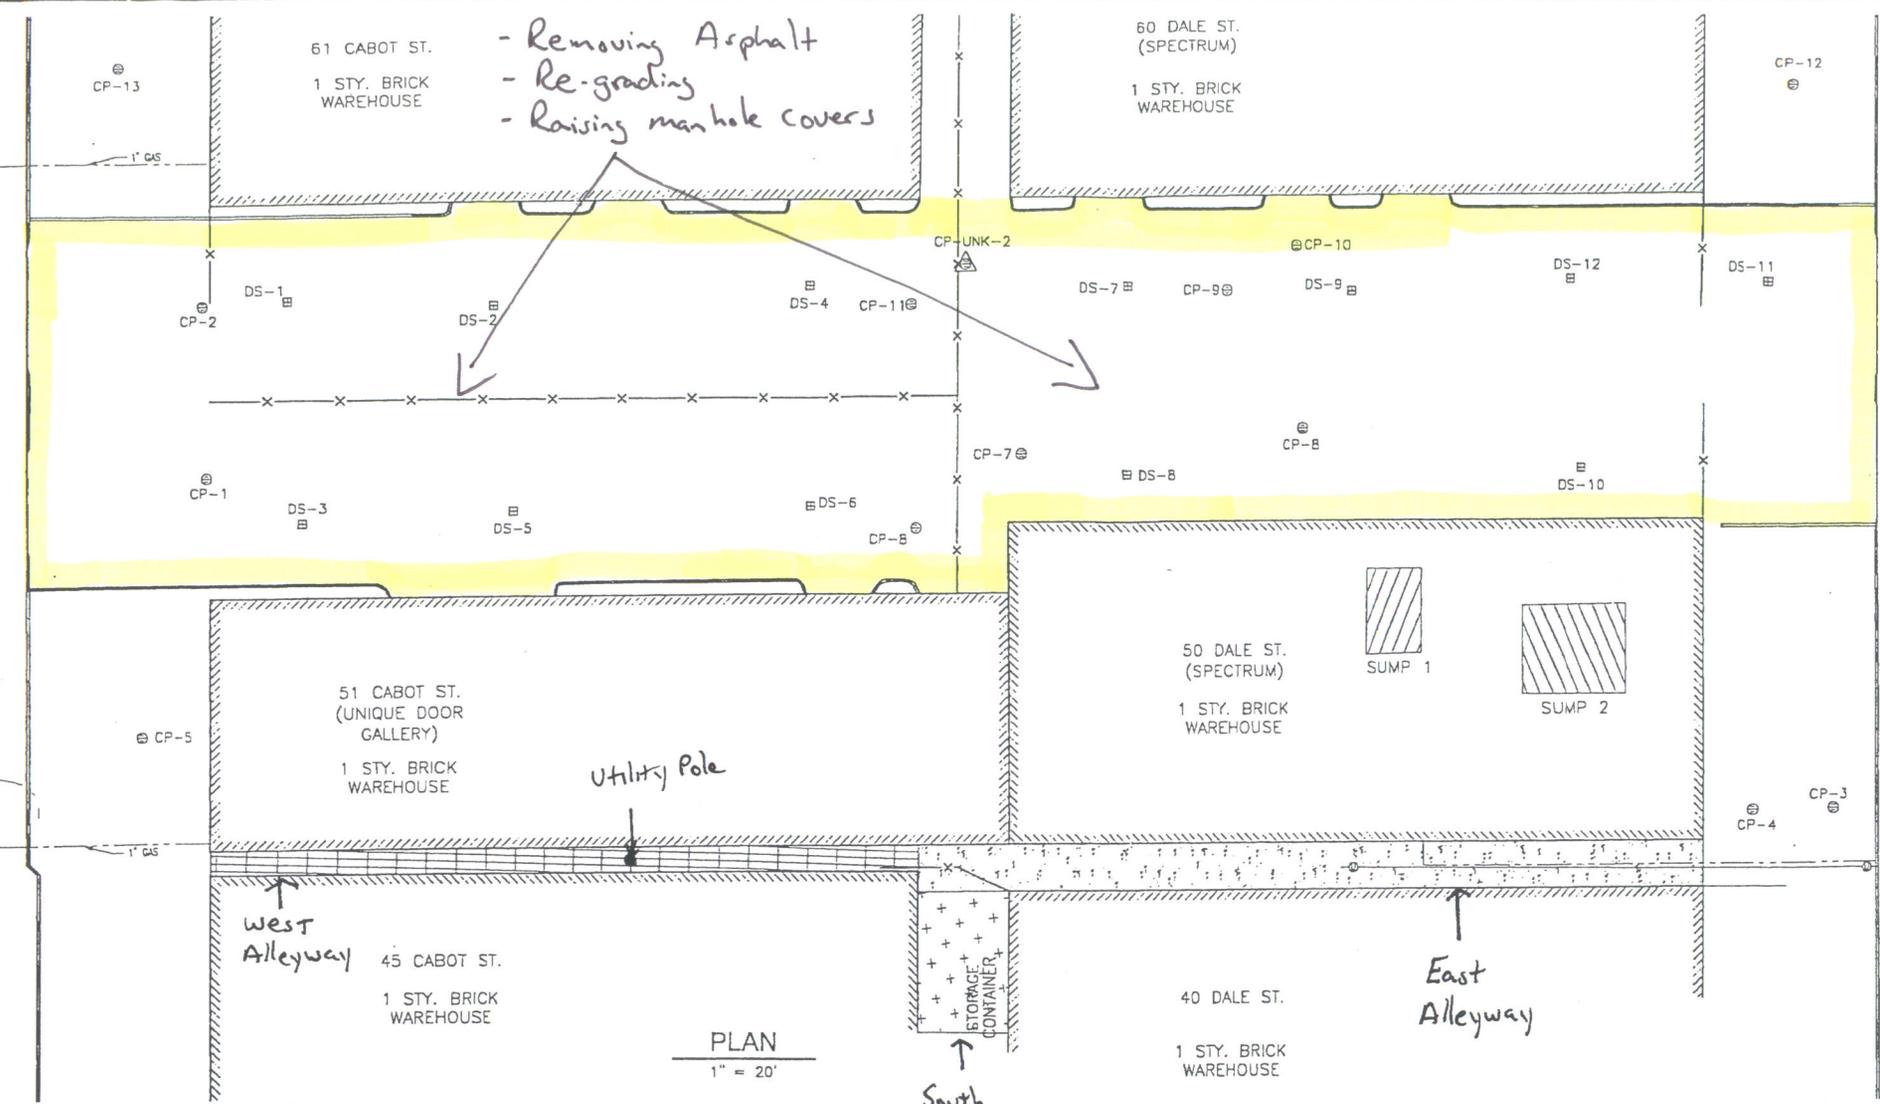

- Removing Asphalt
- Re-grading
- Raising manhole covers

PLAN  
1" = 20'

7/8/09

Work Area

STREET

DALE
