

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 14-Jul-09
 REPORT No. 184
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		64/79			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction manager	1x8 hrs	M.Rose
EnviroTrac	Operator	1x8 hrs	B.Gimbel
EnviroTrac	Technician	1x8 hrs	K.Davies
Double Eagle Fencing	Supervisor	1x8 hrs	S.Vricciariello
Double Eagle Fencing	Laborer	1x8 hrs	V.Mendoza

EQUIPMENT AT THE SITE

I = Idle W = Working

20" Storage Container - W	
Daewoo 450 Skid Steer - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in level D-PPE		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1- A H&S tailgate meeting was held before the start of work.
2-Double Eagle Fencing installed fence fabric: between 50/60 Dale St., 51/61 Cabot St., 61 Cabot St. and 60 Dale St. and 50 Dale St. and 51 Cabot St. Installed fence posts at the front of 50 Dale St.
3-EnviroTrac: repaired the sidewalk in front of 51 Cabot St. by jacking up the sidewalk section and inserting RCA to raise the sidewalk to the proper elevation; removed the fence between the field trailer and Dale St. and cleaned up the front of 50 Dale St.



x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 07/14/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0956.jpg	7/14/2009	AM	Fence fabric installed between 50/60 Dale St.
100_0957.jpg	7/14/2009	AM	Sidewalk repaired in front of 51 Cabot St.
100_0958.jpg	7/14/2009	AM	Fence fabric installed between 51/61 Cabot St.
100_0959.jpg	7/14/2009	AM	Fence fabric installed between 60 Dale St. and 61 Cabot St.

PHOTOS 7-14-09



100_0956.jpg - Fence fabric installed between 50/60 Dale St.




100_0957.jpg - Side walk repaired in front of 51 Cabot St.



100_0958.jpg - Fence fabric installed between 51/61 Cabot St.



100_0959.jpg - Fence fabric installed between 60 Dale St. & 61 Cabot St.

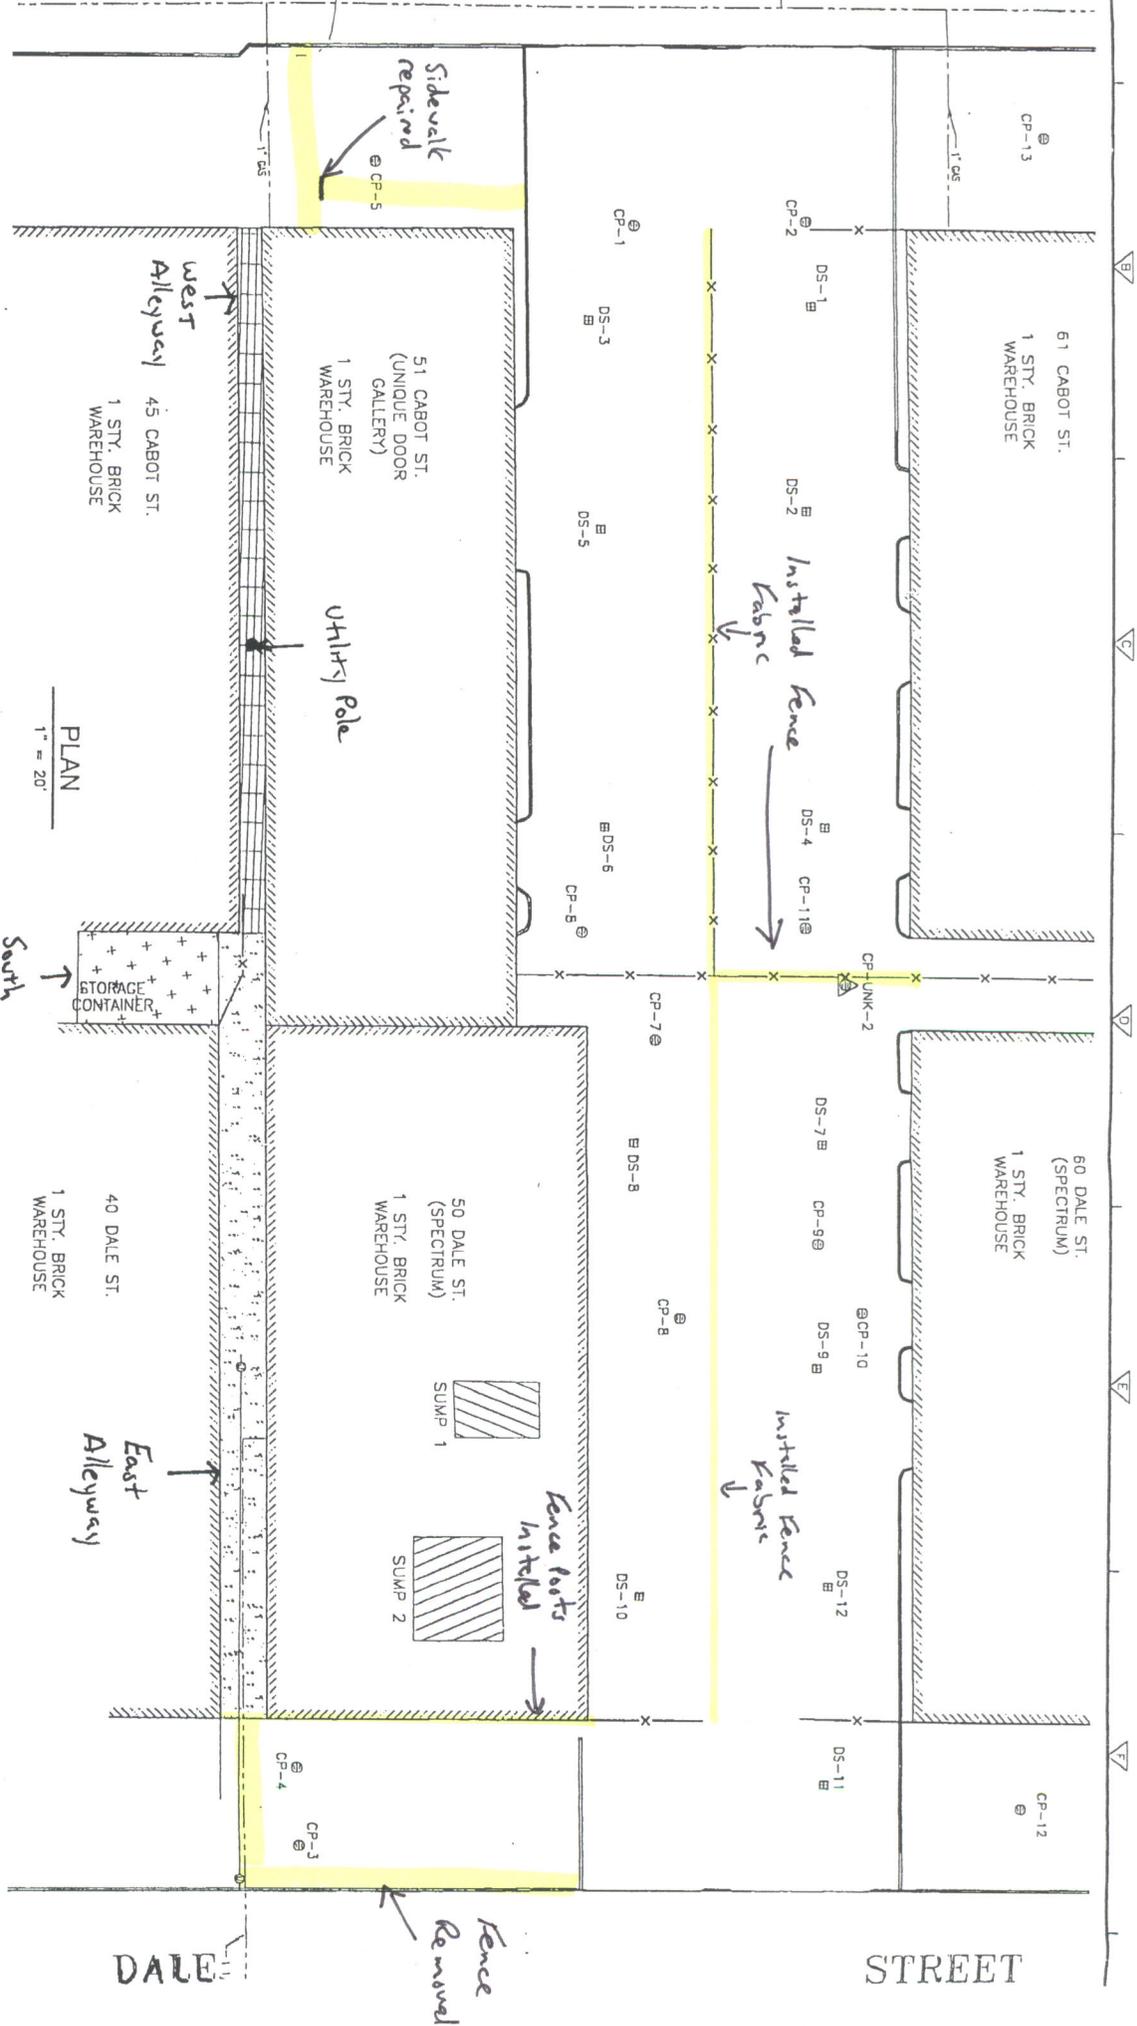

PLAN
1" = 20'

7/14/05

Work Areas
