

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP073115 Date: July 31, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2


Report No.: ACSMGP073115 Date: July 31, 2015

Contractor Severson loaded previously stockpiled soils on trucks for transportation to and disposal at Seneca Meadows.

Contractor worked constructing in-situ stabilization wall sections Q-R, to 12' below ground surface and F-G, to 11.5' (See attached figure)





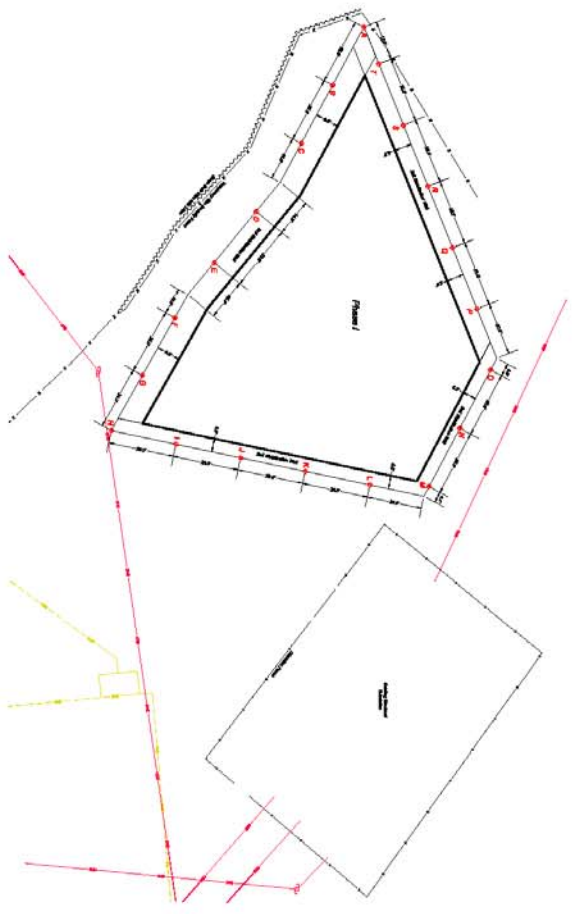

- Legend**
- Easement
 - Boundary
 - 5-foot Buffer
 - 10-foot Buffer
 - 20-foot Buffer
 - 30-foot Buffer
 - 40-foot Buffer
 - 50-foot Buffer
 - 60-foot Buffer
 - 70-foot Buffer
 - 80-foot Buffer
 - 90-foot Buffer
 - 100-foot Buffer
 - 110-foot Buffer
 - 120-foot Buffer
 - 130-foot Buffer
 - 140-foot Buffer
 - 150-foot Buffer
 - 160-foot Buffer
 - 170-foot Buffer
 - 180-foot Buffer
 - 190-foot Buffer
 - 200-foot Buffer

- Notes:**
1. The site is shown as a 100-foot wide easement.
 2. The site is shown as a 100-foot wide easement.
 3. The site is shown as a 100-foot wide easement.
 4. The site is shown as a 100-foot wide easement.
 5. The site is shown as a 100-foot wide easement.
 6. The site is shown as a 100-foot wide easement.
 7. The site is shown as a 100-foot wide easement.
 8. The site is shown as a 100-foot wide easement.
 9. The site is shown as a 100-foot wide easement.
 10. The site is shown as a 100-foot wide easement.
 11. The site is shown as a 100-foot wide easement.
 12. The site is shown as a 100-foot wide easement.
 13. The site is shown as a 100-foot wide easement.
 14. The site is shown as a 100-foot wide easement.
 15. The site is shown as a 100-foot wide easement.
 16. The site is shown as a 100-foot wide easement.
 17. The site is shown as a 100-foot wide easement.
 18. The site is shown as a 100-foot wide easement.
 19. The site is shown as a 100-foot wide easement.
 20. The site is shown as a 100-foot wide easement.



THESE PLANS ARE THE PROPERTY OF THE ENGINEER AND ARCHITECT AND ARE NOT TO BE REPRODUCED OR COPIED IN ANY MANNER WITHOUT THEIR WRITTEN PERMISSION.

Map Showing		DATE
Soil Stabilization Wall Layout		08/20/2014
Plant 1 - Clark Street		
Furnace Room - Clark Street		
Sewer System		
Plant 2 - Clark Street		
Plant 3 - Clark Street		
Plant 4 - Clark Street		
Plant 5 - Clark Street		
Plant 6 - Clark Street		
Plant 7 - Clark Street		
Plant 8 - Clark Street		
Plant 9 - Clark Street		
Plant 10 - Clark Street		
Plant 11 - Clark Street		
Plant 12 - Clark Street		
Plant 13 - Clark Street		
Plant 14 - Clark Street		
Plant 15 - Clark Street		
Plant 16 - Clark Street		
Plant 17 - Clark Street		
Plant 18 - Clark Street		
Plant 19 - Clark Street		
Plant 20 - Clark Street		

THOR ASSOCIATES
 1000 N. W. 10th Street
 Ft. Lauderdale, FL 33304
 Phone: (954) 576-2000
 Fax: (954) 576-2001
 www.thorassociates.com

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP072915 Date: July 29, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP072915 Date: July 29, 2015


Contractor Severson mixed slurry and worked constructing in-situ stabilization wall along east edge of cell, sections "H-I", to 11.5' below ground surface, "L-M", to 10'; and "I-J", to 11.5' (see attached figure.)

Soils were stockpiled on concrete slab within cell.

Inspector: Eric Knapp





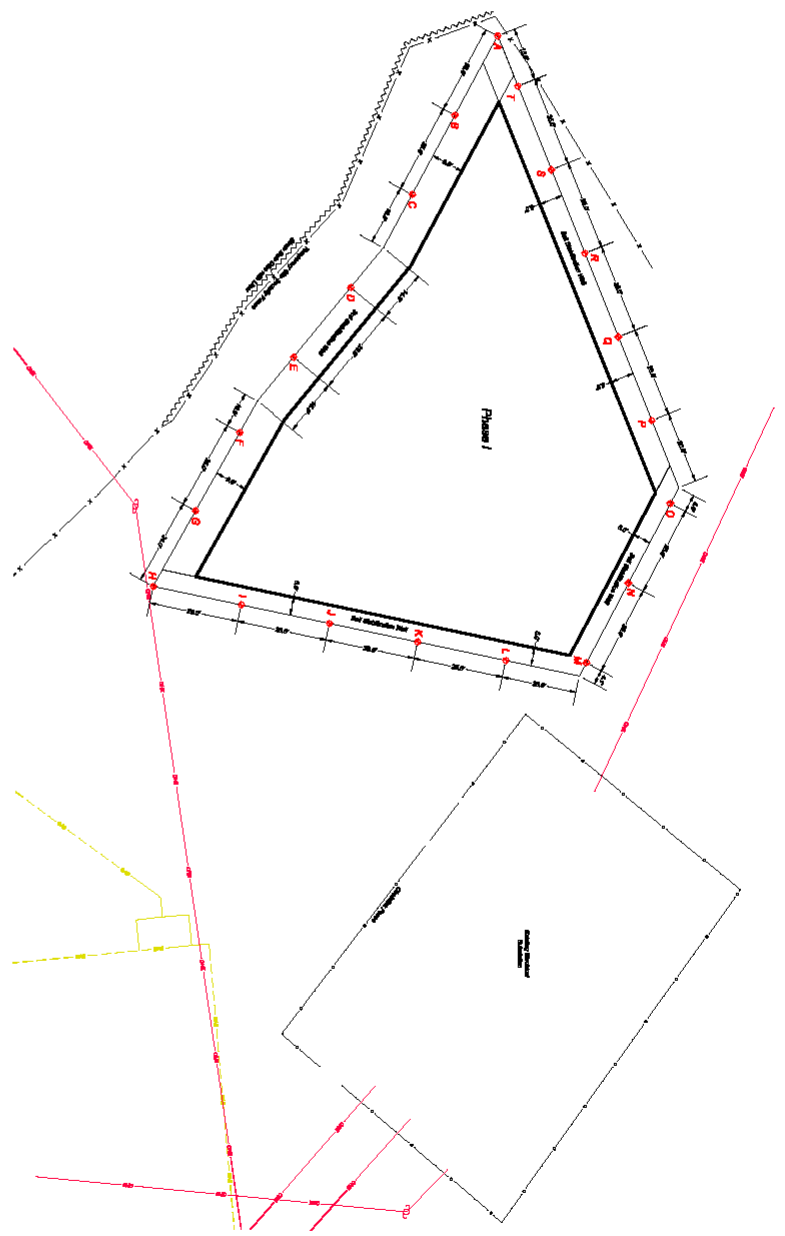


General Notes:

1. This survey is independent of and not to be construed as a confirmation of any previous survey or map of the New York State Canal System (Canal Zone) and vicinity by the State of New York.
2. This survey was conducted in accordance with the provisions of the Surveying Law of the State of New York.
3. The reference monument used in this survey is the intersection of the center lines of the New York State Canal System (Canal Zone) and vicinity by the State of New York.
4. The reference monument is the intersection of the center lines of the New York State Canal System (Canal Zone) and vicinity by the State of New York.
5. The reference monument is the intersection of the center lines of the New York State Canal System (Canal Zone) and vicinity by the State of New York.
6. The reference monument is the intersection of the center lines of the New York State Canal System (Canal Zone) and vicinity by the State of New York.

Professional Statement:

I, the undersigned, being a duly Licensed Professional Engineer in the State of New York, do hereby certify that the foregoing is a true and correct copy of the original survey as shown to me by the client.



Unauthorized alteration or addition to a survey map having a bearing thereon is prohibited by the Surveying Law of the State of New York. Any alteration or addition to a survey map having a bearing thereon is prohibited by the Surveying Law of the State of New York.

DATE	
DESCRIPTION	
DATE	
DESCRIPTION	
DATE	
DESCRIPTION	
DATE	
DESCRIPTION	
DATE	
DESCRIPTION	

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP072815 Date: July 28, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP072815 Date: July 28, 2015


Contractor Severson mixed slurry and worked constructing in-situ stabilization wall near southwest corner and southern leg of cell, sections "C-D", to 11' below ground surface, and "E-F", to 11'.(see attached figure.)

Soils were stockpiled on concrete slab within cell.

Inspector: Eric Knapp






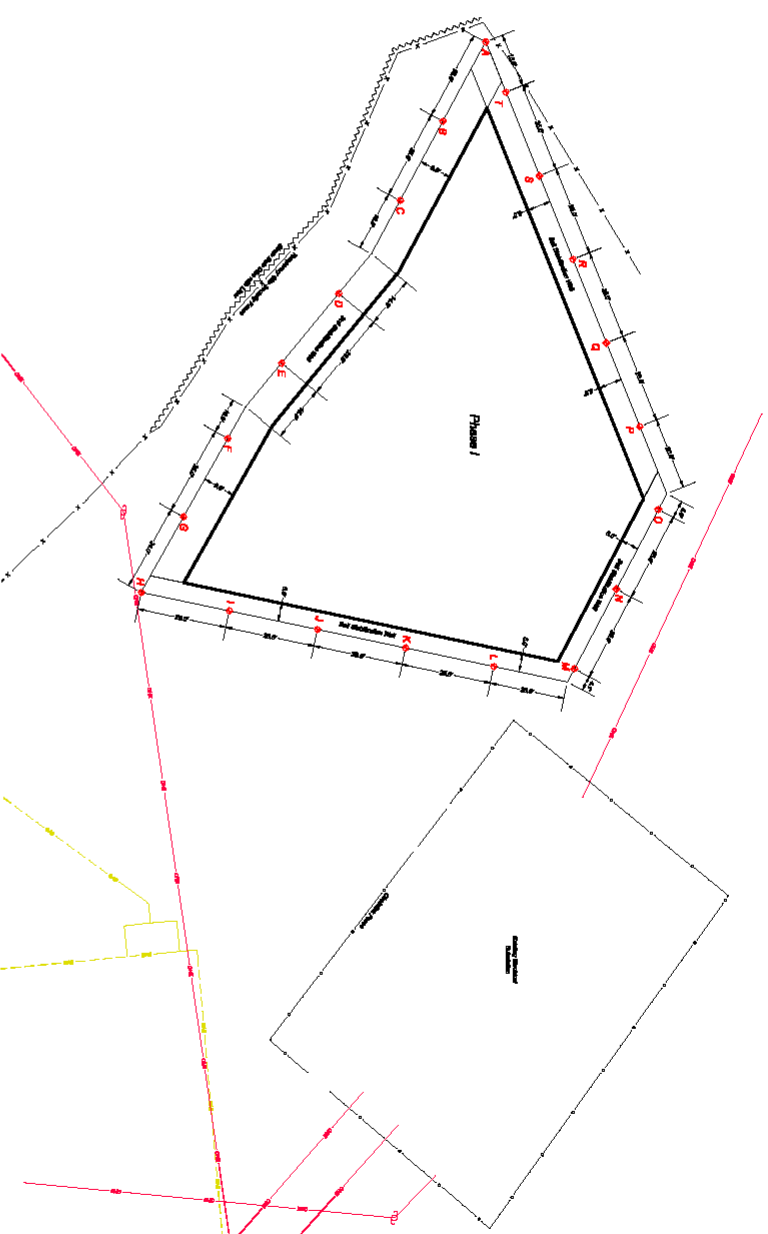

- General Notes:**
1. This survey is independent, successive to the above American Contract of 1893, 2011 Adjustment (SACS/2011) project on the New York State Public Charitable System (Central Zone) and vicinity in the North American Vertical Datum of 2011 (NAVD83) MSL.
 2. Note some of the surveying data have referenced to NAD(2011) and proposed on the New York State Public Charitable System.
 3. The adjacent industrial project within the 1-8280 Corporate Opportunity District (CO) located at 16501 165th Street (R/S) NY, NY is a residential and utility project which was completed by the National Oceanic and Atmospheric Administration (NOAA) in 2007 and completed in August 2011. The adjacent project is to be completed in 2012.
 4. A portion of the survey work shown from referenced drawing No. 1, PMJ modification of others was not performed. (Professional Engineer Report No. 1201201102-001)
 5. The adjacent survey shown is based on an independent survey completed on July 18, 2012.

Professional Statement:

1. I, Paul J. Taylor, Architectural Civil Engineer, No. 19091, Statewide Design, based August 28/14, prepared by ARCHITECT, Project No. 1201201102-001/012.



Unauthorized alteration or addition to a survey map showing a boundary line or other data is prohibited unless the map is first approved by the State Surveying Board or the State Surveying Board. Any person who violates this provision shall be deemed to be guilty of a crime under the laws of the State of New York.

NO.	DESCRIPTION	DATE

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP072715 Date: July 27, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes (x) No () NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP072715 Date: July 27, 2015

Contractor Severson fortified erosion control, adding more hay bales and siltation fence at southwest corner of site.

Contractor mixed slurry and began construction of in-situ stabilization wall at southwest corner, working in section "A-B", to 10.5' below ground surface. (see attached figure.)

Some fugitive dust escaped batch plant during mixing. Increased controls are being implemented, including shrouding and misting. Dust was not seen to leave site.

Inspector: Eric Knapp







DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP072415 Date: July 24, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP072415 Date: July 24, 2015

Contractor Severson worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor completed assembly of waste water treatment system.

Contractor completed assembly of batch plant.

Phone and internet service have been established on site. "Phone tree" is active for community hotline.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP072115 Date: July 21, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP072115 Date: July 21, 2015

Contractor Severson worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Contractor received delivery of parts of their batch plant for constructing the in-situ stabilization wall. Contractor worked assembling batch plant.

Progress meeting held on site at 11:00 am.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP072015 Date: July 20, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP072015 Date: July 20, 2015

Contractor Severson worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Contractor received delivery of parts of their batch plant for constructing the in-situ stabilization wall.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP071715 Date: July 17, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP071715 Date: July 17, 2015

Contractor Severson worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Contractor received delivery of parts of their batch plant for constructing the in-situ stabilization wall.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP071615 Date: July 16, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP071615 Date: July 16, 2015

Contractor Severson worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Contractor worked preparing a staging area for their batch plant for constructing the in-situ stabilization wall.

Subcontractor Thew Associates on site to provide surveying services.

Inspector: Eric Knapp

Potential reuse soil stockpiled atop concrete holder floor



DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP071515 Date: July 15, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP071515 Date: July 15, 2015

Contractor Severson worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Contractor received delivery of parts of their batch plant for constructing the in-situ stabilization wall.

Contractor worked removing soil from atop the concrete holder floor and stockpiled it to be sampled for potential reuse.

Consultant Parsons collected sample from soil stockpile. A composite sample was collected from five (5) points in the pile.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP071415 Date: July 14, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP071415 Date: July 14, 2015

Contractor Severson continued to work installing siltation fence for erosion control. Contractor worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Contractor dug a pretrench along the eastern leg of the proposed In-situ stabilization (ISS) wall. . Large steel pipes with traps were encountered 20-30' from the south end of same trench. They had some tar on the outside surfaces; very little inside. They were cleaned and set aside for disposal.

Weekly progress meeting held on site at 11:00am.

Electrician on site to provide power to trailers and other equipment.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP071315 Date: July 13, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP071315 Date: July 13, 2015

Contractor Severson continued to work installing siltation fence for erosion control. Contractor worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Contractor dug a pretrench along the southern leg of the proposed In-situ stabilization (ISS) wall. Some staining and odor was present within the western 20' of the trench. Contractor worked breaking up concrete holder floor where it encroached on the ISS wall. Contractor began digging eastern leg of pretrench. NAPL encountered 3' below ground surface 15-28' from the north end of the leg. Subcontractor

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP071015 Date: July 10, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP071015 Date: July 10, 2015

Contractor Severson began to pre-trench for construction of in-situ stabilization(ISS) wall. Contractor trenched along western and northern legs of wall. Some small amount of NAPL and stained soils with mild odors was encountered at 3.5' below ground surface in the eastern 15' of the northern leg of the proposed wall. Contractor worked breaking up concrete holder floor where it encroached on the ISS wall.

Contractor worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

Inspector: Eric Knapp

Northern leg of ISS wall facing east



Western leg of ISS wall facing north



DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP070915 Date: July 9, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP070915 Date: July 9, 2015

Contractor Severson continued to work installing siltation fence for erosion control. Contractor worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system. Contractor prepared to begin pre-trenching for in-situ stabilization wall.

.Subcontractor Thew Associates on site for survey/layout.

Some heavy rain showers during afternoon.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP070815 Date: July 8, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP070815 Date: July 8, 2015

Contractor Severson continued to work installing siltation fence for erosion control. Contractor worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

.Subcontractor Thew Associates on site for survey/layout.

Inspector: Eric Knapp

DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP070715 Date: July 7, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP070715 Date: July 7, 2015

Contractor Severson continued to work installing siltation fence for erosion control. Contractor worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor worked assembling waste water treatment system.

.Subcontractor Thew Associates on site for survey/layout.

Project progress meeting held on site at 11:00 am.

Inspector: Eric Knapp

Wastewater treatment system and secondary containment



DAILY OBSERVATION REPORT Pg. 1 of 2

Report No.: ACSMGP070215 Date: July 2, 2015

**Auburn Clark Street
MGP
Remedial Action Site
706008**

**Consultant: Parsons Engineering
Contractor: Severson Environmental
Services**

Were there any changes to the Health & Safety Plan? *Yes () No (X) NA ()

Were there any exceedances at the perimeter Air: *Yes () No () NA (x) action level reported on this date?

**Were there any Noise /Vibration exceedances Noise: *Yes () No () NA (X) reported on this date?
Vibration: *Yes () No () NA (X)**

Were there any breaches to the silt fence reported/observed on this date ? *Yes () No (X) NA ()

Were there any dust/odor issues reported or observed on this date? *Yes () No (X) NA ()

WASTE HAULING :

*(*If any box(s) below are checked "Yes", list the deviation under the "Items of Concern" section of this report).*

Were there any vehicles which did not display proper D.O.T ^{*Yes () No () NA (X)} numbers and placards?

Were there any vehicles which were not lined or tarped? *Yes () No () NA (X)

Were there any vehicles which were not decontaminated * Yes () No () NA (X) prior to exiting the work site?

DAILY OBSERVATION REPORT Pg. 2 of 2

Report No.: ACSMGP070215 Date: July 2, 2015

Contractor Severson continued to work installing siltation fence for erosion control along northern edge of site. Contractor worked on various site preparation activities, including clearing, grading, and receiving supplies and equipment. Contractor constructed a secondary containment area and placed tanks for future water treatment.

Subcontractor drilled for the placement of inclinometers to the south of the site.

Inspector: Eric Knapp

Floating boom in Owasco outlet

