

APPENDIX I

DAILY FIELD REPORTS- LANDFARM CELL

Report No. 2

Date 9/18/96 Contract No. _____

Job GIC Sherburne LF Cell Construction

Contractor Ira D. Conklin & Sons

Project Representative IMH

Signature _____

Time arrived on site 11:00 AM

Time left site _____

What significant construction work was accomplished today, and where?

~ 40% excavation of cells

~ delivery of ~ 10 cy manure

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

D-8 dozer

1 laborer

1 supervisor

3. What special incidents happened?

☒ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☐ None
Manure by J. Howard

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
	P.Cdy & hazy hazy		

7. Who were the visitors that came to the site? List names.

Name	Representing
<i>J. Howard</i>	<i>Landowner</i>
<i>Bob Adsit</i>	<i>Asst Septic & Env</i>
<i>Jenn May</i>	<i>NYSDEC</i>

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative? ☒ Yes ☐ No

If yes, indicate specific location and description.

Cell excavation
Manure pile as delivered

Additional Comments:

☐ Continued on separate page(s).

Report No. 1

Date 9/16/96 Contract No. _____

Job Shurburne GI

Contractor IDC

Project Representative NAC

Signature [Signature]

Time arrived on site 9:30

Time left site 4:00

1. What significant construction work was accomplished today, and where?

Contractor placed stakes to mark out foundation cell and collect elevation data.

The ~~door~~ door will be delivered on Tuesday or Wednesday ~~th~~.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

Transit

3. What special incidents happened?


☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
	<i>Ch</i>	70°	

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☒ Yes ☐ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Daily Field Report



S&W Services, Inc.

Report No. 3Date 9/19/96 Contract No. _____Job Sherburne Landfill cellContractor IDEProject Representative DAKSignature DAKTime arrived on site 9:30Time left site 3:00pm

1. What significant construction work was accomplished today, and where?

The Dozer was replaced by an Excavator. The edges were finished half way.

The Cow power was placed in the cell by Jack Howard. He will continue through the weekend.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

Excavator

Dump Truck

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
<u> </u>	<u>Ch</u>	<u>70°</u>	<u> </u>

7. Who were the visitors that came to the site? List names.

Name

Representing

Tom F...

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes

☒ No

If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☐ Yes

☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Daily Field Report



S&W Services, Inc.

Report No. 4Date 9/20/96 Contract No. _____Job Shenandoah LandformContractor IDCProject Representative LACSignature [Signature]Time arrived on site 9:30Time left site 5:40

1. What significant construction work was accomplished today, and where?

Contractor Excavated the landform cell and collected elevation data. The landform cell is complete w/ the exception of the side walls.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

Dozer
Circuit

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
—	Ch	80°	—

7. Who were the visitors that came to the site? List names.

Name

Tom F.
John Howard

Representing

GI
Indowner

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative? ☐ Yes ☐ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 5

Landfill Cell

Daily Field Report

Date 9/24/96

Contract No. 41093



S&W Services, Inc.

Job Landfill cell GI Sherburne

Contractor IDC

Project Representative NAC

Signature [Signature]

Time arrived on site 9:30

Time left site 5:00 pm

1. What significant construction work was accomplished today, and where?

Contractor finished edges of the landfill cell and spread the available manure along the bottom. We checked the boundaries of the plane before the excavation started in that area. ~~the contractor will~~ The contractor will begin to remove the clean soil to ≈ 2.5 ft below grade.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

IDC - 2 men

Excavator

6 yd (cubic) dump truck

NAC

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☒ Schedules ☐ Damages ☐ Other ☐ None
See field book

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
<i>Light</i>	<i>Cloudy</i>	<i>60°</i>	<i>Heavy</i>

7. Who were the visitors that came to the site? List names.

Name

Don Chiosano

Representing

NYSDOT

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes

☒ No

If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☐ Yes

☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 6



S&W Services, Inc.

Date 9/25/96 Contract No. 410932A

Job Sherburne GE Landfarm Cell

Contractor IDC

Project Representative NAC

Signature [Signature]

Time arrived on site 9:30

Time left site 5:00 pm

1. What significant construction work was accomplished today, and where?

The contractor excavated the clean soil from the plume area. Several piezometers were removed from the plume area. The dump truck was stuck several times making work difficult.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 Excavator
1 Dump
2 men IDC

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
Light	Cloudy	60°F	Heavy

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☒ Yes ☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. Site 7

Daily Field Report



S&W Services, Inc.

Date 9/26/96 Contract No. 410932A

Job Shenburne GT Landform all

Contractor IDC

Project Representative DAC

Signature [Signature]

Time arrived on site 8:00 AM

Time left site 5:00 PM

1. What significant construction work was accomplished today, and where?

Contractor did not arrive on-site until after 10 AM. The contractor completed the excavation over the grade area. Contaminated material will be removed on Monday.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 Excavator
1 Dump Truck
2 men

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
—	Ch	70'	Light

7. Who were the visitors that came to the site? List names.

Name

Jack Howard
Mike Howell

Representing

Land Owner
Stev

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes

☒ No

If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☒ Yes

☐ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 8

Daily Field Report



S&W Services, Inc.

Date 9/27/96 Contract No. 410932A

Job Lundform cell GT Sherburne

Contractor IDC

Project Representative NAC

Signature Yuh Cappe

Time arrived on site 8:00 AM

Time left site 3:40 PM

1. What significant construction work was accomplished today, and where?

Completed clean soil excavation. Transported imported soil from construction of 18" interceptor to land from cell. 2 40 yds of additional soil required to be removed because of location. Covered material in cell w/poly. Very high winds at 25-30 mph.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 Dump Truck

1 Excavator

2 men

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
Light	Ch High Wind	60°F	Light to mod.

7. Who were the visitors that came to the site? List names.

Name	Representing
Don Fletcher	IDC
Tom Favalaro	GI

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☐ Yes ☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 9

Date 9/30/96 Contract No. 4109324

Job GI Shrubane Land farm cell

Contractor J.D.C.

Project Representative WAC

Signature Wick Carson

Time arrived on site ~~10:00~~ 10:10

Time left site 24:30

1. What significant construction work was accomplished today, and where?

Began excavation of trashed soil. G.Water \approx 5.8 FT below grade.
contaminated excavated to 7' 7" below grade.

Built containment area where old soil was stored from Intercept.
trench. More material was ~~excavated~~ excavated from that area.
The cell will be covered w/ tarp after closing site for the day.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 Excavator
1 payloador
3 men
1 Dump Truck.

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
None	Ch	70°F	Light

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes

☒ No

If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☐ Yes

☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 10Date 10/1/96 Contract No. 410942AJob Shurburne landfillContractor IDCProject Representative NACSignature [Signature]Time arrived on site 10:00 AMTime left site 3:40

1. What significant construction work was accomplished today, and where?

Contractor continued to excavate impacted material from the plane area.Will continue to monitor.IDC
Don
Bill

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 EXCAV.1 Payloader2 men

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
None	Ch	70°	Light

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes

☒ No

If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☐ Yes

☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 11

Daily Field Report



S&W Services, Inc.

Date 10/2/96 Contract No. 410942A

Job Landfill cell GI

Contractor JDC

Project Representative NAC

Signature Mike Caggion

Time arrived on site 9:45

Time left site 3:45

1. What significant construction work was accomplished today, and where?

Contractor continues to excavate soil 1 foot below the water table \approx 6 feet. The soil is then placed into the landfill cell.

Don Fletcher stated he will bring more equipment & more men to the site to finish.

A 31-gal. Sheen was noted on the water behind the looms.

The contractor is monitoring the area with their HPLV. No leaks were found to record 3:00pm.

MTW (Steamers + Helen) collected the first of the contaminating samples.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

2 men
1 excavator
1 payloader

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
—	Ch	68°F	—

7. Who were the visitors that came to the site? List names.

Name

Don Fletcher

Representing

FDX

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes

☒ No

If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☐ Yes

☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 12

Daily Field Report



S&W Services, Inc.

Date 10/3/96 Contract No. 460942A

Job Shelburne Landfill Cell

Contractor IDC

Project Representative John C. Carr

Signature [Signature]

Time arrived on site 9:40

Time left site 3:45

1. What significant construction work was accomplished today, and where?

Contractor continues to excavate soil 1 foot below the water table
≈ 6 Foot deep.

Larry H. Huling collected the soil point samples from the excavation.
4 additional samples were collected ≈ 12" above the water table
2 samples were collected on 10/2/96.

The tubes (interceptors) were excavated and pulled from the
plow area.

The contractor used poles and Booms to remove any live poles
from the water.

Doug Stuck MW-19 with payload. Spike w/ Bill Simpson he will straighten it
later.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 Excav.
1 Payloader
4 men

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☒ Schedules ☐ Damages ☒ Other ☐ None

I asked Bill when the pipe would arrive? He did not know.

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
<i>Light</i>	<i>Cloudy</i>	<i>45°</i>	<i>Light</i>

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes

☒ No

If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☐ Yes

☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 13

Daily Field Report



S&W Services, Inc.

Date 10/2/96 Contract No. 410942A

Job Shurburne GE Land Farm cell

Contractor IDC

Project Representative NAC

Signature [Signature]

Time arrived on site 10:40

Time left site 5:20

1. What significant construction work was accomplished today, and where?

Contractor continued to excavate the remainder of the petroleum impacted soil.

The free floating product layer that had formed over the weekend \approx 2000 gallons of oily water that resembles a thick milkshake. IDC will store the product in the 1000 gallon over night. I called the place to explain that I could not run this mixture through the system w/o oil/water separation. IDC wanted to place the mixture into drums. I could not see placing this into 50-60 drums at \$2.00 a piece. I called NYTSK to have a 2500 gallon + a 550 gallon tank. I asked Ron Hansen if it is OK to store the product on site. He stated absolutely not due to the liability. We will place the tanks on the Howard property.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 Excavator
1 Bulldozer
1 Grader
1 Dump truck
1 Vehicle
5 men

3. What special incidents happened?




☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?



☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
		70°	

7. Who were the visitors that came to the-site? List names.

Name  Representing 

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative? ☒ Yes ☐ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 14

Daily Field Report



S&W Services, Inc.

Date 10/8/96 Contract No. 410942 A

Job Shenburne land farm call

Contractor IDC

Project Representative NAC

Signature Nick Capone

Time arrived on site 10:00

Time left site 4:40

1. What significant construction work was accomplished today, and where?

The contractor began back-filling the excavation after the confining ^{samples} were back clean.

- The 2500 gallons & the 550 gallon tanks arrived, IDC pumped the oily water mixture into the tanks.

The contractor got the dozer stuck when he attempted to grade the call, it took 2 hrs to remove it.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

1 Dozer
1 Backhoe
1 Excavator
5 men

3. What special incidents happened?



☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
	ch	70°	

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

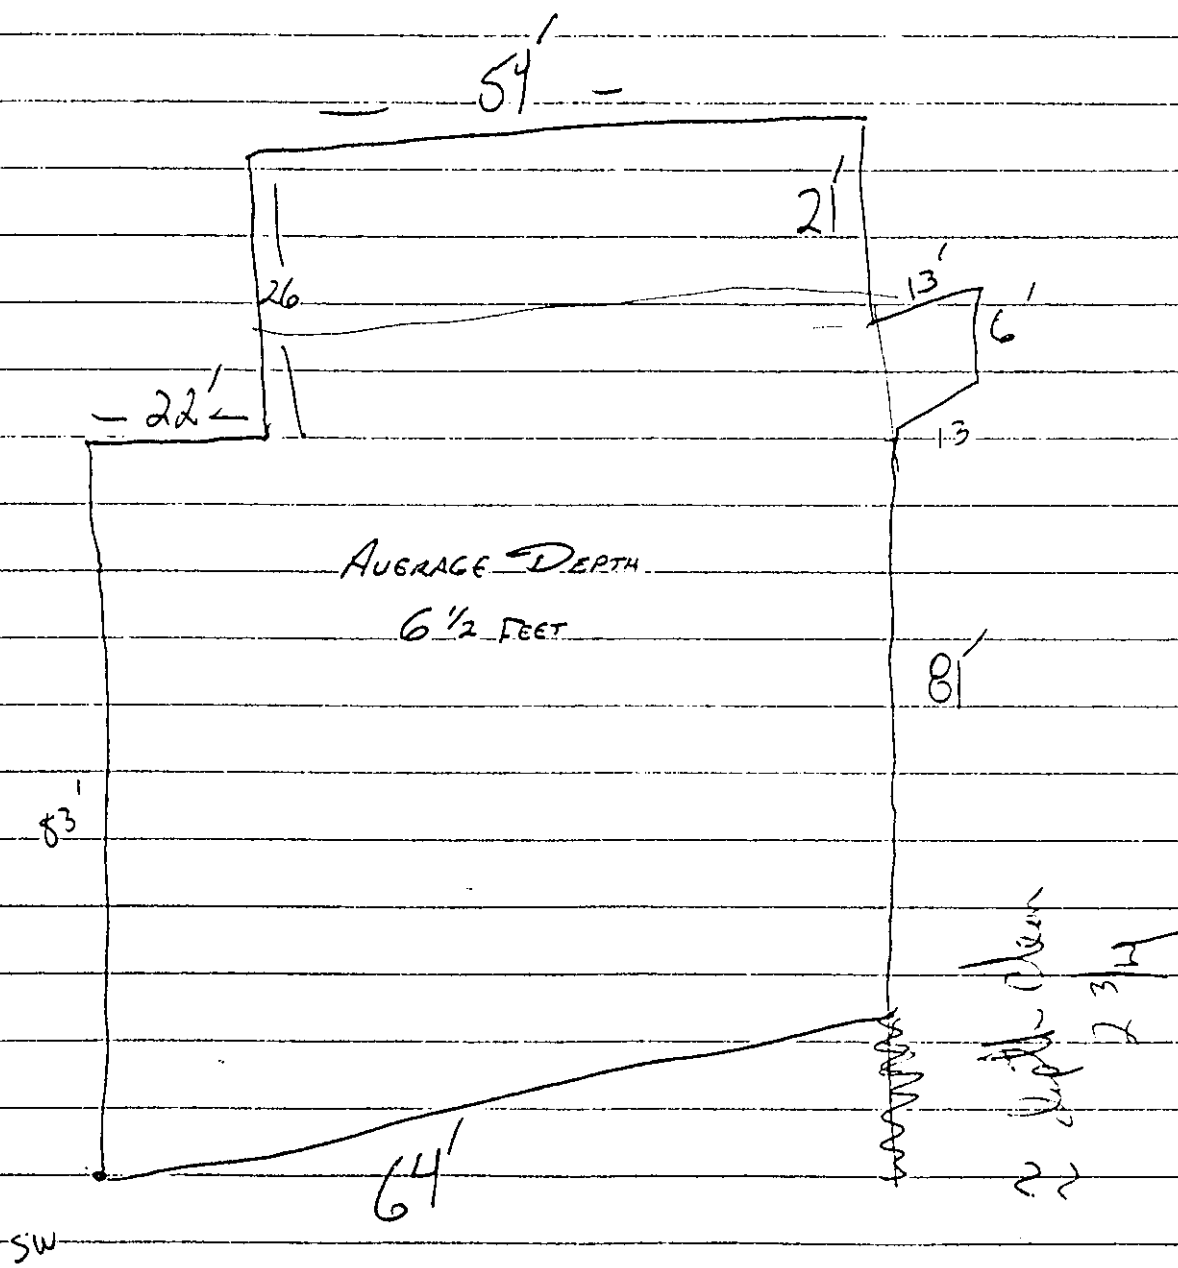
☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative? ☒ Yes ☐ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).



Report No. 15

Daily Field Report



S&W Services, Inc.

Date 10/10/01 Contract No. 4100424

Job Shimizu Land Farm cell

Contractor IDC

Project Representative NAC

Signature [Signature]

Time arrived on site 8:30

Time left site _____

1. What significant construction work was accomplished today, and where?

Contractor installed the trench tubes in pea gravel

The remainder of the imported soil was placed in the cell.

No 45° elbows will be used instead the tube will be flared to the contour. At the stress points the contractor will reinforce the tubing at the joints.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

4 men
1 Excavator
1 Dozer
1 pig load
1 dump truck

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
—	Cloudy	65°	—

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative? ☐ Yes ☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Daily Field Report



S&W Services, Inc.

Report No. 16Date 10/17/96 Contract No. 410972AJob Lafayette cell SherburneContractor IDCProject Representative NACSignature [Signature]Time arrived on site 10:30Time left site 1:40

1. What significant construction work was accomplished today, and where?

The contractor continued to install the tubing. I spoke to Jack Howard & Bill Simpson about uncovering the cell to allow for laying 3 to allow the top layer of Manure to be placed on the cell. It was unclear whose responsibility it was to cover the cell with Manure. I spoke with Don Fletcher and told him the cell was not complete the way it sat.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

4 men
1 Exc
1 Dozer
1 pig back

3. What special incidents happened?

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
None	Clear	70°	

7. Who were the visitors that came to the site? List names.

Name John Howard Representing Land Owner

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative? ☐ Yes ☒ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).

Report No. 17

Daily Field Report



S&W Services, Inc.

Date 10/18/96 Contract No. 410942A

Job Shelburne Land farm cell

Contractor IDC

Project Representative PAC

Signature [Signature]

Time arrived on site 9:30

Time left site 1:02

1. What significant construction work was accomplished today, and where?

Contractor finished installing 24" pipe and 18" wells.
They will backfill and grade the pipe and construction area.

2. What manpower and equipment were used today? (total men/contractor, major power equipment, job superintendent)

4 men
1 Exc.
1 dump
1 loader

3. What special incidents happened.

☐ Deliveries ☐ Blasting ☐ Strikes ☐ Accidents ☐ Other ☒ None

4. What special instructions were given to the Contractor and what was Contractor's response?

☐ Tests ☐ Defective Work ☐ Schedules ☐ Damages ☐ Other ☒ None

5. Where there any damages to property? ☐ Yes ☒ No If yes, explain and locate.

6. What were the weather and site conditions?

Precipitation	Skies	Air Temperature	Ground/Pavement Moisture
	Ch	60°F	

7. Who were the visitors that came to the site? List names.

Name

Representing

8. Did observations reveal any work not in compliance with the Contract Documents?

☐ Yes ☒ No If yes, explain and describe actions taken.

9. Were photographs taken by project representative?

☒ Yes ☐ No

If yes, indicate specific location and description.

Additional Comments:

☐ Continued on separate page(s).
