



**NYSEG - MGP SITE**  
**Penn Yan, New York**

**Construction Manager Weekly Reports**

**DATE:** Week ending 06/18/17

<b>WEEK NO.:</b> 98	<b>HOURS ON SITE:</b> 10/day	<b>WRITTEN BY:</b> Abby Chin	<b>PROJECT NUMBER:</b> 60430543	
<b>Weather:</b> Variable, 55°F to 88°F				
<b>NAME:</b>	<b>TRADE:</b>	<b>COMPANY:</b>	<b>EQUIPMENT:</b>	<b>VISITORS/AFFILIATION:</b>
George Fischer	Construction Oversight	AECOM	5 Barges	Emily Thurston - D&B Engineers (NYSDEC)
Skylar Haas	CAMP Monitoring	AECOM	Smooth Drum Roller	Keith Stahle - AECOM
Chester Adams	Superintendent	SES	31EX Dozer	
Anthony Laurendi	Site Safety Officer	SES	Air compressor	
William Conti	Laborer	SES	Push Boat	
George Schell	Operator	SES	Excavator with Hammer	
Tim Sheehan	Laborer	SES	320 zero turn excavator	
Kevin Daunce	Operator	SES	2 Floats	
Robert Boland	WWTP	SES	PC360 Excavator	
Andrew Stein	Laborer	SES	Komatsu W380 Loader	
Derek Stein	Laborer	SES	Sky Jack High Reach Fd	
			3 Scows	
			PC 300 Excavator - LF	
			Push Boat	
AECOM Site hours this week - 78est.				
<b>SUBCONTRACTORS:</b>		<b>SITE DELIVERIES (indicate size, type, and condition):</b>		
Thew Associates				
<b>WORKED PERFORMED BY Sevenson Environmental Services (SES)</b>				
<b>06/12/2017</b> - Began welding procedures of structural sheetpile on south side of historic structure. Began demobilization of water treatment plant. Assisted Thew Associates with uncovering secant pile form for survey shots. Created sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				
<b>06/13/2017</b> - Continued welding procedures of structural sheetpile on south side of historic structure. Continued demobilization of water treatment plant. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				
<b>06/14/2017</b> - Continued welding procedures of structural sheetpile on south side of historic structure. Continued demobilization of water treatment plant. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Demobilized PC300 LF equipped with GPS from the site. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				
<b>06/15/2017</b> - Continued welding procedures of structural sheetpile on south side of historic structure. Continued demobilization of water treatment plant. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Prepped single scows for demobilization from the site. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				



NYSEG - MGP SITE  
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 06/18/17

WEEK NO.: 98	HOURS ON SITE: 10/day	WRITTEN BY: Abby Chin	PROJECT NUMBER: 60430543
<b>WORK COMPLETED BY SES SUBCONTRACTORS</b>			
Thew Associates was on-site to map out structural sheeting and secant wall locations on 6/12/17.			
<b>AGREEMENTS MADE/CONVERSATIONS (Refer to telecons, phone records, and/or logbooks for details)</b>			
Weekly meeting held 6/13/17. See minutes for details.			
<b>SAMPLING PERFORMED:</b>			
<b>QUALITY CONTROL ACTIVITIES</b>			
Ongoing erosion control inspections. Erosion control measures repaired as necessary.			
<b>REQUEST FOR INFORMATION (RFI)</b>			
<b>TRANSMITTALS / SUBMITTALS</b>			
Submittals reviewed and approved as noted in submittal register.			
<b>VIBRATION/SETTLEMENT MONITORING COMMENTS:</b>			
Settlement monitoring continues, very little movement observed at crack gauges. Have seen some temperature related movement. Data from Leica system shows normal temperature related oscillation. Sensor SP-07 was reconnected to the system which affected readings at the other sensors in the system. These fluctuations are not supported by the readings from the Leica system. The Geokon system will be re-plumbed and re-zeroed.			
Vibration monitoring is conducted daily within the former MGP structure and Water Street Wines & Spirits building. Multiple alert level exceedances 6/13 through 6/15 due to personnel working near the monitor. One stop work exceedance on 6/15 in the SE room due to personnel bumping the monitor.			
Turbidity monitoring conducted daily. No turbidity exceedances observed.			
<b>AIR MONITORING COMMENTS:</b>			
AECOM on site performing CAMP and noise monitoring. No CAMP exceedances observed.			
<b>SAFETY OBSERVATIONS/VIOLATIONS/COMMENTS</b>			
SES performing daily toolbox safety meetings. Approximately 47,250 site hours worked to date without incident.			
<b>CORRECTIVE ACTIONS IMPLEMENTED</b>			



NYSEG - MGP SITE  
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 06/18/17

WEEK NO.: 98

HOURS ON SITE: 10/day

WRITTEN BY: Abby Chin

PROJECT NUMBER: 60430543

PHOTOS



Sheet Splice Welding



Moving sheet to bank area to splice



Partially completed weld splice



Crew cleaning marine equipment

STREAM STAGE MONITORING

DATE	WATER LEVEL (FROM KLA WEBSITE)
6/12/2017	713.98
6/13/2017	713.96
6/14/2017	713.96
6/15/2017	714.07
6/16/2017	714.09
6/17/2017	714.10
6/18/2017	714.15

Construction  
Manager (Signature):

Project Construction Week: 06/12/2017-06/15/2017

Report Date: 6/20/2017

**NYSEG**

**Penn Yan Former MGP Site Remedial Action**

**Penn Yan, New York  
NYSDEC Site No. 8-62-009**

**Weather**

Monday 06/12/2017: High 91.7° Partly cloudy, with 0.00" of rain and an average of 2.8 mph winds (Max 15.0 mph) directed in the northeast direction.

Tuesday 06/13/2017: High 85.6° Cloudy, with 0.10" of rain and an average of 2.2 mph winds (Max 14.0 mph) directed in the northeast direction.

Wednesday 06/14/2017: High 78.1° Partly cloudy, with 0.01" of rain and an average of 1.4 mph winds (Max 10.0 mph) directed in the south southwest direction.

Thursday 06/15/2017: High 79.2° Cloudy, with 0.78" of rain and an average of 2.2 mph winds (Max 13.0 mph) directed in the northeast direction.

**Air/Noise Monitoring Levels within limits: Yes**

**Comments/Responses:**

Equipment	ID	Station	Last Calibration
DustTrak II 8530	8530163902	Unit 1	9/20/2016
DustTrak II 8530	8530133403	Unit 2	3/7/2017
DustTrak II 8530	8530121503	Unit 3	4/12/2017
CEL-352 Noise Dosimeter	3111305	Canal, Water Street	Daily
MiniRAE 3000	592-907919	Unit 1	4/17/2017
MiniRAE 3000	592-907667	Unit 2	4/17/2017
MiniRAE 3000	592-906598	Unit 3	4/17/2017

NA-Not Available

**Consultant's Verification:** On behalf of the Consultant, I certify this report is complete and correct, and all materials and equipment used and work performed during this reporting period are in compliance with the contract plans and specifications, to the best of my knowledge, except as may be noted above.



**Abby Chin**  
**CAMP Review Personnel/ Signature**

6/21/17

**Date**



## WEEKLY CAMP & NOISE REPORT

Project Construction Week: 06/12/2017-06/15/2017

Report Date: 6/20/2017

### **ATTACHMENT #1 CAMP DATA**

Table 1: Particulates Data

Date	Particulate Action Level (ug/m3)	Unit 1 Peak Particulates (µg/m³)	Unit 2 Peak Particulates(µg/m³)	Unit 3 Peak Particulates(µg/m³)	Comments
6/12/2017	150	-	-	-	No data collected due to lack of intrusive activity
6/13/2017		-	76	62	No data collected for Unit 1 (NW) on 6/13 due to a flow error
6/14/2017		21	21	60	
6/15/2017		29	44	32	

- 1. NA-Not Available.
- 2. All particulates data is presented as 15 minute peak averages.
- 3. **Bold** indicates recording in excess of alert level.
- 4. **Bold and highlighted** indicates recording in excess of stop work level.

Table 2: Noise Data

Date	Noise Action Level (dB)	Peak Noise (dB)	Comments
6/12/2017	90	60	
6/13/2017		56.8	
6/14/2017		55.7	
6/15/2017		60	

- 1. NA-Not Available.
- 2. **Bold** indicates exceedance observed.

Table 3: VOC Data

Date	VOC Action Level (ppm)	Unit 1 Peak VOC (ppm)	Unit 2 Peak VOC (ppm)	Unit 3 Peak VOC (ppm)	Comments
6/12/2017	5.0	-	-	-	No data collected due to lack of intrusive activity
6/13/2017		0	2.749	1.401	
6/14/2017		0.948	<b>4.031</b>	1.715	No site source identified for elevated level
6/15/2017		3.708	3.633	<b>11.704</b>	Elevated level was due to a flow and lamp error, this was caused by a sudden severe weather front

- 1. NA-Not Available.
- 2. All VOC data is presented as 15 minute peak averages.
- 3. **Bold** indicates recording in excess of alert level.
- 4. **Bold and highlighted** indicates recording in excess of stop work level.




## WEEKLY CAMP & NOISE REPORT

Project Construction Week: 06/12/2017-06/15/2017

Report Date: 6/20/2017

### **ATTACHMENT #2 CAMP STATION LOCATIONS**



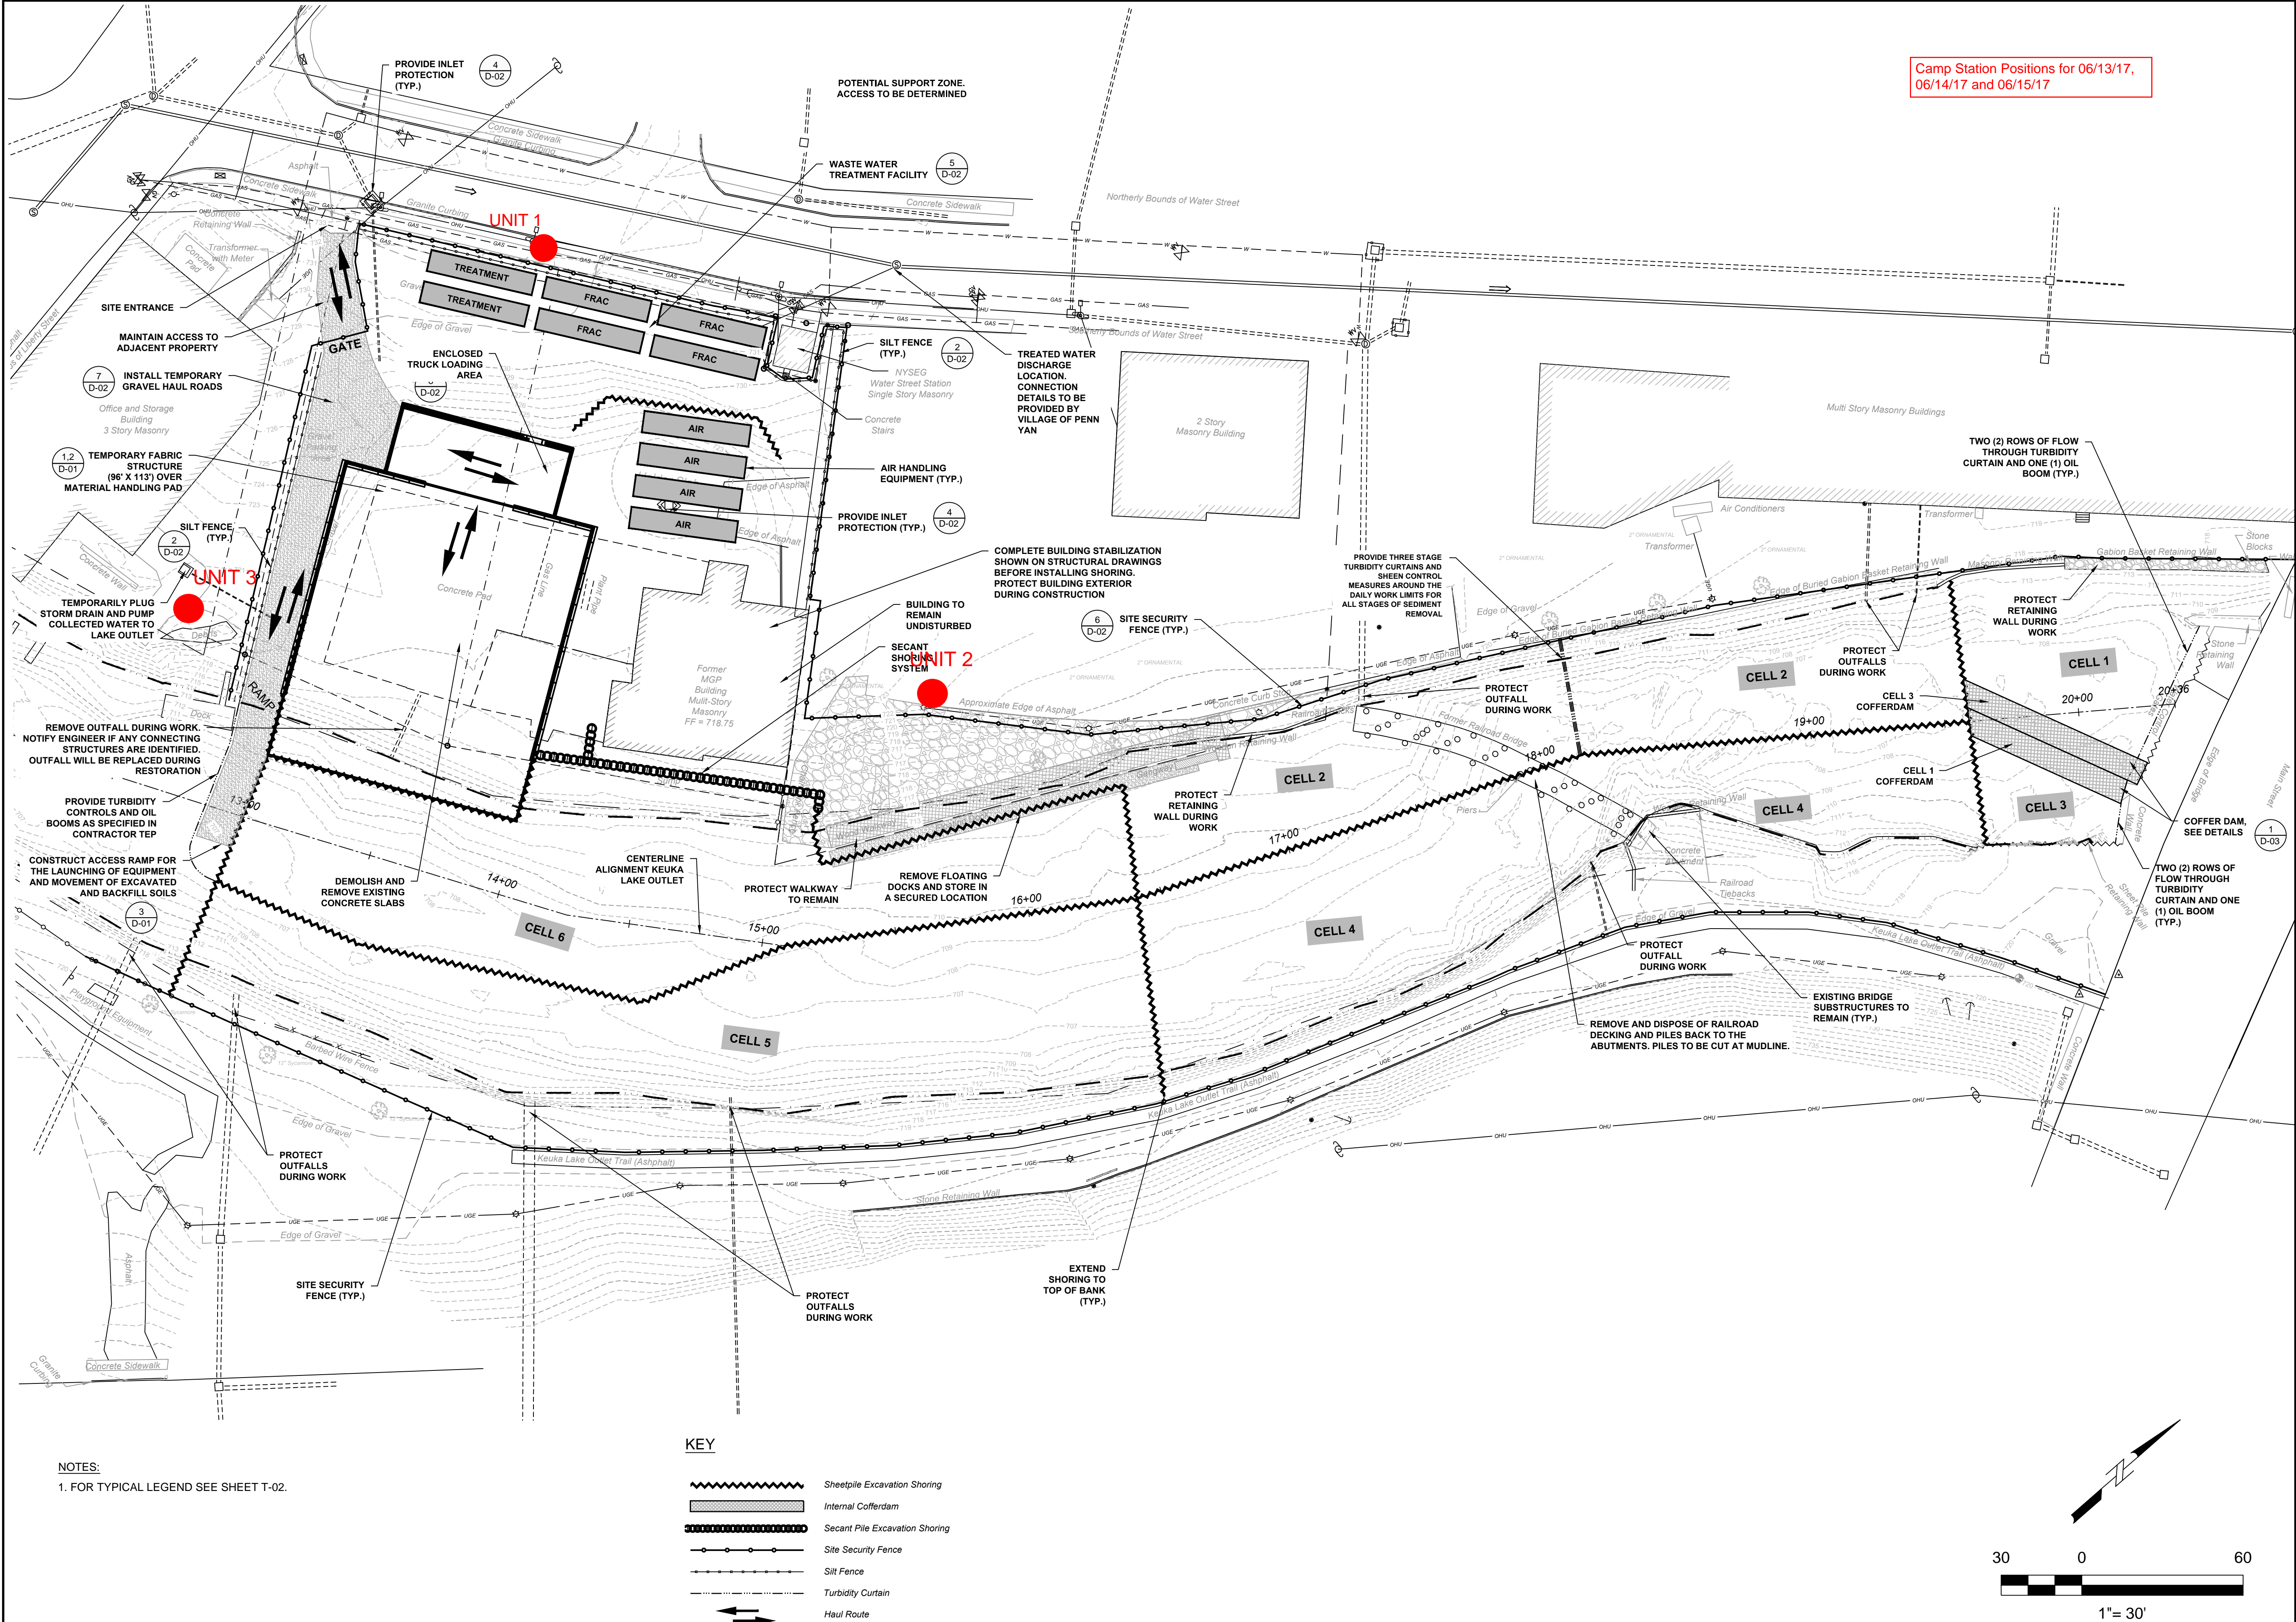

ISSUE/REVISION		
0	02-06-15	ISSUED FOR CONSTRUCTION
I/R	DATE	DESCRIPTION



	Upstream Low	Upstream High	Downstream Low	Downstream High	Within Reporting Limits	Working Day
Date	NTU	NTU	NTU	NTU	( Yes/No )	(Yes/No)
<b>6/12/2017</b>	3.3	5.6	10.5	11.2	Yes	Yes
<b>6/13/2017</b>	4.1	15.4	3.9	11.2	Yes	Yes
<b>6/14/2017</b>	2.2	8.7	-0.1	11.6	Yes	Yes
<b>6/15/2017</b>	2.5	38.1	6.1	11.6	Yes	Yes
<b>6/16/2017</b>	2.8	8.4	4.4	11.5	Yes	No
<b>6/17/2017</b>	2.2	49.2	8.6	11.7	Yes	No
<b>6/18/2017</b>	2.1	23.7	6.5	12.6	Yes	No

High and Low values reported each 24 hr period for each day.

Reporting Limits: exceedance recorded if downstream value exceeds upstream value by 100NTU.

**Shaded and Bold cells indicate turbidity reading exceeded reporting limits.**

**Report Date**

June 12, 2017

**Day of the Week**

Monday

**Report No.**

336

**Project No.**

P1138

**Weather High**

88°F


**Weather Low**

70°F

**Precipitation**

0.0

**Weather  
Conditions**



**Photo 1**



Transporting structural sheetpile to the work area to be welded and driven.

**Photo 2**



Thew Associates on-site to survey recently installed structural sheeting and secant wall locations.

**Photo 3**



Beginning demobilization of water treatment plant.

**Photo 4**



Threading additional 22' sheetpile to be welded for structural sheetpile installation.

**Video**

**No video uploaded.**

**Work Performed by Sevenson**

- Began welding procedures of structural sheetpile on south side of historic structure.
- Began demobilization of water treatment plant.
- Assisted Thew Associates with uncovering secant pile form for survey shots.
- Created sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.

**Planned Activities**

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

-Continued to perform site maintenance.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

### **Safety Remarks**

-No accidents or incidents were reported.  
-Conducted daily safety meeting at 7:00 AM  
Safety Topic: Working in Warm Temperatures

### **Work Performed by Subcontractors**

-Thew Associates was on-site to map out structural sheeting and secant wall locations.

### **Remarks/Verbal Directives**

-None.

### **Equipment/Materials Delivered to Site**

-No equipment or materials were delivered to the site.



### Miscellaneous Information

-None.

### Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	

P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/16
996EF Float		4/18/16	5/30/16
Float		4/18/16	5/30/16
541E Scow	Single Scow	4/19/16	
540E Scow	Single Scow	4/19/16	
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	

## Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		
VM Hammer	PVE		4/24/17	1		
Mini Track Loader	Toro		5/18/17	1		
Electric Core Machine	DP		5/18/17	1		

#### Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
4	Operator	40
3	Laborer	30
1	DEC	10
3	AECOM	30

#### Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Woodford Brothers	0
Mertec	0
Thew Associates	10

#### Labor Totals

**Today's Sevenson  
Labor Total: 130**

**Today's Contractor  
Labor Total: 10**

**Today's Total**

**Labor Hours: 140**

**Total Project Labor  
Hours To Date:  
46860**

**Attachments**

**No Attachments  
Uploaded**

**Report Completed By**

**First Name**

**Anthony**

**Last Name**

**Laurendi**



**Report Date**

June 13, 2017

**Day of the Week**

Tuesday

**Report No.**

337

**Project No.**

P1138

**Weather High**

82°F


**Weather Low**

58°F

**Precipitation**

0.0

**Weather  
Conditions**

 **Sunny**

**Photo 1**



Welding procedures on additional 22' sheetpile for structural sheeting.

**Photo 2**



Grinding end of the 22' sheets in preparation for welding procedures.

**Photo 3**



Placing dunnage under floats for proper stockpiling in the laydown area.

**Photo 4**



Transporting sheetpile to the laydown area adjacent to the work area.

**Photo 5**



Utilizing PC360 equipped with variable moment hammer to drive structural sheetpile to desired elevation.

### **Video**

**No video uploaded.**

### **Work Performed by Severson**

-Continued welding procedures of structural

### **Planned Activities**

-Complete installation of structural sheeting.

sheetpile on south side of historic structure.

-Continued demobilization of water treatment plant.

-Transported sheets to sheetpile laydown area to prep new sheets for welds.

-Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.

-Continued to perform site maintenance.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

-Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

### Safety Remarks

-No accidents or incidents were reported.

-Conducted daily safety meeting at 7:00 AM  
Safety Topic: PPE for Site Tasks

### Work Performed by Subcontractors

-No subcontractors were on-site.

### Remarks/Verbal Directives

### Equipment/Materials Delivered to Site

-None.

-No equipment or materials  
were delivered to the site.

#### Miscellaneous Information

-None.

#### Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	



Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	
P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/16
996EF Float		4/18/16	5/30/16
Float		4/18/16	5/30/16
541E Scow	Single Scow	4/19/16	
540E Scow	Single Scow	4/19/16	
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	

1714E	Bag Filter	9/7/16
TW1253	Polisher	9/8/16
TW1252	Polisher	9/8/16
600-13	PC360	1/17/17
205-60E	Dump Truck	11/2/16

### Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		
VM Hammer	PVE		4/24/17	1		
Mini Track Loader	Toro		5/18/17	1		
Electric Core Machine	DP		5/18/17	1		

### Labor - Severson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
4	Operator	40

### Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Woodford Brothers	0
Mertec	0
Thew Associates	0

3	Laborer	30
1	DEC	10
3	AECOM	30

### Labor Totals

Today's Severson  
Labor Total: 130

Today's Contractor  
Labor Total: 0

Today's Total  
Labor Hours: 130

Total Project Labor  
Hours To Date:  
46990

### Attachments

No Attachments  
Uploaded

### Report Completed By

First Name

Last Name

Anthony

Laurendi

**Report Date**

June 14, 2017

**Day of the Week**

Wednesday

**Report No.**

338

**Project No.**

P1138

**Weather High**

77°F


**Weather Low**

55°F

**Precipitation**

0.0

**Weather  
Conditions**

 **Sunny**

**Photo 1**



Threaded additional 22' sheetpile for welding procedures.

**Photo 2**



Providing traffic control during demobilization of PC300 LF equipped with GPS.

**Photo 3**



Welding additional 22' sheetpile for structural sheeting installation on south side of the historic structure.

**Photo 4**



Continuing demobilization of the water treatment plant by removing hoses connecting storage tanks from pumps.

### **Video**

**No video uploaded.**

### **Work Performed by Severson**

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Continued demobilization of water treatment plant.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Demobilized PC300 LF equipped with GPS from the site.

### **Planned Activities**

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

-Continued to perform site maintenance.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

### **Safety Remarks**

-No accidents or incidents were reported.  
-Conducted daily safety meeting at 7:00 AM  
Safety Topic: Sheetpile  
Safety/Hearing Protection

### **Work Performed by Subcontractors**

-No subcontractors were on-site.

### **Remarks/Verbal Directives**

-None.

### **Equipment/Materials Delivered to Site**

-No equipment or materials were delivered to the site.



### Miscellaneous Information

-None.

### Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	

P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/16
996EF Float		4/18/16	5/30/16
Float		4/18/16	5/30/16
541E Scow	Single Scow	4/19/16	
540E Scow	Single Scow	4/19/16	
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	

## Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		
VM Hammer	PVE		4/24/17	1		

### Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
4	Operator	40
3	Laborer	30
1	DEC	10
3	AECOM	30

### Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Woodford Brothers	0
Mertec	0
Thew Associates	0

### Labor Totals

**Today's Sevenson  
Labor Total: 130**

**Today's Contractor  
Labor Total: 0**

**Today's Total  
Labor Hours: 130**

**Total Project Labor  
Hours To Date:  
47120**

### Attachments

No Attachments  
Uploaded

Report Completed By

First Name

Anthony

Last Name

Laurendi

**Report Date**

June 15, 2017

**Day of the Week**

Thursday

**Report No.**

339

**Project No.**

P1138

**Weather High**

81°F

**Weather Low**

64°F

**Precipitation**

0.0

**Weather  
Conditions**



Partly  
Cloudy

**Photo 1**



Prepping single scows for demobilization by scrapping clean sides and bottom of the scows.

**Photo 2**



Cutting leads into 22' sheetpile to ease with threading to previously installed sheets.

**Photo 3**



Driving welded sheetpile to grade with excavator mounted VM Hammer.

**Photo 4**



Pressure washing scows in preparation for demobilization.

### **Video**

**No video uploaded.**

### **Work Performed by Sevenson**

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Continued demobilization of water treatment plant.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Prepped single scows for demobilization from the site.

### **Planned Activities**

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.



-Continued to perform site maintenance.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

### **Safety Remarks**

-No accidents or incidents were reported.  
-Conducted daily safety meeting at 7:00 AM  
Safety Topic: Visual Communication with Operators/Site Security

### **Work Performed by Subcontractors**

-No subcontractors were on-site.

### **Remarks/Verbal Directives**

-None.

### **Equipment/Materials Delivered to Site**

-No equipment or materials were delivered to the site.

### Miscellaneous Information

-None.

### Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	

P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/16
996EF Float		4/18/16	5/30/16
Float		4/18/16	5/30/16
541E Scow	Single Scow	4/19/16	
540E Scow	Single Scow	4/19/16	
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	

## Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		
VM Hammer	PVE		4/24/17	1		
Mini Track Loader	Toro		5/18/17	1		
Electric Core Machine	DP		5/18/17	1		

#### Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
4	Operator	40
3	Laborer	30
1	DEC	10
3	AECOM	30

#### Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Woodford Brothers	0
Mertec	0
Thew Associates	0

#### Labor Totals

**Today's Sevenson  
Labor Total: 130**

**Today's Contractor  
Labor Total: 0**

**Today's Total**

Labor Hours: 130

Total Project Labor  
Hours To Date:  
47250

#### Attachments

No Attachments  
Uploaded

#### Report Completed By

First Name

Last Name

Anthony

Laurendi
