



NYSEG - MGP SITE
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 06/25/17

WEEK NO.: 99	HOURS ON SITE: 10/day	WRITTEN BY: Abby Chin	PROJECT NUMBER: 60430543	
Weather: Variable, 55°F to 82°F				
NAME:	TRADE:	COMPANY:	EQUIPMENT:	VISITORS/AFFILIATION:
George Fischer	Construction Oversight	AECOM	5 Barges	Eric Knapp - NYSDEC
Skylar Haas	CAMP Monitoring	AECOM	Smooth Drum Roller	Keith Stahle - AECOM
Chester Adams	Superintendent	SES	31EX Dozer	Jake Tudor - Cardno
Anthony Laurendi	Site Safety Officer	SES	Air compressor	Josiah Hartman - Cardno
William Conti	Laborer	SES	Push Boat	Ryan Allison - Cardno
George Schell	Operator	SES	Excavator with Hammer	Kevin Allman - Cardno
Tim Sheehan	Operator	SES	320 zero turn excavator	
Kevin Daunce	Operator	SES	2 Floats	
Zachary Thompson	Laborer	SES	PC360 Excavator	
Andrew Stein	Laborer	SES	Komatsu W380 Loader	
Derek Stein	Laborer	SES	Sky Jack High Reach Fd	
			3 Scows	
			PC 300 Excavator - LF	
			Push Boat	
AECOM Site hours this week - 80est.				
SUBCONTRACTORS:		SITE DELIVERIES (indicate size, type, and condition):		
Cardno				
WORKED PERFORMED BY Sevenson Environmental Services (SES)				
06/19/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Single scows were loaded and demobilized from the site. Provided assistance with mobilization of planting subcontractor. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				
06/20/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Continued to provide assistance with mobilization of planting subcontractor. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				
06/21/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Continued to provide assistance with planting installation with Cardno JF New. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				
06/22/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Continued to provide assistance with planting installation with Cardno JF New. Demobilized double prop push boat from the site. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				
06/23/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Continued to provide assistance with planting installation with Cardno JF New. Continued to perform site maintenance. Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.				



NYSEG - MGP SITE
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 06/25/17

WEEK NO.: 99	HOURS ON SITE: 10/day	WRITTEN BY: Abby Chin	PROJECT NUMBER: 60430543
WORK COMPLETED BY SES SUBCONTRACTORS			
Planting subcontractor, Cardno, on site for plantings in the Keuka Lake Outlet.			
AGREEMENTS MADE/CONVERSATIONS (Refer to telecons, phone records, and/or logbooks for details)			
Weekly meeting held 6/20/17. See minutes for details.			
SAMPLING PERFORMED:			
QUALITY CONTROL ACTIVITIES			
Ongoing erosion control inspections. Erosion control measures repaired as necessary.			
REQUEST FOR INFORMATION (RFI)			
TRANSMITTALS / SUBMITTALS			
Submittals reviewed and approved as noted in submittal register.			
VIBRATION/SETTLEMENT MONITORING COMMENTS:			
Settlement monitoring continues, very little movement observed at crack gauges. Have seen some temperature related movement. Data from Leica system shows normal temperature related oscillation. Sensor SP-07 was reconnected to the system which affected readings at the other sensors in the system. These fluctuations are not supported by the readings from the Leica system. The Geokon system will be re-plumbed and re-zeroed.			
Vibration monitoring is conducted daily within the former MGP structure and Water Street Wines & Spirits building. The vibration monitoring equipment shut down on 6/21, the modem was replaced on 6/22. SE room monitor was reinstalled and anchor bolt was replaced on 6/22. Multiple alert level exceedances due to driving sheet pile. One stop work exceedance on 6/21 in the NW room and one stop work exceedance on 6/19 and one stop work exceedance on 6/20 in the SE room due to personnel contact with the sensor.			
Turbidity monitoring conducted daily. No turbidity exceedances observed.			
AIR MONITORING COMMENTS:			
AECOM on site performing CAMP and noise monitoring. No CAMP exceedances observed.			
SAFETY OBSERVATIONS/VIOLATIONS/COMMENTS			
SES performing daily toolbox safety meetings. Approximately 48,080 site hours worked to date without incident.			
CORRECTIVE ACTIONS IMPLEMENTED			



NYSEG - MGP SITE
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 06/25/17

WEEK NO.: 99	HOURS ON SITE: 10/day	WRITTEN BY: Abby Chin	PROJECT NUMBER: 60430543
---------------------	------------------------------	------------------------------	---------------------------------

PHOTOS



SAV planting units - Bulrush



SAV planting units - Lilies



SAV planting units - Bulrush



Installation of bank area structural sheets after splice

STREAM STAGE MONITORING

DATE	WATER LEVEL (FROM KLA WEBSITE)
6/19/2017	714.16
6/20/2017	714.12
6/21/2017	714.09
6/22/2017	714.11
6/23/2017	714.12
6/24/2017	714.11
6/25/2017	714.12

**Construction
Manager (Signature):**

Project Construction Week: 06/19/2017-06/23/2017

Report Date: 6/26/2017

NYSEG

Penn Yan Former MGP Site Remedial Action

Penn Yan, New York
NYSDEC Site No. 8-62-009

Weather

Monday 06/19/2017: High 76.1° Cloudy, with 0.22" of rain and an average of 2.9 mph winds (Max 13.0 mph) directed in the northeast direction.

Tuesday 06/20/2017: High 77.8° Clear, with 0.00" of rain and an average of 3.8 mph winds (Max 21.0 mph) directed in the northeast direction.

Wednesday 06/21/2017: High 78.0° Partly cloudy, with 0.12" of rain and an average of 1.6 mph winds (Max 14.0 mph) directed in the northeast direction.

Thursday 06/22/2017: High 83.9° Clear, with 0.00" of rain and an average of 2.9 mph winds (Max 13.0 mph) directed in the northeast direction.

Friday 06/23/2017: High 79.3° Partly cloudy, with 0.00" of rain and an average of 3.2 mph winds (Max 17.0 mph) directed in the northeast direction.

Air/Noise Monitoring Levels within limits: Yes

Comments/Responses:

Equipment	ID	Station	Last Calibration
DustTrak II 8530	8530163902	Unit 1	9/20/2016
DustTrak II 8530	8530133403	Unit 2	3/7/2017
DustTrak II 8530	8530121503	Unit 3	4/12/2017
CEL-352 Noise Dosimeter	3111305	Canal, Water Street	Daily
MiniRAE 3000	592-907919	Unit 1	4/17/2017
MiniRAE 3000	592-907667	Unit 2	4/17/2017
MiniRAE 3000	592-906598	Unit 3	4/17/2017

NA-Not Available

Consultant's Verification: On behalf of the Consultant, I certify this report is complete and correct, and all materials and equipment used and work performed during this reporting period are in compliance with the contract plans and specifications, to the best of my knowledge, except as may be noted above.



Abby Chin

CAMP Review Personnel/ Signature

07/10/17

Date



WEEKLY CAMP & NOISE REPORT

Project Construction Week: 06/19/2017-06/23/2017

Report Date: 6/26/2017

ATTACHMENT #1 CAMP DATA

Table 1: Particulates Data

Date	Particulate Action Level (ug/m3)	Unit 1 Peak Particulates (µg/m³)	Unit 2 Peak Particulates(µg/m³)	Unit 3 Peak Particulates(µg/m³)	Comments
6/19/2017	150	-	-	-	No data collected due to rain
6/20/2017		14	12	39	
6/21/2017		13	17	8	
6/22/2017		-	-	-	No data collected due to humid conditions creating machine errors
6/23/2017		-	-	-	No data collected due to humid conditions creating machine errors

- 1. NA-Not Available.
- 2. All particulates data is presented as 15 minute peak averages.
- 3. **Bold** indicates recording in excess of alert level.
- 4. **Bold and highlighted** indicates recording in excess of stop work level.

Table 2: Noise Data

Date	Noise Action Level (dB)	Peak Noise (dB)	Comments
6/19/2017	90	55.2	
6/20/2017		56.9	
6/21/2017		55	
6/22/2017		55.3	
6/23/2017		55.4	

- 1. NA-Not Available.
- 2. **Bold** indicates exceedance observed.

Table 3: VOC Data

Date	VOC Action Level (ppm)	Unit 1 Peak VOC (ppm)	Unit 2 Peak VOC (ppm)	Unit 3 Peak VOC (ppm)	Comments
6/19/2017	5.0	-	-	-	No data collected due to rain
6/20/2017		0	0	1.519	
6/21/2017		0	0	0	
6/22/2017		-	-	-	No data collected due to humid conditions creating machine errors
6/23/2017		-	-	-	No data collected due to humid conditions creating machine errors

- 1. NA-Not Available.
- 2. All VOC data is presented as 15 minute peak averages.
- 3. **Bold** indicates recording in excess of alert level.
- 4. **Bold and highlighted** indicates recording in excess of stop work level.




WEEKLY CAMP & NOISE REPORT

Project Construction Week: 06/19/2017-06/23/2017

Report Date: 6/26/2017

ATTACHMENT #2 CAMP STATION LOCATIONS

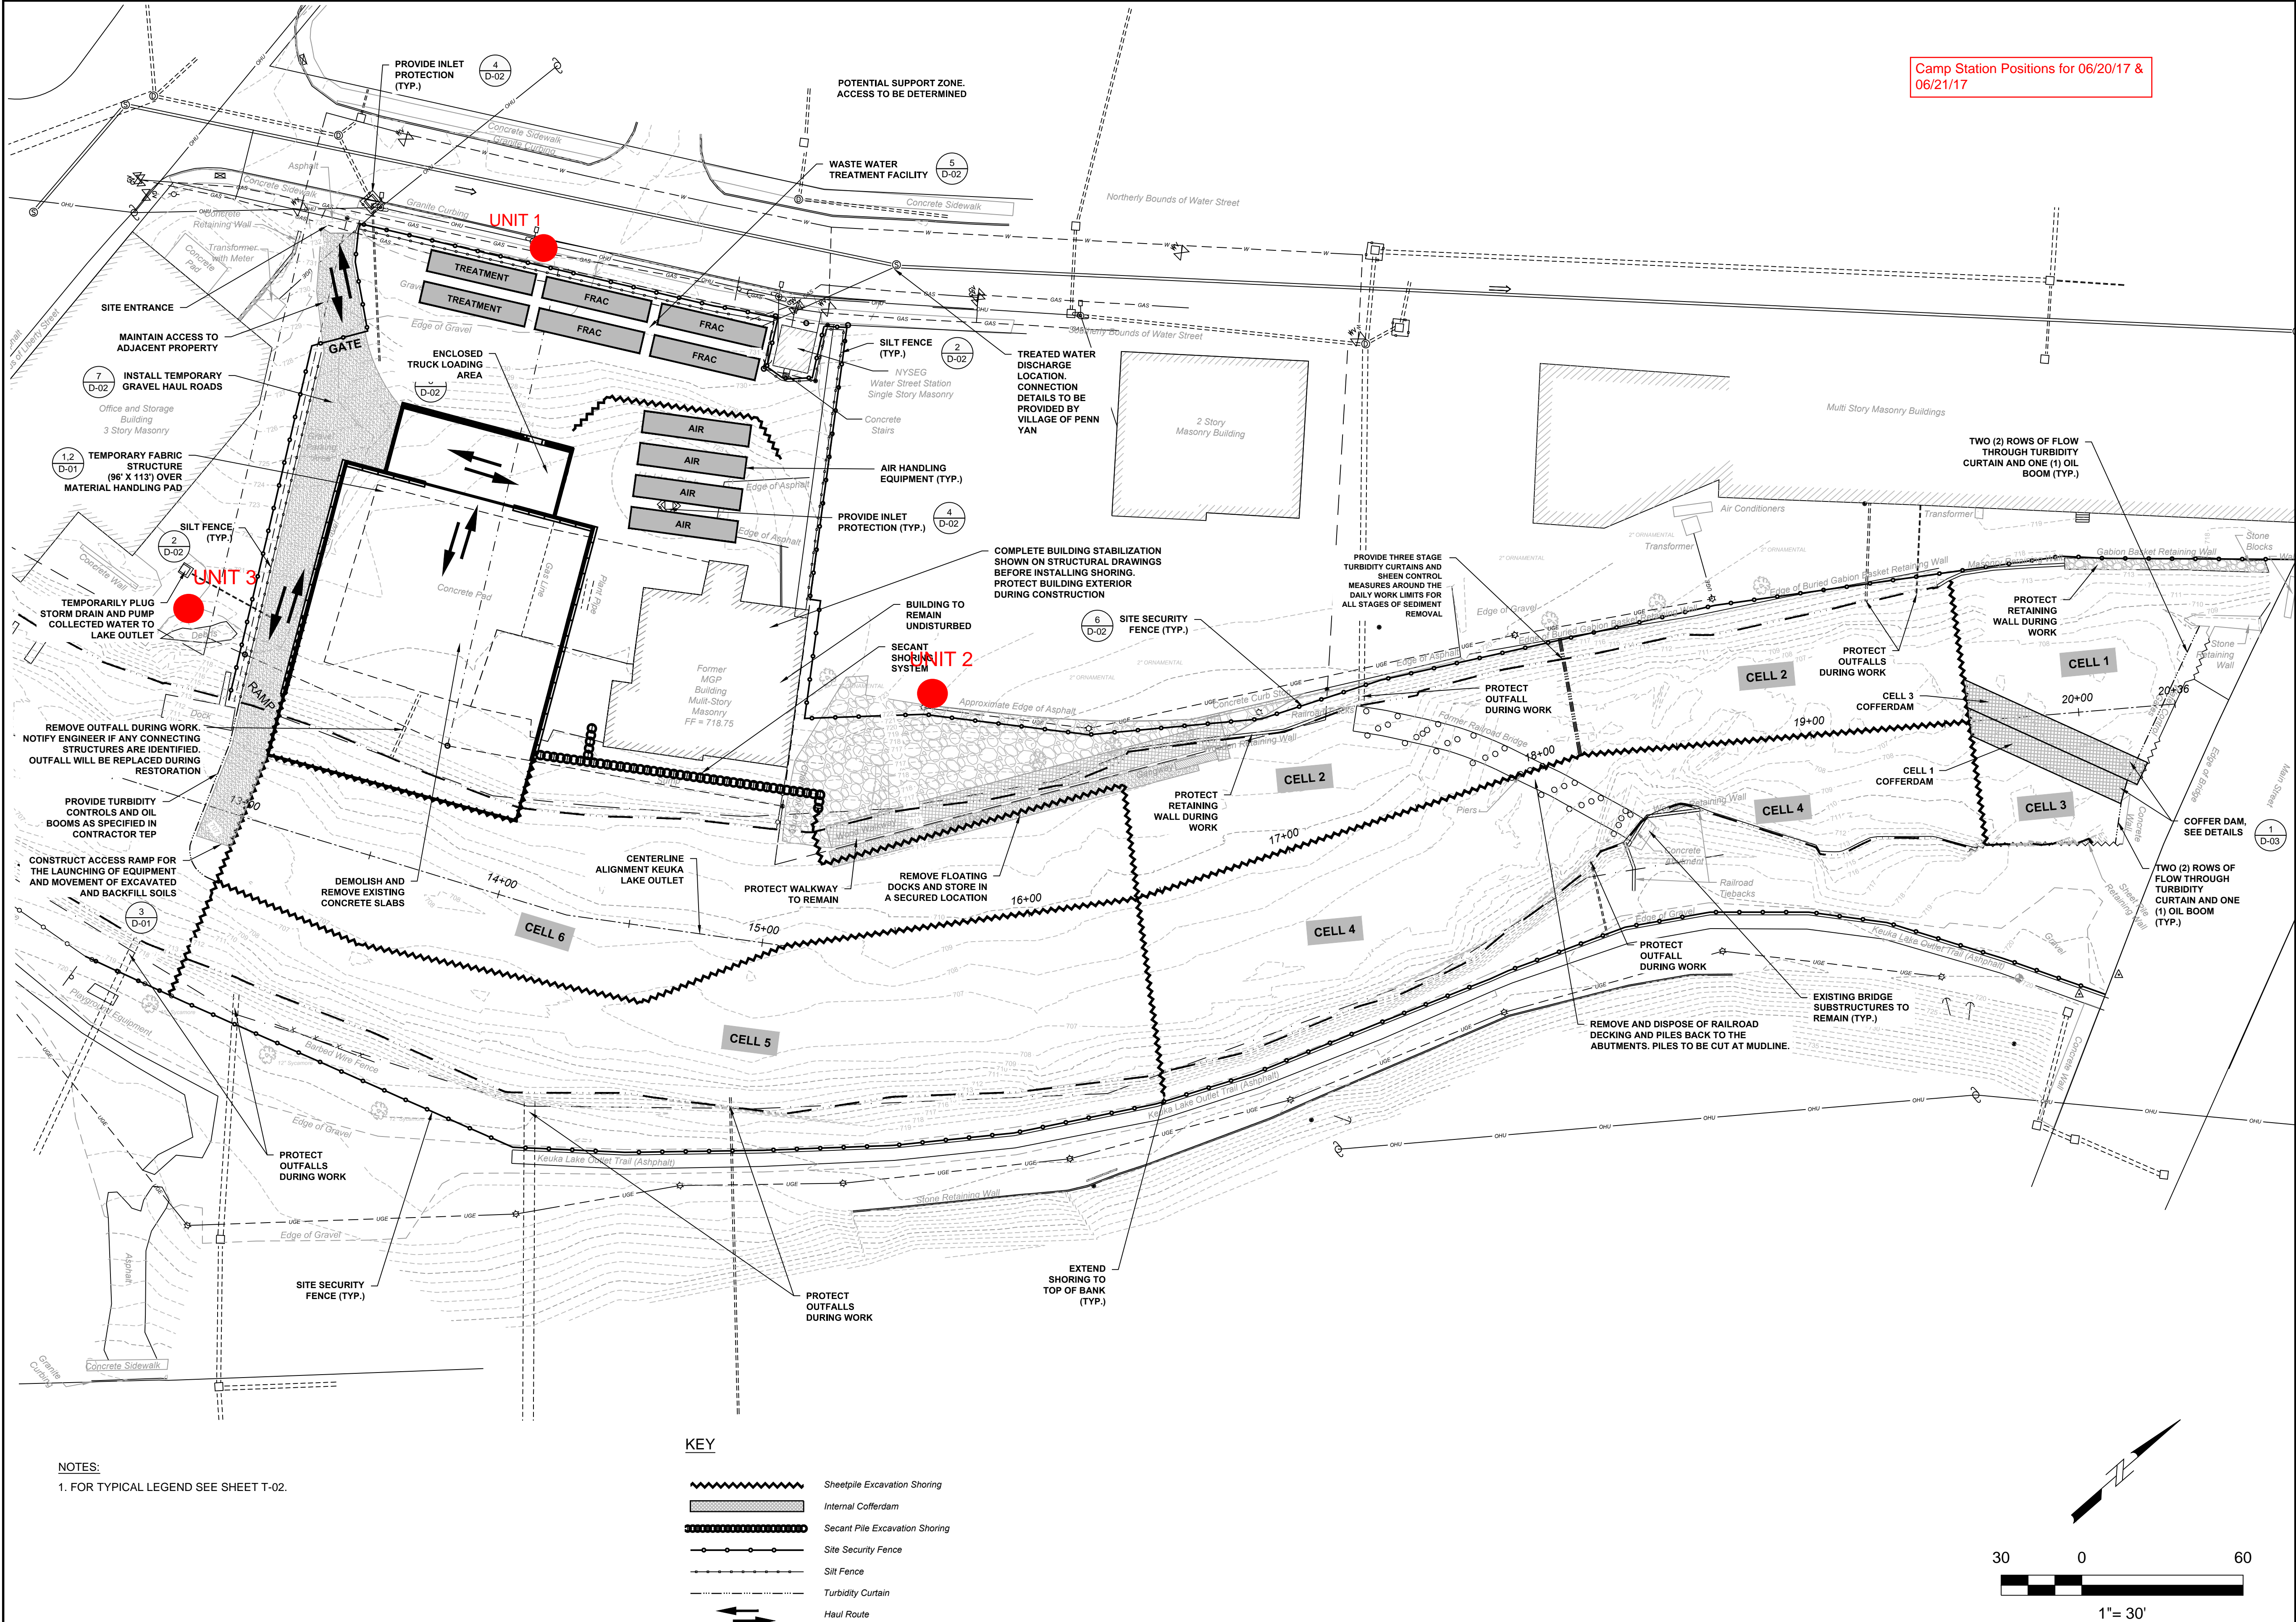

ISSUE/REVISION		
0	02-06-15	ISSUED FOR CONSTRUCTION
I/R	DATE	DESCRIPTION

	Upstream Low	Upstream High	Downstream Low	Downstream High	Within Reporting Limits	Working Day
Date	NTU	NTU	NTU	NTU	(Yes/No)	(Yes/No)
6/19/2017	1.1	7	0.6	29.9	Yes	Yes
6/20/2017	0.9	2.2	2	3.7	Yes	Yes
6/21/2017	0.6	1.8	0.7	15.9	Yes	Yes
6/22/2017	0.6	1.5	14.8	16.3	Yes	Yes
6/23/2017	0.7	1.5	10.3	16.1	Yes	Yes
6/24/2017	1.2	7.6	1.7	16.2	Yes	No
6/25/2017	1.2	4.8	5.4	20.5	Yes	No

High and Low values reported each 24 hr period for each day.

Reporting Limits: exceedance recorded if downstream value exceeds upstream value by 100NTU.

Shaded and Bold cells indicate turbidity reading exceeded reporting limits.

Report Date

June 19, 2017

Day of the Week

Monday

Report No.

340

Project No.

P1138

Weather High

75°F

Weather Low

67°F

Precipitation

0.0

**Weather
Conditions**



Partly
Cloudy

Photo 1



Transporting sheetpile from laydown area to the south side of the historic structure for welding and installation.

Photo 2



Planting subcontractor mobilized to the site in preparation for installation of aquatic beds.

Photo 3



Prepping 22' sheetpile for welding procedures.

Photo 4



Welding additional 22' sheetpile for structural sheeting installation.

Video

No video uploaded.

Work Performed by Severson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Single scows were loaded and demobilized from the site.
- Provided assistance with mobilization of planting subcontractor.

Planned Activities

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

-Continued to perform site maintenance.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

Safety Remarks

-No accidents or incidents were reported.
-Conducted daily safety meeting at 7:00 AM
Safety Topic: Sheetpile Safety

Work Performed by Subcontractors

-Planting subcontractor, Cardno, mobilized to the site and received deliveries of plantings for aquatic beds.

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-None.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	

P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/17
996EF Float		4/18/16	5/30/17
Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		
VM Hammer	PVE		4/24/17	1		

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
4	Operator	40
3	Laborer	30
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	40
Woodford Brothers	0
Mertec	0
Thew Associates	0

Labor Totals

**Today's Sevenson
Labor Total: 130**

**Today's Contractor
Labor Total: 40**

**Today's Total
Labor Hours: 170**

**Total Project Labor
Hours To Date:
47420**

Attachments

No Attachments
Uploaded

Report Completed By

First Name

Anthony

Last Name

Laurendi

Report Date

June 20, 2017

Day of the Week

Tuesday

Report No.

341

Project No.

P1138

Weather High

74°F

Weather Low

57°F

Precipitation

0.0

**Weather
Conditions**


 Sunny

Photo 1




Utilizing PC220 with Robovibe attachment to grab sheet from loader and thread for welding.

Photo 2



Continuing to weld additional 22' sheetpile for structural sheeting installation.

Photo 3

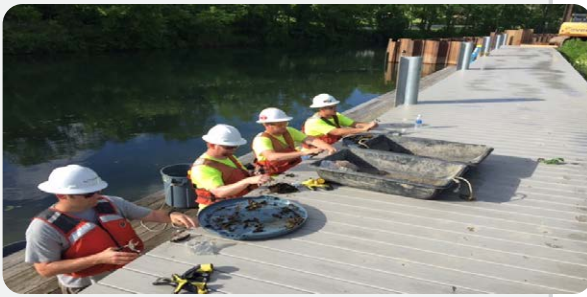

Planting subcontractor preparing plants for installation in the Keuka Lake Outlet.

Photo 4



Utilizing excavator mounted VM hammer to drive welded sheets to desired elevations.

Video

No video uploaded.

Work Performed by Sevenson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Continued to provide assistance with mobilization of planting subcontractor.
- Continued to perform site maintenance.

Planned Activities

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

Safety Remarks

-No accidents or incidents were reported.
-Conducted daily safety meeting at 7:00 AM
Safety Topic: Site Traffic

Work Performed by Subcontractors

-Planting subcontractor, Cardno, began prepping plantings for installation in the Keuka Lake Outlet.

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-None.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	
P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	

1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/17
996EF Float		4/18/16	5/30/17
Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	6/20/17

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
-------------------	------------	-------------	-------------	----------	------------	-------

Dumpster	Riccelli	40 CY Rolloff	7/14/15	1
Porta-Jon's	Larry's Latrines		7/14/15	3
Office Trailer	Modspace	60' x 12'	3/22/16	1
Office Trailer	Modspace	44' x 10'	3/23/16	1
VM Hammer	PVE		4/24/17	1

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
4	Operator	40
3	Laborer	30
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	40
Woodford Brothers	0
Mertec	0
Thew Associates	0

Labor Totals

**Today's Sevenson
Labor Total: 130**

**Today's Contractor
Labor Total: 40**

**Today's Total
Labor Hours: 170**

**Total Project Labor
Hours To Date:
47590**

Attachments

**No Attachments
Uploaded**

Report Completed By

First Name

Anthony

Last Name

Laurendi

Report Date

June 21, 2017

Day of the Week

Wednesday

Report No.

342

Project No.

P1138

Weather High

75°F

Weather Low

55°F

Precipitation

0.0

**Weather
Conditions**


 Sunny

Photo 1



Utilizing PC220 with Robovibe attachment to thread additional 22' sheetpile for welding.

Photo 2



Prepping installed 22' sheet pile for welding procedures.

Photo 3



Driving welded sheets to desired elevation utilizing PC360 with VM hammer.

Photo 4



Cardno beginning plantings near the Keuka Lake Outlet control structure.

Video

No video uploaded.

Work Performed by Severson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Continued to provide assistance with planting installation with Cardno JF New.
- Continued to perform site maintenance.

Planned Activities

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

Safety Remarks

-No accidents or incidents were reported.
-Conducted daily safety meeting at 7:00 AM
Safety Topic: Avoiding Complacency

Work Performed by Subcontractors

-Planting subcontractor, Cardno, plantings in the Keuka Lake Outlet.

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-None.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	
P259M Barge	Working Platform 50' x40'	4/6/16	

P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/17
996EF Float		4/18/16	5/30/17
Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	6/20/17

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
-------------------	------------	-------------	-------------	----------	------------	-------

Dumpster	Riccelli	40 CY Rolloff	7/14/15	1
Porta-Jon's	Larry's Latrines		7/14/15	3
Office Trailer	Modspace	60' x 12'	3/22/16	1
Office Trailer	Modspace	44' x 10'	3/23/16	1
VM Hammer	PVE		4/24/17	1

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
4	Operator	40
3	Laborer	30
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	40
Woodford Brothers	0
Mertec	0
Thew Associates	0

Labor Totals

**Today's Sevenson
Labor Total: 130**

**Today's Contractor
Labor Total: 40**

**Today's Total
Labor Hours: 170**

**Total Project Labor
Hours To Date:
47760**

Attachments

**No Attachments
Uploaded**

Report Completed By

First Name

Anthony

Last Name

Laurendi

Report Date

June 22, 2017

Day of the Week

Thursday

Report No.

343

Project No.

P1138

Weather High

82°F

Weather Low

70°F

Precipitation

0.0

**Weather
Conditions**


 **Sunny**

Photo 1



Excavator mounted variable moment hammer driving welded sheets to desired elevation.

Photo 2



Planting bulrush plants in the shallow fringes of the Keuka Lake Outlet.

Photo 3



Demobilization of double prop push boat from the site.

Photo 4



Certified welder conducting double v groove weld to structural sheetpile.

Video

No video uploaded.

Work Performed by Severson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Continued to provide assistance with planting installation with Cardno JF New.
- Demobilized double prop push boat from the site.

Planned Activities

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

-Continued to perform site maintenance.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

Safety Remarks

-No accidents or incidents were reported.
-Conducted daily safety meeting at 7:00 AM
Safety Topic: Traffic Control/Social Media Policy

Work Performed by Subcontractors

-Planting subcontractor, Cardno, plantings in the Keuka Lake Outlet.

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-None.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	

P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/17
996EF Float		4/18/16	5/30/17
Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	6/20/17

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		
VM Hammer	PVE		4/24/17	1		

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
3	Operator	30
2	Laborer	20
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	40
Woodford Brothers	0
Mertec	0
Thew Associates	0

Labor Totals

**Today's Sevenson
Labor Total: 110**

**Today's Contractor
Labor Total: 40**

**Today's Total
Labor Hours: 150**

**Total Project Labor
Hours To Date:
48080**

Attachments

No Attachments
Uploaded

Report Completed By

First Name

Anthony

Last Name

Laurendi

Report Date

June 23, 2017

Day of the Week

Friday

Report No.

344

Project No.

P1138

Weather High

81°F

Weather Low

63°F

Precipitation

0.0

**Weather
Conditions**


 **Sunny**

Photo 1



Prepping the 22' sheetpile for welding procedures with 6" grinder.

Photo 2



Welding additional 22' sheetpile to previously driven sheets to create 44' structural sheet.

Photo 3



Cardno JF New planting along the north bank of the Keuka Lake Outlet.

Photo 4



Driving welded sheetpile to desired elevation utilizing the excavator mounted VM hammer.

Video

No video uploaded.

Work Performed by Severson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Continued to provide assistance with planting installation with Cardno JF New.
- Demobilized double prop

Planned Activities

- Complete installation of structural sheeting.
- Begin plantings within the Keuka Lake Outlet prior to June 30th deadline.

push boat from the site.

-Continued to perform site maintenance.

-Continued maintenance of sidewalks and roads, implementing traffic control during delivery of materials.

Safety Remarks

-No accidents or incidents were reported.

-Conducted daily safety meeting at 7:00 AM

Safety Topic: Lightning Safety

Work Performed by Subcontractors

-Cardno continued plantings in the Keuka Lake Outlet as well as received the second shipment of plants for next week.

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-Planting subcontractor was also on-site Saturday June 24th to plant Valisneria within the Keuka Lake Outlet.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	

P229M Barge	Working Platform 50' x40'	4/6/16	
P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	
1287-92	Hydraulic Spud Winch	4/21/16	
1904E Scow		4/18/16	5/30/17
996EF Float		4/18/16	5/30/17
Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	6/22/17
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	6/20/17

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		
VM Hammer	PVE		4/24/17	1		

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
3	Operator	30
2	Laborer	20
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	40
Woodford Brothers	0
Mertec	0
Thew Associates	0

Labor Totals

**Today's Sevenson
Labor Total: 110**

**Today's Contractor
Labor Total: 40**

**Today's Total
Labor Hours: 150**

**Total Project Labor
Hours To Date:
48080**

Attachments



Report Completed By

First Name

Anthony

Last Name

Laurendi
