



NYSEG - MGP SITE
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 07/02/17

WEEK NO.: 100	HOURS ON SITE: 10/day	WRITTEN BY: Abby Chin	PROJECT NUMBER: 60430543	
Weather: Variable, 52°F to 83°F				
NAME:	TRADE:	COMPANY:	EQUIPMENT:	VISITORS/AFFILIATION:
George Fischer	Construction Oversight	AECOM	5 Barges	Eric Knapp - NYSDEC
Skylar Haas	CAMP Monitoring	AECOM	Smooth Drum Roller	Abby Chin - AECOM
Chester Adams	Superintendent	SES	31EX Dozer	John Ruspantini - NYSEG
Anthony Laurendi	Site Safety Officer	SES	Air compressor	Karis Manning - NYSDEC
William Conti	Laborer	SES	Push Boat	Ryan Allison - Cardno
Kevin Daunce	Operator	SES	Excavator with Hammer	Jack Tudor - Cardno
Tim Sheehan	Laborer	SES	320 zero turn excavator	
Derek Stein	Laborer	SES	2 Floats	
Andrew Stein	Laborer	SES	PC360 Excavator	
Zachary Thompson	Laborer	SES	Komatsu W380 Loader	
Matthew Thorpe	Project Manager	AECOM	Sky Jack High Reach Fd	
			3 Scows	
			PC 300 Excavator - LF	
			Push Boat	
AECOM Site hours this week - 100est.				
SUBCONTRACTORS:		SITE DELIVERIES (indicate size, type, and condition):		
Cardno				
Mertec				
WORKED PERFORMED BY Severson Environmental Services (SES)				
06/26/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Demobilized miscellaneous load of marine equipment including power packs, spuds, and spud pockets. Began removal of weeds and maintenance along the Birkett Landing dock located behind site fence.				
06/27/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Continued removal of weeds and maintenance along the Birkett Landing dock located behind site fence.				
06/28/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Prepped water treatment trailer for demobilization from the site.				
06/29/2017 - Continued welding procedures of structural sheetpile on south side of historic structure. Transported sheets to sheetpile laydown area to prep new sheets for welds. Continued preparation for welding 22' sheetpile by grinding sheets for weld joints. Assisted with demobilization of water treatment trailer from the site.				



NYSEG - MGP SITE
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 07/02/17

WEEK NO.: 100	HOURS ON SITE: 10/day	WRITTEN BY: Abby Chin	PROJECT NUMBER: 60430543
----------------------	------------------------------	------------------------------	---------------------------------

WORK COMPLETED BY SES SUBCONTRACTORS

Planting subcontractor, Cardno, was on site to complete installation of all species that had to be planted prior to the June 30th deadline.
Mertec was on-site to remove power to the water treatment trailer in preparation for demobilization.

AGREEMENTS MADE/CONVERSATIONS (Refer to telecons, phone records, and/or logbooks for details)

Weekly meeting held 6/27/17. See minutes for details.

SAMPLING PERFORMED:

QUALITY CONTROL ACTIVITIES

Ongoing erosion control inspections. Erosion control measures repaired as necessary.

REQUEST FOR INFORMATION (RFI)

TRANSMITTALS / SUBMITTALS

Submittals reviewed and approved as noted in submittal register.

VIBRATION/SETTLEMENT MONITORING COMMENTS:

Settlement monitoring continues, very little movement observed at crack gauges. Have seen some temperature related movement. Data from Leica system shows normal temperature related oscillation. Sensor SP-07 was reconnected to the system which affected readings at the other sensors in the system. These fluctuations are not supported by the readings from the Leica system. The Geokon system will be re-plumbed and re-zeroed.

Vibration monitoring is conducted daily within the former MGP structure. Multiple alert level exceedances due to sheet pile driving activities. These alert level events are generally only slightly over the alert level. The alert level exceedances seem to be from driving equipment along the south side of the building and not the installation of the sheeting.

Turbidity monitoring conducted daily. One turbidity exceedance (453.6 NTU) occurred on 7/1/17. No work was occurring on site, this peak in turbidity was due to a rain event.

AIR MONITORING COMMENTS:

AECOM on site performing CAMP and noise monitoring. No CAMP exceedances observed.

SAFETY OBSERVATIONS/VIOLATIONS/COMMENTS

SES performing daily toolbox safety meetings. Approximately 48,620 site hours worked to date without incident.

CORRECTIVE ACTIONS IMPLEMENTED



NYSEG - MGP SITE
Penn Yan, New York

Construction Manager Weekly Reports

DATE: Week ending 07/02/17

WEEK NO.: 100

HOURS ON SITE: 10/day

WRITTEN BY: Abby Chin

PROJECT NUMBER: 60430543

PHOTOS



SAV planting area in front of Birkett Landing Dock



SAV plants prior to planting prep - Valisneria Americana (Wild Celery)



New buoys installed in outlet by others



SES crew preparing to thread a top section of AZ-48 sheet pile to be spliced and driven to final depth

STREAM STAGE MONITORING

DATE	WATER LEVEL (FROM KLA WEBSITE)
6/26/2017	714.09
6/27/2017	714.04
6/28/2017	714.01
6/29/2017	714.01
6/30/2017	714.00
7/1/2017	714.11
7/2/2017	714.13

**Construction
Manager (Signature):**

Project Construction Week: 06/26/2017-06/29/2017

Report Date: 07/06/2017

NYSEG

Penn Yan Former MGP Site Remedial Action

**Penn Yan, New York
NYSDEC Site No. 8-62-009**

Weather

Monday 06/26/2017: High 72.6° Cloudy, with 0.05" of rain and an average of 2.9 mph winds (Max 21.0 mph) directed in the northeast direction.

Tuesday 06/27/2017: High 69.3° Cloudy, with 0.23" of rain and an average of 3.1 mph winds (Max 20.0 mph) directed in the northeast direction.

Wednesday 06/28/2017: High 79.0° Partly cloudy, with 0.00" of rain and an average of 2.1 mph winds (Max 14.0 mph) directed in the northeast direction.

Thursday 06/29/2017: High 81.8° Clear, with 0.00" of rain and an average of 2.9 mph winds (Max 18.0 mph) directed in the northeast direction.

Air/Noise Monitoring Levels within limits: Yes

Comments/Responses:

Equipment	ID	Station	Last Calibration
DustTrak II 8530	8530163902	Unit 1	9/20/2016
DustTrak II 8530	8530133403	Unit 2	3/7/2017
DustTrak II 8530	8530121503	Unit 3	4/12/2017
CEL-352 Noise Dosimeter	3111305	Canal, Water Street	Daily
MiniRAE 3000	592-907919	Unit 1	4/17/2017
MiniRAE 3000	592-907667	Unit 2	4/17/2017
MiniRAE 3000	592-906598	Unit 3	4/17/2017

NA-Not Available

Consultant's Verification: On behalf of the Consultant, I certify this report is complete and correct, and all materials and equipment used and work performed during this reporting period are in compliance with the contract plans and specifications, to the best of my knowledge, except as may be noted above.



Abby Chin

CAMP Review Personnel/ Signature

7/10/17

Date



WEEKLY CAMP & NOISE REPORT

Project Construction Week: 06/26/2017-06/29/2017

Report Date: 07/06/2017

ATTACHMENT #1 CAMP DATA

Table 1: Particulates Data

Date	Particulate Action Level (ug/m3)	Unit 1 Peak Particulates (µg/m³)	Unit 2 Peak Particulates(µg/m³)	Unit 3 Peak Particulates(µg/m³)	Comments
6/26/2017	150	-	-	-	No data collected due to rain
6/27/2017		-	-	-	No data collected due to rain
6/28/2017		14	17	11	
6/29/2017		23	22	23	

- 1. NA-Not Available.
- 2. All particulates data is presented as 15 minute peak averages.
- 3. **Bold** indicates recording in excess of alert level.
- 4. **Bold and highlighted** indicates recording in excess of stop work level.

Table 2: Noise Data

Date	Noise Action Level (dB)	Peak Noise (dB)	Comments
6/26/2017	90	60.4	
6/27/2017		56.7	
6/28/2017		54.6	
6/29/2017		57.8	

- 1. NA-Not Available.
- 2. **Bold** indicates exceedance observed.

Table 3: VOC Data

Date	VOC Action Level (ppm)	Unit 1 Peak VOC (ppm)	Unit 2 Peak VOC (ppm)	Unit 3 Peak VOC (ppm)	Comments
6/26/2017	5.0	-	-	-	No data collected due to rain
6/27/2017		-	-	-	No data collected due to rain
6/28/2017		0.419	1.905	0.068	
6/29/2017		0	2.27	0.754	

- 1. NA-Not Available.
- 2. All VOC data is presented as 15 minute peak averages.
- 3. **Bold** indicates recording in excess of alert level.
- 4. **Bold and highlighted** indicates recording in excess of stop work level.




WEEKLY CAMP & NOISE REPORT

Project Construction Week: 06/26/2017-06/29/2017

Report Date: 07/06/2017

ATTACHMENT #2 CAMP STATION LOCATIONS

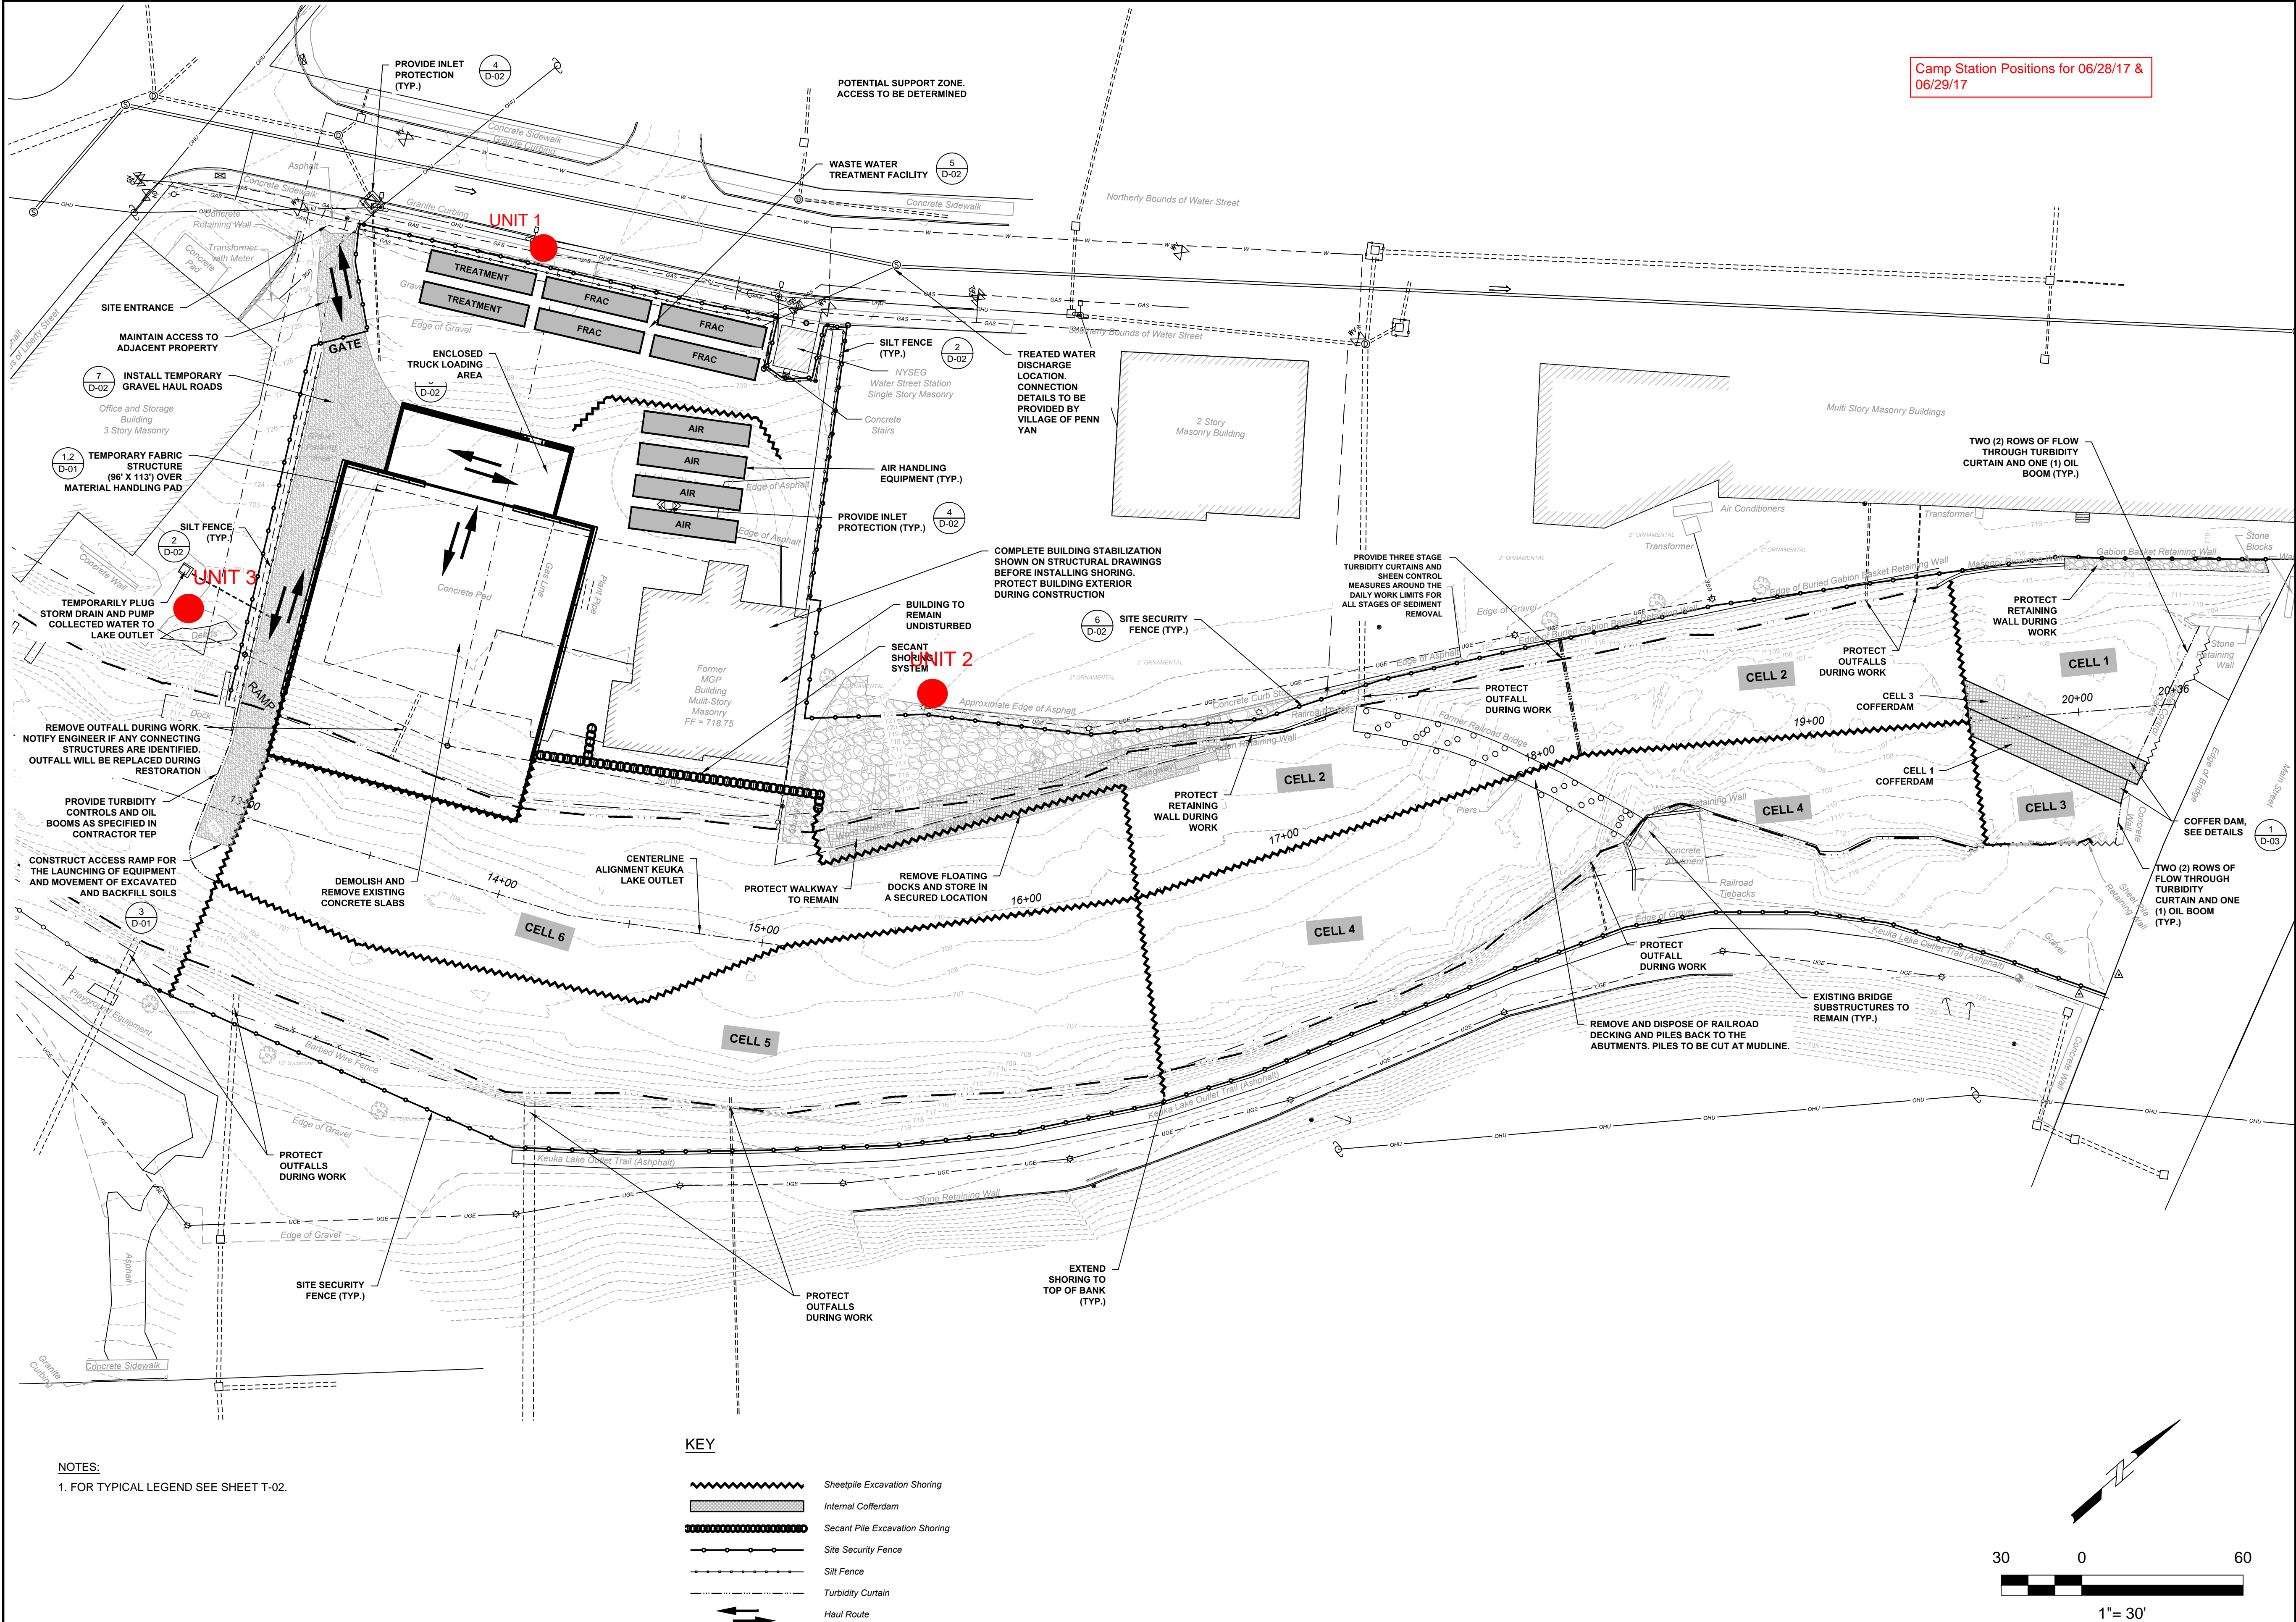

Camp Station Positions for 06/28/17 & 06/29/17

AECOM

PROJECT
100% REMEDIAL DESIGN
WATER STREET
MANUFACTURED GAS PLANT
VILLAGE OF PENN YAN
YATES COUNTY, NEW YORK
NYSDEC SITE # 8-62-009

CLIENT
NYSEG
New York State Electric and Gas Corp.
18 Link Drive
P.O. Box 5224
Binghamton, New York 13905

REGISTRATION

ISSUE/REVISION

0	02-06-15	ISSUED FOR CONSTRUCTION
I/R	DATE	DESCRIPTION

KEY PLAN

SHEET TITLE
SITE PREPARATION PLAN

SHEET NUMBER
C-02

	Upstream Low	Upstream High	Downstream Low	Downstream High	Within Reporting Limits	Working Day
Date	NTU	NTU	NTU	NTU	(Yes/No)	(Yes/No)
6/26/2017	0.9	2.3	2.6	669.6	No	Yes
6/27/2017	0.6	5.1	1.8	7.4	Yes	Yes
6/28/2017	0.4	1.7	0.6	4.2	Yes	Yes
6/29/2017	0.5	1.4	0.8	9.2	Yes	Yes
6/30/2017	0.5	10.3	0.6	1.1	Yes	No
7/1/2017	0.6	18.5	0.7	453.6	No	No
7/2/2017	0.9	3.2	2	2.3	Yes	No

Sonde most likely covered with debris

Rain event

High and Low values reported each 24 hr period for each day.

Reporting Limits: exceedance recorded if downstream value exceeds upstream value by 100NTU.

Shaded and Bold cells indicate turbidity reading exceeded reporting limits.

Report Date

June 26, 2017

Day of the Week

Monday

Report No.

345

Project No.

P1138

Weather High

70°F

Weather Low

53°F

Precipitation

0.0

**Weather
Conditions**



Rain

Photo 1



Threading 22' sheetpile utilizing PC220 with robovibe attachment.

Photo 2



Welding 22' sheetpile for structural sheeting installation along south side of the historic structure.

Photo 3



Demobilization of miscellaneous marine equipment including power packs, spuds, and spud pockets.

Photo 4



VM Hammer driving welded sheetpile to desired elevation.

Video

No video uploaded.

Work Performed by Severson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Demobilized miscellaneous load of marine equipment including power packs, spuds, and spud pockets.

Planned Activities

- Complete installation of structural sheeting.
- Complete plantings within the Keuka Lake Outlet prior to June 30th deadline.
- Demob necessary equipment and materials, secure site for shut down.

-Began removal of weeds and maintenance along the Birkett Landing dock located behind site fence.

Safety Remarks

-No accidents or incidents were reported.
-Conducted daily safety meeting at 7:00 AM
Safety Topic: Traffic Control

Work Performed by Subcontractors

-Planting subcontractor was not on-site today as they are awaiting shipment of remaining plants on Tuesday June 27th.

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-None.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	
P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	

1116-92	Winch Power Pack 80hp Poseidon	4/21/16	6/26/17
1287-92	Hydraulic Spud Winch	4/21/16	6/26/17
1904E Scow		4/18/16	5/30/17
996EF Float		4/18/16	5/30/17
Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	6/22/17
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	6/20/17

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
-------------------	------------	-------------	-------------	----------	------------	-------

Dumpster	Riccelli	40 CY Rolloff	7/14/15	1
Porta-Jon's	Larry's Latrines		7/14/15	3
Office Trailer	Modspace	60' x 12'	3/22/16	1
Office Trailer	Modspace	44' x 10'	3/23/16	1
VM Hammer	PVE		4/24/17	1

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
3	Operator	30
3	Laborer	30
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	0
Woodford Brothers	0
Mertec	0
Thew Associates	0

Labor Totals

**Today's Sevenson
Labor Total: 120**

**Today's Contractor
Labor Total: 0**

**Today's Total
Labor Hours: 120**

**Total Project Labor
Hours To Date:
48200**

Attachments



**Download
Attachment 1**

Report Completed By

First Name

Anthony

Last Name

Laurendi

Report Date

June 27, 2017

Day of the Week

Tuesday

Report No.

346

Project No.

P1138

Weather High

67°F

Weather Low

52°F

Precipitation

0.0

**Weather
Conditions**



Rain

Photo 1



Prepping sheets for welding procedures utilizing 6" grinder.

Photo 2



PC220 with Robovibe attachment grabbing prepped 22' sheet from laydown area.

Photo 3



Continuing weed removal throughout the site prior to demobilization.

Photo 4



Welding procedures on structural sheetpile on the south side of the historic structure.

Video

No video uploaded.

Work Performed by Sevenson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Continued removal of weeds and maintenance along the Birkett Landing dock located behind site fence.

Planned Activities

- Complete installation of structural sheeting.
- Complete plantings within the Keuka Lake Outlet prior to June 30th deadline.
- Demobilize necessary equipment and materials, secure site for shut down.

Safety Remarks

-No accidents or incidents were reported.
-Conducted daily safety meeting at 7:00 AM
Safety Topic: Weather Safety

Work Performed by Subcontractors

-Planting subcontractor received delivery of remaining plants and began prepping for installation tomorrow

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-None.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	
P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	6/26/17
1287-92	Hydraulic Spud Winch	4/21/16	6/26/17
1904E Scow		4/18/16	5/30/17

996EF Float		4/18/16	5/30/17
Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	6/22/17
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	6/20/17

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		

Office Trailer	Modspace	44' x 10'	3/23/16	1
VM Hammer	PVE		4/24/17	1

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
3	Operator	30
3	Laborer	30
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	10
Woodford Brothers	0
Mertec	0
Thew Associates	0

Labor Totals

Today's Sevenson
Labor Total: 120

Today's Contractor
Labor Total: 10

Today's Total
Labor Hours: 130

Total Project Labor
Hours To Date:
48330

Attachments

Download
Attachment 1

Report Completed By

First Name

Anthony

Last Name

Laurendi

Report Date

June 28, 2017

Day of the Week

Wednesday

Report No.

347

Project No.

P1138

Weather High

76°F

Weather Low

61°F

Precipitation

0.0

**Weather
Conditions**




Photo 1



Prepping 22' structural sheeting by cutting leads in sheets to ease in threading.

Photo 2



Transporting prepped sheetpile to the work area utilizing PC220 with Robovibe attachment.

Photo 3



Cardno JF New planting wild celery and american pond weed within the Outlet.

Photo 4



Driving structural sheetpile with excavator mounted variable moment hammer.

Video

No video uploaded.

Work Performed by Severson

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Prepped water treatment trailer for demobilization from the site.

Planned Activities

- Complete installation of structural sheeting.
- Complete plantings of cat tails within the Keuka Lake Outlet.
- Demobilize necessary equipment and materials, secure site for shut down.

Safety Remarks

-No accidents or incidents were reported.
-Conducted daily safety meeting at 7:00 AM
Safety Topic: PPE

Work Performed by Subcontractors

-Planting subcontractor received delivery of remaining plants and has completed installation of all species that had to be planted prior to the June 30th deadline.

-Mertec was on-site to remove power to the water treatment trailer in preparation for demobilization.

Remarks/Verbal Directives

-None.

Equipment/Materials Delivered to Site

-No equipment or materials were delivered to the site.

Miscellaneous Information

-None.

Contractor Equipment List

EQUIPMENT NAME	MAKE/MODEL	MOB DATE	DEMOB DATE
Bulldozer 408E	41 EX Dozer	11/18/15	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/08/15	
Excavator 783E	PC 220	11/23/15	
Excavator 563E	PC300	2/23/16	5/8/17
Excavator 1052-13	PC300 LF	8/24/16	6/14/17
Air Compressor 808E		2/23/16	
Loader 1124E	Komatsu WA 380	2/25/16	
P218M Barge	Working Platform 50' x40'	4/6/16	
P215M Barge	Working Platform 50' x40'	4/6/16	
P229M Barge	Working Platform 50' x40'	4/6/16	
P259M Barge	Working Platform 50' x40'	4/6/16	
P115O Barge	Working Platform 50' x40'	4/7/16	
1116-92	Winch Power Pack 80hp Poseidon	4/21/16	6/26/17
1287-92	Hydraulic Spud Winch	4/21/16	6/26/17
1904E Scow		4/18/16	5/30/17
996EF Float		4/18/16	5/30/17

Float		4/18/16	5/30/17
541E Scow	Single Scow	4/19/16	6/19/17
540E Scow	Single Scow	4/19/16	6/19/17
535E JCB		5/16/16	6/7/16
1037-12 320 Zero Turn		9/19/16	
1313-82 Push Boat	J-Boat Utility	7/21/16	6/22/17
1031-90	Terex RL 4000 Light Plant	9/6/16	
970-90	IR Light Plant	9/6/16	
1718E	Water Treatment Trailer	8/31/16	
1818E	Mixing Tank	8/30/16	
1816E	Mixing Tank	8/30/16	
1408E	Bag Filter	9/7/16	
1714E	Bag Filter	9/7/16	
TW1253	Polisher	9/8/16	
TW1252	Polisher	9/8/16	
600-13	PC360	1/17/17	
205-60E	Dump Truck	11/2/16	6/20/17

Rental Equipment List

EQUIPMENT NAME	MAKE/MODEL	DESCRIPTION	MOB DATE	QUANTITY	EQUIP #	HOURS
Dumpster	Riccelli	40 CY Rolloff	7/14/15	1		
Porta-Jon's	Larry's Latrines		7/14/15	3		
Office Trailer	Modspace	60' x 12'	3/22/16	1		
Office Trailer	Modspace	44' x 10'	3/23/16	1		

Labor - Sevenson

# OF PERSONNEL	TYPE OF PERSONNEL	HOURS WORKED
1	Project Engineer	10
1	Project Superintendent	10
3	Operator	30
3	Laborer	30
1	DEC	10
3	AECOM	30

Labor - Sub Contractors

SUB CONTRACTORS	HOURS WORKED
Cardno	30
Woodford Brothers	0
Mertec	20
Thew Associates	0

Labor Totals

**Today's Sevenson
Labor Total: 120**

**Today's Contractor
Labor Total: 50**

**Today's Total
Labor Hours: 170**

**Total Project Labor
Hours To Date:
48500**

Attachments

**Download
Attachme
nt 1**

Report Completed By

First Name

Anthony

Last Name

Laurendi

DATE

5/29/2017

WEEK DAY

Thursday

REPORT NO.

348

PROJECT NO.

1138

TEMP HIGH

83

TEMP LOW

69

PRECIP.

0

WEATHER

Partly Cloudy



Threading 22' structural sheeting along south side of the historic structure.



Prepping sheetpile for welding procedures.



Demobilization of waste water treatment trailer.



Excavator mounted variable moment hammer driving welded sheetpile to desired elevation.

WORK PERFORMED BY SEVENSON

- Continued welding procedures of structural sheetpile on south side of historic structure.
- Transported sheets to sheetpile laydown area to prep new sheets for welds.
- Continued preparation for welding 22' sheetpile by grinding sheets for weld joints.
- Assisted with demobilization of water treatment trailer from the site.

WORK PERFORMED BY SUBCONTRACTORS

- No subcontractors were on-site.

PLANNED ACTIVITIES

- Complete the structural sheetpile installation on south side of the historic structure.
- Demobilize equipment prior to shutdown.

SAFETY REMARKS

- No accidents or incidents were reported.
 - Conducted daily safety meeting at 7:00 AM
- Safety Topic: Traffic Control during Demobilization

REMARKS/VERBAL DIRECTIVES

- None.

EQUIPMENT/MATERIALS DELIVERED

- No equipment or materials were delivered to the site.

MISCELLANEOUS INFORMATION

-None.

CONTRACTOR EQUIPMENT

<i>Equipment Name</i>	<i>Make/Model</i>	<i>MOB Date</i>	<i>DEMOB Date</i>
Bulldozer 408E	41 EX Dozer	11/18/2015	
Smooth Drum Roller 315E	IR SD-115 D Roller	12/8/2015	
Excavator 783E	PC 220	11/23/2015	
Excavator 563E	PC300	2/23/2016	5/8/2017
Excavator 1052-13	PC300 LF	8/24/2016	6/14/2017
Air Compressor 808E		2/23/2016	
Loader 1124E	Komatsu WA 380	2/25/2016	
P218M Barge	Working Platform 50' x40'	4/6/2016	
P215M Barge	Working Platform 50' x40'	4/6/2016	
P229M Barge	Working Platform 50' x40'	4/6/2016	
P259M Barge	Working Platform 50' x40'	4/6/2016	
P1150 Barge	Working Platform 50' x40'	4/7/2016	
1116-92	Winch Power Pack 80hp Poseidon	4/21/2016	6/26/2017
1287-92	Hydraulic Spud Winch	4/21/2016	6/26/2017
1904E Scow		4/18/2016	5/30/2017
996EF Float		4/18/2016	5/30/2017
Float		4/18/2016	5/30/2017
541E Scow	Single Scow	4/19/2016	6/19/2017
540E Scow	Single Scow	4/19/2016	6/19/2017
535E JCB		5/16/2016	6/7/2017
1037-12 320 Zero Turn		9/19/2016	
1313-82 Push Boat	J-Boat Utility	7/21/2016	6/22/2017
1031-90	Terex RL 4000 Light Plant	9/6/2016	
970-90	IR Light Plant	9/6/2016	

1718E	Water Treatment Trailer	8/31/2016	6/29/2017
1818E	Mixing Tank	8/30/2016	
1816E	Mixing Tank	8/30/2016	
1408E	Bag Filter	9/7/2016	
1714E	Bag Filter	9/7/2016	
TW1253	Polisher	9/8/2016	
TW1252	Polisher	9/8/2016	
600-13	PC360	1/17/2017	
205-60E	Dump Truck	11/2/2016	6/20/2017

RENTAL EQUIPMENT

<i>Equipment Name</i>	<i>Make/Model</i>	<i>Description</i>	<i>MOB Date</i>	<i>Quantity</i>	<i>Equip #</i>
Dumpster	Riccelli	40 CY Rolloff	7/14/2015	1	
Porta-Jon's	Larry's Latrines		7/14/2015	3	
Office Trailer	Modspace	60' x 12'	3/22/2016	1	
Office Trailer	Modspace	44' x 10'	3/23/2016	1	
VM Hammer	PVE		4/24/2017	1	

SEVENSON LABOR

<i># of Personnel</i>	<i>Type of Personnel</i>	<i>Hours Worked</i>
1	Project Engineer	10
1	Project Superintendent	10
3	Operator	30

3	Laborer	30
1	DEC	10
3	AECOM	30

SUBCONTRACTOR LABOR

<i>Name</i>	<i>Position</i>	<i>Hours Worked</i>
Cardno	Aquatic Plantings	0
Woodford Brothers	Structural Stabilization	0
Mertec	Electrician	0
Thew Associates	Surveyor	0

Today's Severson Labor: **120** hours

Today's Contractor Labor: **0** hours

Today's Total Labor Hours: **120** hours

Project's Total Hours: **48620** hours

Report completed by

Anthony Laurendi
