

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/1/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:15 AM	0.022	7:11 AM	0.02	-0.002
7:30 AM	0.022	7:26 AM	0.026	0.004
7:45 AM	0.022	7:41 AM	0.026	0.004
8:00 AM	0.023	7:56 AM	0.024	0.001
8:15 AM	0.025	8:11 AM	0.027	0.002
8:30 AM	0.020	8:26 AM	0.03	0.010
8:45 AM	0.021	8:41 AM	0.03	0.009
9:00 AM	0.020	8:56 AM	0.031	0.011
9:15 AM	0.019	9:11 AM	0.028	0.009
9:30 AM	0.022	9:26 AM	0.027	0.005
9:45 AM	0.022	9:41 AM	0.029	0.007
10:00 AM	0.023	9:56 AM	0.029	0.006
10:15 AM	0.025	10:11 AM	0.029	0.004
10:30 AM	0.022	10:26 AM	0.029	0.007
10:45 AM	0.052	10:41 AM	0.033	-0.019
11:00 AM	0.021	10:56 AM	0.03	0.009
11:15 AM	0.036	11:11 AM	0.031	-0.005
11:30 AM	0.023	11:26 AM	0.031	0.008
11:45 AM	0.019	11:41 AM	0.029	0.010
12:00 PM	0.017	11:56 AM	0.03	0.013
12:15 PM	0.015	12:11 PM	0.03	0.015
12:30 PM	0.014	12:26 PM	0.029	0.015
12:45 PM	0.018	12:41 PM	0.031	0.013
1:00 PM	0.021	12:56 PM	0.033	0.012
1:15 PM	0.017	1:11 PM	0.031	0.014
1:30 PM	0.017	1:26 PM	0.031	0.014
1:45 PM	0.016	1:41 PM	0.037	0.021
2:00 PM	0.019	1:56 PM	0.034	0.015
2:15 PM	0.015	2:11 PM	0.036	0.021
2:30 PM	0.038	2:26 PM	0.036	-0.002
2:45 PM	0.022	2:41 PM	0.035	0.013
3:00 PM	0.015	2:56 PM	0.036	0.021

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/1/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:17 AM	0.0	7:12 AM	0.1	0.1
7:32 AM	0.1	7:27 AM	0.1	0.0
7:47 AM	0.1	7:42 AM	0.1	0.0
8:02 AM	0.1	7:57 AM	0.2	0.1
8:17 AM	0.1	8:12 AM	0.2	0.1
8:32 AM	0.1	8:27 AM	0.2	0.1
8:47 AM	0.1	8:42 AM	0.2	0.1
9:02 AM	0.1	8:57 AM	0.2	0.1
9:17 AM	0.1	9:12 AM	0.2	0.1
9:32 AM	0.1	9:27 AM	0.2	0.1
9:47 AM	0.1	9:42 AM	0.2	0.1
10:02 AM	0.1	9:57 AM	0.2	0.1
10:17 AM	0.1	10:12 AM	0.2	0.1
10:32 AM	0.1	10:27 AM	0.3	0.2
10:47 AM	0.1	10:42 AM	0.3	0.2
11:02 AM	0.2	10:57 AM	0.3	0.1
11:17 AM	0.2	11:12 AM	0.3	0.1
11:32 AM	0.2	11:27 AM	0.3	0.1
11:47 AM	0.2	11:42 AM	0.3	0.1
12:02 PM	0.2	11:57 AM	0.3	0.1
12:17 PM	0.2	12:12 PM	0.3	0.1
12:32 PM	0.2	12:27 PM	0.3	0.1
12:47 PM	0.2	12:42 PM	0.3	0.1
1:02 PM	0.2	12:57 PM	0.3	0.1
1:17 PM	0.1	1:12 PM	0.3	0.2
1:32 PM	0.1	1:27 PM	0.3	0.2
1:47 PM	0.1	1:42 PM	0.3	0.2
2:02 PM	0.1	1:57 PM	0.3	0.2
2:17 PM	0.1	2:12 PM	0.3	0.2
2:32 PM	0.1	2:27 PM	0.3	0.2
2:47 PM	0.1	2:42 PM	0.3	0.2
3:02 PM	0.1	2:57 PM	0.3	0.2

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/1/2022  
Times: 6:55 AM to 3:00 PM

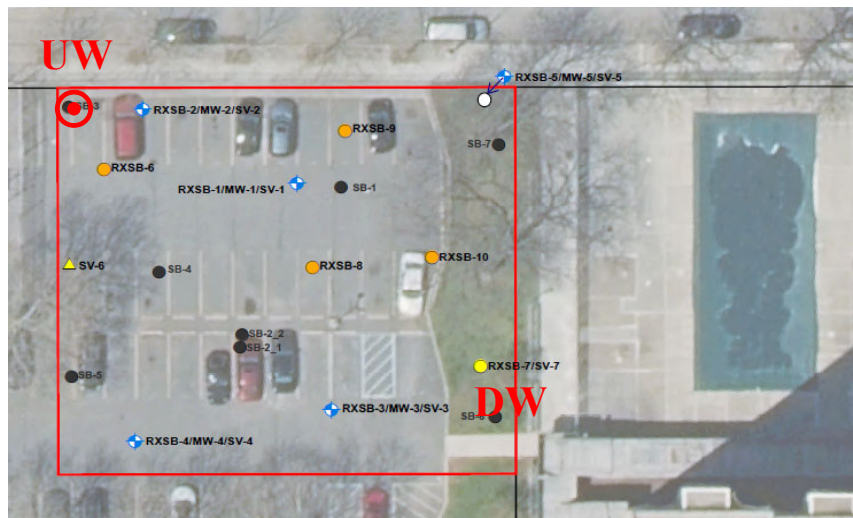

**Wind Direction**  
**WNW @ 10 mph**

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/2/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:22 AM	0.154	7:16 AM	0.01	-0.144
7:37 AM	0.072	7:31 AM	0.01	-0.062
7:52 AM	0.059	7:46 AM	0.013	-0.046
8:07 AM	0.059	8:01 AM	0.013	-0.046
8:22 AM	0.051	8:16 AM	0.016	-0.035
8:37 AM	0.056	8:31 AM	0.017	-0.039
8:52 AM	0.054	8:46 AM	0.018	-0.036
9:07 AM	0.044	9:01 AM	0.017	-0.027
9:22 AM	0.049	9:16 AM	0.016	-0.033
9:37 AM	0.041	9:31 AM	0.012	-0.029
9:52 AM	0.041	9:46 AM	0.013	-0.028
10:07 AM	0.050	10:01 AM	0.017	-0.033
10:22 AM	0.037	10:16 AM	0.019	-0.018
10:37 AM	0.050	10:31 AM	0.019	-0.031
10:52 AM	0.032	10:46 AM	0.019	-0.013
11:07 AM	0.053	11:01 AM	0.019	-0.034
11:22 AM	0.048	11:16 AM	0.018	-0.030
11:37 AM	0.056	11:31 AM	0.022	-0.034
11:52 AM	0.049	11:46 AM	0.02	-0.029
12:07 PM	0.003	12:01 PM	0.016	0.013
12:22 PM	0.003	12:16 PM	0.016	0.013
12:37 PM	0.124	12:31 PM	0.016	-0.108
12:52 PM	0.042	12:46 PM	0.024	-0.018
1:07 PM	0.041	1:01 PM	0.038	-0.003
1:22 PM	0.033	1:16 PM	0.027	-0.006
1:37 PM	0.031	1:31 PM	0.025	-0.006
1:52 PM	0.034	1:46 PM	0.026	-0.008
2:07 PM	0.049	2:01 PM	0.026	-0.023
2:22 PM	0.046	2:16 PM	0.032	-0.014
2:37 PM	0.025	2:31 PM	0.028	0.003
2:52 PM	NM	2:46 PM	0.024	NM

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/2/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:22 AM	0.1	7:18 AM	0.0	-0.1
7:37 AM	0.1	7:33 AM	0.1	0.0
7:52 AM	0.2	7:48 AM	0.1	-0.1
8:07 AM	0.2	8:03 AM	0.1	-0.1
8:22 AM	0.2	8:18 AM	0.1	-0.1
8:37 AM	0.2	8:33 AM	0.1	-0.1
8:52 AM	0.2	8:48 AM	0.2	0.0
9:07 AM	0.1	9:03 AM	0.2	0.1
9:22 AM	0.2	9:18 AM	0.2	0.0
9:37 AM	0.2	9:33 AM	0.2	0.0
9:52 AM	0.2	9:48 AM	0.2	0.0
10:07 AM	0.2	10:03 AM	0.2	0.0
10:22 AM	0.2	10:18 AM	0.2	0.0
10:37 AM	0.2	10:33 AM	0.2	0.0
10:52 AM	0.2	10:48 AM	0.2	0.0
11:07 AM	0.2	11:03 AM	0.2	0.0
11:22 AM	0.2	11:18 AM	0.2	0.0
11:37 AM	0.2	11:33 AM	0.2	0.0
11:52 AM	0.2	11:48 AM	0.2	0.0
12:07 PM	0.2	12:03 PM	0.2	0.0
12:22 PM	0.2	12:18 PM	0.2	0.0
12:37 PM	0.2	12:33 PM	0.2	0.0
12:52 PM	0.3	12:48 PM	0.2	-0.1
1:07 PM	0.3	1:03 PM	0.2	-0.1
1:22 PM	0.3	1:18 PM	0.2	-0.1
1:37 PM	0.3	1:33 PM	0.2	-0.1
1:52 PM	0.3	1:48 PM	0.2	-0.1
2:07 PM	0.3	2:03 PM	0.2	-0.1
2:22 PM	0.3	2:18 PM	0.2	-0.1
2:37 PM	0.3	2:33 PM	0.2	-0.1
2:52 PM	NM	2:48 PM	0.2	NM

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/2/2022  
Times: 7:00 AM to 2:55 PM

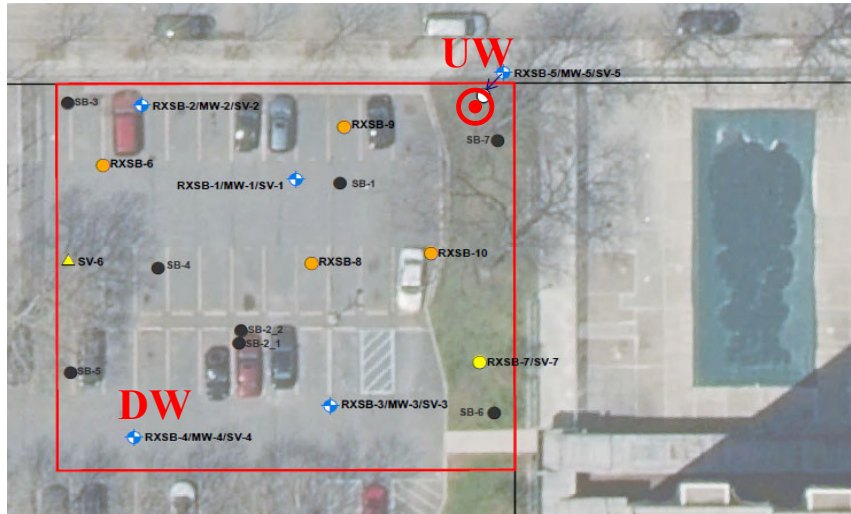

**Wind Direction**  
**NE @ 10 mph**

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/14/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:19 AM	0.015	7:14 AM	0.012	-0.003
7:34 AM	0.015	7:29 AM	0.014	-0.001
7:49 AM	0.015	7:44 AM	0.019	0.004
8:04 AM	0.016	7:59 AM	0.023	0.007
8:19 AM	0.016	8:14 AM	0.023	0.007
8:34 AM	0.012	8:29 AM	0.023	0.011
8:49 AM	0.012	8:44 AM	0.021	0.009
9:04 AM	0.012	8:59 AM	0.021	0.009
9:19 AM	0.012	9:14 AM	0.021	0.009
9:34 AM	0.012	9:29 AM	0.021	0.009
9:49 AM	0.015	9:44 AM	0.025	0.010
10:04 AM	0.015	9:59 AM	0.024	0.009
10:19 AM	0.016	10:14 AM	0.03	0.014
10:34 AM	0.017	10:29 AM	0.025	0.008
10:49 AM	0.015	10:44 AM	0.023	0.008
11:04 AM	0.013	10:59 AM	0.025	0.012
11:19 AM	0.013	11:14 AM	0.025	0.012
11:34 AM	0.012	11:29 AM	0.028	0.016
11:49 AM	0.013	11:44 AM	0.03	0.017
12:04 PM	0.011	11:59 AM	0.026	0.015
12:19 PM	0.015	12:14 PM	0.028	0.013
12:34 PM	0.013	12:29 PM	0.028	0.015
12:49 PM	0.018	12:44 PM	0.031	0.013
1:04 PM	0.018	12:59 PM	0.036	0.018
1:19 PM	0.014	1:14 PM	0.032	0.018
1:34 PM	0.026	1:29 PM	0.038	0.012
1:49 PM	0.018	1:44 PM	0.032	0.014
2:04 PM	0.014	1:59 PM	0.032	0.018
2:19 PM	0.014	2:14 PM	0.035	0.021
2:34 PM	0.012	2:29 PM	0.034	0.022
2:49 PM	0.013	2:44 PM	0.036	0.023
3:04 PM	0.012	2:59 PM	0.035	0.023

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**


Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/14/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:20 AM	0.0	7:16 AM	0.1	0.1
7:35 AM	0.0	7:31 AM	0.1	0.1
7:50 AM	0.0	7:46 AM	0.1	0.1
8:05 AM	0.0	8:01 AM	0.2	0.2
8:20 AM	0.0	8:16 AM	0.2	0.2
8:35 AM	0.0	8:31 AM	0.2	0.2
8:50 AM	0.0	8:46 AM	0.2	0.2
9:05 AM	0.0	9:01 AM	0.2	0.2
9:20 AM	0.0	9:16 AM	0.2	0.2
9:35 AM	0.0	9:31 AM	0.2	0.2
9:50 AM	0.0	9:46 AM	0.2	0.2
10:05 AM	0.1	10:01 AM	0.2	0.1
10:20 AM	0.1	10:16 AM	0.2	0.1
10:35 AM	0.1	10:31 AM	0.3	0.2
10:50 AM	0.1	10:46 AM	0.2	0.1
11:05 AM	0.1	11:01 AM	0.2	0.1
11:20 AM	0.2	11:16 AM	0.3	0.1
11:35 AM	0.2	11:31 AM	0.3	0.1
11:50 AM	0.1	11:46 AM	0.3	0.2
12:05 PM	0.1	12:01 PM	0.3	0.2
12:20 PM	0.1	12:16 PM	0.3	0.2
12:35 PM	0.1	12:31 PM	0.3	0.2
12:50 PM	0.1	12:46 PM	0.3	0.2
1:05 PM	0.2	1:01 PM	0.3	0.1
1:20 PM	0.2	1:16 PM	0.3	0.1
1:35 PM	0.1	1:31 PM	0.3	0.2
1:50 PM	0.1	1:46 PM	0.3	0.2
2:05 PM	0.1	2:01 PM	0.3	0.2
2:20 PM	0.1	2:16 PM	0.3	0.2
2:35 PM	0.1	2:31 PM	0.2	0.1
2:50 PM	0.1	2:46 PM	0.2	0.1
3:05 PM	0.1	3:01 PM	0.2	0.1

Notes:

NM - Not Measured

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/14/2022  
 Times: 7:00 AM to 3:05 PM

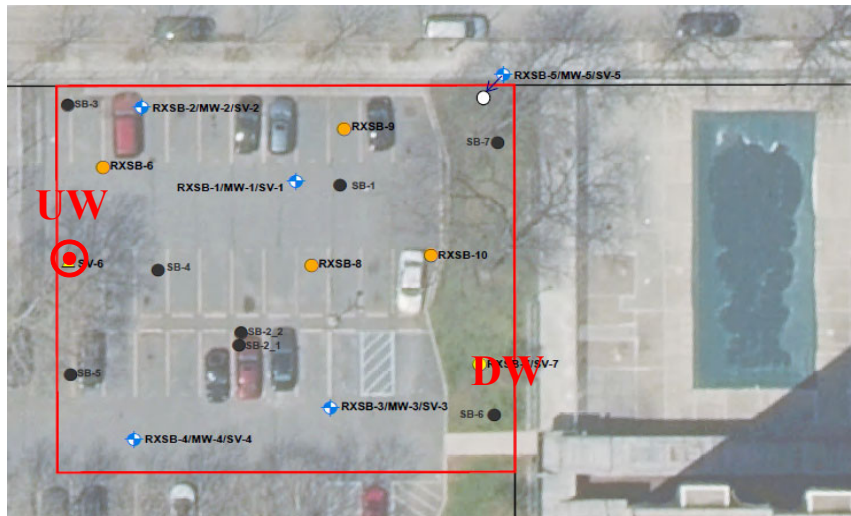

**Wind Direction**  
**WNW @ 8 mph**

2022-09-14 Park Lane Senior Daily CAMP Report

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/15/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:23 AM	0.013	7:17 AM	0.014	0.001
7:38 AM	0.015	7:32 AM	0.018	0.003
7:53 AM	0.013	7:47 AM	0.026	0.013
8:08 AM	0.013	8:02 AM	0.02	0.007
8:23 AM	0.013	8:17 AM	0.018	0.005
8:38 AM	0.014	8:32 AM	0.019	0.005
8:53 AM	0.020	8:47 AM	0.021	0.001
9:08 AM	0.015	9:02 AM	0.021	0.006
9:23 AM	0.016	9:17 AM	0.021	0.005
9:38 AM	0.017	9:32 AM	0.02	0.003
9:53 AM	0.018	9:47 AM	0.021	0.003
10:08 AM	0.017	10:02 AM	0.022	0.005
10:23 AM	0.014	10:17 AM	0.021	0.007
10:38 AM	0.013	10:32 AM	0.021	0.008
10:53 AM	0.015	10:47 AM	0.021	0.006
11:08 AM	0.014	11:02 AM	0.021	0.007
11:23 AM	0.014	11:17 AM	0.02	0.006
11:38 AM	0.016	11:32 AM	0.019	0.003
11:53 AM	0.011	11:47 AM	0.02	0.009
12:08 PM	0.008	12:02 PM	0.019	0.011
12:23 PM	0.008	12:17 PM	0.018	0.010
12:38 PM	0.009	12:32 PM	0.018	0.009
12:53 PM	0.031	12:47 PM	0.018	-0.013
1:08 PM	0.014	1:02 PM	0.024	0.010
1:23 PM	0.008	1:17 PM	0.018	0.010
1:38 PM	0.024	1:32 PM	0.021	-0.003
1:53 PM	0.013	1:47 PM	0.023	0.010
2:08 PM	0.011	2:02 PM	0.02	0.009
2:23 PM	0.014	2:17 PM	0.025	0.011
2:38 PM	0.019	2:32 PM	0.022	0.003
2:53 PM	0.019	2:47 PM	0.024	0.005
3:08 PM	0.011	3:02 PM	0.022	0.011

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/15/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:24 AM	0.0	7:19 AM	0.1	0.1
7:39 AM	0.0	7:34 AM	0.1	0.1
7:54 AM	0.0	7:49 AM	0.2	0.2
8:09 AM	0.0	8:04 AM	0.2	0.2
8:24 AM	0.0	8:19 AM	0.2	0.2
8:39 AM	0.0	8:34 AM	0.2	0.2
8:54 AM	0.0	8:49 AM	0.2	0.2
9:09 AM	0.0	9:04 AM	0.2	0.2
9:24 AM	0.0	9:19 AM	0.2	0.2
9:39 AM	0.0	9:34 AM	0.2	0.2
9:54 AM	0.0	9:49 AM	0.2	0.2
10:09 AM	0.0	10:04 AM	0.2	0.2
10:24 AM	0.0	10:19 AM	0.2	0.2
10:39 AM	0.0	10:34 AM	0.2	0.2
10:54 AM	0.1	10:49 AM	0.2	0.1
11:09 AM	0.1	11:04 AM	0.2	0.1
11:24 AM	0.1	11:19 AM	0.2	0.1
11:39 AM	0.1	11:34 AM	0.2	0.1
11:54 AM	0.1	11:49 AM	0.2	0.1
12:09 PM	0.1	12:04 PM	0.2	0.1
12:24 PM	0.1	12:19 PM	0.2	0.1
12:39 PM	0.1	12:34 PM	0.2	0.1
12:54 PM	0.1	12:49 PM	0.2	0.1
1:09 PM	0.1	1:04 PM	0.2	0.1
1:24 PM	0.1	1:19 PM	0.2	0.1
1:39 PM	0.1	1:34 PM	0.2	0.1
1:54 PM	0.1	1:49 PM	0.2	0.1
2:09 PM	0.1	2:04 PM	0.2	0.1
2:24 PM	0.0	2:19 PM	0.2	0.2
2:39 PM	0.1	2:34 PM	0.2	0.1
2:54 PM	0.1	2:49 PM	0.2	0.1
3:09 PM	0.0	3:04 PM	0.2	0.2

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/15/2022  
Times: 7:00 AM to 3:05 PM

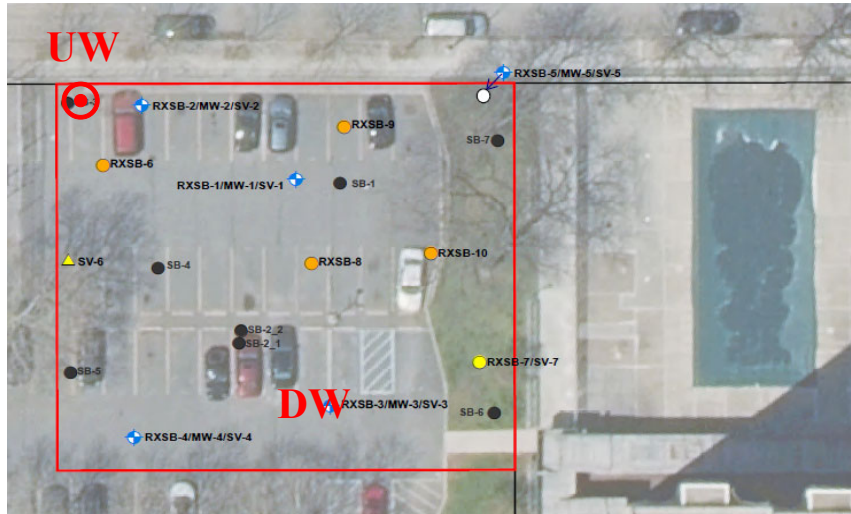

Wind Direction  
N @ 15 mph

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/16/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:21 AM	0.011	7:18 AM	0.005	-0.006
7:36 AM	0.007	7:33 AM	0.009	0.002
7:51 AM	0.009	7:48 AM	0.01	0.001
8:06 AM	0.016	8:03 AM	0.018	0.002
8:21 AM	0.016	8:18 AM	0.014	-0.002
8:36 AM	0.008	8:33 AM	0.014	0.006
8:51 AM	0.008	8:48 AM	0.015	0.007
9:06 AM	0.006	9:03 AM	0.016	0.010
9:21 AM	0.006	9:18 AM	0.013	0.007
9:36 AM	0.006	9:33 AM	0.017	0.011
9:51 AM	0.024	9:48 AM	0.017	-0.007
10:06 AM	0.011	10:03 AM	0.015	0.004
10:21 AM	0.006	10:18 AM	0.015	0.009
10:36 AM	0.009	10:33 AM	0.017	0.008
10:51 AM	0.026	10:48 AM	0.018	-0.008
11:06 AM	0.082	11:03 AM	0.018	-0.064
11:21 AM	0.034	11:18 AM	0.019	-0.015
11:36 AM	0.010	11:33 AM	0.018	0.008
11:51 AM	0.005	11:48 AM	0.018	0.013
12:06 PM	0.012	12:03 PM	0.019	0.007
12:21 PM	0.007	12:18 PM	0.02	0.013
12:36 PM	0.006	12:33 PM	0.02	0.014
12:51 PM	0.011	12:48 PM	0.021	0.010
1:06 PM	0.014	1:03 PM	0.024	0.010
1:21 PM	0.009	1:18 PM	0.023	0.014
1:36 PM	0.010	1:33 PM	0.022	0.012
1:51 PM	0.014	1:48 PM	0.026	0.012
2:06 PM	0.009	2:03 PM	0.022	0.013
2:21 PM	0.011	2:18 PM	0.025	0.014
2:36 PM	0.007	2:33 PM	0.023	0.016
2:51 PM	0.007	2:48 PM	0.023	0.016

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/16/2022



Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:23 AM	0.0	7:20 AM	0.0	0.0
7:38 AM	0.0	7:35 AM	0.0	0.0
7:53 AM	0.0	7:50 AM	0.0	0.0
8:08 AM	0.0	8:05 AM	0.0	0.0
8:23 AM	0.0	8:20 AM	0.0	0.0
8:38 AM	0.0	8:35 AM	0.0	0.0
8:53 AM	0.0	8:50 AM	0.0	0.0
9:08 AM	0.0	9:05 AM	0.0	0.0
9:23 AM	0.0	9:20 AM	0.0	0.0
9:38 AM	0.0	9:35 AM	0.0	0.0
9:53 AM	0.0	9:50 AM	0.0	0.0
10:08 AM	0.0	10:05 AM	0.0	0.0
10:23 AM	0.0	10:20 AM	0.0	0.0
10:38 AM	0.0	10:35 AM	0.0	0.0
10:53 AM	0.0	10:50 AM	0.0	0.0
11:08 AM	0.0	11:05 AM	0.0	0.0
11:23 AM	0.0	11:20 AM	0.0	0.0
11:38 AM	0.0	11:35 AM	0.0	0.0
11:53 AM	0.0	11:50 AM	0.0	0.0
12:08 PM	0.0	12:05 PM	0.0	0.0
12:23 PM	0.0	12:20 PM	0.0	0.0
12:38 PM	0.0	12:35 PM	0.0	0.0
12:53 PM	0.0	12:50 PM	0.0	0.0
1:08 PM	0.0	1:05 PM	0.0	0.0
1:23 PM	0.0	1:20 PM	0.0	0.0
1:38 PM	0.0	1:35 PM	0.0	0.0
1:53 PM	0.0	1:50 PM	0.0	0.0
2:08 PM	0.0	2:05 PM	0.0	0.0
2:23 PM	0.0	2:20 PM	0.0	0.0
2:38 PM	0.0	2:35 PM	0.0	0.0
2:53 PM	0.0	2:50 PM	0.0	0.0

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/16/2022  
Times: 7:00 AM to 2:55 PM

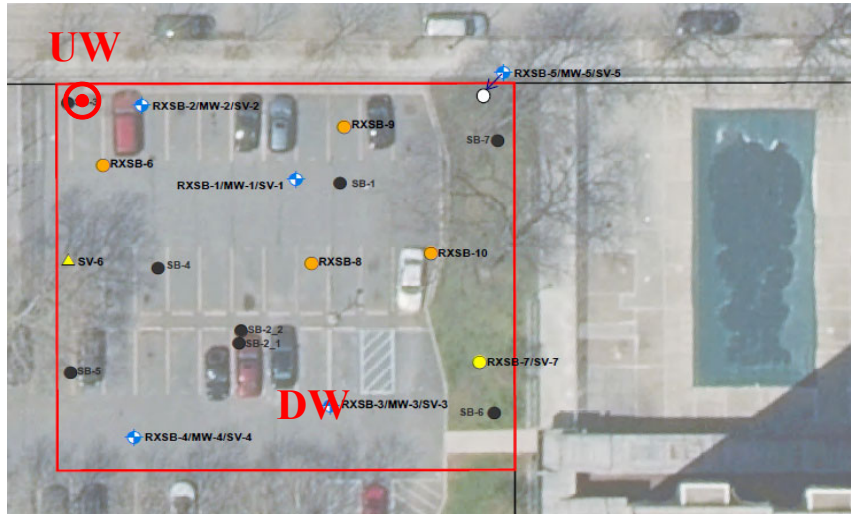

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/19/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:31 AM	NM	7:22 AM	0.045	NM
7:46 AM	NM	7:37 AM	0.04	NM
8:01 AM	NM	7:52 AM	0.041	NM
8:16 AM	0.035	8:07 AM	0.041	0.006
8:31 AM	0.034	8:22 AM	0.051	0.018
8:46 AM	0.038	8:37 AM	0.045	0.011
9:01 AM	0.035	8:52 AM	0.05	0.015
9:16 AM	0.033	9:07 AM	0.045	0.011
9:31 AM	0.034	9:22 AM	0.047	0.010
9:46 AM	0.035	9:37 AM	0.05	0.015
10:01 AM	0.034	9:52 AM	0.048	0.015
10:16 AM	0.037	10:07 AM	0.049	0.016
10:31 AM	0.035	10:22 AM	0.05	0.020
10:46 AM	0.033	10:37 AM	0.048	0.017
11:01 AM	0.033	10:52 AM	0.055	0.025
11:16 AM	0.030	11:07 AM	0.05	0.021
11:31 AM	0.031	11:22 AM	0.048	0.019
11:46 AM	0.030	11:37 AM	0.049	0.019
12:01 PM	0.029	11:52 AM	0.048	0.018
12:16 PM	0.029	12:07 PM	0.048	0.019
12:31 PM	0.030	12:22 PM	0.049	0.020
12:46 PM	0.030	12:37 PM	0.051	0.022
1:01 PM	0.029	12:52 PM	0.051	0.022
1:16 PM	0.029	1:07 PM	0.051	0.021
1:31 PM	0.029	1:22 PM	0.052	0.020
1:46 PM	0.029	1:37 PM	0.053	0.021
2:01 PM	0.030	1:52 PM	0.053	0.023
2:16 PM	0.032	2:07 PM	0.055	0.021
2:31 PM	0.032	2:22 PM	0.058	0.058
2:46 PM	0.030	2:37 PM	0.055	0.055
3:01 PM	0.034	2:52 PM	0.056	0.056

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/19/2022



Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:28 AM	0.0	7:23 AM	0.1	0.1
7:43 AM	0.1	7:38 AM	0.1	0.0
7:58 AM	0.0	7:53 AM	0.1	0.1
8:13 AM	0.1	8:08 AM	0.1	0.0
8:28 AM	0.1	8:23 AM	0.2	0.1
8:43 AM	0.1	8:38 AM	0.2	0.1
8:58 AM	0.1	8:53 AM	0.2	0.1
9:13 AM	0.1	9:08 AM	0.2	0.1
9:28 AM	0.1	9:23 AM	0.2	0.1
9:43 AM	0.1	9:38 AM	0.2	0.1
9:58 AM	0.1	9:53 AM	0.2	0.1
10:13 AM	0.0	10:08 AM	0.2	0.2
10:28 AM	0.0	10:23 AM	0.2	0.2
10:43 AM	0.0	10:38 AM	0.2	0.2
10:58 AM	0.0	10:53 AM	0.2	0.2
11:13 AM	0.0	11:08 AM	0.2	0.2
11:28 AM	0.0	11:23 AM	0.2	0.2
11:43 AM	0.0	11:38 AM	0.2	0.2
11:58 AM	0.0	11:53 AM	0.2	0.2
12:13 PM	0.0	12:08 PM	0.2	0.2
12:28 PM	0.0	12:23 PM	0.2	0.2
12:43 PM	0.0	12:38 PM	0.2	0.2
12:58 PM	0.0	12:53 PM	0.2	0.2
1:13 PM	0.0	1:08 PM	0.2	0.2
1:28 PM	0.0	1:23 PM	0.2	0.2
1:43 PM	0.0	1:38 PM	0.2	0.2
1:58 PM	0.0	1:53 PM	0.2	0.2
2:13 PM	0.0	2:08 PM	0.2	0.2
2:28 PM	0.0	2:23 PM	0.2	0.2
2:43 PM	0.0	2:38 PM	0.2	0.2
2:58 PM	0.0	2:53 PM	0.2	0.2

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/19/2022  
Times: 7:05 AM to 3:05 PM

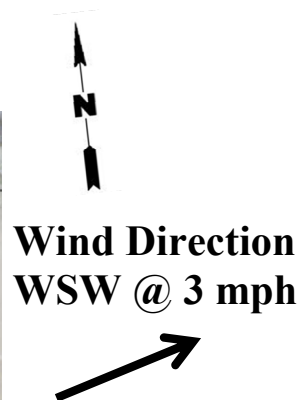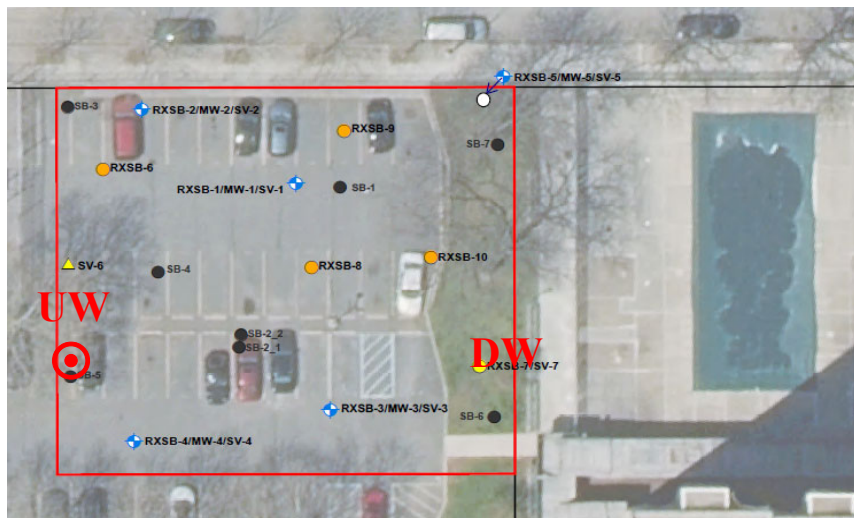

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/20/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:20 AM	0.026	7:16 AM	0.03	0.004
7:35 AM	0.062	7:31 AM	0.034	-0.028
7:50 AM	0.051	7:46 AM	0.039	-0.012
8:05 AM	0.03	8:01 AM	0.032	0.002
8:20 AM	0.027	8:16 AM	0.036	0.009
8:35 AM	0.024	8:31 AM	0.032	0.008
8:50 AM	0.019	8:46 AM	0.028	0.009
9:05 AM	0.017	9:01 AM	0.027	0.010
9:20 AM	0.017	9:16 AM	0.026	0.009
9:35 AM	0.021	9:31 AM	0.029	0.008
9:50 AM	0.035	9:46 AM	0.034	-0.001
10:05 AM	0.021	10:01 AM	0.032	0.011
10:20 AM	0.031	10:16 AM	0.03	-0.001
10:35 AM	0.022	10:31 AM	0.03	0.008
10:50 AM	0.016	10:46 AM	0.029	0.013
11:05 AM	0.015	11:01 AM	0.029	0.014
11:20 AM	0.016	11:16 AM	0.028	0.012
11:35 AM	0.016	11:31 AM	0.028	0.012
11:50 AM	0.018	11:46 AM	0.03	0.012
12:05 PM	0.017	12:01 PM	0.029	0.012
12:20 PM	0.015	12:16 PM	0.029	0.014
12:35 PM	0.015	12:31 PM	0.027	0.012
12:50 PM	0.024	12:46 PM	0.032	0.008
1:05 PM	0.018	1:01 PM	0.037	0.019
1:20 PM	0.016	1:16 PM	0.032	0.016
1:35 PM	0.021	1:31 PM	0.031	0.010
1:50 PM	0.025	1:46 PM	0.031	0.006
2:05 PM	0.014	2:01 PM	0.03	0.016
2:20 PM	0.014	2:16 PM	0.029	0.015
2:35 PM	0.023	2:31 PM	0.062	0.039
2:50 PM	0.02	2:46 PM	0.046	0.026
3:05 PM	NM	3:01 PM	0.03	NM

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/20/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:21 AM	0.0	7:17 AM	0.1	0.1
7:36 AM	0.0	7:32 AM	0.1	0.1
7:51 AM	0.0	7:47 AM	0.1	0.1
8:06 AM	0.0	8:02 AM	0.2	0.2
8:21 AM	0.0	8:17 AM	0.2	0.2
8:36 AM	0.0	8:32 AM	0.2	0.2
8:51 AM	0.0	8:47 AM	0.2	0.2
9:06 AM	0.0	9:02 AM	0.2	0.2
9:21 AM	0.0	9:17 AM	0.2	0.2
9:36 AM	0.0	9:32 AM	0.2	0.2
9:51 AM	0.0	9:47 AM	0.2	0.2
10:06 AM	0.0	10:02 AM	0.2	0.2
10:21 AM	0.0	10:17 AM	0.2	0.2
10:36 AM	0.0	10:32 AM	0.3	0.3
10:51 AM	0.0	10:47 AM	0.3	0.3
11:06 AM	0.0	11:02 AM	0.3	0.3
11:21 AM	0.0	11:17 AM	0.3	0.3
11:36 AM	0.0	11:32 AM	0.3	0.3
11:51 AM	0.0	11:47 AM	0.3	0.3
12:06 PM	0.0	12:02 PM	0.3	0.3
12:21 PM	0.1	12:17 PM	0.3	0.2
12:36 PM	0.1	12:32 PM	0.3	0.2
12:51 PM	0.0	12:47 PM	0.3	0.3
1:06 PM	0.0	1:02 PM	0.3	0.3
1:21 PM	0.0	1:17 PM	0.3	0.3
1:36 PM	0.0	1:32 PM	0.3	0.3
1:51 PM	0.0	1:47 PM	0.3	0.3
2:06 PM	0.0	2:02 PM	0.3	0.3
2:21 PM	0.0	2:17 PM	0.3	0.3
2:36 PM	0.0	2:32 PM	0.3	0.3
2:51 PM	0.0	2:47 PM	0.3	0.3
3:06 PM	0.0	3:02 PM	0.3	0.3

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/20/2022  
Times: 7:05 AM to 3:05 PM

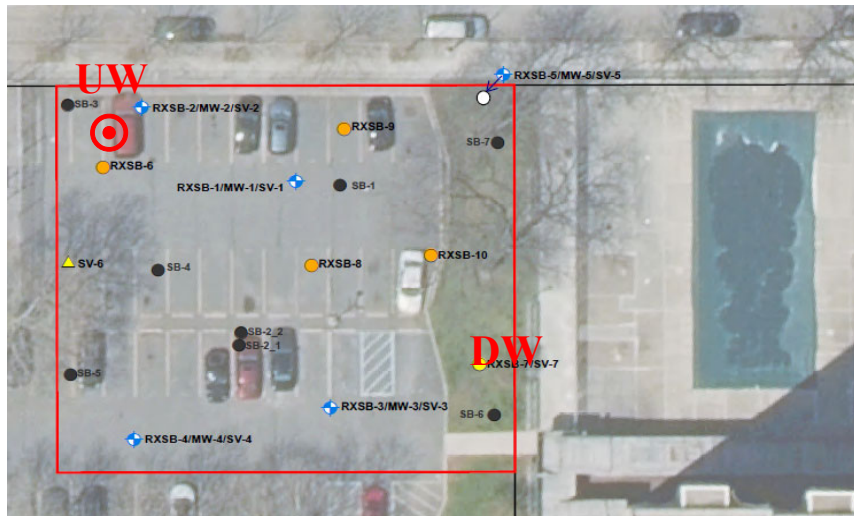

**Wind Direction**  
**NW @ 9 mph**

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/21/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
8:19 AM	0.018	8:23 AM	0.011	-0.007
8:34 AM	0.014	8:38 AM	0.014	0.000
8:49 AM	0.008	8:53 AM	0.015	0.007
9:04 AM	0.011	9:08 AM	0.016	0.005
9:19 AM	0.008	9:23 AM	0.014	0.006
9:34 AM	0.008	9:38 AM	0.015	0.007
9:49 AM	0.01	9:53 AM	0.023	0.013
10:04 AM	0.013	10:08 AM	0.021	0.008
10:19 AM	0.025	10:23 AM	0.018	-0.007
10:34 AM	0.017	10:38 AM	0.02	0.003
10:49 AM	0.008	10:53 AM	0.019	0.011
11:04 AM	0.008	11:08 AM	0.028	0.020
11:19 AM	0.014	11:23 AM	0.025	0.011
11:34 AM	0.022	11:38 AM	0.027	0.005
11:49 AM	0.021	11:53 AM	0.027	0.006
12:04 PM	0.013	12:08 PM	0.026	0.013
12:19 PM	0.012	12:23 PM	0.027	0.015
12:34 PM	0.019	12:38 PM	0.033	0.014
12:49 PM	0.02	12:53 PM	0.038	0.018
1:04 PM	0.02	1:08 PM	0.037	0.017
1:19 PM	0.017	1:23 PM	0.037	0.020
1:34 PM	0.02	1:38 PM	0.038	0.018
1:49 PM	0.022	1:53 PM	0.04	0.018
2:04 PM	0.021	2:08 PM	0.041	0.020
2:19 PM	0.019	2:23 PM	0.04	0.021
2:34 PM	0.02	2:38 PM	0.041	0.021
2:49 PM	0.021	2:53 PM	0.043	0.022
3:04 PM	0.022	3:08 PM	0.044	0.022

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/21/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
8:20 AM	0.0	8:25 AM	0.2	0.2
8:35 AM	0.0	8:40 AM	0.3	0.3
8:50 AM	0.0	8:55 AM	0.3	0.3
9:05 AM	0.0	9:10 AM	0.3	0.3
9:20 AM	0.0	9:25 AM	0.3	0.3
9:35 AM	0.0	9:40 AM	0.3	0.3
9:50 AM	0.1	9:55 AM	0.3	0.2
10:05 AM	0.1	10:10 AM	0.3	0.2
10:20 AM	0.1	10:25 AM	0.3	0.2
10:35 AM	0.1	10:40 AM	0.3	0.2
10:50 AM	0.1	10:55 AM	0.3	0.2
11:05 AM	0.1	11:10 AM	0.4	0.3
11:20 AM	0.1	11:25 AM	0.3	0.2
11:35 AM	0.2	11:40 AM	0.3	0.1
11:50 AM	0.2	11:55 AM	0.3	0.1
12:05 PM	0.4	12:10 PM	0.3	-0.1
12:20 PM	0.3	12:25 PM	0.3	0.0
12:35 PM	0.2	12:40 PM	0.3	0.1
12:50 PM	0.2	12:55 PM	0.3	0.1
1:05 PM	0.2	1:10 PM	0.3	0.1
1:20 PM	0.2	1:25 PM	0.3	0.1
1:35 PM	0.2	1:40 PM	0.4	0.2
1:50 PM	0.2	1:55 PM	0.4	0.2
2:05 PM	0.1	2:10 PM	0.4	0.3
2:20 PM	0.1	2:25 PM	0.4	0.3
2:35 PM	0.1	2:40 PM	0.4	0.3
2:50 PM	0.1	2:55 PM	0.4	0.3
3:05 PM	0.1	3:10 PM	0.3	0.2

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/21/2022  
Times: 8:00 AM to 3:10 PM

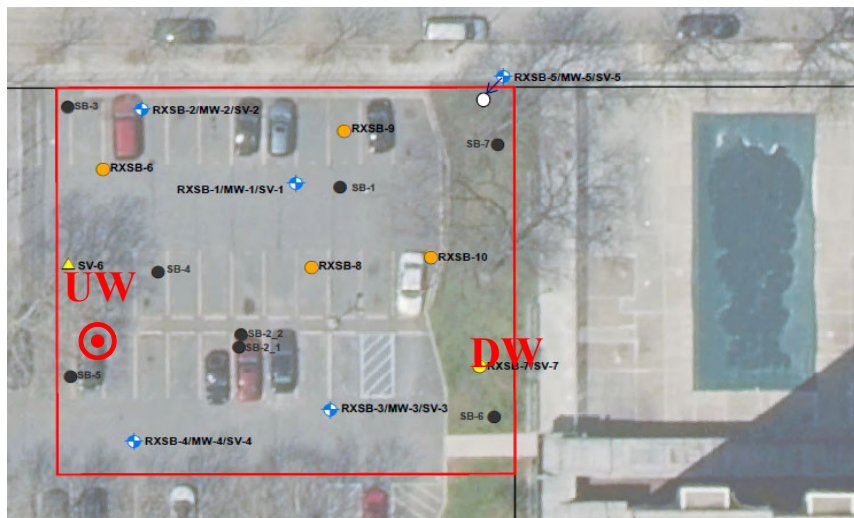

Wind Direction  
NNW @ 1 mph

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/22/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
8:37 AM	0.042	8:32 AM	0.049	<b>0.007</b>
8:52 AM	0.037	8:47 AM	0.039	<b>0.002</b>
9:07 AM	0.041	9:02 AM	0.042	<b>0.001</b>
9:22 AM	0.044	9:17 AM	0.046	<b>0.002</b>
9:37 AM	0.045	9:32 AM	0.049	<b>0.004</b>
9:52 AM	0.046	9:47 AM	0.05	<b>0.004</b>
10:07 AM	0.046	10:02 AM	0.05	<b>0.004</b>
10:22 AM	0.047	10:17 AM	0.05	<b>0.003</b>
10:37 AM	0.047	10:32 AM	0.052	<b>0.005</b>
10:52 AM	0.046	10:47 AM	0.053	<b>0.007</b>
11:07 AM	0.044	11:02 AM	0.053	<b>0.009</b>
11:22 AM	0.05	11:17 AM	0.056	<b>0.006</b>
11:37 AM	0	11:32 AM	NM	<b>NM</b>

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/22/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
8:40 AM	0.0	8:34 AM	0.1	<b>0.1</b>
8:55 AM	0.0	8:49 AM	0.1	<b>0.1</b>
9:10 AM	0.0	9:04 AM	0.1	<b>0.1</b>
9:25 AM	0.0	9:19 AM	0.1	<b>0.1</b>
9:40 AM	0.0	9:34 AM	0.1	<b>0.1</b>
9:55 AM	0.0	9:49 AM	0.1	<b>0.1</b>
10:10 AM	0.0	10:04 AM	0.2	<b>0.2</b>
10:25 AM	0.0	10:19 AM	0.2	<b>0.2</b>
10:40 AM	0.0	10:34 AM	0.2	<b>0.2</b>
10:55 AM	0.0	10:49 AM	0.2	<b>0.2</b>
11:10 AM	0.0	11:04 AM	0.2	<b>0.2</b>
11:25 AM	0.0	11:19 AM	0.2	<b>0.2</b>


Notes:

NM - Not Measured

Due to inclement weather conditions, CAMP was delayed in start and stopped early for the day.

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/22/2022  
Times: 8:15 AM to 11:30 AM

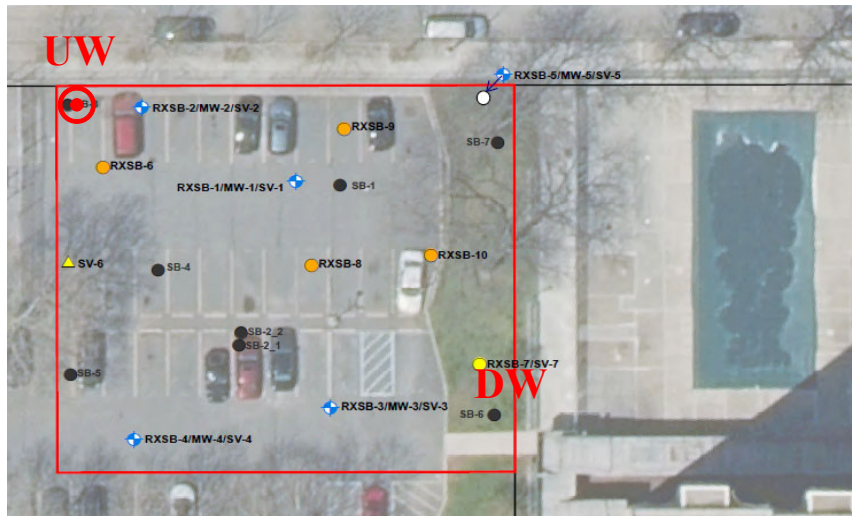

**Wind Direction**  
**WNW @ 9 mph**



Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/23/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:27 AM	0.004	7:22 AM	0.004	0.000
7:42 AM	0.004	7:37 AM	0.006	0.002
7:57 AM	0.007	7:52 AM	0.008	0.001
8:12 AM	0.005	8:07 AM	0.008	0.003
8:27 AM	0.004	8:22 AM	0.008	0.004
8:42 AM	0.004	8:37 AM	0.01	0.006
8:57 AM	0.004	8:52 AM	0.01	0.006
9:12 AM	0.004	9:07 AM	0.01	0.006
9:27 AM	0.002	9:22 AM	0.009	0.007
9:42 AM	0.003	9:37 AM	0.011	0.008
9:57 AM	0.003	9:52 AM	0.012	0.009
10:12 AM	0.004	10:07 AM	0.012	0.008
10:27 AM	0.004	10:22 AM	0.013	0.009
10:42 AM	0.005	10:37 AM	0.012	0.007
10:57 AM	0.004	10:52 AM	0.012	0.008
11:12 AM	0.004	11:07 AM	0.012	0.008
11:27 AM	0.004	11:22 AM	0.013	0.009
11:42 AM	0.003	11:37 AM	0.014	0.011
11:57 AM	0.004	11:52 AM	0.014	0.010
12:12 PM	0.004	12:07 PM	0.014	0.010
12:27 PM	0.005	12:22 PM	0.014	0.009
12:42 PM	0.005	12:37 PM	0.015	0.010
12:57 PM	0.008	12:52 PM	0.018	0.010
1:12 PM	0.006	1:07 PM	0.017	0.011
1:27 PM	0.009	1:22 PM	0.019	0.010
1:42 PM	0.006	1:37 PM	0.017	0.011
1:57 PM	0.009	1:52 PM	0.018	0.009
2:12 PM	0.007	2:07 PM	0.019	0.012
2:27 PM	0.005	2:22 PM	0.018	0.013
2:42 PM	0.005	2:37 PM	0.018	0.013
2:57 PM	0.005	2:52 PM	0.018	0.013
3:12 PM	0.005	3:07 PM	0.019	0.014

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/23/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:28 AM	0.0	7:24 AM	0.1	0.1
7:43 AM	0.0	7:39 AM	0.1	0.1
7:58 AM	0.0	7:54 AM	0.1	0.1
8:13 AM	0.0	8:09 AM	0.1	0.1
8:28 AM	0.1	8:24 AM	0.1	0.0
8:43 AM	0.1	8:39 AM	0.1	0.0
8:58 AM	0.1	8:54 AM	0.1	0.0
9:13 AM	0.1	9:09 AM	0.1	0.0
9:28 AM	0.1	9:24 AM	0.1	0.0
9:43 AM	0.1	9:39 AM	0.1	0.0
9:58 AM	0.1	9:54 AM	0.1	0.0
10:13 AM	0.1	10:09 AM	0.1	0.0
10:28 AM	0.1	10:24 AM	0.1	0.0
10:43 AM	0.1	10:39 AM	0.1	0.0
10:58 AM	0.2	10:54 AM	0.1	-0.1
11:13 AM	0.2	11:09 AM	0.1	-0.1
11:28 AM	0.2	11:24 AM	0.1	-0.1
11:43 AM	0.2	11:39 AM	0.1	-0.1
11:58 AM	0.2	11:54 AM	0.1	-0.1
12:13 PM	0.2	12:09 PM	0.1	-0.1
12:28 PM	0.2	12:24 PM	0.1	-0.1
12:43 PM	0.2	12:39 PM	0.1	-0.1
12:58 PM	0.2	12:54 PM	0.1	-0.1
1:13 PM	0.2	1:09 PM	0.1	-0.1
1:28 PM	0.2	1:24 PM	0.1	-0.1
1:43 PM	0.2	1:39 PM	0.1	-0.1
1:58 PM	0.2	1:54 PM	0.1	-0.1
2:13 PM	0.2	2:09 PM	0.1	-0.1
2:28 PM	0.2	2:24 PM	0.1	-0.1
2:43 PM	0.2	2:39 PM	0.1	-0.1
2:58 PM	0.2	2:54 PM	0.1	-0.1
3:13 PM	0.2	3:09 PM	0.1	-0.1



Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

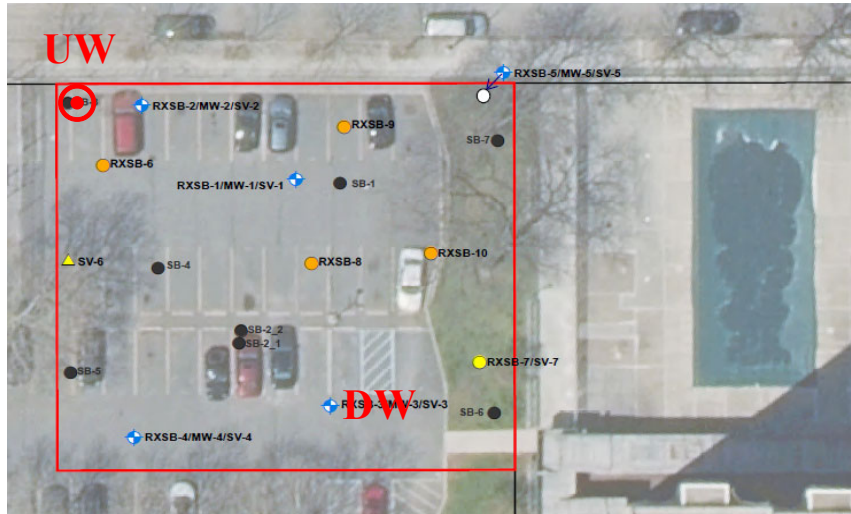Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/23/2022  
Times: 7:05 AM to 3:15 PM



  
**Wind Direction**  
**NNW @ 16 mph**  


Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/26/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:26 AM	0.014	7:22 AM	0.018	0.004
7:41 AM	0.012	7:37 AM	0.016	0.004
7:56 AM	0.016	7:52 AM	0.018	0.002
8:11 AM	0.021	8:07 AM	0.023	0.002
8:26 AM	0.013	8:22 AM	0.026	0.013
8:41 AM	0.012	8:37 AM	0.056	0.044
8:56 AM	0.013	8:52 AM	0.052	0.039
9:11 AM	0.013	9:07 AM	0.025	0.012
9:26 AM	0.014	9:22 AM	0.027	0.013
9:41 AM	0.014	9:37 AM	0.034	0.020
9:56 AM	0.012	9:52 AM	0.03	0.018
10:11 AM	0.013	10:07 AM	0.054	0.041
10:26 AM	0.01	10:22 AM	0.077	0.067
10:41 AM	0.01	10:37 AM	0.049	0.039
10:56 AM	0.01	10:52 AM	0.077	0.067
11:11 AM	0.014	11:07 AM	0.059	0.045
11:26 AM	0.009	11:22 AM	0.039	0.030
11:41 AM	0.015	11:37 AM	0.045	0.030
11:56 AM	0.012	11:52 AM	0.034	0.022
12:11 PM	0.01	12:07 PM	0.024	0.014
12:26 PM	0.009	12:22 PM	0.024	0.015
12:41 PM	0.018	12:37 PM	0.027	0.009
12:56 PM	0.009	12:52 PM	0.084	0.075
1:11 PM	0.01	1:07 PM	0.08	0.070
1:26 PM	0.008	1:22 PM	0.061	0.053
1:41 PM	0.008	1:37 PM	0.078	0.070
1:56 PM	0.009	1:52 PM	0.053	0.044
2:11 PM	0.008	2:07 PM	0.033	0.025
2:26 PM	0.009	2:22 PM	0.033	0.024
2:41 PM	0.009	2:37 PM	0.032	0.023
2:56 PM	0.008	2:52 PM	0.046	0.038

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/26/2022



Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:26 AM	0.0	7:23 AM	0.1	0.1
7:41 AM	0.0	7:38 AM	0.1	0.1
7:56 AM	0.1	7:53 AM	0.1	0.0
8:11 AM	0.1	8:08 AM	0.2	0.1
8:26 AM	0.1	8:23 AM	0.2	0.1
8:41 AM	0.1	8:38 AM	0.2	0.1
8:56 AM	0.1	8:53 AM	0.2	0.1
9:11 AM	0.1	9:08 AM	0.2	0.1
9:26 AM	0.1	9:23 AM	0.2	0.1
9:41 AM	0.1	9:38 AM	0.2	0.1
9:56 AM	0.1	9:53 AM	0.3	0.2
10:11 AM	0.1	10:08 AM	0.3	0.2
10:26 AM	0.1	10:23 AM	0.3	0.2
10:41 AM	0.1	10:38 AM	0.3	0.2
10:56 AM	0.1	10:53 AM	0.3	0.2
11:11 AM	0.1	11:08 AM	0.3	0.2
11:26 AM	0.1	11:23 AM	0.3	0.2
11:41 AM	0.1	11:38 AM	0.2	0.1
11:56 AM	0.2	11:53 AM	0.2	0.0
12:11 PM	0.2	12:08 PM	0.2	0.0
12:26 PM	0.2	12:23 PM	0.2	0.0
12:41 PM	0.2	12:38 PM	0.3	0.1
12:56 PM	0.2	12:53 PM	0.3	0.1
1:11 PM	0.2	1:08 PM	0.3	0.1
1:26 PM	0.2	1:23 PM	0.3	0.1
1:41 PM	0.2	1:38 PM	0.3	0.1
1:56 PM	0.2	1:53 PM	0.3	0.1
2:11 PM	0.2	2:08 PM	0.3	0.1
2:26 PM	0.2	2:23 PM	0.2	0.0
2:41 PM	0.2	2:38 PM	0.4	0.2
2:56 PM	0.2	2:53 PM	0.2	0.0

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/26/2022  
Times: 7:05 AM to 3:00 PM

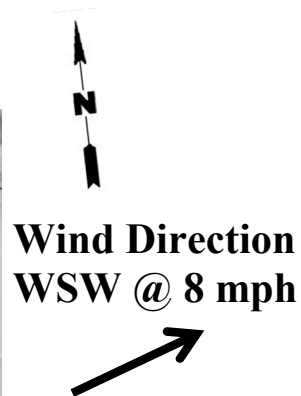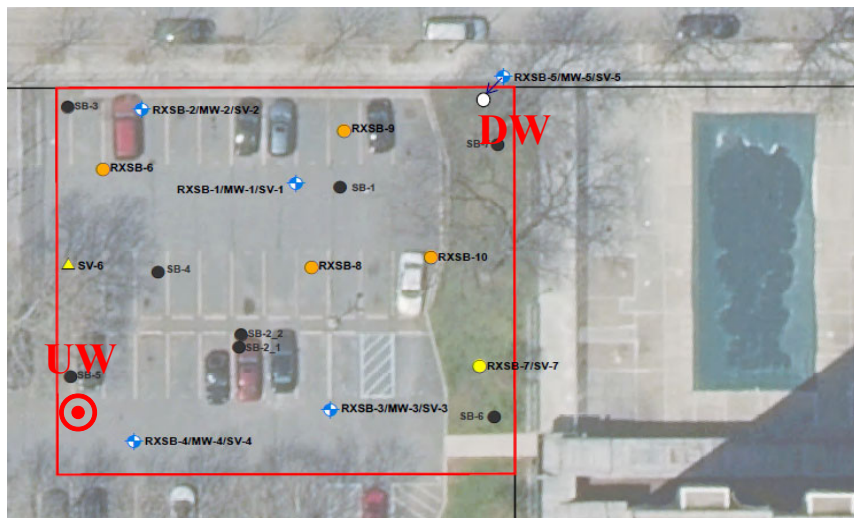

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/27/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:18 AM	0.01	7:22 AM	0.029	<b>0.019</b>
7:33 AM	0.008	7:37 AM	0.016	<b>0.008</b>
7:48 AM	0.007	7:52 AM	0.016	<b>0.009</b>
8:03 AM	0.007	8:07 AM	0.018	<b>0.011</b>
8:18 AM	0.007	8:22 AM	0.021	<b>0.014</b>
8:33 AM	0.009	8:37 AM	0.021	<b>0.012</b>
8:48 AM	0.007	8:52 AM	0.017	<b>0.010</b>
9:03 AM	0.007	9:07 AM	0.019	<b>0.012</b>
9:18 AM	0.007	9:22 AM	0.017	<b>0.010</b>
9:33 AM	0.007	9:37 AM	0.018	<b>0.011</b>
9:48 AM	0.008	9:52 AM	0.043	<b>0.035</b>
10:03 AM	0.009	10:07 AM	0.029	<b>0.020</b>
10:18 AM	0.009	10:22 AM	0.03	<b>0.021</b>
10:33 AM	0.006	10:37 AM	0.051	<b>0.045</b>
10:48 AM	0.007	10:52 AM	0.03	<b>0.023</b>
11:03 AM	0.008	11:07 AM	0.05	<b>0.042</b>
11:18 AM	0.007	11:22 AM	0.026	<b>0.019</b>
11:33 AM	0.007	11:37 AM	0.024	<b>0.017</b>
11:48 AM	0.009	11:52 AM	0.021	<b>0.012</b>
12:03 PM	0.007	12:07 PM	0.02	<b>0.013</b>
12:18 PM	0.007	12:22 PM	0.019	<b>0.012</b>
12:33 PM	0.007	12:37 PM	0.028	<b>0.021</b>
12:48 PM	0.008	12:52 PM	0.034	<b>0.026</b>
1:03 PM	0.007	1:07 PM	0.075	<b>0.068</b>
1:18 PM	0.01	1:22 PM	0.038	<b>0.028</b>
1:33 PM	0.014	1:37 PM	0.06	<b>0.046</b>
1:48 PM	0.007	1:52 PM	0.033	<b>0.026</b>
2:03 PM	0.01	2:07 PM	0.043	<b>0.033</b>
2:18 PM	0.007	2:22 PM	0.036	<b>0.029</b>
2:33 PM	0.011	2:37 PM	0.037	<b>0.026</b>
2:48 PM	0.013	2:52 PM	0.044	<b>0.031</b>

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/27/2022



Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:19 AM	0.0	7:22 AM	0.1	0.1
7:34 AM	0.1	7:37 AM	0.1	0.0
7:49 AM	0.1	7:52 AM	0.2	0.1
8:04 AM	0.1	8:07 AM	0.2	0.1
8:19 AM	0.1	8:22 AM	0.2	0.1
8:34 AM	0.1	8:37 AM	0.2	0.1
8:49 AM	0.1	8:52 AM	0.2	0.1
9:04 AM	0.1	9:07 AM	0.2	0.1
9:19 AM	0.1	9:22 AM	0.2	0.1
9:34 AM	0.1	9:37 AM	0.2	0.1
9:49 AM	0.1	9:52 AM	0.2	0.1
10:04 AM	0.1	10:07 AM	0.2	0.1
10:19 AM	0.1	10:22 AM	0.2	0.1
10:34 AM	0.1	10:37 AM	0.2	0.1
10:49 AM	0.1	10:52 AM	0.3	0.2
11:04 AM	0.1	11:07 AM	0.3	0.2
11:19 AM	0.1	11:22 AM	0.2	0.1
11:34 AM	0.1	11:37 AM	0.2	0.1
11:49 AM	0.1	11:52 AM	0.2	0.1
12:04 PM	0.1	12:07 PM	0.2	0.1
12:19 PM	0.1	12:22 PM	0.2	0.1
12:34 PM	0.1	12:37 PM	0.3	0.2
12:49 PM	0.1	12:52 PM	0.3	0.2
1:04 PM	0.1	1:07 PM	0.3	0.2
1:19 PM	0.1	1:22 PM	0.3	0.2
1:34 PM	0.1	1:37 PM	0.3	0.2
1:49 PM	0.1	1:52 PM	0.3	0.2
2:04 PM	0.1	2:07 PM	0.3	0.2
2:19 PM	0.1	2:22 PM	0.3	0.2
2:34 PM	0.1	2:37 PM	0.3	0.2
2:49 PM	0.1	2:52 PM	0.3	0.2

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/27/2022  
Times: 7:00 AM to 3:00 PM

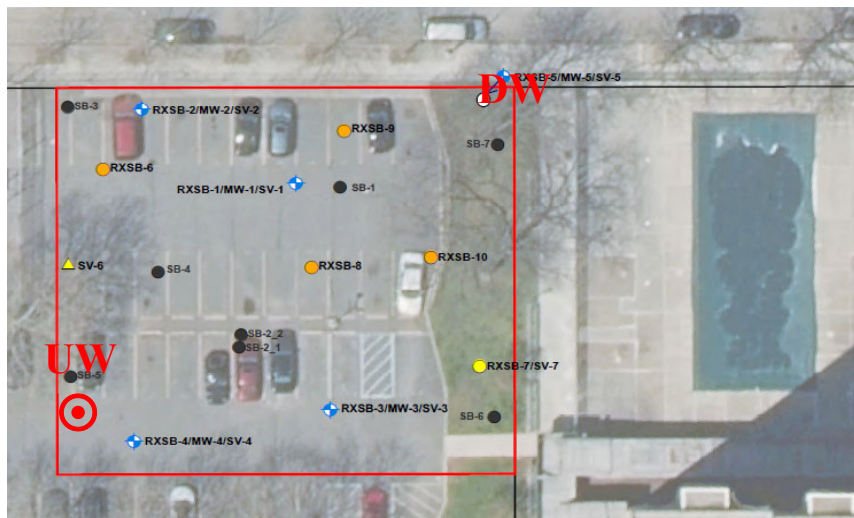

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/28/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:22 AM	0.027	7:18 AM	0.026	-0.001
7:37 AM	0.032	7:33 AM	0.015	-0.017
7:52 AM	0.013	7:48 AM	0.02	0.007
8:07 AM	0.014	8:03 AM	0.027	0.013
8:22 AM	0.016	8:18 AM	0.017	0.001
8:37 AM	0.019	8:33 AM	0.019	0.000
8:52 AM	0.029	8:48 AM	0.016	-0.013
9:07 AM	0.018	9:03 AM	0.016	-0.002
9:22 AM	0.011	9:18 AM	0.013	0.002
9:37 AM	0.012	9:33 AM	0.015	0.003
9:52 AM	0.012	9:48 AM	0.019	0.007
10:07 AM	0.014	10:03 AM	0.018	0.004
10:22 AM	0.016	10:18 AM	0.093	0.077
10:37 AM	0.024	10:33 AM	0.115	0.091
10:52 AM	0.011	10:48 AM	0.029	0.018
11:07 AM	0.017	11:03 AM	0.031	0.014
11:22 AM	0.015	11:18 AM	0.027	0.012
11:37 AM	0.016	11:33 AM	0.031	0.015
11:52 AM	0.018	11:48 AM	0.029	0.011
12:07 PM	0.008	12:03 PM	0.021	0.013
12:22 PM	0.008	12:18 PM	0.022	0.014
12:37 PM	0.008	12:33 PM	0.023	0.015
12:52 PM	0.012	12:48 PM	0.026	0.014
1:07 PM	0.026	1:03 PM	0.036	0.010
1:22 PM	0.02	1:18 PM	0.03	0.010
1:37 PM	0.015	1:33 PM	0.035	0.020
1:52 PM	0.01	1:48 PM	0.03	0.020
2:07 PM	0.007	2:03 PM	0.024	0.017
2:22 PM	0.009	2:18 PM	0.025	0.016
2:37 PM	0.006	2:33 PM	0.024	0.018
2:52 PM	0.005	2:48 PM	0.024	0.019

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/28/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:23 AM	0.0	7:19 AM	0.1	0.1
7:38 AM	0.0	7:34 AM	0.1	0.1
7:53 AM	0.0	7:49 AM	0.2	0.2
8:08 AM	0.1	8:04 AM	0.2	0.1
8:23 AM	0.1	8:19 AM	0.2	0.1
8:38 AM	0.0	8:34 AM	0.2	0.2
8:53 AM	0.1	8:49 AM	0.2	0.1
9:08 AM	0.1	9:04 AM	0.2	0.1
9:23 AM	0.1	9:19 AM	0.2	0.1
9:38 AM	0.1	9:34 AM	0.2	0.1
9:53 AM	0.1	9:49 AM	0.3	0.2
10:08 AM	0.1	10:04 AM	0.3	0.2
10:23 AM	0.1	10:19 AM	0.4	0.3
10:38 AM	0.1	10:34 AM	0.3	0.2
10:53 AM	0.1	10:49 AM	0.3	0.2
11:08 AM	0.2	11:04 AM	0.3	0.1
11:23 AM	0.1	11:19 AM	0.3	0.2
11:38 AM	0.2	11:34 AM	0.3	0.1
11:53 AM	0.2	11:49 AM	0.3	0.1
12:08 PM	0.1	12:04 PM	0.3	0.2
12:23 PM	0.1	12:19 PM	0.3	0.2
12:38 PM	0.1	12:34 PM	0.3	0.2
12:53 PM	0.1	12:49 PM	0.3	0.2
1:08 PM	0.1	1:04 PM	0.3	0.2
1:23 PM	0.1	1:19 PM	0.2	0.1
1:38 PM	0.1	1:34 PM	0.2	0.1
1:53 PM	0.1	1:49 PM	0.2	0.1
2:08 PM	0.1	2:04 PM	0.2	0.1
2:23 PM	0.1	2:19 PM	0.2	0.1
2:38 PM	0.1	2:34 PM	0.2	0.1
2:53 PM	0.1	2:49 PM	0.2	0.1

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/28/2022  
Times: 7:00 AM to 2:55 PM

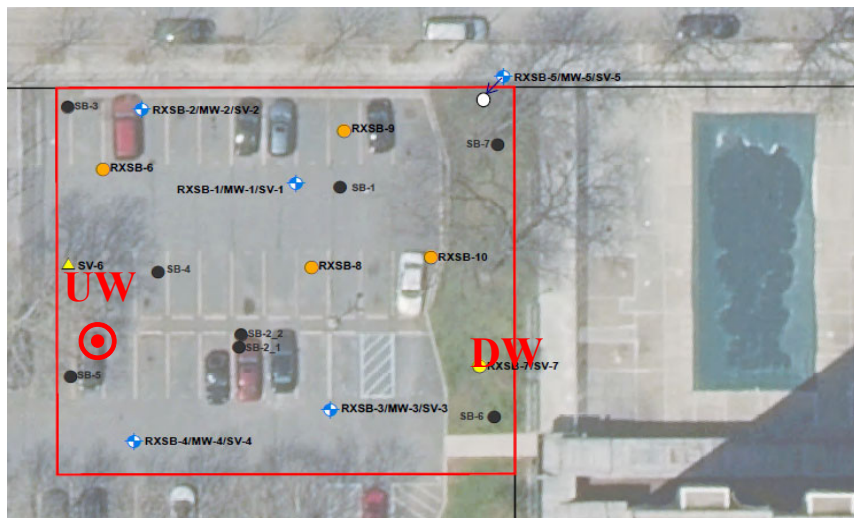

Wind Direction  
WNW @ 9 mph

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/29/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:34 AM	0.012	7:38 AM	0.018	0.006
7:49 AM	0.013	7:53 AM	0.01	-0.003
8:04 AM	0.029	8:08 AM	0.012	-0.017
8:19 AM	0.023	8:23 AM	0.011	-0.012
8:34 AM	0.009	8:38 AM	0.011	0.002
8:49 AM	0.01	8:53 AM	0.012	0.002
9:04 AM	0.006	9:08 AM	0.012	0.006
9:19 AM	0.006	9:23 AM	0.012	0.006
9:34 AM	0.006	9:38 AM	0.012	0.006
9:49 AM	0.007	9:53 AM	0.013	0.006
10:04 AM	0.004	10:08 AM	0.017	0.013
10:19 AM	0.006	10:23 AM	0.021	0.015
10:34 AM	0.006	10:38 AM	0.014	0.008
10:49 AM	0.009	10:53 AM	0.018	0.009
11:04 AM	0.009	11:08 AM	0.018	0.009
11:19 AM	0.006	11:23 AM	0.018	0.012
11:34 AM	0.01	11:38 AM	0.02	0.010
11:49 AM	0.007	11:53 AM	0.02	0.013
12:04 PM	0.005	12:08 PM	0.019	0.014
12:19 PM	0.005	12:23 PM	0.018	0.013
12:34 PM	0.012	12:38 PM	0.02	0.008
12:49 PM	0.006	12:53 PM	0.021	0.015
1:04 PM	0.006	1:08 PM	0.023	0.017
1:19 PM	0.005	1:23 PM	0.022	0.017
1:34 PM	0.008	1:38 PM	0.023	0.015
1:49 PM	0.006	1:53 PM	0.023	0.017
2:04 PM	0.009	2:08 PM	0.026	0.017
2:19 PM	0.009	2:23 PM	0.025	0.016
2:34 PM	0.011	2:38 PM	0.028	0.017
2:49 PM	0.007	2:53 PM	0.028	0.021
3:04 PM	0.007	3:08 PM	0.023	0.016
3:19 PM	0.006	3:23 PM	NM	NM

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/29/2022


Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:35 AM	0.0	7:38 AM	0.1	0.1
7:50 AM	0.0	7:53 AM	0.1	0.1
8:05 AM	0.0	8:08 AM	0.1	0.1
8:20 AM	0.0	8:23 AM	0.2	0.2
8:35 AM	0.1	8:38 AM	0.2	0.1
8:50 AM	0.1	8:53 AM	0.2	0.1
9:05 AM	0.1	9:08 AM	0.2	0.1
9:20 AM	0.1	9:23 AM	0.2	0.1
9:35 AM	0.1	9:38 AM	0.2	0.1
9:50 AM	0.1	9:53 AM	0.2	0.1
10:05 AM	0.1	10:08 AM	0.2	0.1
10:20 AM	0.1	10:23 AM	0.2	0.1
10:35 AM	0.1	10:38 AM	0.2	0.1
10:50 AM	0.1	10:53 AM	0.2	0.1
11:05 AM	0.1	11:08 AM	0.2	0.1
11:20 AM	0.1	11:23 AM	0.2	0.1
11:35 AM	0.1	11:38 AM	0.2	0.1
11:50 AM	0.1	11:53 AM	0.2	0.1
12:05 PM	0.1	12:08 PM	0.2	0.1
12:20 PM	0.1	12:23 PM	0.2	0.1
12:35 PM	0.1	12:38 PM	0.2	0.1
12:50 PM	0.1	12:53 PM	0.2	0.1
1:05 PM	0.1	1:08 PM	0.2	0.1
1:20 PM	0.1	1:23 PM	0.2	0.1
1:35 PM	0.1	1:38 PM	0.2	0.1
1:50 PM	0.1	1:53 PM	0.2	0.1
2:05 PM	0.1	2:08 PM	0.2	0.1
2:20 PM	0.1	2:23 PM	0.2	0.1
2:35 PM	0.1	2:38 PM	0.2	0.1
2:50 PM	0.1	2:53 PM	0.2	0.1
3:05 PM	0.1	3:08 PM	0.2	0.1
3:20 PM	0.1	3:23 PM	NM	NM

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/29/2022  
Times: 7:15 AM to 3:20 PM

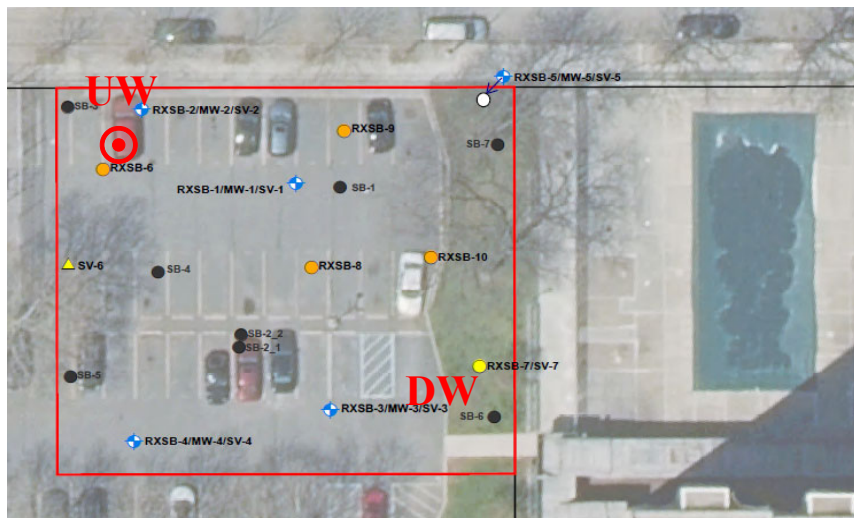

**Wind Direction**  
**NW @ 2 mph**

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind Dust**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/30/2022

Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (mg/m <sup>3</sup> )	Time	15-min Avg. (mg/m <sup>3</sup> )	
7:13 AM	NM	7:17 AM	0.029	NM
7:28 AM	0.005	7:32 AM	0.005	0.000
7:43 AM	0.005	7:47 AM	0.007	0.002
7:58 AM	0.007	8:02 AM	0.013	0.006
8:13 AM	0.011	8:17 AM	0.01	-0.001
8:28 AM	0.006	8:32 AM	0.008	0.002
8:43 AM	0.007	8:47 AM	0.01	0.003
8:58 AM	0.007	9:02 AM	0.011	0.004
9:13 AM	0.006	9:17 AM	0.008	0.002
9:28 AM	0.006	9:32 AM	0.007	0.001
9:43 AM	0.006	9:47 AM	0.007	0.001
9:58 AM	0.01	10:02 AM	0.012	0.002
10:13 AM	0.007	10:17 AM	0.014	0.007
10:28 AM	0.006	10:32 AM	0.011	0.005
10:43 AM	0.007	10:47 AM	0.014	0.007
10:58 AM	0.01	11:02 AM	0.011	0.001
11:13 AM	0.006	11:17 AM	0.01	0.004
11:28 AM	0.006	11:32 AM	0.014	0.008
11:43 AM	0.024	11:47 AM	0.012	-0.012
11:58 AM	0.006	12:02 PM	0.01	0.004
12:13 PM	0.006	12:17 PM	0.011	0.005
12:28 PM	0.006	12:32 PM	0.011	0.005
12:43 PM	0.006	12:47 PM	0.018	0.012
12:58 PM	0.012	1:02 PM	0.018	0.006
1:13 PM	0.024	1:17 PM	0.019	-0.005
1:28 PM	0.008	1:32 PM	0.014	0.006
1:43 PM	0.008	1:47 PM	0.014	0.006
1:58 PM	0.008	2:02 PM	0.014	0.006
2:13 PM	0.009	2:17 PM	0.015	0.006
2:28 PM	0.017	2:32 PM	0.016	-0.001
2:43 PM	0.027	2:47 PM	0.017	-0.010
2:58 PM	0.013	3:02 PM	0.015	0.002
3:13 PM	0.007	3:17 PM	0.018	0.011
3:28 PM	0.006	3:32 PM	0.015	0.009

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Downwind VOC**

Project: Park Lane Senior  
 NYSDEC BCP Number: C203138  
 Project Manager: Kathryn Sommo  
 Location: 1940 Turnbull Avenue, Bronx, New York  
 Date: 9/30/2022



Upwind Station		Downwind Station		15-min Average (Corrected for Background)
Time	15-min Avg. (PPM)	Time	15-min Avg. (PPM)	
7:13 AM	NM	7:18 AM	0.1	NM
7:28 AM	0.0	7:33 AM	0.1	0.1
7:43 AM	0.0	7:48 AM	0.1	0.1
7:58 AM	0.0	8:03 AM	0.2	0.2
8:13 AM	0.0	8:18 AM	0.2	0.2
8:28 AM	0.0	8:33 AM	0.2	0.2
8:43 AM	0.0	8:48 AM	0.2	0.2
8:58 AM	0.0	9:03 AM	0.2	0.2
9:13 AM	0.0	9:18 AM	0.2	0.2
9:28 AM	0.0	9:33 AM	0.2	0.2
9:43 AM	0.0	9:48 AM	0.2	0.2
9:58 AM	0.0	10:03 AM	0.2	0.2
10:13 AM	0.0	10:18 AM	0.2	0.2
10:28 AM	0.0	10:33 AM	0.2	0.2
10:43 AM	0.0	10:48 AM	0.2	0.2
10:58 AM	0.0	11:03 AM	0.2	0.2
11:13 AM	0.0	11:18 AM	0.2	0.2
11:28 AM	0.0	11:33 AM	0.2	0.2
11:43 AM	0.0	11:48 AM	0.2	0.2
11:58 AM	0.0	12:03 PM	0.2	0.2
12:13 PM	0.0	12:18 PM	0.2	0.2
12:28 PM	0.0	12:33 PM	0.2	0.2
12:43 PM	0.0	12:48 PM	0.2	0.2
12:58 PM	0.0	1:03 PM	0.2	0.2
1:13 PM	0.0	1:18 PM	0.2	0.2
1:28 PM	0.0	1:33 PM	0.2	0.2
1:43 PM	0.0	1:48 PM	0.2	0.2
1:58 PM	0.0	2:03 PM	0.2	0.2
2:13 PM	0.0	2:18 PM	0.2	0.2
2:28 PM	0.0	2:33 PM	0.2	0.2
2:43 PM	0.0	2:48 PM	0.2	0.2
2:58 PM	0.0	3:03 PM	0.2	0.2
3:13 PM	0.0	3:18 PM	0.2	0.2
3:28 PM	0.0	3:33 PM	0.2	0.2

Notes:

NM - Not Measured

**Roux Environmental Engineering and Geology, D.P.C.**  
**Community Air Monitoring Program - Meter Locations**

Project: Park Lane Senior  
NYSDEC BCP Number: C203138  
Project Manager: Kathryn Sommo  
Location: 1940 Turnbull Avenue, Bronx, New York  
Date: 9/30/2022  
Times: 7:05 AM to 3:35 PM

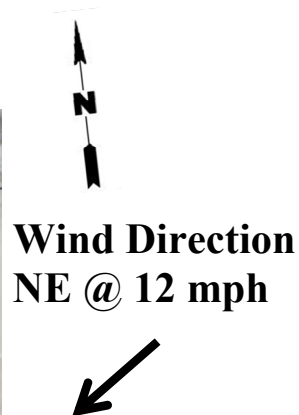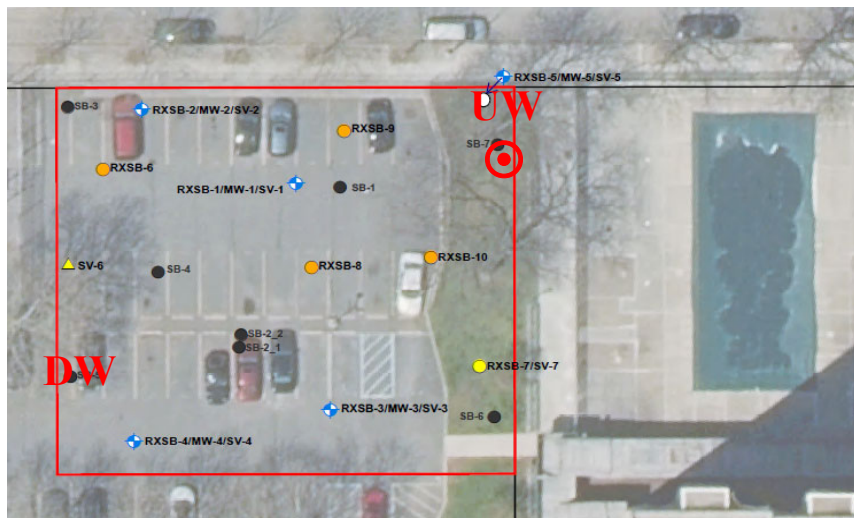

Notes: CAMP - Community Air Monitoring Program  
UW - Upwind CAMP Station  
DW - Downwind CAMP Station

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	70-85°F, fair RH: 75%, P: 29.78" of Hg Wind: WNW @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:35 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 1, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Frank Marino, Consigli</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Manning, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Dave S., Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Masoud Janbaz, MRCE</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<u>Roux Work Activities Performed Onsite:</u> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> <li>Collected the following endpoint soil sample from within the Track 4 Lead Hotspot: <ul style="list-style-type: none"> <li>Composite sample B1 (13-14) from the bottom of the hotspot.</li> </ul> </li> <li>The composite sample taken today was collected into a plastic container to be analyzed for PFAS.</li> </ul>	
<u>Contractor Work Performed Onsite:</u>	
<u>Consigli</u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u>Urban</u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in the northern half of the building footprint.</li> <li>Additional watering digouts were made for pile grout-casing work within the building footprint.</li> <li>Continued drilling for secondary tiebacks within building footprint along east-northeast shoring.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	70-85°F, fair RH: 75%, P: 29.78" of Hg Wind: WNW @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:35 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 1, 2022

- Partial restoration of soil ramp within west boundary of the building footprint.
- Occasional dewatering needed for the tieback work area.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 6:55 am to 3:00 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was in the northwest corner of the Site and the downwind CAMP station was in the southeast corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.021 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Mobilize materials for casing drill work.
- Monitor pile casing/grout drilling activities.
- Continue drilling tiebacks.
- Load and transport concrete debris off-site for disposal.
- Construct detention tank structure.
- Prepare excavation within Track 4 area for detention tank placement.
- Backfill excavation within Track 4 area following detention tank placement.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	70-85°F, fair RH: 75%, P: 29.78" of Hg Wind: WNW @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:35 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 1, 2022

### Site Layout

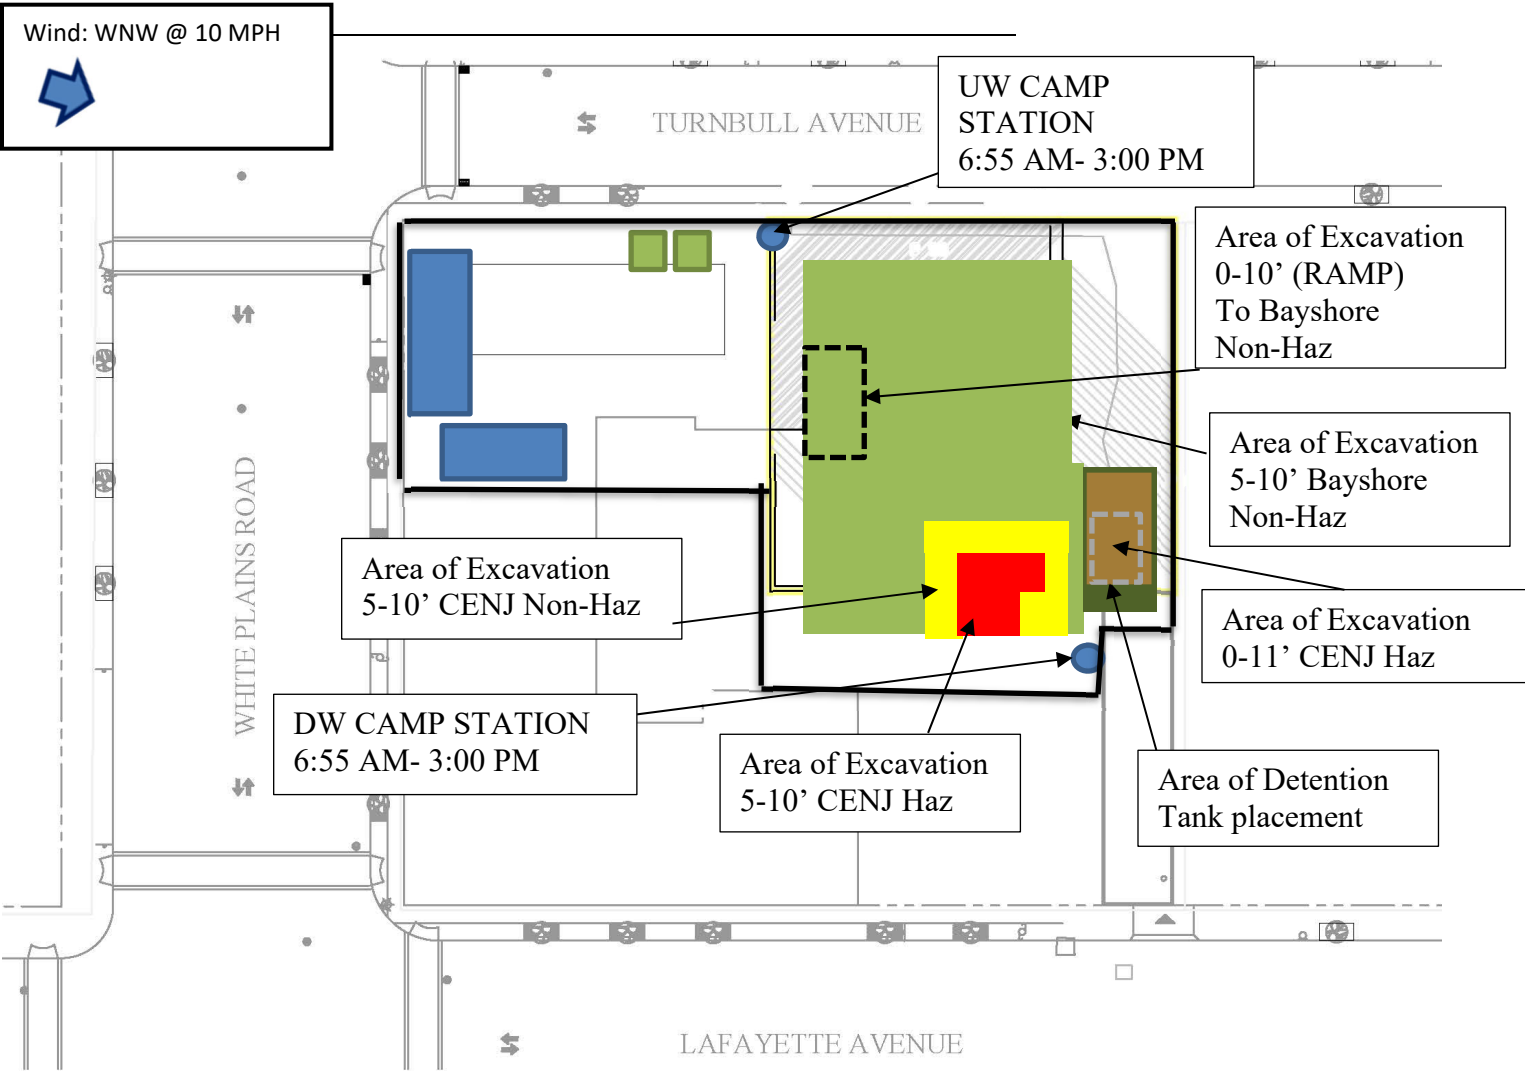

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	70-85°F, fair RH: 75%, P: 29.78" of Hg Wind: WNW @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:35 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 1, 2022

## PHOTOGRAPHS TAKEN TODAY:



**Photo 1:** View of tieback drilling into east-northeast shoring.



**Photo 2:** Looking east, view of surveyors plotting markers for pipe casing drill work within the building footprint.

DAILY STATUS REPORT

PROJECT: BCP SITE No.	Park Lane Senior C203138	WEATHER:	70-85°F, fair RH: 75%, P: 29.78" of Hg Wind: WNW @ 10 mph
LOCATION:	1940 Turnbull Ave, Bronx, NY (Site)	TIME:	6:45 AM – 3:35 PM
PREPARED BY:	TJ Jennings	DATE:	September 1, 2022



**Photo 3:**  
Looking east, concrete debris stockpiled for future disposal.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-80°F, fair RH: 56%, P: 30.22" of Hg Wind: NE @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:40 AM – 3:00 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 2, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Frank Marino, Consigli</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Manning, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Dave S., Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Masoud Janbaz, MRCE</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRV5 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<u>Roux Work Activities Performed Onsite:</u> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<u>Contractor Work Performed Onsite:</u>	
<u>Consigli</u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u>Urban</u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in northern half of the building footprint.</li> <li>Continued drilling for secondary tiebacks within building footprint along east-northeast shoring.</li> <li>Began dewatering in vicinity of tieback work area.</li> <li>Concrete, stone, and debris was loaded onto trucks. One truck was loaded and transported to Faztec Industries in Staten Island, NY for offsite disposal.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-80°F, fair RH: 56%, P: 30.22" of Hg Wind: NE @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:40 AM – 3:00 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 2, 2022

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:00 am to 2:55 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was in the northeast corner of the Site and the downwind CAMP station was along the southwest perimeter.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.013 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.1 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue drilling tiebacks.
- Construct detention tank structure.
- Prepare excavation within Track 4 area for detention tank placement.
- Backfill excavation within Track 4 area following detention tank placement.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-80°F, fair RH: 56%, P: 30.22" of Hg Wind: NE @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:40 AM – 3:00 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 2, 2022

### Site Layout

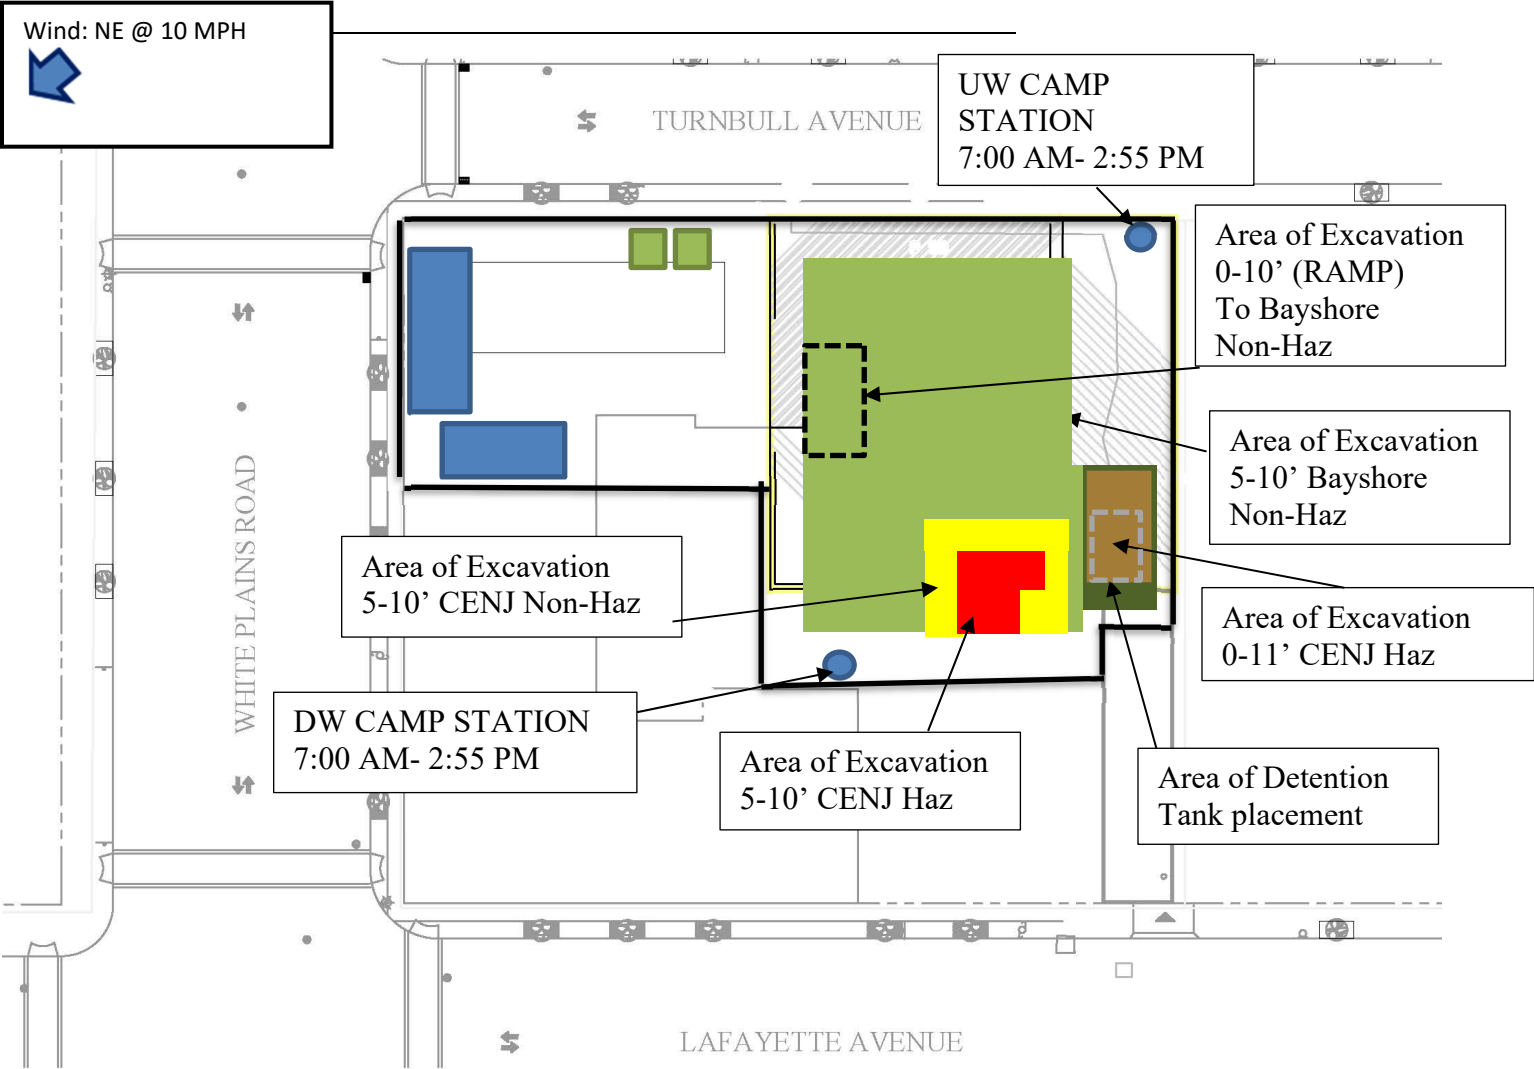

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-80°F, fair RH: 56%, P: 30.22" of Hg Wind: NE @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:40 AM – 3:00 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 2, 2022

### PHOTOGRAPHS TAKEN TODAY:



**Photo 1:** Looking north, view of site conditions at start of the day.



**Photo 2:** View of tie-back drilling and dewatering along east-northeast shoring.

DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-80°F, fair RH: 56%, P: 30.22" of Hg Wind: NE @ 10 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:40 AM – 3:00 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 2, 2022



**Photo 3:**  
Looking north, Corbett  
Enterprise truck is being loaded  
with concrete, stone, and debris.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	66-74°F, heavy rain RH: 87%, P: 29.99" of Hg Wind: SE @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 6, 2022

<b>Pro8ject Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Frank Marino, Consigli</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Manning, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Dave S., Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Masoud Janbaz, MRCE</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRV5 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux did not conduct CAMP during ground intrusive activities today. Roux performed management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b>	
<u><b>Consigli</b></u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u><b>Urban</b></u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in northwest corner and center of the building footprint.</li> <li>Continued drilling for secondary tiebacks within building footprint along the eastern shoring.</li> <li>Continued dewatering in vicinity of tieback and grout-casing drill work areas.</li> </ul>	
<u><b>Mueser Rutledge Consulting Engineers</b></u> <ul style="list-style-type: none"> <li>Oversight of pile casing activities.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	66-74°F, heavy rain RH: 87%, P: 29.99" of Hg Wind: SE @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 6, 2022

## Air Monitoring:

- CAMP was not conducted for the day due to inclement weather conditions.

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue drilling tiebacks.
- Construct detention tank structure.
- Prepare excavation within Track 4 area for detention tank placement.
- Backfill excavation within Track 4 area following detention tank placement.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	66-74°F, heavy rain RH: 87%, P: 29.99" of Hg Wind: SE @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 6, 2022

### Site Layout

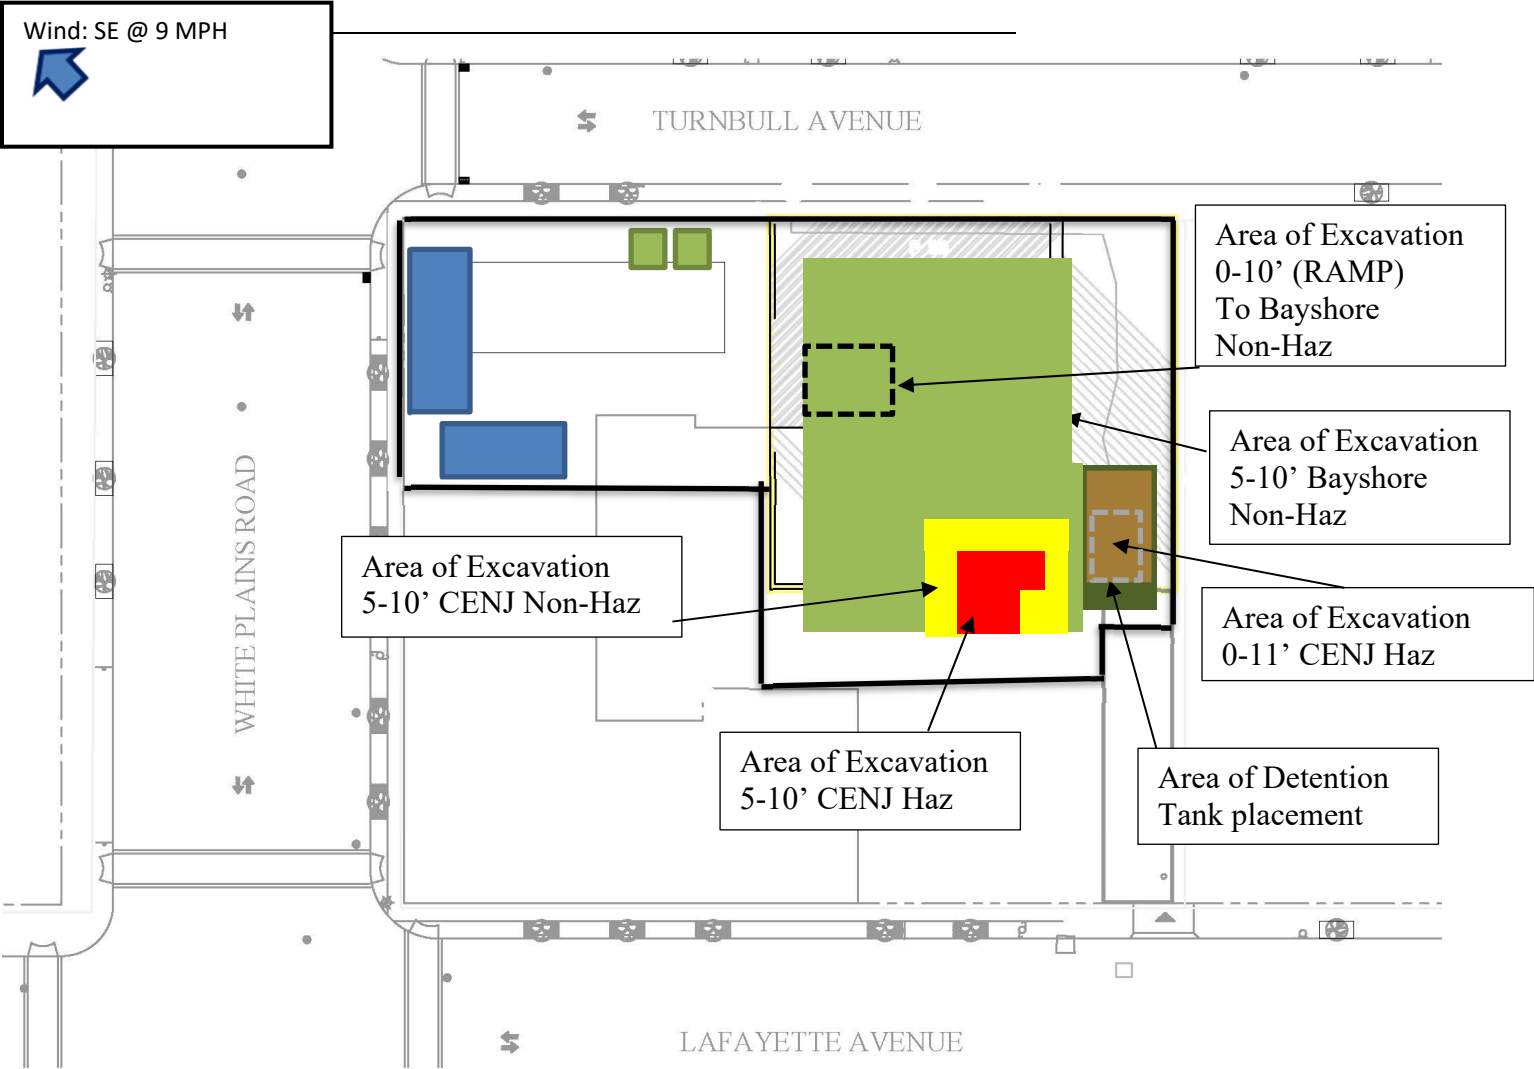

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	66-74°F, heavy rain RH: 87%, P: 29.99" of Hg Wind: SE @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 6, 2022

### PHOTOGRAPHS TAKEN TODAY:



**Photo 1:** Looking northeast, view of drilling pile casings within the building footprint.



**Photo 2:**  
View of tie-back drilling along the eastern shoring.

DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	66-74°F, heavy rain RH: 87%, P: 29.99" of Hg Wind: SE @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 6, 2022



**Photo 3:**  
Looking east, view of pile casing drilling work in the center of building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-82°F, sunny RH: 65%, P: 29.91" of Hg Wind: WNW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 14, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRVS 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b> <u>Consigli</u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u>Urban Foundation Engineering</u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in northern area of the building footprint.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-82°F, sunny RH: 65%, P: 29.91" of Hg Wind: WNW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 14, 2022

- Continued to reinforce secondary tiebacks along the eastern shoring.
- Continued dewatering in vicinity of pile casing work areas.
- Mobilized materials for upcoming work of detention tank structure.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:00 am to 3:05 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was along the center of the west perimeter of the Site and the downwind CAMP station was in the southeast corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.023 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue to finish setting tiebacks into place.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-82°F, sunny RH: 65%, P: 29.91" of Hg Wind: WNW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 14, 2022

### Site Layout

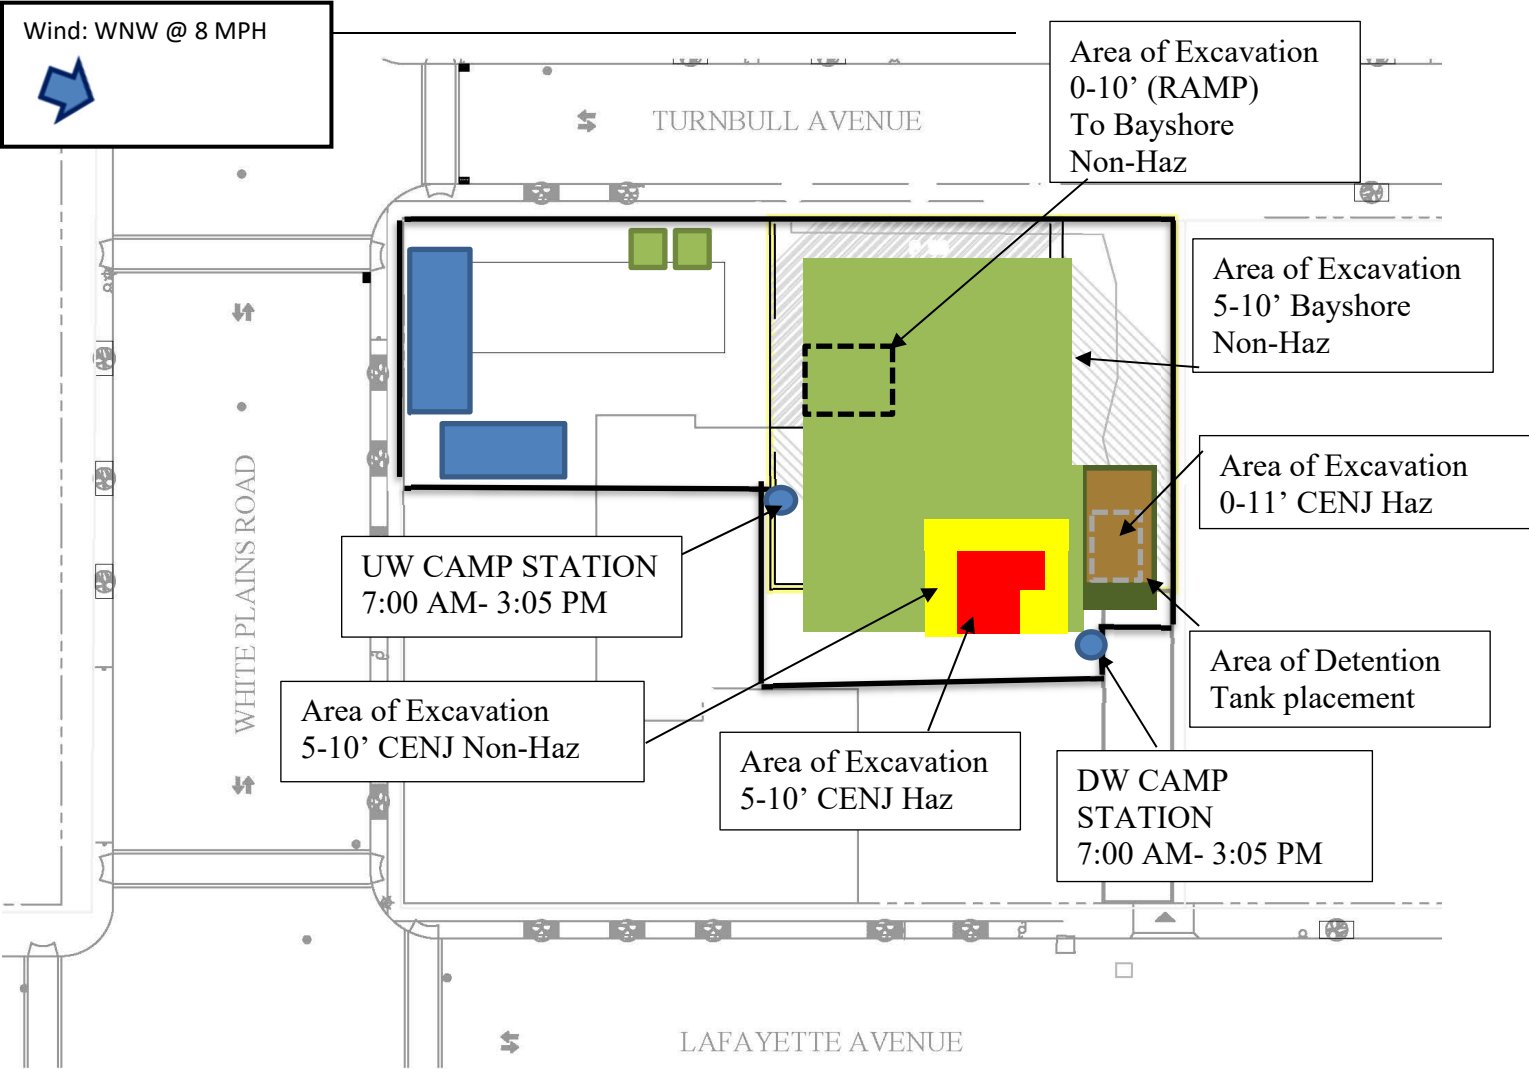

# DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-82°F, sunny RH: 65%, P: 29.91" of Hg Wind: WNW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 14, 2022

## PHOTOGRAPHS TAKEN TODAY:



**Photo 1:** Looking north, conditions of the Site at the start of day.



**Photo 2:** Looking west, drilling of pile casing within the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-82°F, sunny RH: 65%, P: 29.91" of Hg Wind: WNW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:20 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 14, 2022



**Photo 3:**  
View of concrete pad for  
detention tank.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-75°F, fair RH: 55%, P: 30.1" of Hg Wind: N @ 15 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 15, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRVS 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b> <u>Consigli</u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u>Urban Foundation Engineering</u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work along the northeast shoring of the building footprint.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-75°F, fair RH: 55%, P: 30.1" of Hg Wind: N @ 15 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 15, 2022

- Continued dewatering in vicinity of pile casing work areas.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:00 am to 3:05 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was along the northern perimeter of the Site and the downwind CAMP station was in the southeast corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.013 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue to finish setting tiebacks into place.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-75°F, fair RH: 55%, P: 30.1" of Hg Wind: N @ 15 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 15, 2022

### Site Layout

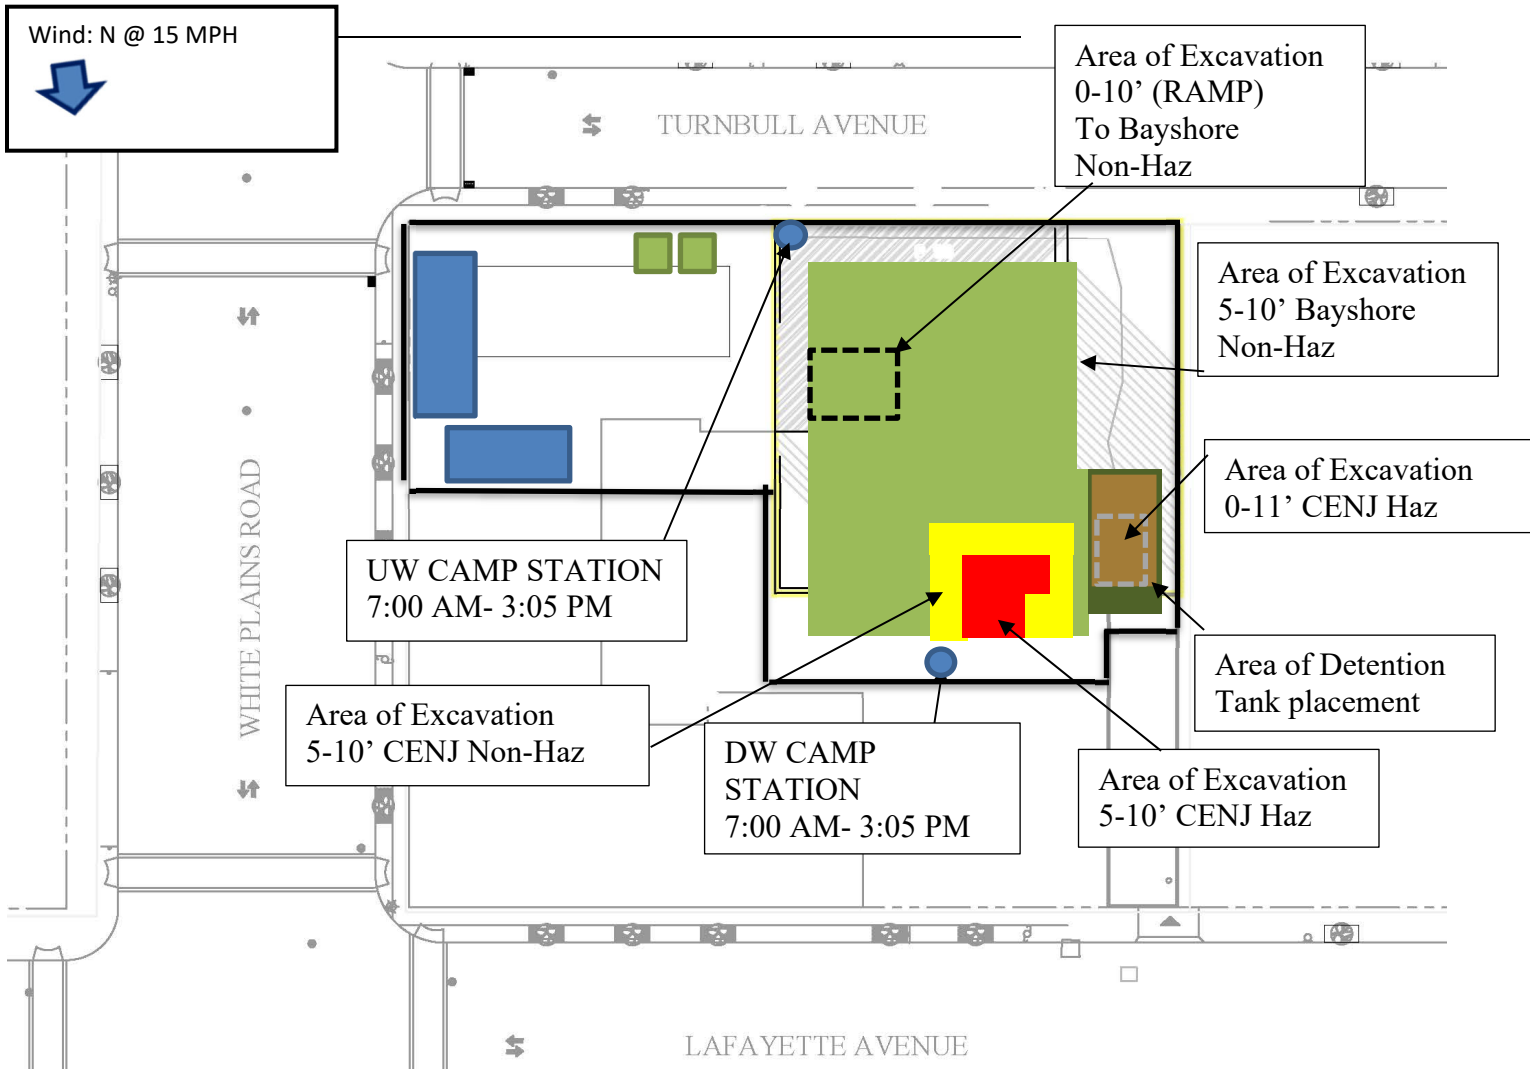

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-75°F, fair RH: 55%, P: 30.1" of Hg Wind: N @ 15 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 15, 2022

### PHOTOGRAPHS TAKEN TODAY:



**Photo 1:** Looking east, conditions of the Site at the start of day.



**Photo 2:** Looking east, Urban repairs shoring that was damaged from inclement weather.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-75°F, fair RH: 55%, P: 30.1" of Hg Wind: N @ 15 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 15, 2022



**Photo 3:**  
Looking south, drilling of pile casing along the east shoring of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-78°F, partly cloudy RH: 62%, P: 30.2" of Hg Wind: N @ 5 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 16, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRVS 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b> <u>Consigli</u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u>Urban Foundation Engineering</u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in the northern half of the building footprint.</li> </ul>	

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-78°F, partly cloudy RH: 62%, P: 30.2" of Hg Wind: N @ 5 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 16, 2022

- Continued dewatering in vicinity of pile casing work areas.
- Assembled formwork for walls above existing pad in the detention tank area.

### Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

### Air Monitoring:

- CAMP was conducted from 7:00 am to 2:55 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located in the northwest corner of the Site and the downwind CAMP station was along the center of the south perimeter.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.016 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.0 parts per million (ppm).

### Other Relevant Comments or Problems Encountered:

- None.

### **Anticipated Work Activities for the Next Day/ Week**

#### Roux

- Continue with CAMP and management of remedial action implementation activities.


#### Contractors

- Monitor pile casing/grout drilling activities.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-78°F, partly cloudy RH: 62%, P: 30.2" of Hg Wind: N @ 5 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 16, 2022

### Site Layout

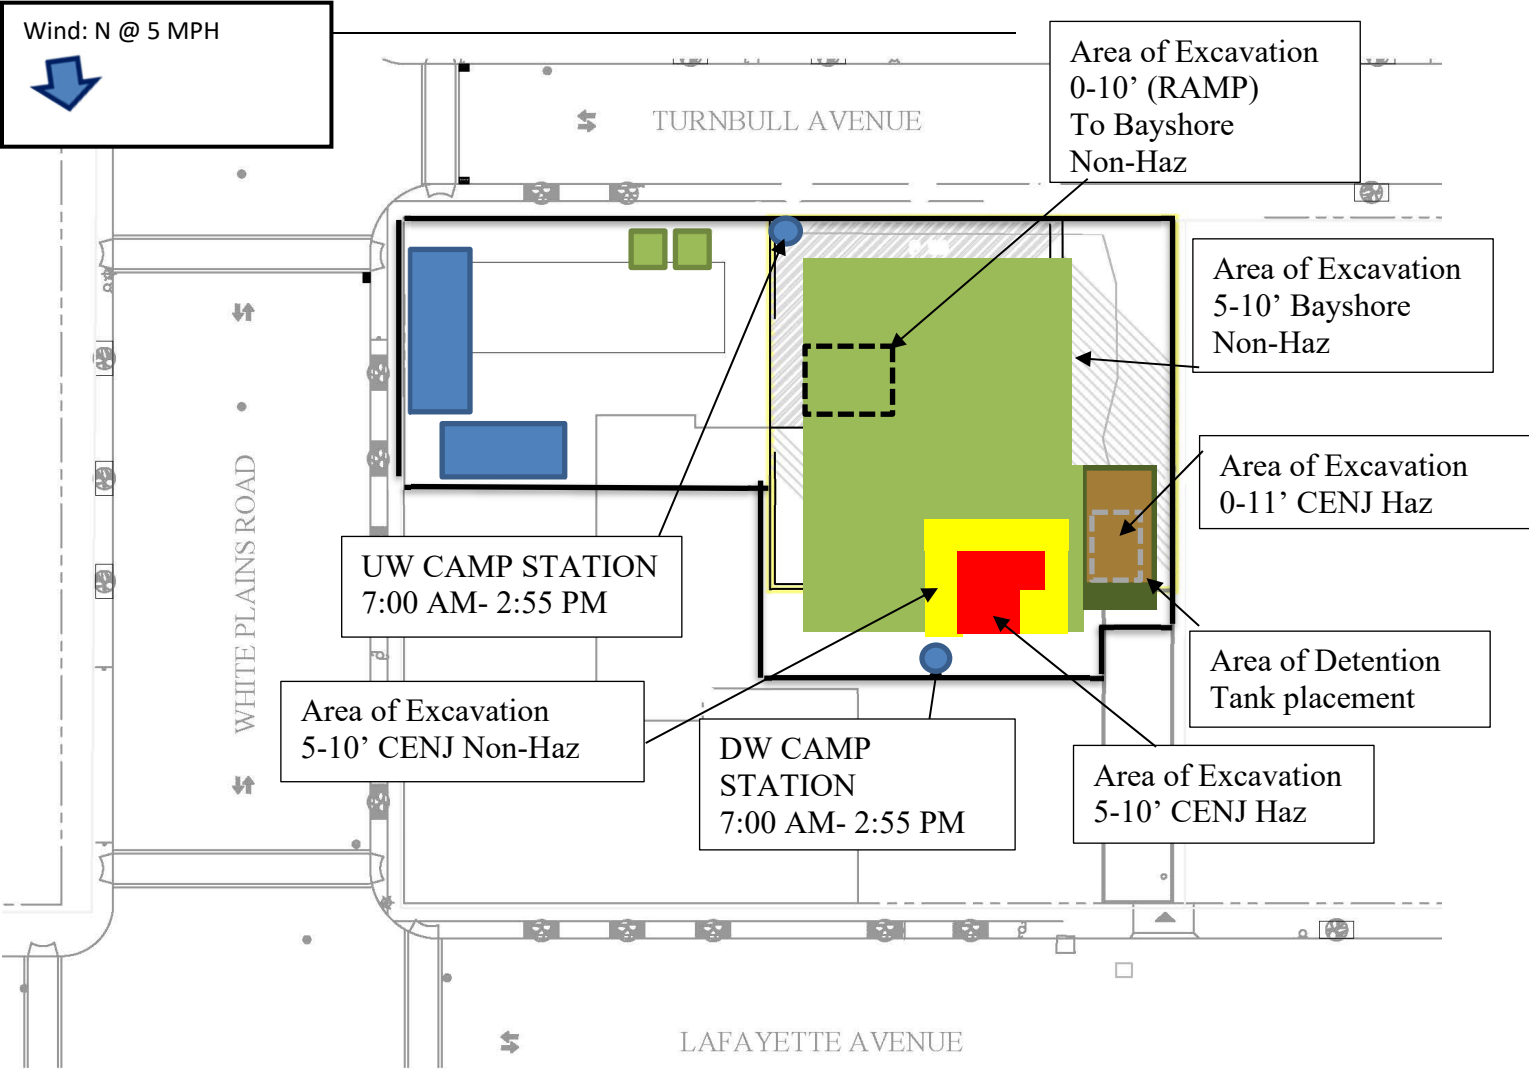

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	57-78°F, partly cloudy RH: 62%, P: 30.2" of Hg Wind: N @ 5 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 16, 2022

**PHOTOGRAPHS TAKEN TODAY:**



**Photo 1:** Looking east, drilling of pile casings along the eastern shoring and assembly of formwork in the detention tank area.



**Photo 2:** Looking northeast, progress of formwork assembly.

DAILY STATUS REPORT

PROJECT: BCP SITE No.	Park Lane Senior C203138	WEATHER:	57-78°F, partly cloudy RH: 62%, P: 30.2" of Hg Wind: N @ 5 mph
LOCATION:	1940 Turnbull Ave, Bronx, NY (Site)	TIME:	6:50 AM – 3:15 PM
PREPARED BY:	TJ Jennings	DATE:	September 16, 2022



**Photo 3:**  
View facing east, Urban excavates digout for grout mixture to be injected into pile casing.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-86°F, mostly cloudy RH: 67%, P: 29.94" of Hg Wind: WSW @ 3 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 19, 2022

Project Team	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRVS 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>

## Remedial Action Daily Inspection Description (Since Last Report)

### Roux Work Activities Performed Onsite:

- Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.

### Contractor Work Performed Onsite:

#### Consigli

- Oversight of construction activities.

#### Urban Foundation Engineering

- Continued pile grout-casing drill work in the northern half of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-86°F, mostly cloudy RH: 67%, P: 29.94" of Hg Wind: WSW @ 3 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 19, 2022

- Continued to assemble formwork for walls above existing pad in the detention tank area.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:05 am to 3:05 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located along the west-southwest perimeter of the Site and the downwind CAMP station was in the southeast corner due to accessibility.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.058 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-86°F, mostly cloudy RH: 67%, P: 29.94" of Hg Wind: WSW @ 3 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 19, 2022

### Site Layout

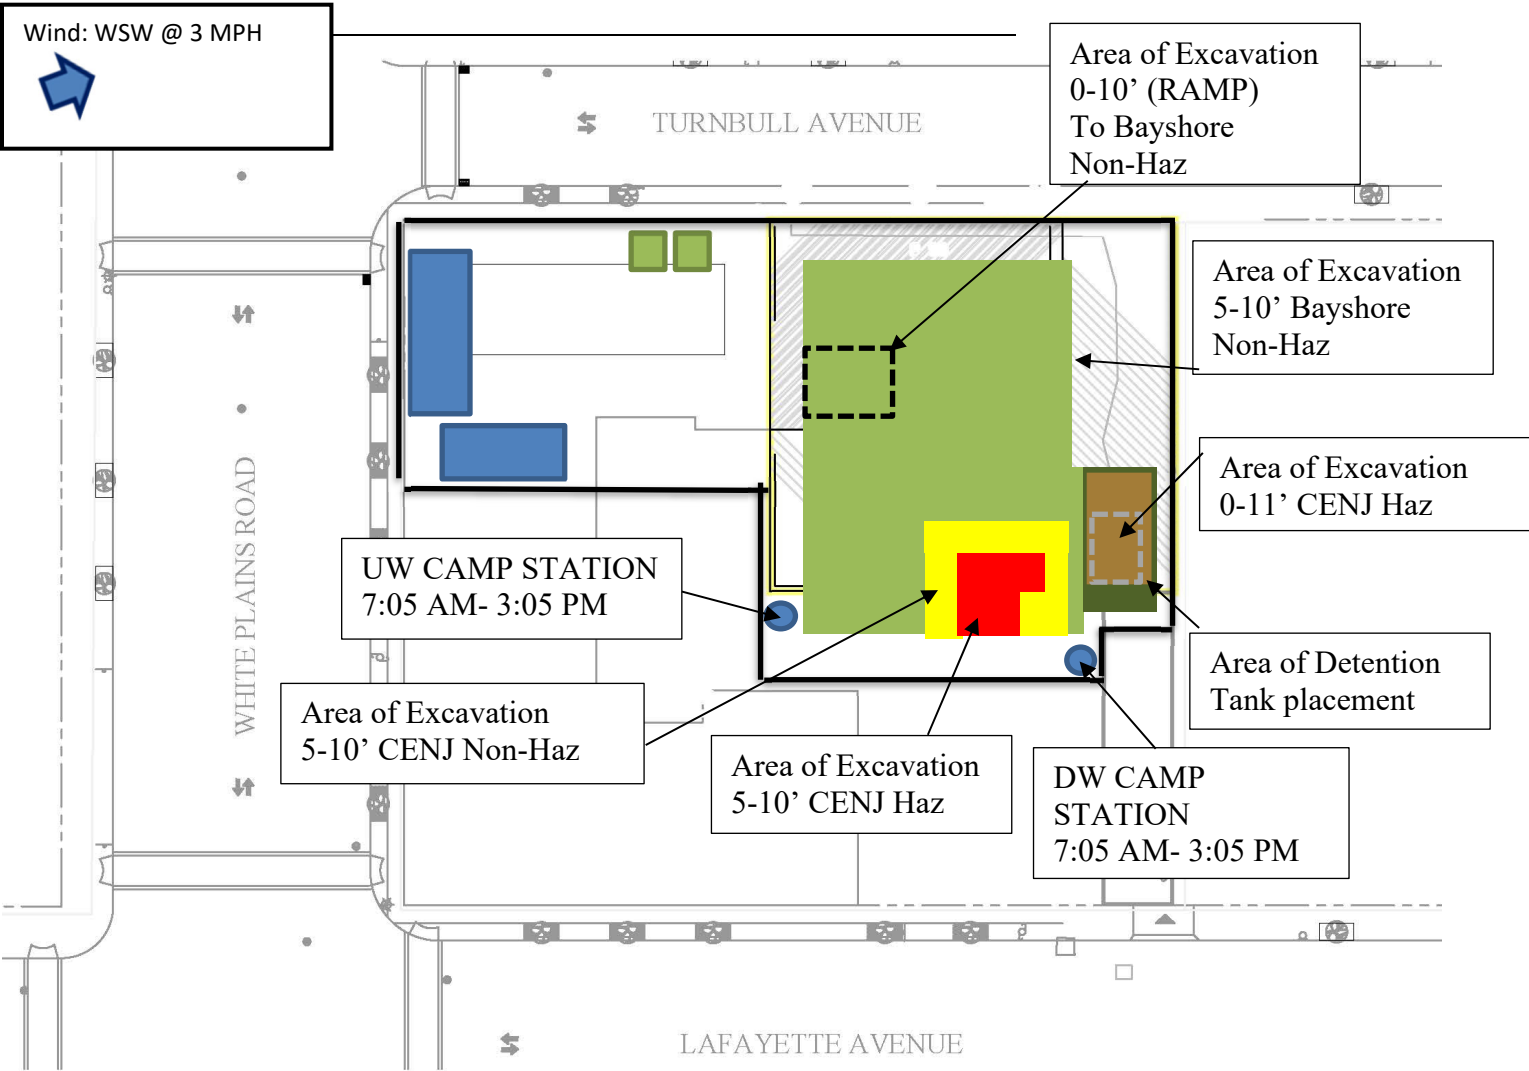

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-86°F, mostly cloudy RH: 67%, P: 29.94" of Hg Wind: WSW @ 3 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 19, 2022

**PHOTOGRAPHS TAKEN TODAY:**



**Photo 1:**  
Looking northeast, progress of formwork assembly in the detention tank area.



**Photo 2:**  
Looking east, drilling of pile casings in the northern half of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	68-86°F, mostly cloudy RH: 67%, P: 29.94" of Hg Wind: WSW @ 3 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 19, 2022



**Photo 3:**  
Looking east, drilling of pile casing and excavation of digout for grout mixture along east shoring.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-80°F, sunny RH: 79%, P: 29.86" of Hg Wind: NW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 20, 2022

Project Team	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Christian Hoelzli, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRV5 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>

## Remedial Action Daily Inspection Description (Since Last Report)

### Roux Work Activities Performed Onsite:

- Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.

### Contractor Work Performed Onsite:

#### Consigli

- Oversight of construction activities.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-80°F, sunny RH: 79%, P: 29.86" of Hg Wind: NW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 20, 2022

## Urban Foundation Engineering

- Continued pile grout-casing drill work in the northern half of the building footprint.
- Continued to assemble formwork for walls above existing pad in the detention tank area.
- Began to install waterproofing within formwork.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:05 am to 3:05 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located in the northwest corner and the downwind CAMP station was in the southeast corner of the Site.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.039 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.3 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-80°F, sunny RH: 79%, P: 29.86" of Hg Wind: NW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 20, 2022

### Site Layout

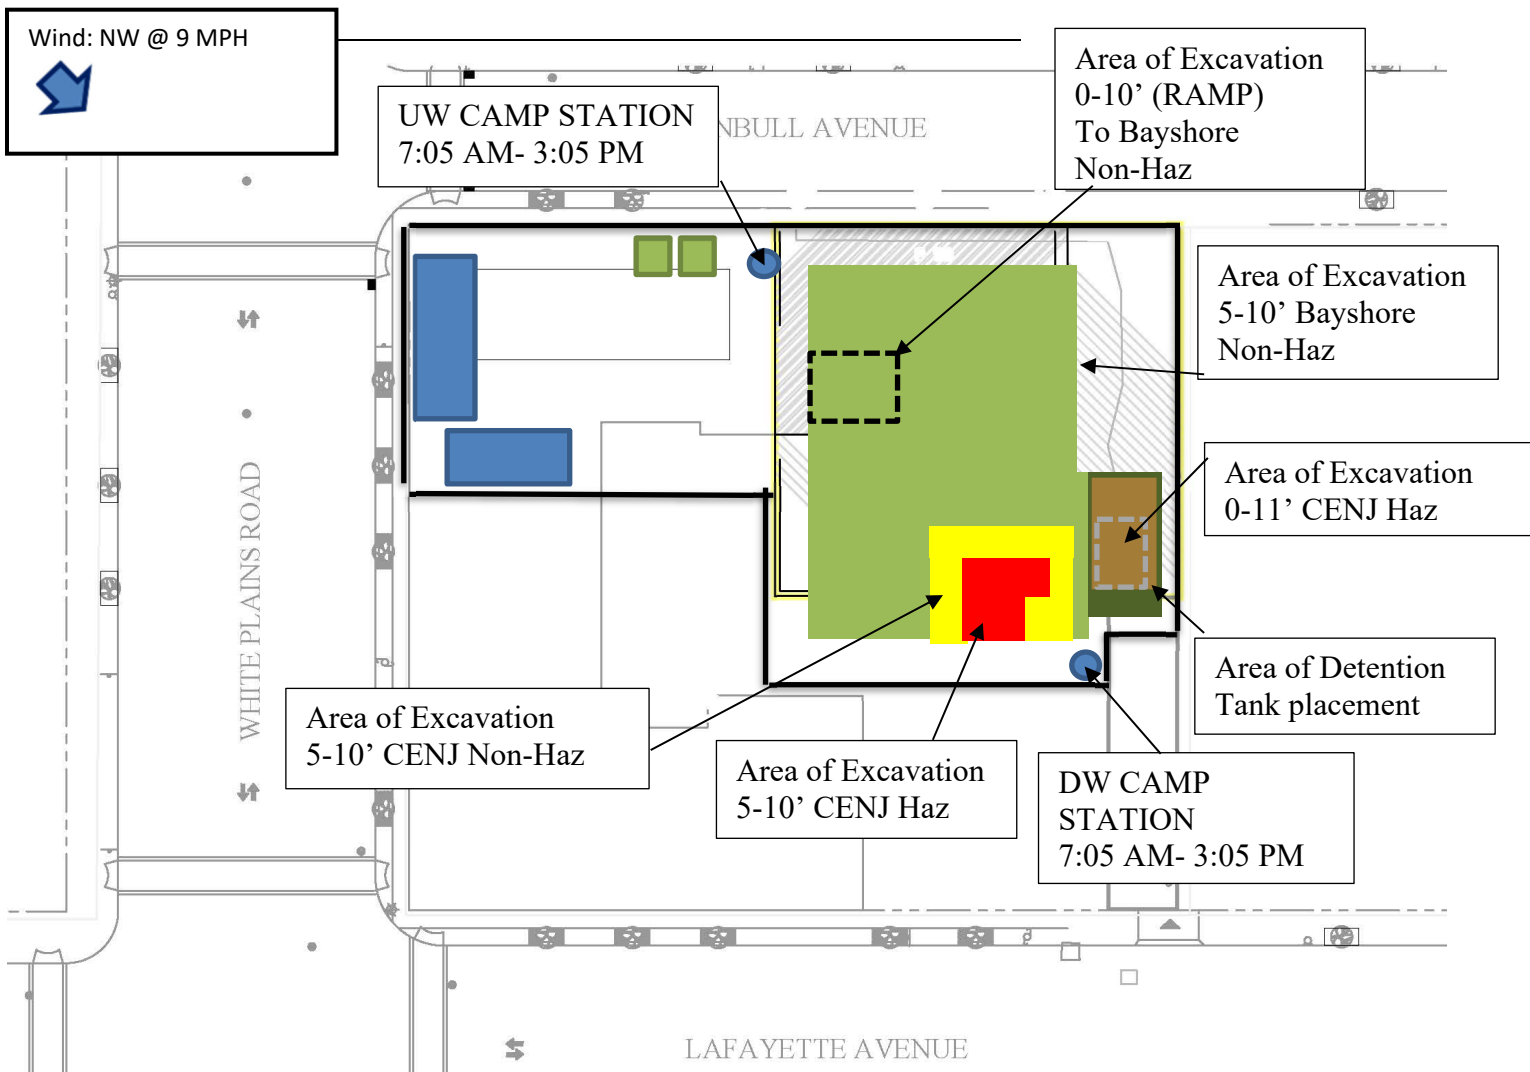

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-80°F, sunny RH: 79%, P: 29.86" of Hg Wind: NW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 20, 2022

### PHOTOGRAPHS TAKEN TODAY:



**Photo 1:**  
Looking northeast, progress of formwork assembly in the detention tank area.



**Photo 2:**  
Looking north, drilling of pile casing in the northern half of the building footprint.

DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	64-80°F, sunny RH: 79%, P: 29.86" of Hg Wind: NW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 20, 2022



**Photo 3:**  
Looking northwest, excavator removes soil from ramp.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	63-80°F, sunny RH: 66%, P: 29.96" of Hg Wind: NNW @ 1 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 21, 2022

Project Team	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>Christian Hoelzli, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRVS 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>

## Remedial Action Daily Inspection Description (Since Last Report)

### Roux Work Activities Performed Onsite:

- Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.

### Contractor Work Performed Onsite:

#### Consigli

- Oversight of construction activities.

#### Urban Foundation Engineering

- Continued pile grout-casing drill work in the northern half and the southeast corner of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	63-80°F, sunny RH: 66%, P: 29.96" of Hg Wind: NNW @ 1 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 21, 2022

- Continued to assemble formwork for walls above existing pad in the detention tank area.
- Continued to install waterproofing within formwork.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 8:00 am to 3:10 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located along the western boundary and the downwind CAMP station was in the southeast corner of the Site.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.022 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.3 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT


<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	63-80°F, sunny RH: 66%, P: 29.96" of Hg Wind: NNW @ 1 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 21, 2022

### Site Layout

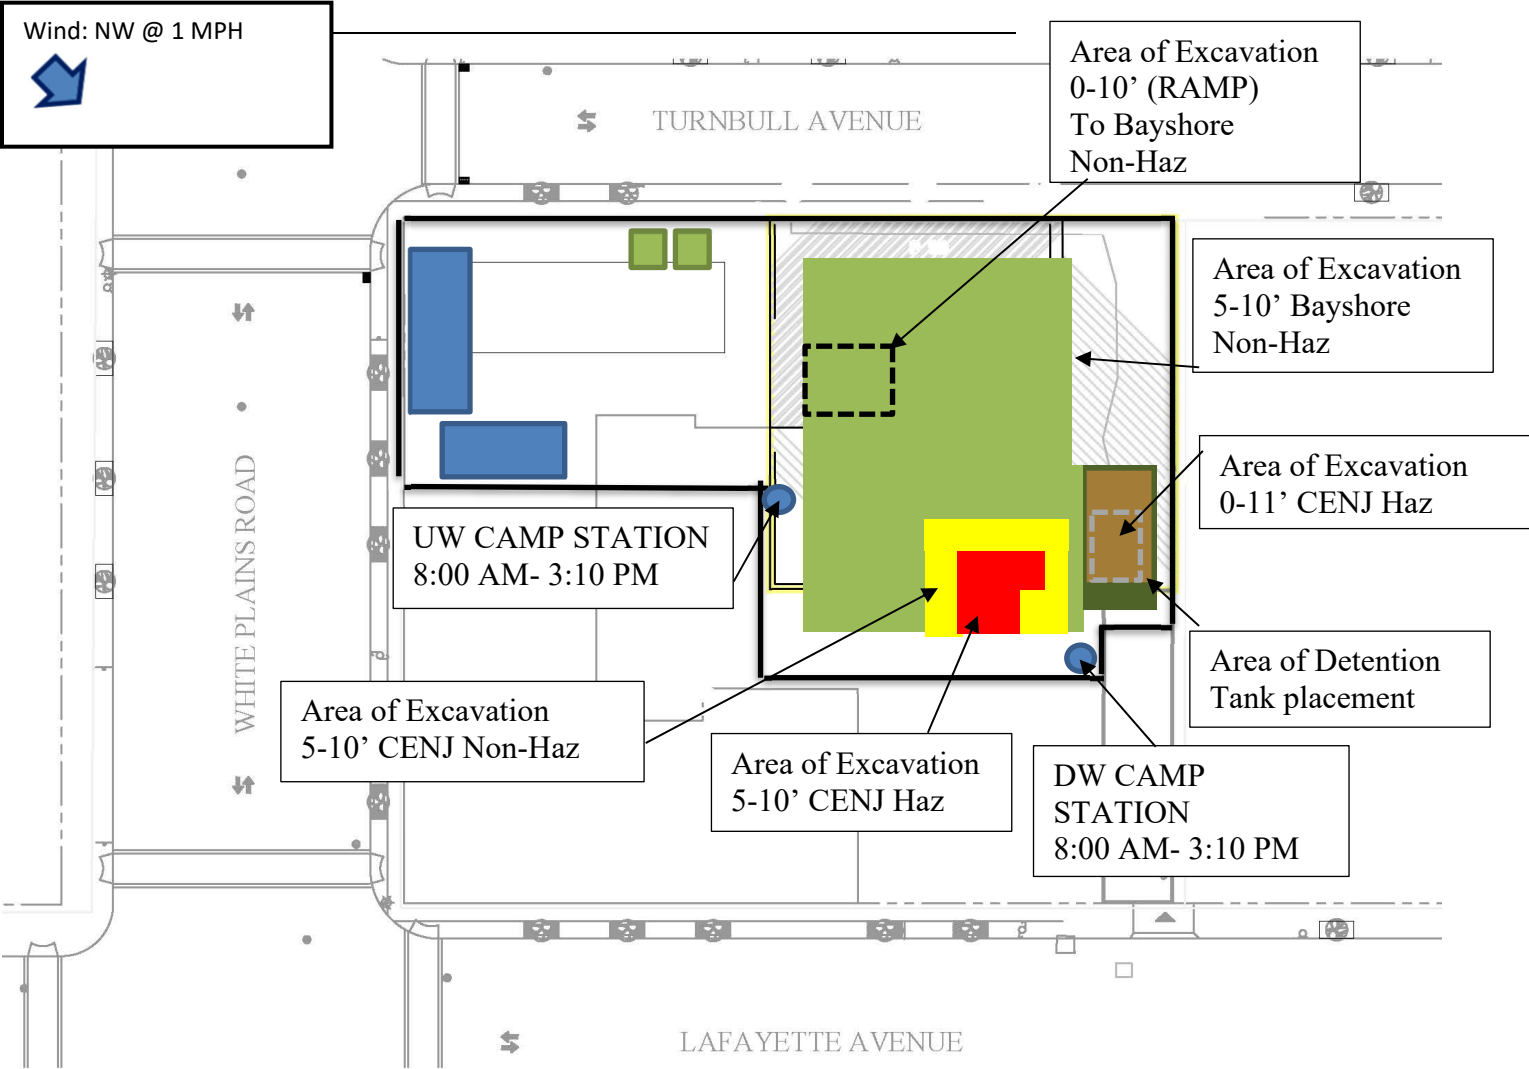

# DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	63-80°F, sunny RH: 66%, P: 29.96" of Hg Wind: NNW @ 1 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 21, 2022

<b>PHOTOGRAPHS TAKEN TODAY:</b>	
	<p><b>Photo 1:</b> Looking north, progress of formwork assembly in the detention tank area.</p>

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	63-80°F, sunny RH: 66%, P: 29.96" of Hg Wind: NNW @ 1 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 21, 2022



**Photo 2:**  
Looking northeast, drilling of pile casing in the southeast corner of the building footprint.

DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	63-80°F, sunny RH: 66%, P: 29.96" of Hg Wind: NNW @ 1 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	7:00 AM – 3:30 PM
<b>PREPARED BY:</b>	Christian Hoelzli	<b>DATE:</b>	September 21, 2022



**Photo 3:**  
Looking east, digout made in southwestern corner of Site for drilling the pile casing.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-74°F, cloudy w/ heavy rain RH: 74%, P: 29.65" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:05 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 22, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny De-La Cruz, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRVS 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b> <u>Consigli</u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u>Urban Foundation Engineering</u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in the northern half and the southeast corner of the building footprint.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-74°F, cloudy w/ heavy rain RH: 74%, P: 29.65" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:05 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 22, 2022

- Continued to install waterproofing within formwork in the detention tank area.
- Moved soil to reconfigure the digout for grout mixing.
- Started dewatering in the northwest corner of the building footprint.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 8:15 am to 11:30 am for when soil intrusive activities were performed for the day. The shortened timeframe for conducting CAMP was due to heavy rainfall throughout the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located in the northwest corner of the Site and the downwind CAMP station was along the east-southeastern perimeter.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.009 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue modifications of digouts, when necessary.
- Continue dewatering of digouts, when necessary.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-74°F, cloudy w/ heavy rain RH: 74%, P: 29.65" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:05 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 22, 2022

### Site Layout

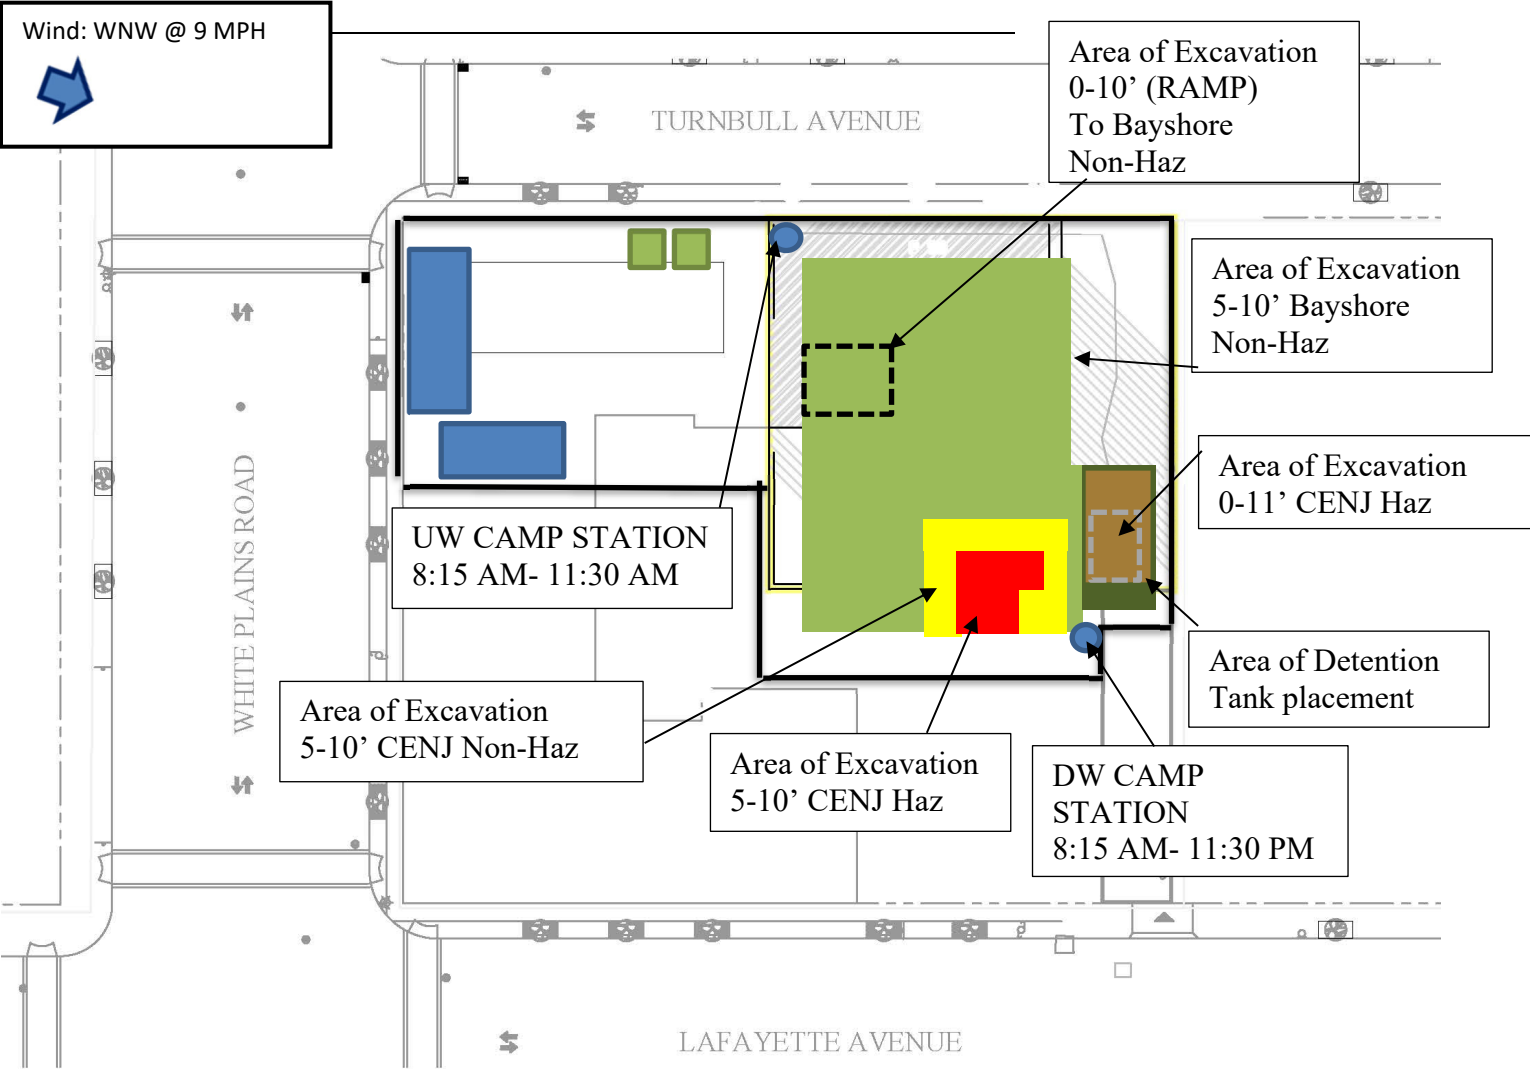

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-74°F, cloudy w/ heavy rain RH: 74%, P: 29.65" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:05 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 22, 2022

### PHOTOGRAPHS TAKEN TODAY:



**Photo 1:**  
Looking north, progress of formwork assembly in the detention tank area.



**Photo 2:**  
Looking north, drilling of pile casing along the central eastern shoring of the building footprint.

DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-74°F, cloudy w/ heavy rain RH: 74%, P: 29.65" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:05 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 22, 2022



**Photo 3:**  
Looking east, digout made in southwestern corner of Site for drilling of the pile casing.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-63°F, fair RH: 54%, P: 29.92" of Hg Wind: NNW @ 16 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:30 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 23, 2022

Project Team	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny De-La Cruz, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Atlas Copco XRVS 1350 CD7 Compressed Air Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>

## Remedial Action Daily Inspection Description (Since Last Report)

### Roux Work Activities Performed Onsite:

- Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.

### Contractor Work Performed Onsite:

#### Consigli

- Oversight of construction activities.

#### Urban Foundation Engineering

- Continued pile grout-casing drill work in the northern half and the southeast corner of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-63°F, fair RH: 54%, P: 29.92" of Hg Wind: NNW @ 16 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:30 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 23, 2022

- Continued to move soil to reconfigure the digout for grout mixing.
- Continued dewatering in the northwest corner of the building footprint.
- Mobilized cement for detention tank structure.
- Poured concrete for the walls of the detention tank structure.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:05 am to 3:15 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located in the northwest corner of the Site and the downwind CAMP station was along the southern perimeter.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.014 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.1 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.
- Collect endpoint soil sample BDS-14 within the Track 4 area.


### Contractors

- Monitor pile casing/grout drilling activities.
- Continue modification and/or dewatering of digouts, when necessary.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-63°F, fair RH: 54%, P: 29.92" of Hg Wind: NNW @ 16 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:30 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 23, 2022

### Site Layout

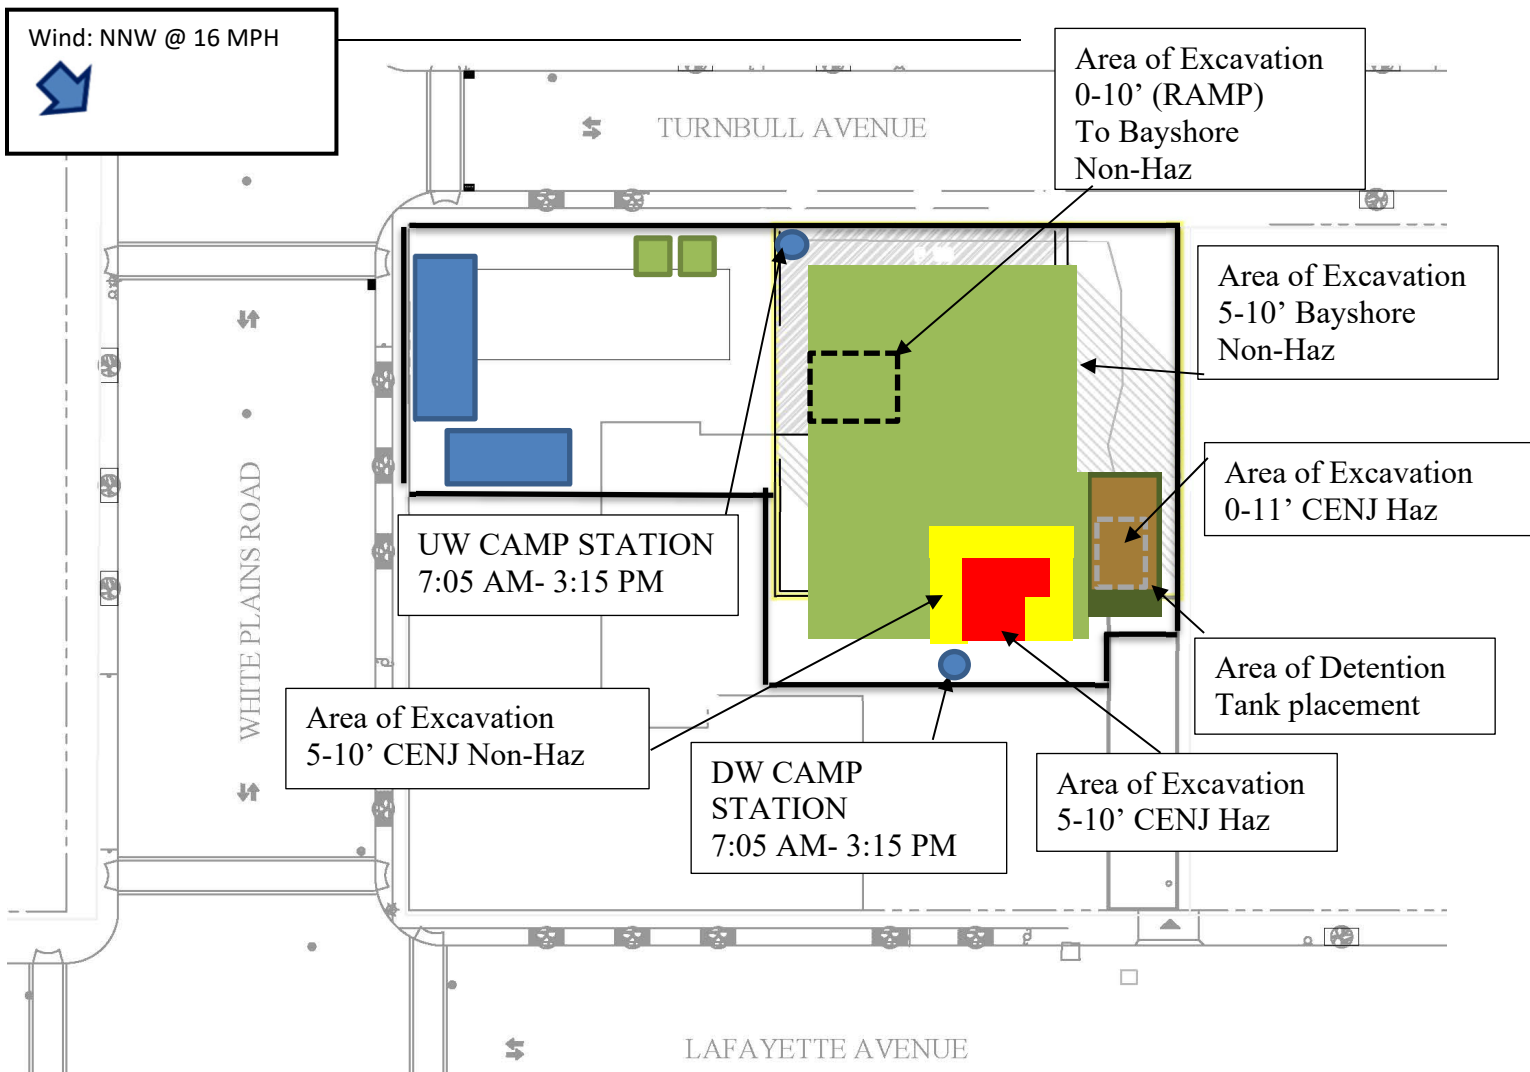

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-63°F, fair RH: 54%, P: 29.92" of Hg Wind: NNW @ 16 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:30 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 23, 2022

### PHOTOGRAPHS TAKEN TODAY:



**Photo 1:**  
Looking northeast, drilling of pile casing and modification of digout for grout mixing.



**Photo 2:**  
Looking northwest, Urban receiving delivery of cement for detention tank structure.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	51-63°F, fair RH: 54%, P: 29.92" of Hg Wind: NNW @ 16 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:30 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 23, 2022



**Photo 3:**  
Looking northeast, pouring of concrete for the walls of the detention tank structure.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	60-75°F, fair RH: 78%, P: 29.68" of Hg Wind: WSW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 26, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny De-La Cruz, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Sullair 1150XH Air Compressor Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b> <u>Consigli</u> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<u>Urban Foundation Engineering</u> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in the northern half and the southeast corner of the building footprint.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	60-75°F, fair RH: 78%, P: 29.68" of Hg Wind: WSW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 26, 2022

- Continued to assemble formwork for the detention tank structure.
- Continued to move soil for grout mixing and site accessibility.
- Continued dewatering in the northwest corner of the building footprint.
- Demobilized existing air compressor and mobilized replacement machine, Sullair 1150XH.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:05 am to 3:00 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located towards the southwest corner of the Site and the downwind CAMP station was towards the northeast corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.075 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.
- Collect endpoint soil sample BDS-14 within the Track 4 area.


### Contractors

- Continue to monitor pile casing/grout drilling activities until completion.
- Continue modification and/or dewatering of digouts, when necessary.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	60-75°F, fair RH: 78%, P: 29.68" of Hg Wind: WSW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 26, 2022

### Site Layout

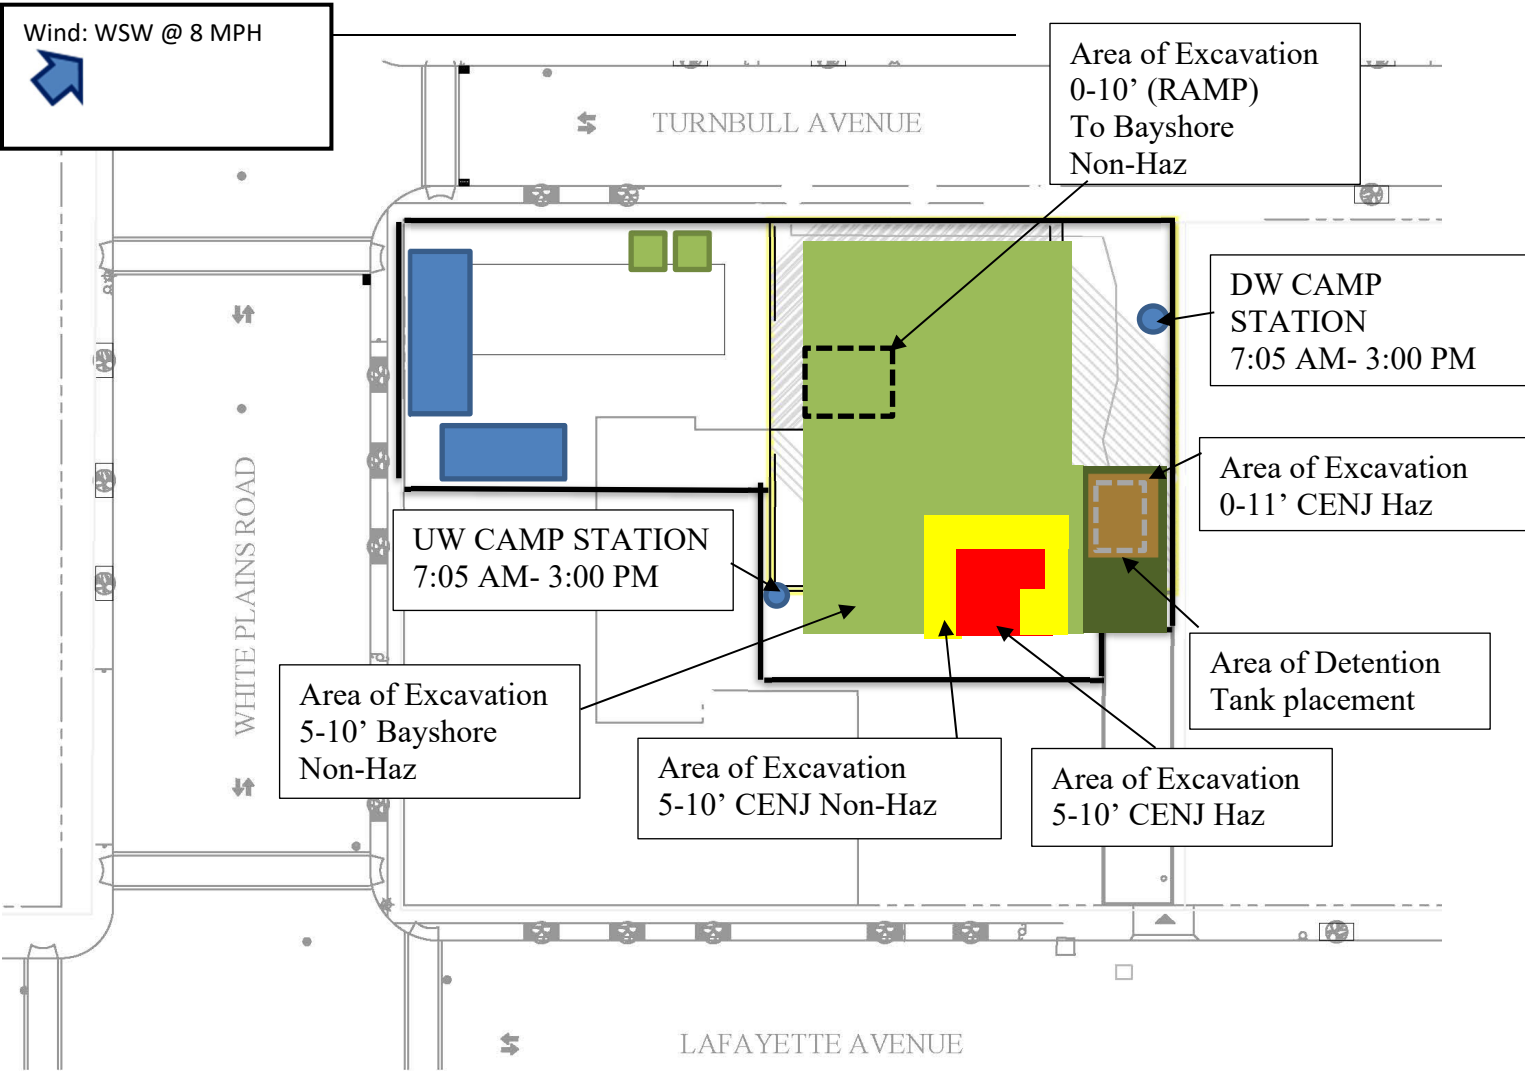

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	60-75°F, fair RH: 78%, P: 29.68" of Hg Wind: WSW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 26, 2022

### PHOTOGRAPHS TAKEN TODAY:



**Photo 1:**  
Looking northeast, modification of previous digout for grout mixing.



**Photo 2:**  
Looking southwest, progress of formwork assembly in the detention tank area.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	60-75°F, fair RH: 78%, P: 29.68" of Hg Wind: WSW @ 8 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 26, 2022



**Photo 3:**  
Drilling of pile casing and modification of terrain for grout mixing path in the northeast area of the Site.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	55-73°F, partly cloudy RH: 51%, P: 29.83" of Hg Wind: WSW @ 11 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 27, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny De-La Cruz, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Sullair 1150XH Air Compressor Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b> <b>Consigli</b> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<b>Urban Foundation Engineering</b> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in the central north portion and along the east shoring of the building footprint.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	55-73°F, partly cloudy RH: 51%, P: 29.83" of Hg Wind: WSW @ 11 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 27, 2022

- Continued to assemble formwork of the detention tank structure.
- Continued to move soil for grout mixing and site accessibility.
- Continued dewatering in the northwest corner of the building footprint.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:00 am to 3:00 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located towards the southwest corner of the Site and the downwind CAMP station was towards the northeast corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.068 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.
- Collect endpoint soil sample BDS-14 within the Track 4 area.


### Contractors

- Continue to monitor pile casing/grout drilling activities until completion.
- Continue modification and/or dewatering of digouts, when necessary.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

# DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	55-73°F, partly cloudy RH: 51%, P: 29.83" of Hg Wind: WSW @ 11 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 27, 2022

## Site Layout

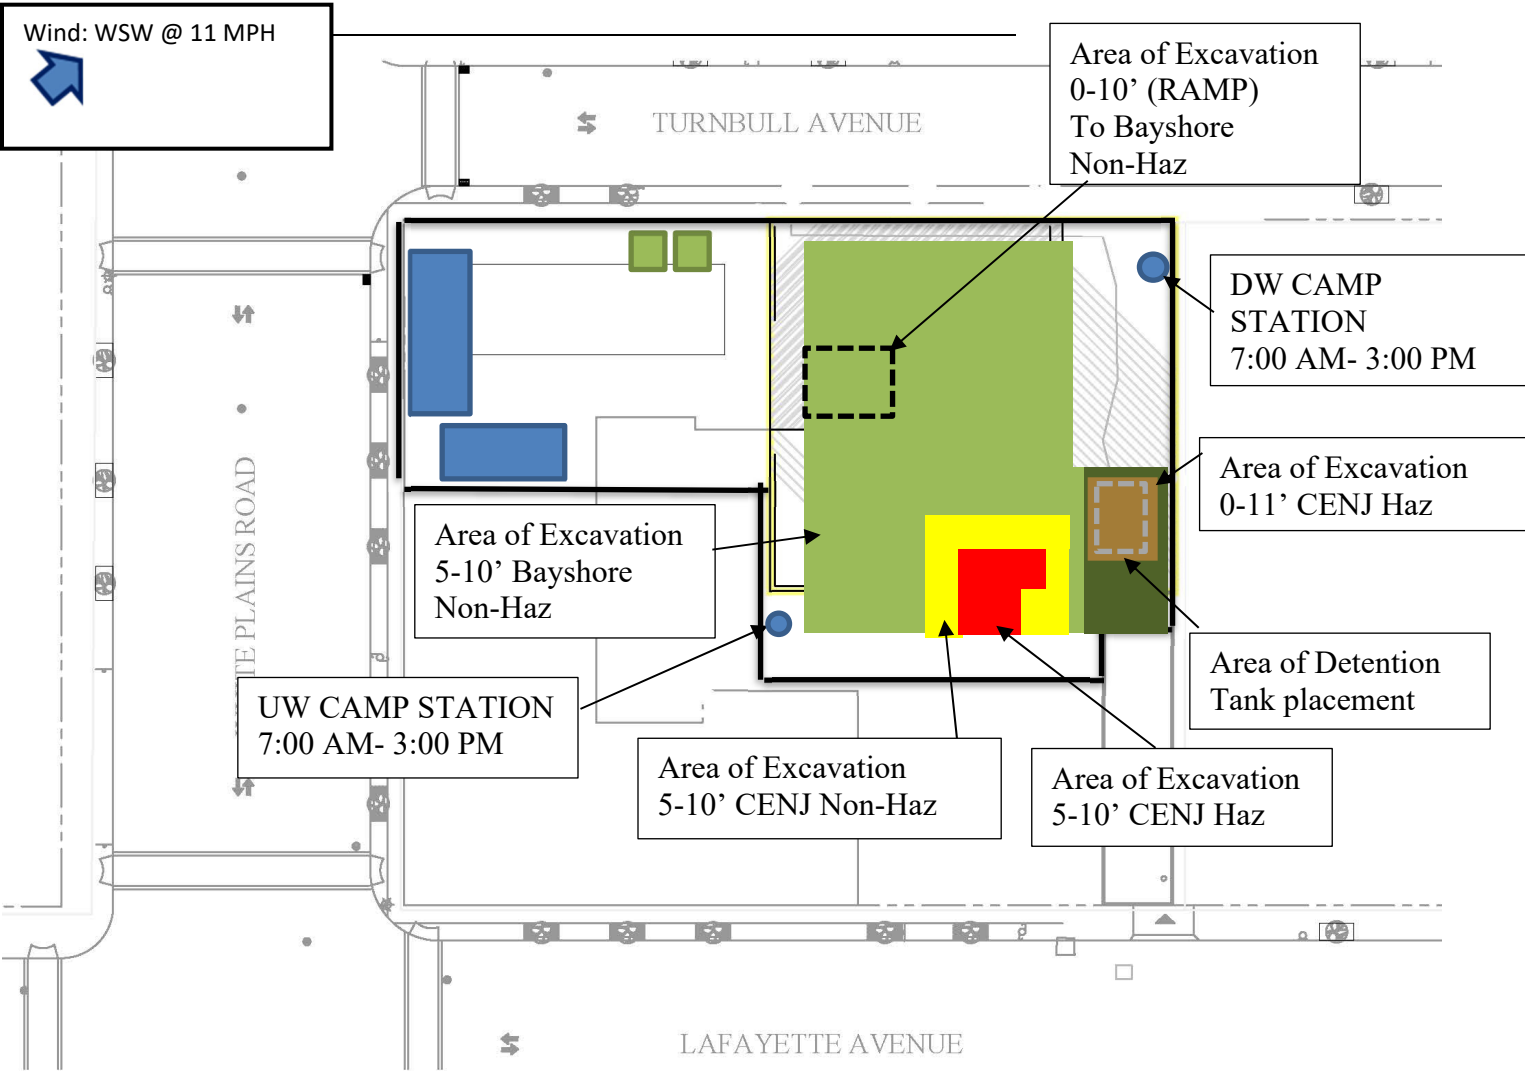

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	55-73°F, partly cloudy RH: 51%, P: 29.83" of Hg Wind: WSW @ 11 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 27, 2022

### PHOTOGRAPHS TAKEN TODAY:



#### **Photo 1:**

Looking northeast, soil stockpiled from previous digout.



#### **Photo 2:**

Looking south, formwork of the detention tank in progress.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	55-73°F, partly cloudy RH: 51%, P: 29.83" of Hg Wind: WSW @ 11 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:45 AM – 3:15 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 27, 2022



**Photo 3:**  
Looking northeast, progress of pile casing work along the east shoring of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-72°F, fair RH: 67%, P: 30.06" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 28, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny De-La Cruz, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Sullair 1150XH Air Compressor Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>
<b>Remedial Action Daily Inspection Description (Since Last Report)</b>	
<b>Roux Work Activities Performed Onsite:</b> <ul style="list-style-type: none"> <li>Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.</li> </ul>	
<b>Contractor Work Performed Onsite:</b> <b>Consigli</b> <ul style="list-style-type: none"> <li>Oversight of construction activities.</li> </ul>	
<b>Urban Foundation Engineering</b> <ul style="list-style-type: none"> <li>Continued pile grout-casing drill work in the central north portion and along the east shoring of the building footprint.</li> </ul>	

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-72°F, fair RH: 67%, P: 30.06" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 28, 2022

- Continued to assemble formwork of the detention tank structure.
- Continued to move soil for grout mixing and site accessibility.
- Continued dewatering in the northwest corner of the building footprint.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:00 am to 2:55 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located towards the southwest corner of the Site and the downwind CAMP station was towards the southeast corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.091 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.3 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.
- Collect endpoint soil sample BDS-14 within the Track 4 area.


### Contractors

- Continue to monitor pile casing/grout drilling activities until completion.
- Continue modification and/or dewatering of digouts, when necessary.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-72°F, fair RH: 67%, P: 30.06" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 28, 2022

### Site Layout

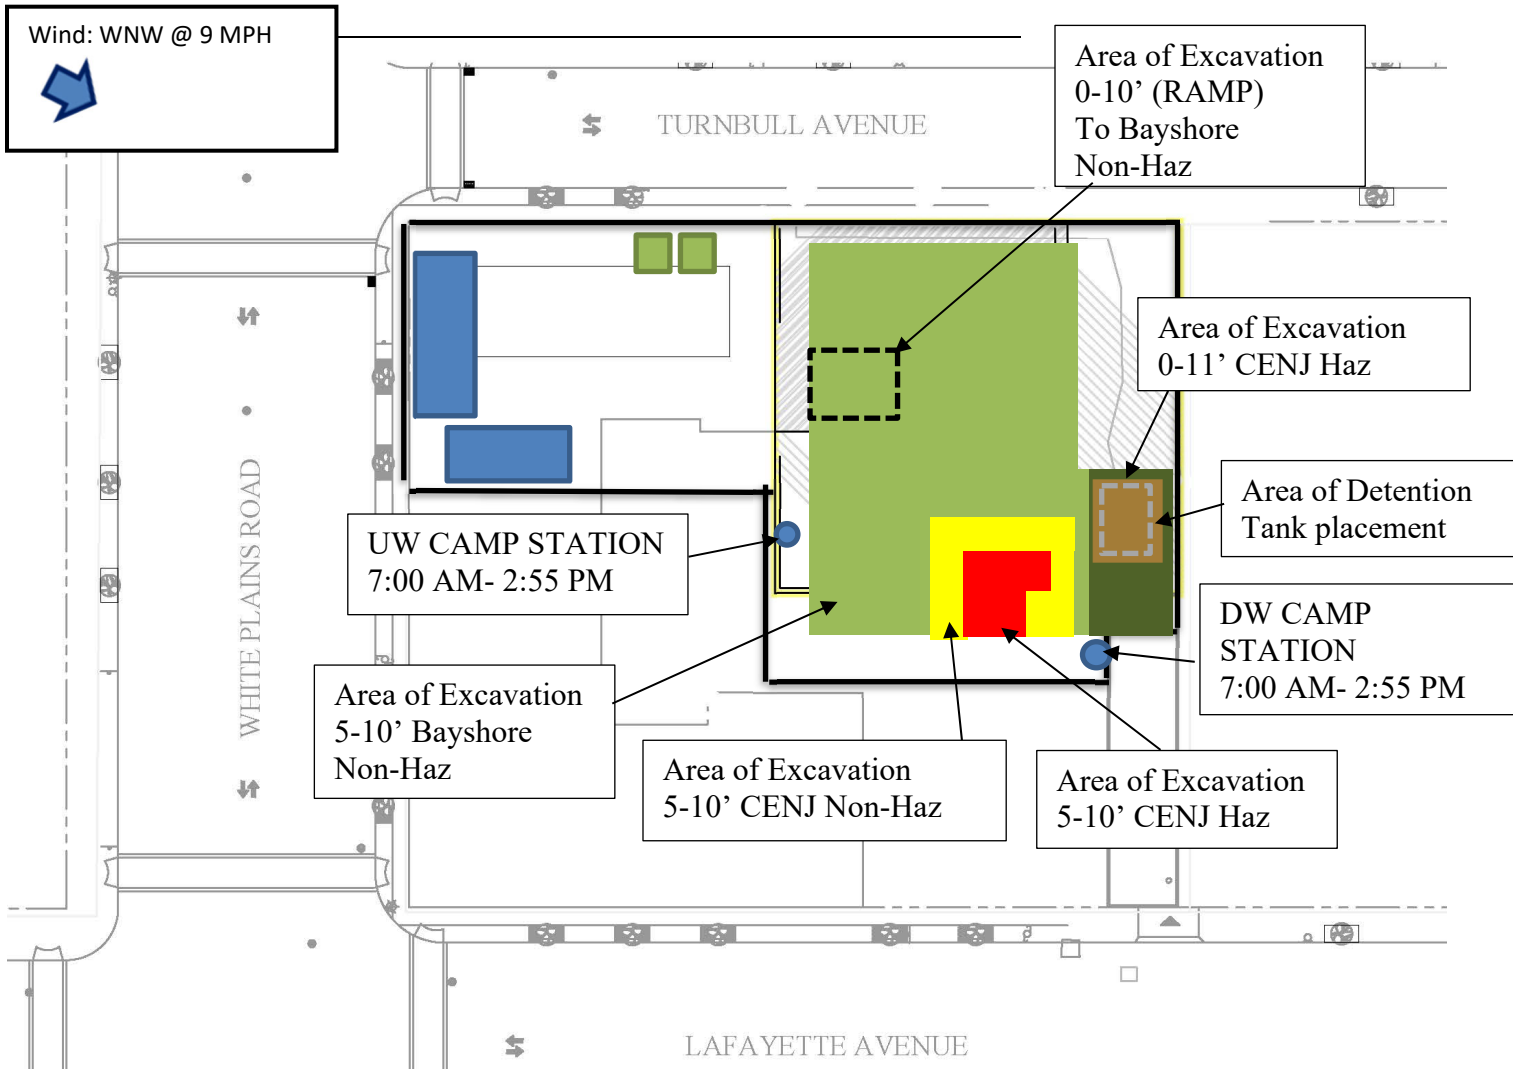

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-72°F, fair RH: 67%, P: 30.06" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 28, 2022

## PHOTOGRAPHS TAKEN TODAY:



### **Photo 1:**

Looking northeast, excavator and drill rig positioning pile casing within the building footprint.



### **Photo 2:**

Looking north, drilling of pile casing along the eastern shoring.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-72°F, fair RH: 67%, P: 30.06" of Hg Wind: WNW @ 9 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:25 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 28, 2022



**Photo 3:**  
Facing east, Urban receives  
delivery of cement.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-66°F, mostly sunny RH: 77%, P: 30.29" of Hg Wind: NW @ 2 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:50 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 29, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>Christian Hoelzli, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny De-La Cruz, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Sullair 1150XH Air Compressor Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>

## Remedial Action Daily Inspection Description (Since Last Report)

### Roux Work Activities Performed Onsite:

- Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.
- Collected the following endpoint soil sample from within the Track 4 Lead Hotspot:
  - Composite sample BDS-14 (2-4) from the bottom of the Grid 14 within the Track 4 area.
- The composite sample taken today was collected into Encore kits to be analyzed for VOCs by EPA Method 8260; amber jars to be analyzed for TCL SVOCs by EPA Method 8270, Pesticides by EPA Method 8081B, TAL Metals by Method 6010, Hexavalent Chromium by EPA Method 7196A, PCBs by EPA Method SW-846 8082A, Total Cyanide via EPA Method 902B, Mercury by EPA Method 7471B, Herbicides by Method 8151A, and Trivalent Chromium; and plastic bottles to be analyzed for PFAS.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-66°F, mostly sunny RH: 77%, P: 30.29" of Hg Wind: NW @ 2 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:50 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 29, 2022

- Spraypainted gridlines demarcating the soil grids on the eastern construction fence of the Site in dark green.

## Contractor Work Performed Onsite:

### Consigli

- Oversight of construction activities.

### Urban Foundation Engineering

- Continued pile grout-casing drill work in the central region and southeast corner of the building footprint.
- Continued to assemble formwork of the detention tank structure.
- Continued to move soil for grout mixing and site accessibility.

### Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:15 am to 3:15 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located in the northwest corner of the Site and the downwind CAMP station was in the southeast corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.021 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## Anticipated Work Activities for the Next Day/ Week

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Continue to monitor pile casing/grout drilling activities until completion.
- Continue modification and/or dewatering of digouts, when necessary.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

## DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-66°F, mostly sunny RH: 77%, P: 30.29" of Hg Wind: NW @ 2 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:50 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 29, 2022

### Site Layout

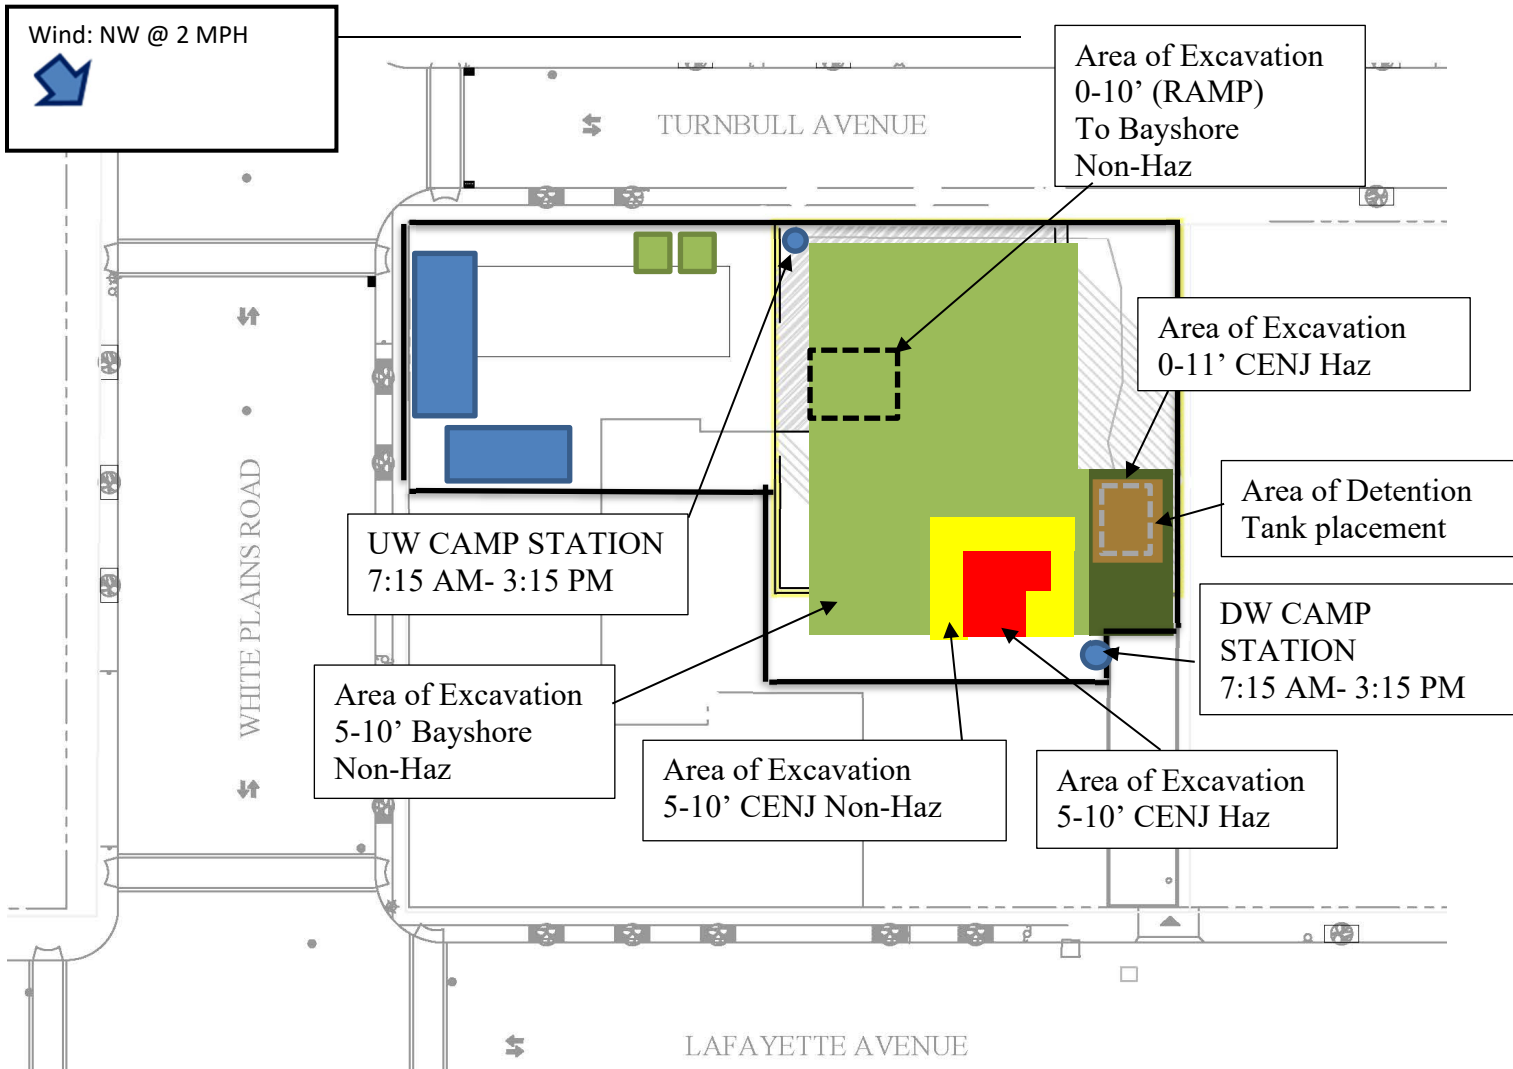

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-66°F, mostly sunny RH: 77%, P: 30.29" of Hg Wind: NW @ 2 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:50 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 29, 2022

**PHOTOGRAPHS TAKEN TODAY:**



**Photo 1:**  
Facing north, steel rods being installed into pile casing along the east shoring.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-66°F, mostly sunny RH: 77%, P: 30.29" of Hg Wind: NW @ 2 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:50 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 29, 2022



**Photo 2:**  
Facing north, view of case drilling  
in the southeast corner of the  
building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-66°F, mostly sunny RH: 77%, P: 30.29" of Hg Wind: NW @ 2 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:50 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 29, 2022



**Photo 3:**  
Looking east, view of construction fence with approximate locations of grid lines for endpoint sampling spraypainted in green.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-65°F, partly sunny RH: 63%, P: 30.33" of Hg Wind: NE @ 12 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:55 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 30, 2022

<b>Project Team</b>	
<b>Consultant/Engineer:</b> <ul style="list-style-type: none"> <li>Frank Cherena, Roux</li> <li>Kathryn Sommo, Roux</li> <li>Christian Hoelzli, Roux</li> </ul>	<b>Safety Officer:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> </ul>
<b>General Contractor:</b> <ul style="list-style-type: none"> <li>Consigli</li> <li>Urban</li> <li>Mueser Rutledge Consulting Engineers (MRCE)</li> </ul>	<b>Site Manager/ Supervisor:</b> <ul style="list-style-type: none"> <li>Ray Romani, Consigli</li> </ul>
<b>Personnel Present Onsite and Affiliation:</b> <ul style="list-style-type: none"> <li>TJ Jennings, Roux</li> <li>Jan Velebir, DOB</li> <li>Ray Romani, Consigli</li> <li>Pat Sullivan, Consigli</li> <li>Brianny De-La Cruz, Consigli (Intern)</li> <li>Tom Henchy, Urban (Super)</li> <li>Chris Lucchese, Urban</li> <li>Lancelot Samuel, Urban</li> <li>Ambrosio Ramirez, Urban</li> <li>Boyie Ballai, Urban</li> <li>Anthony Rodriguez, Urban</li> <li>Eugene McFadden, Urban</li> <li>Jose Ramirez, Urban</li> <li>Sylvia Garcia, Urban</li> <li>Elijah Mercado, Urban</li> <li>Dave Seebant, Urban</li> <li>Henry P., Urban</li> <li>Philip Fiet, Urban</li> <li>Victor Damaso</li> <li>Masoud Janbaz, MRCE</li> <li>A. Chebli, VTI</li> </ul>	<b>Equipment Onsite:</b> <ul style="list-style-type: none"> <li>1 CAT UFE 214 Excavator</li> <li>1 Comacchio MC 800 S Drill Rig</li> <li>1 Rotary Drill Rig</li> <li>1 Sullair 1150XH Air Compressor Machine</li> <li>1 Dumpster</li> <li>3 Generators</li> <li>2 Concrete Pan Mixer</li> <li>1 Hand Cutting Torch</li> <li>1 Chainsaw</li> </ul>

## Remedial Action Daily Inspection Description (Since Last Report)

### Roux Work Activities Performed Onsite:

- Roux conducted CAMP during ground intrusive activities and management of remedial action implementation activities.

### Contractor Work Performed Onsite:

#### Consigli

- Oversight of construction activities.

#### Urban Foundation Engineering

- Continued pile grout-casing drill work in the central region and southeast corner of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-65°F, partly sunny RH: 63%, P: 30.33" of Hg Wind: NE @ 12 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:55 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 30, 2022

- Continued to assemble formwork for the detention tank structure.
- Continued to move soil for grout mixing and site accessibility.
- Mobilized materials onto the Site.

## Mueser Rutledge Consulting Engineers

- Oversight of pile casing activities.

## Air Monitoring:

- CAMP was conducted from 7:05 am to 3:35 pm for when soil intrusive activities were performed for the day. CAMP station points were chosen based on wind direction, accessibility, and safety. The upwind CAMP station was located towards the northeast corner of the Site and the downwind CAMP station was towards the southwest corner.
- There were no exceedances of dust or volatile organic compounds (VOCs). The maximum corrected downwind concentration for dust was 0.012 milligrams per cubic meter (mg/m<sup>3</sup>). The maximum corrected downwind concentration of VOCs was 0.2 parts per million (ppm).

## Other Relevant Comments or Problems Encountered:

- None.

## **Anticipated Work Activities for the Next Day/ Week**

### Roux

- Continue with CAMP and management of remedial action implementation activities.


### Contractors

- Continue to monitor well drilling activities until completion.
- Continue modification and/or dewatering of digouts, when necessary.
- Continue construction of detention tank structure.
- Backfill excavation within Track 4 Lead Hotspot following placement of detention tank.

# DAILY STATUS REPORT

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-65°F, partly sunny RH: 63%, P: 30.33" of Hg Wind: NE @ 12 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:55 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 30, 2022

## Site Layout

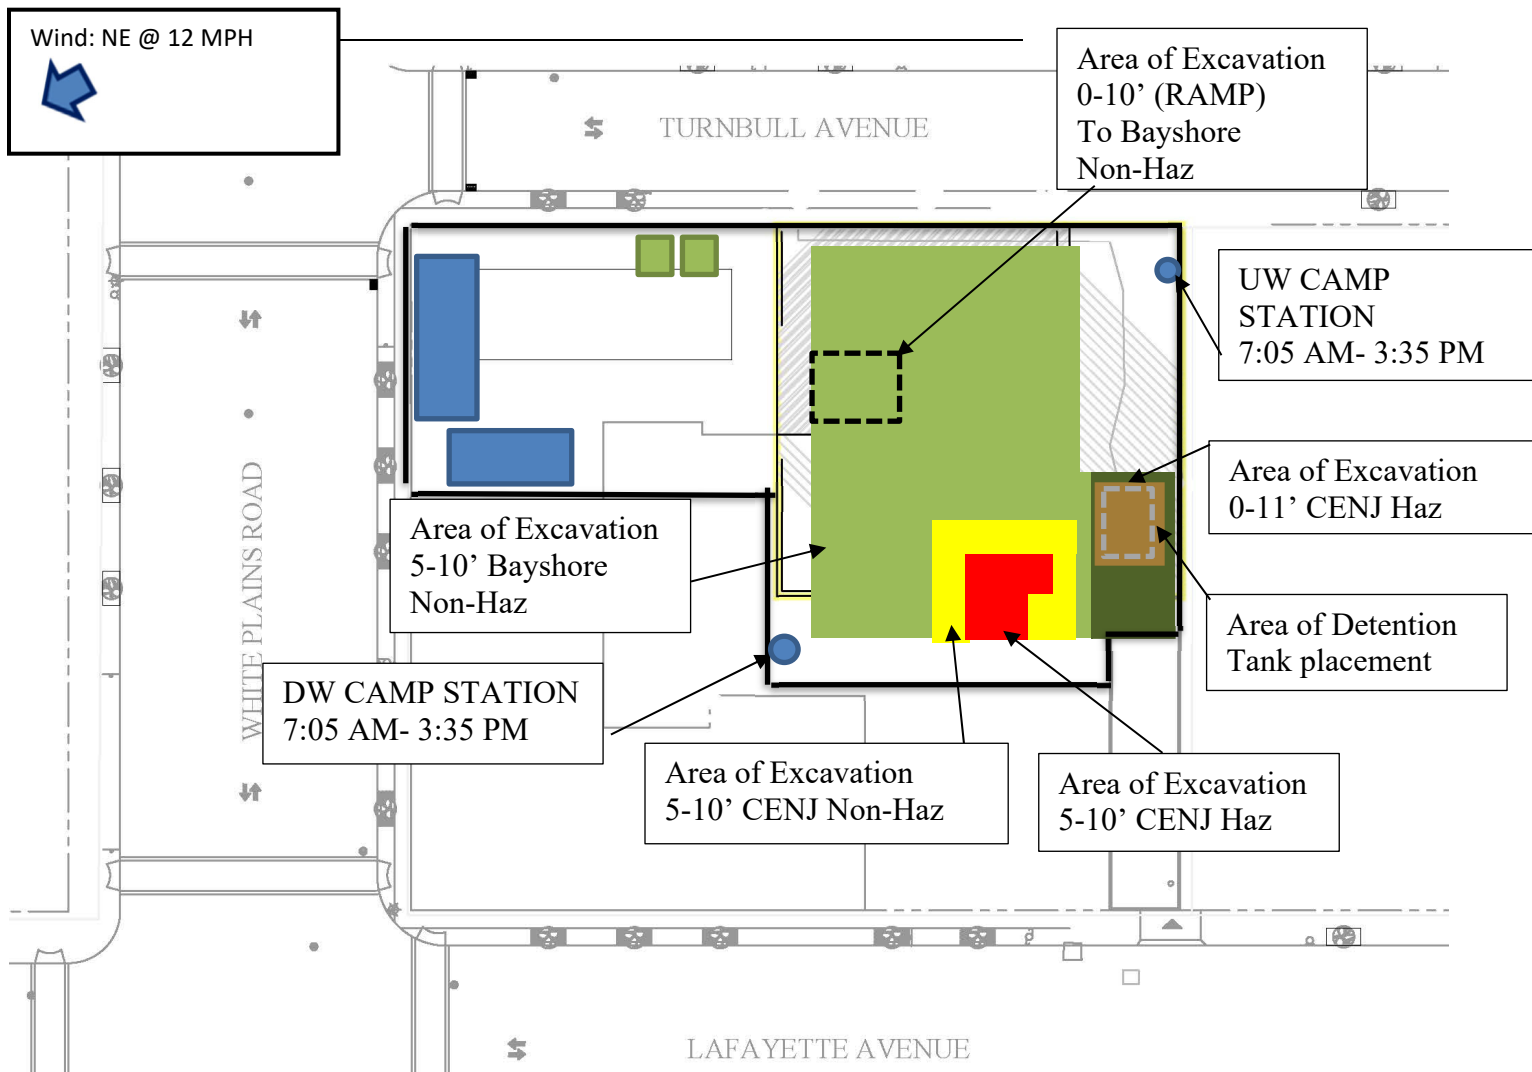

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-65°F, partly sunny RH: 63%, P: 30.33" of Hg Wind: NE @ 12 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:55 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 30, 2022

**PHOTOGRAPHS TAKEN TODAY:**



**Photo 1:**  
Facing north, view of well drilling in the southwest corner of the building footprint.



**Photo 2:**  
Facing north, steel rods being inserted in to casing in the central east region of the building footprint.

<b>PROJECT:</b> <b>BCP SITE No.</b>	Park Lane Senior C203138	<b>WEATHER:</b>	56-65°F, partly sunny RH: 63%, P: 30.33" of Hg Wind: NE @ 12 mph
<b>LOCATION:</b>	1940 Turnbull Ave, Bronx, NY (Site)	<b>TIME:</b>	6:50 AM – 3:55 PM
<b>PREPARED BY:</b>	TJ Jennings	<b>DATE:</b>	September 30, 2022



**Photo 3:**  
Facing west, general site conditions at the end of the day.
