

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/04/2022

Weather: 55 deg F., Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: EDC NY

Work Activities Performed:

- 1) ECD staging materials in preparation for the future bulkhead revision;
- 2) Complete construction walkway on Kent Avenue, and;
- 3) Continue to locate suspected underground storage tanks (USTs) location.

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to rain.

Problems Encountered: None.

Planned Work Activities for Next Day/Week: Locating the suspected UST for subsequent cleaning and removal.

Site Layout Map

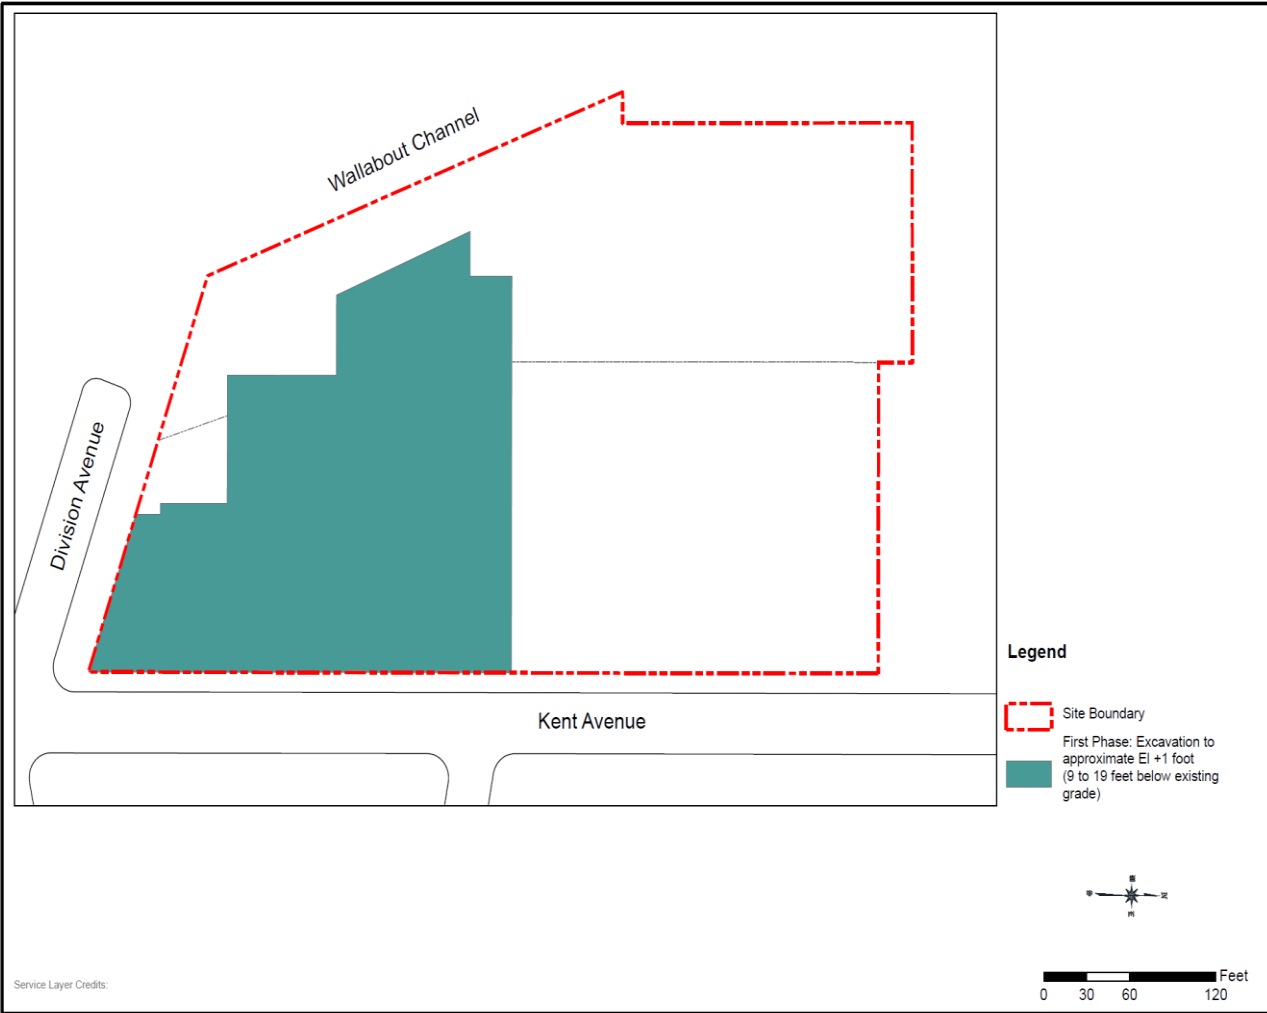


Photo 1:

Forming the construction walkway along Kent Avenue.



Photo 2:

Scratching away the surface to find the exact location of the suspected UST. Soil was backfilled immediately upon completion.



CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP:
Upwind
Particulates

NA
