

## Daily Status Report

Prepared by: C. Zaccheo

Date: 05/06/2022

Weather: 65 deg F., Rain

**Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053**

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: EDC NY

### Work Activities Performed:

- 1) Minor excavation to access USTs for cleaning in preparation for removal;
- 2) Install composite sock along the UST pit perimeter;
- 3) Uncover second UST and pump out water and contents; and,
- 4) Cover excavated RCA location with poly sheeting.


**Samples Collected (Since Last Report):** None.

**Air Monitoring (Since Last Report):** CAMP stations were not set up due to rain.

**Problems Encountered:** None.

**Planned Work Activities for Next Day/Week:** Locating the second suspected UST for subsequent cleaning and removal; Restoration of the turbidity curtain located in the water.

Site Layout Map

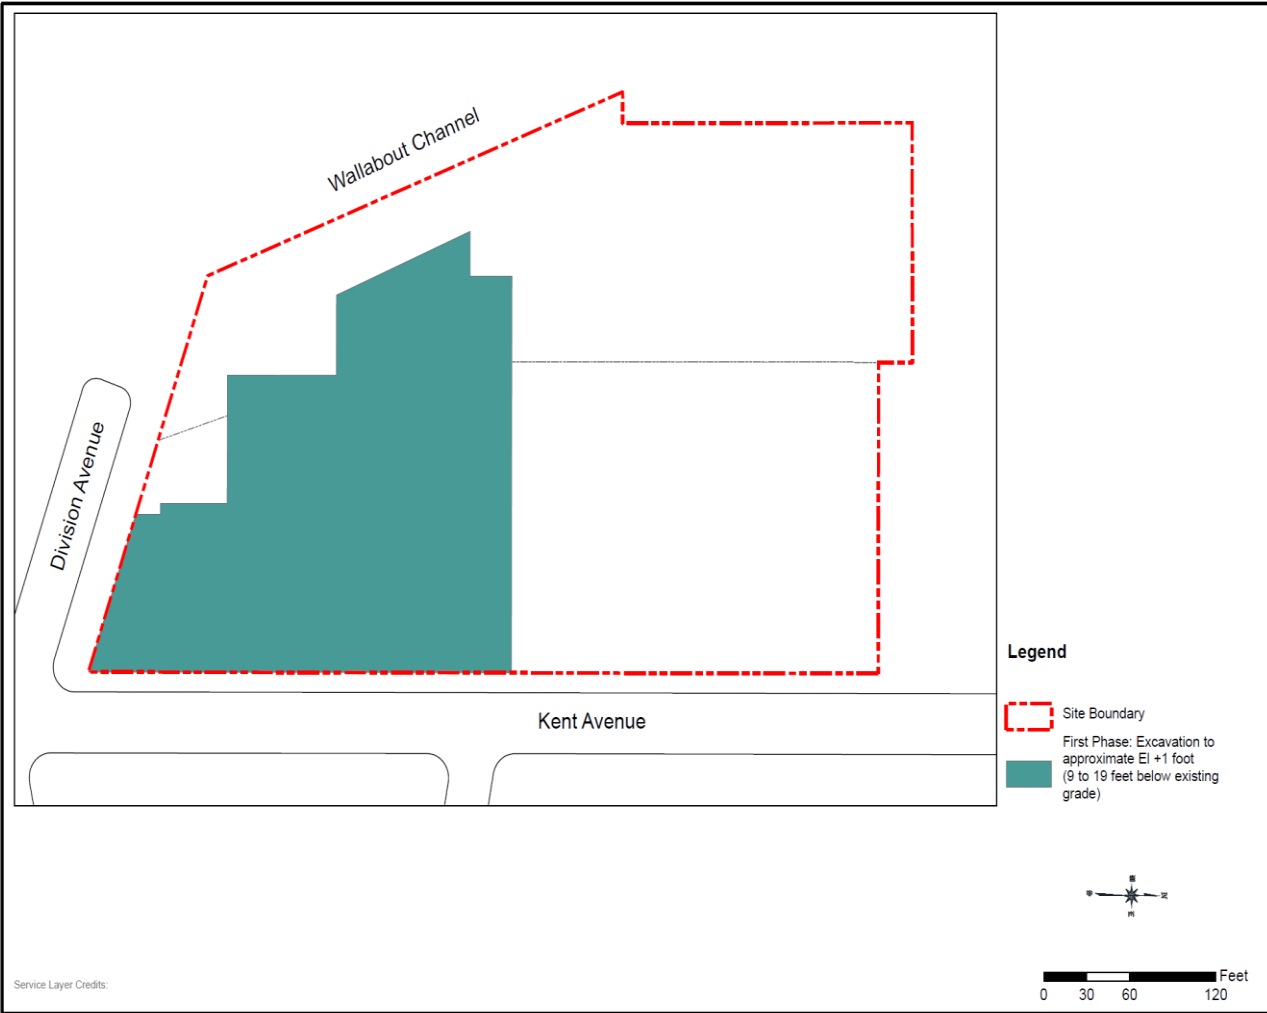


**Photo 1:**

Pumping out tank of contents in preparation for removal.



**Photo 2:**

Site conditions facing west during tank cleaning.

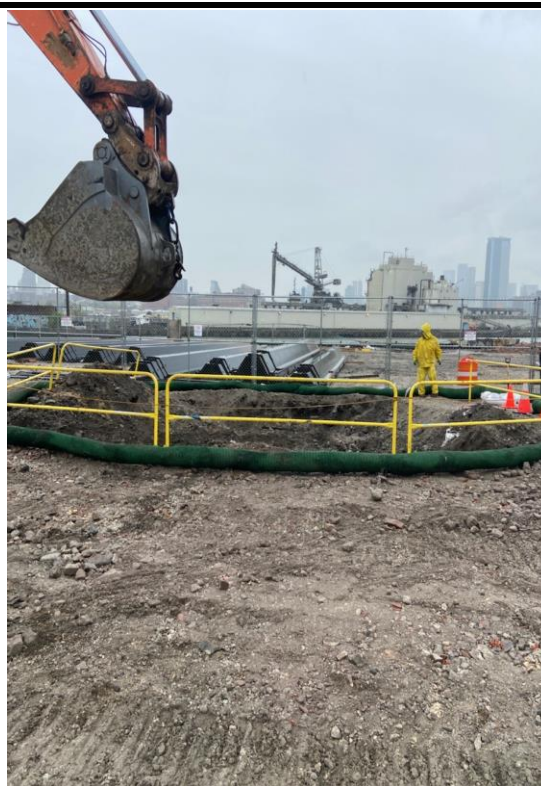

<b>CAMP: Downwind Particulates</b>	<b>NA</b>
<b>CAMP: Downwind VOCs</b>	<b>NA</b>

<b>CAMP: Upwind Particulates</b>	<b>NA</b>
--	-----------
