



INSPECTION/FIELD ACTIVITY REPORT

BCP Site No.:	C224148	AUTHOR:	Wynne Casteel
PROJECT NO.:	3165.0006R000	DATE:	09/06/2022
PROJECT:	Sunset Industrial Park 74 20th St., Brooklyn, NY	WEATHER:	Rain, 68-74°F, Wind: SSE @ 9 mph Humidity: 91%, Pressure: 30.00" Hg
CLIENT:	SIP Holdings Venture, LLC	TIME:	07:00 AM – 1:30 PM

CONTRACTOR AND EQUIPMENT:	PERSONNEL PRESENT AT SITE AND AFFILIATION:
<u>Kingdom – Excavation/Foundation Contractor</u> <ul style="list-style-type: none"> • Komatsu PC 350 LC Hydraulic Excavator • Komatsu PC 228US LC Hydraulic Excavator • Komatsu PC 50 MR Hydraulic Mini Excavator • Benford PT9100 Site Dumper • Komatsu WA380-5 Wheel Loader • Dynapac CA1300 Roller 	<u>Roux Environmental Engineering & Geology, D.P.C</u> Wynne Casteel, Staff Geologist <u>Kingdom</u> David Szmuc, Assistant Project Manager <u>Suffolk</u> Cal Ho, Project Manager

GENERAL COMMENTS:

As part of the of the NYSDEC-approved Remedial Action Work Plan, Roux Environmental Engineering and Geology D.P.C. (Roux) performed environmental oversight and operated air monitoring equipment in compliance with the Community Air Monitoring Plan (CAMP) during foundation installation activities.

RAWP Activities Performed:

- Kingdom continued rebar installation within cells B1, B2, and B3
- Stockpile management was observed moving the current stockpiles into grid cells A2 and A4

CAMP Performed:

- CAMP was not performed due to continuous rain. Conditions were damp and no fugitive dust was observed traveling offsite.

Other Relevant Comments or Issues:

- Two truck-mounted concrete pumps arrived onsite in preparation for concrete pour scheduled for 9/7/2022.

Upcoming work activities:

- Installation of SOE and deeper foundation elements (footings, piers, pile caps, etc.) expected to continue throughout the site area through October 2022. Localized excavation will occur, as necessary.
- Roux will continue oversight, performance of CAMP during intrusive construction activities and collecting soil documentation end point samples as required by the RAWP.
- Kingdom to perform concrete pour scheduled for tomorrow, 9/7 in grids B1, B2, and B3.
- Stockpile movement expected to continue into cell A4.

Submitted By: Wynne Casteel of Roux Environmental Engineering and Geology, D.P.C.	Approved By: Levi Curnutte of Roux Environmental Engineering and Geology, D.P.C.
--	---

BCP Site No.:	C224148	AUTHOR:	Wynne Casteel
PROJECT NO.:	3165.0006R000	DATE:	09/06/2022
PROJECT:	Sunset Industrial Park 74 20 th St., Brooklyn, NY	WEATHER:	Rain, 68-74°F, Wind: SSE @ 9 mph Humidity: 91%, Pressure: 30.00" Hg
CLIENT:	SIP Holdings Venture, LLC	TIME:	07:00 AM – 1:30 PM

PHOTOS:**Photo 1:**

Looking west: Kingdom continuing rebar installation in grids B1, B2, and B3.

**Photo 2 :**

Looking southeast: Representative photo of damp conditions onsite.

Submitted By: Wynne Casteel of
Roux Environmental Engineering and Geology, D.P.C.

Approved By: Levi Curnutte of
Roux Environmental Engineering and Geology, D.P.C.

BCP Site No.:	C224148	AUTHOR:	Wynne Casteel
PROJECT NO.:	3165.0006R000	DATE:	09/06/2022
PROJECT:	Sunset Industrial Park 74 20 th St., Brooklyn, NY	WEATHER:	Rain, 68-74°F, Wind: SSE @ 9 mph Humidity: 91%, Pressure: 30.00" Hg
CLIENT:	SIP Holdings Venture, LLC	TIME:	07:00 AM – 1:30 PM

**Photo 3:**

Looking east: Kingdom completed rebar installation in cells B1, B2, and B3.


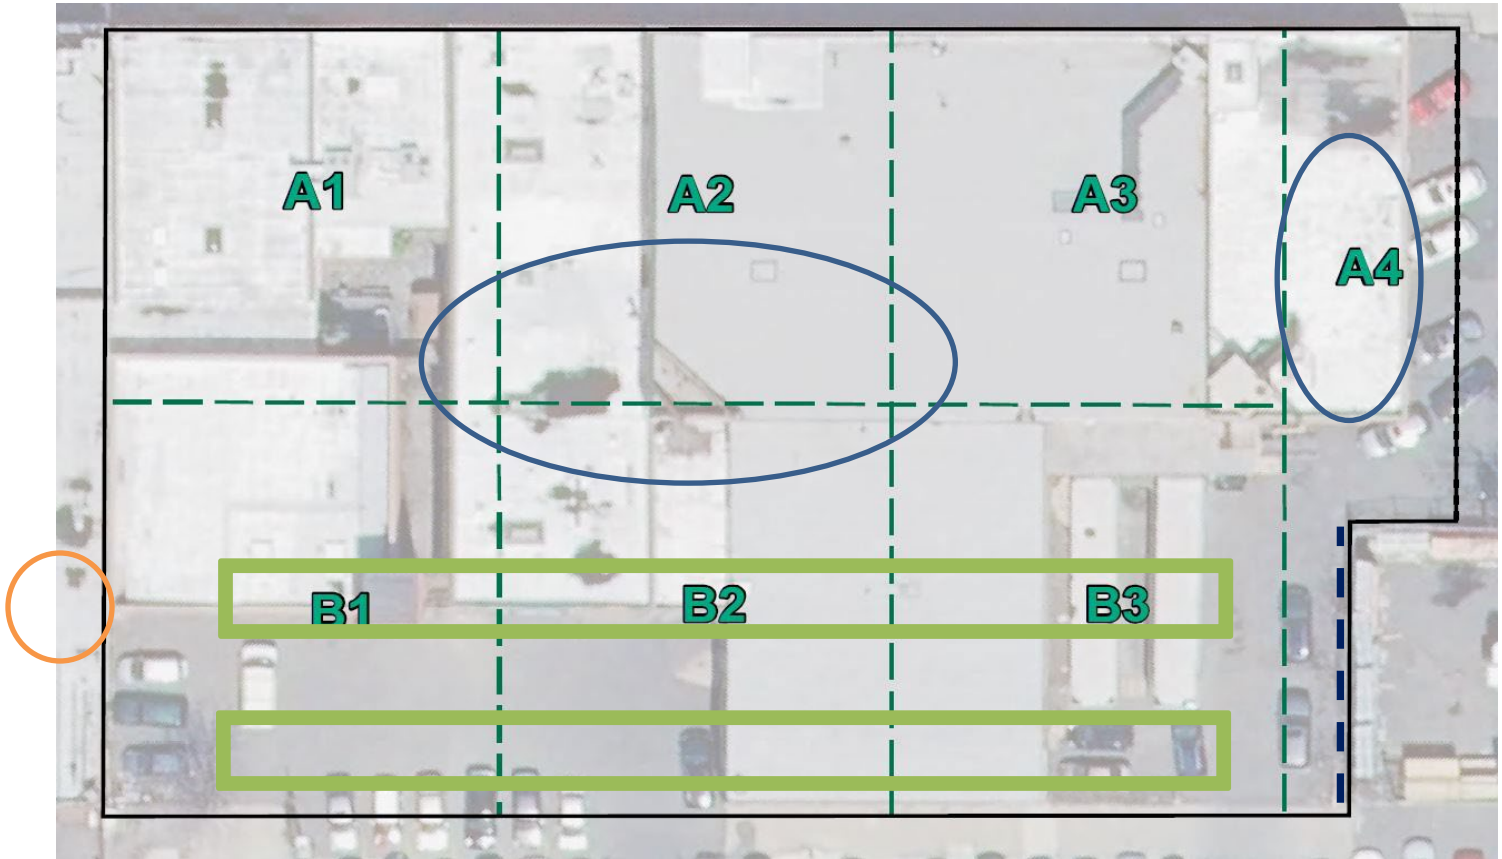
**Photo 4:**




Looking south: Truck-mounted concrete pump is staged on site in cell B1 for tomorrow's concrete pour.

Submitted By: Wynne Casteel of
Roux Environmental Engineering and Geology, D.P.C.

Approved By: Levi Curnutte of
Roux Environmental Engineering and Geology, D.P.C.

Site Map



-  Current area of localized excavation for foundation installation
-  Soil Stockpile
-  Concrete Stockpile

Submitted By: Wynne Casteel of Roux Environmental Engineering and Geology, D.P.C.	Approved By: Levi Curnutte of Roux Environmental Engineering and Geology, D.P.C.
--	---
