

1665 STILLWELL AVENUE

Project: Brownfield Site C224307

Date: Friday, May 27, 2022

Weather: Sunny, 70's

Work Performed:

8:00 RSK Environmental onsite. Set up CAMP (two stations), Decon area with drums for wash water and waste, and set up at GW-2.
9:00 Purge GW-2. Decon equipment. Set up at GW-5.
9:15 Purge GW-5. Decon equipment. Set up at GW-3.
9:25 Purge GW-3. Decon equipment. Set up at GW-4.
9:35 Purge GW-4. Decon equipment. Set up at GW-6.
9:45 Purge GW-6. Decon equipment. Set up at GW-1.
9:55 Purge GW-1. Decon equipment.
10:00 - 12:30 Additional RSK field techs onsite to install caps and concrete. Clean up from purging operations.
12:30 Lunch. Phoenix Labs onsite to pick up soil samples.
1:00 Resume installation of well caps and concrete.
1:45 Clean up. All waste stored in drums to be left onsite until sampling results obtained.
2:15 End of Day.

Photographs:

1 - 2 - CAMP locations upwind and downwind.
3 - 4 - Decon and Drum storage areas.
5 - At GW-2
6 - Decon after each purge (typical).
7 - At GW-5
8 - At GW-3
9 - At GW-4
10 - At GW-6
11 - At GW-1
12 - Installing flush mounted well cap and concrete (typical)
13 - 15 - End of Day

Anticipated Schedule:

Monday - May 30th - Holiday, no work.

Tuesday - May 31st - Perform soil gas sampling and groundwater sampling.

Ted Yen, P.E.



**PHOTOS OF 1665
STILLWELL AVE, N.Y.
TAKEN FRIDAY
5/27/2022**





1

2








5



6



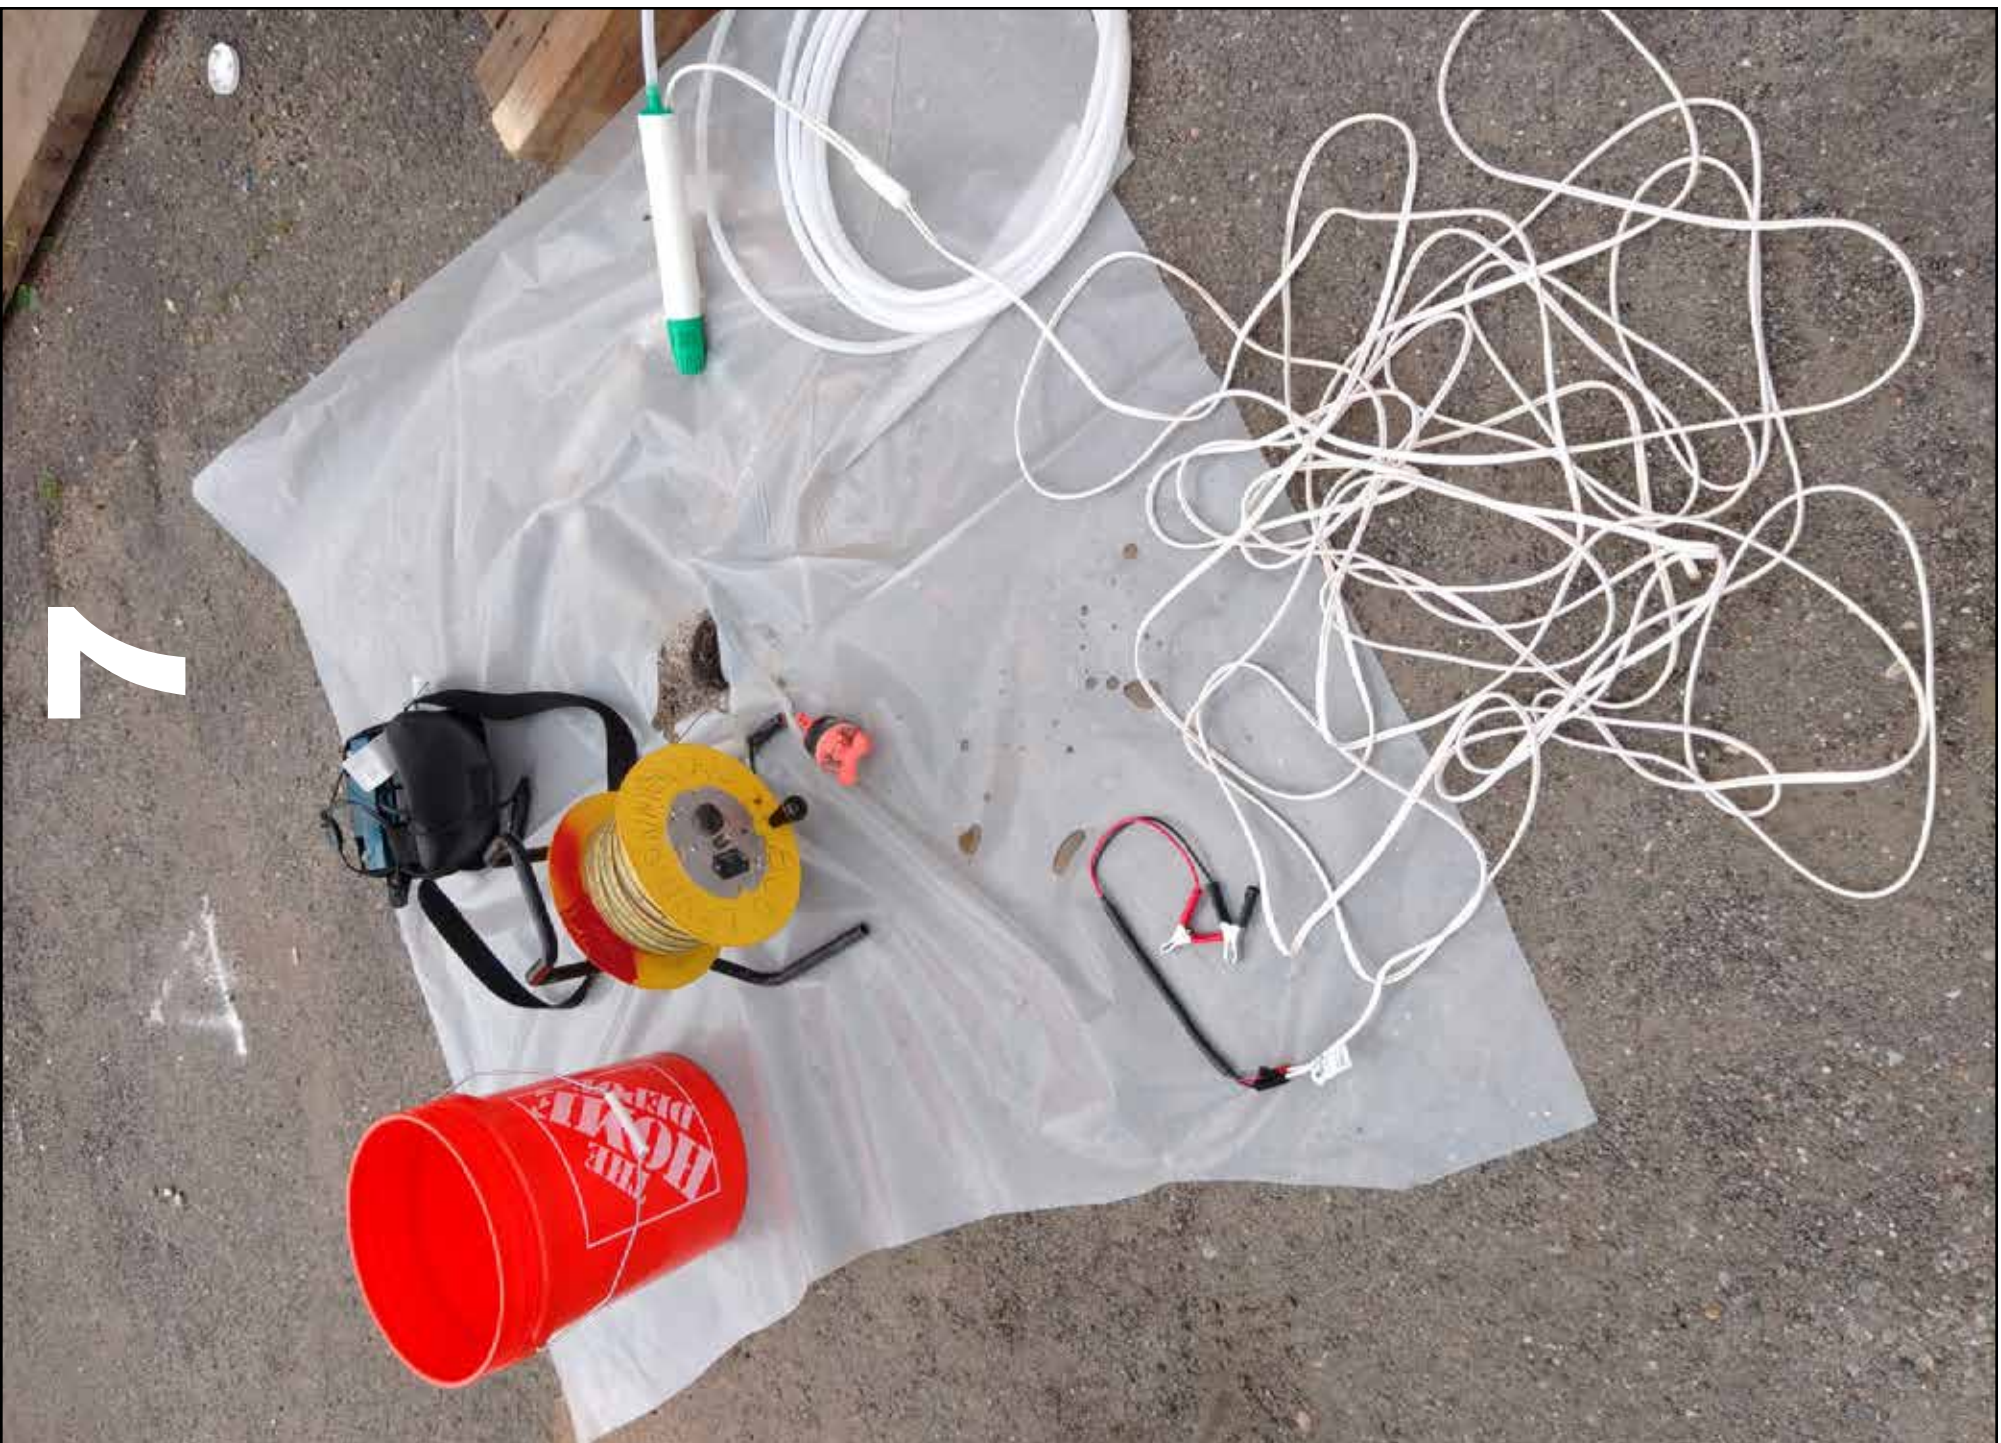

7





6







13



14





15
