

WEEKLY INSPECTION REPORT

Prepared By:	WEATHER	Snow	Rain		Overcast		Partly Cloudy	х	Bright Sun	х	Wind
Thomas Jensen	TEMP.	< 32	32-50	X	50-70	X	70-85		>85		5 – SW mph

IEC Project No:	14729	NYSDEC BCP Site No:	C224329	Date:	11/2/23
Project:	585 Union Street, Brooklyn, NY				

Consultant:	Personnel On Site:
Impact Environmental Engineering and	IEEG (Environmental) – Thomas Jensen
Geology, PLLC (IEEG)	Broadway Construction Group, Shannon Dowling
Time On: 7:30	
Time Out: 7:45	

Scope of Work:

• Weekly site inspection.

Site Activities:

- Interior framing up to the 7th floor;
- Electrical and Plumbing work up to the 7th floor;
- Exterior framing; and
- General super structure work.

Community Air Monitoring Program (CAMP):

• CAMP was not deployed as the purpose of the Site visit was for a weekly inspection.

Notable Site Conditions:

 A partial stop work order was issued due to a fall from a ladder, most trades are not on site, work will resume next week.

Planned for the Next Day/Week:

• Continued Superstructure work.

Photo 1 –
Representative
photo of the
building
exterior.



Photo 2 –
Representative
photo of
building interior
at the 2nd floor.

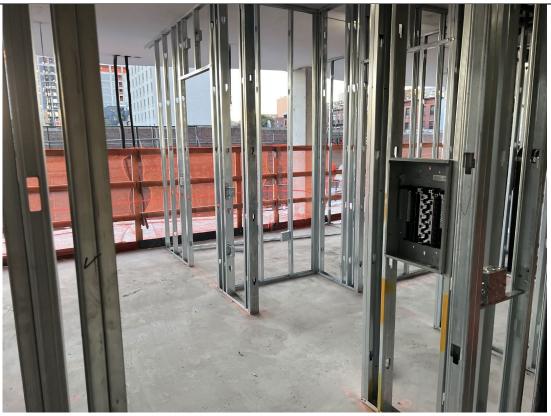


Photo 3 – Representative photo of the first floor.

