



Daily Report for March 3, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, D1- D4, E2- E4, and F2- F4.
- SOE installation in E5 and E6.
- Graded soil in D5 and E5.
- Poured concrete in A1-A4, and B1-B4.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B first through third floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating soil for Building H.

Photo Log

Photo 1- View of rebar installation and formwork in grid D1.



Photo 2- View of grading soil in D5 and E5.



Photo 3- View of rebar, formwork installation, and pouring concrete in A3, A4, B3, and B4.





Daily Report for March 4, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in D5 and E5.

2. Locations of work and quantities of material imported and exported from the Site.

- Exported 2 loads of concrete and debris to the Mount Materials LLC facility in Fairless Hills, PA.

-No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of formwork in grid C5 and D5.



Photo 2- View of formwork and rebar installation in A3, A4, B3, and B4.



Photo 3- View
of rebar
installation and
formwork in
grid D1.





Daily Report for March 5, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in D5 and E5.
- Installed waterproofing membrane Preprufe 200 in C5, C6, D5, and D6.
- Collected Endpoint samples EP-75 through EP-81.

2. Locations of work and quantities of material imported and exported from the Site.

- 8 loads of non-hazardous soil were exported from the Site today to Clean Earth of Bethlehem in Bethlehem, PA from grids C8 (0-7) and D8 (0-7).
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of installation of Preprufe 200 in grids C5, C6, D5, and D6.



Photo 2- View of loading out of soil in grid C8.



Photo 3- View
of rebar
installation and
formwork in
grid D1.





Daily Report for March 6, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in D5 and E5.
- Backfilled soil in D5- D8 and E5- E8.

2. Locations of work and quantities of material imported and exported from the Site.

- 5 loads of non-hazardous soil were exported from the Site today to Clean Earth of Bethlehem in Bethlehem, PA from grids C8 (0-7) and D8 (0-7).
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of loading out of soil in grid C8.



Photo 3- View
of rebar
installation and
formwork in
grid D1.





Daily Report for March 9, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in D5 and E5.

2. Locations of work and quantities of material imported and exported from the Site.

- 10 loads of non-hazardous soil were exported from the Site today to Clean Earth of Bethlehem in Bethlehem, PA from grids C8 (0-7) and D8 (0-7).
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of loading out of soil in grid C8.



Photo 3- View
of rebar
installation and
formwork in
grid D1.





Daily Report for March 10, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in D6 and D7.
- Poured concrete for Building C.
- Spread stone in D1.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of grading soil in D6 and D7.



Photo 3- View
of spreading
stone in grid
D1.





Daily Report for March 11, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C6 and C7.
- Installed waterproofing membrane Preprufe 200 in C5, C6, D5, and D6.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log


Photo 1- View of Preprufe 200 and rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of grading soil in C6 and C7.



Photo 3- View
of installed
Preprufe 200
and rebar.

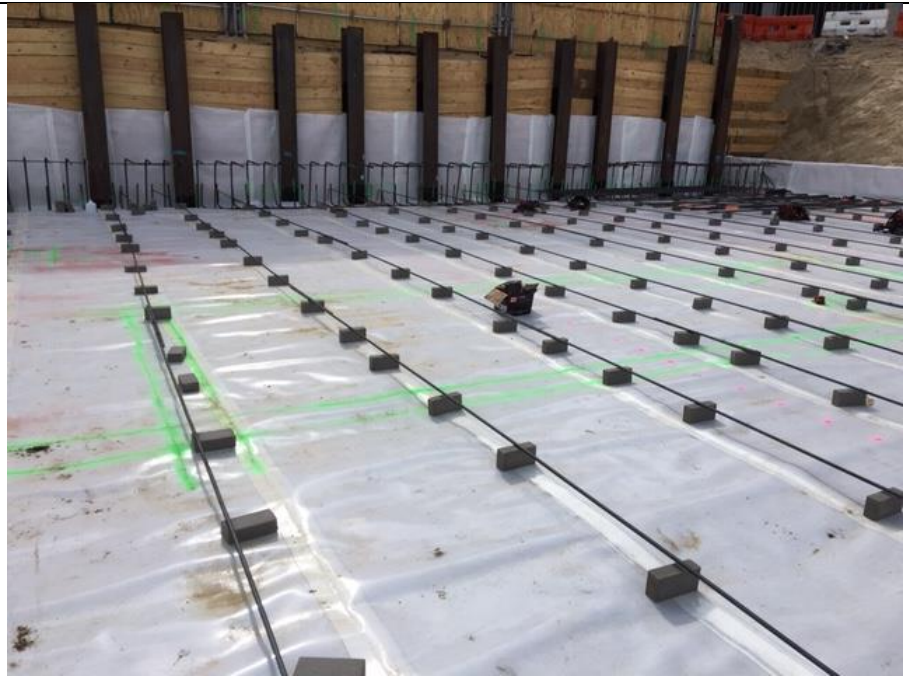



Daily Report for March 12, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C6 and C7.
- Installed waterproofing membrane Preprufe 200 in C5, C6, D5, and D6.
- Laid stone in D1.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of Preprufe 200 and rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of graded soil in C6 and C7.



Photo 3- View
of laid stone in
grid D1.





Daily Report for March 16, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Installed waterproofing membrane Preprufe 200 in D1, C5, C6, D5, and D6.
- Backfilling soil in C6 and C7.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of Preprufe 200, formwork, and rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of backfilling soil in C6.



Photo 3- View
of installed
Preprufe 200 in
grid D1.





Daily Report for March 17, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Installed waterproofing membrane Preprufe 200 in D1, C5, C6, D5, and D6.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of Preprufe 200, formwork, and rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of formwork in A3, A4, B3, and B4.



Photo 3- View
of installed
Preprufe 200
and rebar in
grid D1.





Daily Report for March 18, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Installed waterproofing membrane Preprufe 200 in D1, C5, C6, D5, and D6.
- Poured concrete in D1.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of Preprufe 200, formwork, and rebar installation in grids C5, C6, D5, and D6.

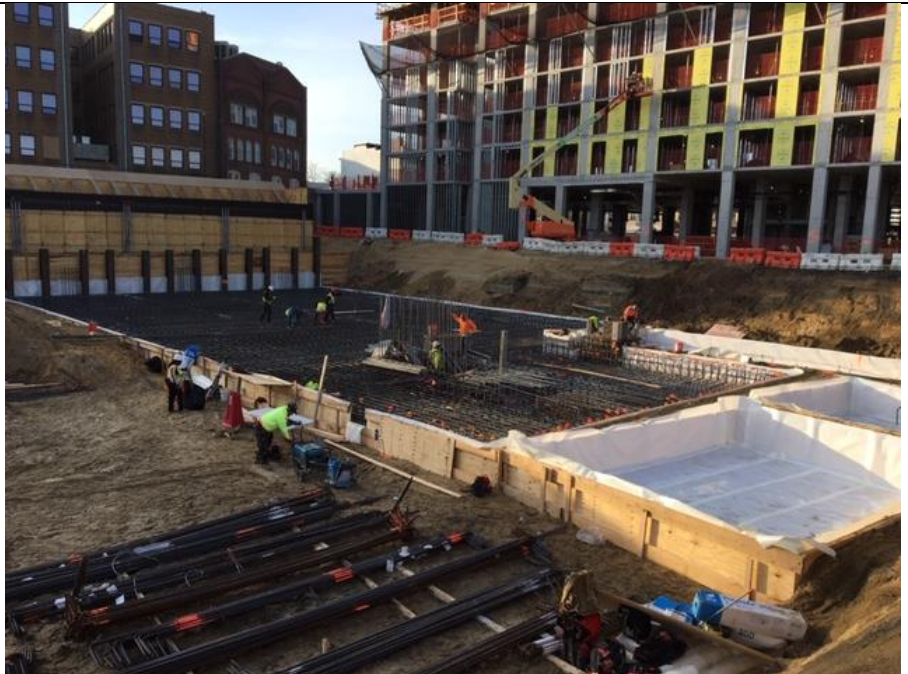


Photo 2- View of formwork in A3, A4, B3, and B4.



Photo 3- View of rebar and formwork installation in D4, D5, E4, and E5.





Daily Report for March 19, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Installed rebar and formwork in D1.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of Preprufe 200, formwork, and rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of formwork and rebar installation in D1.



Photo 3- View of rebar and formwork installation in D4, D5, E4, and E5.





Daily Report for March 20, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Installed rebar and formwork in D1.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of formwork and rebar installation in D1.

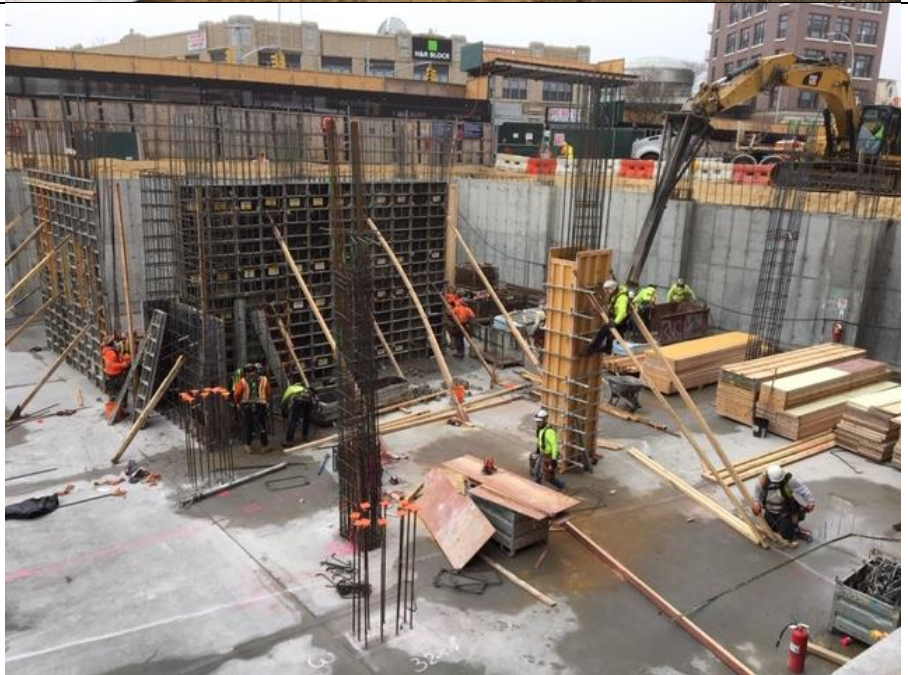


Photo 3- View of rebar and formwork installation in A3, A4, B3, and B4.





Daily Report for March 23, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C7 and C8.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of formwork and rebar installation in D3, D4, E3, and E4.



Photo 3- View of rebar and formwork installation in A3, A4, B3, and B4.





Daily Report for March 24, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C7 and C8.
- Excavated soil for utilities in C5.
- Poured concrete in D2-D4, and E2-E4.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of pouring concrete in D3, D4, E3, and E4.



Photo 3- View
of excavating
soil for utilities
in grid C5.





Daily Report for March 25, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C6 and C7.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B fourth through sixth floors.
- Continue formwork and rebar installation for Building C first floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of installing rebar and formwork in D3, D4, E3, and E4.



Photo 3- View of installing rebar and formwork in A3, A4, B3, and B4.





Daily Report for March 26, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C6 and C7.
- Backfilling soil in C5 and C6.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B sixth through eighth floors.
- Continue formwork and rebar installation for Building C second floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of formwork and rebar installation in grids C5, C6, D5, and D6.



Photo 2- View of grading soil in C6.



Photo 3- View of installing rebar and formwork in A3, A4, B3, and B4.





Daily Report for March 27, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C6, C7, and C8.
- Backfilled soil in C5 and C6.
- Installed waterproofing membrane Preprufe 200 in C6 and C7.
- Utility installation in C5.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B sixth through eighth floors.
- Continue formwork and rebar installation for Building C second floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of waterproofing installation in C6.



Photo 2- View of formwork and grading soil in C7 and C8.



Photo 3- View
of backfilling in
C6.





Daily Report for March 31, 2020

**Far Rockaway Project
20-02 Mott Avenue
Far Rockaway, NY
BCP #C241224**

1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.

- Formwork and rebar installation in A1- A4, B1- B4, C5, C6, D1- D6, E2- E4, and F2- F4.
- Graded soil in C6, C7, and C8.
- Backfilled soil in C6, C7, C8, D7, and D8.
- Installed waterproofing membrane Preprufe 200 in C6, C7, C8, D7, and D8.
- Utility installation in C5 and C6.

2. Locations of work and quantities of material imported and exported from the Site.

- No materials were exported from the site today.
- No materials were imported to the site today.

3. A summary of any and all complaints with relevant details (names, phone numbers).

- No complaints.

4. A summary of CAMP findings (air and dust readings).

- No elevated PID or dust readings were identified.

5. An explanation of notable Site conditions.

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

6. Planned Activities

- Continue formwork and rebar installation for Building B sixth through eighth floors.
- Continue formwork and rebar installation for Building C second floor.
- Continue excavating and installing formwork for footings in Building H.

Photo Log

Photo 1- View of rebar and waterproofing installation in C6-C8, D7, and D8.



Photo 2- View of utility installation in C5 and C6.



Photo 3- View
of formwork
and rebar
installation in
D1.

