



## **Daily Report for December 1, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B4, C5-C8, D1- D7, E2- E4, and F2-F4.
- Backfilling, compacting, and grading clean fill in B5 and C5.
- Excavated clean fill in C5 for utility installation.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- 10 loads (~250 tons) of approved clean fill were imported to the site today from the P Park facility in Prospect Park, NJ.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View of backfilling and compacting clean fill in B5 and C5.



Photo 2- View of backfilling and compacting clean fill in B5 and C5.



Photo 3- View  
of utility  
installation in  
C5.





## **Daily Report for December 2, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B4, C5-C8, D1- D7, E2- E4, and F2-F4.
- Backfilling, compacting, and grading clean fill in B5 and C5.
- Excavated clean fill in C5 for utility installation.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- 20 loads (~500 tons) of approved clean fill were imported to the site today from the P Park facility in Prospect Park, NJ.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of backfilling and compacting clean fill in B5.



Photo 2- View of backfilling and compacting clean fill in B5 and C5.



Photo 3- View of utility and formwork installation in A3, A4, B3, and B4.





## **Daily Report for December 3, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B4, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in C4, D4, and E4 for utility installation.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of excavating clean fill and utility installation in C4 and D4.



Photo 2- View of excavating clean fill and utility installation in D4 and E4.



Photo 3- View of utility and formwork installation in A3, A4, B3, and B4.







## **Daily Report for December 4, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B4, C5-C8, D1- D7, E2- E4, and F2-F4.
- Backfilled with clean fill in C4, D4, and E4.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- 10 loads (~250 tons) of approved clean fill were imported to the site today from the P Park facility in Prospect Park, NJ.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View of backfilled area in C4 and D4.



Photo 2- View of utility and formwork installation in D4, D5, E4, and E5.



Photo 3- View of utility and formwork installation in A3, A4, B3, and B4.





## **Daily Report for December 7, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated and backfilled clean fill in B5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- 2 loads of concrete and debris were exported from the site today to Russo Recycling in Rosedale, NY.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of excavated clean fill and utility installation in B5.



Photo 2- View of loading out of concrete and debris for export offsite.





Photo 3- View of utility and formwork installation in A3, A4, B3, and B4.





## **Daily Report for December 8, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated and backfilled clean fill in B4 and B5.
- Broke up concrete in D5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- 1 load of concrete and debris was exported from the site today to Russo Recycling in Rosedale, NY.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View of excavated clean fill and utility installation in B4 and B5.



Photo 2- View of excavated clean fill and utility installation in B4 and B5.



Photo 3- View  
of breaking up  
concrete in D5.







## **Daily Report for December 9, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Graded clean fill in C6 and C7.
- Broke up concrete in D5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View  
of grading  
clean fill in C6.



Photo 2- View  
of breaking up  
and stockpiling  
concrete in D5.



Photo 3- View of utility and formwork installation in C6-C8.





## **Daily Report for December 10, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in B5, D5, E5, and F5 for utility installation.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of excavating clean fill and installing utilities in D5 and E5.



Photo 2- View of excavating clean fill in C5 for utility installation.



Photo 3- View  
of utility B5.







## **Daily Report for December 11, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in B5, D5, E5, and F5 for utility installation.
- Backfilling clean fill in C5, D5, and E5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View of excavating clean fill and installing utilities in D5 and E5.



Photo 2- View of backfilling clean fill in C5 for utility installation.



Photo 3- View of utility and formwork installation in A3, A4, B3, and B4.





## **Daily Report for December 14, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in C5 and D5 for utility installation.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of excavating clean fill and installing utilities in D5 and C5.



Photo 2- View of utility and formwork installation in C6-C8.



Photo 3- View of utility and formwork installation in A3, A4, B3, and B4.





## **Daily Report for December 15, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in C5 and D5 for utility installation.
- Installed utilities in C5 and D5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of clean fill excavation and utilities installation in D5 and C5.



Photo 2- View of utility installation in C5 and D5.





Photo 3- View of utility and formwork installation in D4, D5, E4, and E5.





## **Daily Report for December 16, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in B5 and C5 for utility installation.
- Installed utilities in B5 and C5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View of clean fill excavation and utilities installation in B5 and C5.



Photo 2- View of utility installation in B5 and C5.



Photo 3- View  
of utility and  
formwork  
installation in  
C6-C8.







## **Daily Report for December 17, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

**1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

-General construction activities.

**2. Locations of work and quantities of material imported and exported from the Site.**

-No material was exported from the site today.

-No material was imported to the site today.

**3. A summary of any and all complaints with relevant details (names, phone numbers).**

-No complaints.

**4. A summary of CAMP findings (air and dust readings).**

-No elevated PID or dust readings were identified.

**5. An explanation of notable Site conditions.**

-Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

**6. Planned Activities**

-Continue formwork and rebar installation for Building B.

-Continue formwork and rebar installation for Building C.

-Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View  
of A3, A4, B3,  
and B4.





## **Daily Report for December 18, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in B5 and C5 for utility installation.
- Installed utilities in B5 and C5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View of clean fill excavation and utilities installation in B5 and C5.



Photo 2- View of utility and formwork installation in A3, A4, B3, and B4.





Photo 3- View  
of utility and  
formwork  
installation in  
C6-C8.





## **Daily Report for December 21, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

**1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

-General construction activities site wide.

**2. Locations of work and quantities of material imported and exported from the Site.**

-No material was exported from the site today.

-No material was imported to the site today.

**3. A summary of any and all complaints with relevant details (names, phone numbers).**

-No complaints.

**4. A summary of CAMP findings (air and dust readings).**

-No elevated PID or dust readings were identified.

**5. An explanation of notable Site conditions.**

-Today's work was overseen by Thomas Brown of CA RICH. No conditions of note were observed.

**6. Planned Activities**

-Continue formwork and rebar installation for Building B.

-Continue formwork and rebar installation for Building C.

-Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1-  
View of  
clean fill  
excavati  
on and  
utilities  
installati  
on A5  
and B5.





Photo 2-  
View of  
Building  
B grids  
C4 and  
D4.





Photo 3-  
View of  
Building  
H grids  
C5, C6,  
and C7.





## **Daily Report for December 22, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in B5 and C5 for utility installation.
- Installed utilities in B5 and C5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of clean fill excavation and utilities installation in B5 and C5.



Photo 2- View of utility installation in B5.



Photo 3- View  
of utility  
installation in  
C8.







## **Daily Report for December 23, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.
- Excavated clean fill in B1, B2, B5 and C5 for utility installation.
- Laid gravel down in B1 and B2.
- Installed utilities in B1, B2, B5 and C5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View of clean fill excavation and utilities installation in B5 and C5.



Photo 2- View of utility installation in B1 and B2.



Photo 3- View  
of installed  
utility in C8.





## **Daily Report for December 24, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2- F4.
- Excavated clean fill in C5 and D5 for utility installation.
- Installed utilities in C5 and D5.

### **2. Locations of work and quantities of material imported and exported from the Site.**

- No material was exported from the site today.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by David Klein of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View of clean fill excavation and utilities installation in C5 and D5.



Photo 2- View of formwork and utility installation in A3, A4, B3, and B4.



Photo 3- View of formwork and utility installation in C6 through C8.





## **Daily Report for December 28, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

### **1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

- Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2- F4.
- Excavated clean fill in B1 to B4 for utility installation.
- Installed utilities in B1 to B4.
- Collected three endpoints, EP-92 (7ft); EP-93(7ft); and EP-94(7ft)

### **2. Locations of work and quantities of material imported and exported from the Site.**

- 19 loads of contaminated material was exported from the site today to Posillico.
- No material was imported to the site today.

### **3. A summary of any and all complaints with relevant details (names, phone numbers).**

- No complaints.

### **4. A summary of CAMP findings (air and dust readings).**

- No elevated PID or dust readings were identified.

### **5. An explanation of notable Site conditions.**

- Today's work was overseen by Thomas Brown of CA RICH. No conditions of note were observed.

### **6. Planned Activities**

- Continue formwork and rebar installation for Building B.
- Continue formwork and rebar installation for Building C.
- Continue formwork and rebar installation for Building H.



## **Photo Log**

Photo 1- View of clean fill excavation and utilities installation in B1 and B4.





Photo 2- View of formwork and utility installation at Building B in C3, C4, and D4.



Photo 3- View of excavation and soil export from C6, C7, and C8.





## **Daily Report for December 29, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

**1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

-Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2-F4.

**2. Locations of work and quantities of material imported and exported from the Site.**

-6 loads of contaminated material was exported from the site today to Posillico.

-7 loads of concrete was removed from the site today.

-No material was imported to the site today.

**3. A summary of any and all complaints with relevant details (names, phone numbers).**

-No complaints.

**4. A summary of CAMP findings (air and dust readings).**

-No elevated PID or dust readings were identified.

**5. An explanation of notable Site conditions.**

-Today's work was overseen by Thomas Brown of CA RICH. No conditions of note were observed.

**6. Planned Activities**

-Continue formwork and rebar installation for Building B.

-Continue formwork and rebar installation for Building C.

-Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View  
of concrete  
removal.

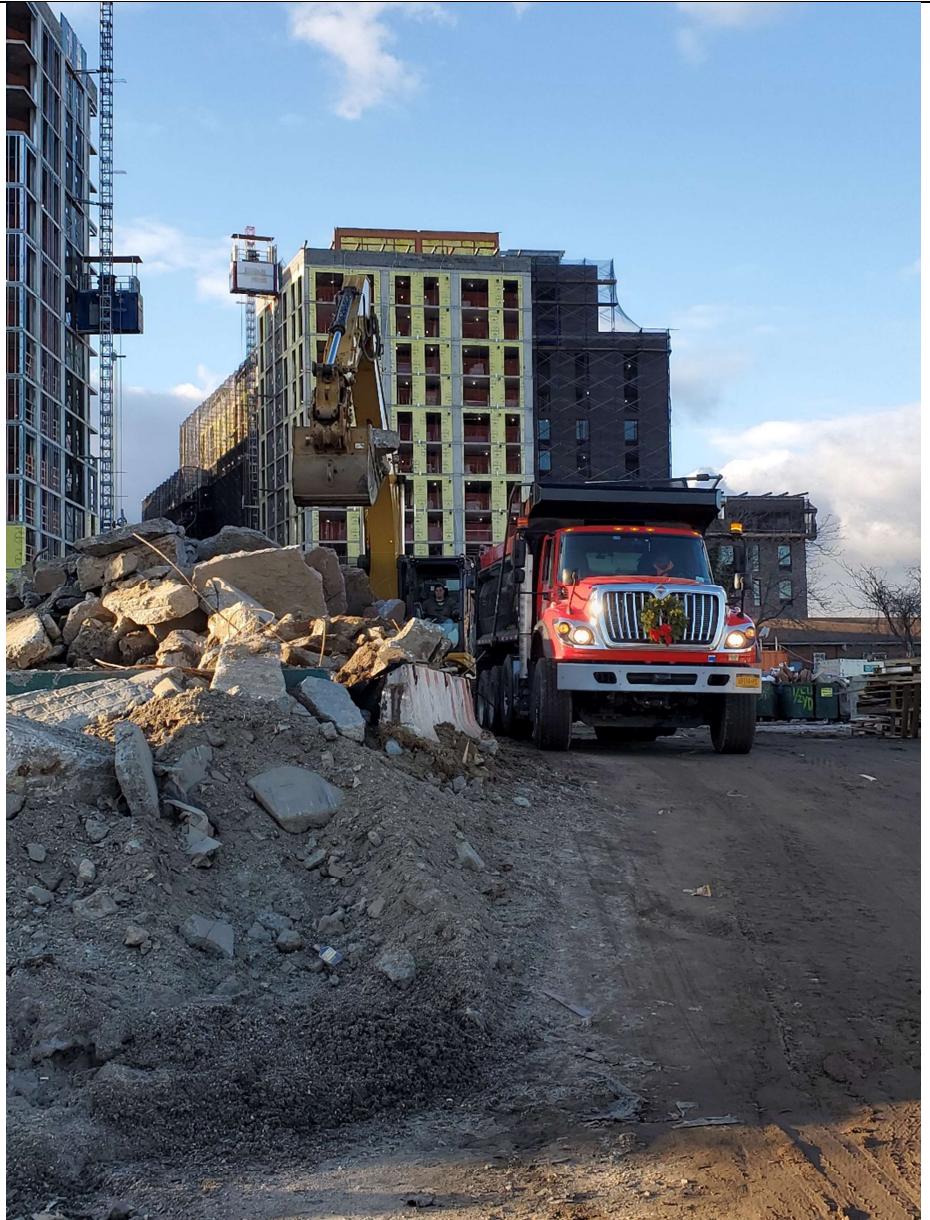




Photo 2- View of formwork and utility installation at Building H in C5, C6, and C7.



Photo 3- View of excavation and soil export from C6, C7, and C8.





## **Daily Report for December 30, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

**1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

-Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2- F4.

**2. Locations of work and quantities of material imported and exported from the Site.**

-No loads of contaminated material was exported from the site today.

-No material was imported to the site today.

**3. A summary of any and all complaints with relevant details (names, phone numbers).**

-No complaints.

**4. A summary of CAMP findings (air and dust readings).**

-No elevated PID or dust readings were identified.

**5. An explanation of notable Site conditions.**

-Today's work was overseen by Thomas Brown of CA RICH. No conditions of note were observed.

**6. Planned Activities**

-Continue formwork and rebar installation for Building B.

-Continue formwork and rebar installation for Building C.

-Continue formwork and rebar installation for Building H.



## Photo Log

Photo 1- View  
of Building B  
grids C3, C4,  
and D4.



Photo 2- View  
of Building C  
grids B3, B4,  
and A4.



Photo 3- View  
of Building H  
grids C6, C7,  
C8, and D8.







## **Daily Report for December 31, 2020**

**Far Rockaway Project  
20-02 Mott Avenue  
Far Rockaway, NY  
BCP #C241224**

**1. An update of progress made during the reporting day including references to alpha-numeric map for Site activities.**

-Utility, rebar, and formwork installation in A1- A4, B1- B5, C5-C8, D1- D7, E2- E4, and F2- F4.

**2. Locations of work and quantities of material imported and exported from the Site.**

-No material was exported from the site today.

-No material was imported to the site today.

**3. A summary of any and all complaints with relevant details (names, phone numbers).**

-No complaints.

**4. A summary of CAMP findings (air and dust readings).**

-No elevated PID or dust readings were identified.

**5. An explanation of notable Site conditions.**

-Today's work was overseen by Thomas Brown of CA RICH. No conditions of note were observed.

**6. Planned Activities**

-Continue formwork and rebar installation for Building B.

-Continue formwork and rebar installation for Building C.

-Continue formwork and rebar installation for Building H.

## Photo Log

Photo 1- View  
of Building C  
grids B1, B2,  
B3, and B4.



Photo 2- View  
between  
Building B and  
Building H  
grids B1, C1,  
B2, C2, B3, C3,  
B4, and C4.





Photo 3- View  
in front of  
Building H  
grids C5, C6,  
and C7.

