

# **Daily Activity Report**

Newtown Creek Bud Site - North Block 2-10 54th Avenue, Long Island City, New York

BCP No. C241248

General	Site	Information	

Date:	Tuesday, August 22, 2023			
Weather:	67-82 °F, Overcast and Rain			
Wind Direction/Speed:	W @ 9 mph			
AKRF Personnel on Site:	Mackenzie Miller			

AKRF Equipment on Site: Mini RAE 3000 Photoionization Detector [(PID) x1], TSI Sidepak Aerosol Monitor

#### **Contractor Information**

Contracting Company	Main Personnel	Equipment
Bud North GC LLC	Chris Steinmann	None.
Steven Dubner Landscaping	Luca Toscano	Small Excavator, hand tools.

### **Description and Location of Work Activities Performed**

Dubner imported 57 Stone from Astro Aggregates in Masepth, NY to the Site and spread it over the existing composite cover in grids WC-22 through WC-25.

Dubner imported and stockpiled Naturcycle planting soil from 110 Sand Company in Melville, NY and spread it over the existing composite cover in landscaping areas in grids WC-22 through WC25.

# Site Soil Disposal Tracking Information


Destination Facility	Daily Trucks	Total Trucks	Daily Approx. Cubic Yds	Total Approx. Cubic Yds	Total Site Loads	Total Approximate Cubic Yards
Clean Earth Carteret	0	79	0	1,580		
Clean Earth North Jersey	0	213	0	4,260		
Bayshore Management LLC	0	620	0	12,400	912	18,240
ACUA	-	-	0	0		
-	-	-	0	0		
Total	0	912	0	18,240	912	18,240


#### **CAMP Air Monitoring Results**

CAMP Station	UPWIND	DOWNWIND
Odors:	None.	None.
VOC Action Level Exceedance(s):	None.	None.
Particulate Action Level Exceedance(s):	N/A	N/A
Maximum VOC Level (ppm):	N/A	N/A
Maximum Particulate Level (mg/m³):	N/A	N/A

Comments: AKRF performed roving air monitoring during import and spreading activities. No odors were detected and particulates were not observed at or near the Site boundaries.

Planned Work Activity for Following Day/Week:	Construction of building superstructure.
Comments:	

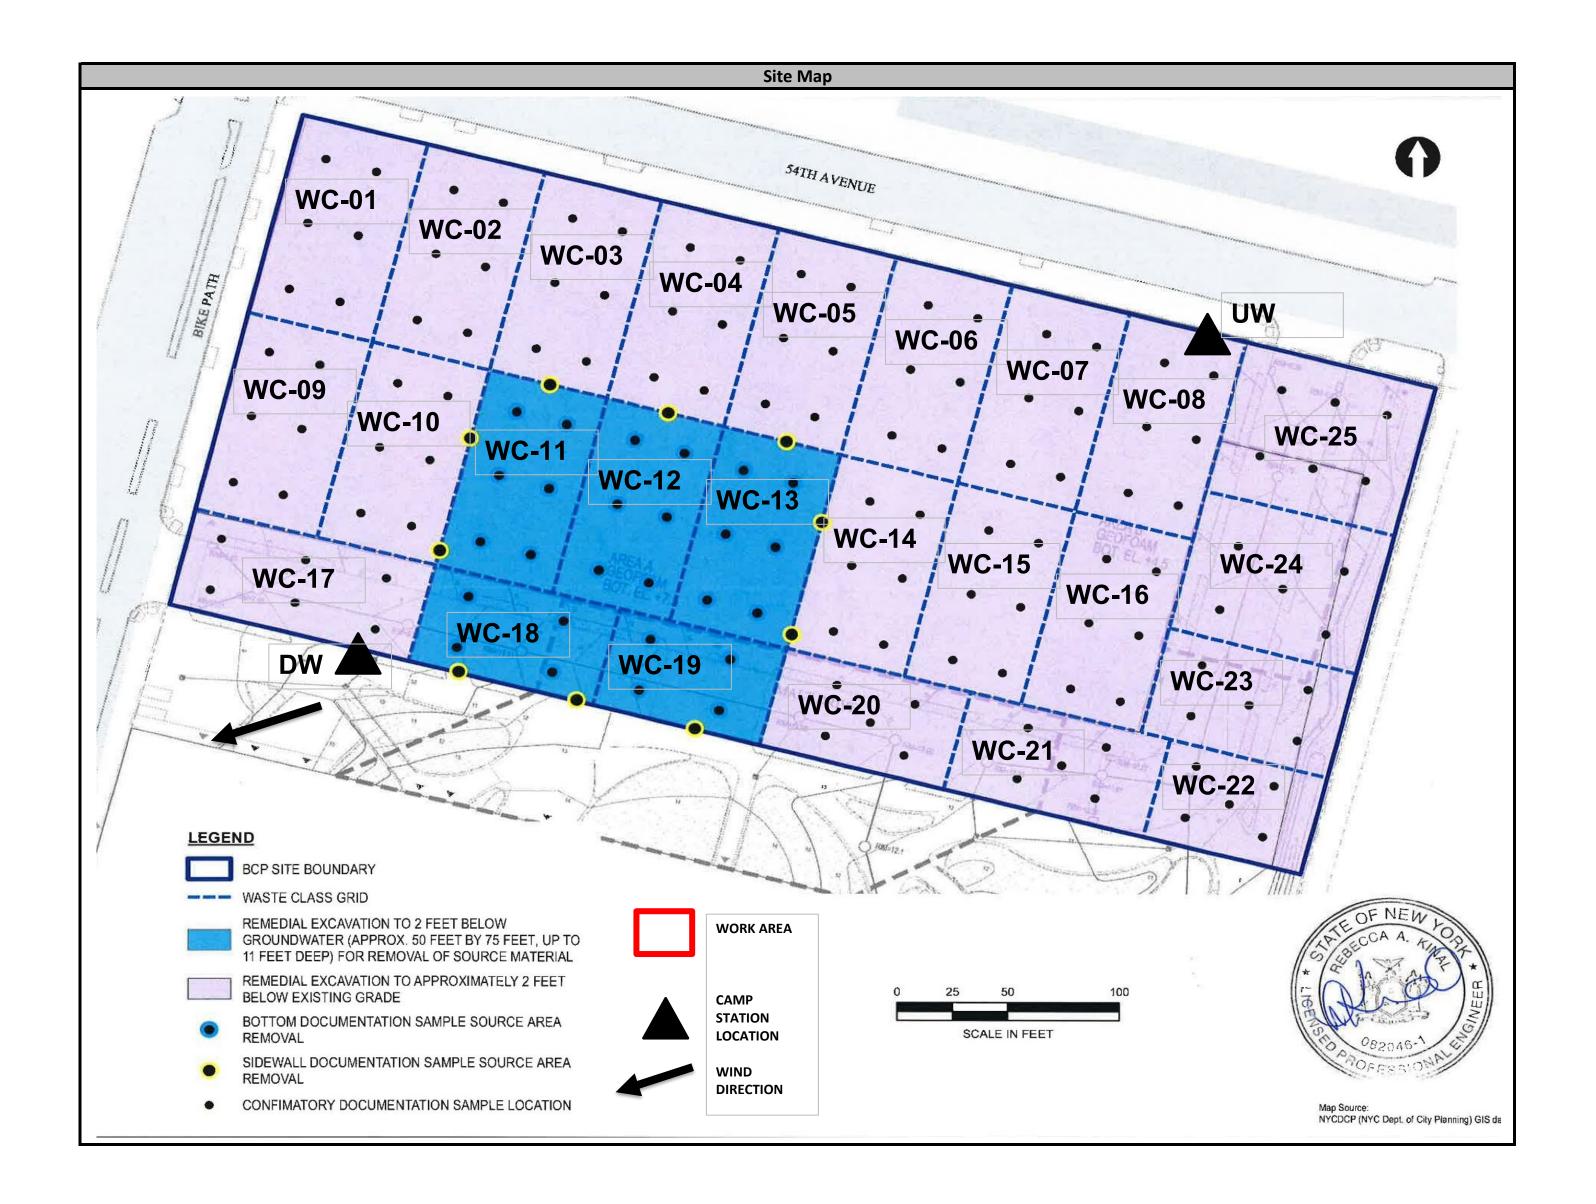

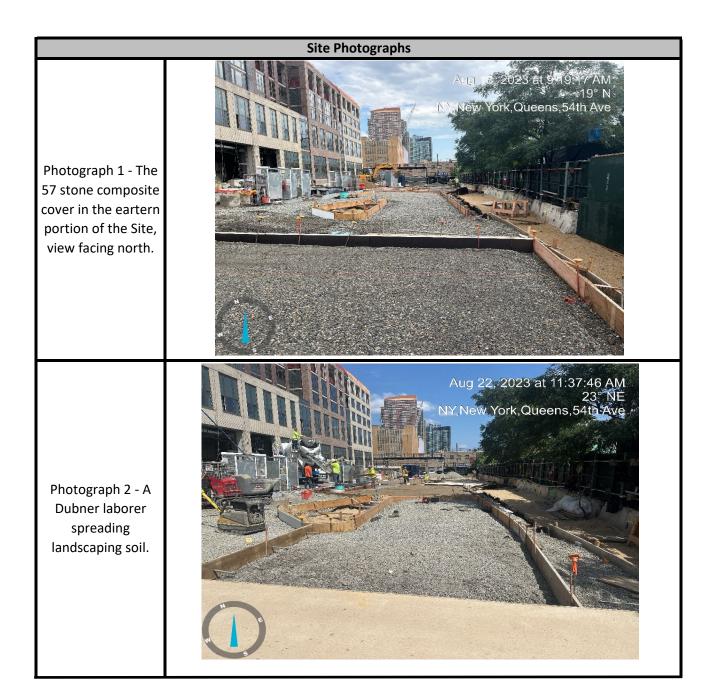



# **Daily Activity Report**

Newtown Creek Bud Site - North Block 2-10 54th Avenue, Long Island City, New York

BCP No. C241248

### **General Site Information**

Date:	Wednesday, August 30, 2023
Weather:	70-86 °F, Overcast and Rain
Wind Direction/Speed:	SW @ 8 mph
AKRF Personnel on Site:	Mackenzie Miller

AKRF Equipment on Site:

Mini RAE 3000 Photoionization Detector [(PID) x1], TSI Sidepak Aerosol Monitor

#### **Contractor Information**

Contracting Company	Main Personnel	Equipment				
Bud North GC LLC	Chris Steinmann	None.				
Steven Dubner Landscaping	Luca Toscano	Small Excavator, hand tools.				

#### **Description and Location of Work Activities Performed**

- Dubner poured concrete for the sidewalks in grids WC-24 and WC-25.
- Dubner excavated in discrete locations for installation of a permitter fence.

### Site Soil Disposal Tracking Information

Destination Facility	Daily Trucks	Total Trucks	Daily Approx. Cubic Yds	Total Approx. Cubic Yds	Total Site Loads	Total Approximate Cubic Yards
Clean Earth Carteret	0	79	0	1,580		
Clean Earth North Jersey	0	213	0	4,260		
Bayshore Management LLC	0	620	0	12,400	912	18,240
ACUA	-	-	0	0		
-	-	-	0	0		
Total	0	912	0	18,240	912	18,240


### **CAMP Air Monitoring Results**


CAMP Station	UPWIND	DOWNWIND
Odors:	None.	None.
VOC Action Level Exceedance(s):	None.	None.
Particulate Action Level Exceedance(s):	N/A	N/A
Maximum VOC Level (ppm):	0.0452	0.0
Maximum Particulate Level (mg/m³):	0.0587	0.0601


Comments: Air monitoring was suspended from 09:15 AM to 11:15 AM due to rainy conditions.

Lenoitibha	Intormatio

Planned Work Activity for Following Day/Week:	Construction of building superstructure.
Comments:	

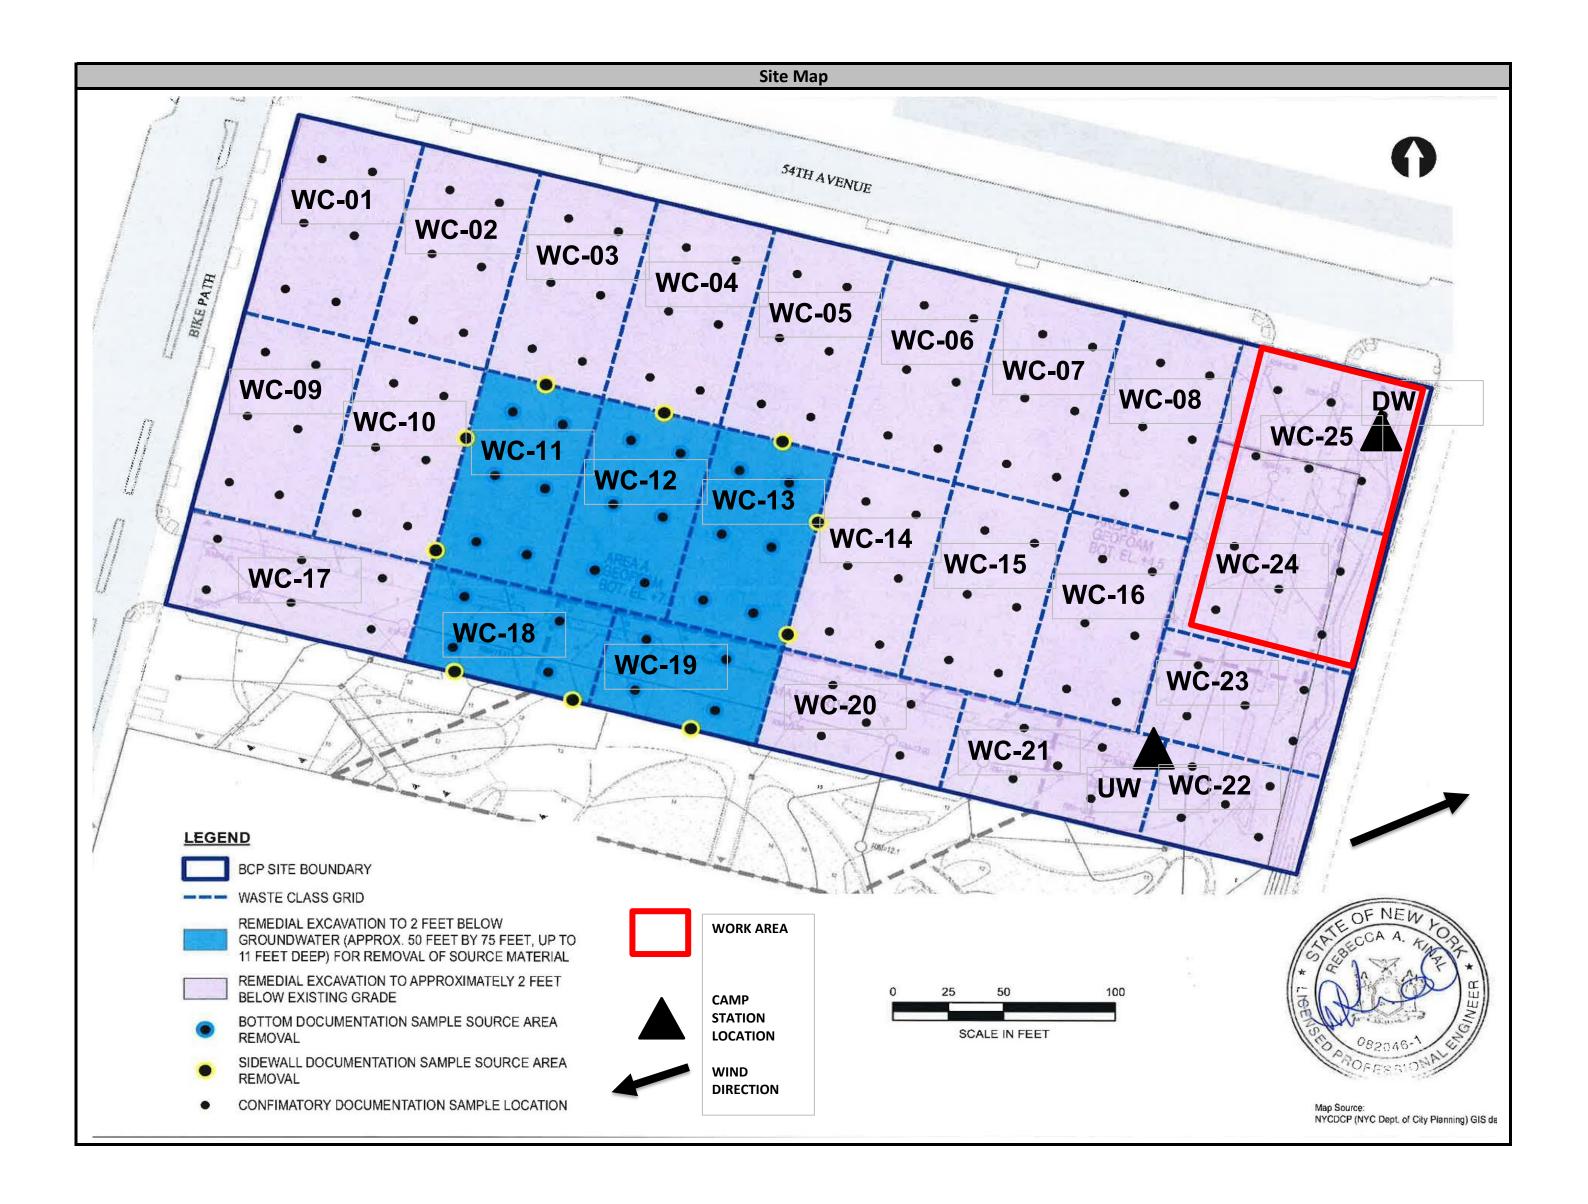

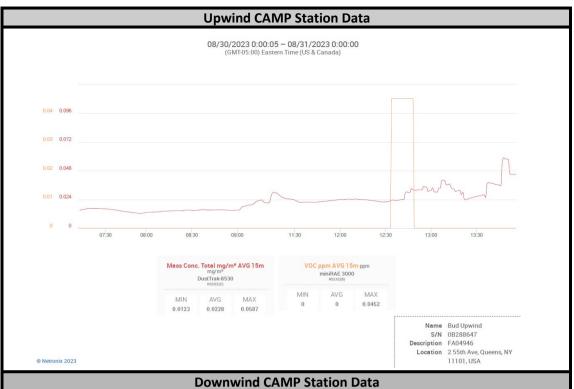

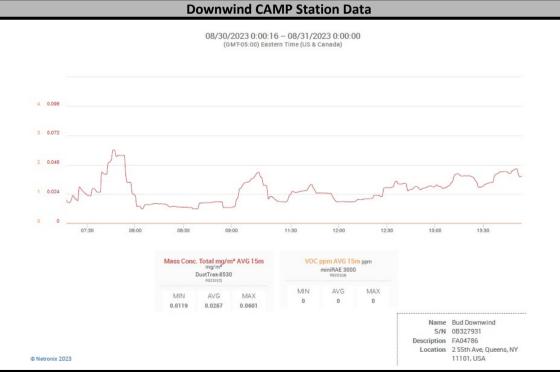

# **Site Photographs** 2023 at 9:09:04 AM 255° W Photograph 1 - A small excavation through the composite cover in WC-24, facing west. Photograph 2 - A small excavation through the composite cover in WC-24, facing southwest. Photograph 3 -Stockpiled soil coved with plastic sheeting at the end of the day, view facing east.



# **Daily Activity Report**

Newtown Creek Bud Site - North Block 2-10 54th Avenue, Long Island City, New York

BCP No. C241248

#### **General Site Information**

Date:	Thursday, August 31, 2023
Weather:	64-77 °F, Cloudy
Wind Direction/Speed:	N @ 10 mph
AKRF Personnel on Site:	Chad Walters

AKRF Equipment on Site: Mini RAE 3000 Photoionization Detector [(PID) x1], TSI Sidepak Aerosol Monitor

#### **Contractor Information**

Contracting Company		Main Personnel	Equipment	
	Bud North GC LLC	Chris Steinmann	None.	
	Steven Dubner Landscaping	Luca Toscano	Small Excavator, hand tools.	

# **Description and Location of Work Activities Performed**

- Dubner excavated in discrete locations for installation of a perimeter fence.
- Dubner stockpiling excavated soil [WC-24 (0-4)/WC-25 (0-4)] for future off-site disposal. Excavated material was covered with plastic sheeting.

## Site Soil Disposal Tracking Information

Destination Facility	Daily Trucks	Total Trucks	Daily Approx. Cubic Yds	Total Approx. Cubic Yds	Total Site Loads	Total Approximate Cubic Yards
Clean Earth Carteret	0	79	0	1,580	912	18,240
Clean Earth North Jersey	0	213	0	4,260		
Bayshore Management LLC	0	620	0	12,400		
ACUA	-	-	0	0		
-	-	-	0	0		
Total	0	912	0	18,240	912	18,240


### **CAMP Air Monitoring Results**


CAMP Station	UPWIND	DOWNWIND
Odors:	None.	None.
VOC Action Level Exceedance(s):	None.	None.
Particulate Action Level Exceedance(s):	N/A	Yes (1)
Maximum VOC Level (ppm):	0.0007	0.0
Maximum Particulate Level (mg/m³):	0.0339	0.429


Comments: Elevated levels of particulates (>0.100 mg/m3 above background) were detected at the Downwind CAMP station from approximately 08:12 to 08:26 due to dust associated with high winds and the movement of building materials around the Site (not excavation for fence installation). Water was applied to the work area and particulate levels returned to background levels.

## Additional Information

Planned Work Activity for	Construction of building superstructure
Following Day/Week:	Construction of building superstructure.
Comments:	

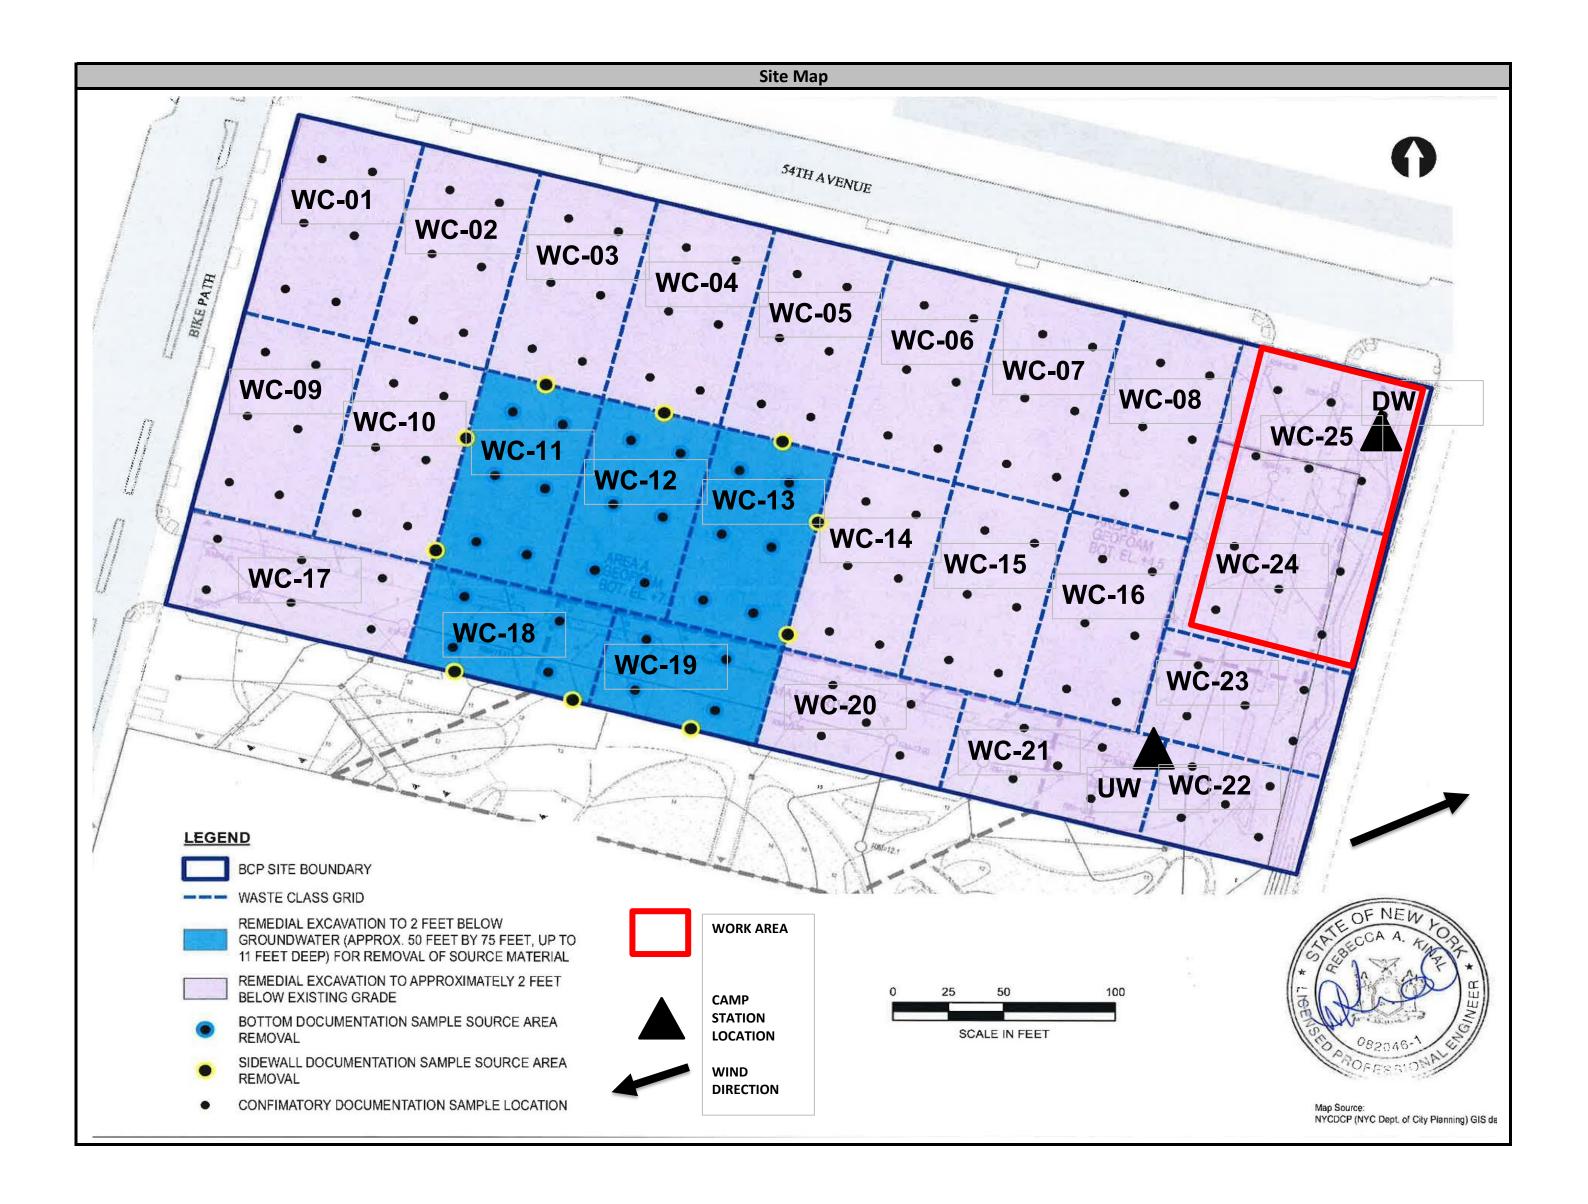


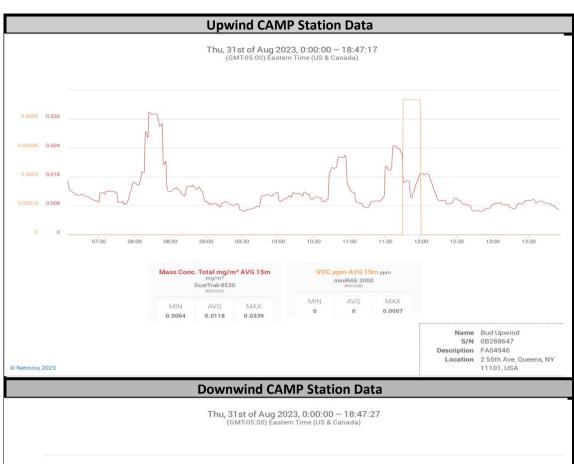

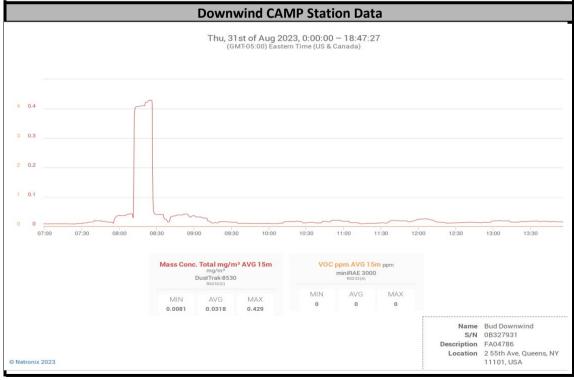

# **Site Photographs**

Photograph 1 -Exacavted material added to stockpile in WC-25, facing northwest.

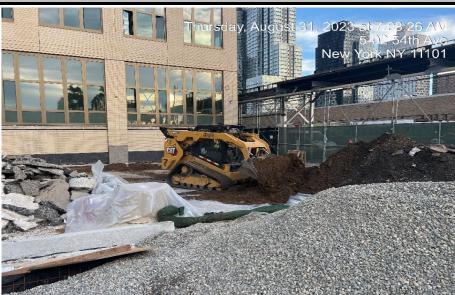

Photograph 2 -General view of the work zone in WC-24, facing north.



Photograph 3 -Stockpiled soil coved with poly sheeting, view facing southeast.

