

	Daily Activity Report					
	Magnolia Gardens					
	39-03 College Point Boulevard, Queens, NY					
	BCP Site No. C241273					
General Site Information						
Date:	Tuesday, June 11, 2024					
Weather:	60-75°F, Clear					
Wind Direction/Speed (towards):	N @ 3 mph					
AKRF Personnel on Site:	Mackenzie Miller					
AKRF Equipment on Site:	Mini RAE 3000 Photoionization Detectors [(PID) x3] and DustTrak Aerosol Monitors (x3)					
Visitors:	None					
Contractor Information						
Subcontractor						
Archstone Builders LLC				General Contractor (GC)		
Capstone Contracting Corp.				Foundation Contractor		
Description and Location of Work Activities Performed						
Excavation and site grading occurred in Grids WC-1/5/6 for lagging installation (as part of SOE).						
Contractor installed concrete forms and rebar in Grids WC-04, WC-05, and WC-07. Contractor poured concrete for walls in WC-4 and the elevator pit in WC-1.						
Material Disposal Tracking Information						
Destination Facility/Material Type	Daily Trucks	Total Trucks	Daily Approx. Cubic Yds	Total Approx. Cubic Yds	Total Site Loads	Total Approximate Cubic Yards
Clean Earth of North Jersey (CENJ)/(haz lead soil)	0	7	0	140	375	7,500
Clean Earth of North Jersey (CENJ)/(haz TCE soil)	0	6	0	120		
Bayshore Soil Management, LLC (Bayshore)	0	318	0	6,360		
River Front Recycling (C&D)	0	13	0	260		
Clean Earth of Carteret (CEC)	0	31	0	620		
Import Material Tracking Information						
Origin Facility	Daily Trucks	Total Trucks	Daily Tonnage	Total Tonnage	Total Site Loads	Total Quantity (tons)
Vulcan, Wantage or Hamburg Quarry	0	9	0.00	203.07	9	203.07
CAMP Air Monitoring Results						
CAMP Station	UPWIND			DOWNWIND		
Odors:	None			None		
VOC Action Level Exceedance(s):	None			None		
Particulate Action Level Exceedance(s):	None			None		
Maximum VOC Level (ppm) 15-min avg:	0.0000			0.0000		
Maximum Particulate Level (mg/m³) 15-min avg:	0.1021			0.1645		
CAMP Response Actions: None.						
Additional Information						
Planned Work Activity for Next Day/Week:	Continued installation of lagging in WC-2. Excavation and export soil for off-site disposal.					
Comments:	None.					

Soil Waste Classification Grid Plan

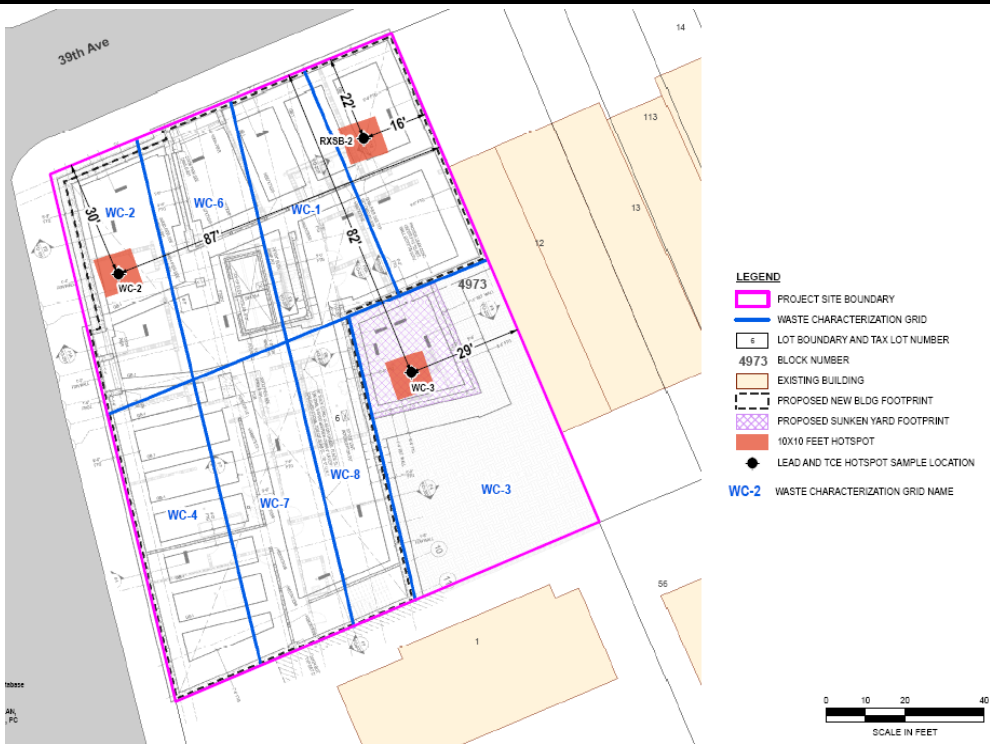

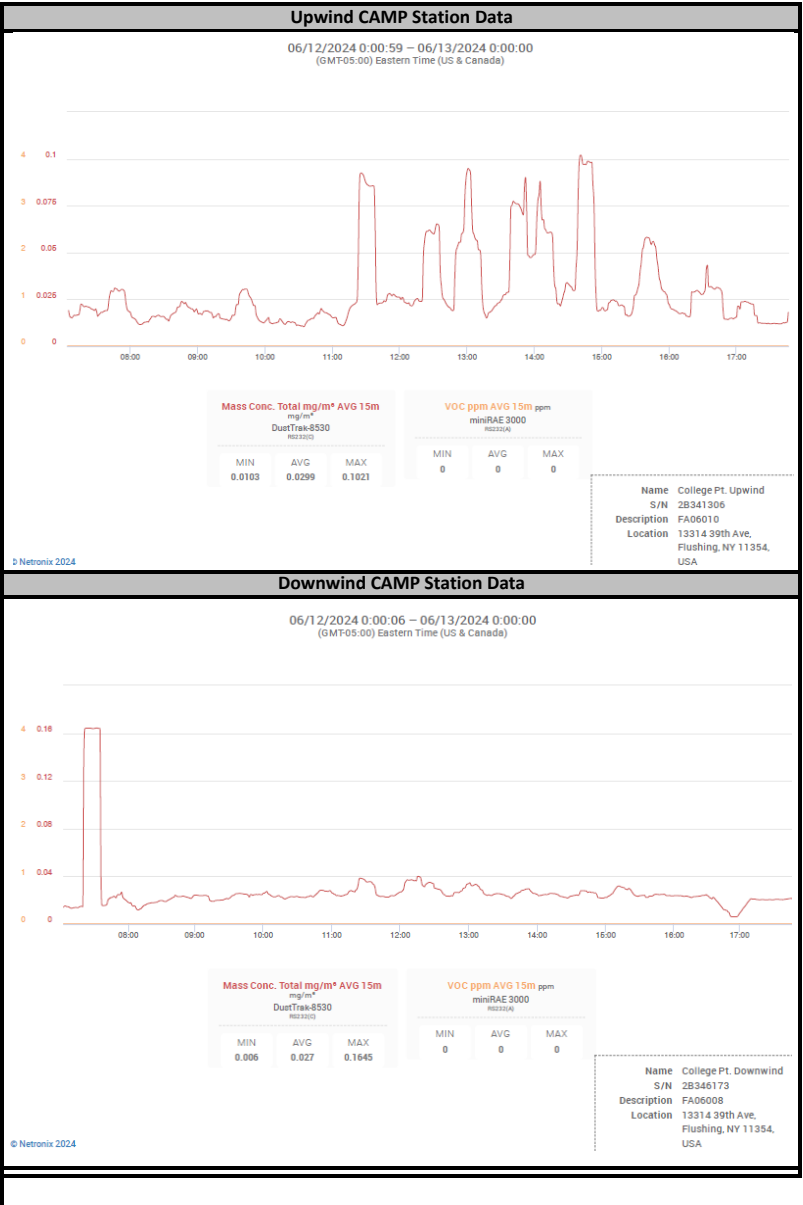

Site Photographs

Photograph 1 -
Excavation and
grading in WC-5 for
lagging installation,
view facing northeast.
Soil stockpile remains
covered with poly
sheeting.



Photograph 2 -
View of Site
conditions, view
facing northeast.



Photograph 3 -
View of Site
conditions, facing
southeast.

