

Principals

Anthony Castillo, PE
Fuad Dahan, PhD, PE, LSRP
Franz W. Laki, PE
John M. Nederfield, PE
Justin M. Protasiewicz, PE
Jose M. Rodriguez, PE
Michael St. Pierre, PE

September 29, 2025

via email: matthew.hubicki@dec.ny.gov

Mr. Matthew Hubicki
New York State Department of Environmental Conservation
Division of Environmental Remediation
625 Broadway
Albany, New York 12266-7014

**Re: Weekly Progress Report #7 – September 22 to September 26
130 Midland Avenue Site (C360195)
120 Midland Avenue
Port Chester, New York
SESI Project No. 13364**

Dear Mr. Hubicki:

On behalf of our Clients, 130 Midland Ave Owner LLC and 120 Midland Ave Owner LLC (the “Volunteers”), SESI Consulting Engineers (SESI) has prepared this Weekly Progress Report (WPR) at the request of the New York Department of Environmental Conservation (NYSDEC) regarding activities at the above referenced Site. This MPR includes the following:

- Actions related to the Site during the previous reporting period;
- Anticipated actions for the next reporting period;
- Approved activity modifications;
- Information regarding percentage of completion;

SESI performed or coordinated the performance of the activities listed below.

1. SUMMARY OF PROJECT ACTIVITIES:

A. TASKS PERFORMED DURING CURRENT REPORTING PERIOD

SESI, as the Environmental Engineering Consultant for the project, performed or coordinated the performance of the following tasks:

- Two (2) air monitoring stations were set up to monitor particulates and volatile organic compound (VOC): one (1) air monitoring station upwind and one (1) station downwind of the Site activities. No CAMP exceedance were recorded. No dust was observed to be migrating off-Site.
- The air monitoring data reports from each day are saved in this folder  [13364 CAMP Data Midland Ave.](#)

Monday, 09/22/2025

- Set-up and run upwind and downwind CAMP Monitors.
- The contractor began installing insulation along the exterior face of the foundation wall.
- The contractor backfilled and compacted areas adjacent to the foundation with approved RCA.

Tuesday, 09/23/2025

- Set-up and run upwind and downwind CAMP Monitors.
- The contractor continued backfill and compaction of areas along the exterior face of the foundation wall.

Wednesday, 09/24/2025

- Set-up and run upwind and downwind CAMP Monitors.
- The contractor continued backfill and compaction of areas along the exterior face of the foundation wall.

Thursday, 09/25/2025

- Set-up and run upwind and downwind CAMP Monitors.
- The contractor breaks up old concrete footings for off-site recycling.

Friday, 09/26/2025

- Set-up and run upwind and downwind CAMP Monitors.
- The contractor backfilled and compaction of areas footings and the garage.

B. CHANGES OR DEVIATIONS FROM ORIGINAL PLANS

- No changes or deviations from the original plans were made during this weekly reporting period.

2. SAMPLING ACTIVITIES AND ANALYTICAL RESULTS

- No sampling is planned.

3. ANTICIPATED TASKS FOR NEXT REPORTING PERIOD

SESI anticipates performing the following tasks in the next weekly reporting period:

- Continued CAMP monitoring.
- Continued excavation and proof rolling for building foundation.
- Continued pouring concrete foundation.

If you have any questions, please feel free to call me at (973) 808-9050.

Sincerely,

SESI CONSULTING ENGINEERS, DPC

A handwritten signature in blue ink, appearing to read "St. Gustems".


Steven Gustems, PG
Senior Project Manager

Attachments:

Figure

Photographs

FIGURE

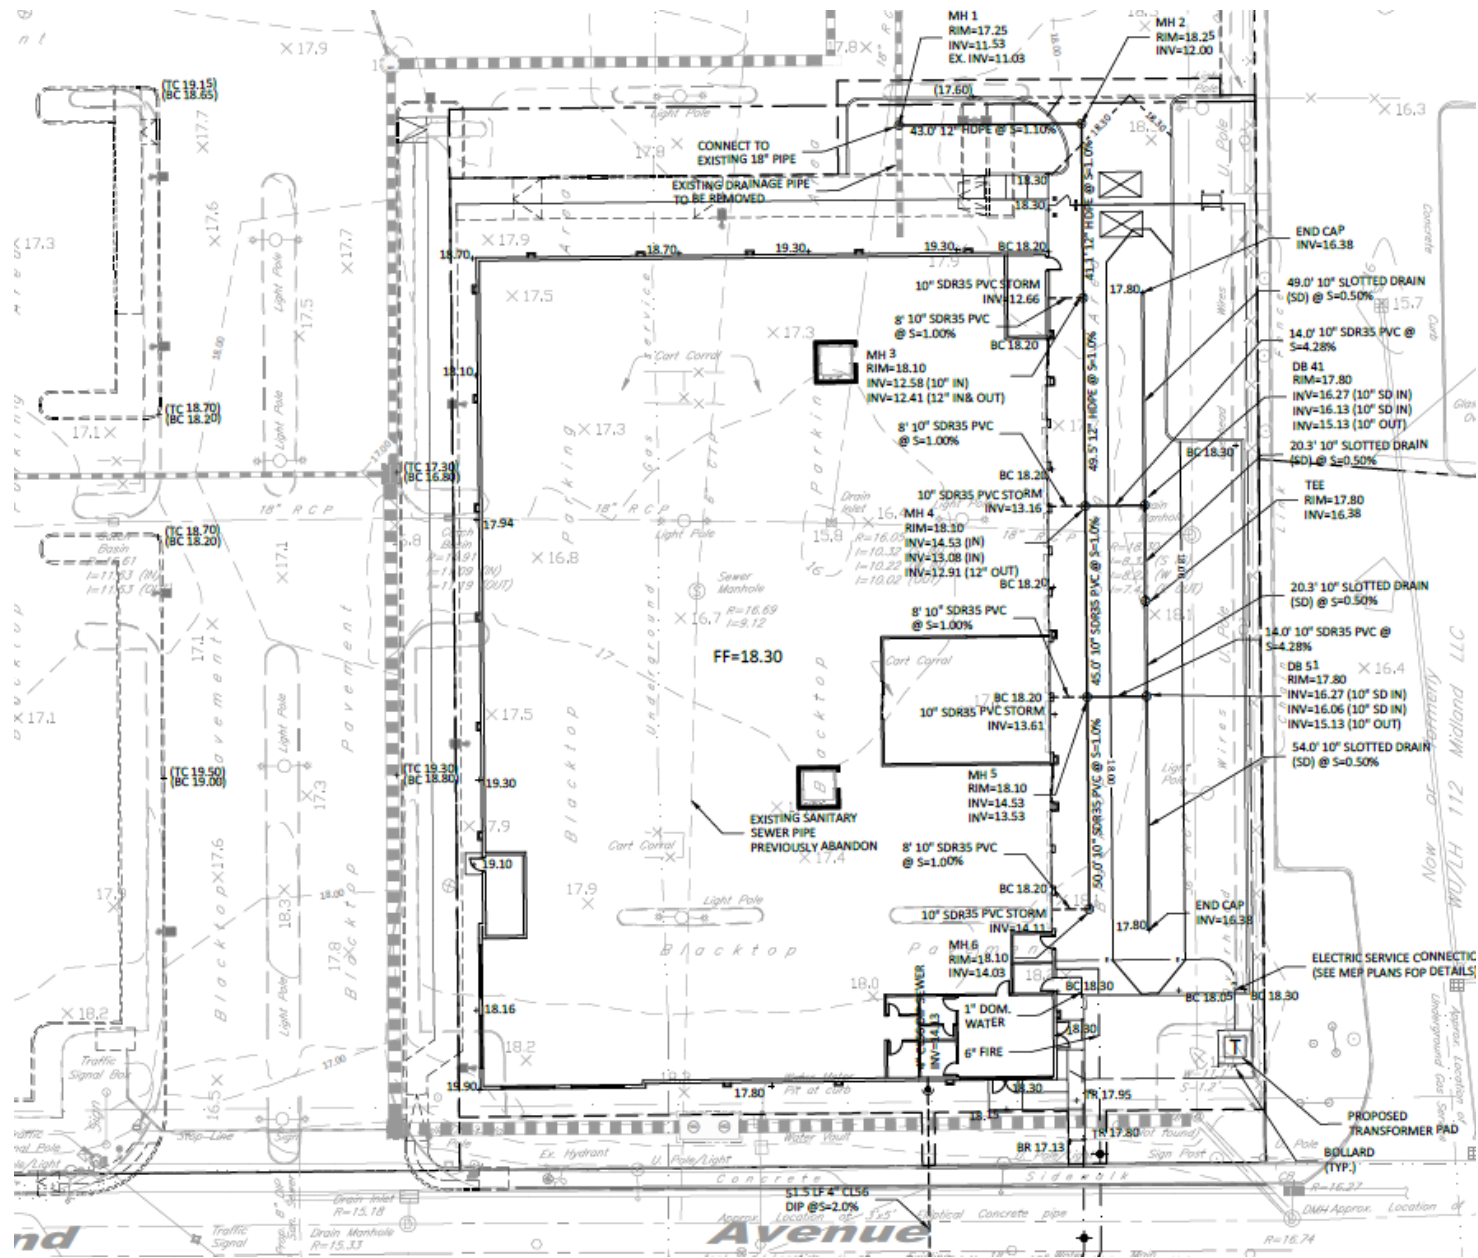

PHOTOGRAPHS

Photographs



Photo 1. Insulating (09/22/2025)



Photo 2. Insulating (09 /22/2025)



Photo 3. Backfilling (09/23/2025)



Photo 4. Backfilling (09/24/2025)

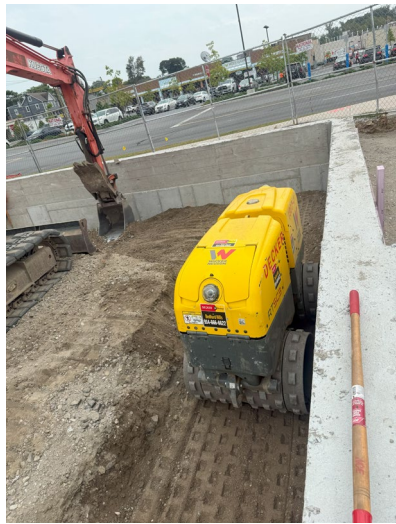


Photo 5. Proof-rolling (09/24/2025)



Photo 6. Breaking up Concrete(09/25/2025)



Photo 7. Backfilling (09/26/2025)



Photo 8. Proof-rolling (09/26/2025)
