

### Environmental, Planning, and Engineering Consultants

440 Park Avenue South 7<sup>th</sup> Floor New York, NY 10016 tel: 212 696-0670 fax: 212 213-3191 www.akrf.com

February 26, 2024

Mr. Matthew Hubicki NYS Department of Environmental Conservation Division of Environmental Remediation 625 Broadway Albany, New York 12233-7016

Re: Monthly Progress Report – January 2024

Former United Hospital – 406 Boston Post Road, Port Chester, New York

NYSDEC BCP Site No. C360202

Dear Mr. Hubicki:

This Monthly Progress Report has been prepared by AKRF, Inc. (AKRF) to summarize the work performed at the Former United Hospital site located at 406 Boston Post Road in Port Chester, New York [New York State Department of Environmental Conservation (NYSDEC) Brownfield Cleanup Program (BCP) Site No. C360202] (the Site) during the month of January 2024. The following activities were conducted:

- The demolition contractor continued with the handling of building materials (sorting of scrap metal, and concrete and demolition debris for off-site disposal) associated with Phase 3 (Structural Demolition) of the former hospital buildings. As the work included the exterior handling of building materials associated with the demolition of exterior and interior building elements (partition walls, drop ceilings, mechanical equipment, etc.), AKRF implemented the full-scale Community Air Monitoring Program (CAMP)/environmental monitoring included in the Remedial Investigation Work Plan (RIWP) during each workday. A total of six CAMP stations (three fixed stations deployed at the same location each day and three portable stations that were adjusted daily for changes in wind and/or work zones) were deployed prior to the start of each workday. Each CAMP station was equipped with a photoionization detector (PID) and dust monitor capable of calculating 15-minute running averages for volatile organic compound (VOC) and particulate concentrations, respectively, and a Netronix<sup>TM</sup> Global System for Mobile Communication (GSM)/Global Positioning System (GPS) device capable of recording air monitoring and location data. All air monitoring data was posted on a password-protected, project-specific, online database and was regularly downloaded/saved, with real-time e-mail/mobile alerts sent to AKRF staff to indicate action level exceedances (if any). A Daily Activity Report was prepared and submitted to NYSDEC and NYSDOH for each workday, which documented the work completed that day, provided the schedule for near-term field work, and included a summary of the findings from the CAMP monitoring activities. Copies of the Daily Activity Reports are included in Attachment A of this Monthly Progress Report.
- The excavation contractor demolished the existing asphalt cap within the antennae Change of Use (COU) area and exported the asphalt generated for off-site disposal. Following demolition of the asphalt cap, the excavation contractor excavated a 2-foot cut (0-2 feet below grade) across the entirety of the antennae COU area, and excavated 10-foot by 10-foot hotspots centered around soil borings RI-SB-53 and RI-SB-54 to 6 feet below grade (4 feet beneath the initial COU area 2-foot cut). Excavations were performed and endpoint samples collected at each hotspot in accordance with email correspondence between AKRF and NYSDEC dated November 7, 2023.

- Thirty-five loads (approximately 700 cubic yards) of soil generated from the excavations within the antennae COU area was exported for off-site disposal at Clean Earth of Carteret in Carteret, NJ.
- During all work that occurred within the antennae COU area AKRF continued to implement the full-scale CAMP/environmental monitoring included in the RIWP, utilizing six CAMP stations as detailed previously. Locations of the CAMP stations were modified in accordance with email correspondence between AKRF and NYSDEC dated November 15, 2023 to accurately reflect the work area.
- The excavation contractor began construction of a retaining wall, and rebar and concrete form assembly for the future antenna concrete pad within the antennae COU area. A demarcation layer was placed at the base of all completed excavations within the antennae COU area, including the RI-SB-53 hotspot, where endpoint sample results below the Restricted Residential Soil Cleanup Objectives (RRSCOs) were achieved. Additional remedial excavation will be performed for the RI-SB-54 hotspot, as described below, which will be completed in February 2024.
- The excavation contractor imported 56 loads of NYSDEC-approved Item #4 (approximately 1,335 cubic yards) and two loads of 3/4" stone (approximately 45 cubic yards) for use as structural backfill above the demarcation layer within the antennae COU area.

The following work is planned for February 2024:

- The excavation contractor will extend the RI-SB-54 hotspot to bedrock, anticipated at approximately 11 feet below grade, as the endpoint and contingency endpoint samples did not achieve results below the RRSCOs. Following the excavation, a demarcation layer will be placed at the base of the excavation, and it will be backfilled with NYCDEC-approved Item #4 and ¾" stone.
- AKRF will continue implementation of full-scale CAMP/environmental monitoring during active structural demolition, the handling of building materials associated with structural demolition (sorting of scrap metal, and concrete and demolition debris for off-site disposal), and any excavation activities within the antennae COU area.
- Site work related to the antennae construction under the Change of Use Notification dated September 7, 2023 will continue. In addition to extending the RI-SB-54 hotspot to bedrock, work is anticipated to consist of concrete work, grading and compaction activities, and import of NYSDEC-approved Item #4 and 3/4" stone from Tilcon of West Nyack, NY, for placement above the demarcation layer.
- AKRF will continue preparation of the Remedial Investigation report (RIR), which is anticipated to be submitted to NYSDEC in March 2024.

If you have any questions regarding the information presented in this letter, please contact me at (914) 400-9736.

Sincerely, AKRF Inc.

Stephen Schmid

Athe Short

Senior Environmental Scientist

cc (electronic copy only):


Kerry Maloney – NYSDEC Angela Martin – NYSDOH Christopher Gibaldi, Aaron Levy – Boston Post Road Owner LLC Christine Leas – Sive, Paget & Riesel P.C. Marc Godick, Tim McClintock – AKRF

### ATTACHMENT A DAILY ACTIVITY REPORTS

					Daily Activi	ty Poport				
<b>PAK</b>	<b>P</b> F			<u></u>	Daily Activi Former United					
	MM,	Port Chester, NY BCP No. C360202								
		General Site Information								
Date: Weather:		Monday, January 8, 2024 Partly Cloudy, 29 - 42°F								
Wind Direction/Speed	:	Partly Cloudy, 29 - 43°F NW @ 5 mph								
AKRF Personnel on Sit	RF Personnel on Site: Michael Iodice						One Handhald Dust Manites			
AKRF Equipment on Si Visitors:	te:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor None.								
	Contractor Information  Contracting Company Key Personnel Equipment									
	apital Industries Corp.					Various demolition equipment				
	Demolition Contractor)		Joe Cia	nciulli		(e.g., excavators, skid steers, roll off containers, etc.)				
Description and Location of Work Activities Performed										
The demolition contra	ctor continued sorting and loading demolti	on debris into contai	ners for off-site dispo	osal.						
No ground intrusive a	ctivities were conducted onsite.									
			Site Soil Dispo	sal Tracking Informa	ition					
<b>Destination Facility</b> Not Applicable (N/A)		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Not Applicable (N/A)		N/A		N/A		N/A		N/A		
		Daily Import (CY)		0		Total Import (CY)		0		
			Imported Fill Tracking Information							
	Origin Facility	Daily Trucks		Daily Approx. Total Approx.		Total Site Loads		Total Approximate Cubic Yards		
Not Applicable (N/A)		N/A		N/A		N/A		N/A		
		Daily Import (CY)		0		Total Import (CY)		0		
CAMP Information		Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2		
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed		
VOC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
Particulate Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
	Additional Information									
Planned Work Activity for Following Day(s):  The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  Work in the antennae change of use work area is anticipated to begin on Tuesday (1/9).										
Comments: None.										

1 of 69 C360202\_Daily Report\_2023.01.08

### Photograph 1 Handling of structural demolition debris in the eastern portion of the site, view facing northeast.

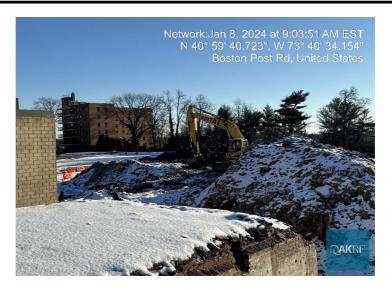


### Photograph 2 Handling of structural demolition debris in the eastern portion of the site, view


facing north.





### Photograph 3 Handling of structural demolition debris in the eastern portion of the site, view facing north.




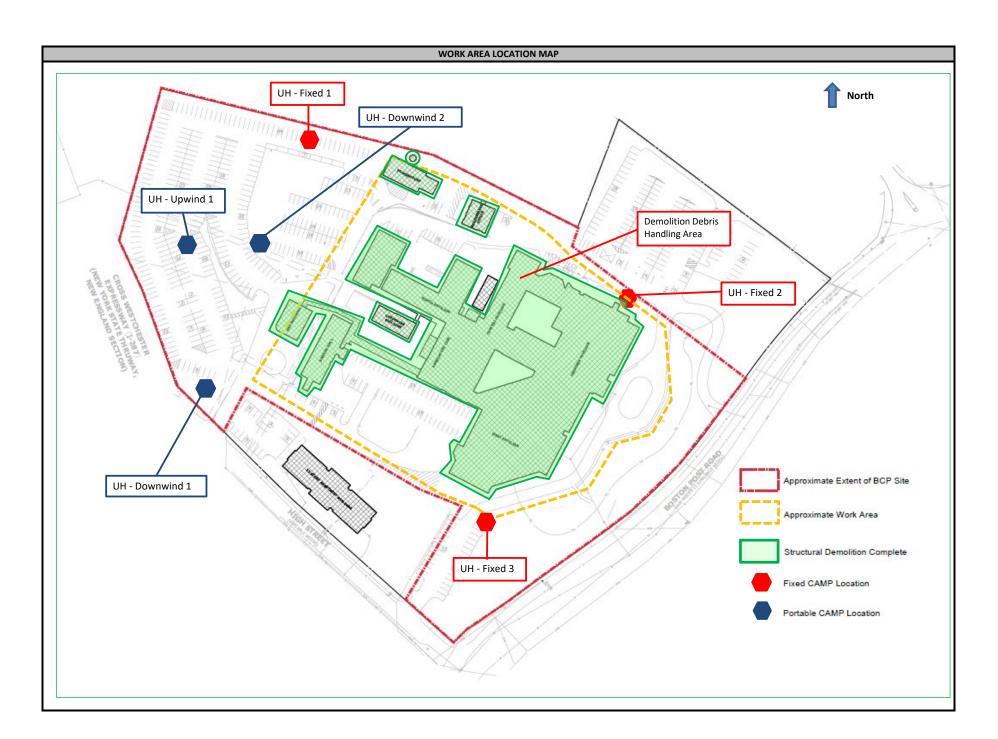


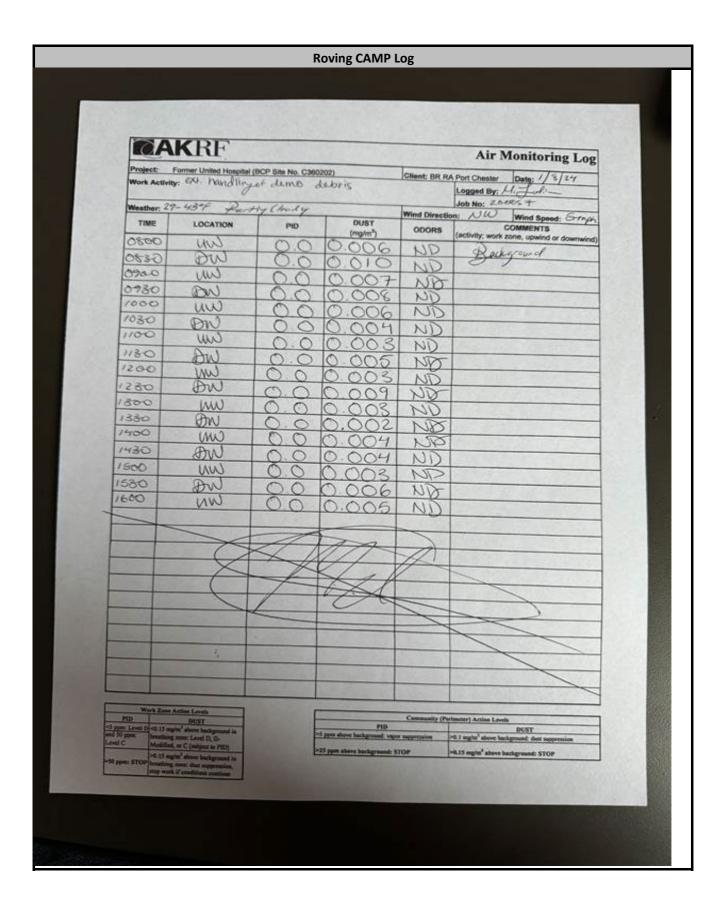


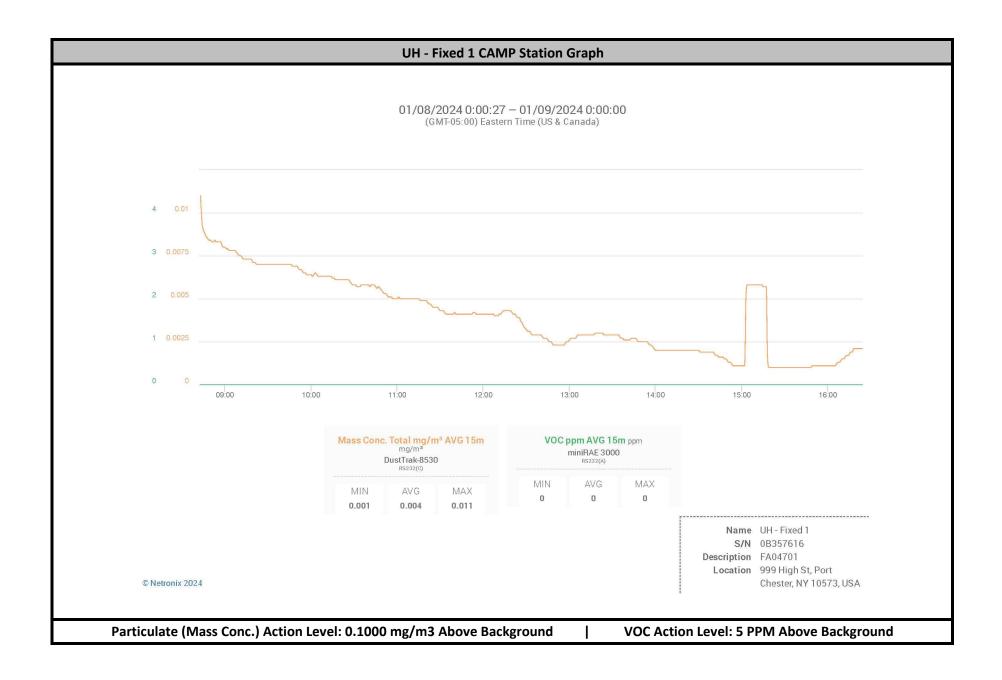


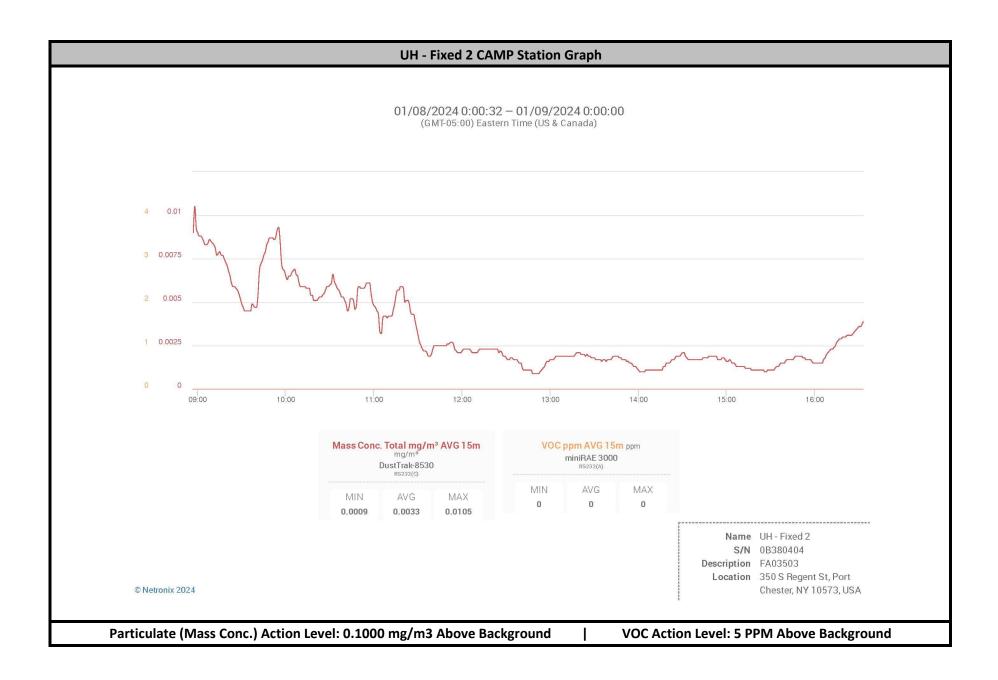

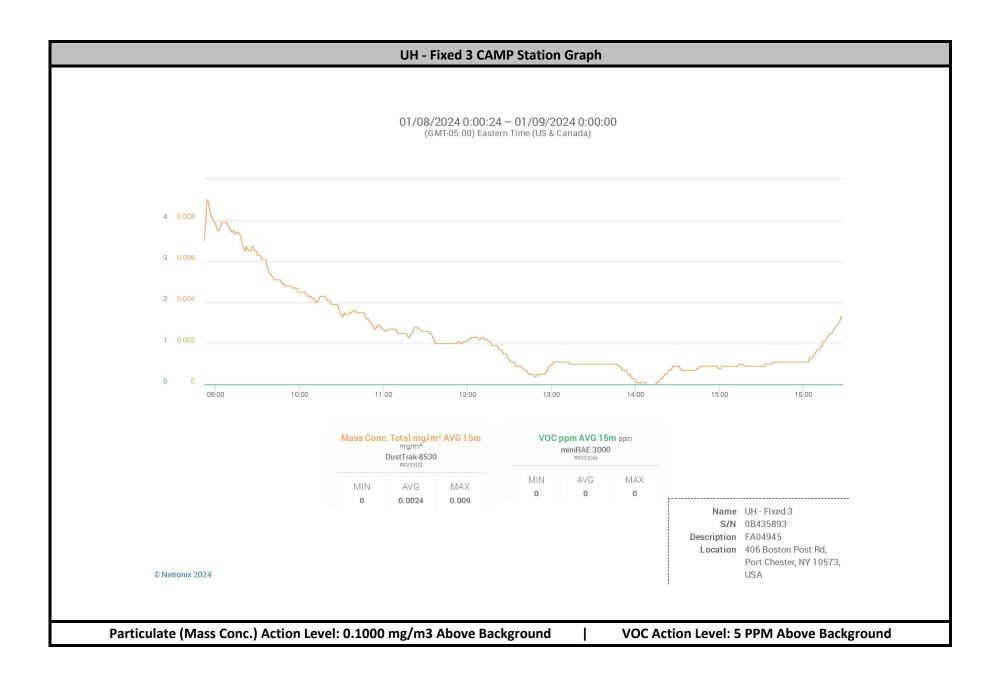

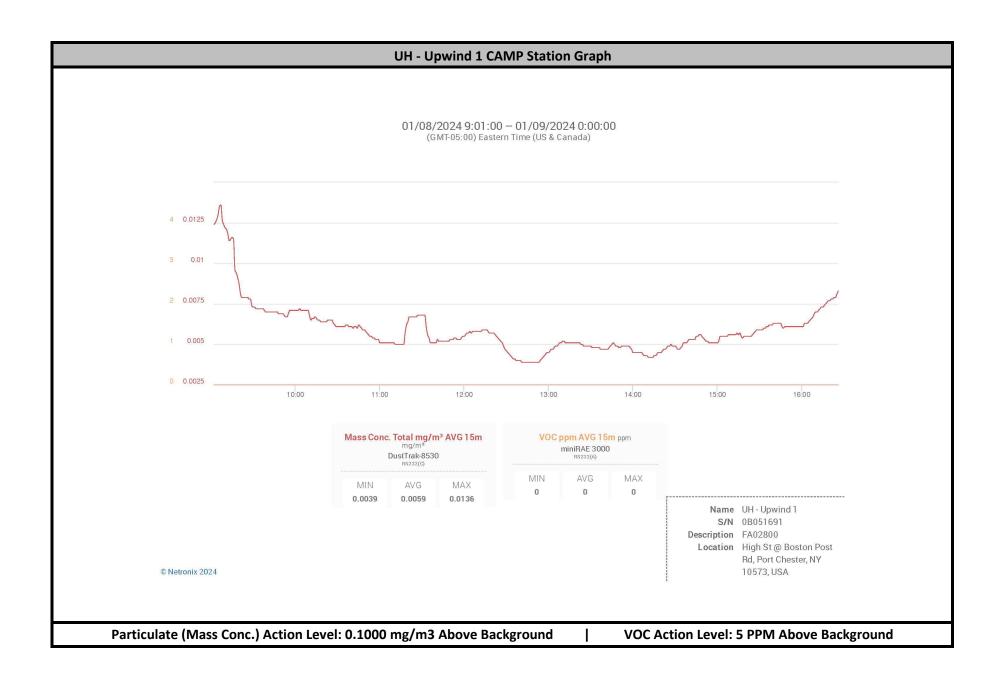

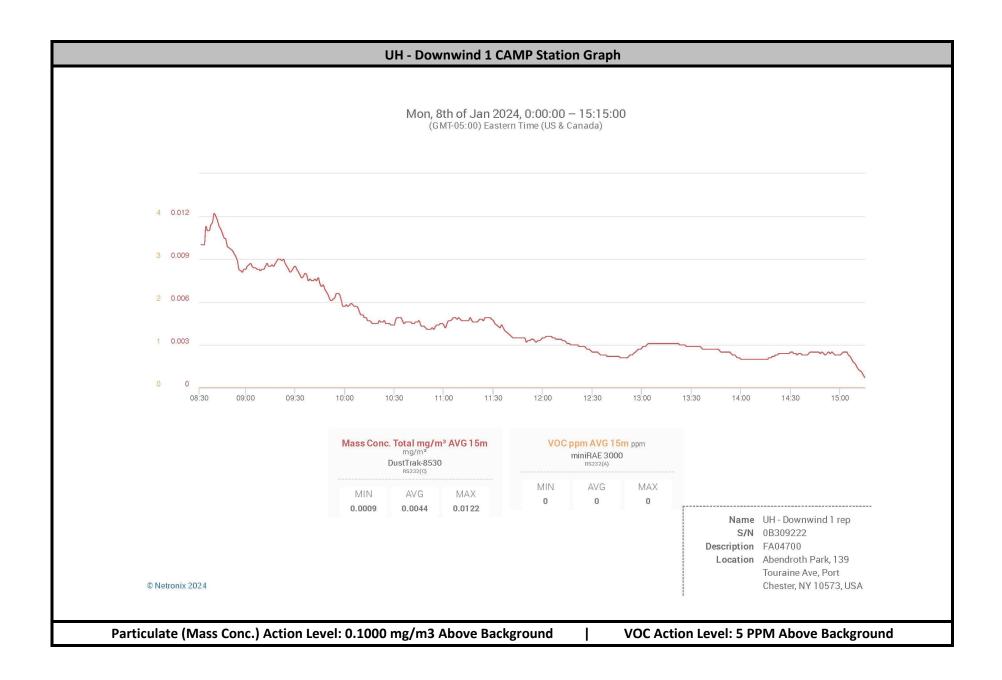

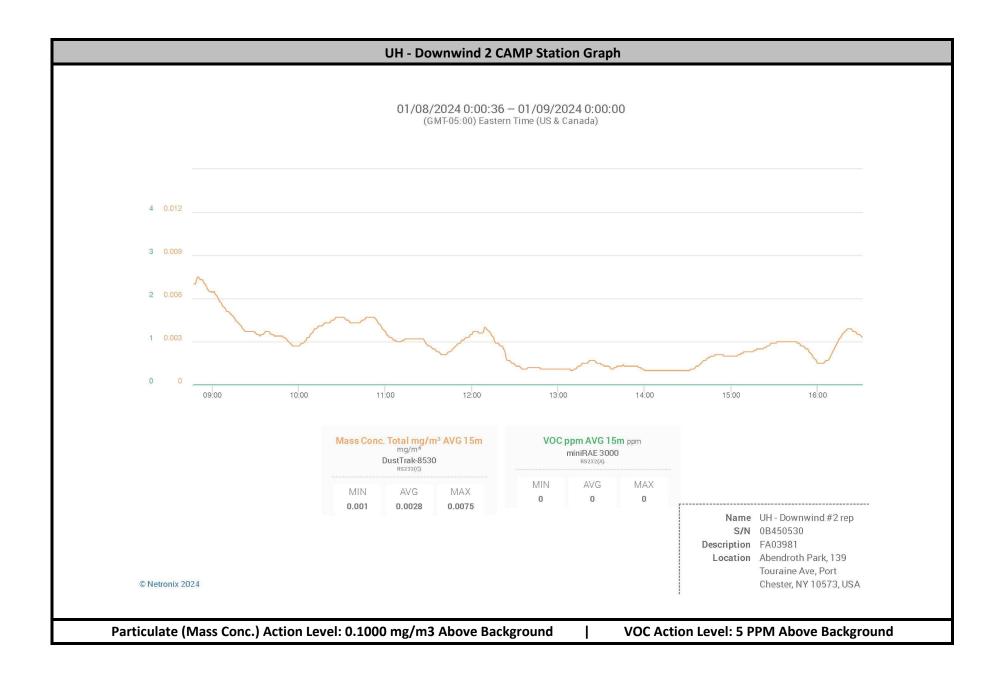

					Daily Activi	ty Report				
<b>PAK</b>	<b>D</b> L	Daily Activity Report Former United Hospital								
	MM,	Port Chester, NY BCP No. C360202								
			Genera	l Site Information	BCL NO. C:	000202				
Date: Weather:				Partly Claus	Tuesday, Janua		6 EE°E			
Wind Direction/Speed:	:	Partly Cloudy (morning) / Heavy Rain (afternoon), 26 - 55°F ESE @ 7 mph								
AKRF Personnel on Site										
AKRF Equipment on Sit /isitors:	te:	3 Fixed CAIV	IP Stations (PID & DU	ist Monitor), 3 Porta	None CAIMP Stations (I		, One Handheid PID,	One Handheid Dust Monitor		
Contractor Information  Contracting Company Key Personnel Equipment										
	apital Industries Corp.					Equipment  Various demolition equipment				
	Demolition Contractor)	Joe Cianciulli			(e.g., excavators, skid steers, roll off containers, etc.)					
		D€	escription and Locati	on of Work Activitie	s Performed					
he demolition contrac	ctor continued sorting and loading demolti	on debris into contai	ners for off-site dispo	osal.						
No ground intrusive ac	ctivities were conducted onsite.									
			Site Soil Dispo	sal Tracking Informa	ition					
Destination Facility		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Not Applicable (N/A)		N/A		N/A		N/A		N/A		
		Daily Import (CY)		0		Total Import (CY)		0		
			Imported Fil	Il Tracking Informati	on					
	Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.	Total Approx. Total S		te Loads	Total Approximate Cubic Yards		
Not Applicable (N/A)		N/A		N/A		N/A		N/A		
			Daily Import (CY)	(	)		Total Import (CY)	0		
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2		
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed		
VOC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
Particulate Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
			Additi	onal Information						
Planned Work Activity for Following Day(s):		ctor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.								
Comments:	The use of air monitoring equipment was suspended at approximately 11:35 due to inclement weather (rain). Visual and olfactory monitoring were performed during the period that the air monitoring equipment was not in use, and no fugitive dust or odors were detected.									

1 of 34 C360202\_Daily Report\_2023.01.09

## Photograph 1 Handling of structural demolition debris in the eastern portion of the site, view facing south.




### Photograph 2 -Handling of structural demolition debris in the eastern portion of the site, view facing

north.





## Photograph 3 Handling of structural demolition debris in the eastern portion of the site, view facing south.




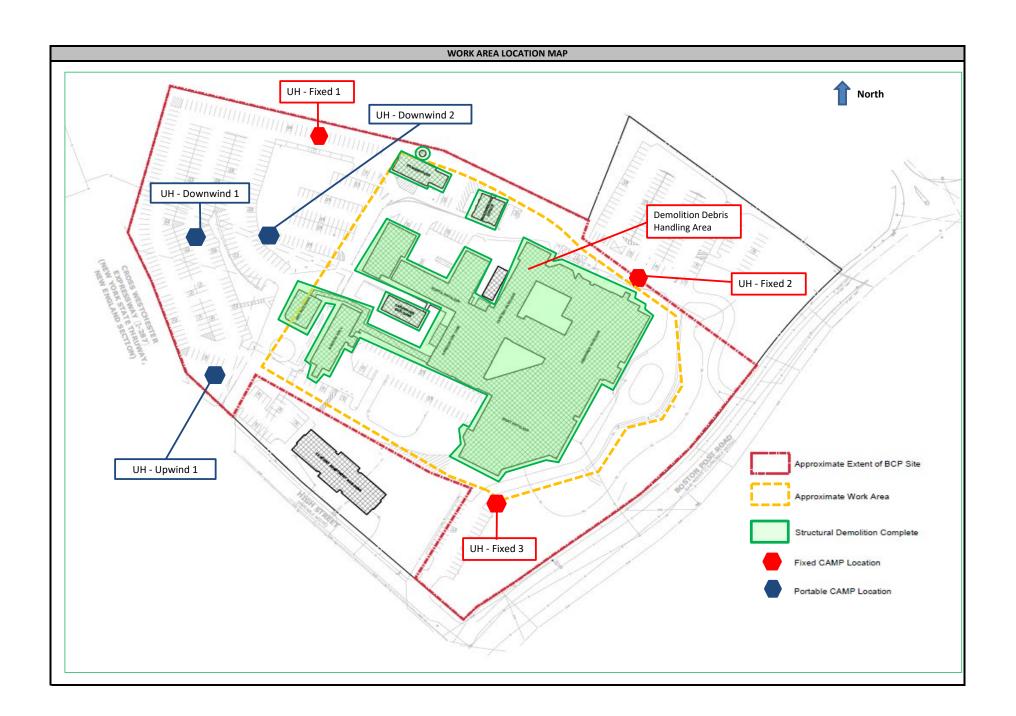



### **Roving CAMP Log** CAKRE Air Monitoring Log Project: Former United Hospital (BCP Site No. C360202) Client: BR RA Port Chester Date: 1/9/27 Work Activity: ext. handly of demo debris Logged By: H. Juli Job No: 200057 ESE Wind Speed: 7 mph Weather: 26 - 55 F Partly (lowly (morn) Hay y Pair (all mon) Wind Direction: COMMENTS (activity; work zone, upwind or downwind) TIME LOCATION ODORS (mg/m<sup>3</sup>) 0600 UND 0,026 Background simi havid 0830 DW 0.031 UN 0900 CUN 0.029 ND 0930 DW 0.045 ND 1000 WW 0.038 ND 1030 DW 0.049 ND 1100 CUN 0.021 NI) 1130 DW 0.031 M 1200 WZ NA ND heavy rain none observed 1230 1300 1330 1200 1430 1800 1530 Community (Perimeter) Action Levels DUST DUST Work Zone Action Levels PID DUST S ppm: Level D on 50,15 mg/m² above background ind 50 ppm: breathing zone: Level D, D. Level C Modified, or C (subject to PID) >5 ppm above background: vapor suppression >0.1 mg/m³ above background: dust suppress >0.15 mg/m³ above background: STOP >25 ppm above background: STOP >0.15 mg/m² above backgroup breathing zone; dust suppress stop work if conditions continued to the stop work is con

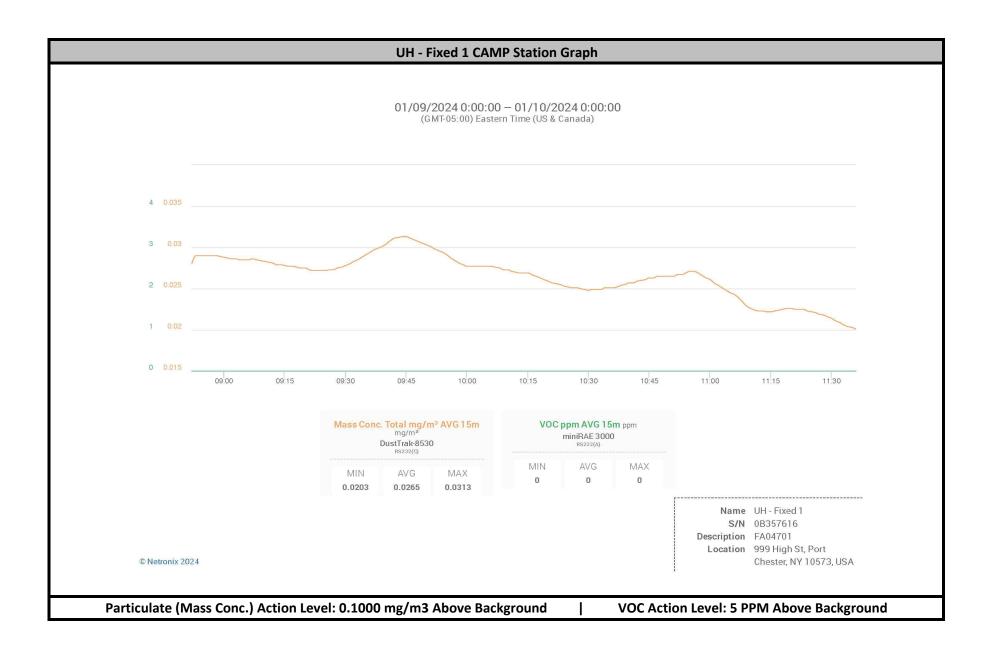


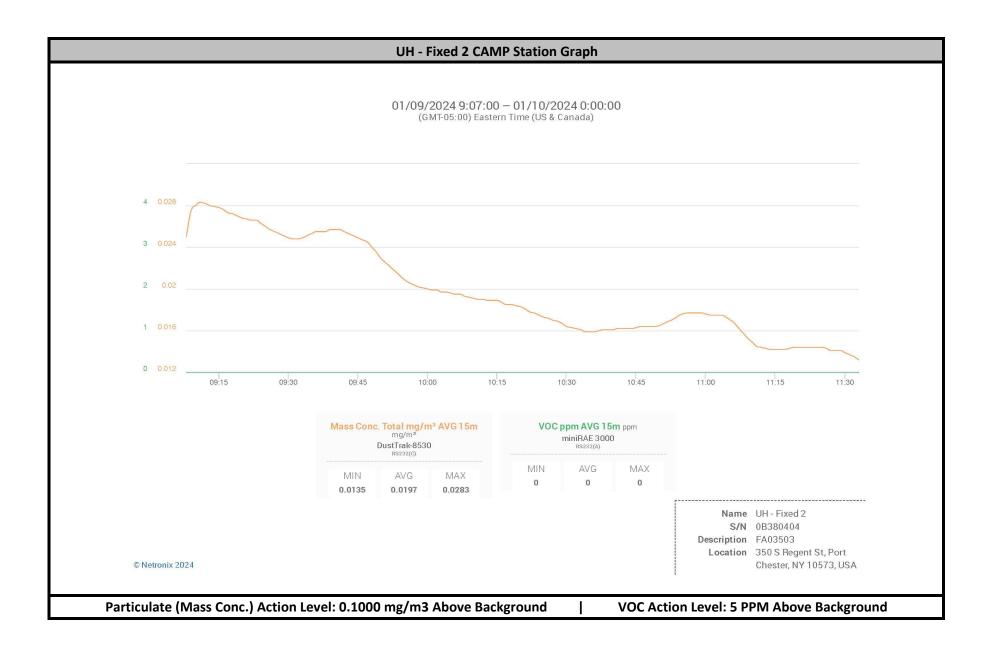

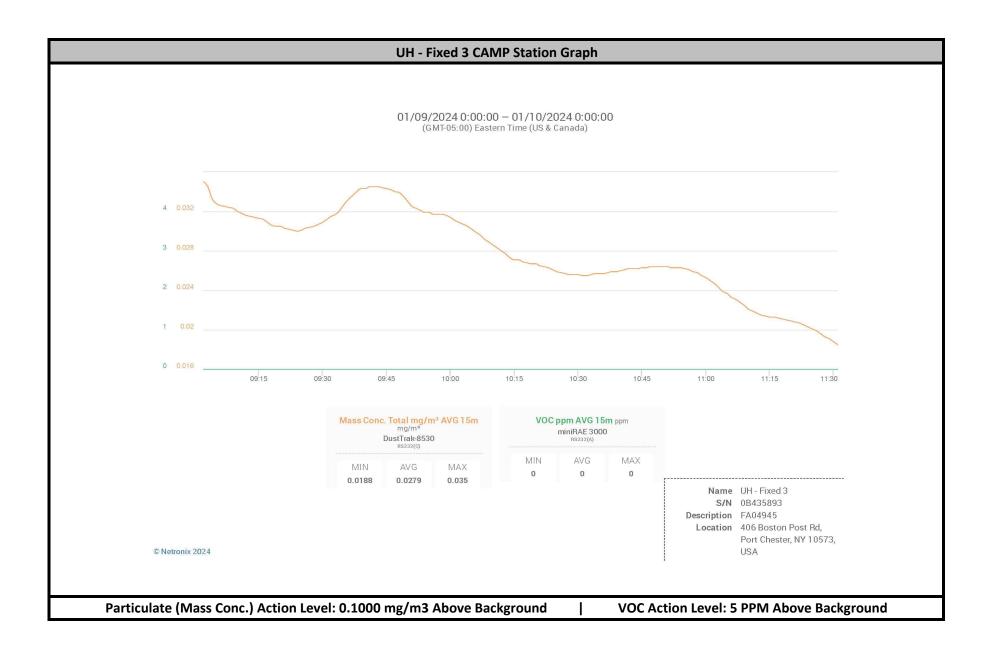

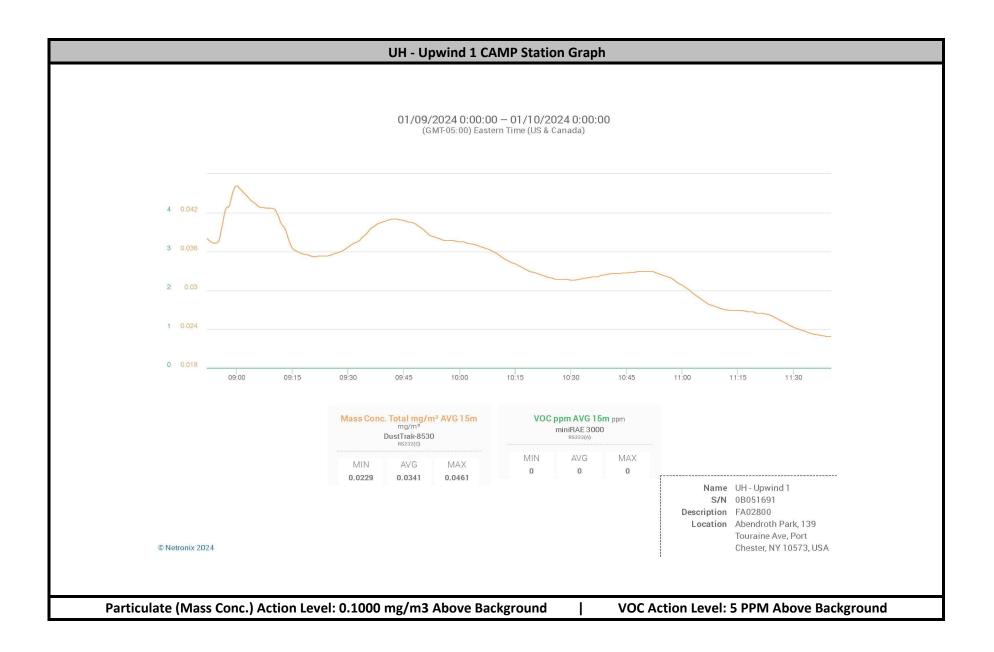

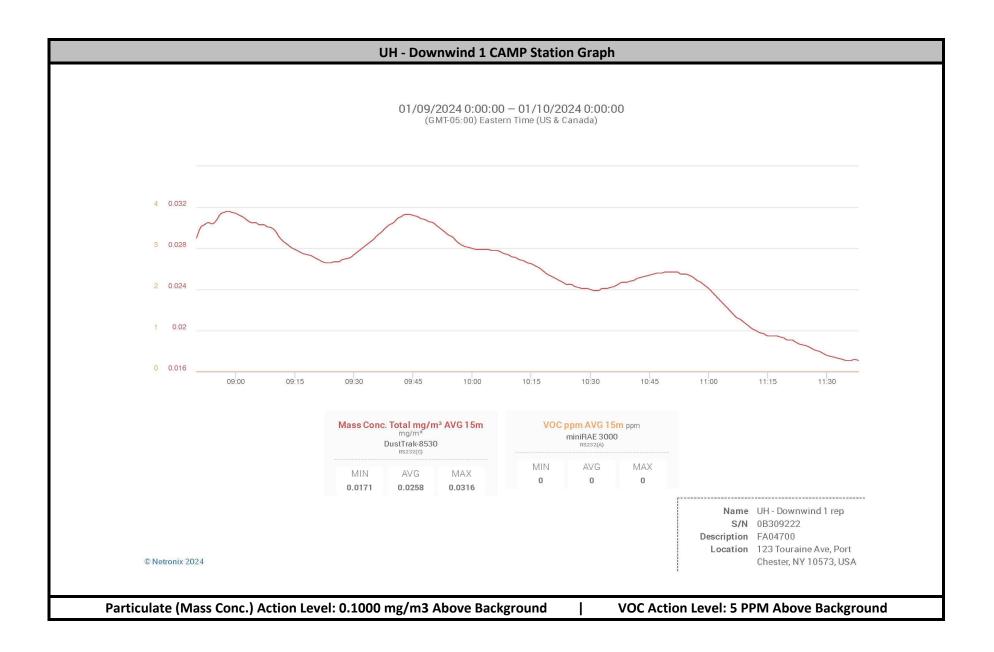

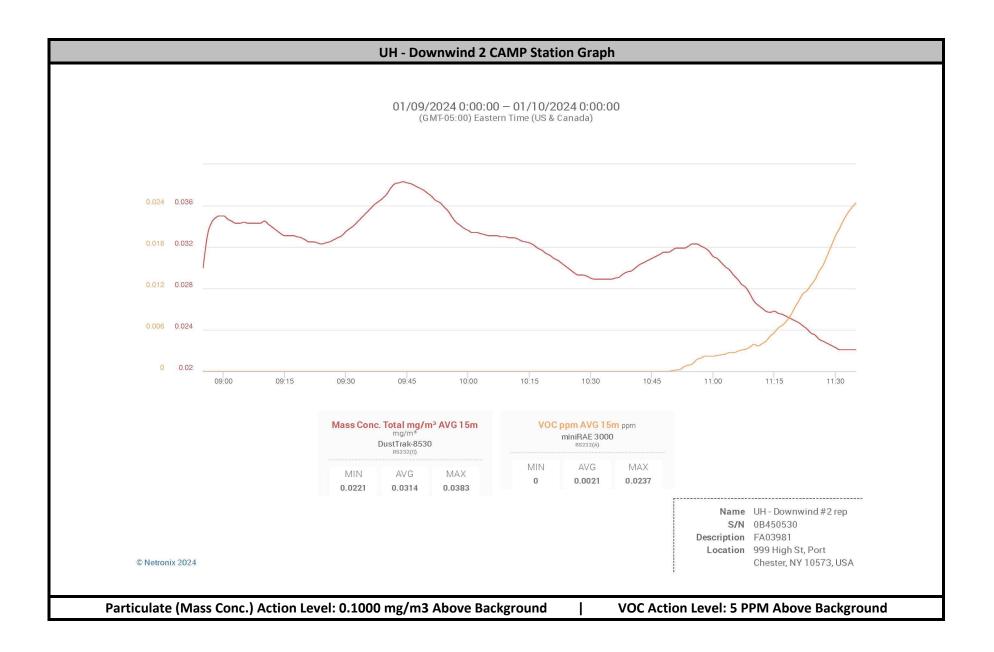

	Daily Activity Report								
PAK	(RF	Former United Hospital							
	MU	Port Chester, NY BCP No. C360202							
			Genera	Site Information					
Date: Weather:					Wednesday, Janu Partly Cloudy				
Wind Direction/Speed		West @ 5 mph							
AKRF Personnel on Sit AKRF Equipment on Si		3 Eived CAN	1D Stations (DID & Du	et Monitor) 3 Porta	Michael I		One Handheld DID	One Handheld Dust Monitor	
Visitors:	te.	3 FIXEU CAIV	IF Stations (FID & Dt	ist Monitor), 3 Porta	None None		, One Handheld FID,	One Handheid Dust Monitor	
		_		ctor Information					
	Contracting Company Tony Casale Inc.	Key Personnel				<b>Equipment</b> Various excavation and grading equipment			
(1	Excavation Contractor)	Rigo Diaz				(e.g., excavators, compactors, roller-compactor, etc.)			
	apital Industries Corp. Demolition Contractor)		Joe Cia	nciulli		Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)			
·		De	escription and Locati	on of Work Activitie	s Performed	(1871			
The excavation contra	ctor began demolition and off-site disposal								
			Site Soil Dispo	sal Tracking Informa	ition				
Destination Facility		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards	
Not Applicable (N/A)		N/A		N/A		N/A		N/A	
		Daily Import (CY)		0		Total Import (CY)		0	
			Imported Fi	ll Tracking Informati	on				
Origin Facility		Daily Trucks		Daily Approx. Cubic Yds.	Total Approx. Cubic Yds.	Total Site Loads		Total Approximate Cubic Yards	
Not Applicable (N/A)		N/A		N/A		N/A		N/A	
		Daily Import (CY)		0		Total Import (CY)		0	
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2	
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	
VOC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No	
Particulate Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No	
			Additi	onal Information					
Planned Work Activity for Following		molition contractor will resume sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.							
Day(s):	The excavation contratcor will continue asphalt reomval, and begin excavation in the antennae COU area.								
Comments:	Negative particulate concentrations were station was fully operational by 13:55. No particulate concentrations.								

1 of 64 C360202\_Daily Report\_2023.01.1

### Photograph 1 Removal of asphalt in the antennae change of se area, view facing east.




## Photograph 2 Loading asphalt from the antennae change of use area for off-site disposal, view facing northeast.





# Photograph 3 Perimeter CAMP monitoring during asphalt demoltion in the antennae change of use area, view facing south.




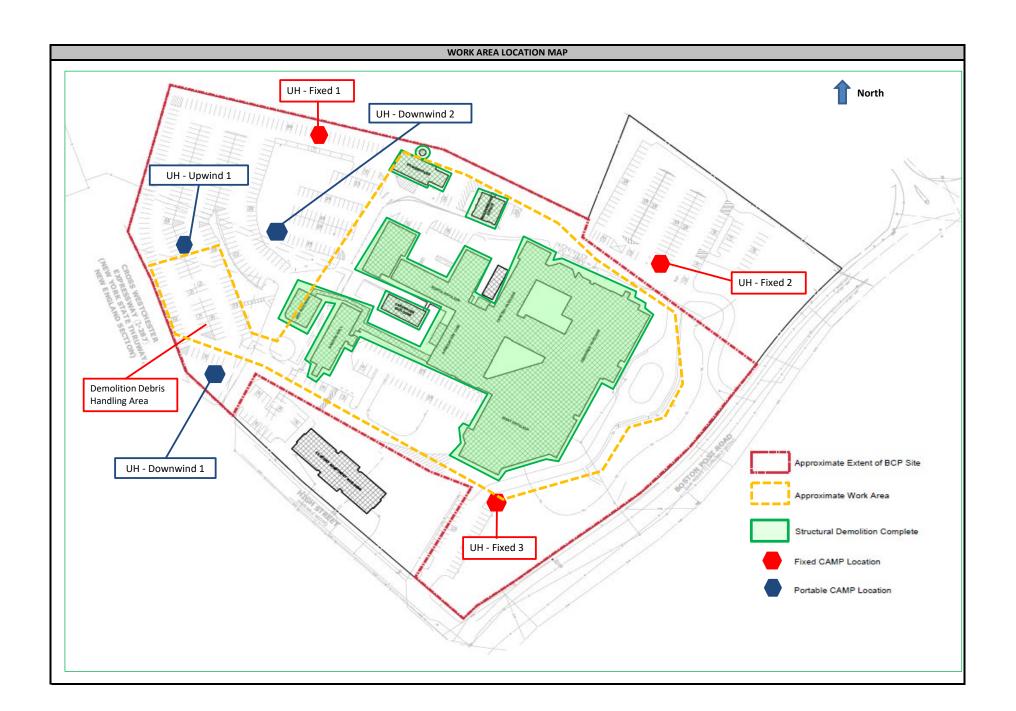



### **Roving CAMP Log** Air Monitoring Log Client: BR RA Port Chester Date: 1/10/29 Former United Hospital (BCP Site No. C360202) Work Activity: Survey points in COU Area of hotspot loc. Ware ontop of asphant bosin asphant numerial from coulana Logged By: M. L. 1-Job No: 200057 Weather: 30 - 42 % Partly Cloudy Wind Direction: West Wind Speed: Smph DUST COMMENTS TIME LOCATION PID ODORS (activity; work zone, upwind or downwind) (mg/m<sup>3</sup>) ND UW 005 0800 Beinground DW 009 ND 0830 uns ND 006 0900 NB OW 0930 007 004 NO 1000 un NO 1030 DW 1100 un ND 1130 DN ND 1200 WW 100 1230 ON 1300 nw 0 004 MI 1380 OW ND 1300 ww 005 ND 1430 DW 003 ND WW 1800 .003 ND Community (Perimeter) Action Levels DUST <0.15 mg/m³ above background i breathing zone: Level D, DModified, or C (subject to PID) PID DUST >25 ppm above background: STOP >0.15 mg/m³ above background: STOP

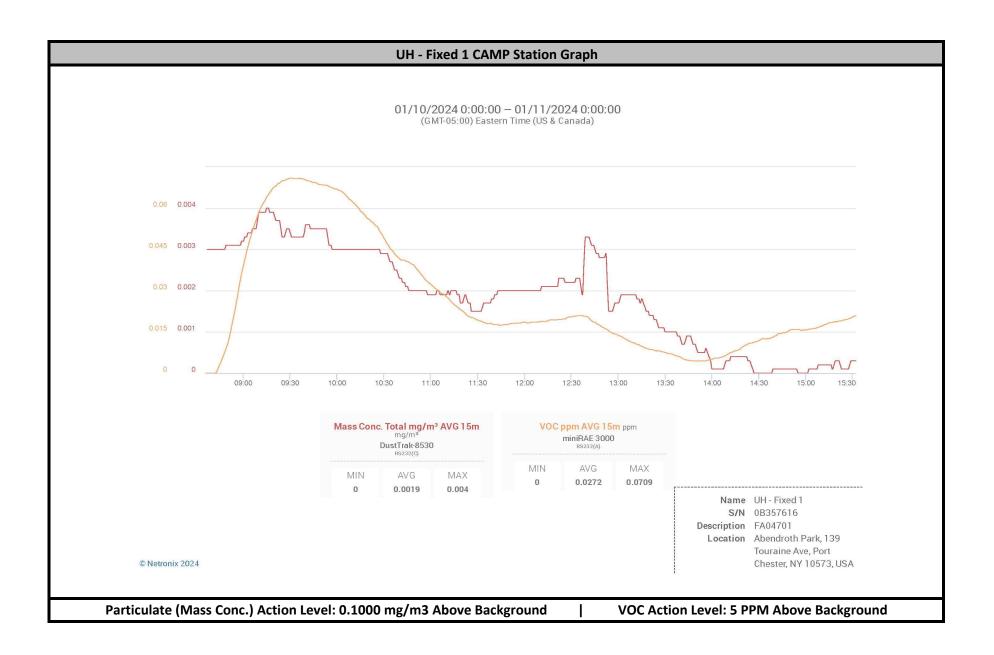


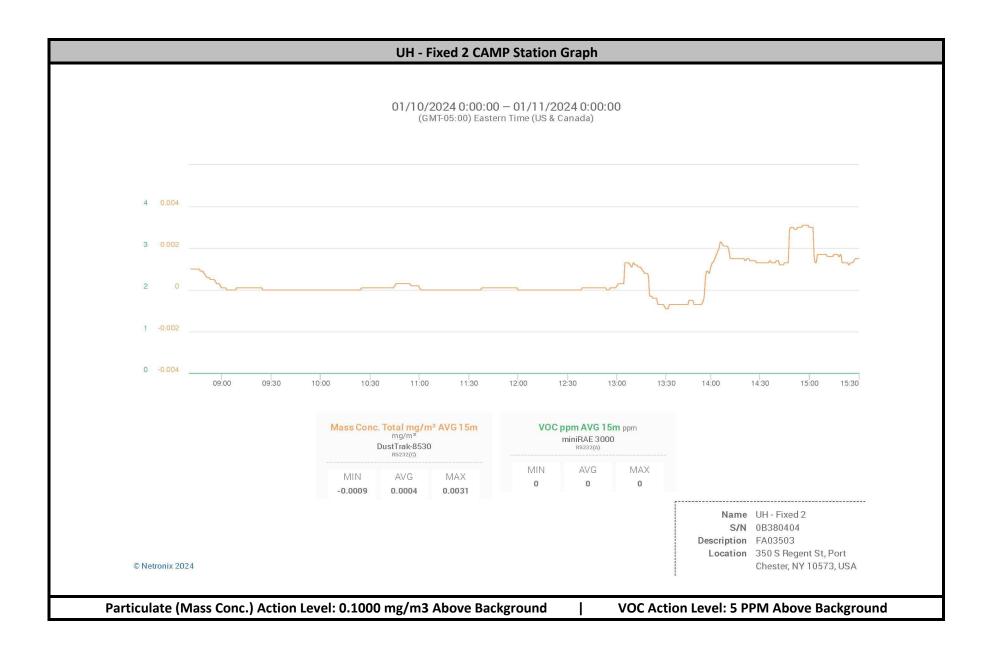

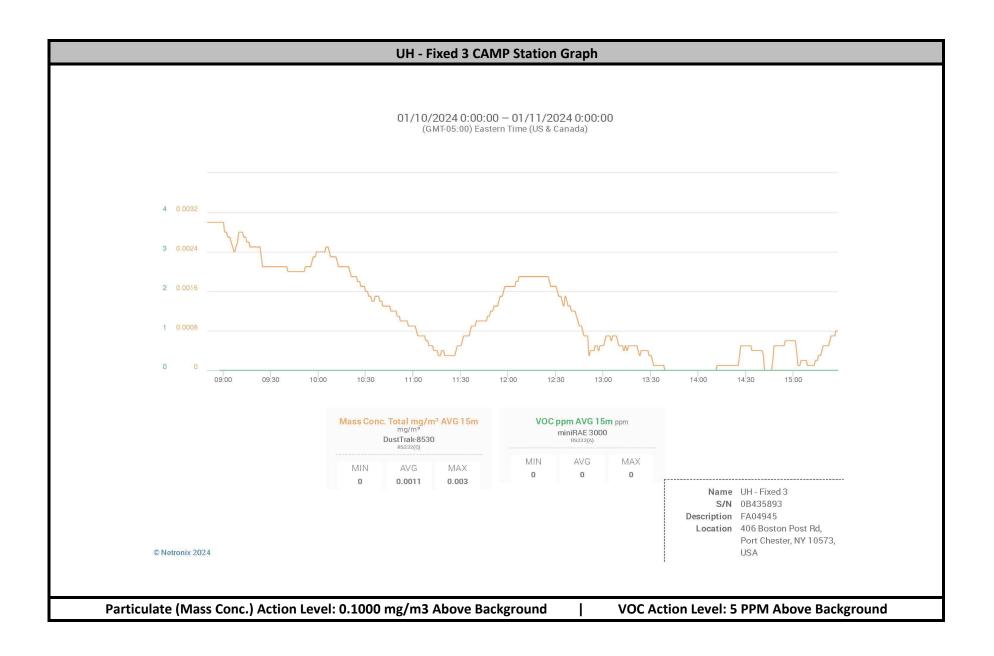

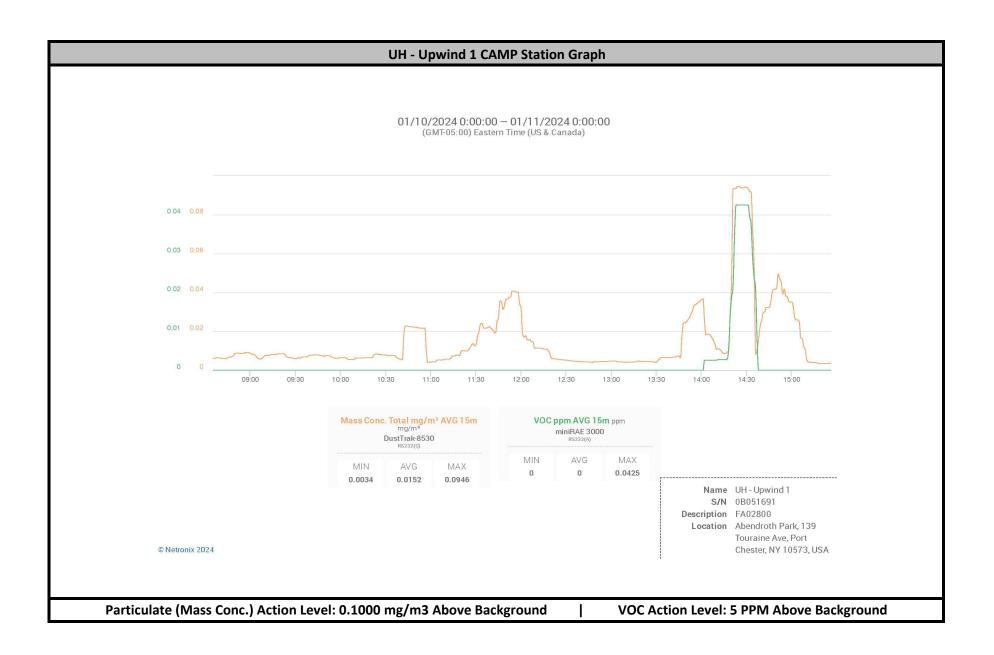

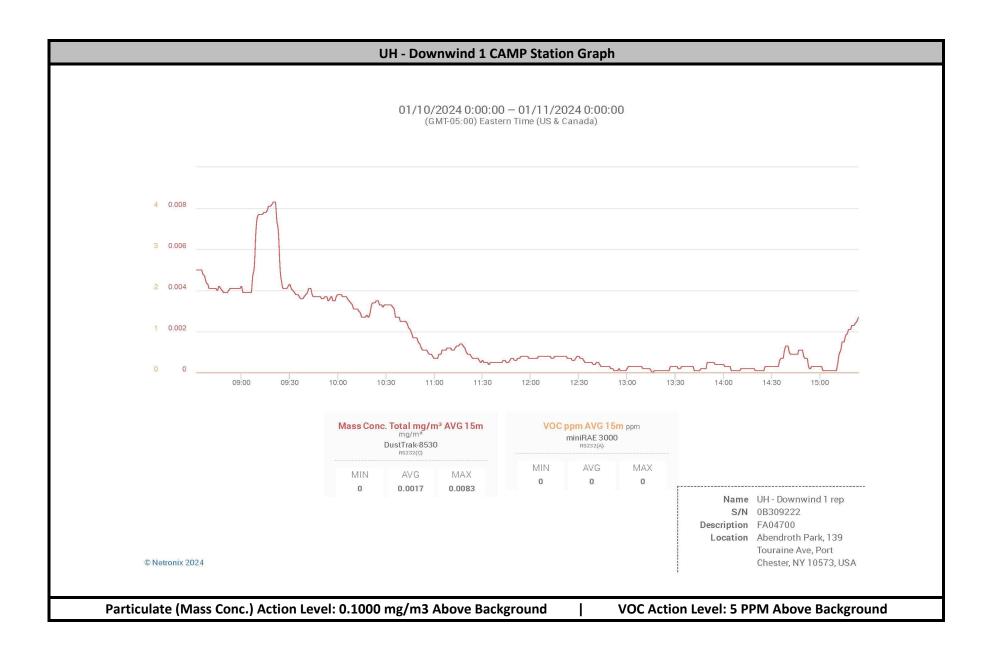

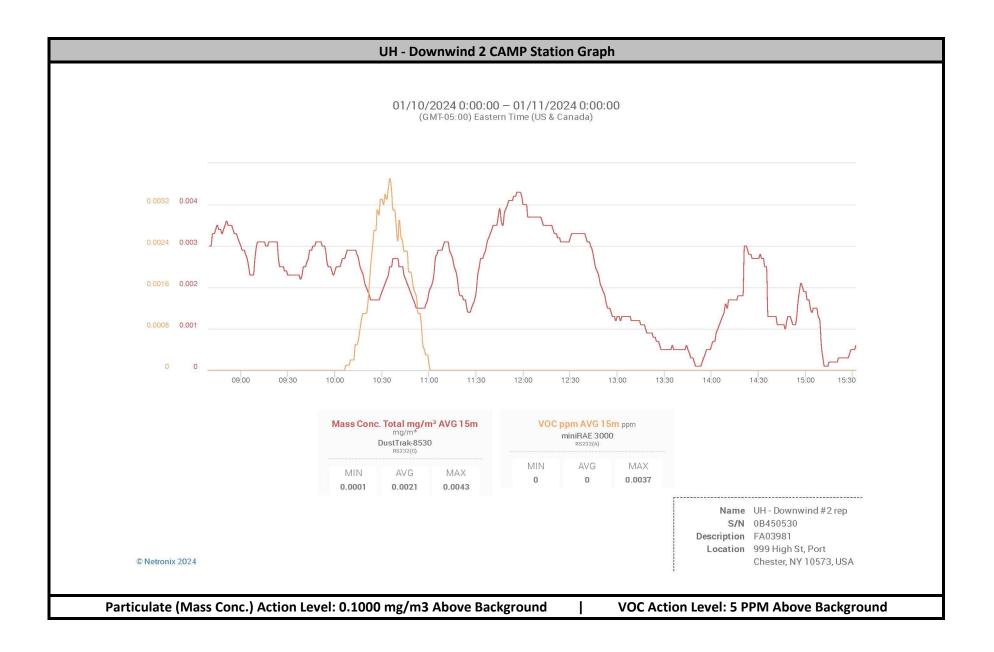

<b>A 17</b> T	Daily Activity Report									
PAKI	<b>(</b>		Former United Hospital Port Chester, NY							
BCP No. C360202  General Site Information										
Date:		Thursday, January 11, 2024 Partly Cloudy, 28 - 45°F								
Weather: Wind Direction/Speed:	nd Direction/Speed: NW @ 7 mph									
AKRF Personnel on Site: Michael Iodice  AKRF Equipment on Site: 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld						One Handheld Dust Monitor				
Visitors:		3 TIXEU CAIV	·		None None		, One Handheid Fib,	One Handheld Dust Worldon		
Contractor Information  Contracting Company Key Personnel Equipment										
Ton	ny Casale Inc.	Rego Diaz				Various excavation and grading equipment				
(Excava					(e.g., excavators, compactors, roller-compactor, e					
·	Industries Corp. ition Contractor)	Joe Cianciulli				(e.g., excavators, skid steers, roll off containers, etc.)				
		De	scription and Locati	ion of Work Activitie	s Performed					
The excavation contractor co	ontinued demolition and off-site dispo	osal of asphalt within	the antennae Chan	nge of Use (COU) area	э.					
The excavation contractor b	egan excavation (0-2 feet below grade	e) and off-site dispos	al of soil within the a	antennae COU area.						
The demolition contractor co	ontinued sorting and loading demoltic	on debris into contai	ners for off-site disp	osal.						
			Site Soil Dispo	sal Tracking Informa	ation					
Destination Facility		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Clean Earth of Carteret - Carteret, NJ		23		460		23		460		
		Daily Export (CY)		460		Total Export (CY)		460		
			Imported Fi	ll Tracking Informati	on					
Or	rigin Facility	Daily Trucks		Daily Approx. Cubic Yds.	Total Approx. Cubic Yds.	Total Site Loads		Total Approximate Cubic Yards		
Not Applicable (N/A)		N/A		N/A		N/A		N/A		
		Daily Import (CY)		0		Total Import (CY)		0		
CAMP Information		Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2		
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed		
VOC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
Particulate Action Level Exceedance(s) Above Background:		No	No	No	No	Yes	No	No		
			Additi	onal Information						
Activity for Following	The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  The excavation contractor will continue asphalt removal, and soil excavation and off-site disposal (0-2 feet below grade) within the antennae COU area.									
	Particulate levels exceeding the CAMP criteria of >0.100 mg/m3 above background were detected at the UH - Upwind 1 CAMP Station from approximately 08:20 to 08:26 due to an instantaneous spike that occurred when a nearby truck was unloading stone building elements adjacent to the CAMP equipment (unrelated to excavation work); the condition was resolved by 08:27.									

1 of 75 C360202\_Daily Report\_2023.01.11

Photograph 1 - Soil excavation and export (0-2ft) within the antennae COU area for off-site disposal, view facing northwest.



### Photograph 2 -


Asphalt demolition and export within the antennae COU area for off-site disposal, view facing west.




### Photograph 3 -


Handling of demolition debris for off-site disposal in the eastern portion of the site, view facing southwest.




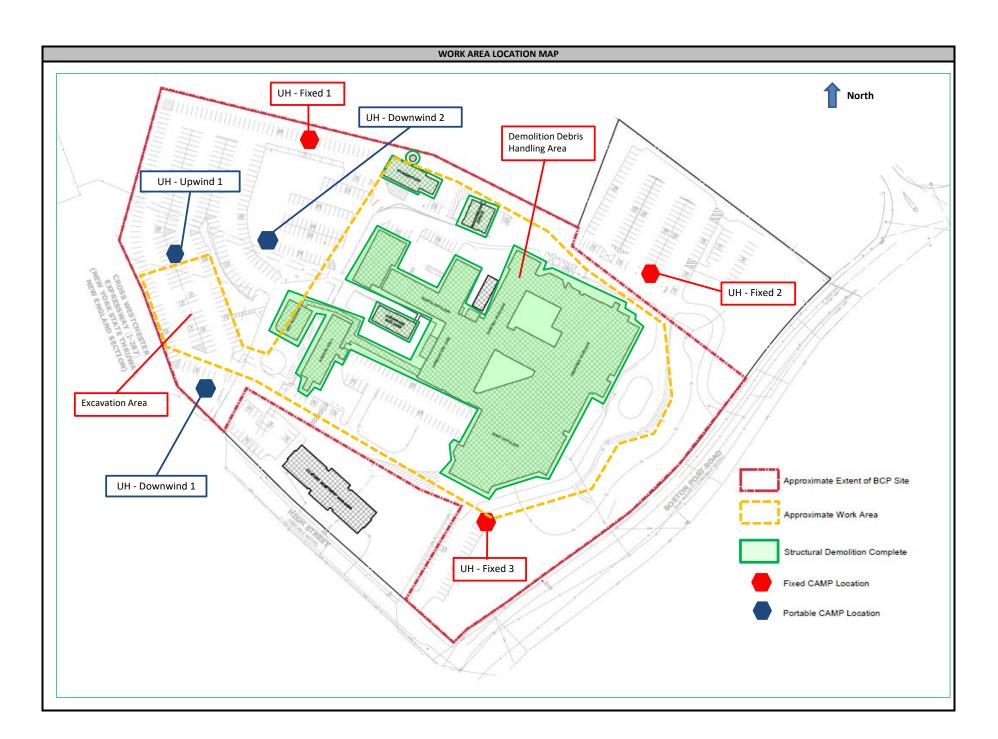



### **Roving CAMP Log** Air Monitoring Log Project: Former United Hospital (BCP Site No. C360202) Client: BR RA Port Chester Work Activity: int handling it dumo debris for disposal excavation of asphanist 2 2pt bgs if soil from county export of it for disposal Date: 1 11 24 Logged By: MJali Job No: 200057 1: NW Wind S Party Cloudy 28-45°F Weather: Wind Direction: Wind Speed: 7mph DUST TIME LOCATION PID COMMENTS ODORS (mg/m³) (activity; work zone, upwind or downwind) 0700 ww ND 0.009 Back grown DW 0780 0.012 OU ww 0800 0013 ND 0830 DW 0 0.006 ND 0900 w 0.005 0 ND 0980 OW 0.011 NA 1000 NW 0.0 0.009 ND DW 1030 0.010 0. ND 1100 WW 0.004 ack 1130 DW 0.0 ND 0.007 noo WW 00 0.008 ND 7.0 1280 DW 0.010 ND 1300 WW 0.0 0.010 DN 0.012 1330 DW 0.0 ND 1400 WW 00 0.007 ND DN 1480 0.009 ND 1500 WW 0.0 0.011 ND DW 0.008 1530 ND Work Zone Action Levels PID DUST <5 ppm: Level D on the standard of t nunity (Perimeter) Action Levels PID DUST >5 ppm above background: vapor >0.1 mg/m<sup>3</sup> above background: dust su >0.15 mg/m³ above background: STOP >25 ppm above background: STOP >0.15 mg/m³ above background in breathing zone: dust suppression, stop work if conditions continue

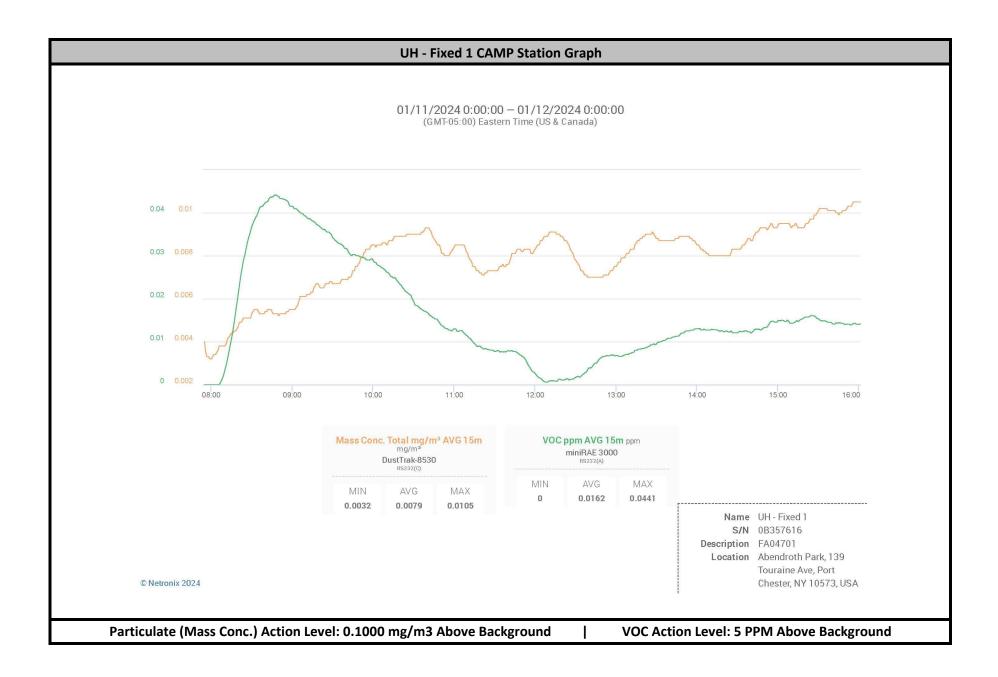


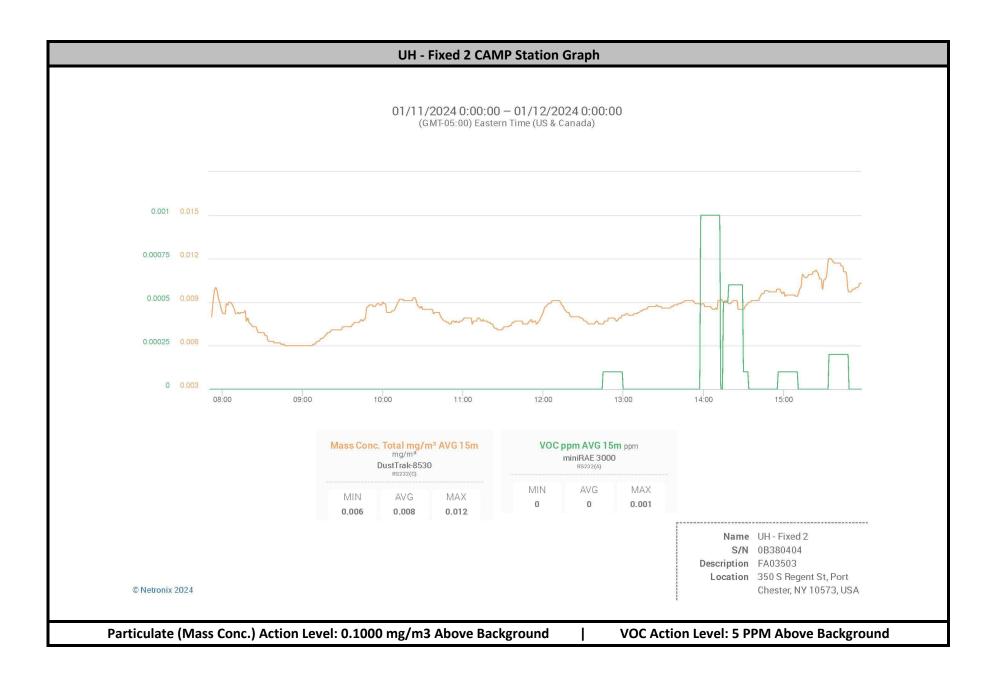

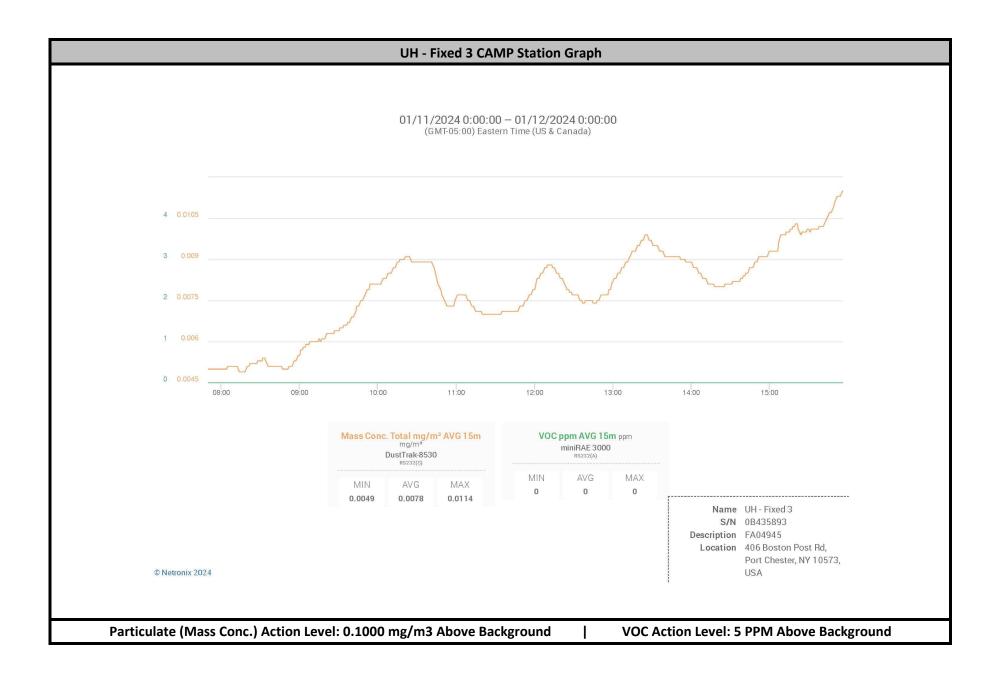

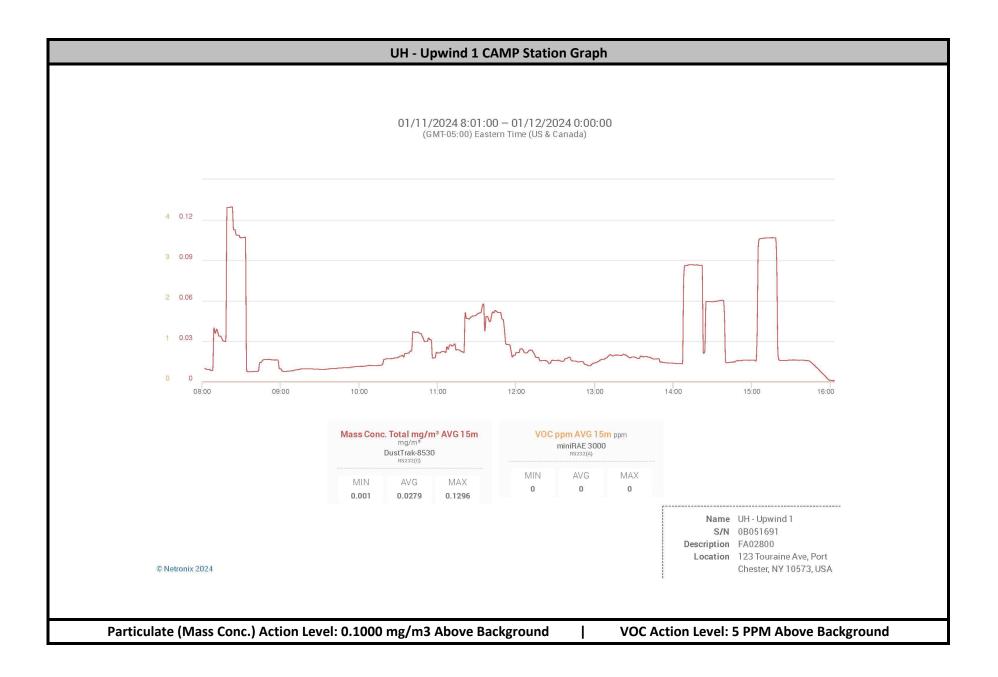

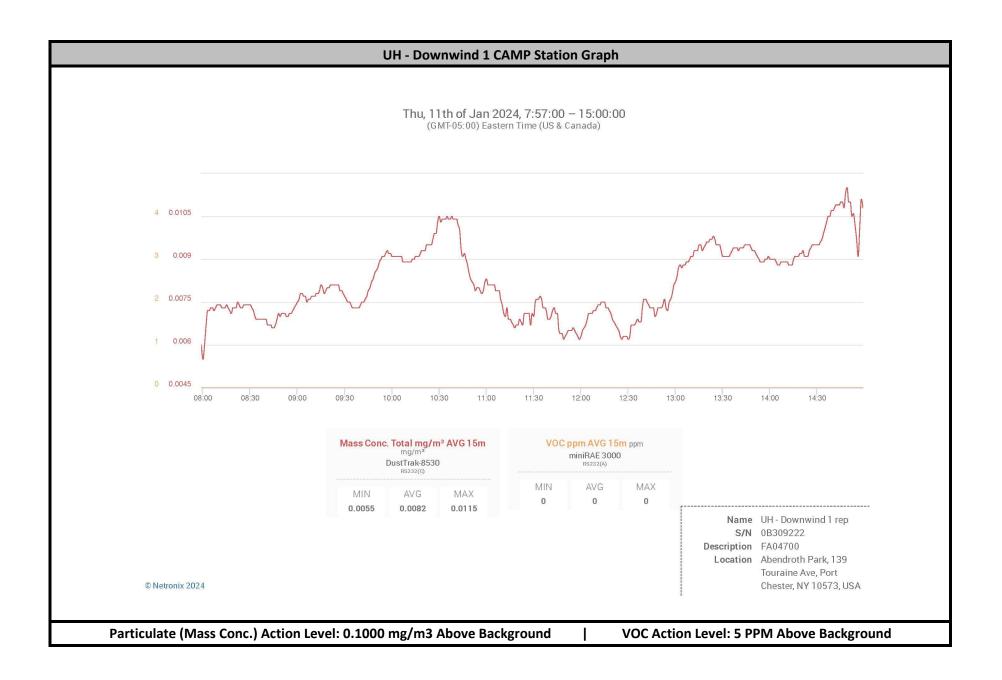

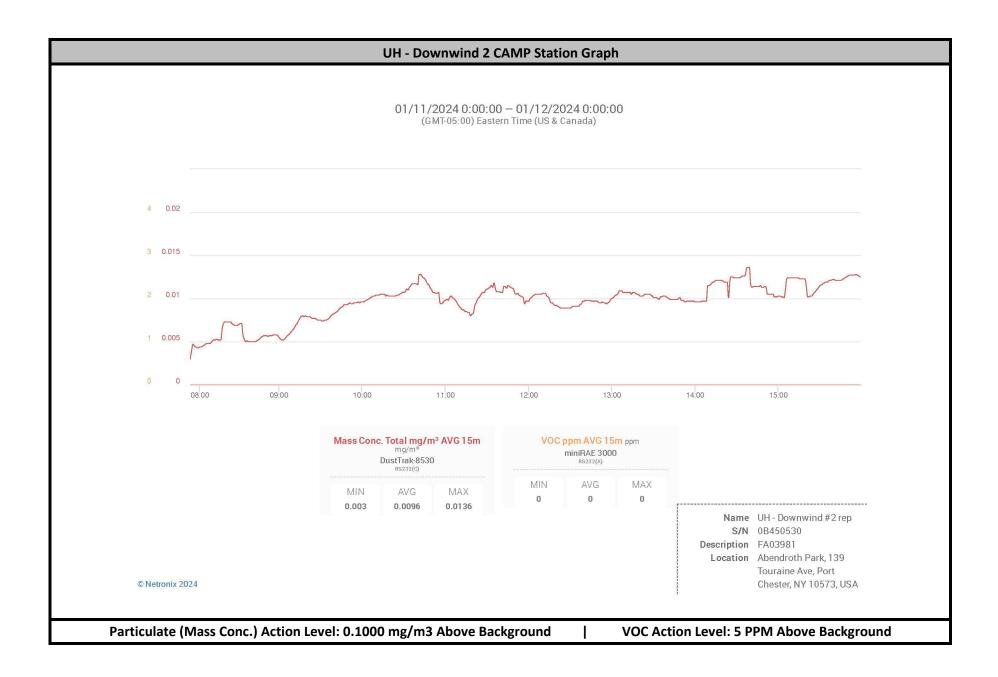

	Daily Activity Report								
<b>PAK</b> RF				Former Unite					
Port Chester, NY BCP No. C360202									
	General Site Information								
Date: Weather:	Friday, January 12, 2024								
Wind Direction/Speed:	Partly Cloudy, 31 - 40°F WNW @ 9 mph								
AKRF Personnel on Site: AKRF Equipment on Site:	Michael Iodice								
Visitors:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor  None.								
	Contractor Information  You Personnel  Fourinment								
Contracting Company  Tony Casale Inc.	Key Personnel     Equipment       Various excavation and grading equipment								
(Excavation Contractor)		Rigo	Rigo Diaz (e.g., excavators, compactors, roller-compact						
Capital Industries Corp.		Joe Cianciulli Various demolition							
(Demolition Contractor)	(e.g., excavators, skid steers, roll off containers, etc.)								
	D	escription and Locat	ion of Work Activitie	s Performed					
The excavation contractor continued demolition and off-site disp	osal of asphalt within	n the antennae Char	nge of Use (COU) are	а.					
The excavation contractor continued excavation (0-2 feet below	grade) and off-site di	isposal of soil within	the antennae COU a	ea to Clean Earth of	Carteret, NJ.				
The demolition contractor continued sorting and loading demolt	ion debris into conta	iners for off-site disp	osal.						
		Site Soil Dispo	osal Tracking Inform	ation					
Destination Facility	Daily	Trucks	Daily Approx	Cubic Vdc	Total Site Leads		Total Annuavimenta Cubia Vanda		
Destination Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Clean Earth of Carteret - Carteret, NJ	8		160		31		620		
	Daily Export (CY)		160		Total Export (CY)		620		
					. Star Export (CT)		020		
		Imported Fi	III Tracking Informati	on					
Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Tilcon West Nyack Quarry - West Nyack, NY	1		20		1		20		
(ITEM #4)									
Tilcon West Nyack Quarry - West Nyack, NY									
(NY2/ASTM #5 - 3/4" Stone)	1		20		1		20		
		Daily Import (CY)	4	0		Total Import (CY)	40		
CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2		
Odors:	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed		
VOC Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No		
Particulate Action Level Exceedance(s) Above Background:	No	No	No	No	Yes	No	No		
	1	Additi	ional Information			1			
The demolition contractor will continue so	orting and loading of	demolition debris fro	om the former hospit	al buildings into cor	tainers for off-site d	isposal.			
Activity for Following									
Day(s).						na endpoint samples	will be collected. The excavation		
contractor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill									
Particulate levels exceeding the CANAR and	eria of >0 100 mg/	R ahove background	were detected at th	a IIH - Unwind 1 CA	MP Station from ann	rovimately 00-10 +- 4	18:32 due to an instantaneous sails		
Particulate levels exceeding the CAMP criteria of >0.100 mg/m3 above background were detected at the UH - Upwind 1 CAMP Station from approximately 08:18 to 08:32 due to an instantaneous stated that occurred when a nearby truck was unloading large limestone building elements adjacent to the CAMP equipment (unrelated to excavation work); the condition was resolved by 08:33.									

1 of 78 C360202\_Daily Report\_2024.01.12

## **Site Photographs**

Photograph 1 - Soil excavation (0-2ft) and export within the antennae COU area for off-site disposal, view facing west.





Photograph 2 -Import of Item #4 for use in the antennae COU area, view facing west.





Photograph 3 Handling of
demolition debris for
disposal in the
eastern portion of
the site, view facing
southeast.




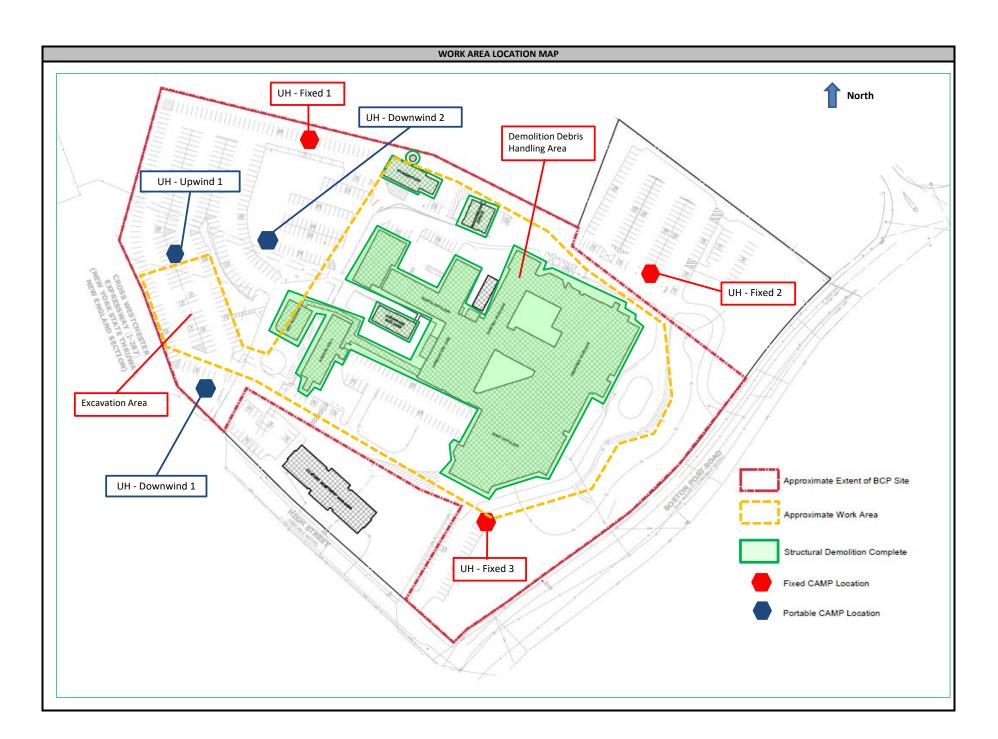


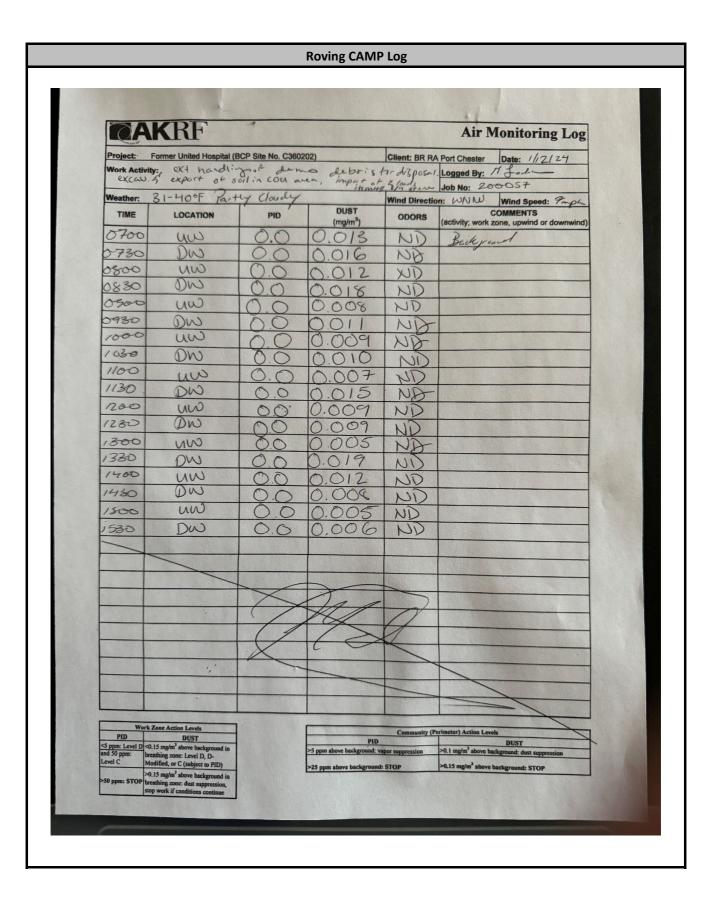


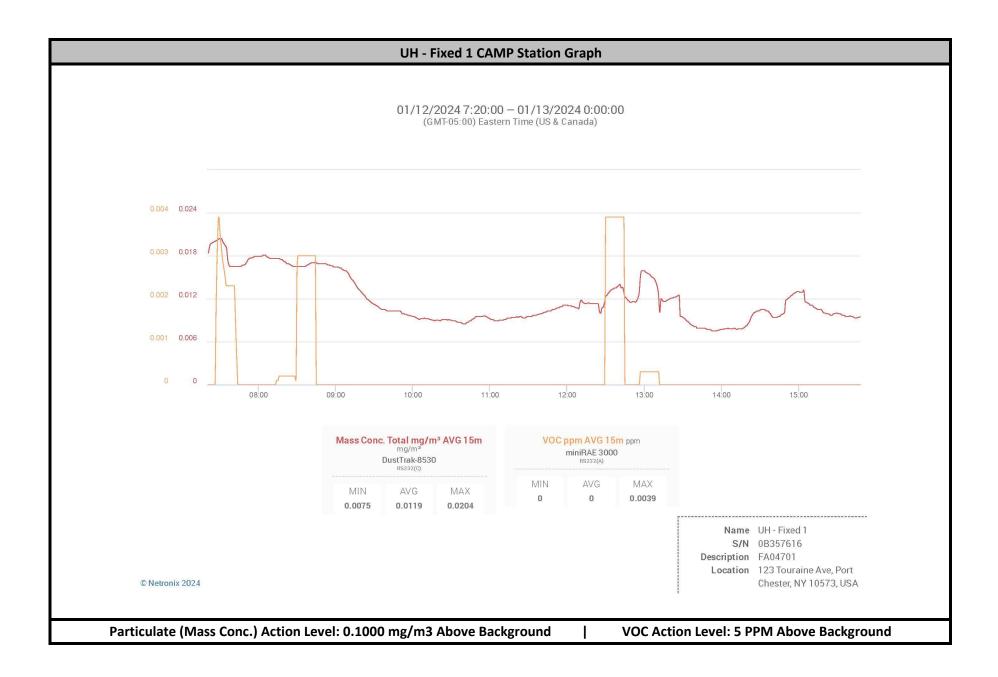


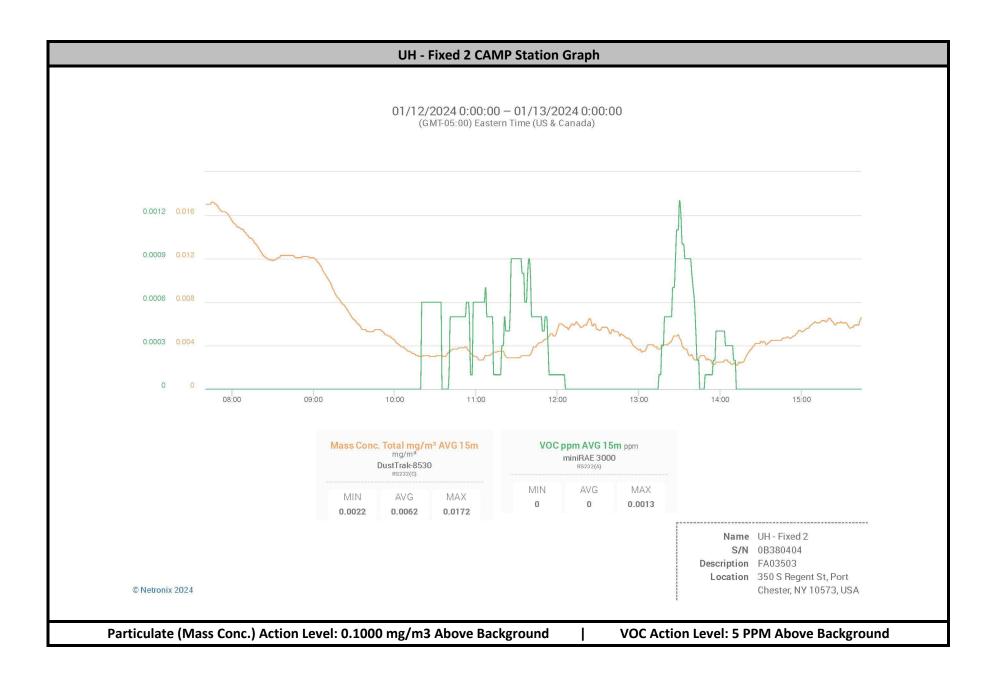

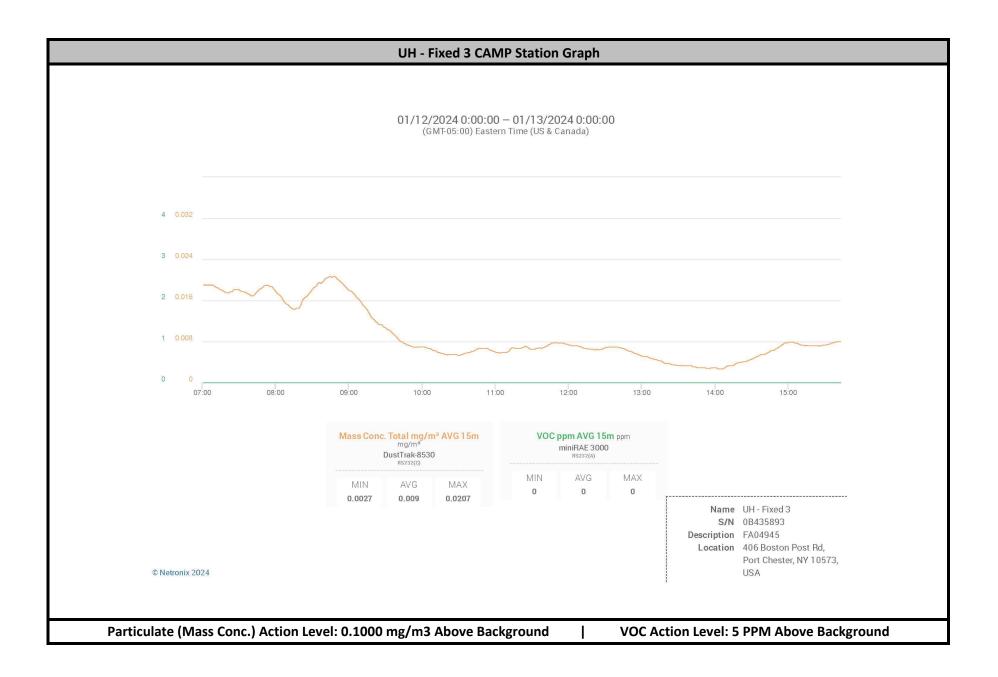

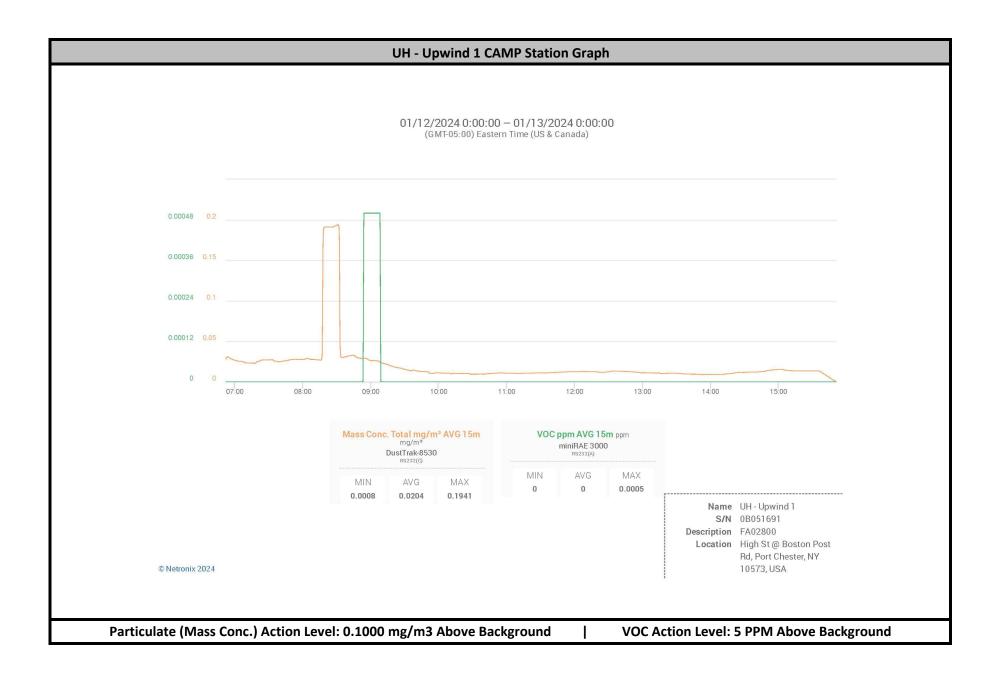

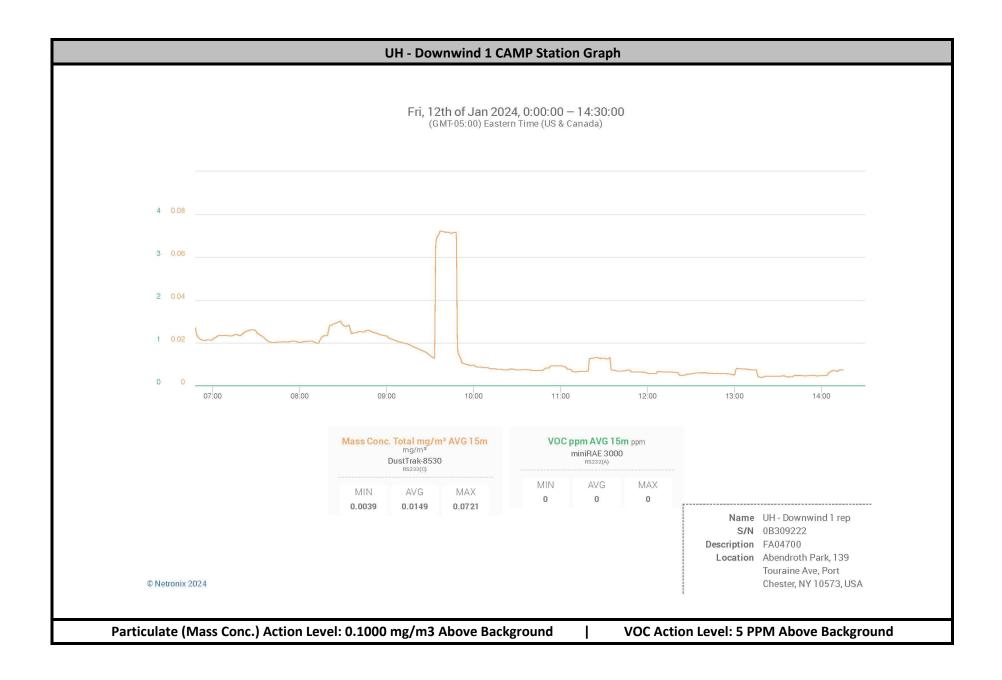

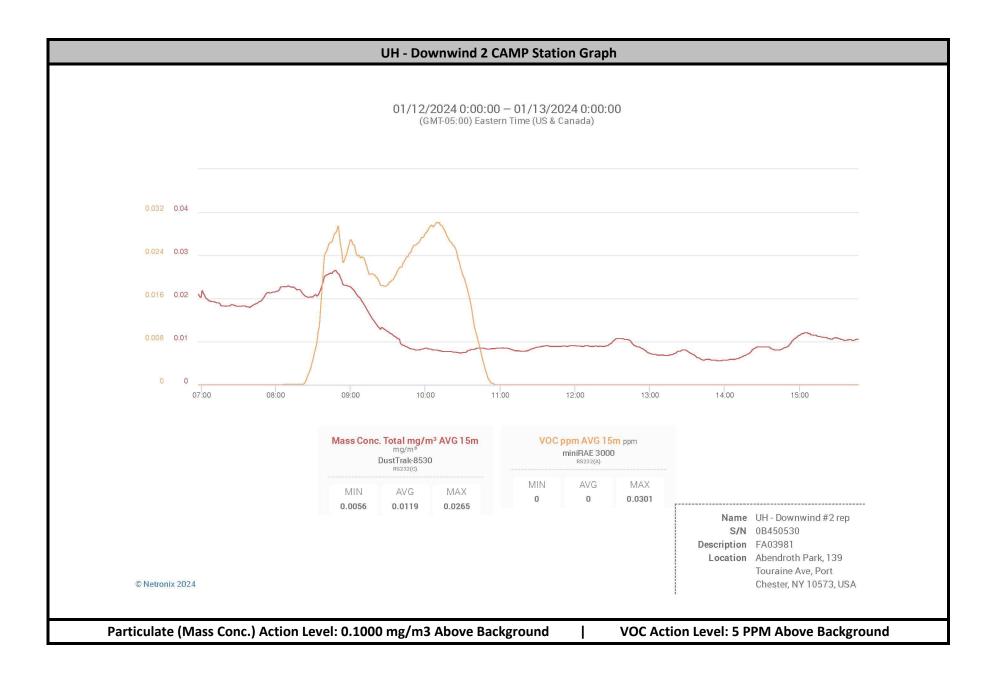

	Daily Activity Report								
<b>PAK</b> RF	Former United Hospital Port Chester, NY BCP No. C360202								
Date	General Site Information								
Date: Weather:	Monday, January 15, 2024  Partly Cloudy, ~30°F								
Wind Direction/Speed: AKRF Personnel on Site:	W @ 7 mph Stephen Schmid								
AKRF Equipment on Site:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor								
rs: None.  Contractor Information									
Contracting Company	Key Personnel Equipment								
Tony Casale Inc.	Rigo Diaz				Various excavation and grading equipment				
(Excavation Contractor)	-			(e.g., excavators, compactors, roller-compactor, etc.)  Various demolition equipment					
Capital Industries Corp. (Demolition Contractor)	Joe Cianciulli				(e.g., excavators, skid steers, roll off containers, etc.)				
	D	escription and Locat	ion of Work Activitie	es Performed					
The excavation contractor excavated 10x10 foot hot spots RI-SB Clean Earth of Carteret, NJ.	-53 and RI-SB-54 to a	final depth of 6 feet	below grade within t	he antennae Chang	e of Usea (COU) area	a. The soil generated	was exported for off-site disposal a		
AKRF collected one (1) endpoint sample at the base of each hot hold.	spot excavation (6 fee	et below grade) to be	e analyzed for TAL me	etals. Additional con	tingency samples we	ere collected at 7 and	8 feet below grade and placed on		
The excavation contractor imported Item #4 from Tilcon of Wes	t Nyack, NY and used	this material as back	fill within the 2-foot	cut of the antennae	COU area, after plac	ing a demarcation la	yer.		
		Site Soil Dispo	osal Tracking Informa	ation					
Destination Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Clean Earth of Carteret - Carteret, NJ	3		60		34		680		
	Daily Export (CY)		60		Total Export (CY)		680		
		Imported Fi	ill Tracking Informati	on					
Origin Facility	Daily	Daily Trucks		Daily Approx. Cubic Yds.		te Loads	Total Approximate Cubic Yards		
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)	1	6	38	30	17		400		
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)	1	0	C	)	1		20		
		Daily Import (CY)	38	30		Total Import (CY)	420		
CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2		
Odors:	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed		
VOC Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No		
Particulate Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No		
		Addit	ional Information						
Planned Work  Activity for Following  Day(s):  The demolition contractor will continue so				_			øyer		
Comments: Due to a telemetry issue, VOC data did no	t report from the UH-	Upwind 1 CAMP stat	tion. No VOCs were o	letected in the area	throughout the day	with roving equipme	nt.		

1 of 73 C360202\_Daily Report\_2024.01.15

# **Site Photographs**

Photograph 1 - Soil excavation (2-6ft) within the RI-SB-53 hotspot in the antennae COU area, and export for offsite disposal, view facing north.




Photograph 2 -Import of Item #4 from Tilcon of West Nyack, NY for use in the antennae COU area, view facing west.





Photograph 3 Placement of Item
#4 above a
demarcation layer
within the antennae
COU area, view
facing northeast.




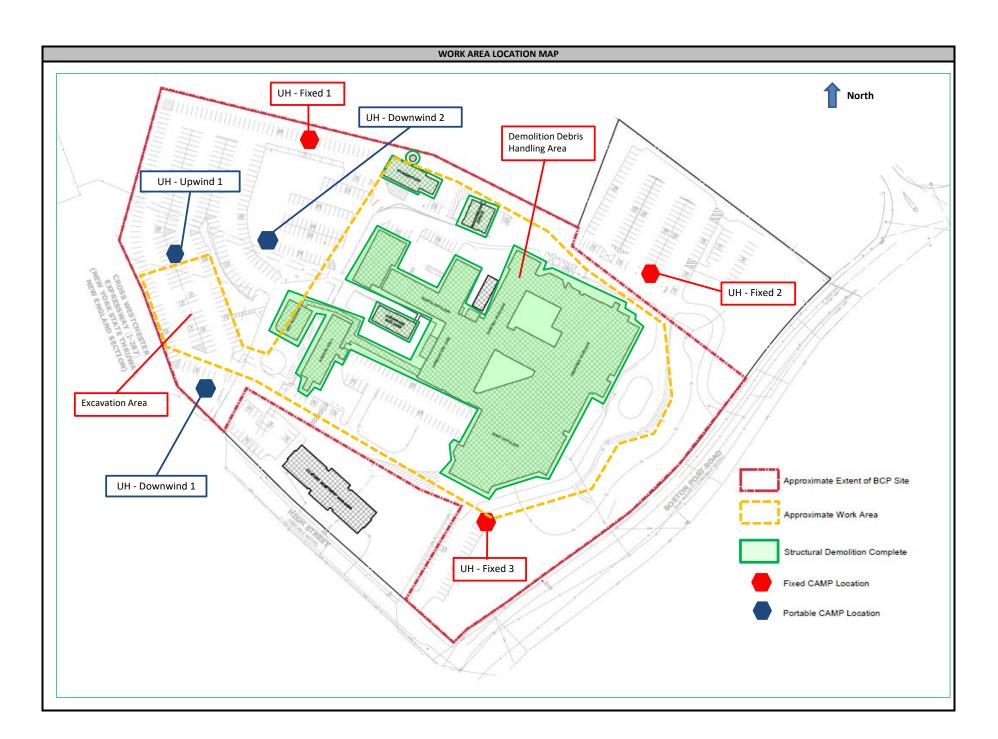



### **Roving CAMP Log** CAKRE Air Monitoring Log Project: Former United Hospital (BCP Site No. C360202) Work Activity: Ocauntum / import respect / dence / backlist / corpete Logged By: Client: BR RA Port Chester Date: 1/15/24 - 30 F Sunny Weather: Job No: 200057 Wind Direction: TIME LOCATION Wind Speed: Toph DUST PID COMMENTS (activity; work zone, upwind or downwind) (mg/m<sup>3</sup>) \$070C Ou 0.0 0.008 More Backgond 0730 DW 0-0 0.012 None 0800 42 prawlyn 0-0 0.021 al Nure 0830 UW 0,0 0,010 None W 0900 Du 0.0 0.016 Nure 4 0930 42 0.0 0,024 Nune V 1000 Cu 0.0 0.011 Nure denur + buckfill 1630 DW 0,0 0.018 None 1100 WZ 0,0 0.017 None 1130 un 0.0 0.011 Muno 1200 Du 0,0 : 0.019 Nice 1230 wz 0.0 0,030 Noe 1300 w 0.0 0,009 None 1330 DW 0.0 0.015 Nune 1400 N2 None 0,0 0,021 1430 CW 0,0 Nine 0,010 1500 Vine DW 0.014 0.6 1530 WZ 0,0 0.026 hon 1, Community (Perimeter) Action Levels DUST Work Zone Action Levels PID >0.1 mg/m<sup>3</sup> above background: dust suppression DUST >5 ppm above background; vapor suppression bm: Level D <0.15 mg/m³ above background breathing zone: Level D, D-Modified, or C (subject to PID) >0.15 mg/m<sup>3</sup> above background: STOP <5 ppm: Lev and 50 ppm: >25 ppm above background: STOP Level C >0.15 mg/m<sup>3</sup> above background in

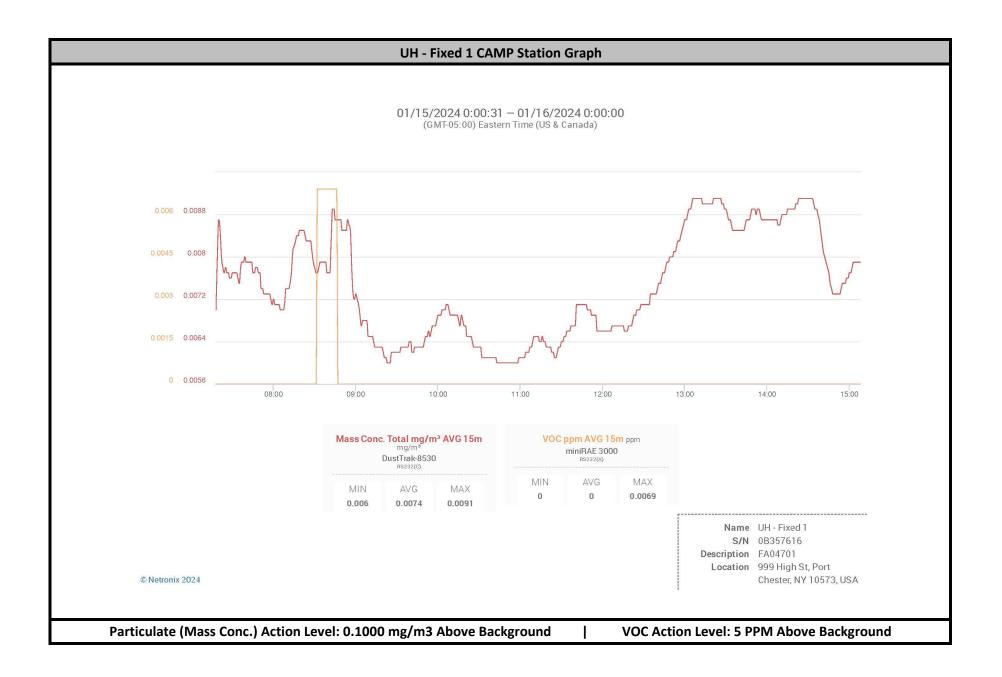


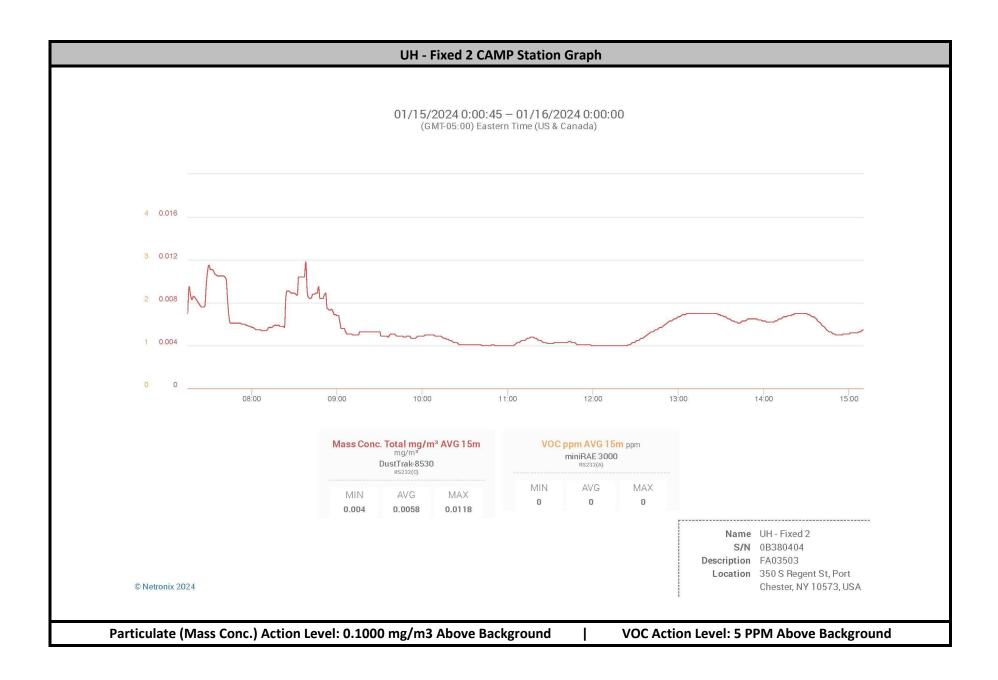

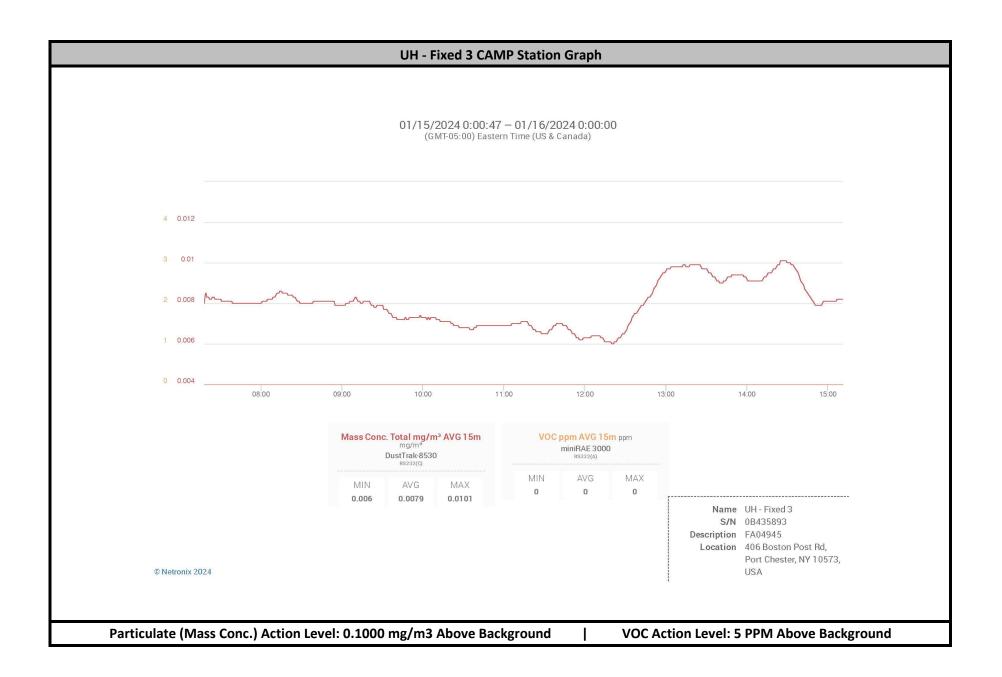

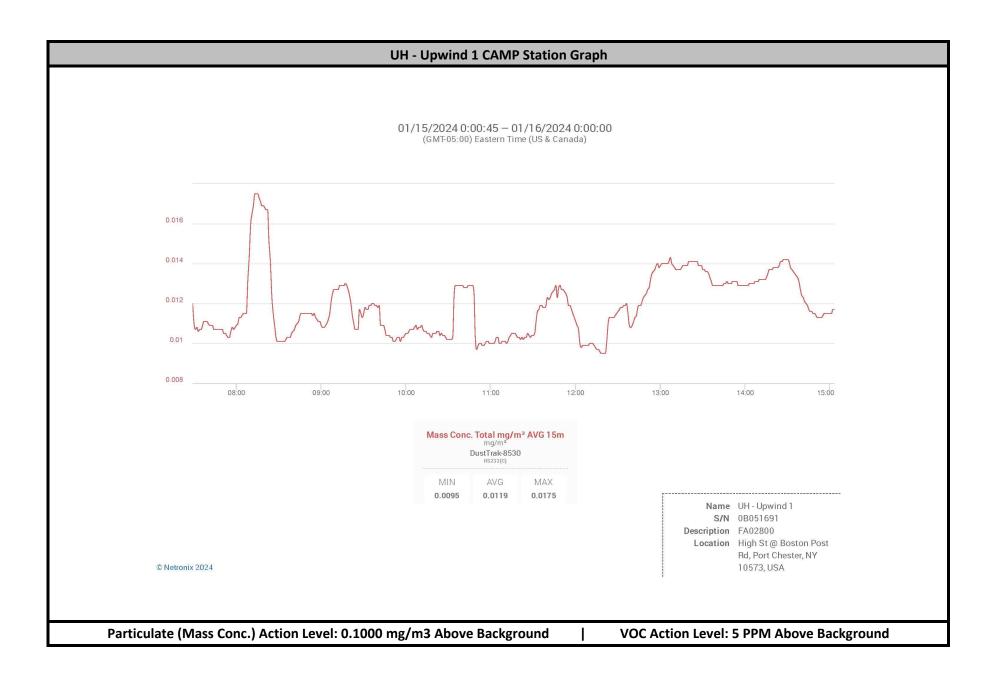

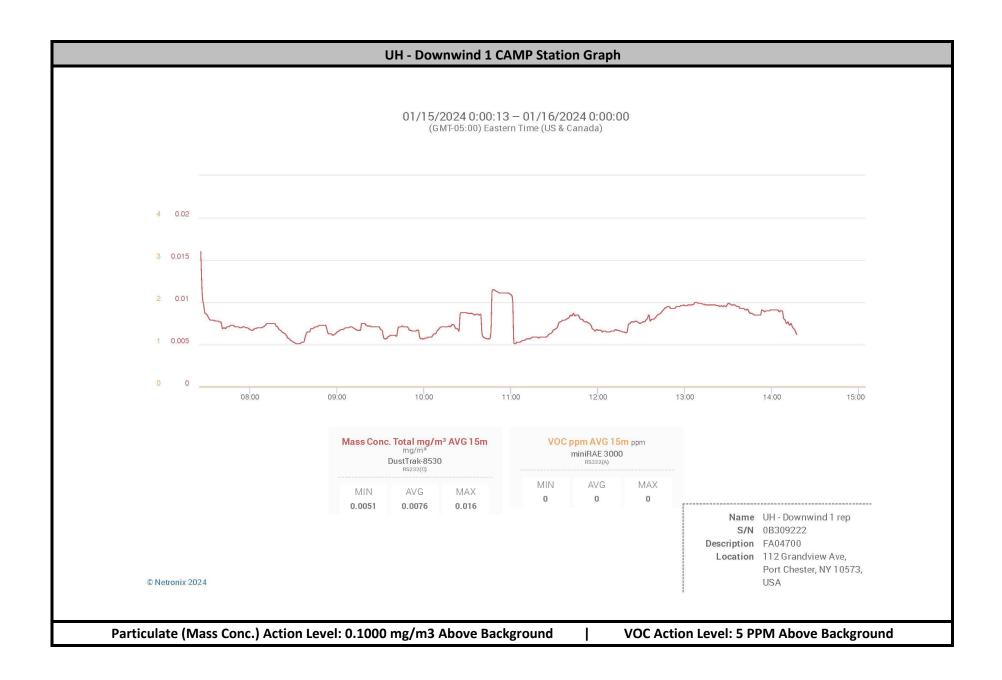

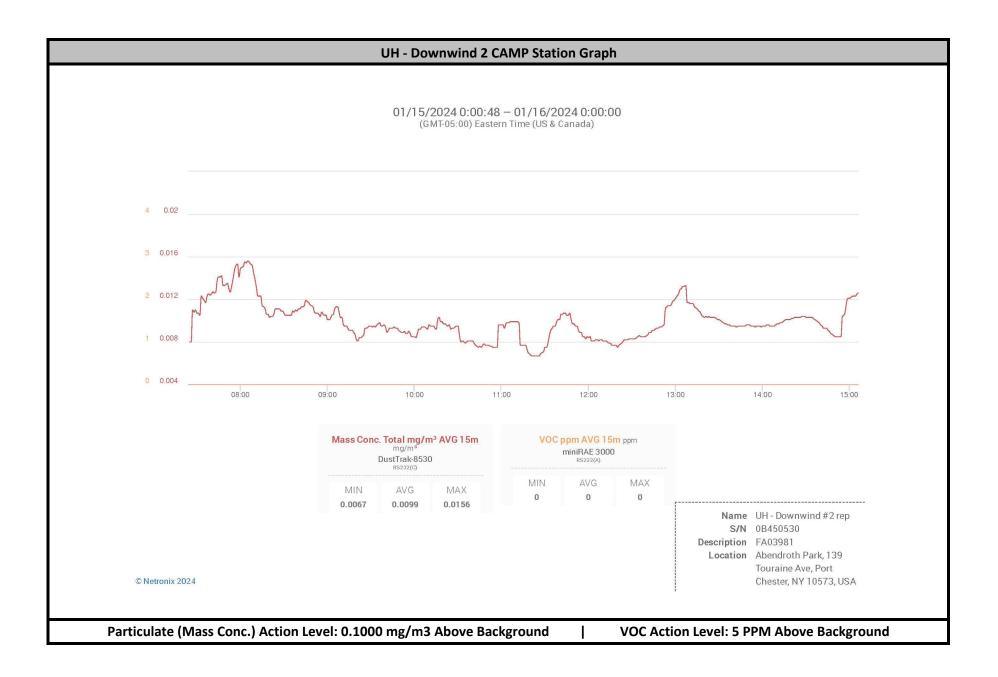

		Daily Activity Report								
PAK	'DL	Daily Activity Report  Former United Hospital								
	MM,	Port Chester, NY								
		BCP No. C360202  General Site Information								
Date:		Wednesday, January 17, 2024								
Weather: Wind Direction/Speed:					Sunny, 16 W @ 7 i					
AKRF Personnel on Site	2:	W @ 7 mpn  Michael Iodice								
AKRF Equipment on Sit	te:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor								
Visitors:		None.  Contractor Information								
C	Contracting Company	Key Personnel Equipment						ent		
(E	Tony Casale Inc. excavation Contractor)	Rigo Diaz			Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.)					
	apital Industries Corp. Jemolition Contractor)	Joe Cianciulli				Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)				
		De	scription and Locati	ion of Work Activitie	s Performed					
The excavation contrac	ctor exported one (1) truckload of soil gene	erated from the ante	nnae Change of Use	area (2-5 feet below	grade) to Clean Eart	th of Carteret, NJ.				
The excavation contrac	ctor began construction of the retaining wa	ll within the antenna	e Change of Use are	a.						
The demolition contrac	ctor continued sorting and loading demoltic	on debris into contain	ners for off-site dispo	osal.						
			Site Seil Diene	and Translaina Informa	. Air					
			Site Soil Dispo	sal Tracking Informa	ition					
	Destination Facility	Daily <sup>·</sup>	Frucks	Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Clean Earth of Carteret	Earth of Carteret - Carteret, NJ		1		20		35	700		
			Daily Export (CY)		20		Total Export (CY)	700		
			Imported Fi	ll Tracking Informati	on					
	Origin Facility	Daily <sup>-</sup>	Daily Trucks Daily Approx. Cubic Yds. Total Site Loads		te Loads	Total Approximate Cubic Yards				
Tilcon West Nyack Qua (ITEM #4)	nrry - West Nyack, NY	0 0		)	17		400			
Tilcon West Nyack Qua (NY2/ASTM #5 - 3/4" S		(	)	C	)	1		20		
			Daily Import (CY)	(	)		Total Import (CY)	420		
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2		
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed		
VOC Action Level Excee	edance(s) Above Background:	No	No	No	No	No	No	No		
Particulate Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
			Additi	onal Information						
Planned Work Activity for Following Day(s):  The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  The excavation contractor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer.										
Comments:	None.									

1 of 59 C360202\_Daily Report\_2024.01.17

# **Site Photographs**

# Photograph 1 Excavation contractor prepping the antennae Change of Use area for installation of the

retaining wall, view facing northwest.



## Photograph 2 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing south.




### Photograph 3 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing southeast.




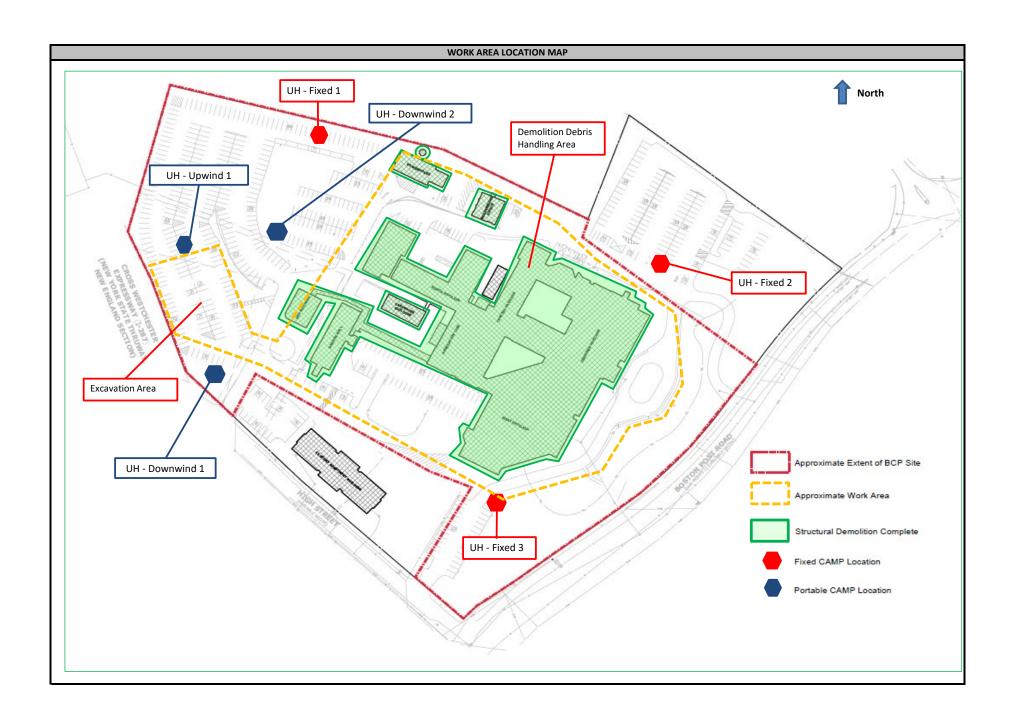



### **Roving CAMP Log** CAKRE Air Monitoring Log Client: BR RA Port Chester Date: 1/17/24 Project: Former United Hospital (BCP Site No. C360202) Work Activity: Pext. handling of durno debris install of retaining wall blacks in COU area Weather: 16-2-1 F Sang Wind Logged By: M. Judic Job No: 200057 Wind Speed: 13 mpk COMMENTS Wind Direction: West DUST TIME LOCATION PID ODORS (activity; work zone, upwind or downwind) (mg/m<sup>3</sup>) 0800 aw 0.013 Buckyowl acy 0830 DIN ND 0900 NW DOCK 017 0930 DW NO 1000 CUN 0.015 ND 1030 DW NA 1100 )9 OUR WW 1130 DW ND un 1200 CIK 1230 WCD NA 1300 UN CUN 1330 DW 0.020 ND 0 1400 CVIV NO 1430 DW 1500 MA 0.01 Community (Perimeter) Action Levels DUST PID >0.1 mg/m3 above background: dust supp >0.15 mg/m³ above background: STOP >25 ppm above background: STOP

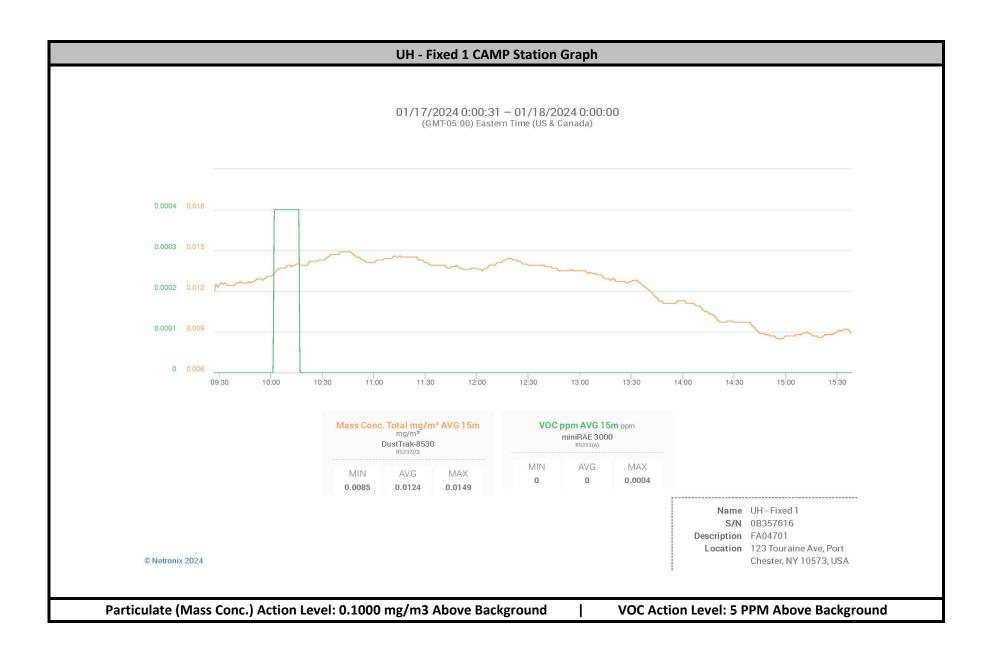


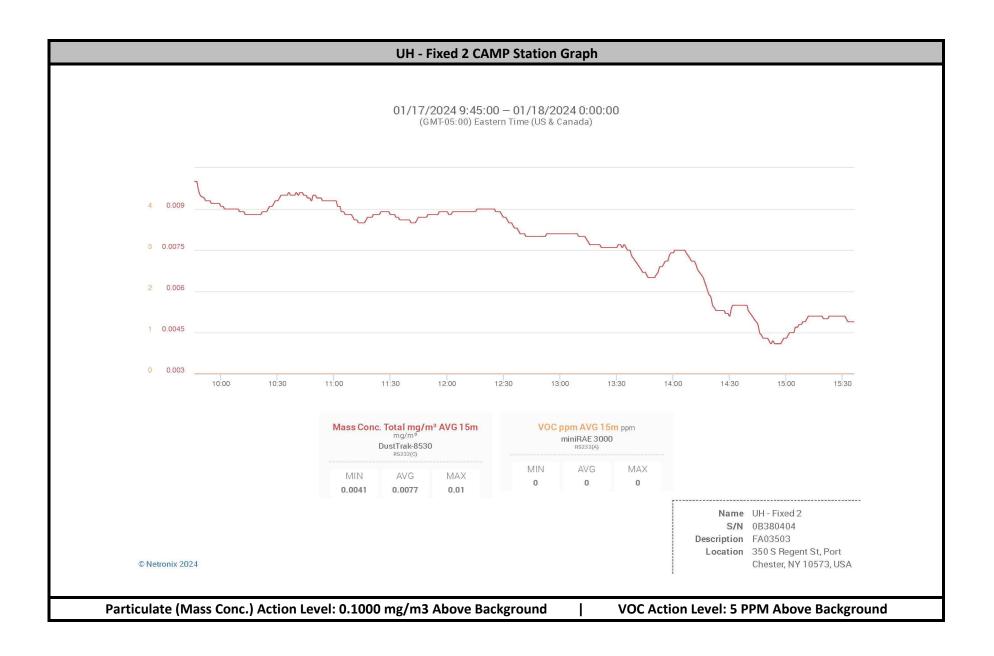

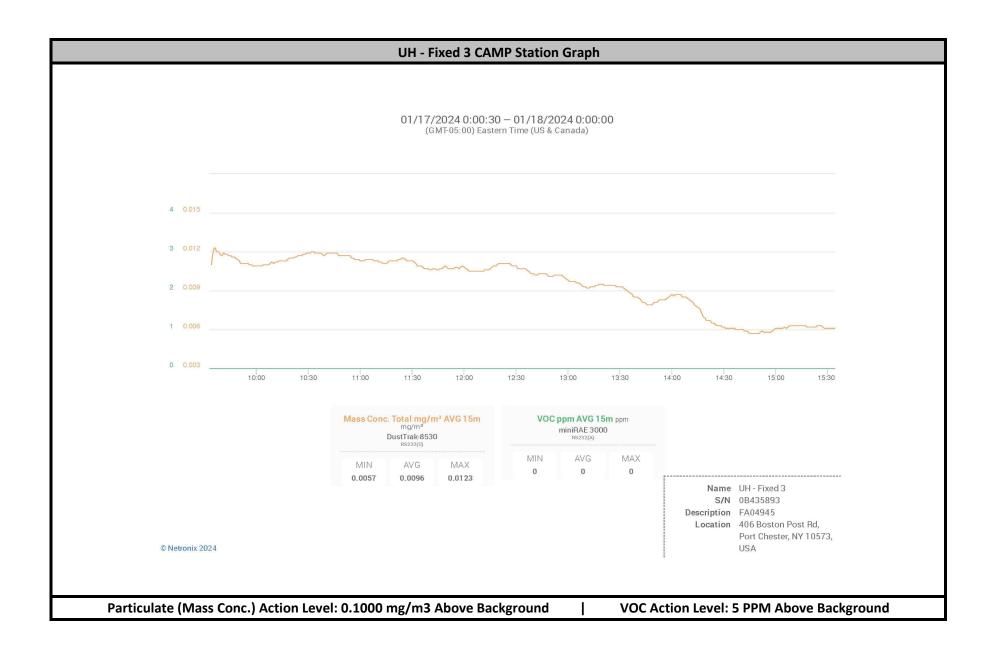

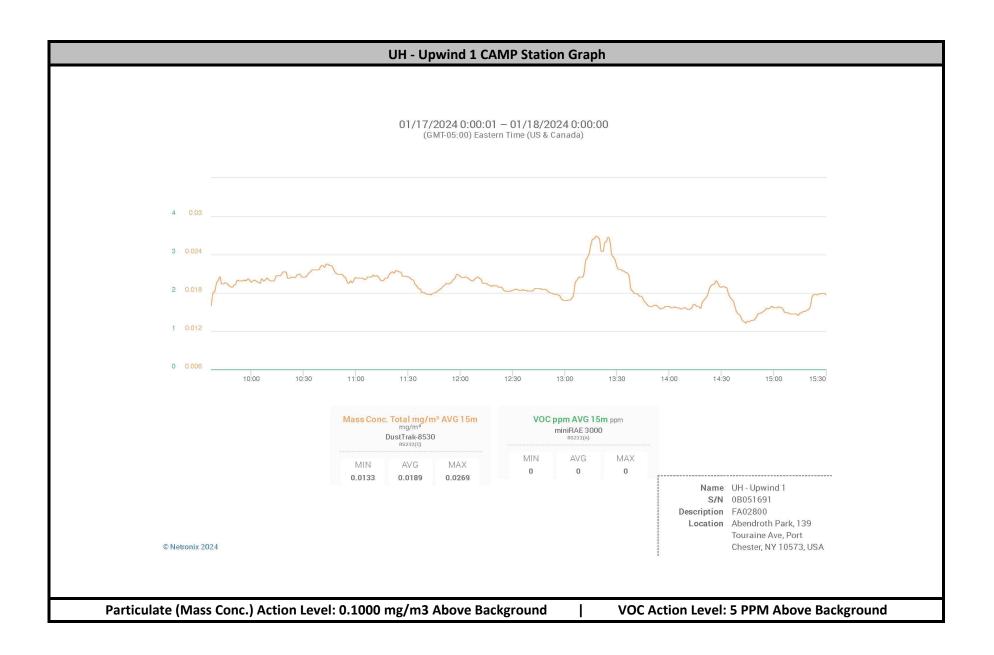

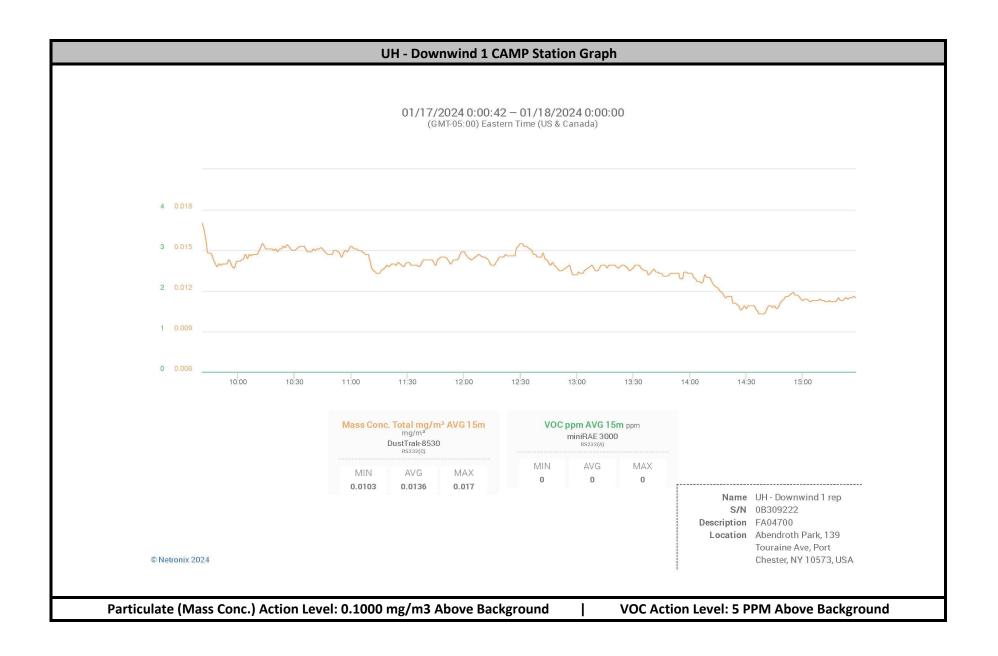

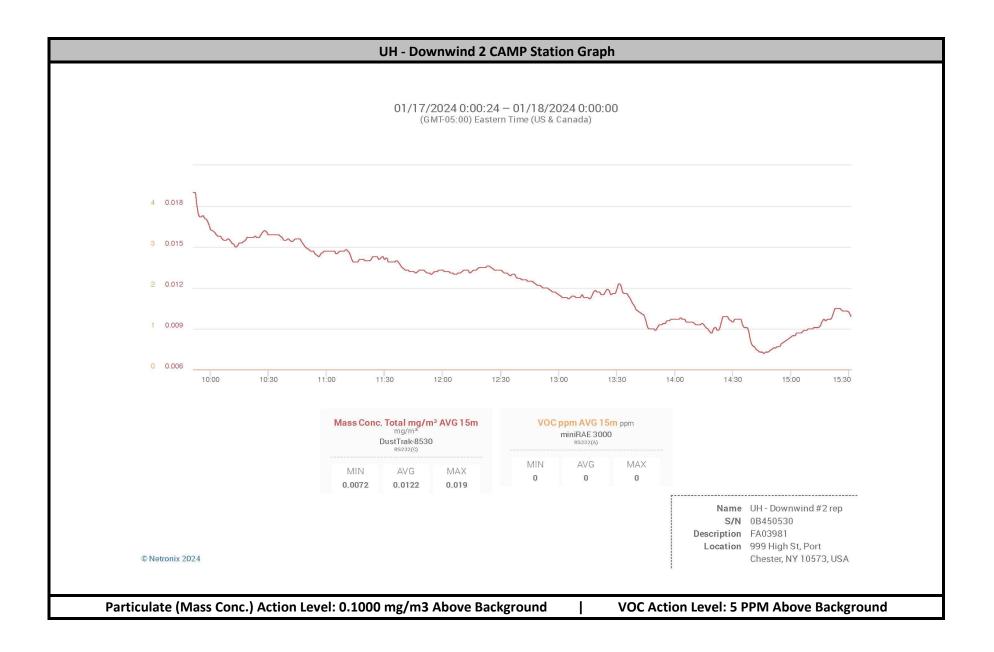

Daily Activity Report											
PAK	KF	Former United Hospital Port Chester, NY									
)	BCP No. C360202  General Site Information										
Date:			Genera	i Site Information	Thursday, Janua						
Weather: Wind Direction/Speed	•	Overcast, 20-31°F  West @ 9 mph									
AKRF Personnel on Site		West @ 9 mph  Michael Iodice									
AKRF Equipment on Si	te:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor									
Visitors:			Combus	actor Information	None	2.					
(	Contracting Company	I	Key Per				Equipm	ent			
	Tony Casale Inc.	Inc. Various excavation and grading equipment						grading equipment			
Capital Industries Corp. (Demolition Contractor)			Joe Cianciulli			Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)					
		De	escription and Locat	ion of Work Activitie	es Performed						
The excavation contra	ctor continued construction of the retainin	g wall within the ant	ennae Change of Use	e area.							
The demolition contra	ctor continued sorting and loading demolt	ion debris into conta	ners for off-site disp	osal.							
			Site Soil Dispo	sal Tracking Informa	ation						
	Destination Facility	Daily Trucks Daily Appro		ι. Cubic Yds.	Total Site Loads		Total Approximate Cubic Yards				
Clean Earth of Carteret - Carteret, NJ		0		0		35		700			
		Daily Export (CY)		0		Total Export (CY)		700			
			Imported Fi	ll Tracking Informati	on						
	Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards			
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)		0		0		17		400			
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)		0		0		1		20			
		Daily Import (CY)		0		Total Import (CY)		420			
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2			
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed			
VOC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No			
Particulate Action Leve	el Exceedance(s) Above Background:	No	No	No	No	No	No	No			
			Additi	onal Information							
Activity for Following Day(s):	llowing										
Comments:	None.										

1 of 64 C360202\_Daily Report\_2024.01.18

## Photograph 1 -Excavation contractor prepping the antennae Chane of Use area for installation of the retaining wall, view

facing southwest.



# Photograph 2 -Demolition contractor handling


structural demolition debris in the eastern portion of the site, view facing north.




### Photograph 3 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing northeast.




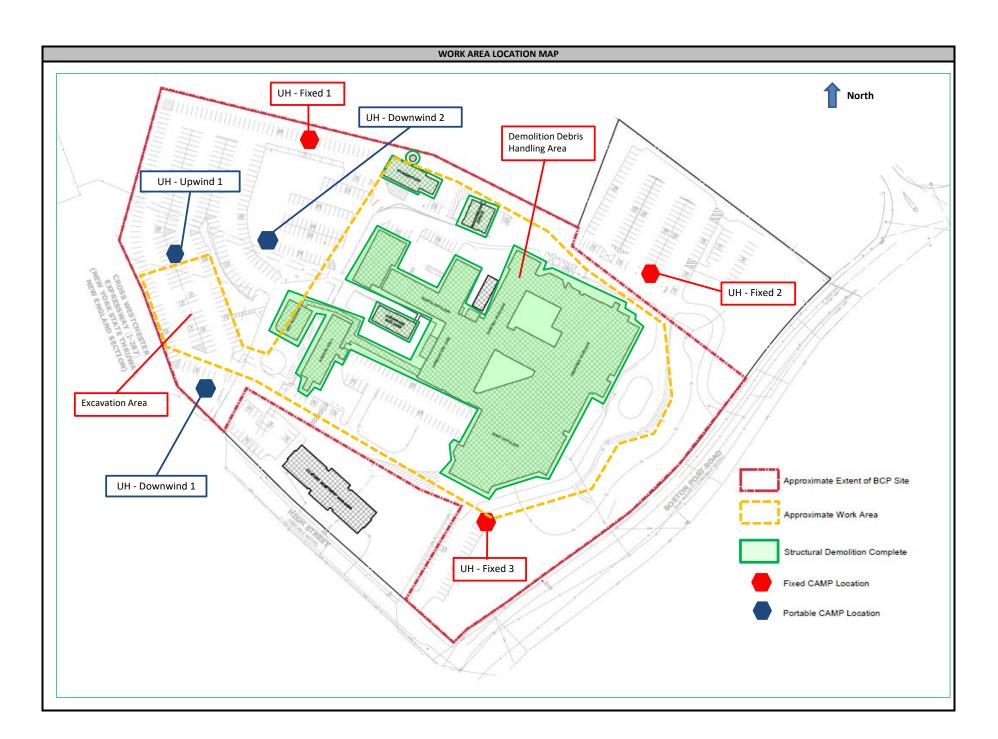



### **Roving CAMP Log** AKRE Air Monitoring Log Project: Former United Hospital (BCP Site No. C360202) Client: BR RA Port Chester Date: 1/18/24 Work Activity: ext. handling of demo dubris for disposal export of the for disposal Logged By: M. Icdae Job No: 200057 Weather: 20-31°F Ourcast Wind Direction: West Wind Speed: 9mph DUST COMMENTS TIME LOCATION PID **ODORS** (activity; work zone, upwind or downwind) (mg/m<sup>3</sup>) Background CUN 0.012 0600 ND 0830 DW 017 NV 0900 WW BK 0930 DW 0.024 ND nw 1000 018 ND 1030 DW ND 1100 uw ND 1130 DW 0.023 NI) 1200 WW 0 0.016 QU 1230 DW 0 0.020 ND 1300 NW 0.0. 0.013 ND 1330 DW ND 1400 WW 0010 ND 0.015 DW 1430 ND uw 0.008 1800 NH Community (Perimeter) Action Levels Work Zone Action Levels PID DUST <5 ppm: Level D <0.15 mg/m² above background breathing zone: Level D, D-Modified, or C (subject to PID) or suppression >0.1 mg/m³ above background: dust suppr >25 ppm above background: STOP >0.15 mg/m<sup>3</sup> above background in breathing zone: dust suppression, stop work if conditions continue

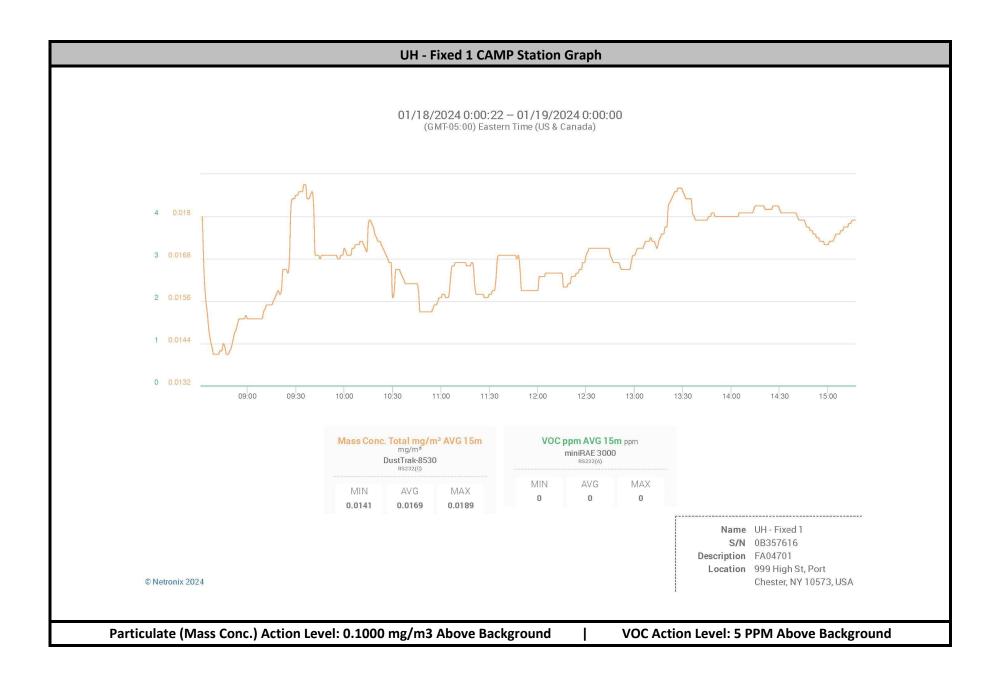


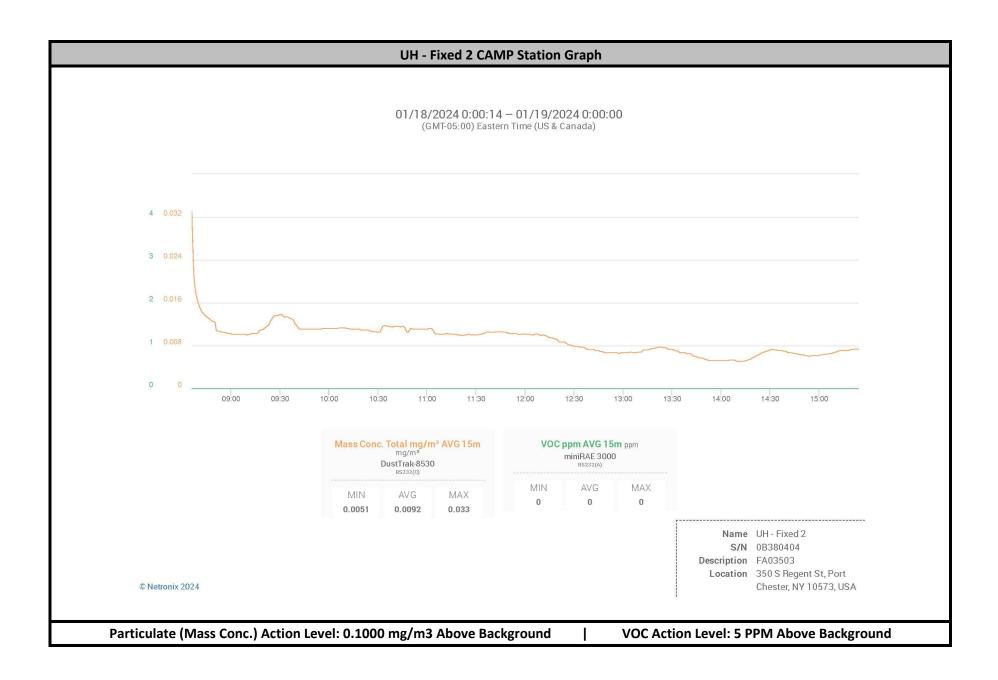

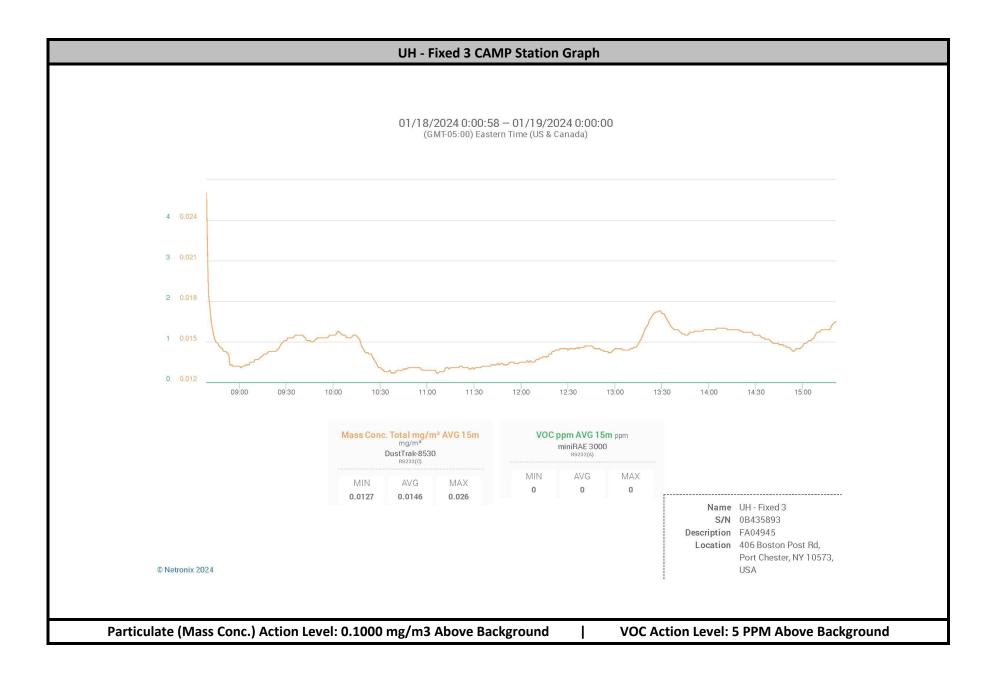

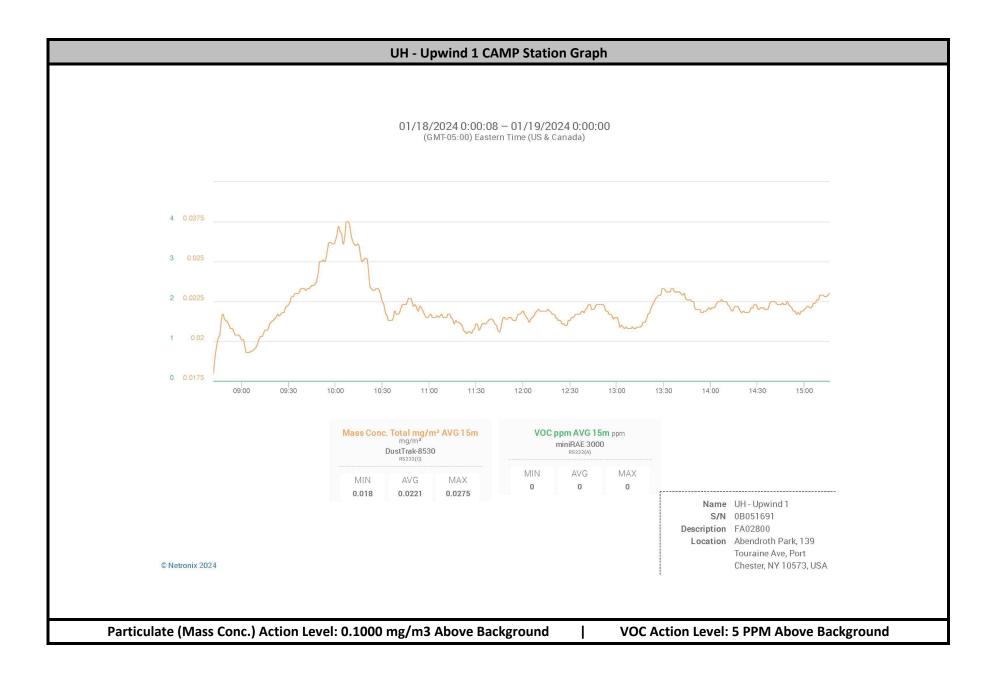

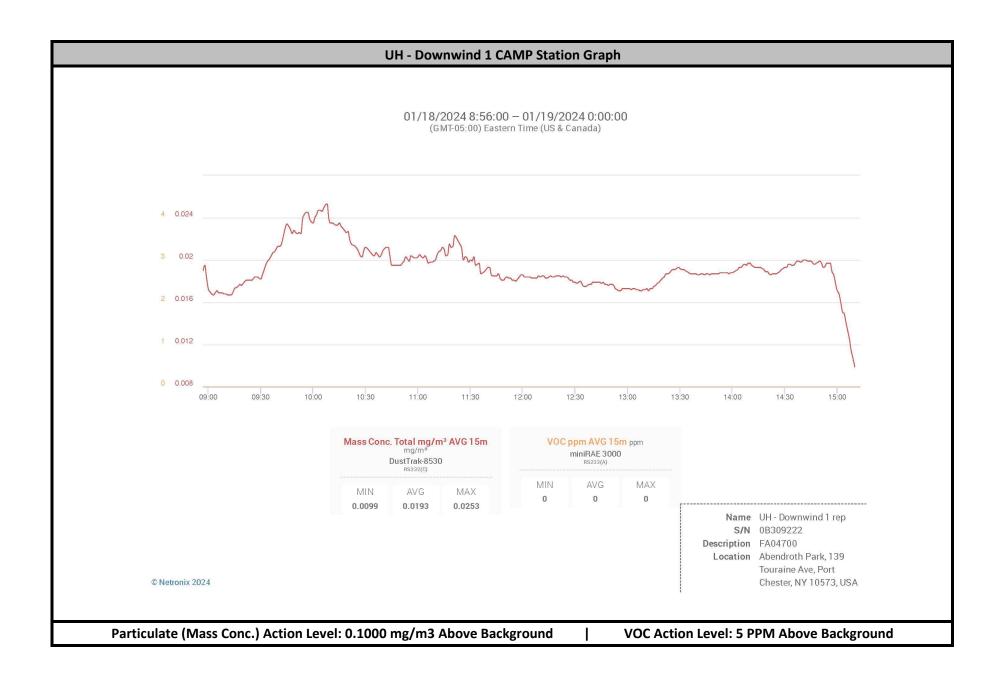

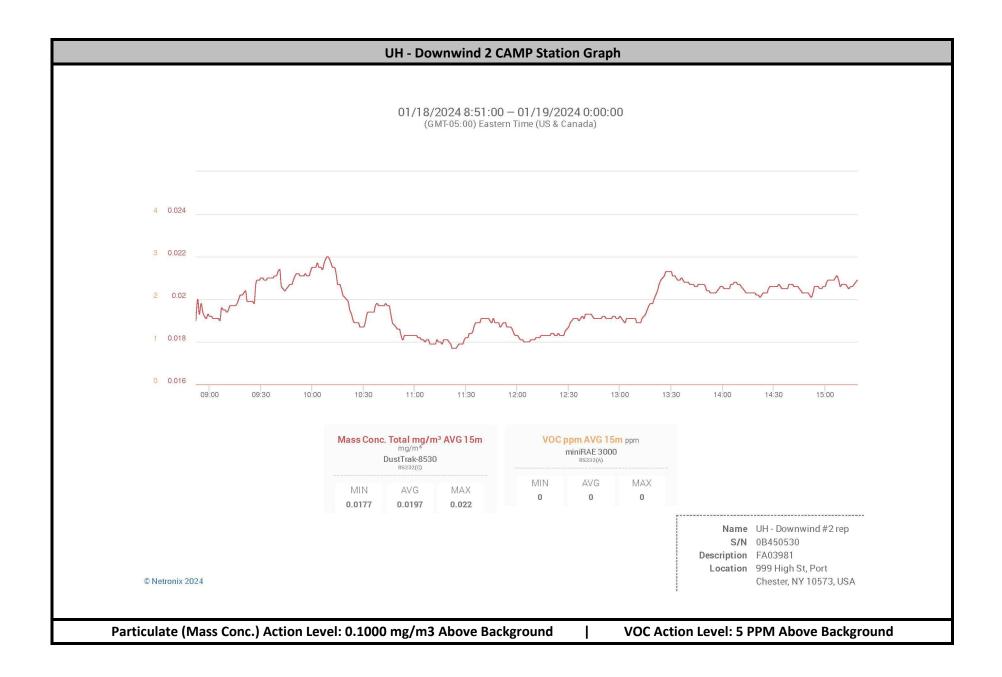

			Daily Activity Report							
PAK	KKF'	Former United Hospital Port Chester, NY								
	BCP No. C360202  General Site Information									
Date:			Genera		Friday, Januar					
Weather: Wind Direction/Speed:	:	Partly Coudy AM with Rain/Snow PM , 22-30°F NW @ 8 mph								
AKRF Personnel on Site	e:	Michael Iodice  3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor								
AKRF Equipment on Sit Visitors:	te:	3 Fixed CAM	IP Stations (PID & Du	ist Monitor), 3 Porta	ble CAMP Stations (I None		, One Handheld PID,	One Handheld Dust Monitor		
				ctor Information						
	tracting Company Key Personnel Equipment  ony Casale Inc. Various excavation and grading equipment									
(E	excavation Contractor)	Rigo Diaz (e.g., excavators, compa								
	apital Industries Corp. Demolition Contractor)	Joe Cianciulli				Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)				
		De	scription and Locati	on of Work Activitie	s Performed					
The excavation contrac	ctor continued construction of the retaining	g wall within the ante	nnae Change of Use	area.						
The demolition contrac	ctor continued sorting and loading demoltic	on debris into contair	ners for off-site dispo	osal.						
			Site Soil Dispo	sal Tracking Informa	ition					
	Destination Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Clean Earth of Carteret - Carteret, NJ		0		0		35		700		
		Daily Export (CY)		0		Total Export (CY)		700		
			Imported Fil	ll Tracking Informati	on					
	Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards		
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)		0		0		17		400		
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)		0		0		1		20		
			Daily Import (CY)	(	)		Total Import (CY)	420		
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2		
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed		
VOC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
Particulate Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No		
			Additi	onal Information						
Planned Work Activity for Following Day(s):	The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  The excavation contractor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer.									
Comments:	The use of air monitoring equipment was suspended at approximately 13:30 due to inclement weather. Visual and olfactory monitoring were performed during the period that the air monitoring equipment was not in use, and no fugitive dust or odors were detected.									

1 of 52 C360202\_Daily Report\_2024.01.

# Photograph 1 Excavation contractor preparing the antennae Change of Use area for installation of the retaining wall, view facing southwest.



### Photograph 2 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing north.





### Photograph 3 -


Demolition contractor loading structural demolition debris in the eastern portion of the site for off-site disposal, view facing west.




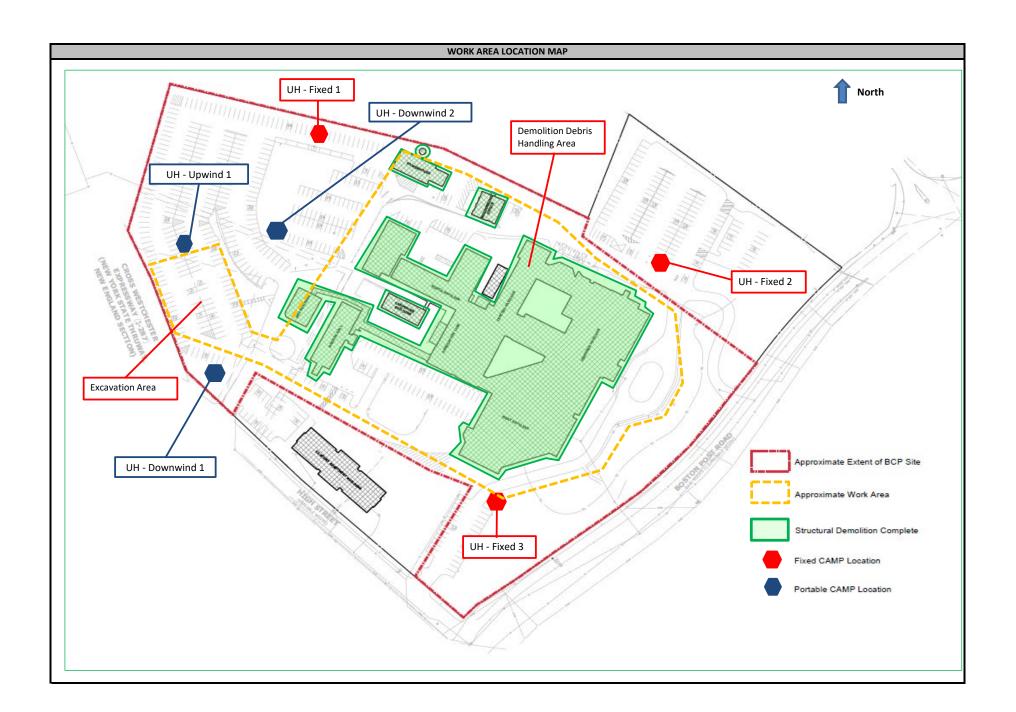


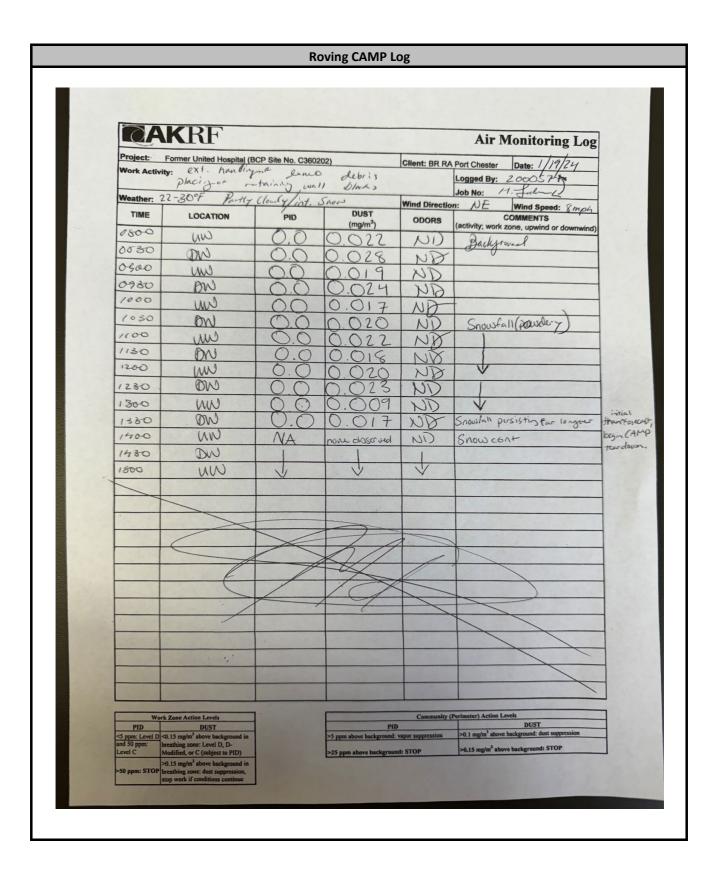


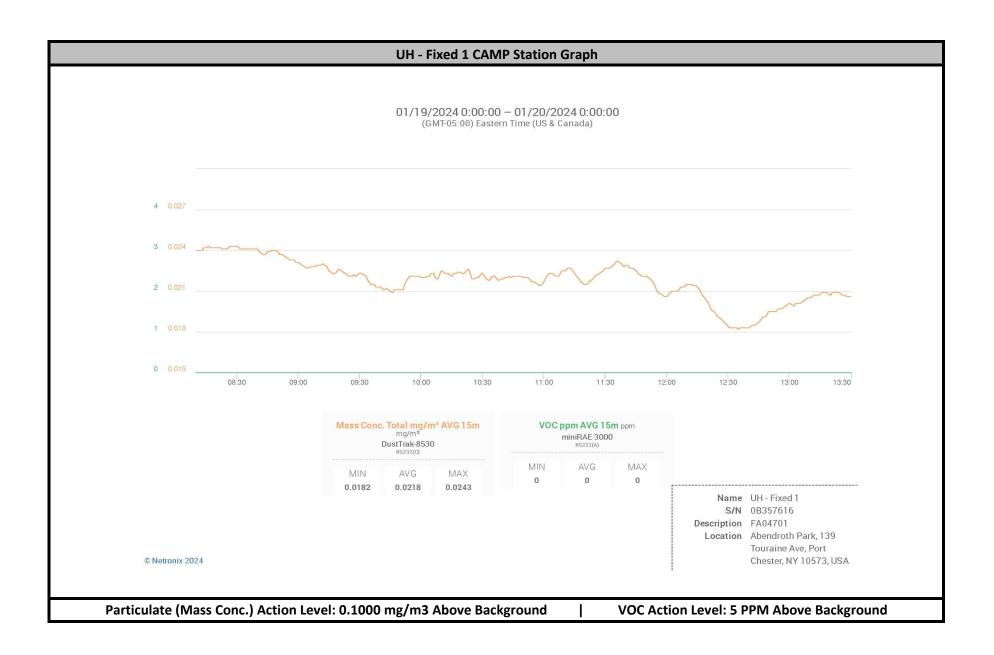


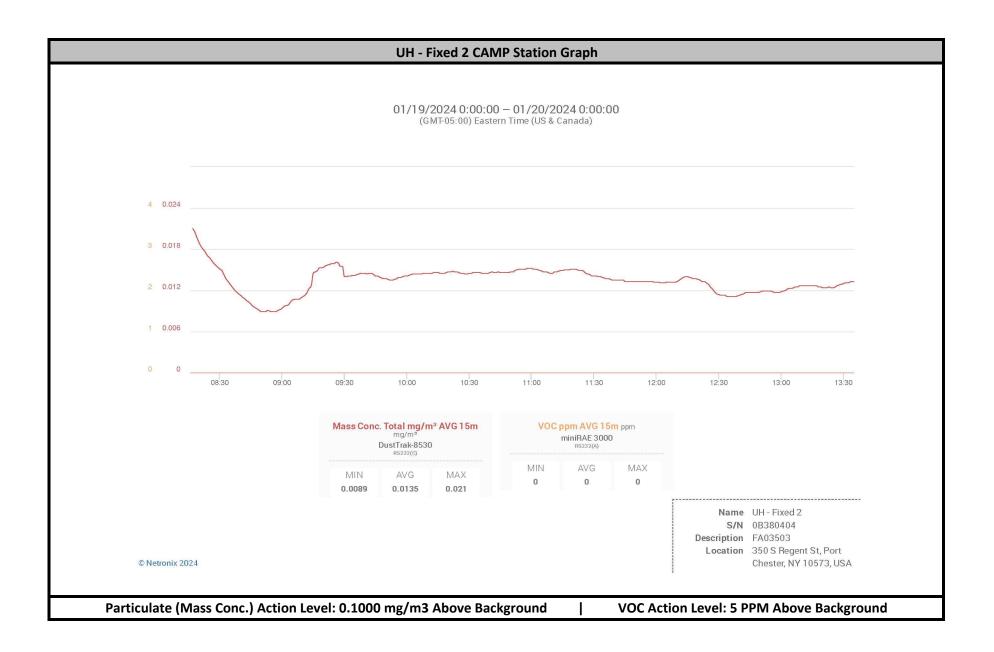

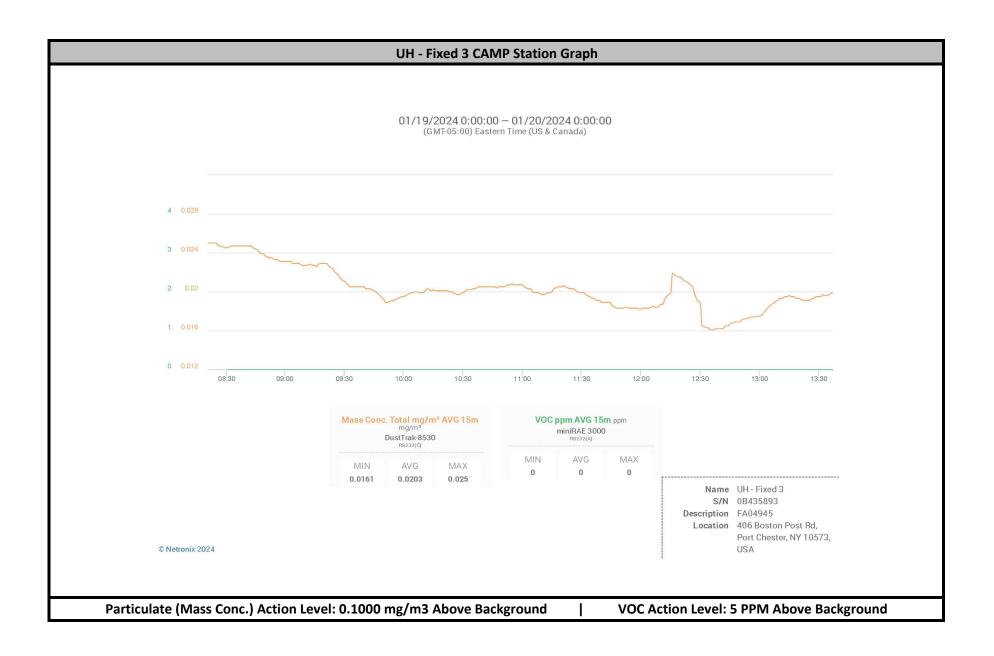

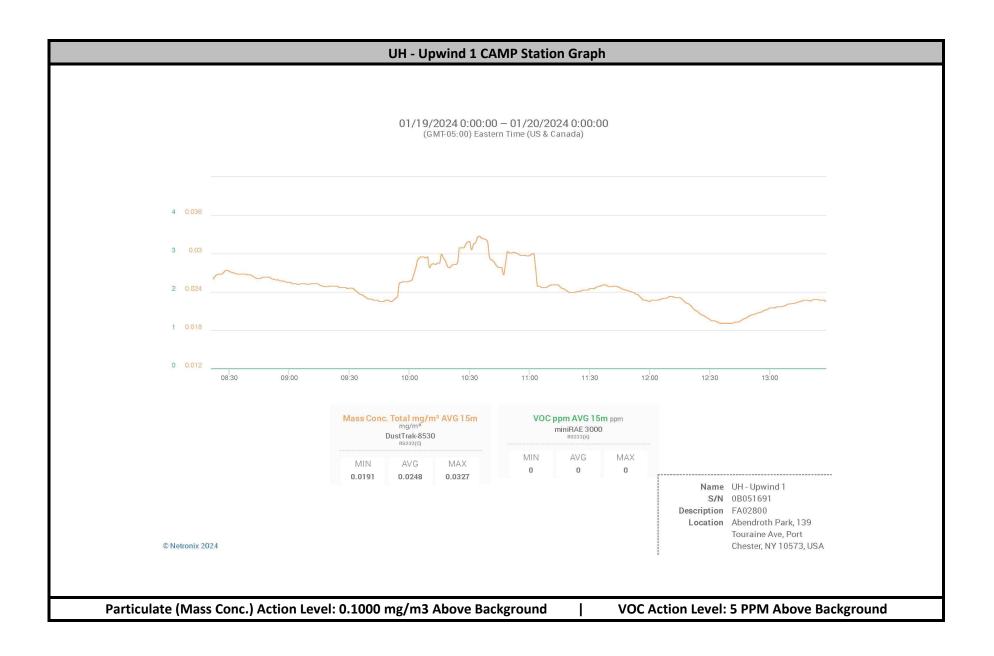

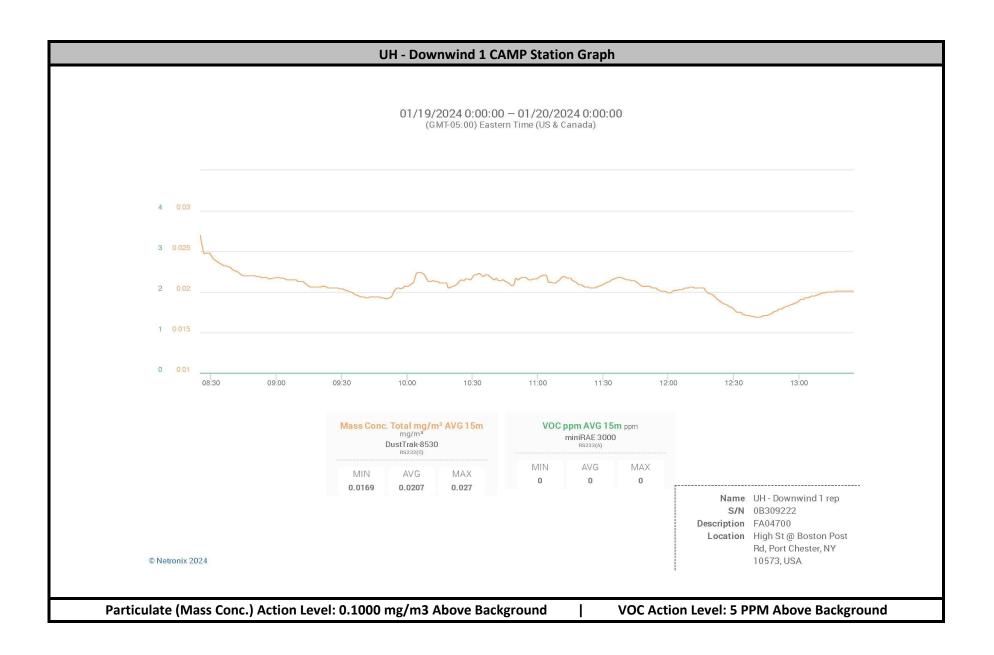

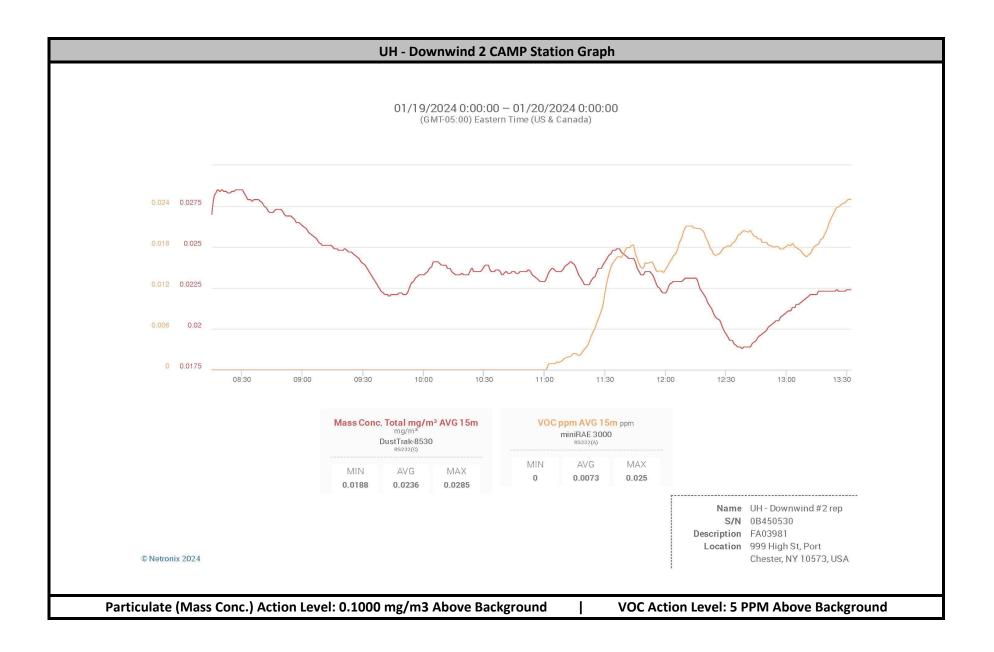

	Daily Activity Report										
Former United Hospital Port Chester, NY BCP No. C360202											
Date:	T	Genera	l Site Information	Monday, Janua	ny 22 2024						
Weather:				Sunny , 1							
Wind Direction/Speed:		WSW @ 9 mph									
AKRF Personnel on Site:	Michael Iodice, Stephen Schmid  3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor										
AKRF Equipment on Site: Visitors:	3 Fixed CAN	1P Stations (PID & Du	ist Monitor), 3 Porta	ble CAMP Stations ( Matt Hubic		, One Handheld PID,	One Handheld Dust Monitor				
visitors.		Contra	ctor Information	Widterrable	KI (DEC)						
Contracting Company Key Personnel Equipment											
Tony Casale Inc.		Rigo Diaz Various excavation and grading equipment									
(Excavation Contractor)		(e.g., excavators, compactors, roller-compactor, etc.)									
Capital Industries Corp. (Demolition Contractor)		Joe Cia	anciulli		Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)						
Description and Location of Work Activities Performed											
The excavation contractor continued the construction of a retain											
The excavation contractor imported Item #4 from Tilcon of West	Nyack, NY, and place	d this material as ba	ckfill above a demarc	cation layer within th	ne the antennae COU	J area.					
The demolition contractor continued sorting and loading demolt	ion debris into contai	ners for off-site dispo	osal.								
The demonstrate contractor continued sorting and rodding demons	ion debris into contai	ners for on site dispo	osui.								
Site Soil Disposal Tracking Information											
<b>Destination Facility</b>	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards				
Clean Earth of Carteret - Carteret, NJ	0		0		35		700				
	Daily Export (CY)		0		Total Export (CY)		700				
		Imported Fi	Il Tracking Informati	on							
Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards				
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)	16		380		33		780				
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)	0		0		1		20				
	Daily Import (CY)		380		Total Import (CY)		800				
CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2				
Odors:	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed				
VOC Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No				
Particulate Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No				
Additional Information											
Planned Work tivity for Following Day(s):  The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  The demolition contractor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer.											
Comments: None.											
comments.											

1 of 65 C360202\_Daily Report\_2024.01.22

### Photograph 1 -

Excavation contractor importing Item #4 from Tilcon of West Nyack, NY for use in antennae Change of Use area, view facing southeast.



### Photograph 2 -


Excavation contractor preparing the Site area for installation of a retaining wall within the antennae Change of Use area, view facing southwest.




### Photograph 3 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing east.




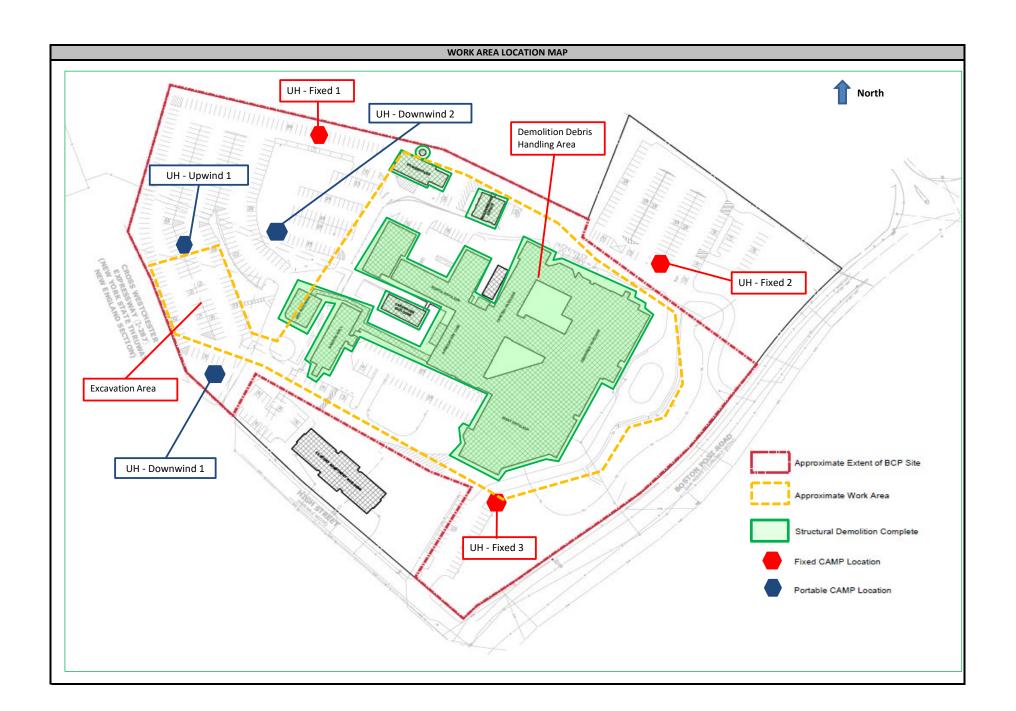



### **Roving CAMP Log** PAKRE Air Monitoring Log Client: BR RA Port Chester Date: 1/22/27 Project: Former United Hospital (BCP Site No. C360202) Work Activity: ext. handligget lens debrie, imperior Iten#17, Logged By: M. fola construction of retaining wall in con enem. Job No: 2000 57 16-36'F Sunny Weather: Wind Direction: WSW Wind Speed: 9mph DUST COMMENTS TIME LOCATION PID ODORS activity; work zone, upwind or downwind) (mg/m<sup>3</sup>) 0.0 0500 UN 0.010 Background ND 0830 0.017 DW ND 0900 nw 0.014 ND 0930 0.016 NB DW 0.014 1000 CUN ND 1030 ON 0.019 ND 1100 w 0.016 ND 1130 OW 0.020 BU 1200 0.014 WW ND 1230 ON 0.018 ND 1300 WW 0.015 ND 0.017 DN 1330 NX w 1400 0.017 ND 1430 OW ND 0.0 0.019 1800 W ND 0.012 Work Zone Action Levels PID Sppm: Level D on the property of the prope PID >0.1 mg/m³ above background: dust su >0.15 mg/m³ above background: STOP >25 ppm above background: STOP >50 ppm: STOP >0.15 mg/m³ above backgrou breathing zone: dust suppress stop work if conditions contin

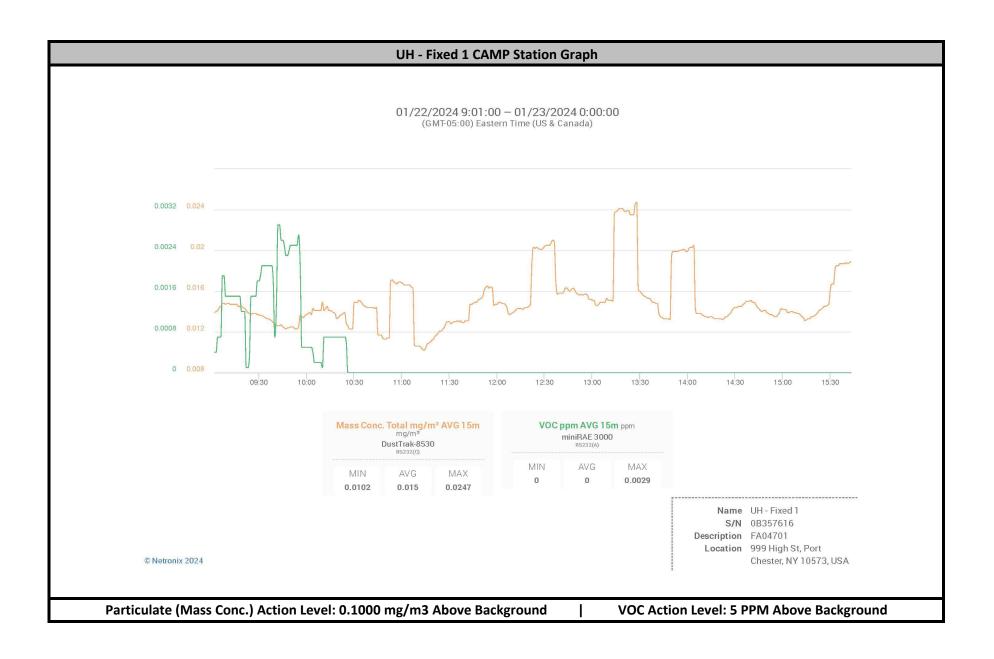


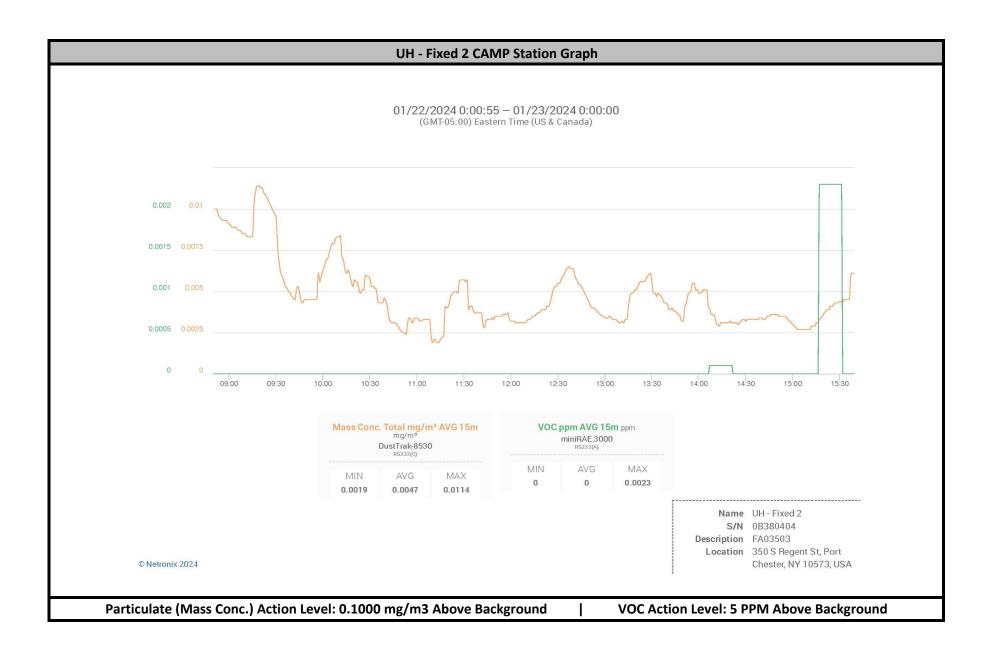

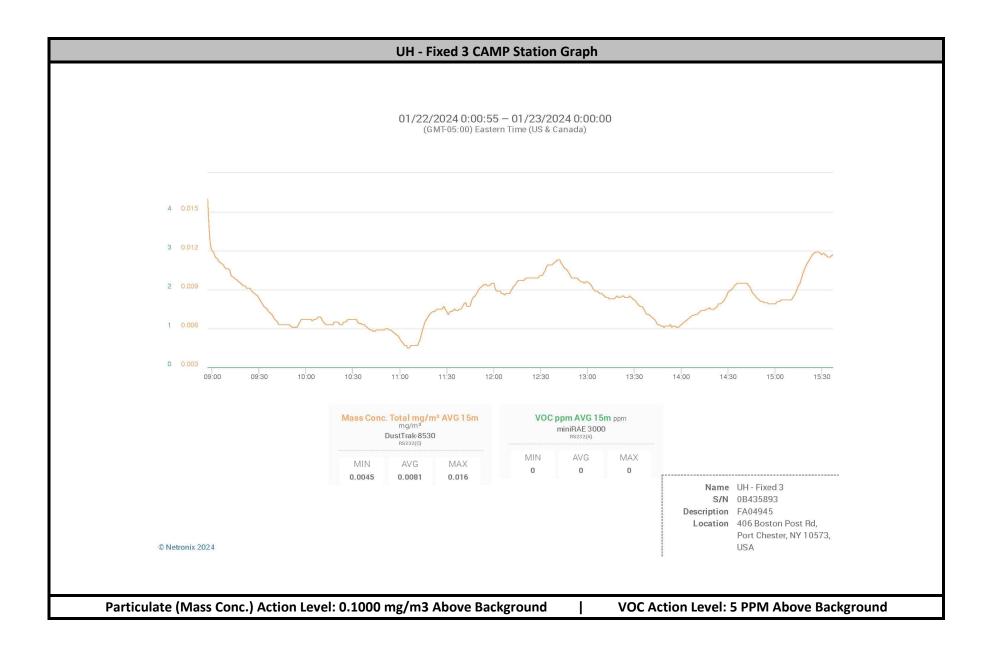

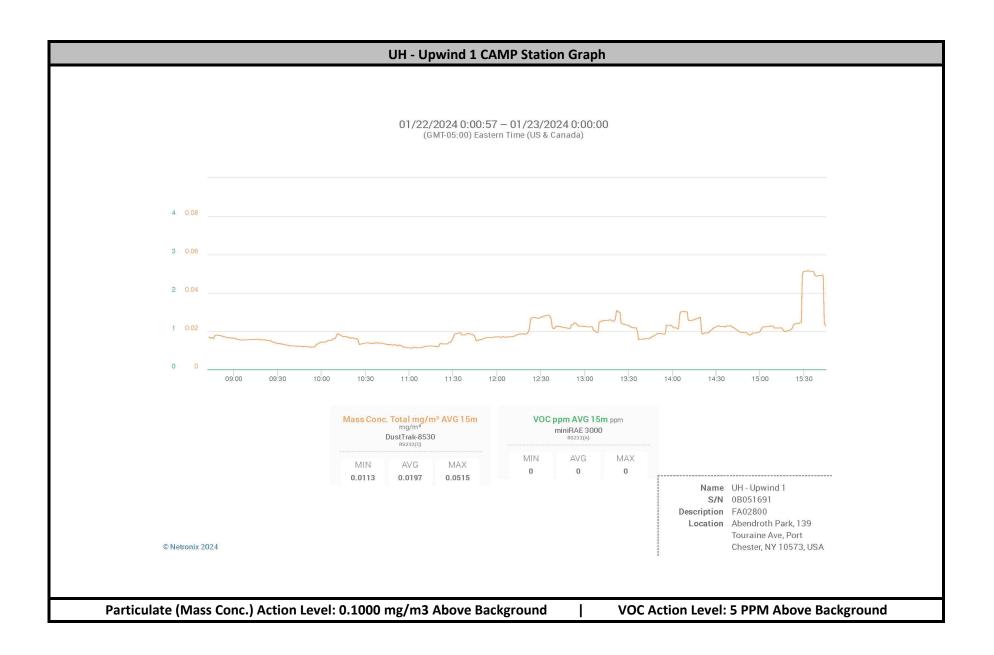

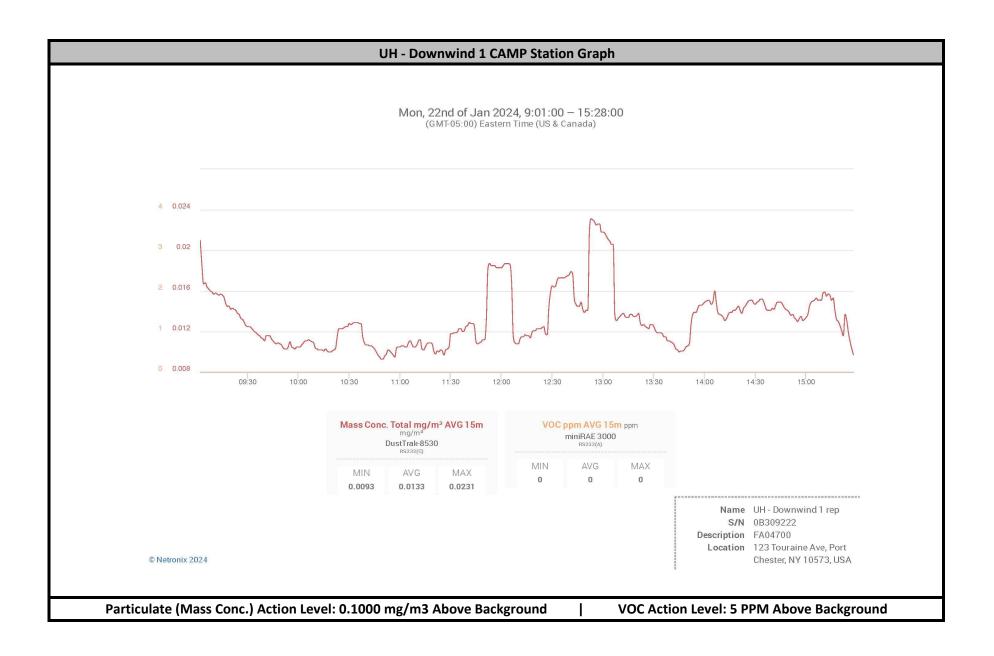

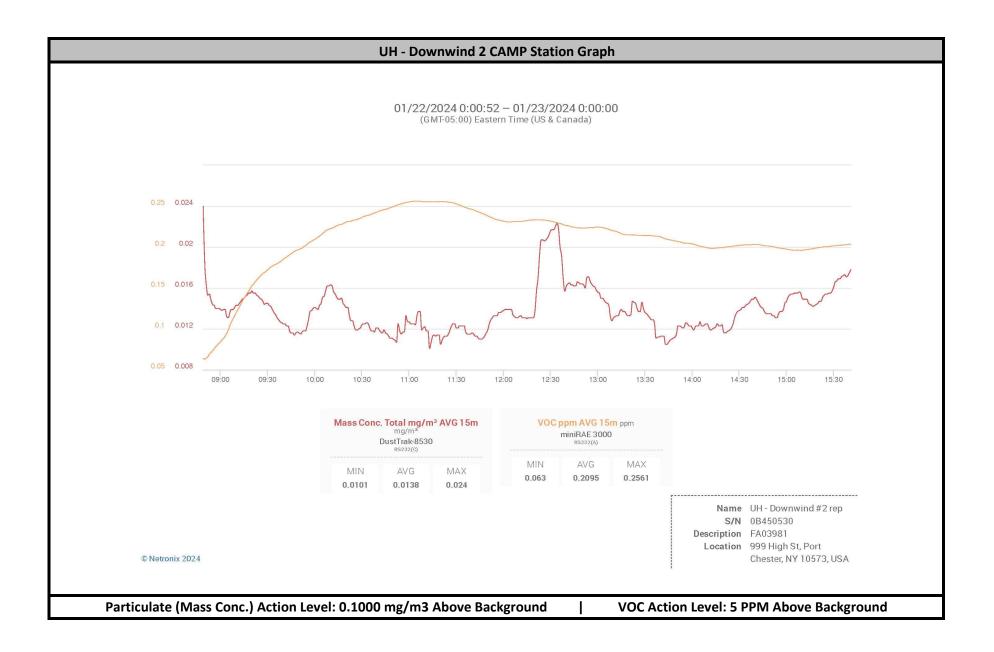

	Daily Activity Report										
Former United Hospital Port Chester, NY											
BCP No. C360202  General Site Information											
Date:			Genera	ar site information	Tuesday, Janua	ry 23, 2024					
Weather:		Overcast/Rain (Afternoon), 31-39°F									
Vind Direction/Speed: KRF Personnel on Site:	;	West @ 4 mph Michael Iodice									
KRF Equipment on Site	2:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor									
'isitors:		None  Contractor Information									
Co	ontracting Company	Key Personnel Equipment									
(Ex	Tony Casale Inc. cavation Contractor)		Rigo	Diaz		Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.)					
	pital Industries Corp. emolition Contractor)	Joe Cianciulli				Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)					
		De	escription and Locat	ion of Work Activitie	es Performed						
he excavation contract	cor continued the construction of a retain	ing wall within the ar	ntennate Change of I	Jse (COU) area.							
he excavation contract	or imported Item #4 from Tilcon of West	Nyack, NY and used	this material as back	fill within the 2-foot	cut of the antennae	COU area, after plac	ing a demarcation la	yer.			
he demolition contract	tor continued sorting and loading demolt	ion debris into contai	ners for off-site disp	osal.							
			Site Soil Dispo	osal Tracking Inform	ation						
Destination Facility		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yard			
Clean Earth of Carteret - Carteret, NJ		0		0		35		700			
		Daily Export (CY)		0		Total Export (CY)		700			
			Imported Fi	II Tracking Informati	on						
Origin Facility		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yard			
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)		1		20		34		800			
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)		0		0		1		20			
		Daily Import (CY)		20		Total Import (CY)		820			
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2			
dors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed			
OC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No			
articulate Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No			
Additional Information											
ctivity for Following	llowing										
Comments: N	lone.										

1 of 38 C360202\_Daily Report\_2024.01.23

# Photograph 1 Excavation contractor installation of retaining wall blocks

within the antennae COU area, view facing southwest.





### Photograph 2 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing north.





### Photograph 3 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing south.




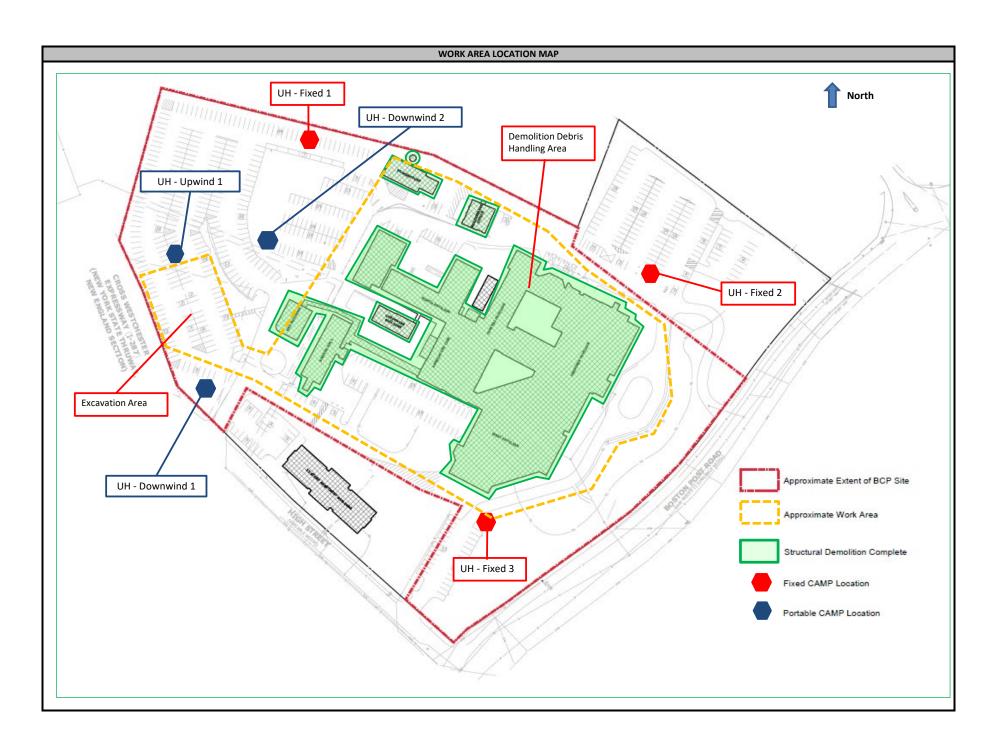


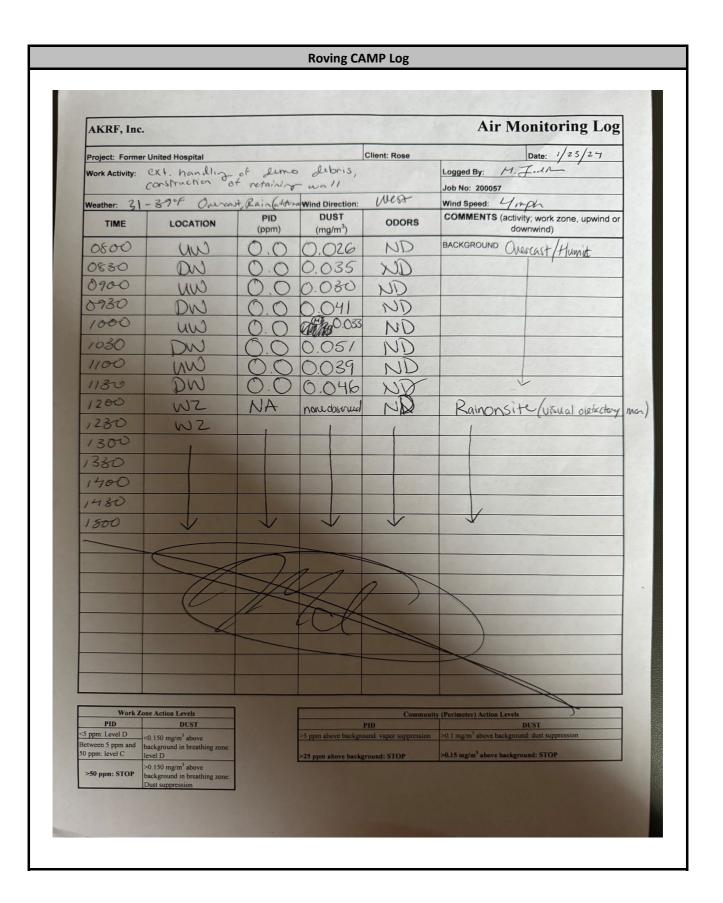


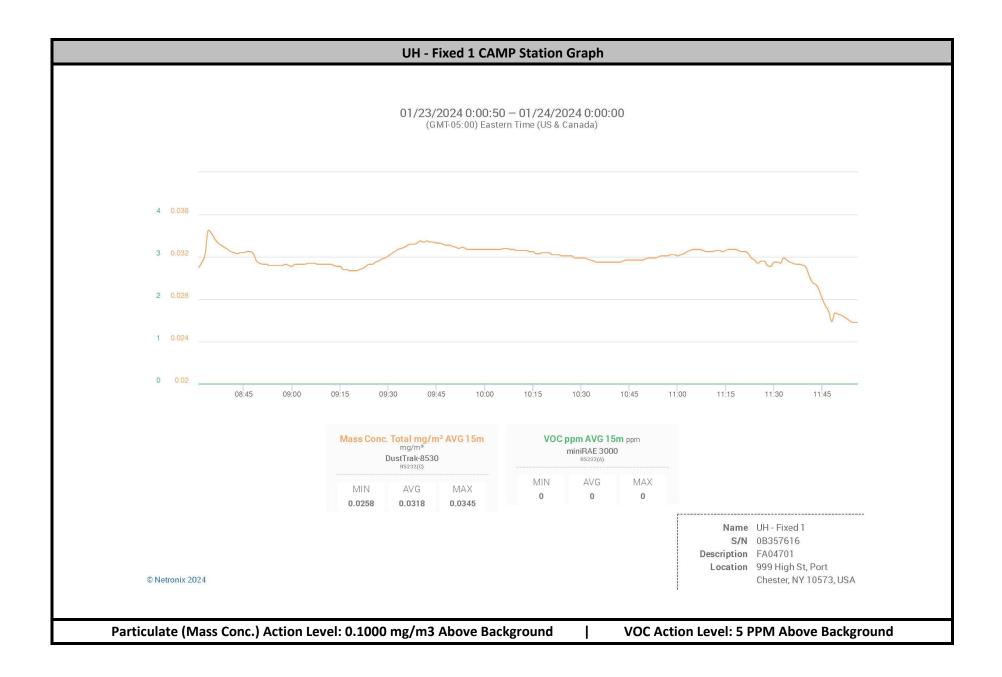


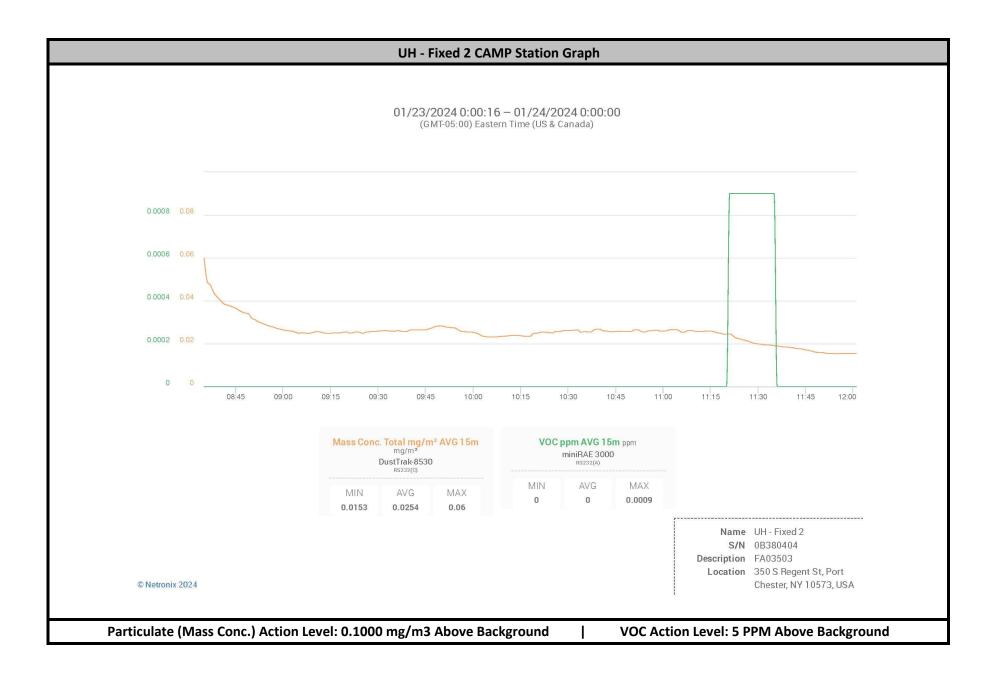

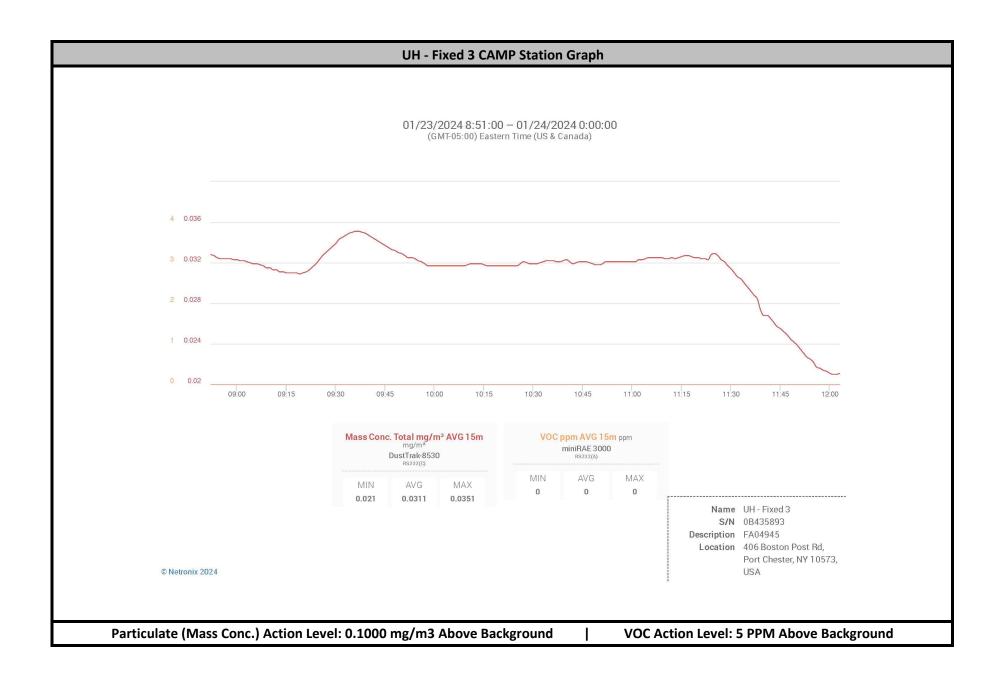

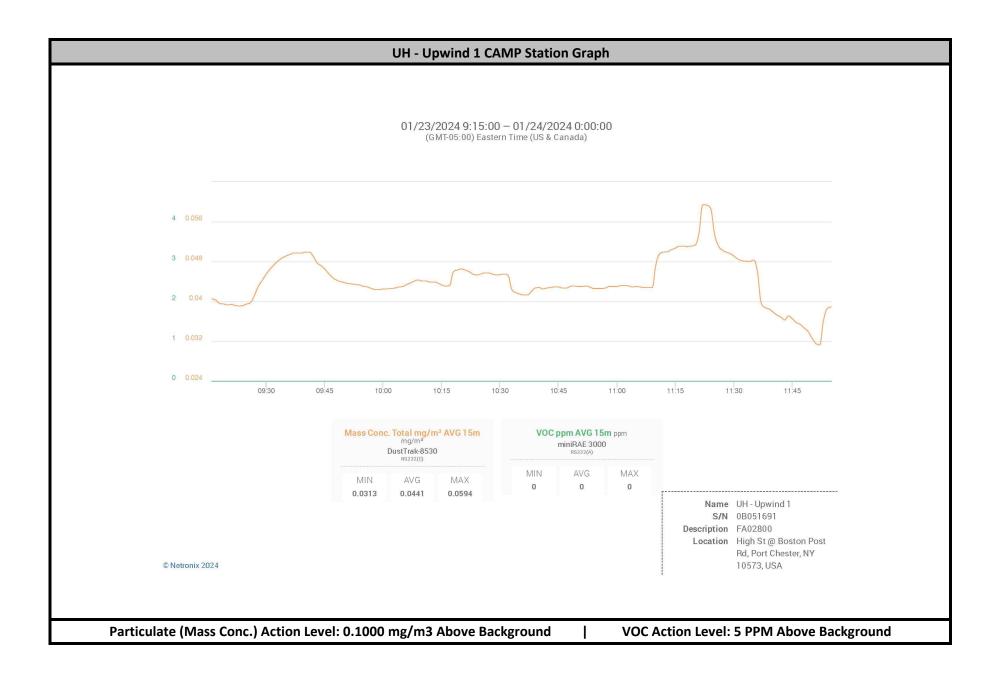

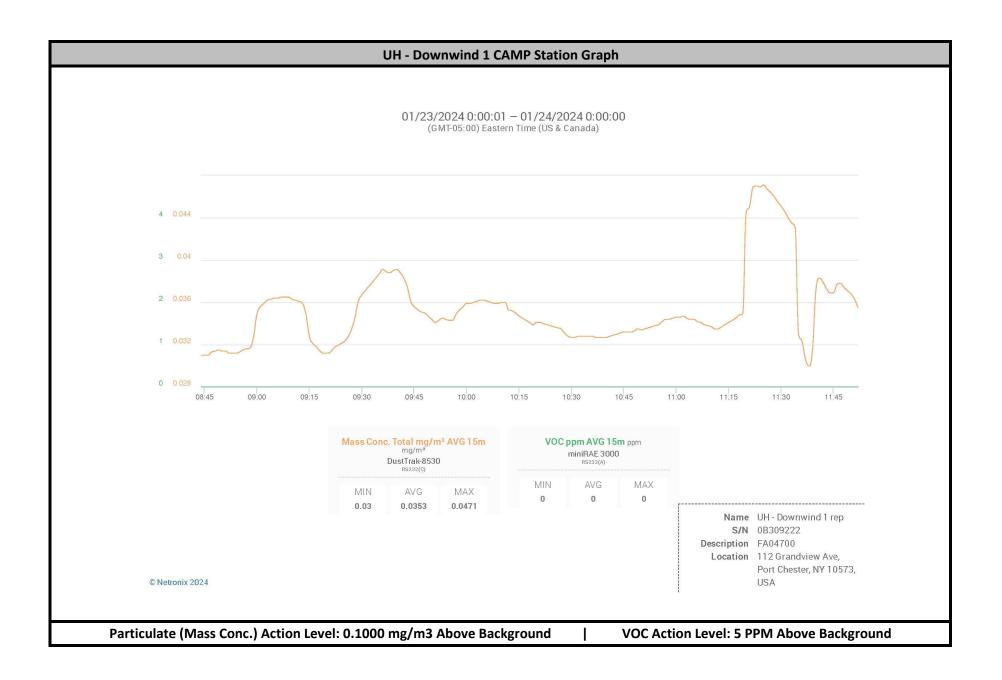

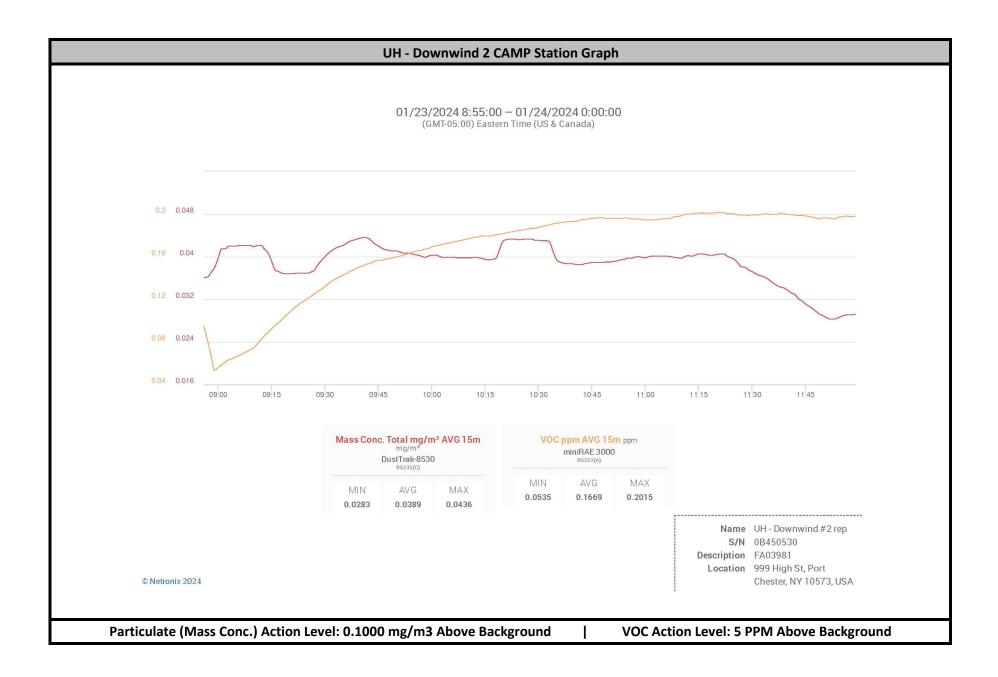

<b>PAK</b> RF	Daily Activity Report  Former United Hospital Port Chester, NY BCP No. C360202									
Date:		Genera	al Site Information	Wednesday, Jan	uary 24, 2024					
Weather:	Wednesday, January 24, 2024 Foggy / Intermittent Rain, 35-43°F									
Vind Direction/Speed: kKRF Personnel on Site:	East @ 5 mph Michael Iodice									
KRF Equipment on Site: //sitors:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor  None									
		Contra	actor Information	14011						
Contracting Company  Tony Casale Inc.	Key Personnel Equipment  Various excavation and grading equipment									
(Excavation Contractor)	Rigo Diaz  (e.g., excavators, compactors, roller-compactor, etc.)									
Capital Industries Corp.	Joe Cianciulli  (e.g., excavators, skid steers, roll off containers, etc.)									
(Demolition Contractor)					(e.g., ex	cavators, skid steers,	, roll off containers, etc.)			
	De	escription and Locat	ion of Work Activitie	s Performed						
he execution contractor continued the construction of a retain										
he excavation contractor continued the construction of a retain	ing wan within the ai	iterinae Change of o	se (COO) area.							
he excavation contractor imported Item #4 from Tilcon of West	Nyack, NY and used	this material as back	fill above a previousl	y placed demarcation	on layer within the 2-	foot cut of the anter	nnae COU area.			
·			•							
he Excavation contractor placed a demarcation layer and used I were received. Endpoint sampe data was conveyed and discusse				ple results below th	neir respective restri	cted residential soil o	leanup objective (RRSCO) values			
vere received. Endpoint sampe data was conveyed and discusse	a with Wisble phon	to proceeding with a	dekinning detivities.							
he demolition contractor continued sorting and loading demolt	ion debris into conta	iners for off-site disp	osal.							
		Site Soil Dispo	osal Tracking Informa	ation						
Destination Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yard			
Clean Earth of Carteret - Carteret, NJ	0		0		35		700			
	Daily Export (CY)		0		Total Export (CY)		700			
						Total Export (CT)	700			
		Imported Fi	ll Tracking Informati	on						
Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Vard			
Oligini acinty	Daily	Trucks	Daily Applox	a. Cubic rus.	Total Si	te Loads	Total Approximate Cubic Yard			
ilcon West Nyack Quarry - West Nyack, NY ITEM #4)	1	.0	25	0	4	14	1,050			
ilcon West Nyack Quarry - West Nyack, NY NY2/ASTM #5 - 3/4" Stone)		0	C	)		1	20			
MIZIASIMIRS SIA Stolley										
		Daily Import (CY)	25	250 Total Import (CY)		1,070				
CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2			
dorr	Name Observed	Name Observed	Name Observed	Name Observed	Name Observed	Name Observed	Name Observed			
odors:	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed			
OC Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No			
articulate Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No			
		Additi	ional Information							
Planned Work The demolition contractor will continue so	rting and loading of	demolition debris fro	om the former bosnit	al huildings into cor	ntainers for off-site d	isnosal				
ctivity for Following				_						
Day(s): The excavation contratcor will continue to	import Item #4 from	Tilcon West Nyack f	or use within the ant	ennae COU area as	structural backfill ab	ove a demarcation la	ayer.			
The use of air monitoring equipment was I	imited from approvin	nately 10:30 to 12:41	5 due to inclement w	eather (rain): the ai	r monitoring equipm	nent was denloved or	nce weather conditions improved			
Comments: 10:30, however the weather conditions or	Site deteriorated at	12:45, resulting in th	ne suspension of CAM	1P monitoring for th						
during the period that the air monitoring e	quipment was not in	use, and no fugitive	dust or odors were	detected.						

1 of 33 C360202\_Daily Report\_2024.01.24

### Photograph 1 -Excavation contractor backfilling the SB-53 hotspot with Item #4, view facing west.



### **Photograph 2 -**Excavation


contractor importing
Item #4 for use in the
antennae COU area,
view facing
southeast.





### Photograph 3 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing north.




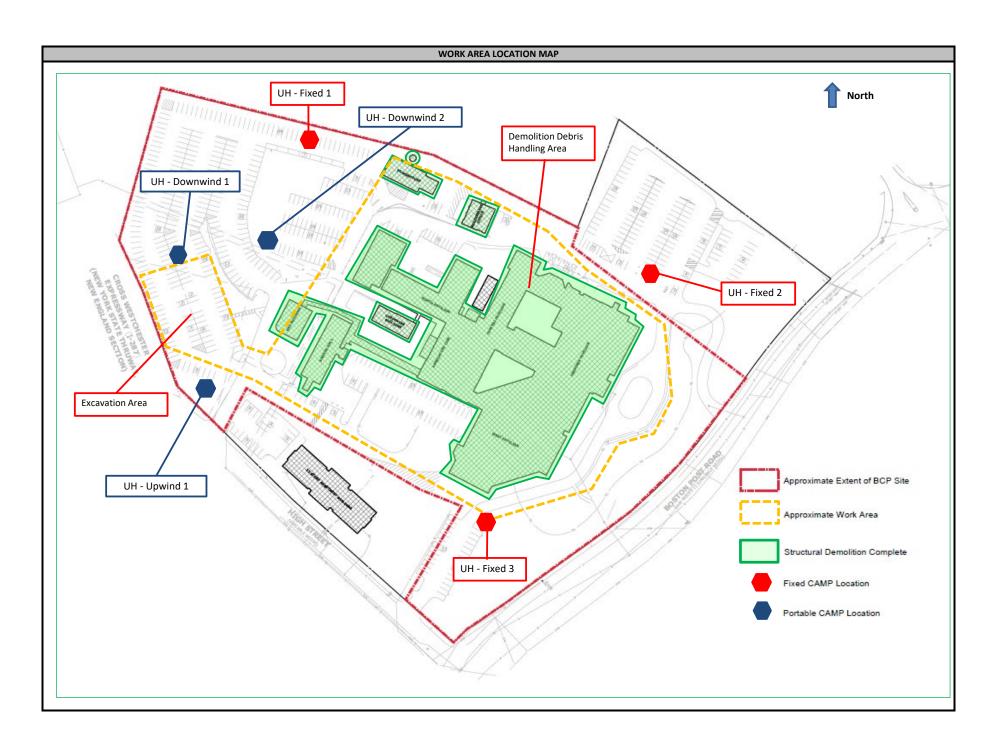


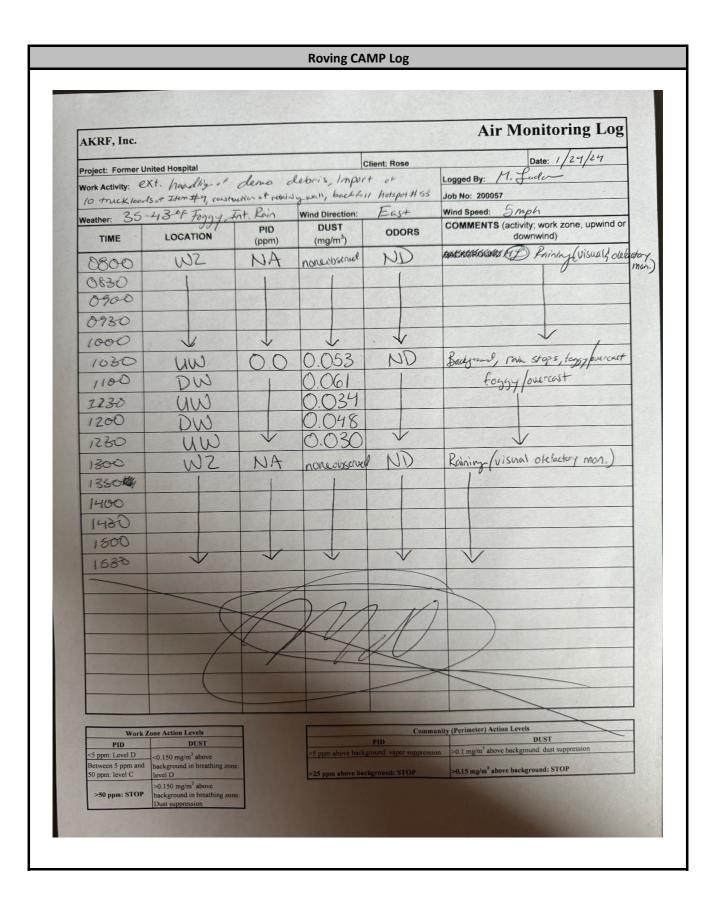


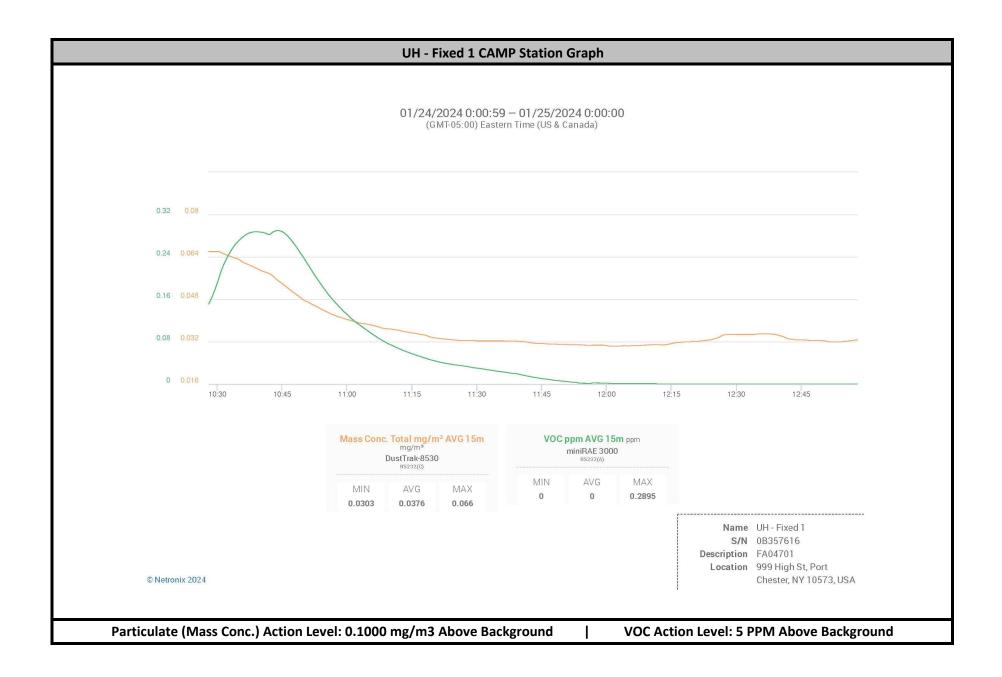


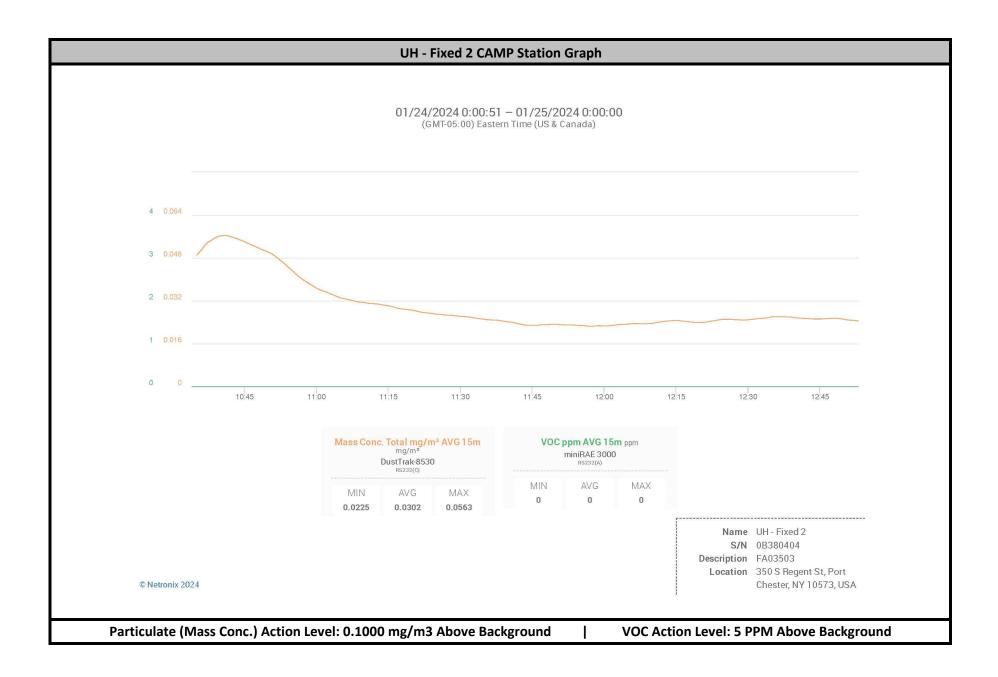

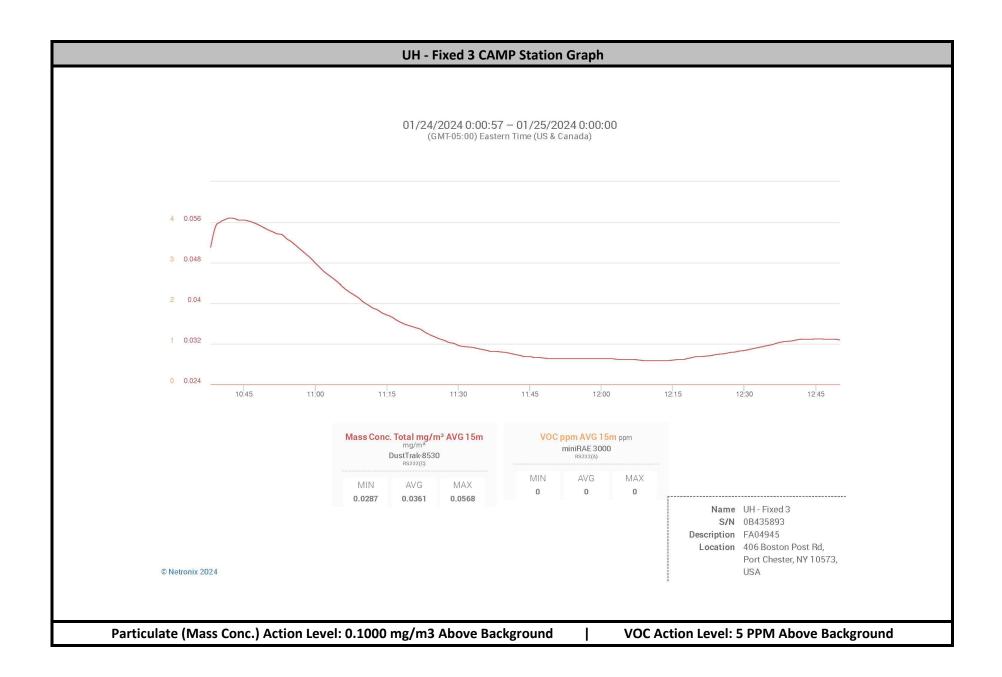

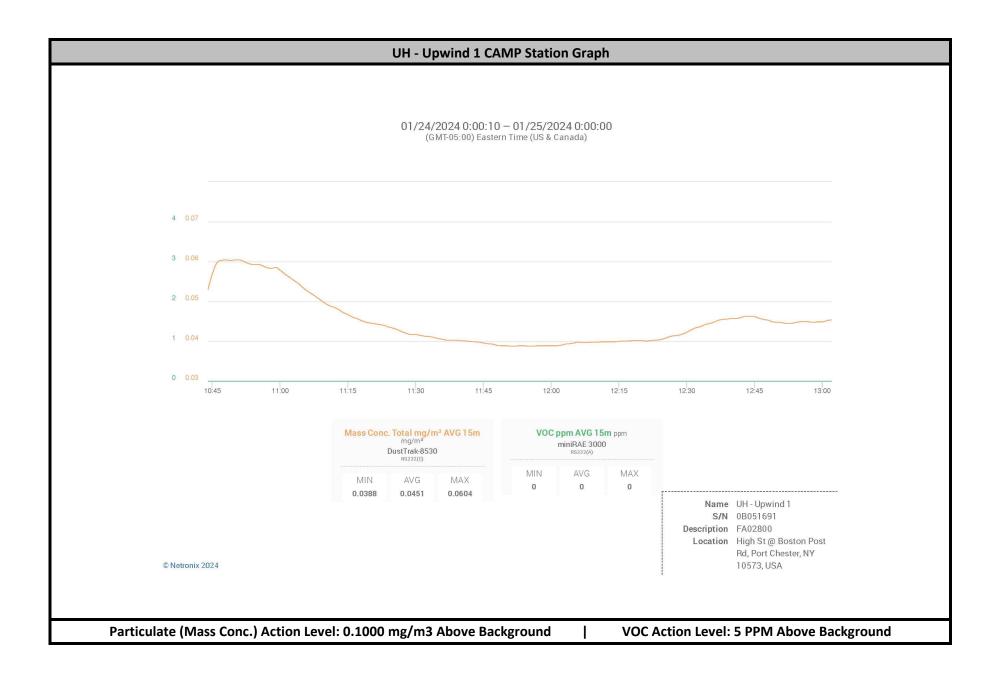

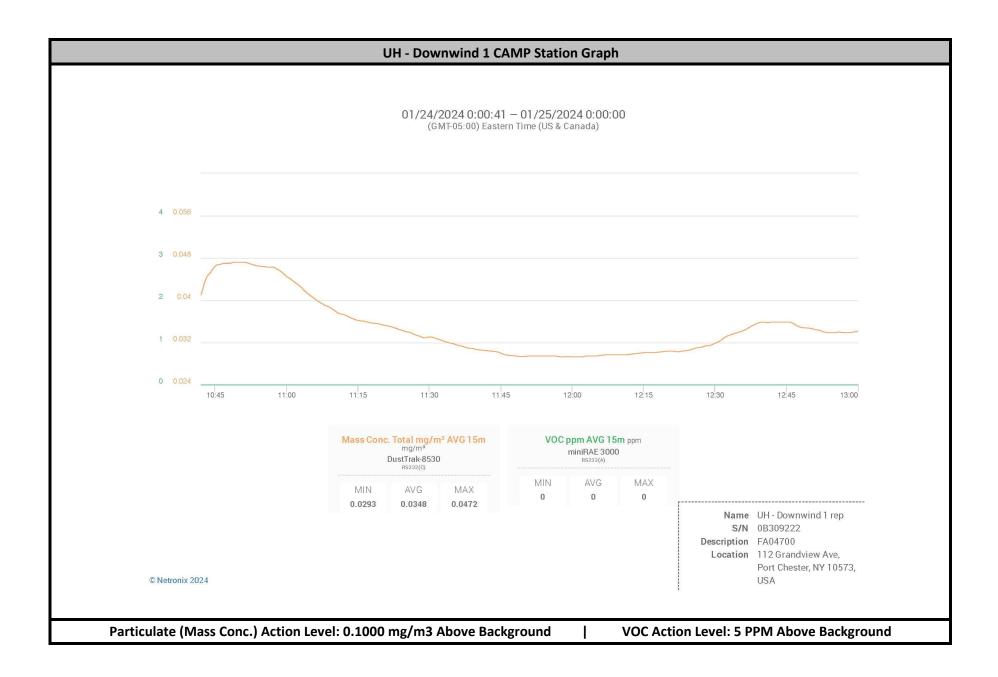

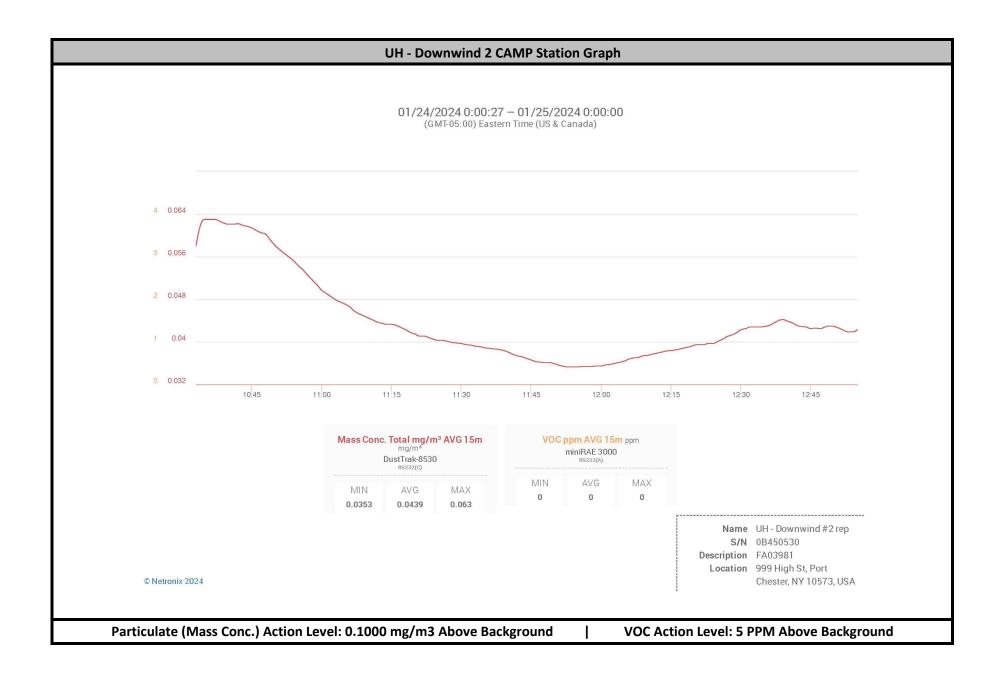

	Daily Activity Report									
<b>CAK</b> RF	Former United Hospital Port Chester, NY BCP No. C360202									
	General Site Information									
Date: Weather:	Thursday, January 25, 2024 Rain, 39-52°F									
Wind Direction/Speed:	NNW @ 3 mph Michael Iodice									
AKRF Personnel on Site: AKRF Equipment on Site:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor									
Visitors:		Contro	actor Information	Non	e					
Contracting Company	I	Key Personnel Equipment								
Tony Casale Inc.		Rigo Diaz  Various excavation and grading equipment  (e.g., excavators, compactors, roller-compactor, etc.)								
(Excavation Contractor)	(e.g., excavators, compactors, roller-compactor, etc.)									
Capital Industries Corp. (Demolition Contractor)	Joe Cianciulli  Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)									
	De	escription and Locat	ion of Work Activitie	es Performed						
The excavation contractor continued the construction of a retain	ing wall within the ar	ntennae Change of U	se (COU) area.							
The demolition contractor continued sorting and loading demolt	ion debris into contai	ners for off-site disp	osal.							
		Site Soil Dispo	osal Tracking Informa	ation						
Destination Facility	Daily '	Daily Trucks		c. Cubic Yds.	Total Site Loads		Total Approximate Cubic Yards			
Clean Earth of Carteret - Carteret, NJ	0		0		35		700			
	Daily Export (CY)		0		Total Export (CY)		700			
		Imported Fi	ll Tracking Informati	on						
Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards			
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)	0 0 44 1,05					1,050				
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) 0 1					20					
		Daily Import (CY)	C	)		Total Import (CY)	1,070			
CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2			
Odors:	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed			
VOC Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No			
Particulate Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No			
		Additi	onal Information							
Planned Work Activity for Following Day(s):  The demolition contractor will continue so							ıyer.			
Comments: The use of air monitoring equipment wassuspended for the duration of the work day due to inclement weather (rain); visual and olfactory monitoring were performed during the period that the air monitoring equipment was not in use, and no fugitive dust or odors were detected.										

# Photograph 1 Excavation contractor installing the retaining wall within the antennae COU area, view facing south.




### Photograph 2 Excavation contractor installing the retaining wall within the antennae COU area, view

facing southwest.



# Photograph 3 Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing northeast.



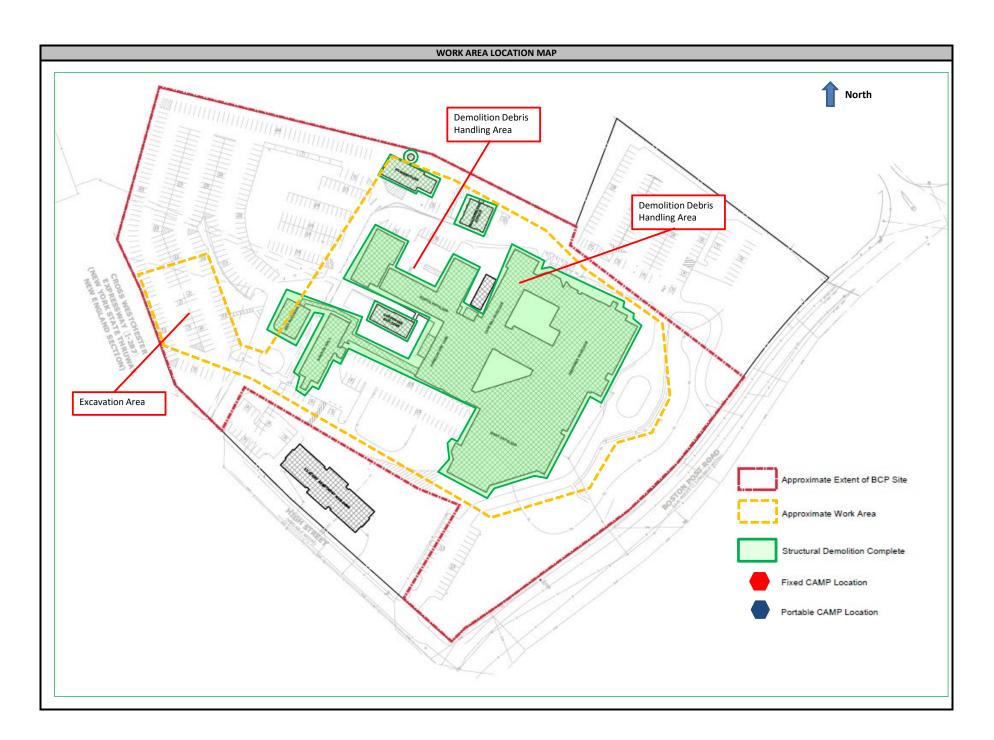

### **Roving CAMP Log** Air Monitoring Log AKRF, Inc. Date: 1/25/24 Client: Rose Project: Former United Hospital Work Activity: Constru Litro of Retaining wall grading course Logged By: M. ext. handling at demo detrisfor disposal Job No: 200057 Weather: 39 - 52 'F Wind Speed: Suph Wind Direction: NNW COMMENTS (activity; work zone, upwind or DUST ODORS LOCATION (ppm) TIME downwind) $(mg/m^3)$ (OU anstrow) ANT NEED AND (II) ND NA noneobserva 0800 WZ Raining 0830 0900 0930 1000 1030 1100 1130 1200 1230 1300 1330 1400 1.430 1500 Community (Perimeter) Action Levels Work Zone Action Levels PID >5 ppm above background: vapor suppression | >0.1 mg/m³ above background: dust suppression <0.150 mg/m<sup>3</sup> above background in breathing ze level D >0.15 mg/m³ above background: STOP >25 ppm above background: STOP >0.150 mg/m³ above background in breathing zo >50 ppm: STOP

	Daily Activity Report									
<b>PAK</b> RF	Former United Hospital									
		Port Chester, NY BCP No. C360202								
Date:		General Site Information Friday, January 26, 2024								
Weather:	Friday, January 26, 2024 Rain, 39-45°F									
Wind Direction/Speed: AKRF Personnel on Site:	ENE @ 5 mph Michael Iodice									
AKRF Equipment on Site:	3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor									
Visitors:	<u> </u>	Contra	ctor Information	Non	e					
Contracting Company		Key Personnel Equipment								
Tony Casale Inc. (Excavation Contractor)		Rigo Diaz  Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.)								
Capital Industries Corp.		loe Cianciulli Various demolition equipment								
(Demolition Contractor)	Joe Cianciulli (e.g., excavators, skid steers, roll off containers, etc.)									
	De	escription and Locati	on of Work Activitie	es Performed						
The excavation contractor continued the construction of a retain	ning wall within the an	tennae Change of Us	e (COU) area.							
The excavation contractor imported Item #4 and 3/4" Stone from	n Tilcon of West Nyac	k, NY for use within t	he antennae COU ar	ea.						
The demolition contractor continued sorting and loading demol	ion debris into contai	ners for off-site dispo	osal.							
		Site Soil Dispo	sal Tracking Informa	ation						
Destination Facility	Daily	Trucks	Daily Approx	Daily Approx. Cubic Yds. Total Site Loads			Total Approximate Cubic Yards			
Clean Earth of Carteret - Carteret, NJ		0 0 35			700					
		Daily Export (CY)			Total Export (CY)		700			
		Imported Fi	l Tracking Informati	on						
Origin Facility	Daily	Trucks	Daily Approx	x. Cubic Yds.	Total Si	te Loads	Total Approximate Cubic Yards			
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)	1	2	28	35	5	66	1,050			
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)		1	2	5	:	2	40			
		Daily Import (CY)	3:	10		Total Import (CY)	1,090			
CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2			
Odors:	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed			
VOC Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No			
Particulate Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No			
		Additi	onal Information							
Planned Work Activity for Following Day(s):  The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  The excavation contractor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer.										
Comments:  The use of air monitoring equipment was suspended for the duration of the work day due to inclement weather (rain); visual and olfactory monitoring were performed during the period that the air monitoring equipment was not in use, and no fugitive dust or odors were detected.										

1 of 4 C360202\_Daily Report\_2024.01.26

## Photograph 1 Excavation contractor importing Item #4 for use within the antennae COU area, view facing west.



### Photograph 2 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing northwest.




### Photograph 3 -

Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing northeast.



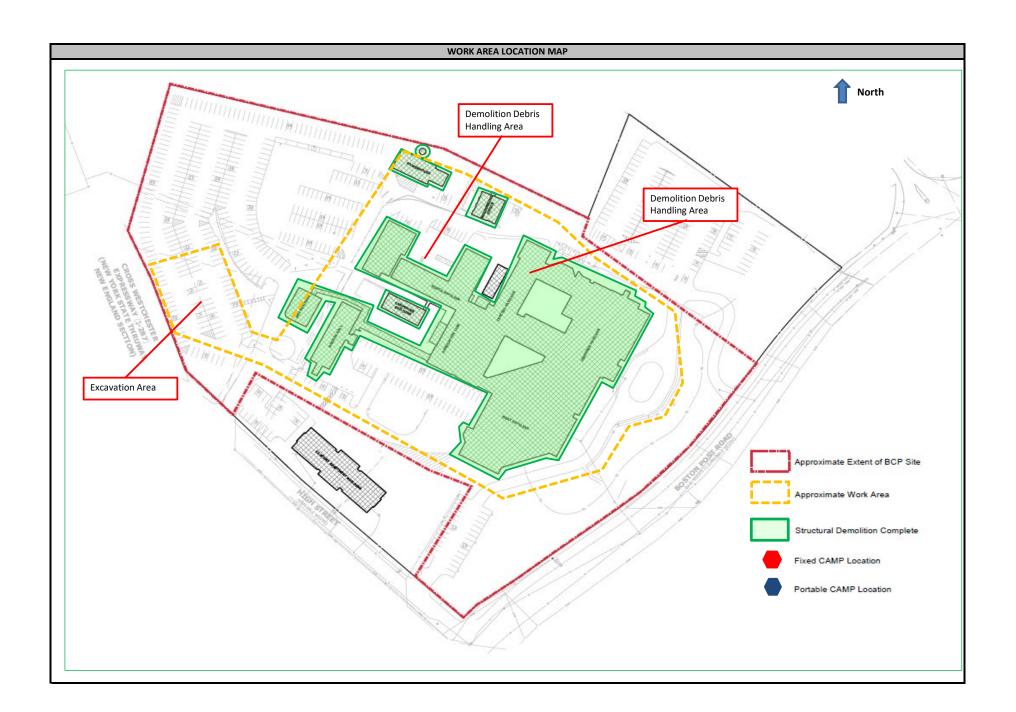

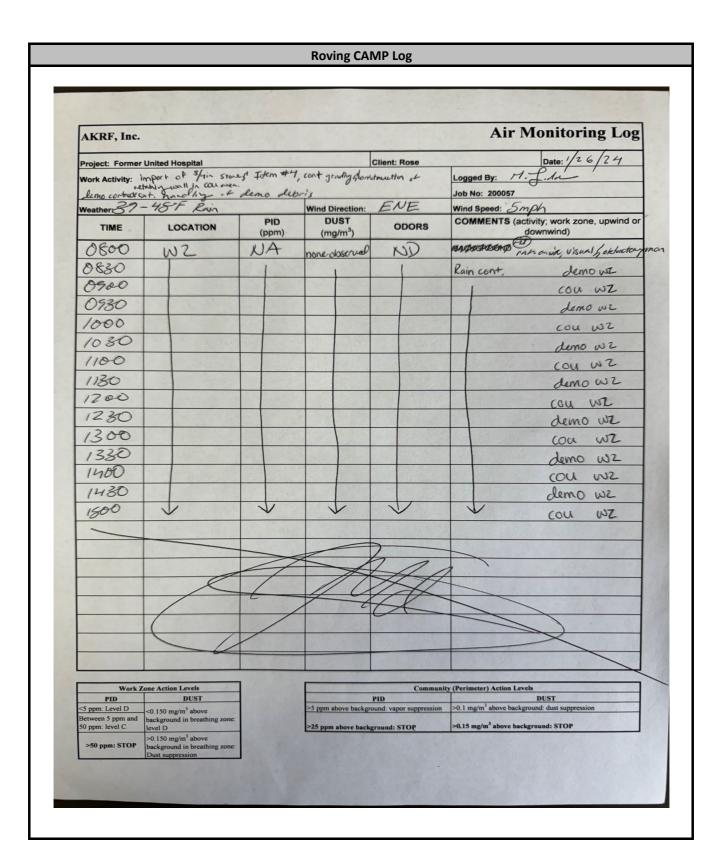

CAKRF	Daily Activity Report  Former United Hospital Port Chester, NY BCP No. C360202										
Date: Weather: Wind Direction/Speed: AKRF Personnel on Site: AKRF Equipment on Site:	General Site Information  Monday, January 29, 2024  Mostly Cloudy, 31-40°F  North @ 14 mph  Michael Iodice  3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor										
Visitors:	5 Fixed CAIV	None  Contractor Information									
Contracting Company  Tony Casale Inc. (Excavation Contractor)	Contractor information  Key Personnel  Rigo Diaz				Equipment  Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.)						
Capital Industries Corp. (Demolition Contractor)		Joe Cia	anciulli		Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)						
				- Berfermed							
The excavation contractor conducted general grading within the			on of Work Activitie	s Performed							
The demolition contractor continued sorting and loading demolti	on debris into contail	ners for off-site disp	osal.								
		Site Soil Dispo	sal Tracking Informa	ntion							
Destination Facility	Daily <sup>1</sup>	Frucks	Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards				
Clean Earth of Carteret - Carteret, NJ	(	0 0		3	35	700					
		Daily Export (CY) 0 Total Export (CY			Total Export (CY)	700					
		Imported Fi	ll Tracking Informati	on							
Origin Facility	Daily '	Trucks	Daily Approx	c. Cubic Yds.	Total Si	te Loads	Total Approximate Cubic Yards				
Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4)	y - West Nyack, NY 0 0 56 1					1,335					
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)	0		0		2		45				
		Daily Import (CY)	(	)		Total Import (CY)	1,380				
CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2				
Odors:	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed				
/OC Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No				
Particulate Action Level Exceedance(s) Above Background:	No	No	No	No	No	No	No				
		Additi	onal Information								
Planned Work Activity for Following Day(s):  The demolition contractor will continue so							ayer.				
Comments:											

1 of 71 C360202\_Daily Report\_2024.01.29

# Photograph 1 Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing southeast.




### Photograph 2 Excavation contractor conducting general grading within the


conducting general grading within the antennae COU area, view facing southwest.




### Photograph 3 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing north.

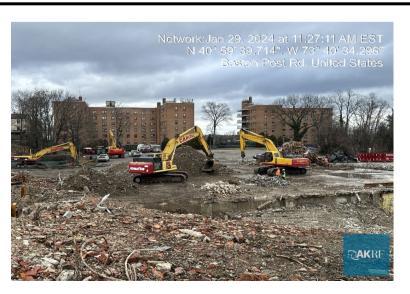


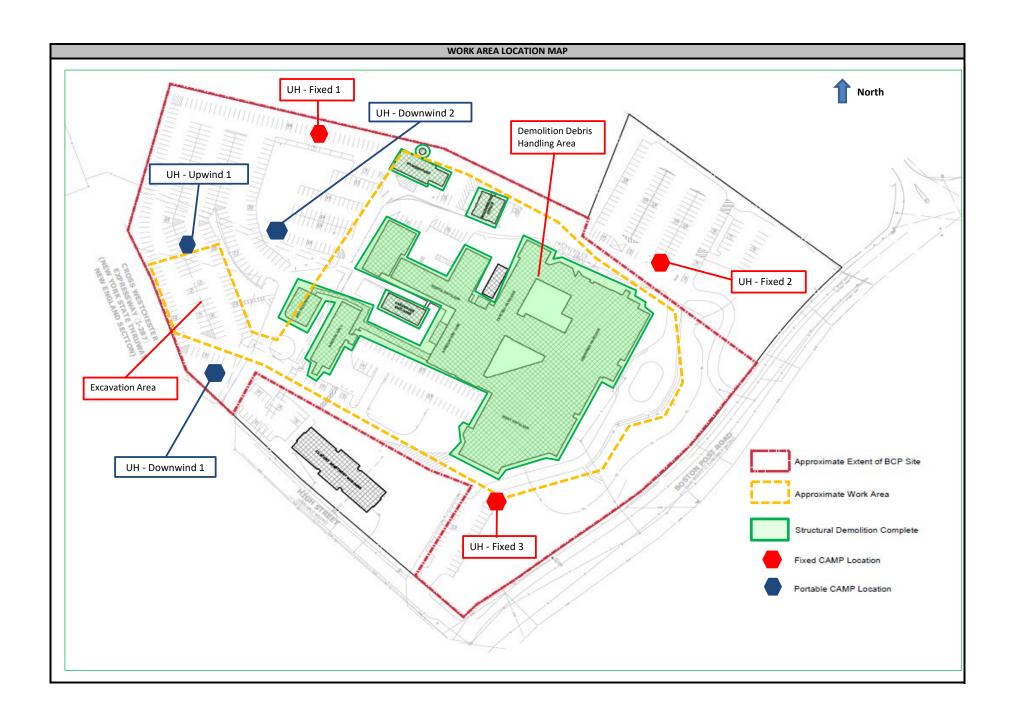



### **Roving CAMP Log** Air Monitoring Log AKRF, Inc. Date: 1/29/23 Project: Former United Hospital Client: Rose Work Activity: Pump water from courant in prepar for concerts pour, propreher Client: Rose Logged By: H. du demo contractor ext. handling of demo debris for disposal Weather: 31-40% Histy Cloudy Wind Direction: North Job No: 200057 Wind Speed: 14 mph PID DUST COMMENTS (activity; work zone, upwind or TIME ODORS LOCATION (ppm) downwind) $(mg/m^3)$ ND BACKGROUND 0800 0.005 WW 0830 WIL 0 0.007 ND 0900 NO NN 0930 OW ND 1000 ND WW 1030 DW ND 0.007 1100 WN 0.004 ND 1130 DW 0.006 ND 200 WW 0.005 ND 1230 DW 0.009 0 ND reg. dust & Fl due to wind gusts, recal. 1300 WW 0.006 ND 0. 1330 DW 0 0.008 ND 1400 Cun 101 1430 OW ND 1800 Wil ND Work Zone Action Levels Community (Perimeter) Action Levels DUST PID DUST <5 ppm: Level D <0.150 mg/m³ above background in breathing zoo level D >0.150 mg/m³ above background in breathing zoo >0.1 mg/m<sup>3</sup> above background: dust suppression >5 ppm above background: vapor suppression Between 5 ppm and 50 ppm: level C >0.15 mg/m³ above background: STOP >25 ppm above background: STOP >50 ppm: STOP

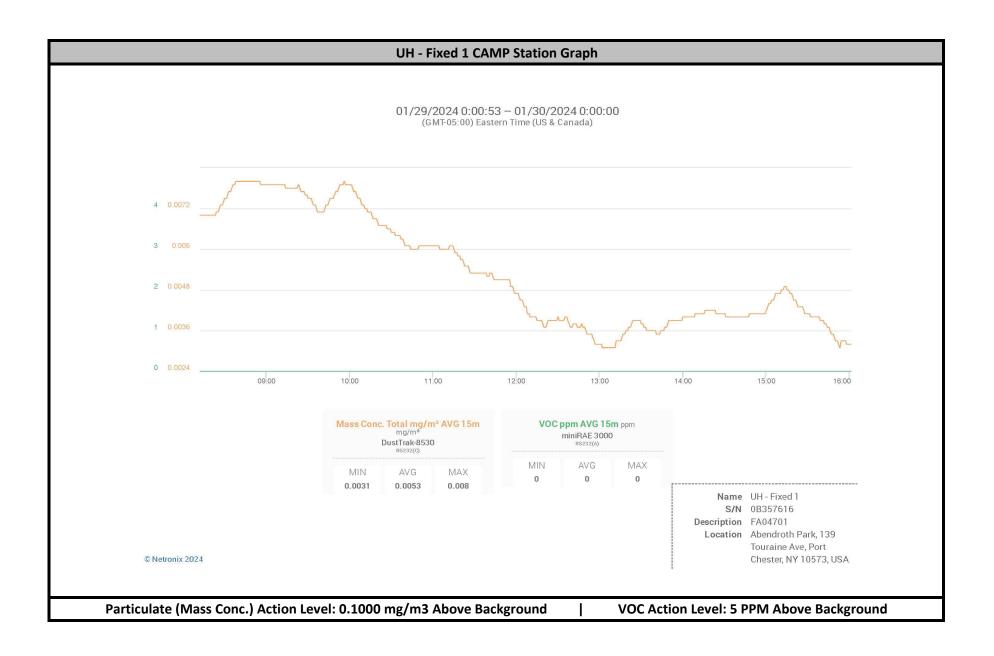


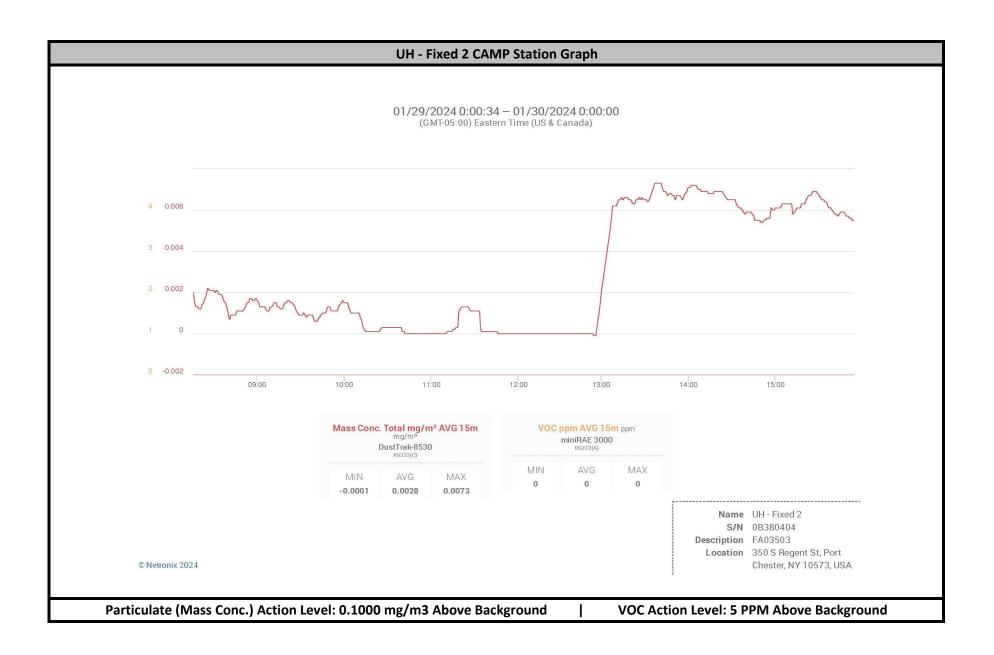

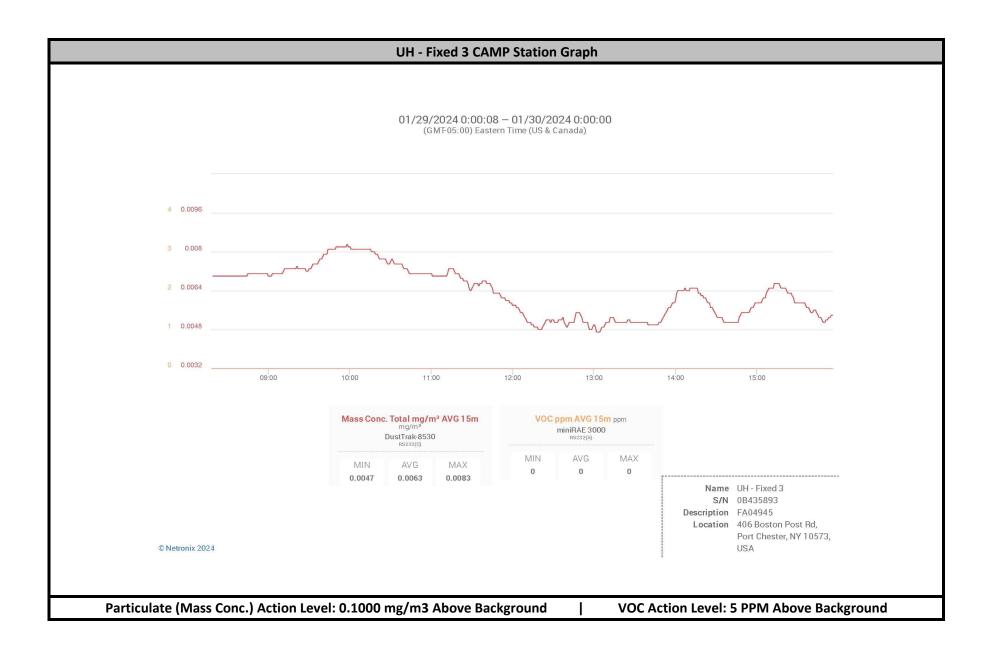

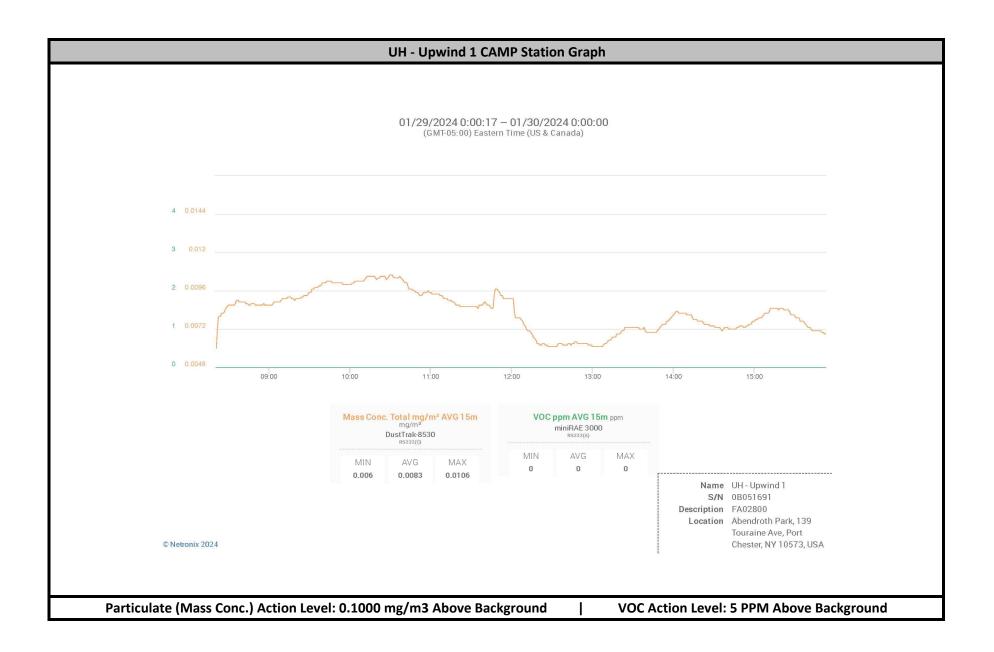

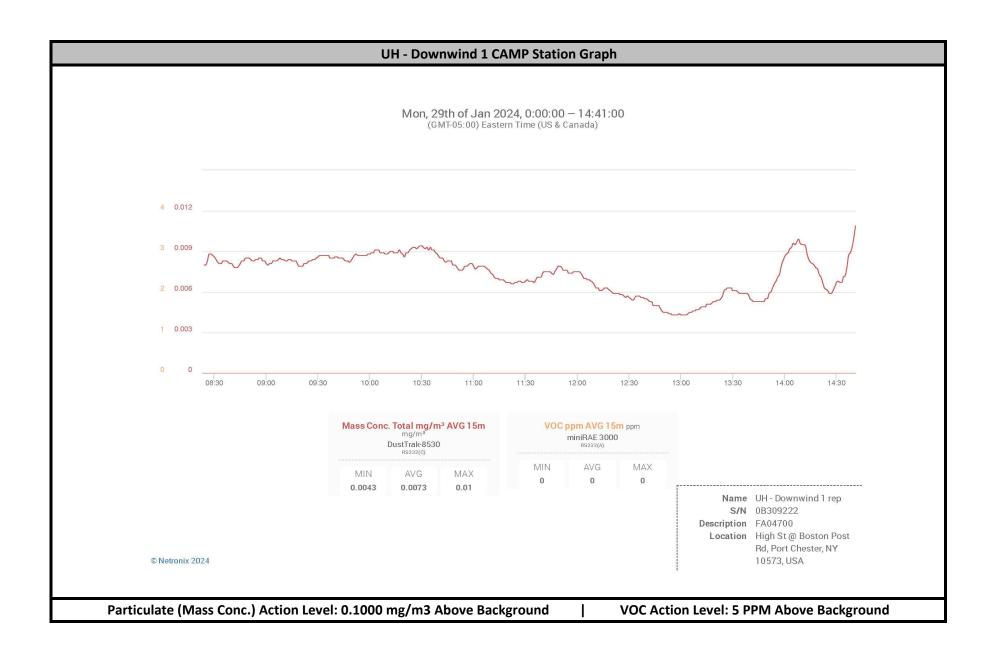

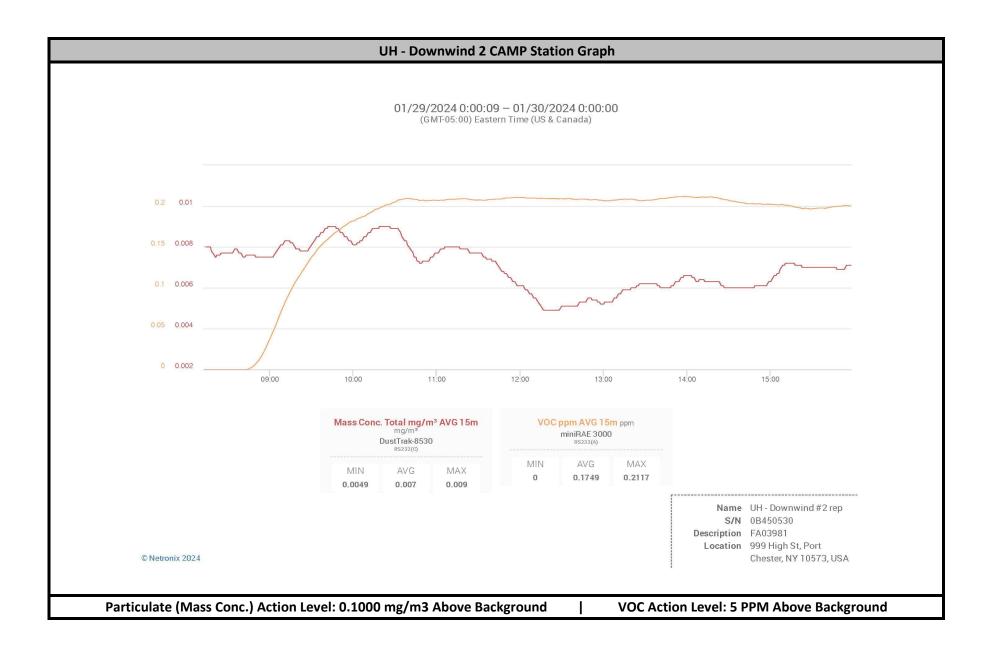

	Daily Activity Report										
<b>PAK</b>	KRF	Former United Hospital Port Chester, NY BCP No. C360202									
			Genera	l Site Information							
Date:		Tuesday, January 30, 2024									
Weather: Wind Direction/Speed	1.				Cloudy, 3						
AKRF Personnel on Sit		North @ 5 mph  Michael Iodice									
AKRF Equipment on Si		3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor									
Visitors:		None									
		Contractor Information									
(	Contracting Company		Key Pe	rsonnel			Equipm	ent			
(E	Tony Casale Inc. Excavation Contractor)	Rigo Diaz				Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.)					
	Capital Industries Corp.  Demolition Contractor)		Joe Cia	nciulli		Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.)					
		De	escription and Locat	on of Work Activitie	es Performed						
The excavation contra	actor conducted general grading within the	antennae Change of	Use (COU) area.								
The demolition contra	actor continued sorting and loading demolti	on debris into contai	iners for off-site disp	osal.							
			Site Soil Dispo	sal Tracking Informa	ation						
	Destination Facility	Daily <sup>·</sup>	Trucks	Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards			
Clean Earth of Cartere	et - Carteret, NJ	0		0		35		700			
		Daily Export (CY)		0		Total Export (CY)		700			
			Imported Fi	ll Tracking Informati	on						
	Origin Facility	Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards			
Tilcon West Nyack Qua (ITEM #4)	arry - West Nyack, NY		0	C	)	5	66	1,335			
Tilcon West Nyack Qua (NY2/ASTM #5 - 3/4" S		0		0		2		45			
			Daily Import (CY)	(	0 Total Imp		Total Import (CY)	1,380			
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2			
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed			
/OC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No			
Particulate Action Leve	el Exceedance(s) Above Background:	No	No	No	No	No	No	No			
			Additi	onal Information							
Planned Work Activity for Following Day(s):  The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.  The excavation contractor will continue to import item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer											
Comments:	None.										

1 of 65 C360202\_Daily Report\_2024.01.30

### Photograph 1 Excavation contractor conducting general grading within the antennae COU area,

view facing southwest.



### **Photograph 2 -**Demolition


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing north.





### Photograph 3 -


Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing north.




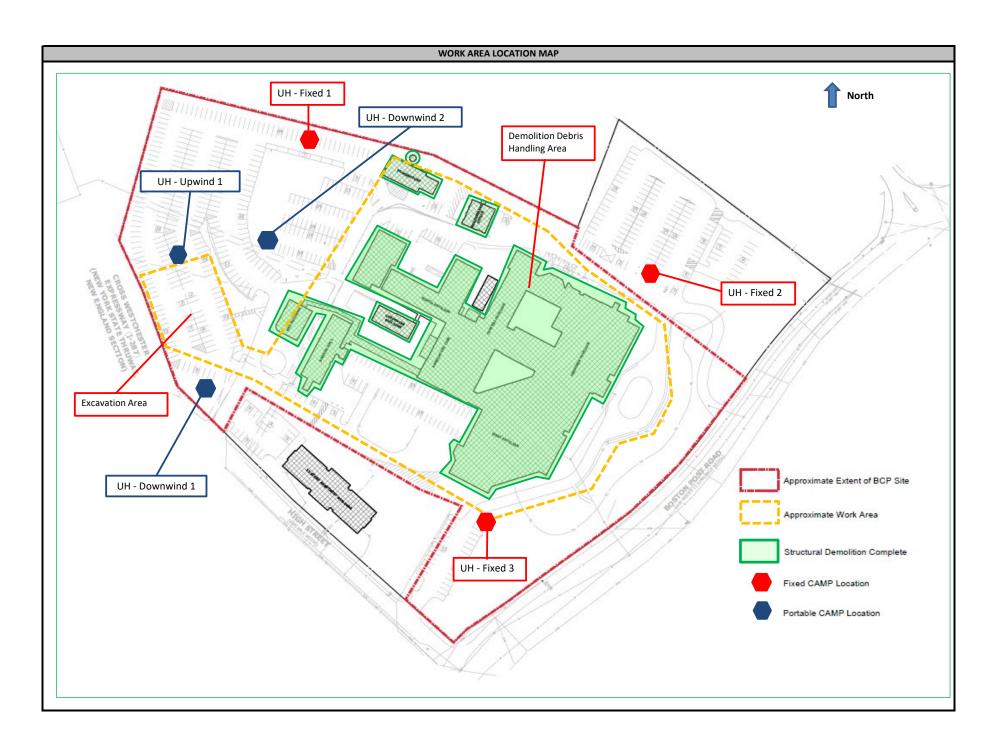


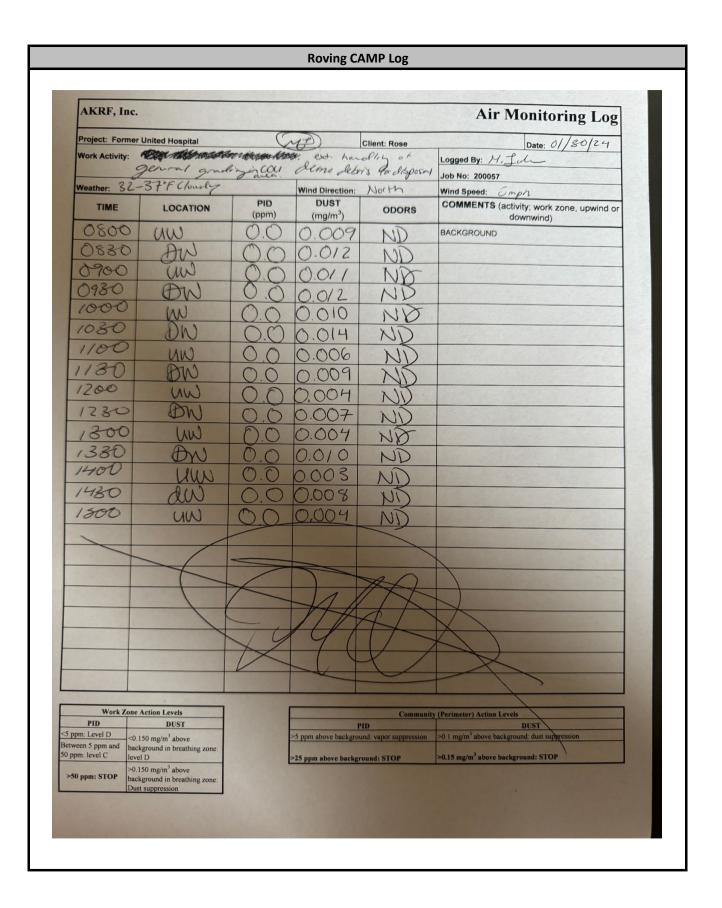


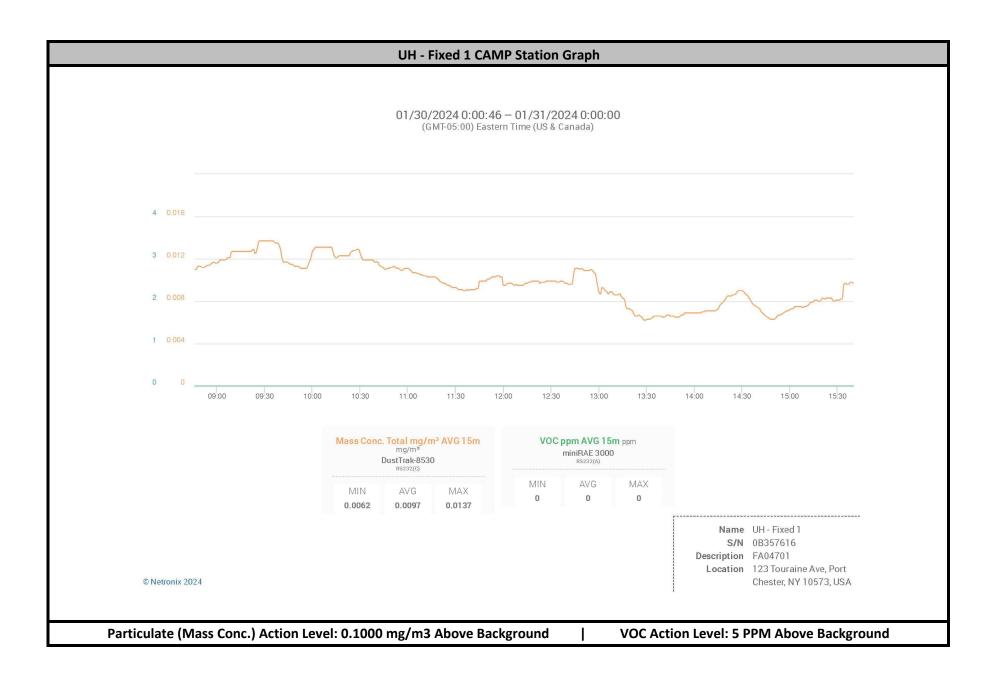


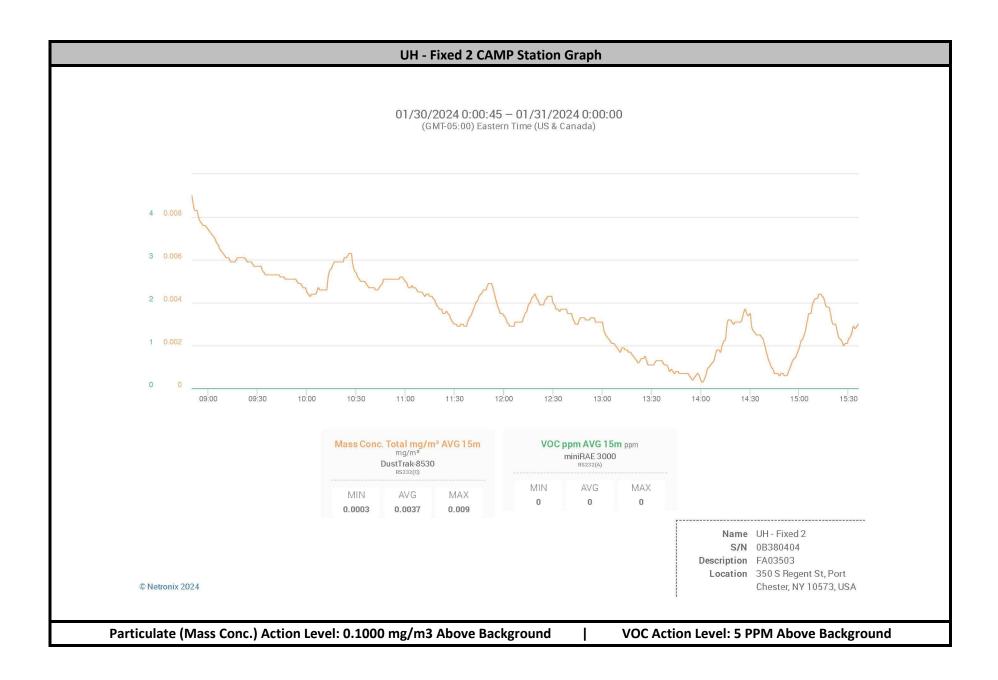

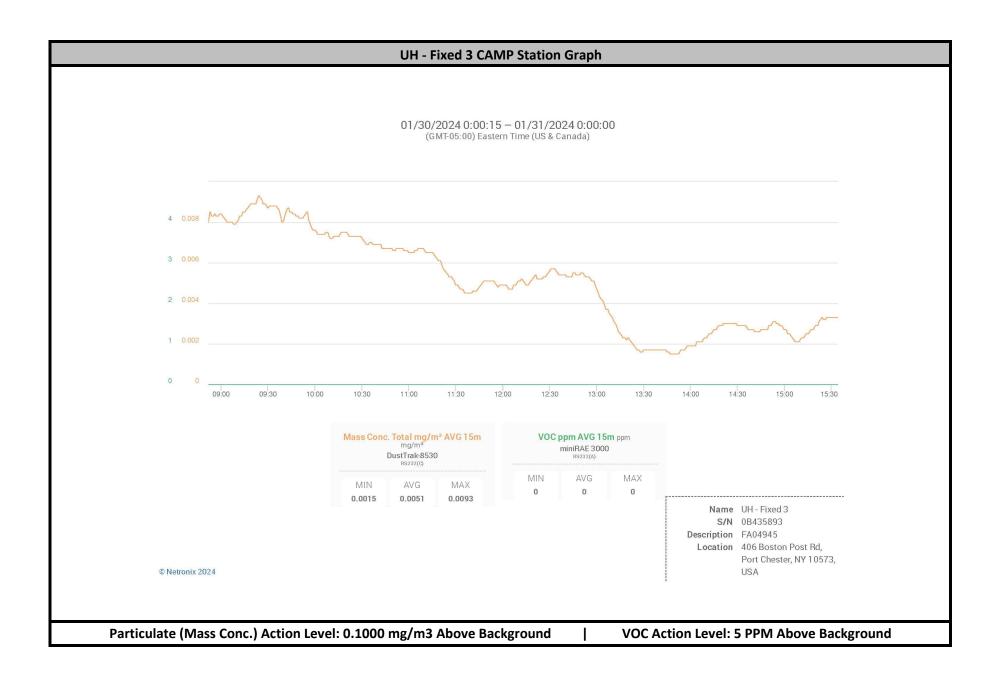

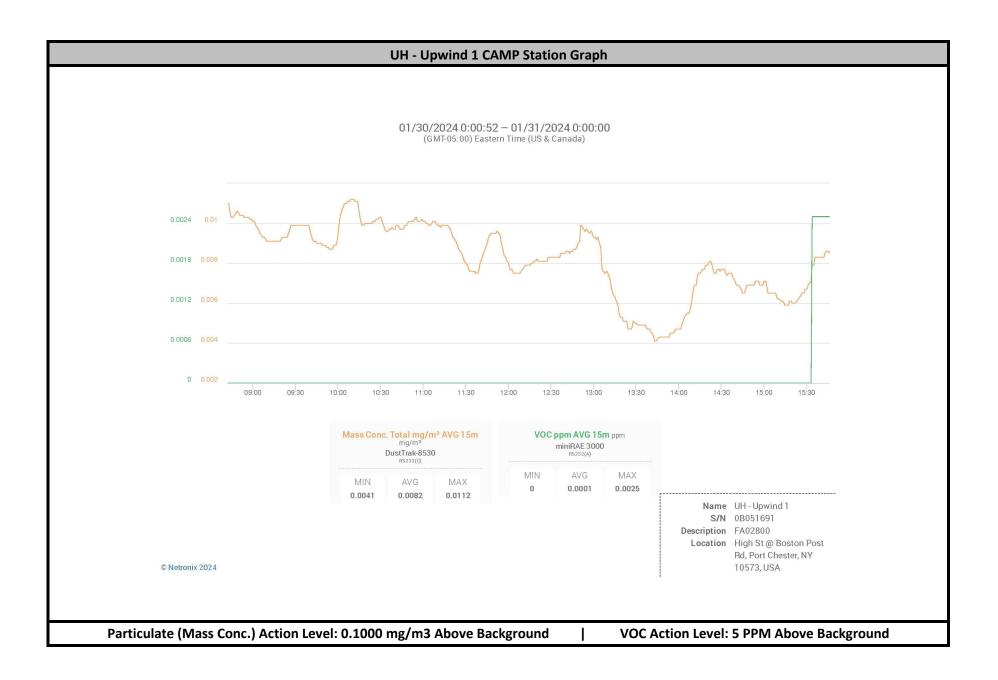

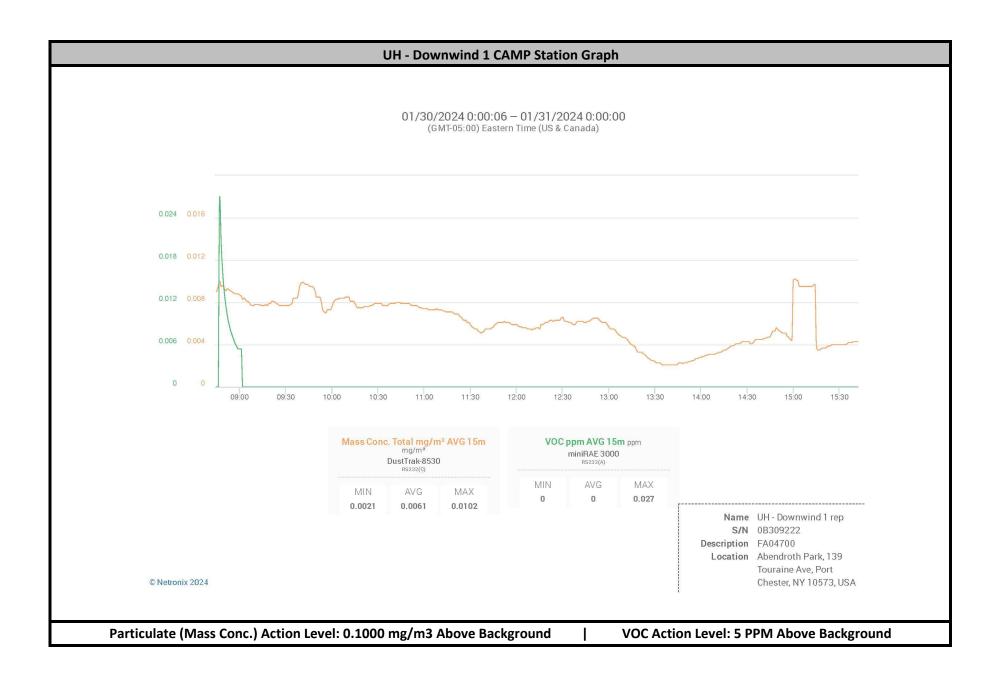

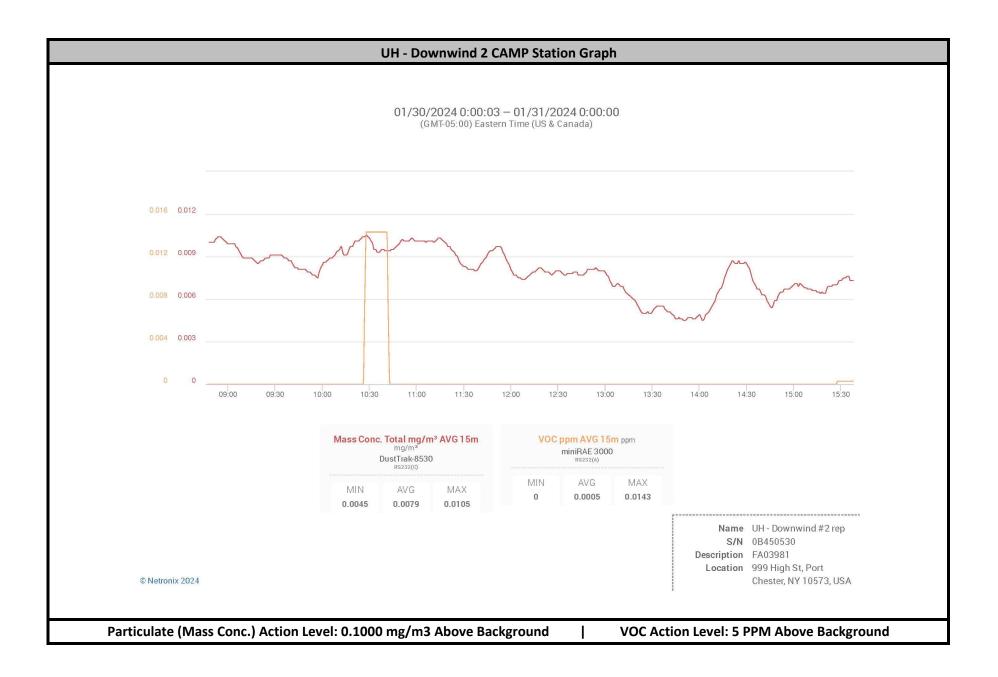

		Daily Activity Report						
<b>CAK</b> RF		Former United Hospital						
		Port Chester, NY BCP No. C360202						
			Genera	I Site Information	BCF NO. C	500202		
Date: Weather:					Wednesday, Janu Mostly Cloud			
Wind Direction/Speed		South @ 4 mph						
AKRF Personnel on Sit AKRF Equipment on S		Michael Iodice  3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor						
Visitors:	ite.	3 TIXCO CAIV		**	Non-		, one Handrick Fib,	One Hamanela Buse Wormeon
	Contracting Company	Contractor Information  Key Personnel					Equipm	ent
	Tony Casale Inc.					Vai	rious excavation and	
(Excavation Contractor)		Rigo Diaz				(e.g., ex	cavators, compactor	s, roller-compactor, etc.)
	Capital Industries Corp. Demolition Contractor)	Joe Cianciulli			Various demolition equipment (e.g., excavators, skid steers, roll off containers, et			
		Di	escription and Locat	ion of Work Activitie	es Performed			
The excavation contra	actor conducted general grading, and assem							
The demolition contra	actor continued sorting and loading demolti	ion debris into conta	iners for off-site disp	osal.				
			Site Soil Dispo	osal Tracking Informa	ation			
Destination Facility		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards
Clean Earth of Carteret - Carteret, NJ		0		0		35		700
		Daily Export (CY)		0		Total Export (CY)		700
			Imported Fi	ll Tracking Informati	on			
Origin Facility		Daily Trucks		Daily Approx. Cubic Yds.		Total Site Loads		Total Approximate Cubic Yards
Tilcon West Nyack Quarry - West Nyack, NY		0		0		56		1 225
(ITEM #4)		U		0		30		1,335
Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone)		0		0		2		45
		Daily Import (CY)		0		Total Import (CY)		1,380
	CAMP Information	Roving Equipment	UH - Fixed 1	UH - Fixed 2	UH - Fixed 3	UH - Upwind 1	UH - Downwind 1	UH - Downwind 2
Odors:		None Observed	None Observed	None Observed	None Observed	None Observed	None Observed	None Observed
VOC Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No
Particulate Action Level Exceedance(s) Above Background:		No	No	No	No	No	No	No
			Additi	onal Information				
Planned Work Activity for Following Day(s):	The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal.							
	he excavation contratcor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer. The excavation contractor will xcavate the SB-54 hotspot to bedrock (anticipated at 11 feet below grade) for off-site disposal.							
Comments:	Due to cellular connectivity issues, the UH - Fixed 3 CAMP station did not report particulate data from approximately 12:52 until the end of the work day. During the time that the CAMP station was not eporting particulate data visual observations were conducted in the area, and no fugitive particulates were noted.							

1 of 71 C360202\_Daily Report\_2024.01.31

## **Site Photographs**

## Photograph 1 Excavation contractor conducting general grading within the antennae COU area, view facing southwest.



## Photograph 2 -Demolition contractor handling

contractor handling structural demolition debris in the eastern portion of the site, view facing north.



## Photograph 3 -

Demolition contractor handling structural demolition debris in the eastern portion of the site, view facing north.



