

Environmental, Planning, and Engineering Consultants

440 Park Avenue South 7th Floor New York, NY 10016 tel: 212 696-0670 fax: 212 213-3191 www.akrf.com

March 18, 2024

Mr. Matthew Hubicki NYS Department of Environmental Conservation Division of Environmental Remediation 625 Broadway Albany, New York 12233-7016

Re: Monthly Progress Report – February 2024

Former United Hospital – 406 Boston Post Road, Port Chester, New York

NYSDEC BCP Site No. C360202

Dear Mr. Hubicki:

This Monthly Progress Report has been prepared by AKRF, Inc. (AKRF) to summarize the work performed at the Former United Hospital site located at 406 Boston Post Road in Port Chester, New York [New York State Department of Environmental Conservation (NYSDEC) Brownfield Cleanup Program (BCP) Site No. C360202] (the Site) during the month of February 2024. The following activities were conducted:

- The demolition contractor continued with the handling of building materials (sorting of scrap metal, and concrete and demolition debris for off-site disposal) associated with Phase 3 (Structural Demolition) of the former hospital buildings. As the work included the exterior handling of building materials associated with the demolition of exterior and interior building elements (partition walls, drop ceilings, mechanical equipment, etc.), AKRF implemented the full-scale Community Air Monitoring Program (CAMP)/environmental monitoring included in the Remedial Investigation Work Plan (RIWP) during each workday. A total of six CAMP stations (three fixed stations deployed at the same location each day and three portable stations that were adjusted daily for changes in wind and/or work zones) were deployed prior to the start of each workday. Each CAMP station was equipped with a photoionization detector (PID) and dust monitor capable of calculating 15-minute running averages for volatile organic compound (VOC) and particulate concentrations, respectively, and a NetronixTM Global System for Mobile Communication (GSM)/Global Positioning System (GPS) device capable of recording air monitoring and location data. All air monitoring data was posted on a password-protected, project-specific, online database and was regularly downloaded/saved, with real-time e-mail/mobile alerts sent to AKRF staff to indicate action level exceedances (if any). A Daily Activity Report was prepared and submitted to NYSDEC and NYSDOH for each workday, which documented the work completed that day, provided the schedule for near-term field work, and included a summary of the findings from the CAMP monitoring activities. Copies of the Daily Activity Reports are included in Attachment A of this Monthly Progress Report.
- Within the antennae Change of Use area (COU), the excavation contractor extended the RI-SB-54 hotspot to bedrock, encountered at approximately 10 feet below grade, as the shallower endpoint and contingency endpoint samples did not achieve results below the RRSCOs. Following the excavation, a demarcation layer was placed at the base of the excavation, and the excavation was backfilled with NYCDEC-approved Item #4 and 34" stone.

- The excavation contractor continued construction of a retaining wall and poured the concrete pad for the future antennae within the antennae COU area.
- Two loads (approximately 10 cubic yards) of soil generated from the RI-SB-54 hotspot excavation within the antennae COU area was exported for off-site disposal at Clean Earth of Carteret in Carteret, NJ.
- The excavation contractor imported 67 loads of NYSDEC-approved Item #4 (approximately 1,965 cubic yards) and three loads of 3/4" stone (approximately 75 cubic yards) for use as structural backfill above the demarcation layer within the antennae COU area.
- The electrical contractor installed two utility poles within the boundary of the BCP Site using a truck-mounted auger. No soil was generated during the utility pole installations.
- During all work that occurred within the antennae COU area, AKRF continued to implement the full-scale CAMP/environmental monitoring included in the RIWP, utilizing six CAMP stations as detailed previously. Locations of the CAMP stations were modified in accordance with email correspondence between AKRF and NYSDEC dated November 15, 2023 to accurately reflect the work area.

The following work is planned for March 2024:

- AKRF will continue implementation of full-scale CAMP/environmental monitoring during active structural demolition, the handling of building materials associated with structural demolition (sorting of scrap metal, and concrete and demolition debris for off-site disposal), and any excavation activities within the antennae COU area, with the aforementioned activities expected to conclude in early March 2024.
- Site work related to the antennae construction under the Change of Use Notification dated September 7, 2023 will continue. Work is anticipated to consist of grading and compaction activities.
- AKRF will continue preparation of the Remedial Investigation report (RIR), which is anticipated to be submitted to NYSDEC in March 2024.
- AKRF will continue preparation of the Remedial Action Work Plan (RAWP), which is anticipated to be submitted to NYSDEC in April 2024.
- Following the completion of demolition and excavation activities at the Site, AKRF plans to demobilize from the Site in early March. AKRF will return to the Site and resume CAMP implementation upon the resumption of full-scale site work under the RAWP anticipated in the fourth quarter of 2024.

If you have any questions regarding the information presented in this letter, please contact me at (914) 400-9736.

Sincerely, AKRF Inc.

Stephen Schmid

Senior Environmental Scientist

cc (electronic copy only):

Kerry Maloney – NYSDEC Angela Martin – NYSDOH

Christopher Gibaldi, Aaron Levy – Boston Post Road Owner LLC

Christine Leas – Sive, Paget & Riesel P.C.

Marc Godick, Tim McClintock - AKRF

ATTACHMENT A DAILY ACTIVITY REPORTS

| PAK RF | | Daily Activity Report Former United Hospital | | | | | | | |
|---|----------------------------------|---|-----------------------|--------------------------------|------------------------|---|--|--|--|
| CAKIT | Port Chester, NY BCP No. C360202 | | | | | | | | |
| | | General Site Information Thursday, February 1, 2024 | | | | | | | |
| Date: Weather: | | | | Thursday, Febr Mostly Cloud | | | | | |
| Wind Direction/Speed: AKRF Personnel on Site: | | SW @ 7 mph Michael lodice | | | | | | | |
| AKRF Equipment on Site: | 3 Fixed CAN | 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor None | | | | | | | |
| Visitors: | | Contra | actor Information | Non | e | | | | |
| Contracting Company | | Key Personnel Equipment | | | | | | | |
| Tony Casale Inc. (Excavation Contractor) | | Rigo Diaz Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.) | | | | | | | |
| Capital Industries Corp. (Demolition Contractor) | | Joe Cia | anciulli | | (e.g., ex | Various demolitic cavators, skid steers, | on equipment , roll off containers, etc.) | | |
| | De | escription and Locat | ion of Work Activitie | es Performed | | | | | |
| The excavation contractor conducted general grading, and c | onstructed rebar and con | crete forms within th | ne antennae Change | of Use (COU) area. | | | | | |
| The excavation contractor excavated the 10x10 ft area of ho | stpot SB-54 to bedrock, a | nd survey points of t | he new bottom dept | h were recorded. Sc | oil was exported for o | off-site disposal at Cle | ean Earth of Carteret, NJ. | | |
| The demolition contractor continued sorting and loading de | moltion debris into contai | ners for off-site disp | osal. | | | | | | |
| | | Site Soil Dispo | osal Tracking Informa | ation | | | | | |
| Destination Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Site Loads | | Total Approximate Cubic Yards | | |
| Clean Earth of Carteret - Carteret, NJ | | 2 | | 10 | | 37 | 710 | | |
| | | Daily Export (CY) | | 10 | | Total Export (CY) | 710 | | |
| | | Imported Fi | II Tracking Informati | on | | | | | |
| Origin Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards | | |
| Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4) | | 0 | C |) | 56 1,335 | | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | 45 | | |
| | | Daily Import (CY) | (|) | | Total Import (CY) | 1,380 | | |
| CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| VOC Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| Particulate Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| | • | | | | | | | | |
| Planned Work Activity for Following Day(s): The demolition contractor will conting the excavation contractor will conting related to the antennae installation. | | demolition debris fro | • | _ | | • | ayer, and continue construction | | |
| Comments: None. | | | | | | | | | |

1 of 70 C360202_Daily Report_2024.02.01

Photograph 1 Excavation contractor conducting general grading within the antennae COU area, view facing southwest.




Photograph 2 Excavation contractor loading soil from the SB-54 hotspot for offsite disposal, view facing northwest.





Photograph 3 Demolition contractor handling structural demolition debris in the central portion of the site, view facing north.




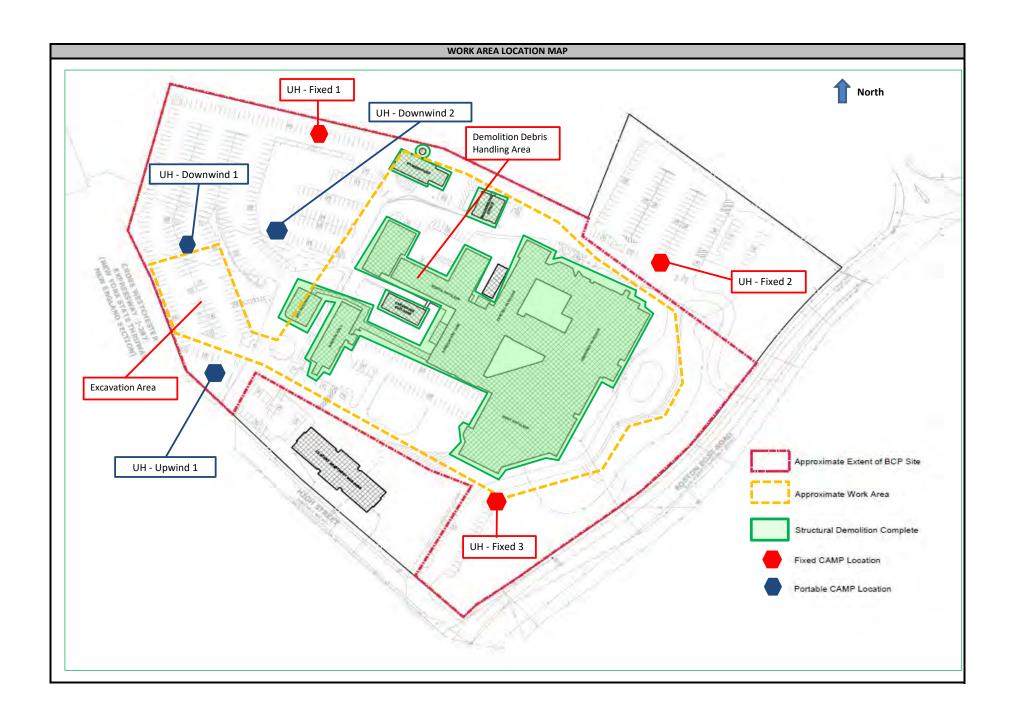



Roving CAMP Log Air Monitoring Log AKRF, Inc. Date: 02/01/24 Client: Rose Project: Former United Hospital Work Activity: ext. handling of demo debnis for disposal Logged By: Hold Job No: 200057 Weather: 32-44°F Mostly Cloudy Wind Direction: 500 Wind Speed: 7mph PID DUST COMMENTS (activity; work zone, upwind or ODORS TIME LOCATION downwind) (ppm) (mg/m^3) BACKGROUND UN 0800 0.041 UN DW 0.047 NY 0830 ND 0900 CUN 0.038 0.0 NI 0930 DW 0. 0.064 1000 0.060 NB CUN NO DW 0 0.063 1030 1100 WN 0 CIM 0.057 1130 DW 0.052 NB 1200 2.060 UND 1280 DW 0.071 ND 0 ND 1300 WN 0.043 NI DW 0.068 0 1330 M 0 UN 0.042 1400 ND 0.060 DW 1480 ND 0.036 MN 1800 Community (Perimeter) Action Levels Work Zone Action Levels PID >0.1 mg/m3 above background; dust suppre <0.150 mg/m³ above background in breathing zo >5 ppm above background: vapor suppression <5 ppm: Level D Between 5 ppm and >0.15 mg/m³ above background: STOP >25 ppm above background: STOP level D 50 ppm: level C >0.150 mg/m³ above background in breathing >50 ppm: STOP

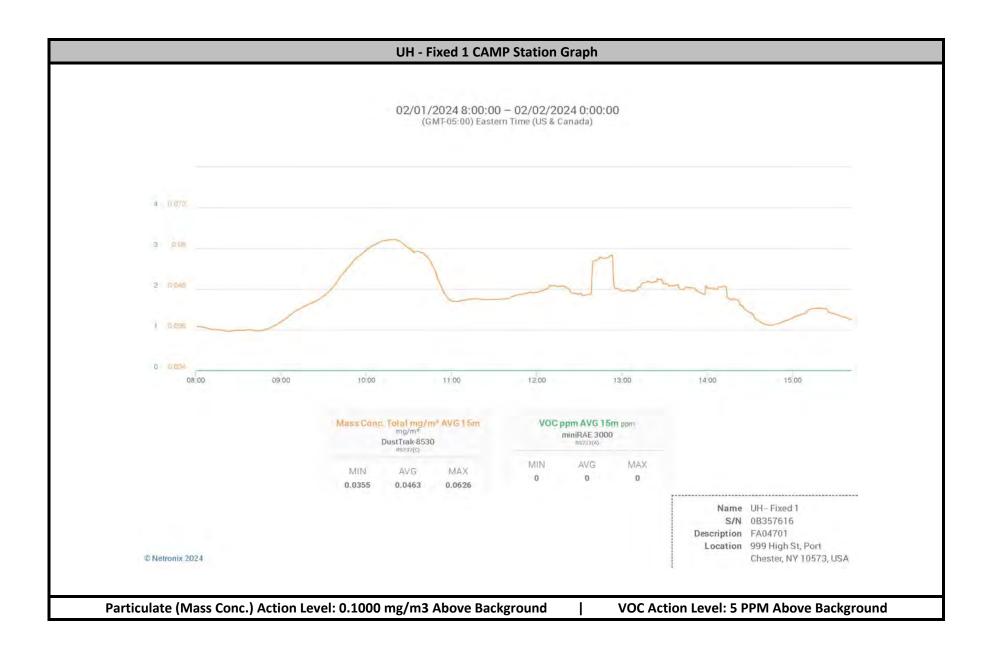


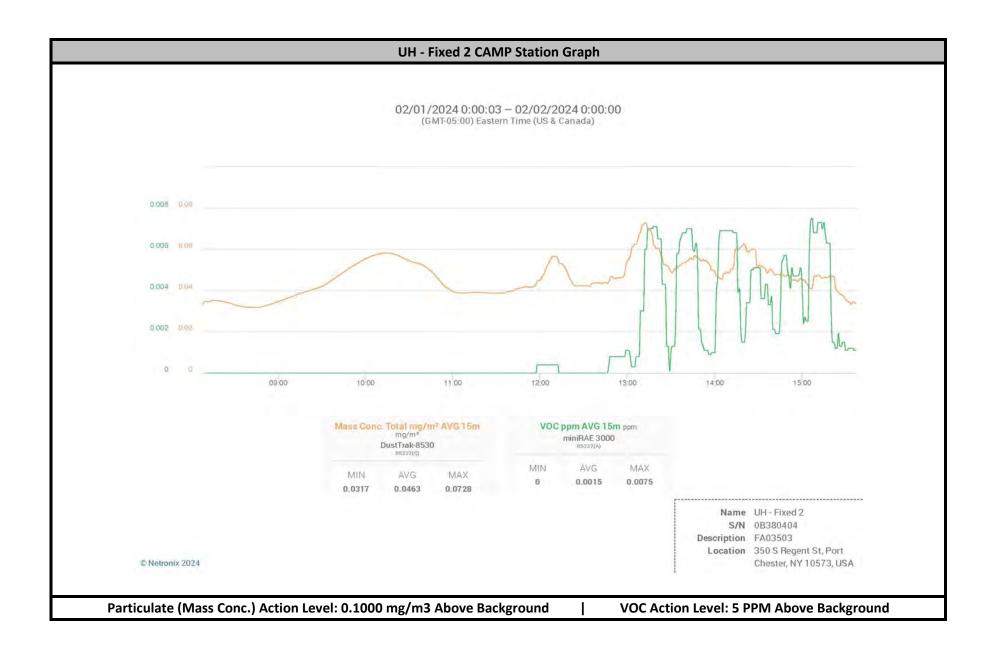

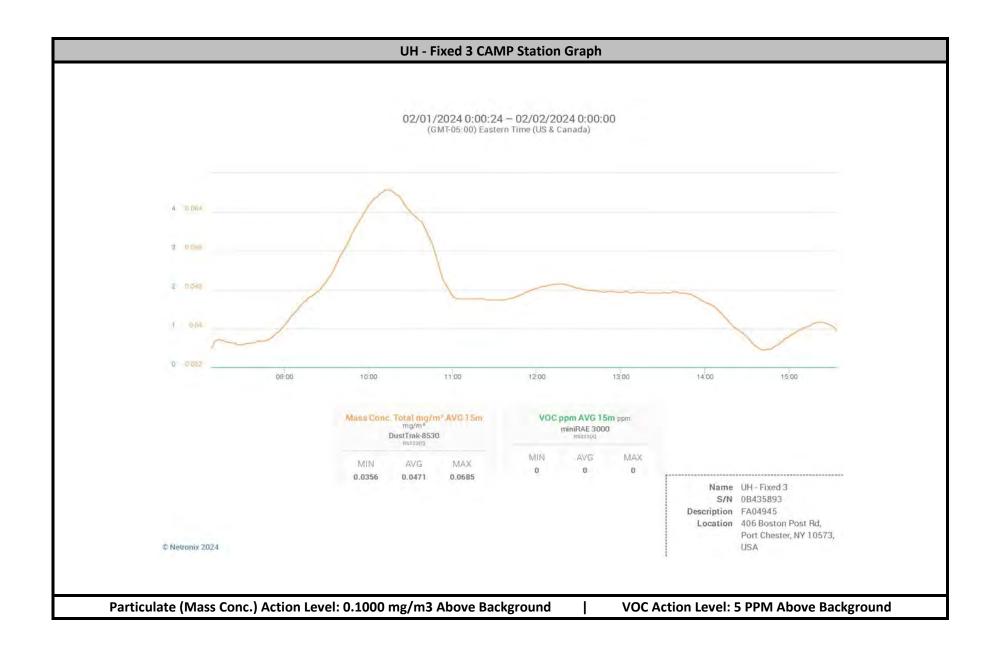

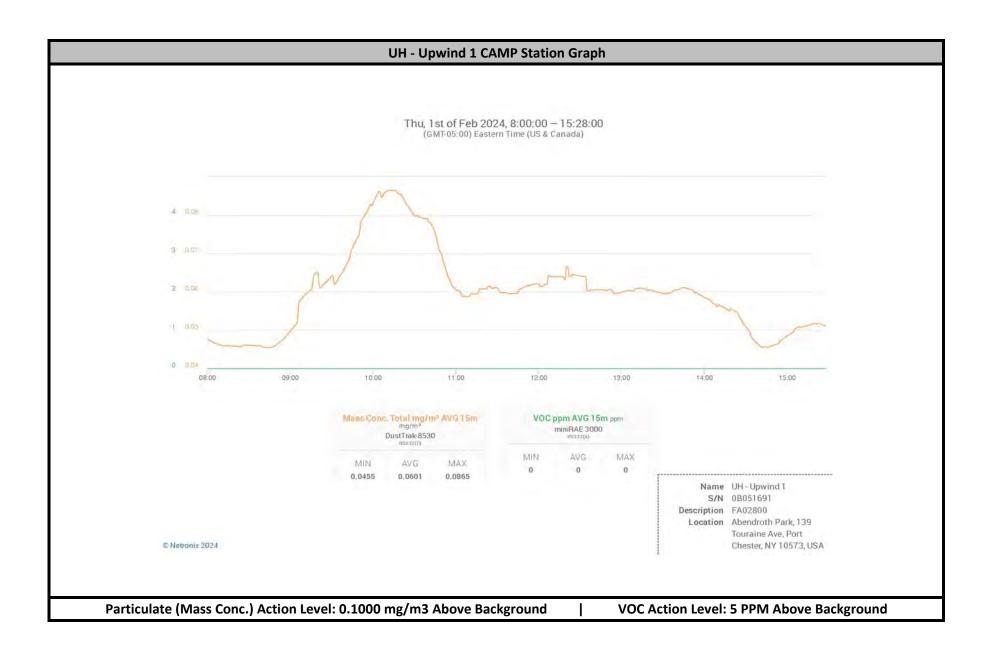

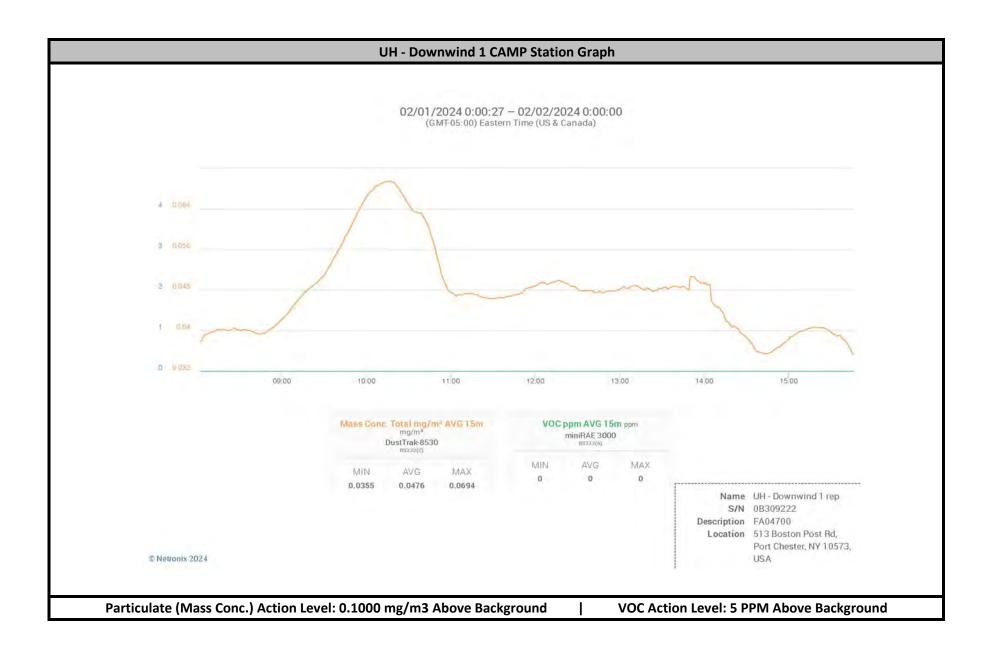

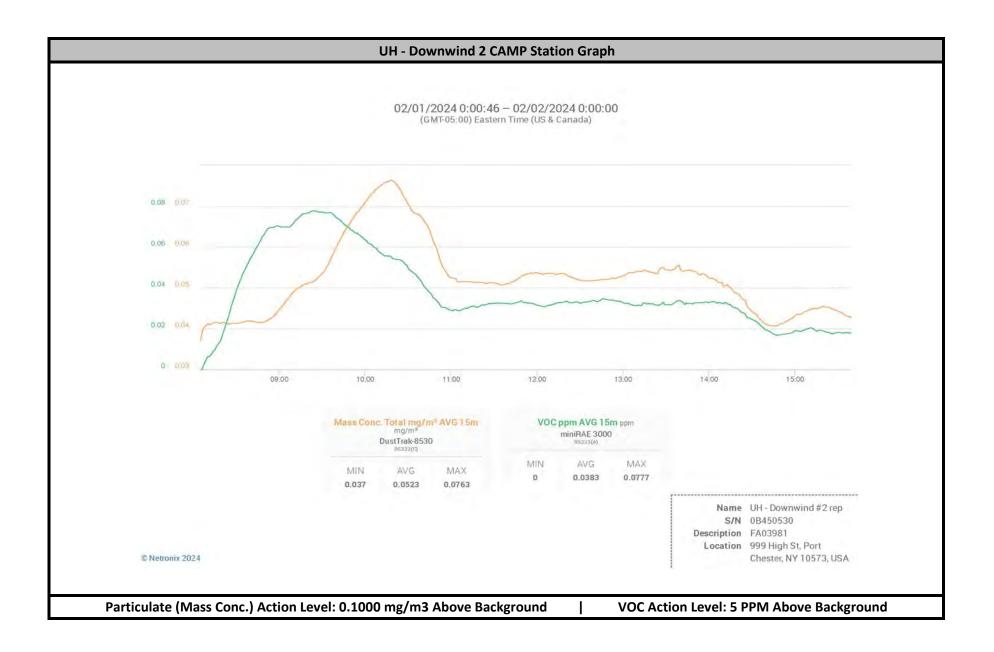

| | Daily Activity Report | | | | | | | | | |
|--|---|--|-------------------------|-----------------------|----------------------|----------------------|------------------------|-------------------------------|--|--|
| | Former United Hospital Port Chester, NY BCP No. C360202 | | | | | | | | | |
| | | | | | | | | | | |
| Date | | | Genera | l Site Information | | | | | | |
| Date: Weather: | | Friday, February 2, 2024 Rain, 32-43°F | | | | | | | | |
| Wind Direction/Speed AKRF Personnel on Site | | North @ 7 mph Michael Iodice | | | | | | | | |
| AKRF Equipment on Si Visitors: | | 3 Fixed CAN | IP Stations (PID & Du | st Monitor), 3 Portal | | PID & Dust Monitor) | , One Handheld PID, | One Handheld Dust Monitor | | |
| | | | | ctor Information | NOII | • | | | | |
| (| Contracting Company Tony Casale Inc. | Key Personnel Equipment Various excavation and grading equipment | | | | | | | | |
| (E | excavation Contractor) | Rigo Diaz Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.) | | | | | | | | |
| | apital Industries Corp. | | Joe Cia | nciulli | | (o.g. ov | Various demolitic | | | |
| (L | Demolition Contractor) | | | | | (e.g., ex | cavators, skiu steers, | , roll off containers, etc.) | | |
| | | De | escription and Locat | ion of Work Activitie | es Performed | | | | | |
| The excavation contra | ctor conducted general grading, and const | ructed rebar and con | crete forms within th | e antennae Change | of Use (COU) area. | | | | | |
| The excavation contra | ctor backfilled the SB-54 hotspot excavatio | n within the antenna | e COU with 3/4" sto | ne and Item #4 that I | had been previously | imported to the Site | e from Tilcon of Wes | t Nyack, NY. | | |
| The demolition contra | ctor continued sorting and loading demolti | on debris into contai | ners for off-site disp | osal. | | | | | | |
| | | | Site Soil Dispo | sal Tracking Informa | ation | | | | | |
| | Destination Facility | Daily ¹ | Trucks | Daily Approx | ι. Cubic Yds. | Total Site Loads | | Total Approximate Cubic Yards | | |
| Clean Earth of Cartere | t - Carteret, NJ | (| ס | C |) | 37 | | 710 | | |
| | | | Daily Export (CY) | C |) | | Total Export (CY) | 710 | | |
| | | | Imported Fi | ll Tracking Informati | ion | | | | | |
| | Origin Facility | Daily ' | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards | | |
| Tilcon West Nyack Qua (ITEM #4) | arry - West Nyack, NY | (| ס | O |) | 56 1,335 | | | | |
| Tilcon West Nyack Qua (NY2/ASTM #5 - 3/4" S | | (|) | 0 | | 2 45 | | | | |
| | | | Daily Import (CY) | C |) | | 1,380 | | | |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| VOC Action Level Exce | edance(s) Above Background: | No | No | No | No | No | No | No | | |
| Particulate Action Leve | el Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| | | | | | | | | | | |
| | | | Additi | onal Information | | | | | | |
| | The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal. | | | | | | | | | |
| Planned Work Activity for Following The excavation contratcor will continue to import item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer. | | | | | | | | | | |
| Day(s): The antenna structure will be delivered to the site, and utility pole installation will be conducted by an electrical subcontractor. | | | | | | | | · • - | | |
| | rne antenna structure will be delivered to | tne site, and utility p | oie installation will b | e conducted by an e | iectrical subcontrac | tor. | | | | |
| | Due to inclement weather (rain); the use of air monitoring equipment was suspended during the work day. Visual and olfactory monitoring were performed during the period that the air monitoring equipment was not in use, and no fugitive dust or odors were detected. | | | | | | | | | |

1 of 4 C360202_Daily Report_2024.02.02

Photograph 1 Excavation contractor conducting general grading and concrete form assembly within the antennae COU area, view facing southwest.





Photograph 2 Excavation contractor backfilling the SB-54 hotspot area with Item #4, view facing southwest.



Photograph 3 Demolition contractor handling structural demolition debris in the central portion of the site, view facing north.



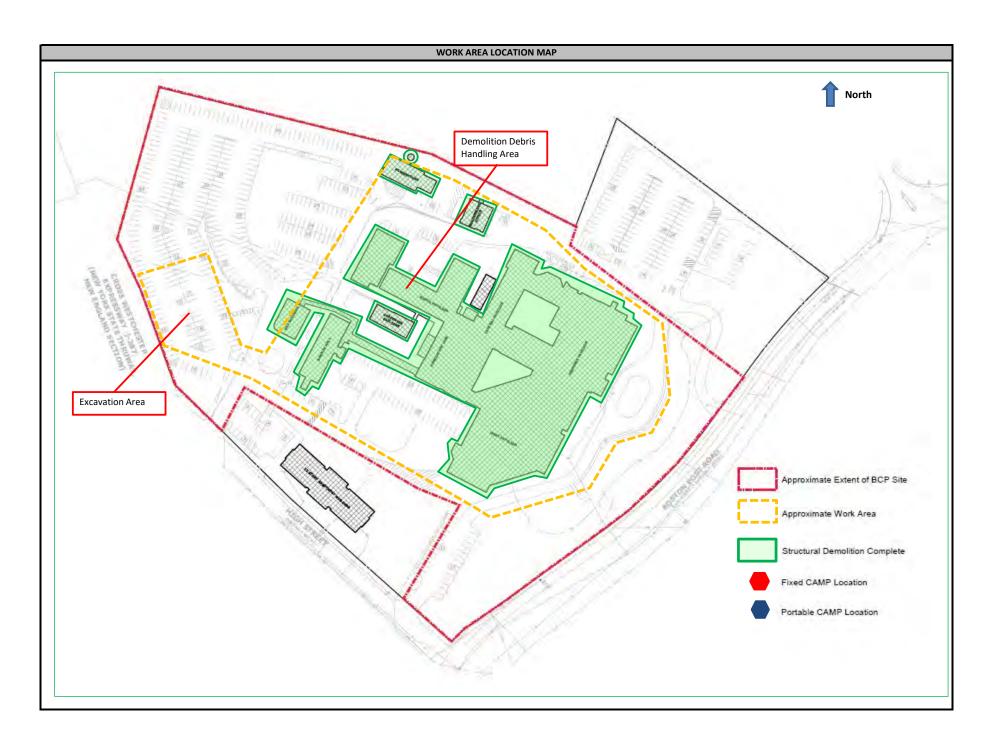

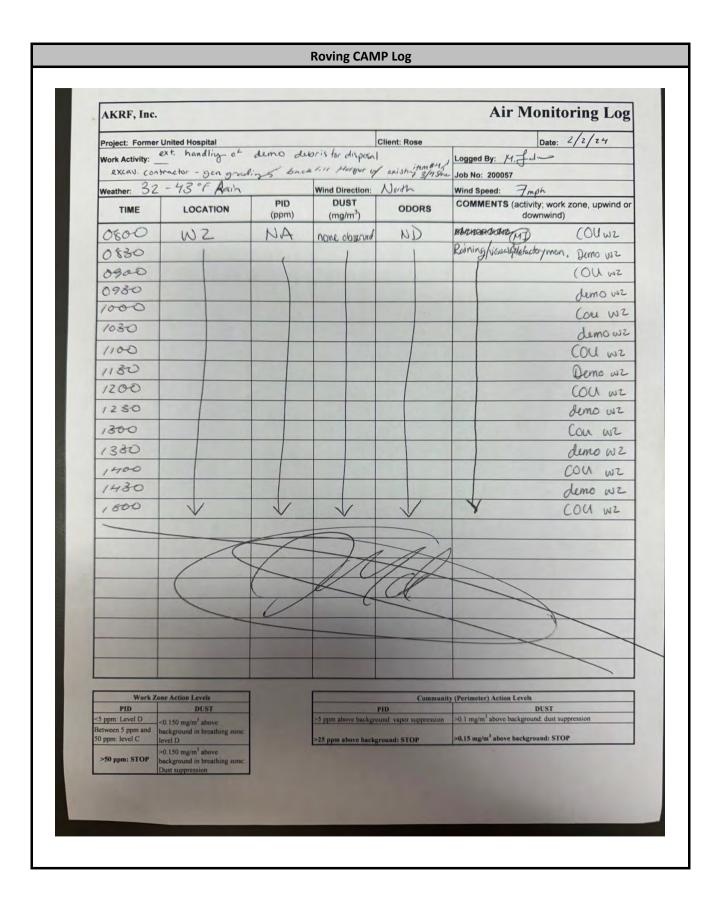

| | Daily Activity Report | | | | | | | | |
|--|--|---|-----------------------|--------------------------------|-------------------|-----------------------|-------------------------------|--|--|
| CAK RF | Former United Hospital | | | | | | | | |
| | | | | Port Ches BCP No. C | | | | | |
| | | Genera | l Site Information | | | | | | |
| Date: Weather: | | | | Monday, Febru Partly Cloudy | | | | | |
| Wind Direction/Speed: | | North @ 8 mph Michael Iodice | | | | | | | |
| AKRF Personnel on Site: AKRF Equipment on Site: | 3 Fixed CAN | Michael Iodice 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor | | | | | | | |
| Visitors: | 3 Fixed CAIV | in Stations (FID & De | ast Worldon, 5 Forta | Non | | , one Handheld F15, | One Handheld Base Worldon | | |
| Contracting Company | ı | | ector Information | | | Fauing | nent | | |
| Tony Casale Inc. | | Key Personnel Equipment Piec Piec Various excavation and grading equipment | | | | | | | |
| (Excavation Contractor) | (e.g., excavators, compactors, roller-compactor, etc.) | | | | | | | | |
| Capital Industries Corp. (Demolition Contractor) | | Joe Cianciulli Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.) | | | | | | | |
| (Demontion Contractor) | | | | | (e.g., ex | cavators, skiu steers | , Toll off containers, etc.) | | |
| | De | escription and Locat | ion of Work Activitie | es Performed | | | | | |
| The excavation contractor conducted general grading, and const | ructed rebar and cond | crete forms within th | e antennae Change | of Use (COU) area. | | | | | |
| | | | | . , | | | | | |
| The antennae structure was delivered to the site and staged adja | cent to the antennae | COU area to await fo | uture installation. | | | | | | |
| The demolition contractor continued sorting and loading demolt | on debris into contai | ners for off-site dispe | osal. | | | | | | |
| | | Site Soil Dispo | sal Tracking Informa | ation | | | | | |
| | | | | | | | | | |
| Destination Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Site Loads | | Total Approximate Cubic Yards | | |
| Clean Earth of Carteret - Carteret, NJ | 0 | | 0 | | 37 | | 710 | | |
| | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | |
| | | Imported Fi | ll Tracking Informati | on | | | | | |
| Origin Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards | | |
| Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4) | | 0 | 0 | | 56 1,335 | | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) 0 2 | | | | 45 | | | | | |
| | | Daily Import (CY) | (|) | | 1,380 | | | |
| CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| VOC Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| Particulate Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| | | | | | | | | | |
| | | Additi | onal Information | | | | | | |
| Planned Work Activity for Following Day(s): The demolition contractor will continue so | | | | | | | ayer. | | |
| Comments: None. | | | | | | | | | |

1 of 71 C360202_Daily Report_2024.02.05


Photograph 1 Excavation contractor conducting general grading within the antennae COU area, view facing southwest.





Photograph 2 Excavation contractor offloading and staging the antenna structure, view facing southwest.





Photograph 3 Demolition contractor handling structural demolition debris in the central portion of the site, view facing north.

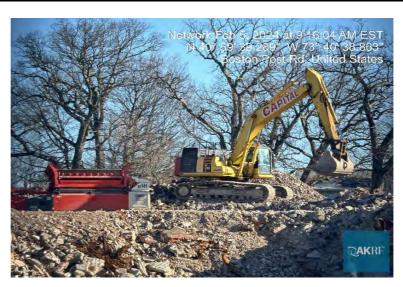


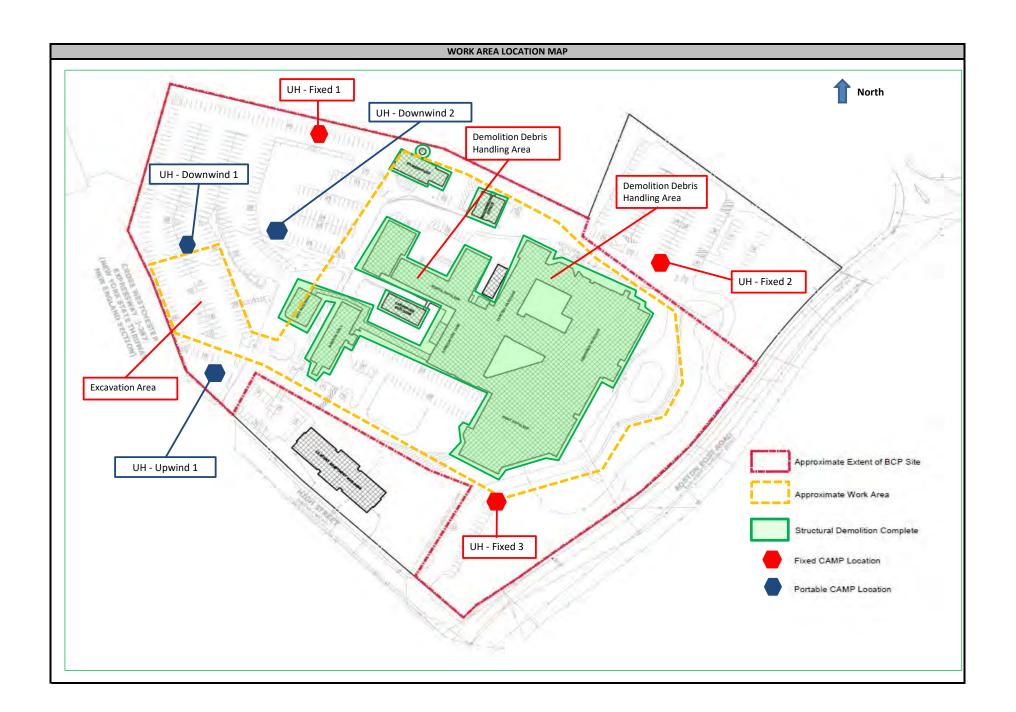


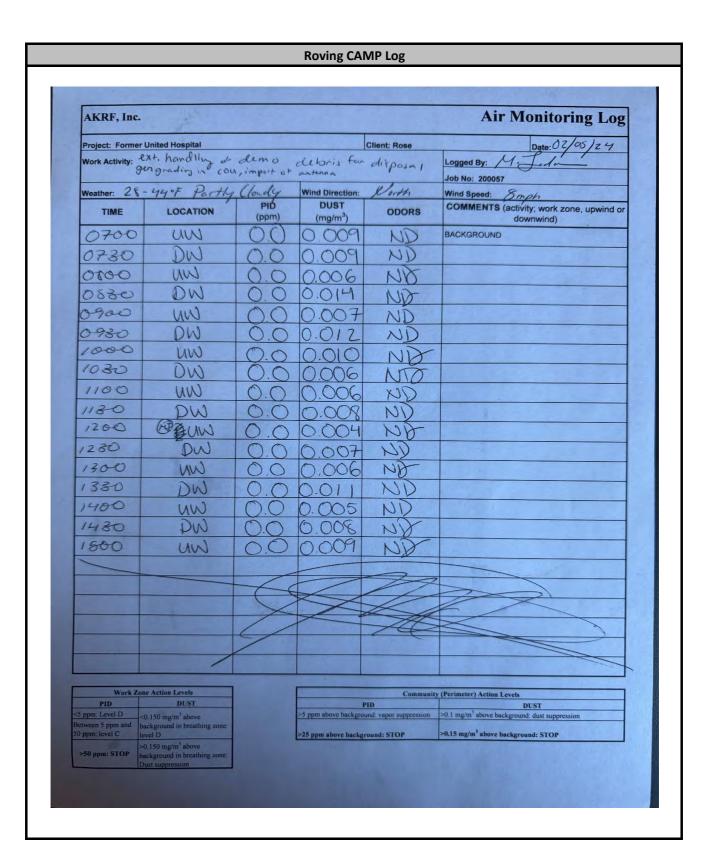


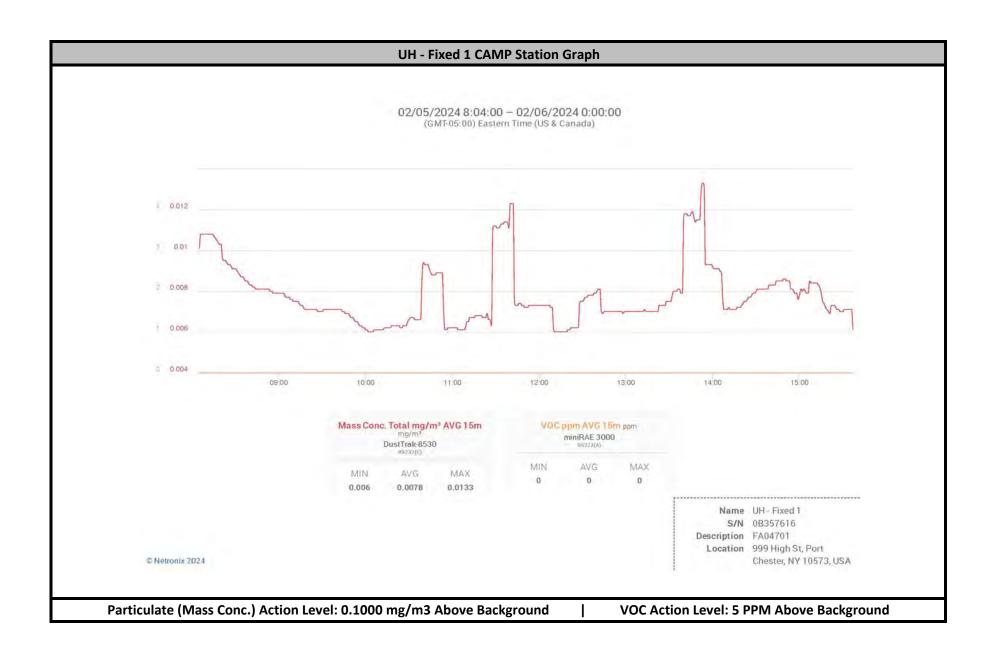


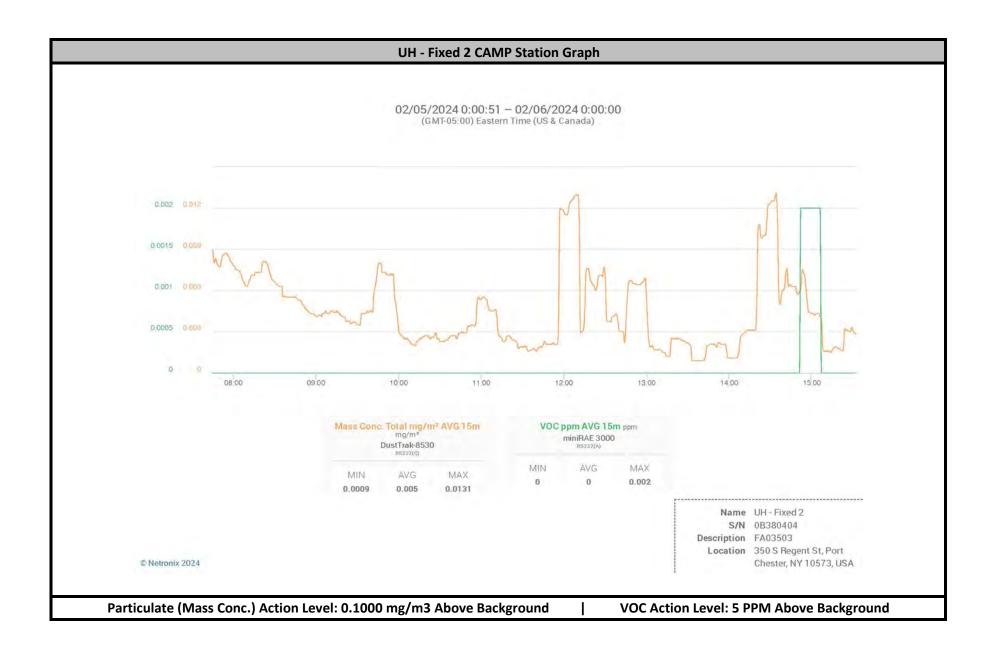

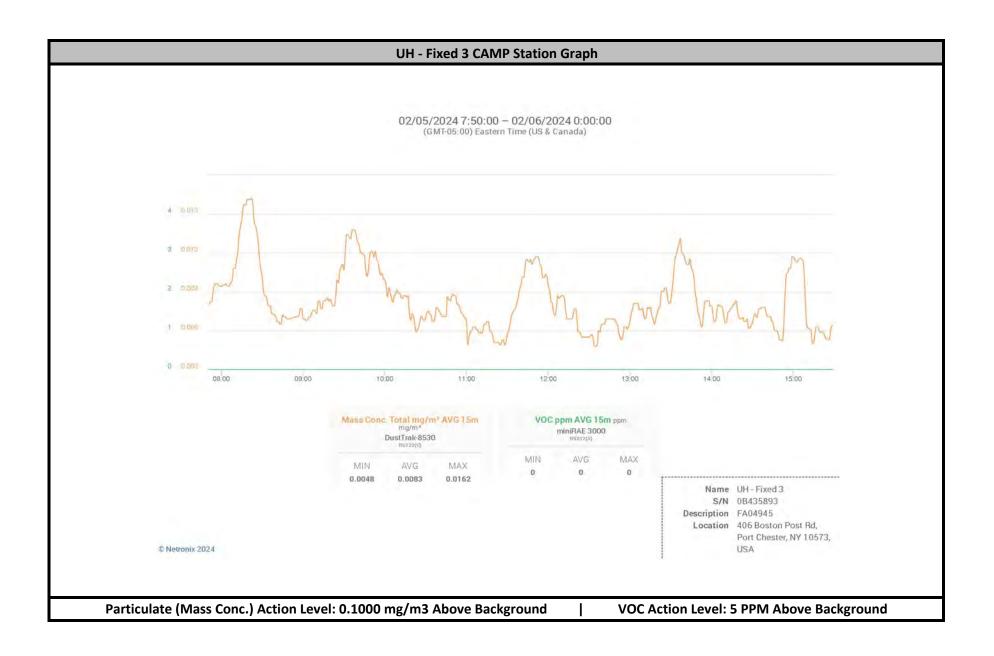

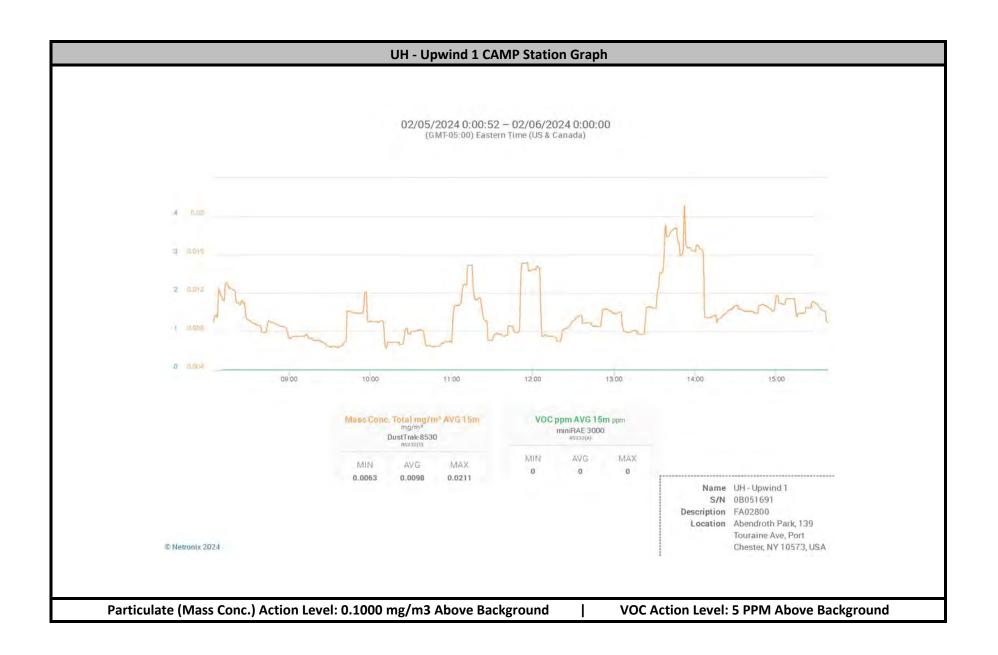

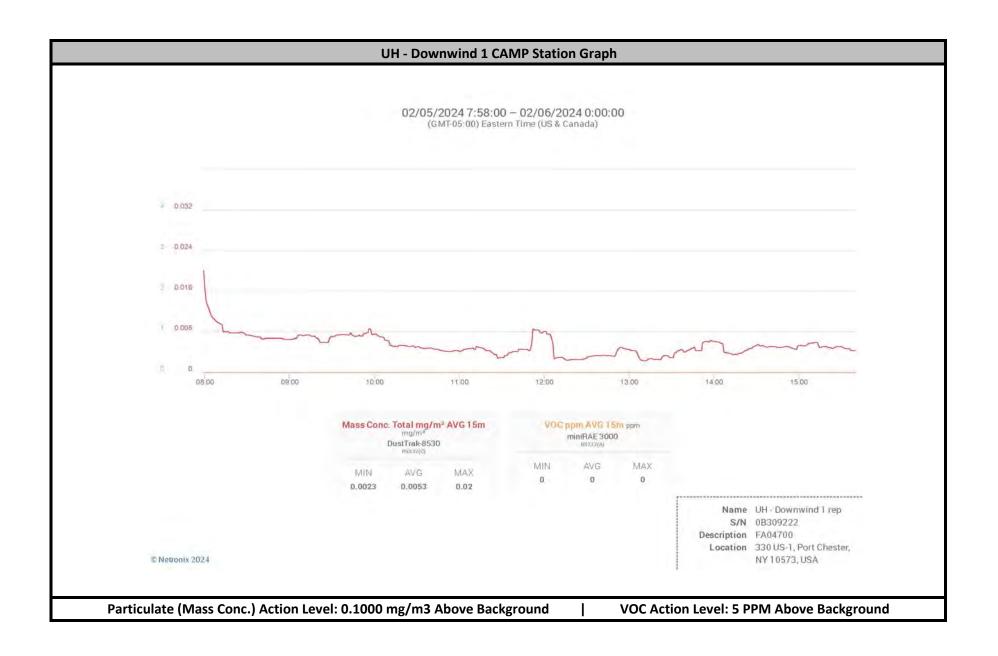

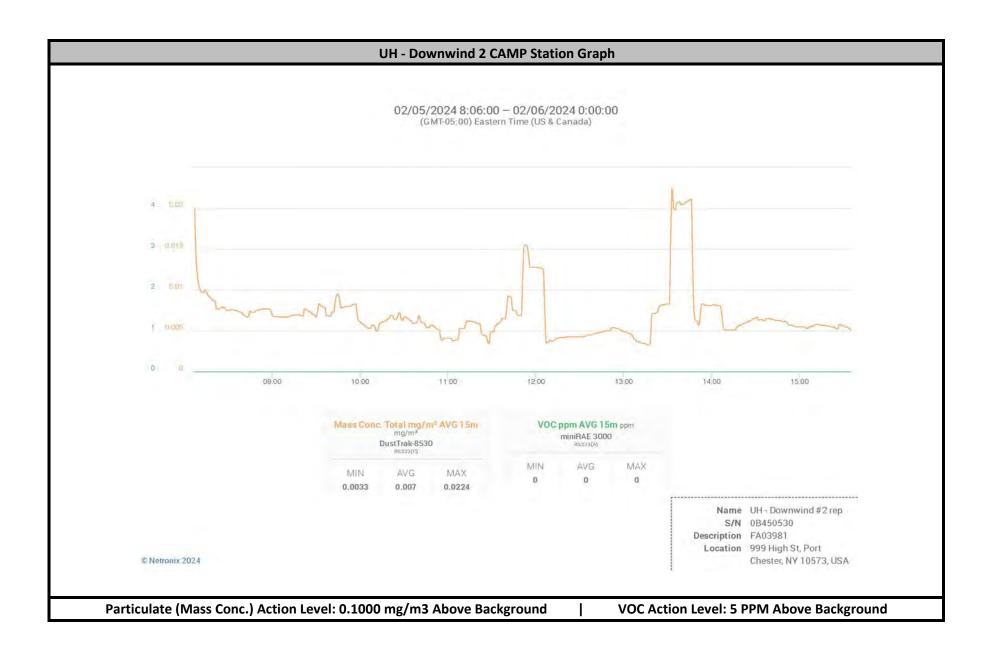

| | Daily Activity Report Former United Hospital Port Chester, NY | | | | | | | | | |
|--|---|---|--|-----------------------|---|---------------------|--|--|--|--|
| PAK | | | | | | | | | | |
| | ш | BCP No. C360202 | | | | | | | | |
| ate: | | ı | Genera | Site Information | Tuesday, Febru | Jany 6, 2024 | | | | |
| /eather: | | | | | Partly Cloudy | , , | | | | |
| /ind Direction/Speed KRF Personnel on Site | | NNE @7 mph Michael Iodice | | | | | | | | |
| (RF Equipment on Si | | 3 Fixed CAM | 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor | | | | | | | |
| sitors: | | | | | Non | e | | | | |
| | Contracting Company | I | Contra Key Pe | rsonnel | | | Equipm | nent | | |
| | Tony Casale Inc. | Rigo Diaz Various excavation and grading equipment | | | | | | | | |
| | Excavation Contractor) | | Nigo | DIAZ | | (e.g., ex | | s, roller-compactor, etc.) | | |
| | apital Industries Corp. Demolition Contractor) | | Joe Cia | nciulli | | | Various demolitic cavators, skid steers | on equipment , roll off containers, etc.) | | |
| | | De | escription and Locati | ion of Work Activitie | es Performed | | | | | |
| e excavation contract d was poured. | ctor conducted general grading, and const | ructed rebar and cond | crete forms within th | e antennae Change (| of Use (COU) area. F | ollowing the comple | etion of the rebar and | form work, the antennae concr | | |
| e demolition contra | ctor continued sorting and loading demolt | on debris into contai | ners for off-site dispo | osal. | | | | | | |
| | | | Site Soil Dispo | sal Tracking Informa | ation | | | | | |
| | Destination Facility | Daily ⁻ | Trucks | Daily Approx | Daily Approx. Cubic Yds. Total Site Loads | | Total Approximate Cubic Yar | | | |
| ean Earth of Carteret | t - Carteret, NJ | |) | C |) | 37 | | 710 | | |
| | | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | |
| | | | Imported Fi | Il Tracking Informati | on | | | | | |
| | | | | | | | Total Approximate Cubic Yar | | | |
| lcon West Nyack Qua FEM #4) | arry - West Nyack, NY | (|) | C |) | 56 | | 1,335 | | |
| Tilcon West Nyack Quarry - West Nyack, NY NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | | |
| | | | Daily Import (CY) | (| ס | Total Import (CY) | | 1,380 | | |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| dors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| /OC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| rticulate Action Leve | el Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| | | | Δdditi | onal Information | | | | | | |
| Planned Work ctivity for Following Day(s): | | Additional Information nue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal. nue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer. | | | | | | | | |
| Comments: | The VOC and particulate data from the UH - Fixed 2 CAMP station did not report to the online database from approximately from 08:35 until 09:14 due to a connectivity issue; the issue was resolved, and the station was fully operational by 09:15. No elevated levels of VOCs or particulates were detected with nearby CAMP equipment during the period that data was not reported at the UH - Fixed 2 CAMP station. | | | | | | | | | |

1 of 75 C360202_Daily Report_2024.02.06

Photograph 1 Excavation contractor conducting concrete pour within the antennae COU area, view facing

southwest.




Photograph 2 -


Demolition contractor handling structural demolition debris in the central portion of the site, view facing north.




Photograph 3 -


Demolition contractor handling structural demolition debris in the central portion of the site, view facing north.

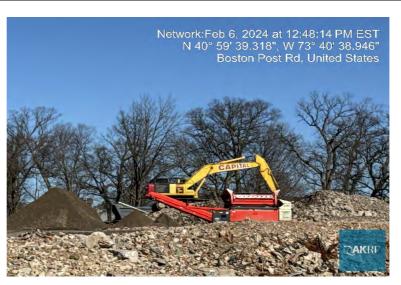


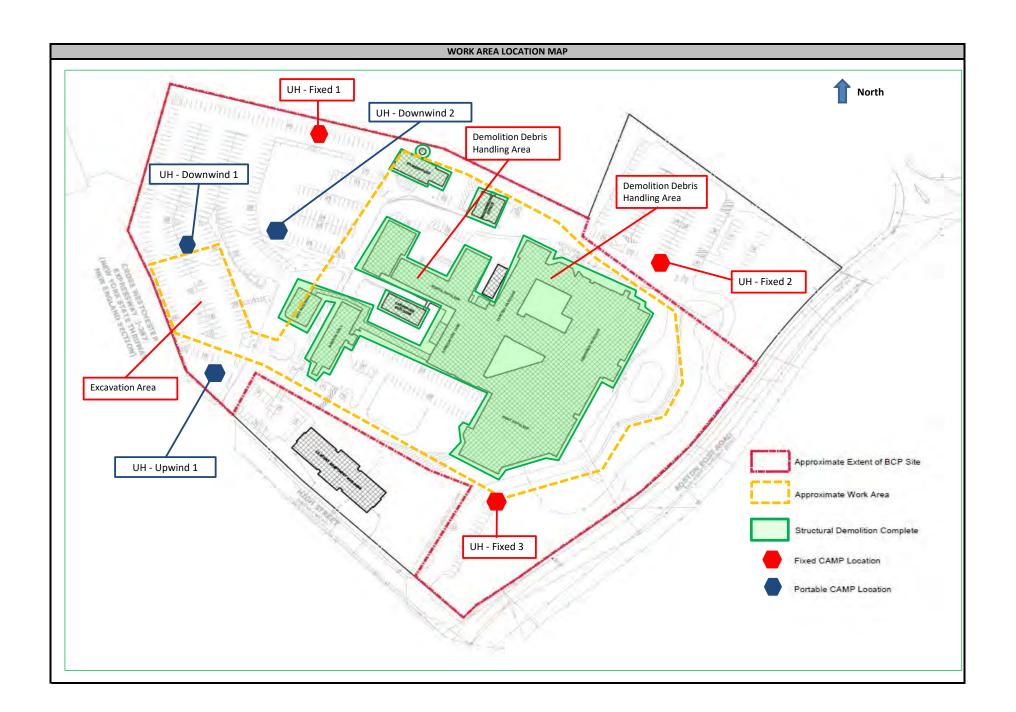



Roving CAMP Log Air Monitoring Log AKRF, Inc. Date: 2/6/24 Client: Rose Project: Former United Hospital Work Activity: ext. handling at dema debris, pup concrete turns, Logged By: H. G. dien cond. concrete polar for mana tandation Job No: 200057 Weather: 25-42°F Partly Cloudy NNE Wind Speed: 7mph Wind Direction: COMMENTS (activity; work zone, upwind or downwind) DUST PID LOCATION **ODORS** TIME . (ppm) (mg/m³) ND BACKGROUND LUN 0 0.006 6700 0730 OW ND NO 0800 SUN QCK 0830 DW 0900 NO UN ND 0930 DW ND 1000 WW 0 1080 DW NN ND 1100 UN ND 1180 DW ND 1200 CND NA 1280 DW WW 0.002 1800_ NI) 1338 DW ND NI 1400 WW 0.005 DW NI 1430 WW NX 1500 Community (Perimeter) Action Levels Work Zone Action Levels DUST <0.150 mg/m³ above background in breathing zo, level D >5 ppm above background: vapor suppression >0.1 mg/m³ above background: dust suppression <5 ppm: Level D etween 5 ppm and 0 ppm: level C >0.15 mg/m³ above background: STOP >25 ppm above background: STOP >0.150 mg/m³ above background in breathing >50 ppm: STOP

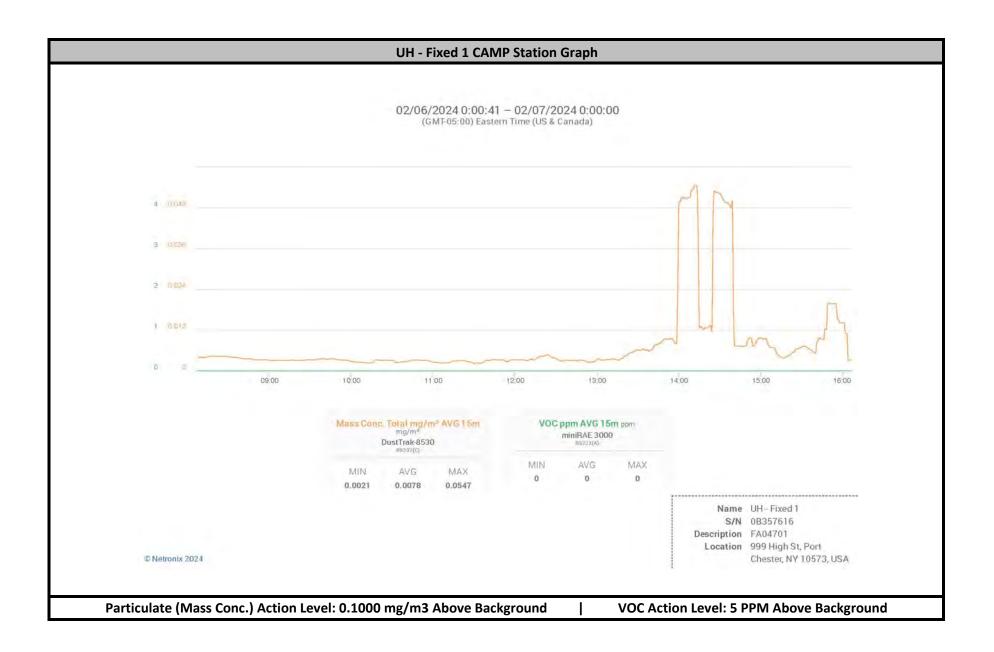


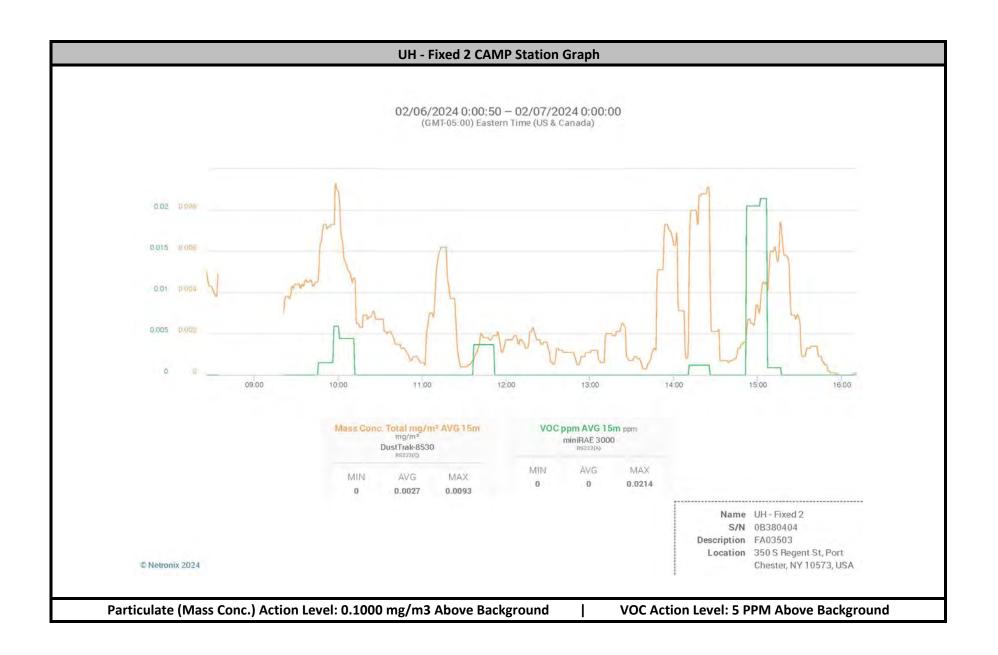

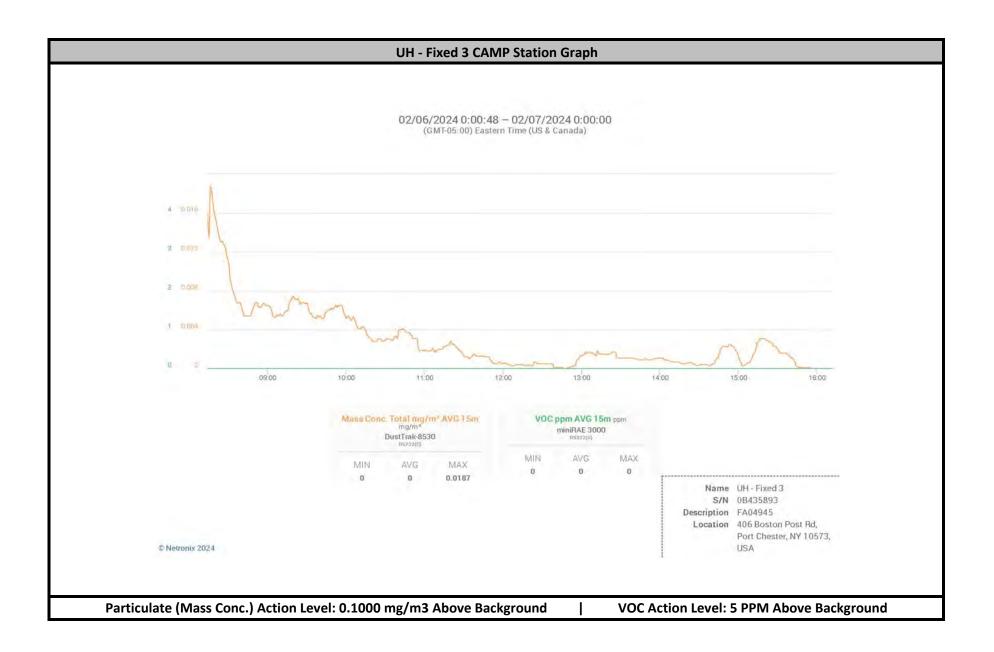

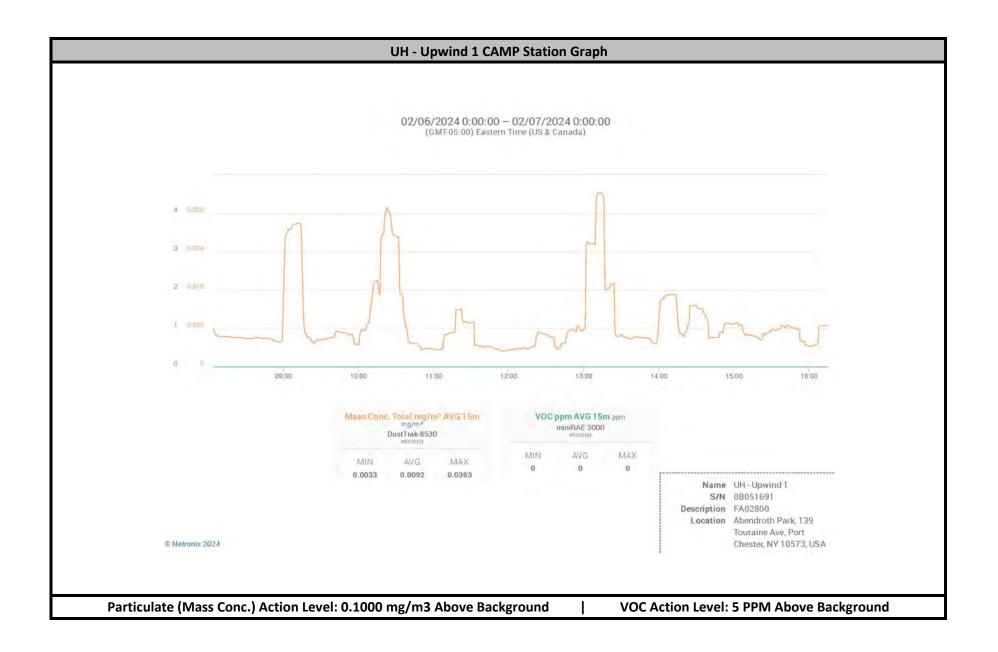

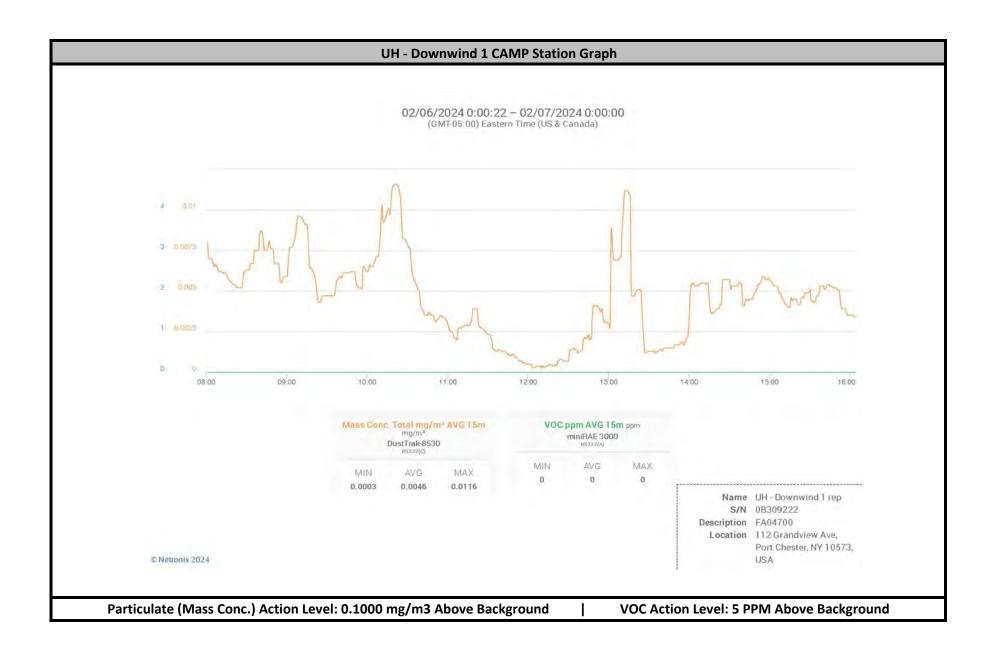

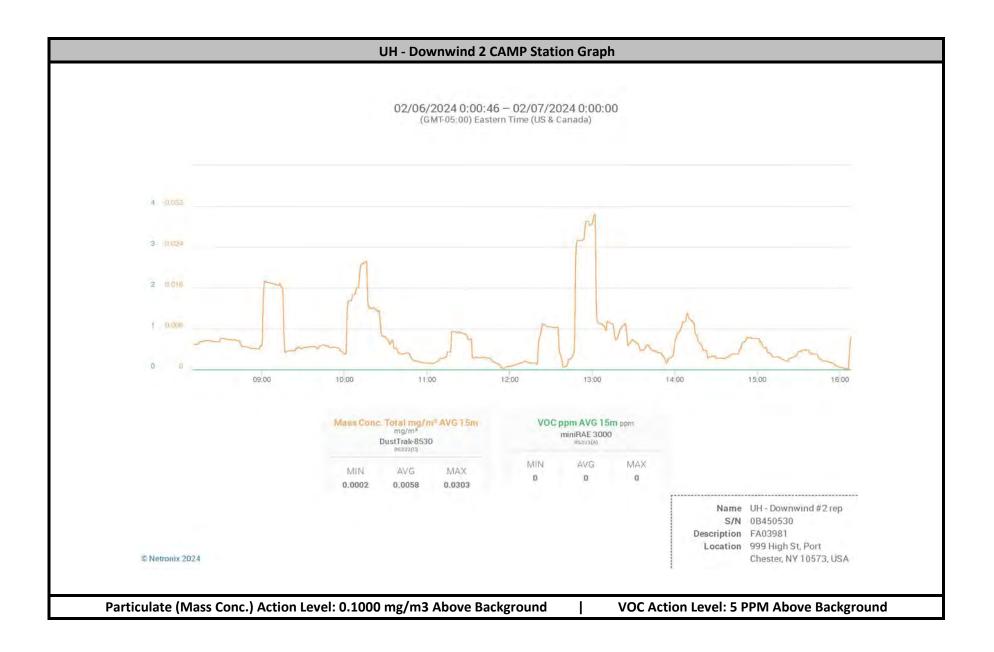

| | | | | Daily Activity Report | | | | | | | |
|---|--|--|-----------------------|--------------------------|---------------------------------|--|---------------------|-------------------------------|--|--|--|
| PAK | RF | Former United Hospital Port Chester, NY BCP No. C360202 | | | | | | | | | |
| | ıu | | | | | | | | | | |
| | | I | Genera | Site Information | | 7.0004 | | | | | |
| Date: Weather: | | | | | Wednesday, Feb Partly Cloudy | | | | | | |
| Wind Direction/Speed: | | N @5 mph | | | | | | | | | |
| AKRF Personnel on Site: AKRF Equipment on Site: | | Michael Iodice 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor | | | | | | | | | |
| /isitors: | | STIXED CAIV | ii Stations (FID & De | ist wiorittory, 5 i orta | Non | | , one Handheld Fib, | one Handheld Bust Worldon | | | |
| Cont | racting Company | ı | | ctor Information | | | Equipm | nont. | | | |
| | ony Casale Inc. | Key Personnel Equipment Various excavation and grading equip | | | | | | | | | |
| | vation Contractor) | Rigo Diaz Various excavation and grading (e.g., excavators, compactors, roller- | | | | | | | | | |
| | al Industries Corp. olition Contractor) | | Joe Cia | ınciulli | | Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.) | | | | | |
| | | De | escription and Locati | ion of Work Activitie | es Performed | | | | | | |
| he demolition contractor | continued sorting and loading demoltic | | | | 3 Terrorineu | | | | | | |
| | | | Site Soil Dispo | sal Tracking Informa | ation | | | | | | |
| Destination Facility | | Daily Trucks | | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic Yards | | | |
| | | | | | | | | | | | |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | | |
| | | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | | |
| | | | Imported Fil | Il Tracking Information | on | | | | | | |
| C | Origin Facility | Daily Trucks | | Daily Approx. Cubic Yds. | | Total Si | te Loads | Total Approximate Cubic Yards | | | |
| Tilcon West Nyack Quarry (ITEM #4) | lcon West Nyack Quarry - West Nyack, NY TEM #4) | | 0 | | 0 | | 56 | 1,335 | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | | | |
| | | | Daily Import (CY) | | 0 | | Total Import (CY) | 1,380 | | | |
| CAI | MP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | | |
| /OC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | | |
| 'articulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | | |
| | | | Additi | onal Information | | | | | | | |
| Activity for Following | Planned Work tivity for Following | | | | | | | | | | |
| Comments: Nor | ne. | | | | | | | | | | |

1 of 69 C360202_Daily Report_2024.02.07

Site Photographs

Photograph 1 -

Demolition contractor clearing structural demolition debris from the basement footprints of the former structures in the eastern portion of the Site, view facing north.



Photograph 2 -


Demolition contractor handling structural demolition debris in the central portion of the site, view facing north.




Photograph 3 -


Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north.




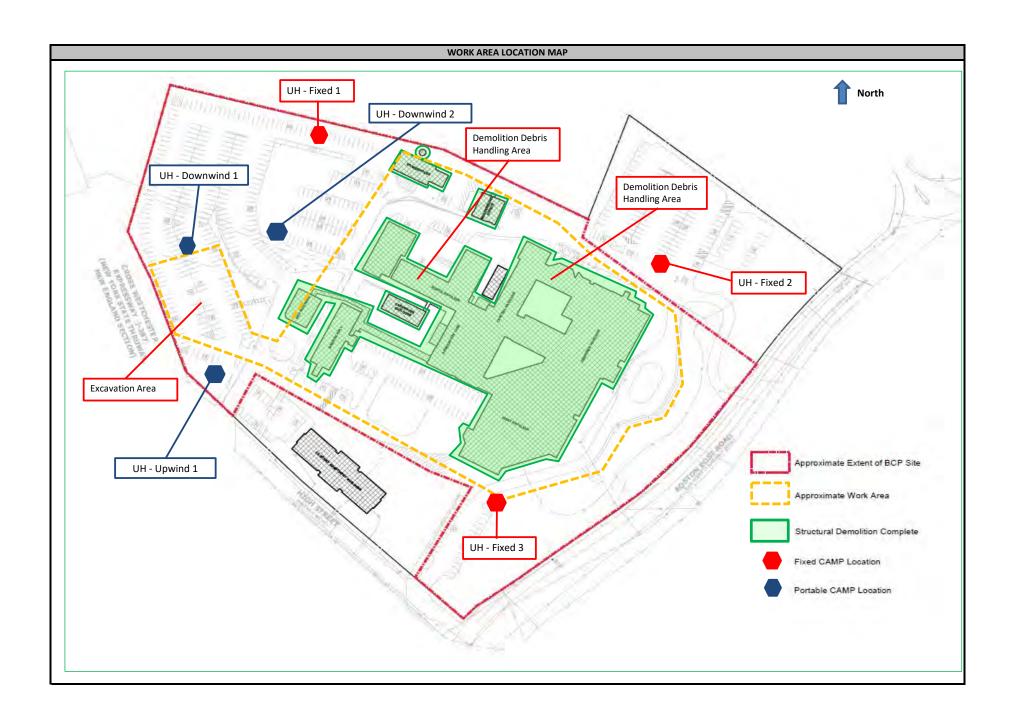



Roving CAMP Log Air Monitoring Log AKRF, Inc. Date: 2/7/24 Client: Rose Project: Former United Hospital Logged By: M. I.d. Work Activity: ext. handling of demo debris for Job No: 200057 disposal Wind Speed: 5mph Weather: 28 - 45°F Partly (loudy Wind Direction: COMMENTS (activity; work zone, upwind or DUST PID ODORS TIME LOCATION downwind) (ppm) (mg/m^3) ND BACKGROUND 0.008 0.0 0600 WN 0.009 ND DW 0830 0.004 NX UW 0900 0930 DW 0.005 ND 0.004 WW 1000 DW 0.007 NI) 1030 ND 1100 NW ND 0.009 1130 ND 0.006 1200 MN WC 1230 NW 1300 DW ND 1330 ND ww 1400 BIN DW 1430 NW 1800 DW O.005 1530 Work Zone Action Levels Community (Perimeter) Action Levels DUST PID DUST <5 ppm: Level D >5 ppm above background: vapor suppression >0.1 mg/m3 above background: dust suppression <0.150 mg/m³ above Between 5 ppm and background in breathing zone level D >0.15 mg/m³ above background: STOP >25 ppm above background: STOP >0.150 mg/m³ above background in breathing zone >50 ppm: STOP

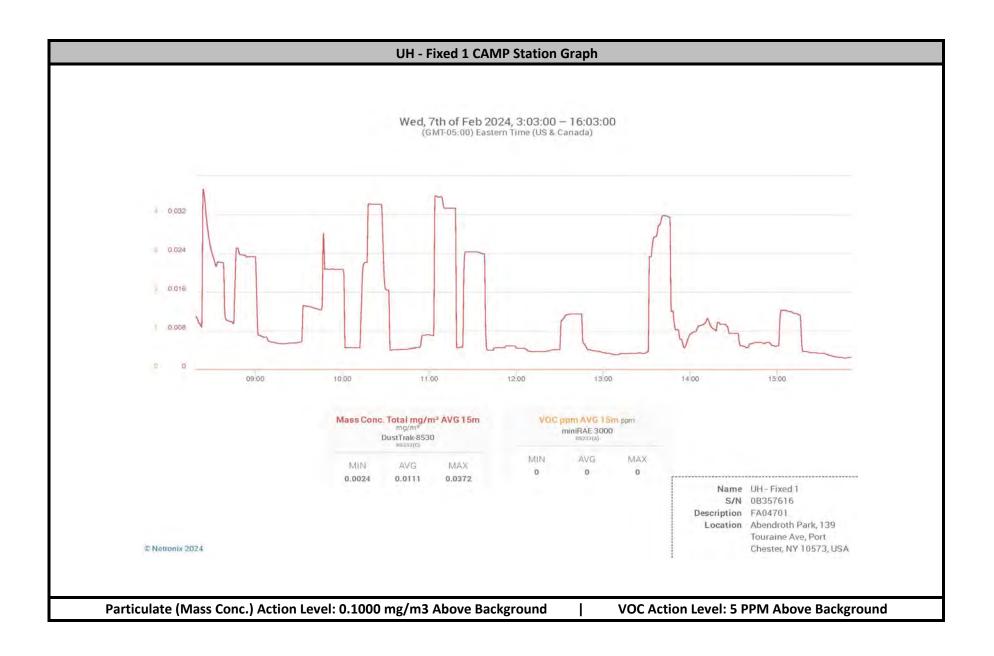


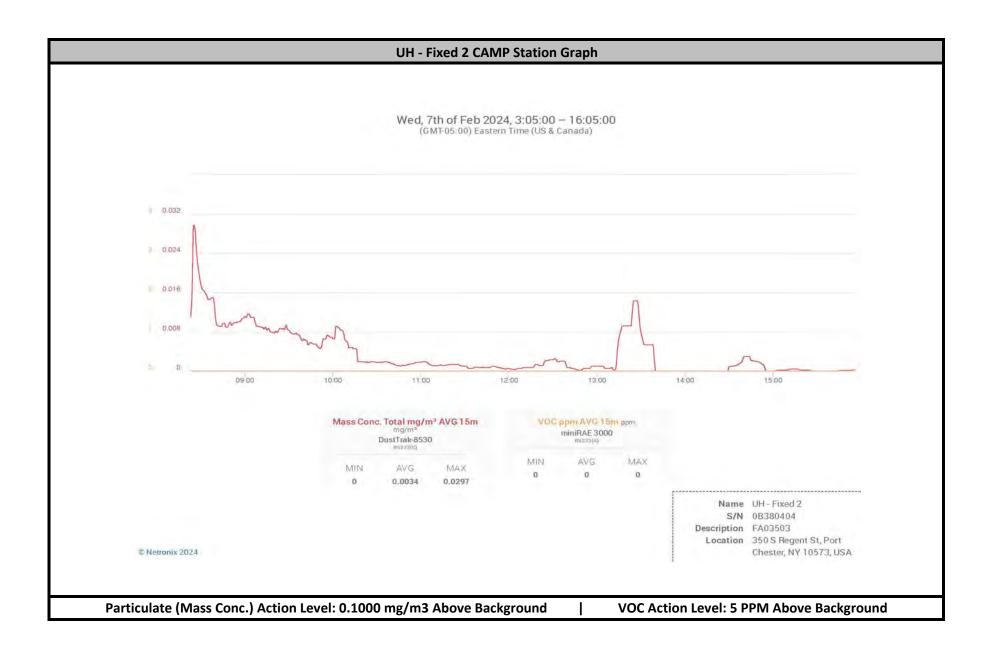

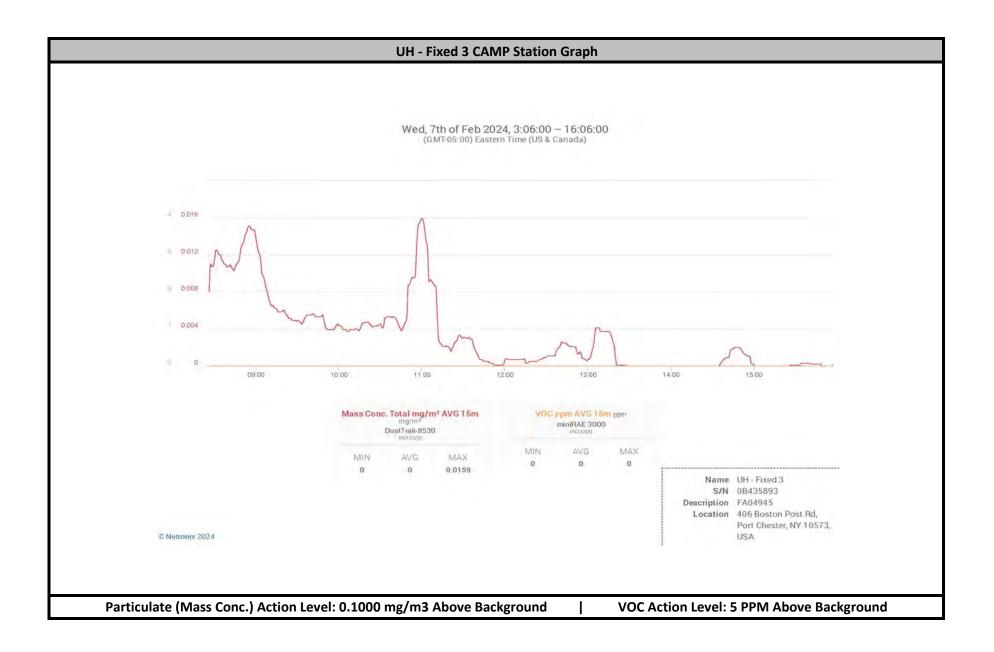

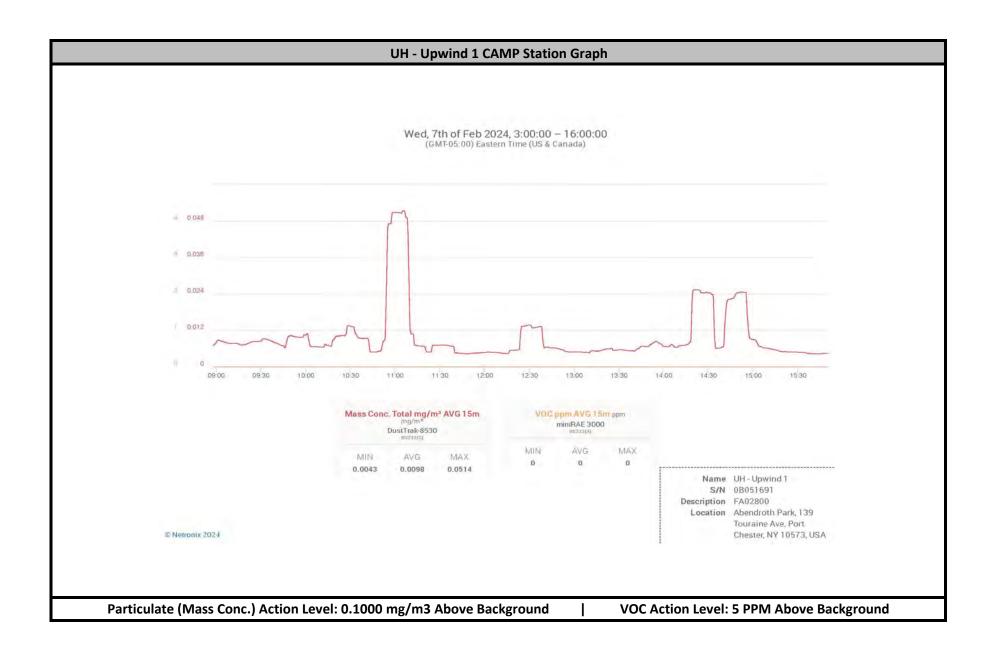

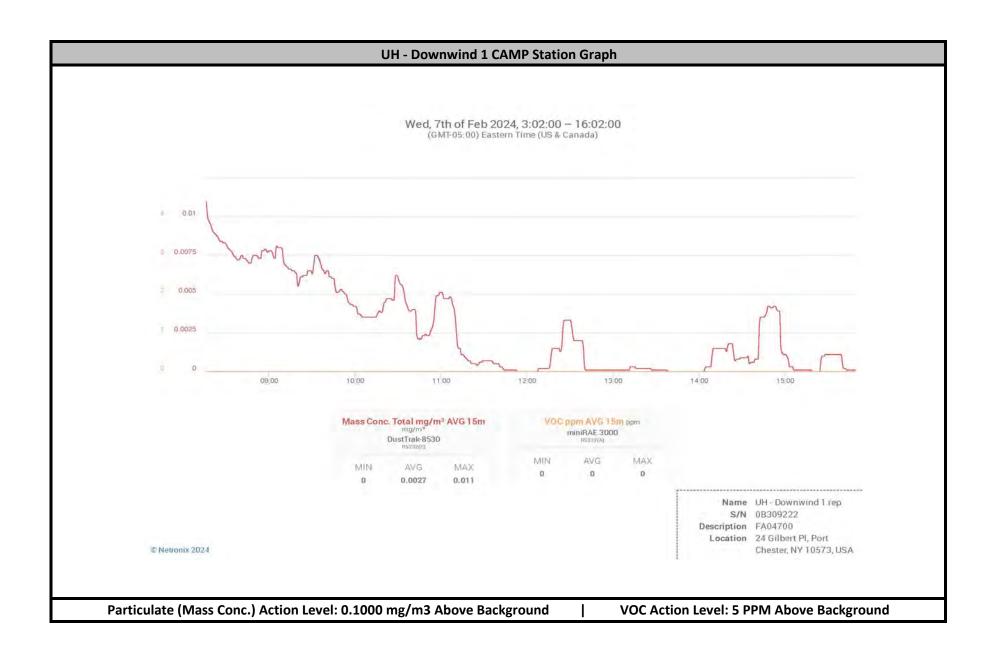


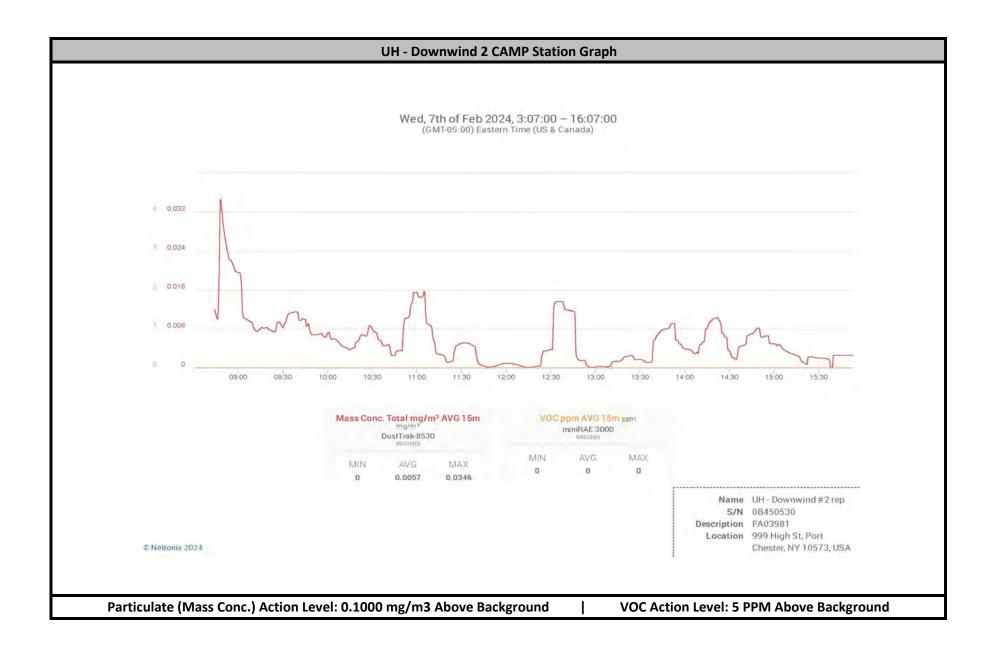


| Daily Activity Report | | | | | | | | | | | |
|--|--|---|-------------------------|--------------------------|----------------------------|--|---------------------|-------------------------------|--|--|--|
| PAK | (RF | Former United Hospital | | | | | | | | | |
| | ии | Port Chester, NY BCP No. C360202 | | | | | | | | | |
| | | | Genera | I Site Information | | | | | | | |
| Date: Weather: | | | | | Thursday, Febr Sunny, 2 | | | | | | |
| Wind Direction/Speed: | | SE @2 mph | | | | | | | | | |
| AKRF Personnel on Site AKRF Equipment on Sit | | Mackenzie Miller and Steve Schmid 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor | | | | | | | | | |
| Visitors: | ie. | 3 Fixeu CAIV | ir stations (FID & Di | ist Monitor), 3 Porta | Non | | , One Handheid FID, | One Handrield Dust Worldon | | | |
| | | | | ector Information | | | | | | | |
| | Contracting Company | Key Personnel Equipment | | | | | | | | | |
| (E | Tony Casale Inc. Excavation Contractor) | Rigo Diaz Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, | | | | | | | | | |
| | apital Industries Corp. | | | | | Various demolition equipment | | | | | |
| (D | Demolition Contractor) | | Joe Cia | inciulli | | (e.g., excavators, skid steers, roll off containers, etc.) | | | | | |
| | | De | escription and Locat | ion of Work Activitie | es Performed | | | | | | |
| The demolition contrac | ctor continued sorting and loading demolt | ion debris into contai | ners for off-site dispe | osal. | | | | | | | |
| | | | Site Soil Dispo | sal Tracking Informa | ation | | | | | | |
| | Destination Facility | | Daily Trucks | | Daily Approx. Cubic Yds. | | ite Loads | Total Approximate Cubic Yards | | | |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | | |
| | | | | | | | | | | | |
| | | | Imported Fi | II Tracking Informati | on | | | | | | |
| | Origin Facility | Daily Trucks | | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic Yards | | | |
| Tilcon West Nyack Qua (ITEM #4) | con West Nyack Quarry - West Nyack, NY EM #4) | | 0 | | 0 | | 56 | 1,335 | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | | | |
| | | Daily Import (CY) | | 0 | | Total Import (CY) | | 1,380 | | | |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | | |
| /OC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | | |
| Particulate Action Leve | el Exceedance(s) Above Background: | No | Yes | No | No | No | No | No | | | |
| | | | Additi | onal Information | | | | | | | |
| Planned Work Activity for Following Day(s): | The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal. for Following | | | | | | | | | | |
| Comments: A momentary particulate exceedance occurred at the UH - Fixed 1 CAMP station from approximately 10:07 to 10:11 due to a truck that was dropping off equipment in the area. Once the work was complete, the exceedance was resolved with no further action needed. | | | | | | | | | | | |


1 of 72 C360202_Daily Report_2024.02.08




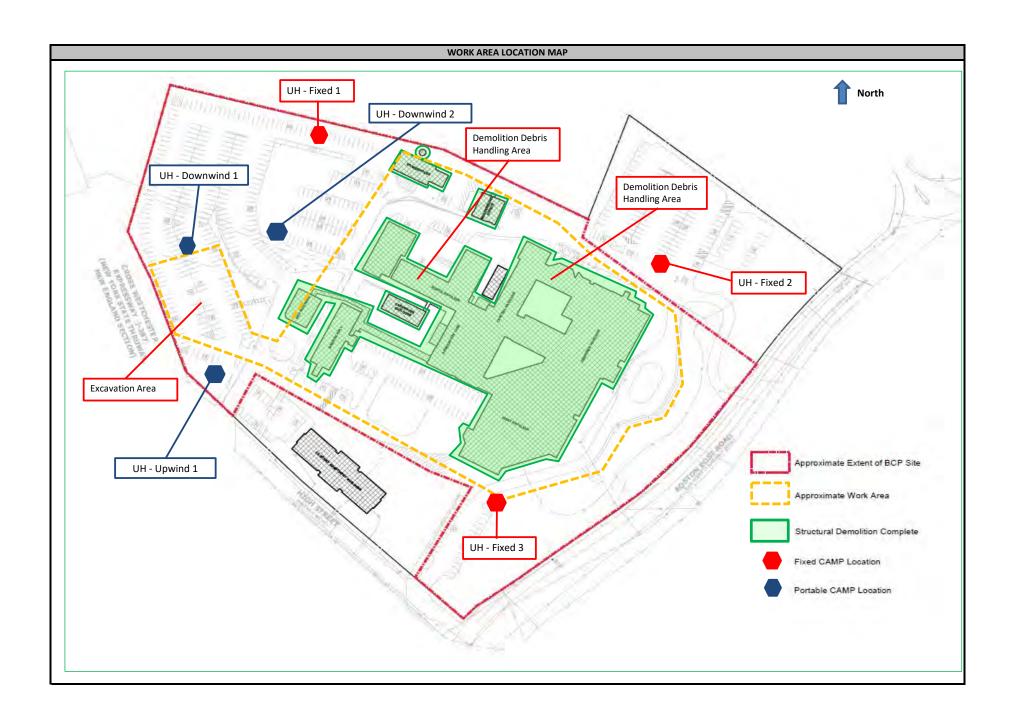



Roving CAMP Log CAKRE Air Monitoring Log Client: BR RA Port Chester Date: 2/8/34 Project: Former United Hospital (BCP Site No. C360202) Work Activity: extenor handling of deme debns Logged By: MMiller Job No: 20005 Weather: 28-50°F, Sunny Wind Speed: ~2 mph Wind Direction: SE COMMENTS TIME PID LOCATION ODORS (activity; work zone, upwind or downwind) (mg/m³) 0.009 none 0730 BACKGROUND 0.0 (uu 0.013 800 0,0 UU 0,0 0.010 UU иш 0,0 0,017 WZ 0.0 0.025 ·WZ 0,0 0,0 050 WZ 1100 DU 0,0 1130 DW 0.013 200 UW 0.0 230 UU 0.014 MZ 10 0.028 ИШ 0 DW 0 430 WZ 0.0 0.0 0.014 ·, ' Work Zose Action Levels PID DUST S ppm: Level D O.15 mg/m² above background in the string zene: Level D, DLevel C Modified, or C (subject to PID) Community (Perimeter) Action Levels PID DUST >5 ppm above background; vapor suppression >0.1 mg/m³ above background: dust suppression >0.15 mg/m³ above background in breathing zone: dust suppression, stop work if conditions continue >25 ppm above background: STOP >6.15 mg/m³ above background: STOP

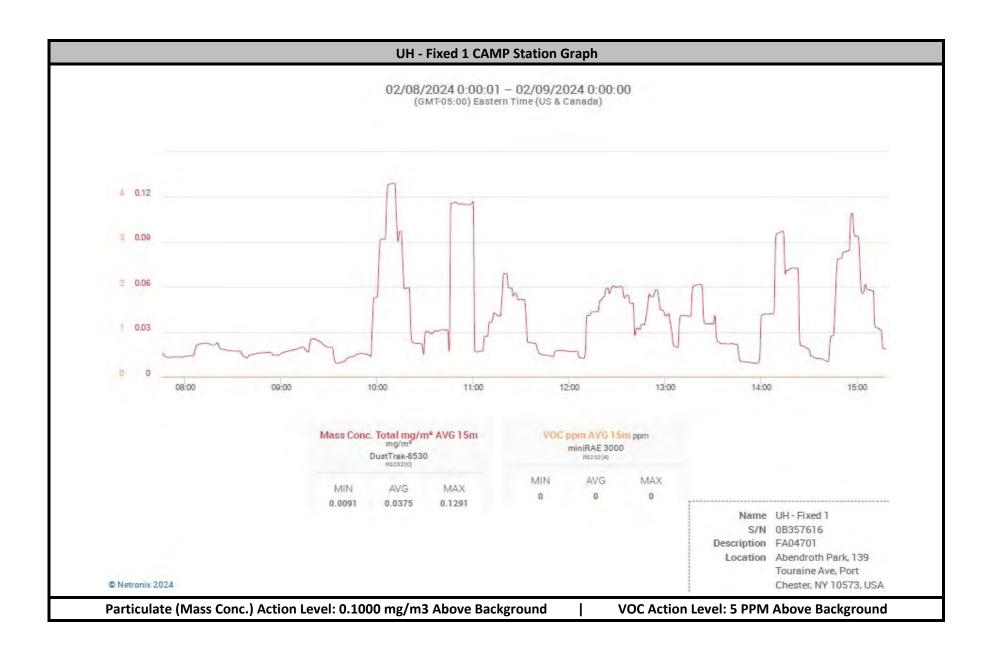


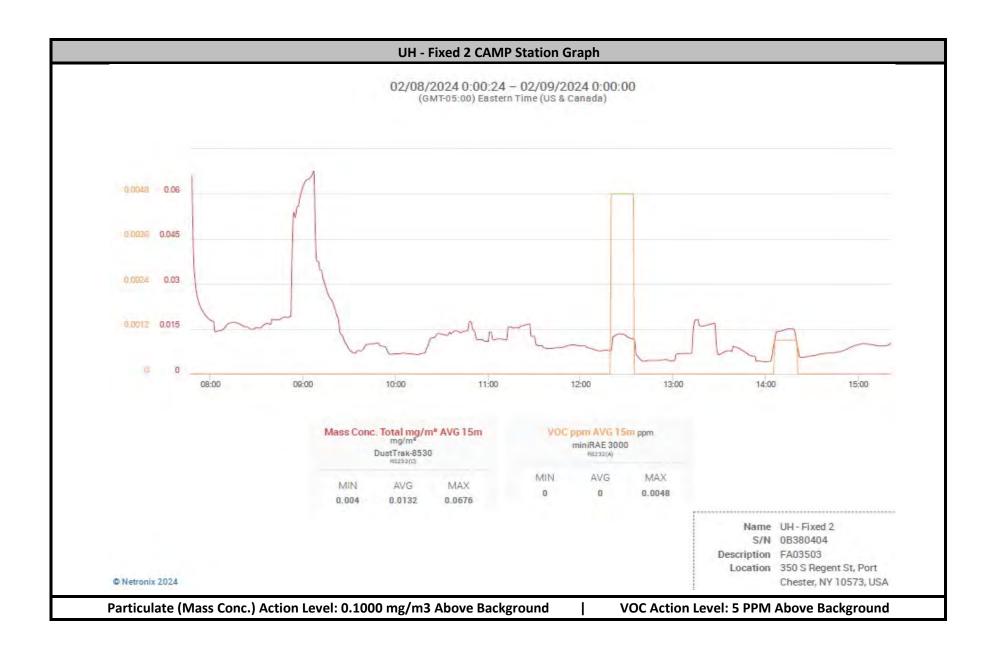

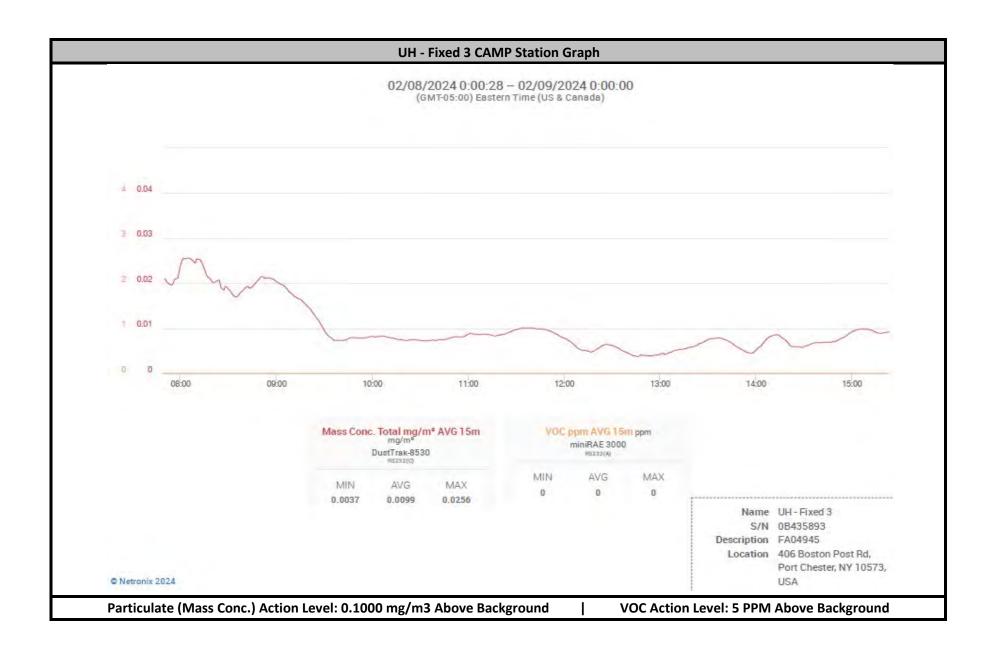

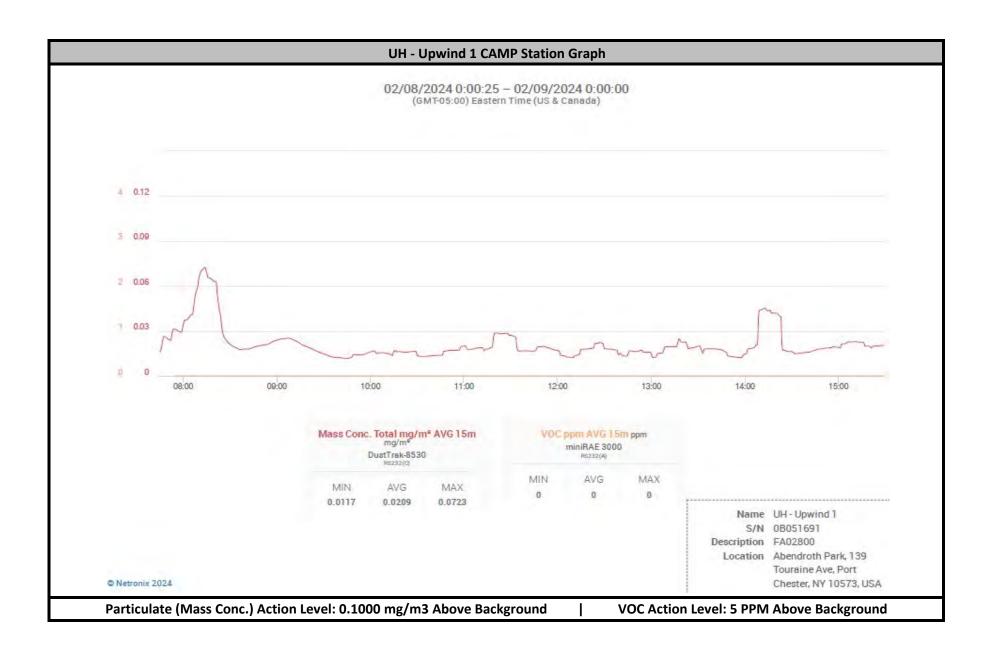

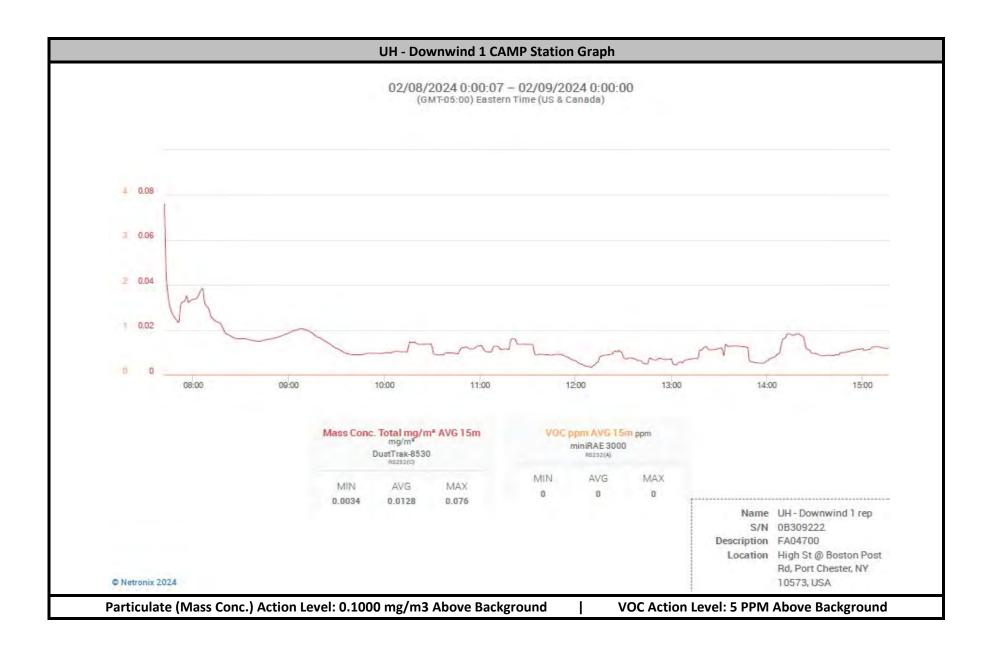

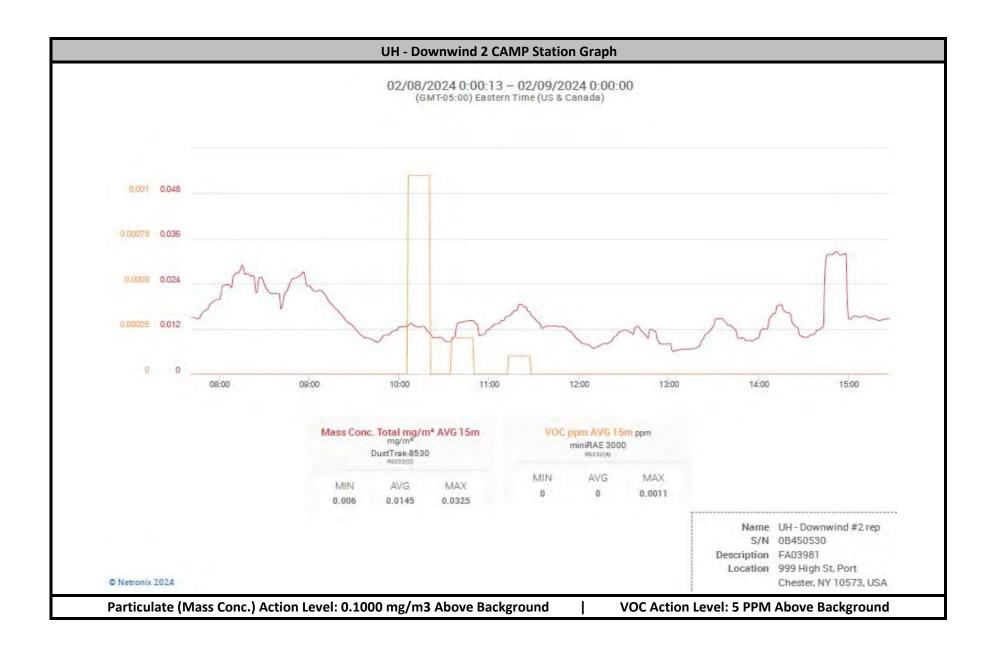

| Daily Activity Report | | | | | | | | | | | |
|--|--|--|--|-----------------------|--------------------------|---------------|--|--|--|--|-------------------|
| PAK | $\mathbf{K}\mathbf{F}'$ | Former United Hospital Port Chester, NY BCP No. C360202 | | | | | | | | | |
| | IU | | | | | | | | | | |
| ate: | | | Genera | I Site Information | Friday, Februa | ary 9 2024 | | | | | |
| /eather: | | | | | Partly Sunny | , 32-50°F | | | | | |
| /ind Direction/Speed: KRF Personnel on Site: | | SE @3 mph Mackenzie Miller and Steve Schmid | | | | | | | | | |
| (RF Equipment on Site: | | 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor | | | | | | | | | |
| sitors: | | | | | Non | e | | | | | |
| Cor | ntracting Company | | Key Pe | rsonnel | | I | Equipm | ent | | | |
| | Tony Casale Inc. | | Various excavation and grading equipment | | | | | | | | |
| | avation Contractor) | | Rigo Diaz (e.g., excavators, compactors, rolle | | | | | | | | |
| | ital Industries Corp. nolition Contractor) | | Joe Cia | nciulli | | (e.g., ex | Various demolitic cavators, skid steers | on equipment roll off containers, etc.) | | | |
| | | De | escription and Locat | ion of Work Activitie | es Performed | | | | | | |
| e excavation contracto | r imported 2 loads of Item #4 from Tilo | on West Nyack and co | nducted general gra | ding within the anter | nnae Change of Use | (COU) area. | | | | | |
| ne demolition contracto | r continued sorting and loading demol | tion debris into contain | ners for off-site disne | ocal | | | | | | | |
| ie demondon contracto | i continued sorting and loading demoi | tion debris into contai | ners for on-site dispi | Jsdi. | | | | | | | |
| | | 1 | Site Soil Dispo | sal Tracking Informa | ation | | | | | | |
| De | estination Facility | Daily | Daily Trucks Dails | | Daily Approx. Cubic Yds. | | te Loads | Total Approximate Cubic Yard | | | |
| ean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | | |
| | | | | | | | | | | | Daily Export (CY) |
| | | | Imported Fi | ll Tracking Informati | on | | | | | | |
| | Origin Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yar | | | |
| Filcon West Nyack Quarry - West Nyack, NY ITEM #4) | | 2 | | 50 | | 58 | | 1,385 | | | |
| rilcon West Nyack Quarry - West Nyack, NY NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | | | |
| | | | Daily Import (CY) | 5 | 0 | | Total Import (CY) | 1,430 | | | |
| C | AMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | | |
| dors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | | |
| OC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | | |
| articulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | | |
| | | | Additi | onal Information | | | | | | | |
| Planned Work Th | The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal. | | | | | | | | | | |
| Day(s): The excavation contratcor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer. | | | | | | | | | | | |
| | | | | | | | | | | | |

1 of 69 C360202_Daily Report_2024.02.09

Site Photographs

Photograph 1 -

Excavation contractor conducting general grading and compacting within the antennae COU area, view facing southwest.



Photograph 2 -


Demolition contractor sorting structural demolition debris in the central portion of the site, view facing southeast.




Photograph 3 -


Demolition contractor loading structural demolition debris in the central portion of the Site for off-site disposal, view facing southeast




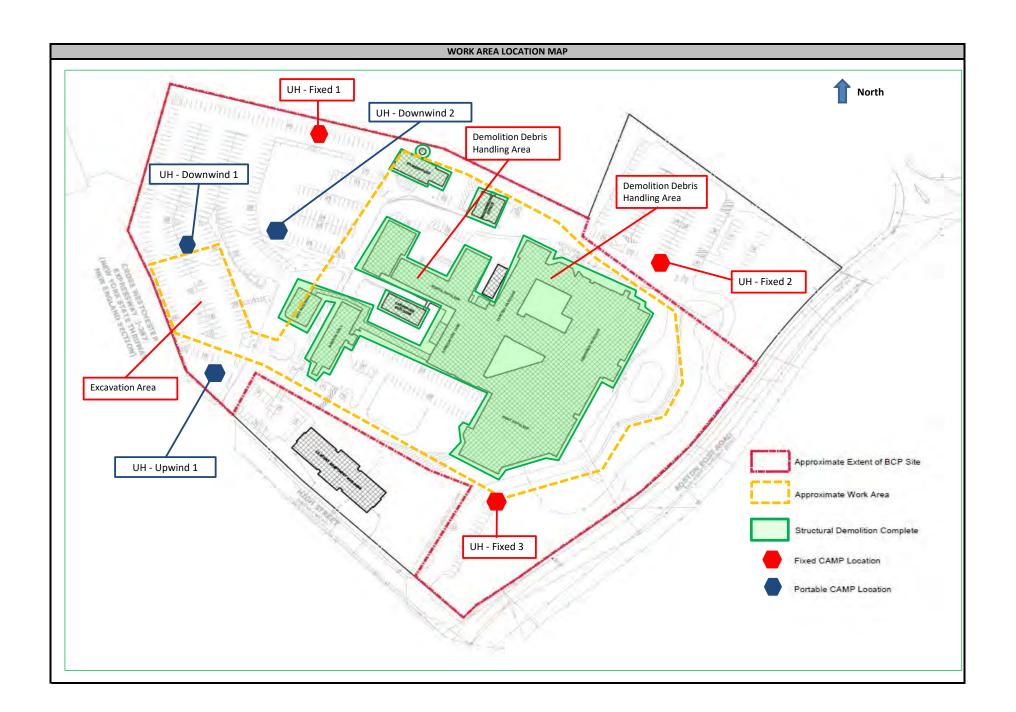



Roving CAMP Log Air Monitoring Log AKRF, Inc. Date: 2/9/24 Client: Rose Project: Former United Hospital Work Activity: import tem +4, demolition ext. Logged By: Miller handling, grading import Job No: 200057 Wind Speed: v 3 mph COMMENTS (activity; work zone, upwind or downwind) Weather: ~ 50 ° F , Darty Sunry Wind Direction: SE ODORS LOCATION TIME (mg/m³) (ppm) none иш BACKGROUND 730 1,0 DUI WZ DW Work Zone Action Levels Community (Perimeter) Action Levels PID DUST DUST <5 ppm: Level D <0.150 mg/m3 above >5 ppm above background: vapor suppression >0.1 mg/m³ above background: dust suppression Between 5 ppm and background in breathing zone 50 ppm: level C level D >25 ppm above background: STOP >0.15 mg/m³ above background: STOP >0.150 mg/m3 above >50 ppm: STOP background in breathing zone Dust suppression

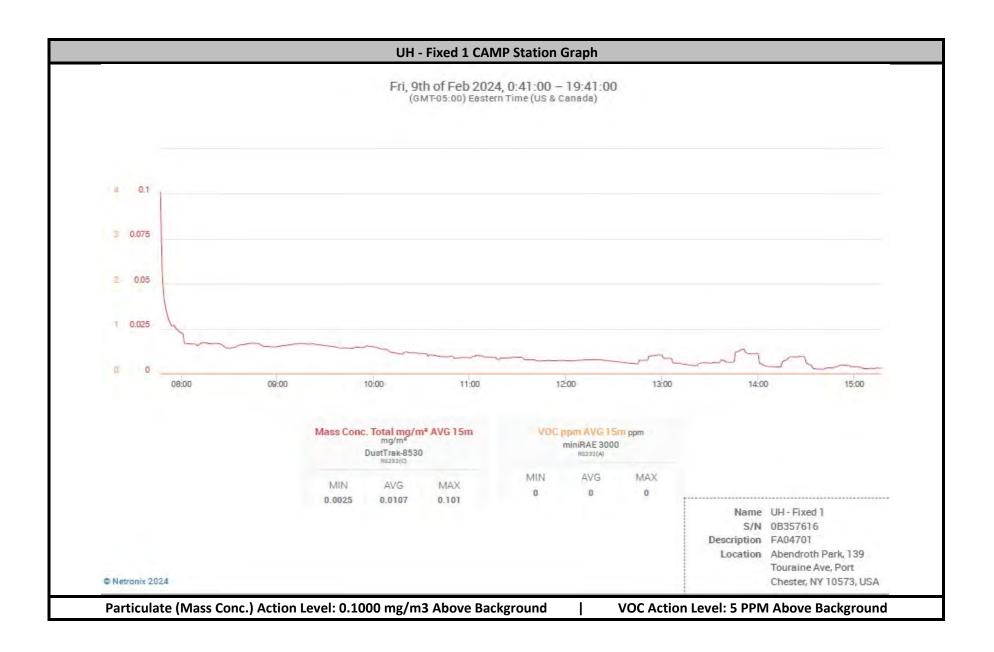


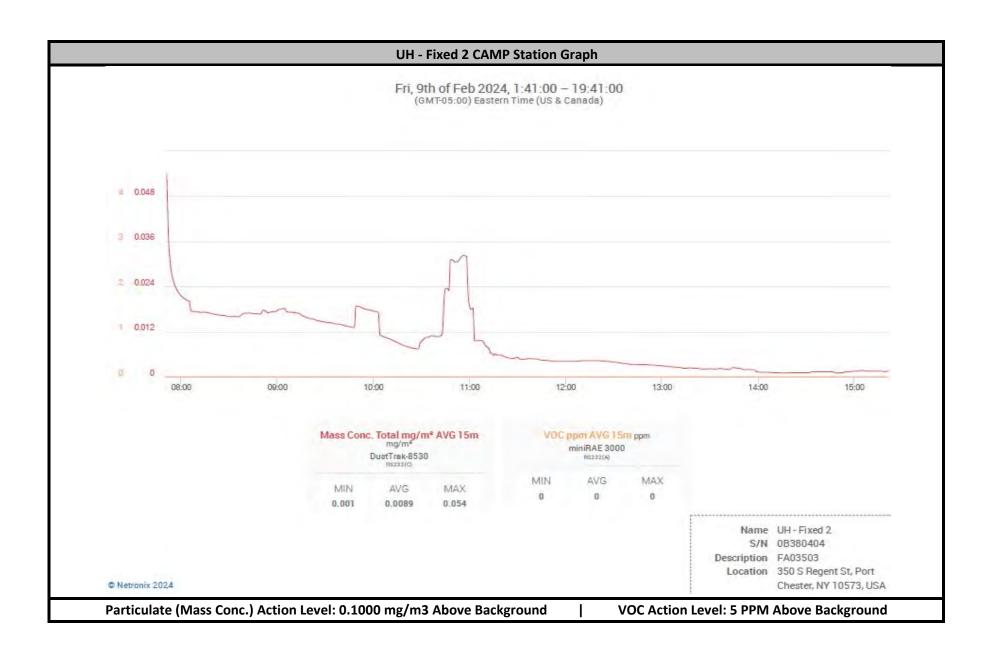

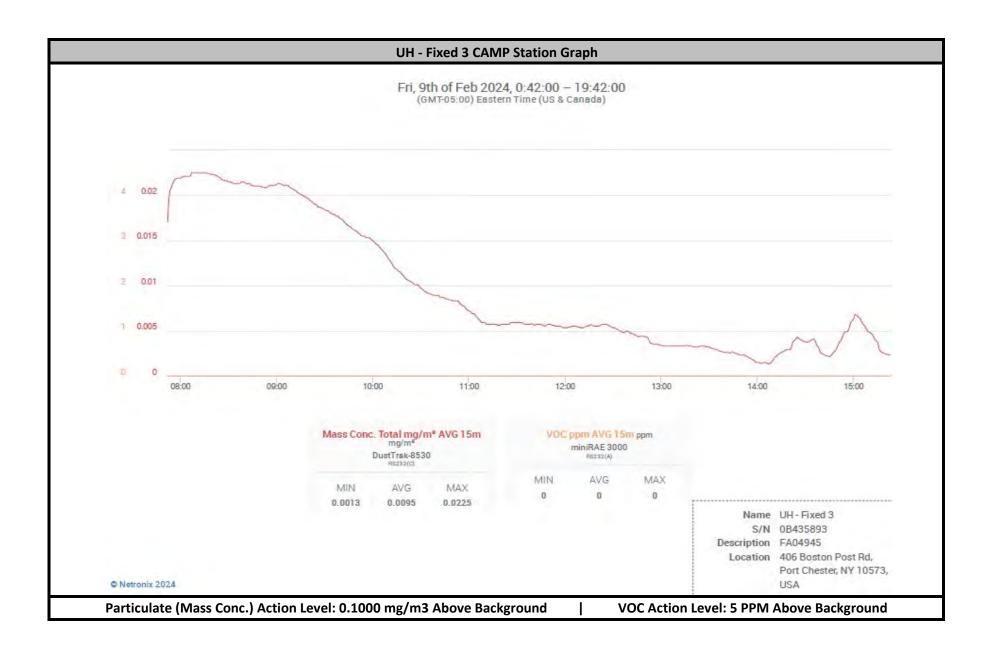

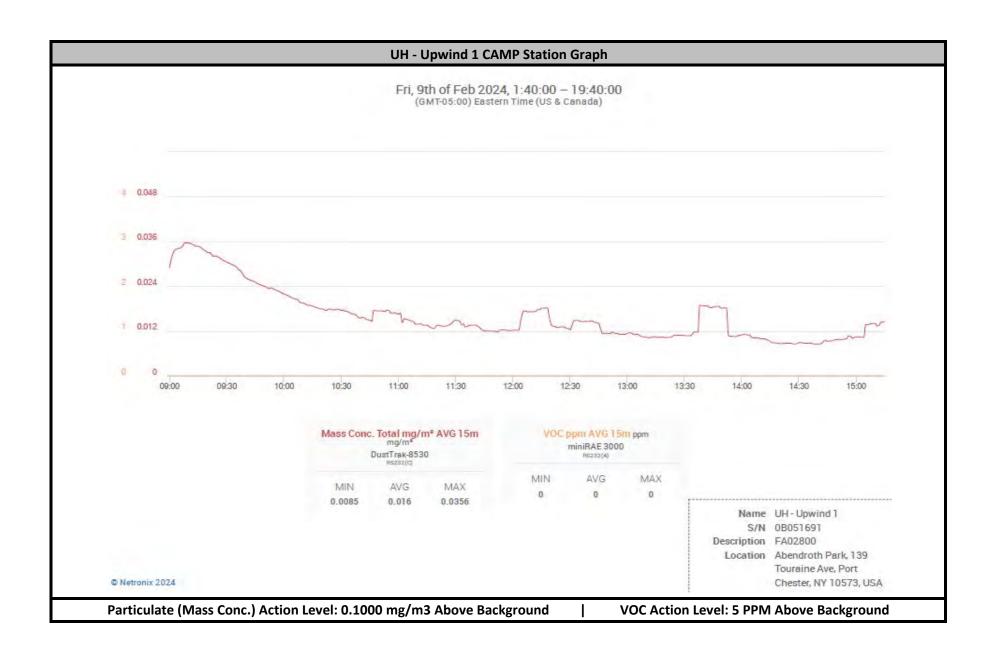

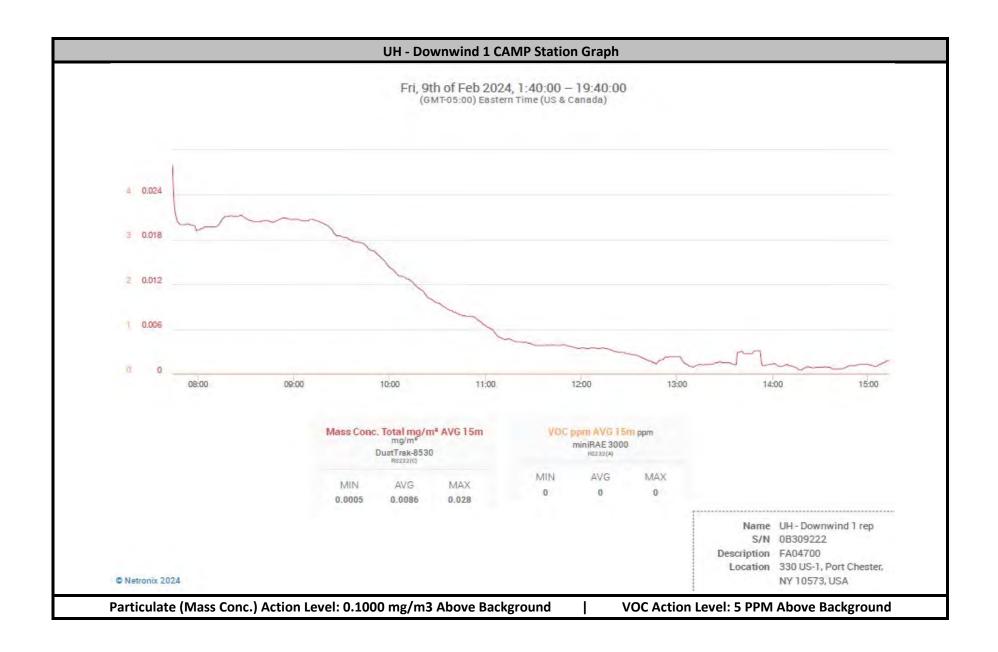


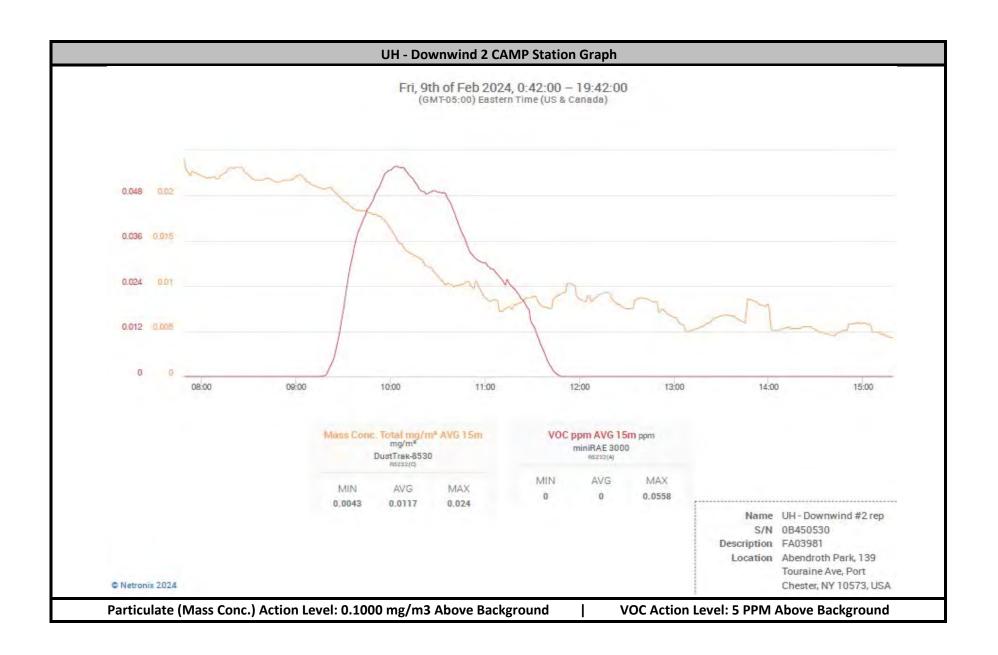



| | | Daily Activity Report | | | | | | | | |
|--|--------------------------|--|------------------------|-------------------------------|--|---------------------|-------------------------------|--|--|--|
| CAK RF | | Former United Hospital | | | | | | | | |
| | | Port Chester, NY BCP No. C360202 | | | | | | | | |
| | Ĭ | Genera | al Site Information | | 40.0004 | | | | | |
| Date: Weather: | | | | Monday, Febru Partly Sunny | | | | | | |
| Wind Direction/Speed: | NNW @5 mph | | | | | | | | | |
| AKRF Personnel on Site: AKRF Equipment on Site: | 3 Fixed CAN | Michael Iodice 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor | | | | | | | | |
| Visitors: | | | | Non | | , , | | | | |
| Contracting Company | 1 | Contractor Information | | | | | | | | |
| Tony Casale Inc. | | Key Personnel Equipment Various excavation and grading equipment | | | | | | | | |
| (Excavation Contractor) | | Rigo | Diaz | | (e.g., ex | cavators, compactor | s, roller-compactor, etc.) | | | |
| Capital Industries Corp. (Demolition Contractor) | | Joe Cianciulli | | | Various demolitio (e.g., excavators, skid steers, | | | | | |
| | D | escription and Locat | ion of Work Activitie | es Performed | | | | | | |
| The excavation contractor imported 6 loads of Item #4 from 1 | ilcon West Nyack, and c | onducted general gr | ading within the ante | ennae Change of Use | e (COU) area. | | | | | |
| The demolition contractor continued sorting and loading den | oltion debris into conta | iners for off-site disp | osal. | | | | | | | |
| | | Site Soil Dispo | osal Tracking Inform | ation | | | | | | |
| Destination Facility | Daily | Daily Trucks | | Daily Approx. Cubic Yds. | | ite Loads | Total Approximate Cubic Yards | | | |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | 710 | | | |
| | | Daily Export (CY) | | 0 | | Total Export (CY) | 710 | | | |
| | | Imported F | ill Tracking Informati | ion | | | | | | |
| Origin Facility | Daily | Daily Trucks | | Daily Approx. Cubic Yds. | | te Loads | Total Approximate Cubic Yards | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4) | | 6 | | 150 | | 54 | 1,535 | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | 45 | | | |
| | | Daily Import (CY) | | 150 | | Total Import (CY) | 1,580 | | | |
| CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | | |
| Odors: | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | | |
| VOC Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | | |
| Particulate Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | | |
| | | Δddi+ | ional Information | | | | | | | |
| Planned Work Activity for Following Day(s): The excavation contractor will continue to import Item #4 from Tilcon West Nyack for use within the antennae COU area as structural backfill above a demarcation layer. | | | | | | | | | | |
| Comments: None | | | | | | | | | | |


1 of 76 C360202_Daily Report_2024.02.12




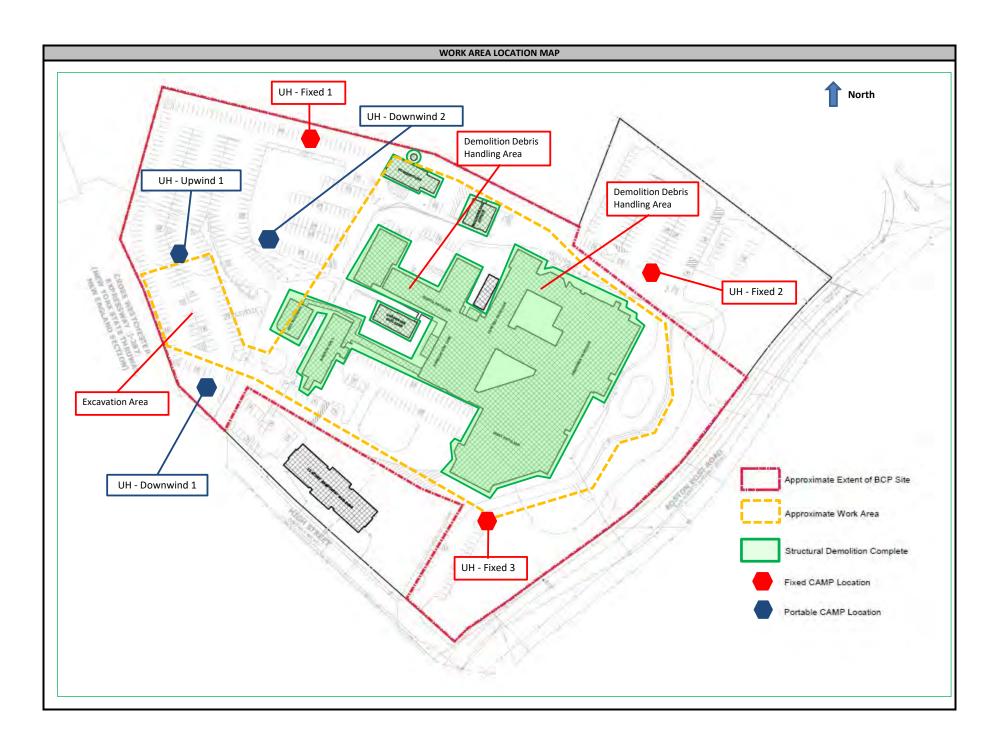


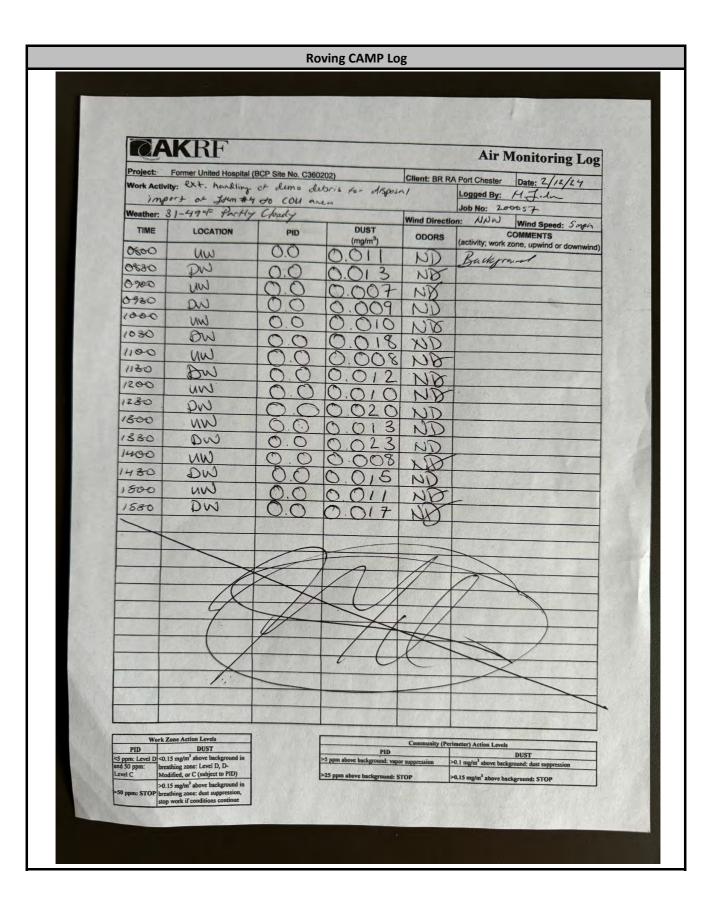


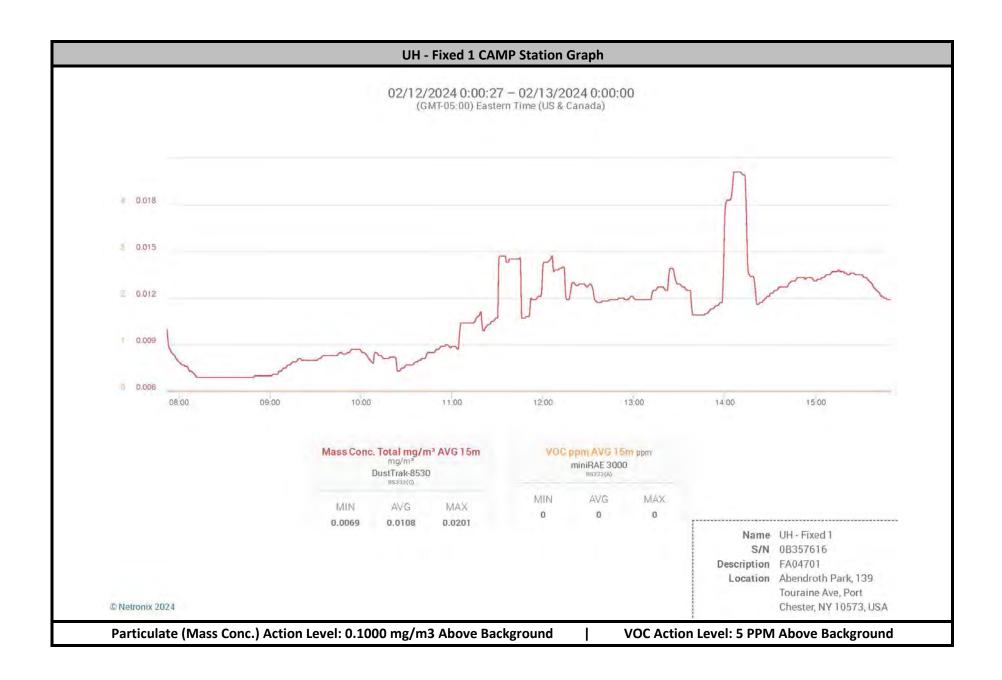


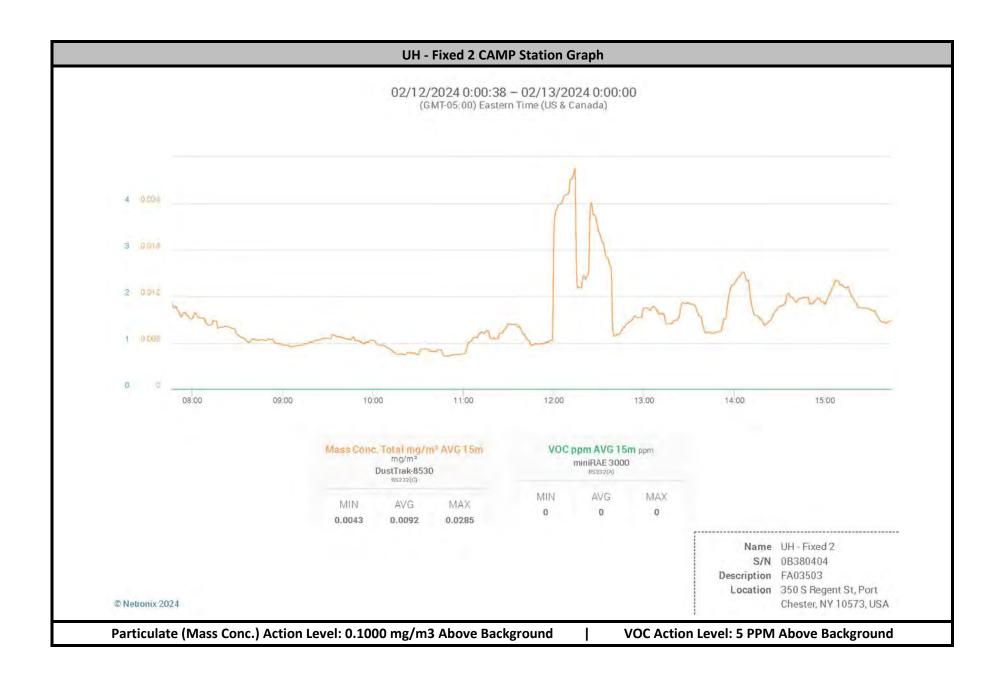

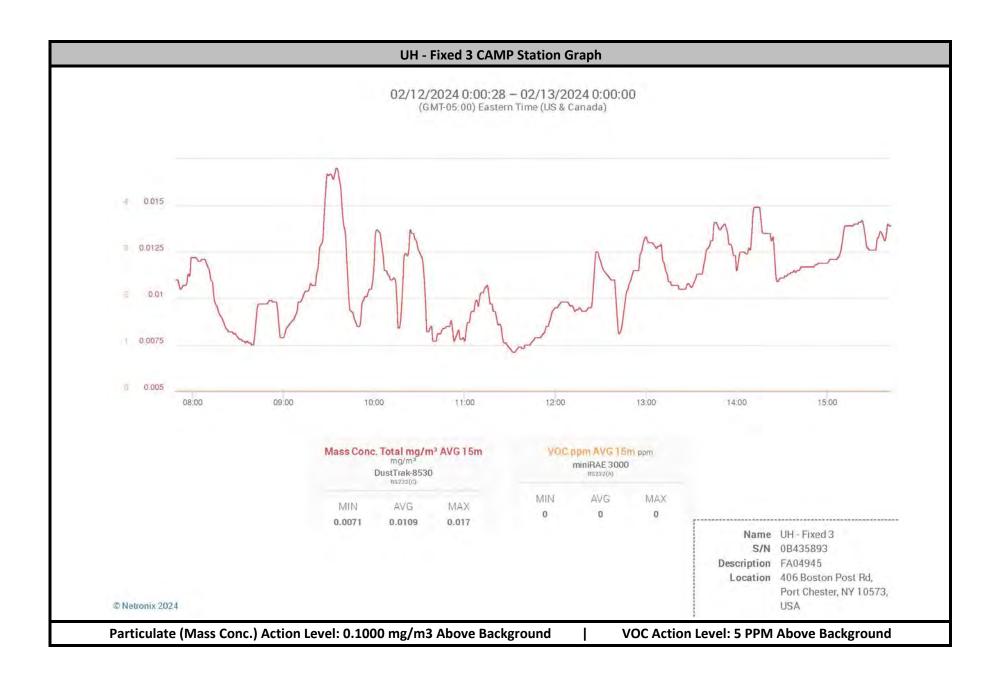

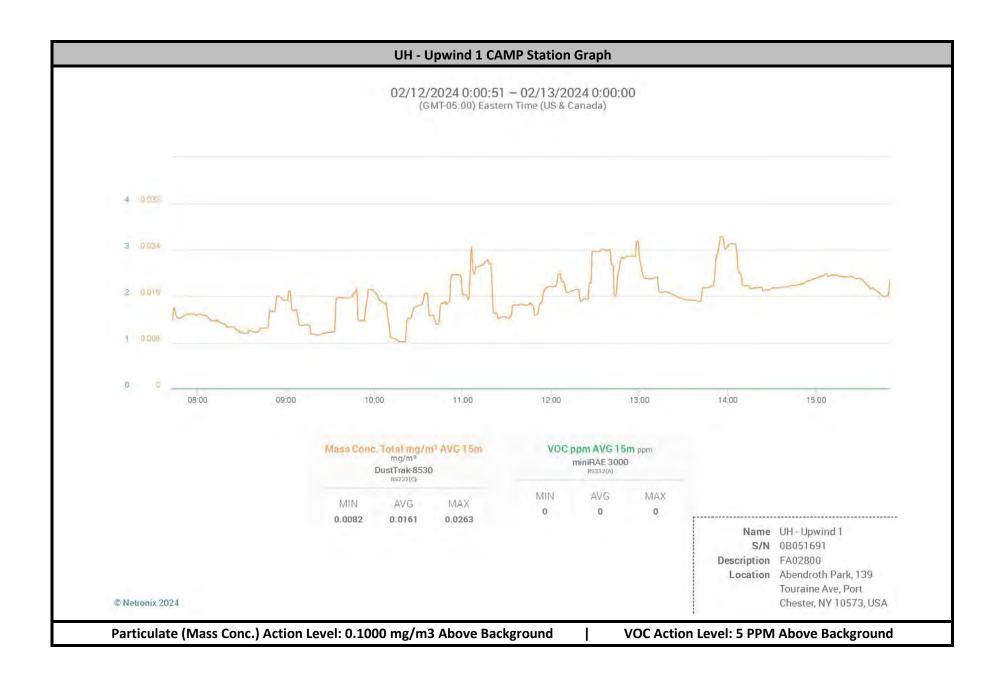

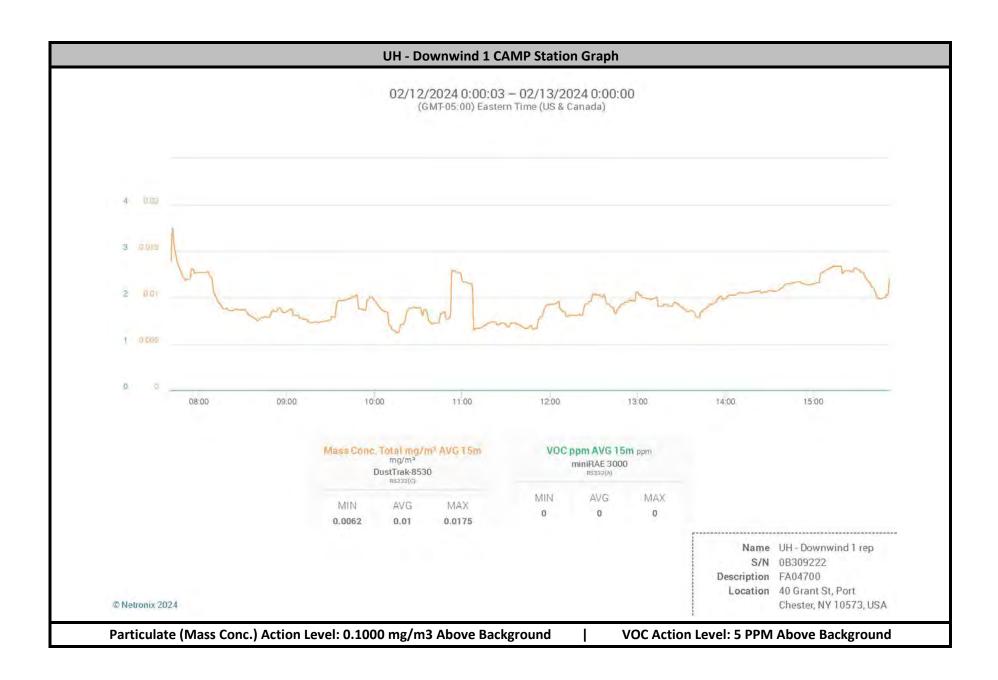


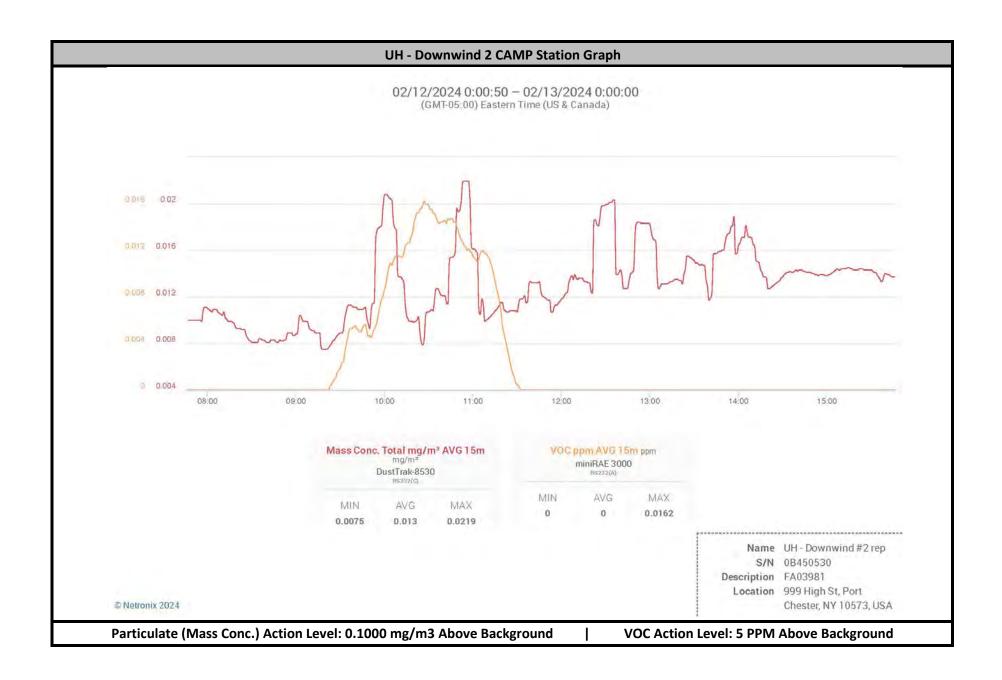



| | | Daily Activity Report | | | | | | | | |
|--|--|--|------------------------|-----------------------|--------------------------|--|---|--|--|--|
| PAKI | ₹ F' | Former United Hospital Port Chester, NY BCP No. C360202 | | | | | | | | |
| | . u | | | | | | | | | |
| Date: | | | Genera | I Site Information | Wednesday, Feb | guany 14, 2024 | | | | |
| Weather: | | | | | Sunny, 2 | | | | | |
| Wind Direction/Speed: AKRF Personnel on Site: | | | NW @ 15 mph | | | | | | | |
| AKRF Equipment on Site: | | Michael Iodice 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monit | | | | | | | | |
| Visitors: | | | 6 | | Non | e | | | | |
| Contra | racting Company | Contractor Information Key Personnel Equipment | | | | | | | | |
| Tor | ny Casale Inc. | | Rigo | Diaz | Va | Various excavation and grading equipment | | | | |
| | ation Contractor) | | | 3102 | | (e.g., ex | | s, roller-compactor, etc.) | | |
| | l Industries Corp. lition Contractor) | | Joe Cia | nciulli | | (e.g., ex | Various demolitic cavators, skid steers, | on equipment roll off containers, etc.) | | |
| | | | escription and Locat | | | | | | | |
| The excavation contractor in | installed forms for an upcoming conre | te pour and conduct | ed general grading w | ithin the antennae C | hange of Use (COU) | area. | | | | |
| The demolition contractor of | continued sorting and loading demolti | on debris into contai | ners for off-site disp | osal. | | | | | | |
| | | | Site Soil Dispo | osal Tracking Inform | ation | | | | | |
| Dest | Destination Facility | | Daily Trucks | | Daily Approx. Cubic Yds. | | te Loads | Total Approximate Cubic Yards | | |
| clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | |
| | | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | |
| | | | Imported Fi | II Tracking Informati | ion | | | | | |
| Origin Facility Daily Trucks Daily Approx. Cubic Yds. Total Site Loads Total Approximate | | | | | | | Total Approximate Cubic Yards | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4) | | 0 | | 0 | | 64 | | 1,535 | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | | |
| | | Daily Import (CY) | | 0 | | Total Import (CY) | | 1,580 | | |
| CAN | AP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| VOC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| Particulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| | | | Additi | onal Information | | | | | | |
| Activity for Following | ed Work The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal. or Following | | | | | | | | | |
| Comments: None | 2. | | | | | | | | | |


1 of 64 C360202_Daily Report_2024.02.


Site Photographs Network:Feb 14, 2024 at 10:15:36 AM EST N 40° 59' 40.005", W 73° 40' 39,603 Boston Post Rd. United Photograph 1 -Excavation contractor conducting general grading within the antennae COU area, view facing southwest. PAKRE Network:Feb 14, 2024 at 11:19:38 AM EST N 40° 59' 39.776", W 73° 40' 36.380" Boston Post Rd, United States Photograph 2 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north. **AK**RF Network:Feb 14, 2024 at 11:19:57 AM EST N 40° 59' 39.469", W 73° 40' 36.606" Boston Post Rd, United States Photograph 3 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north. PAKRE

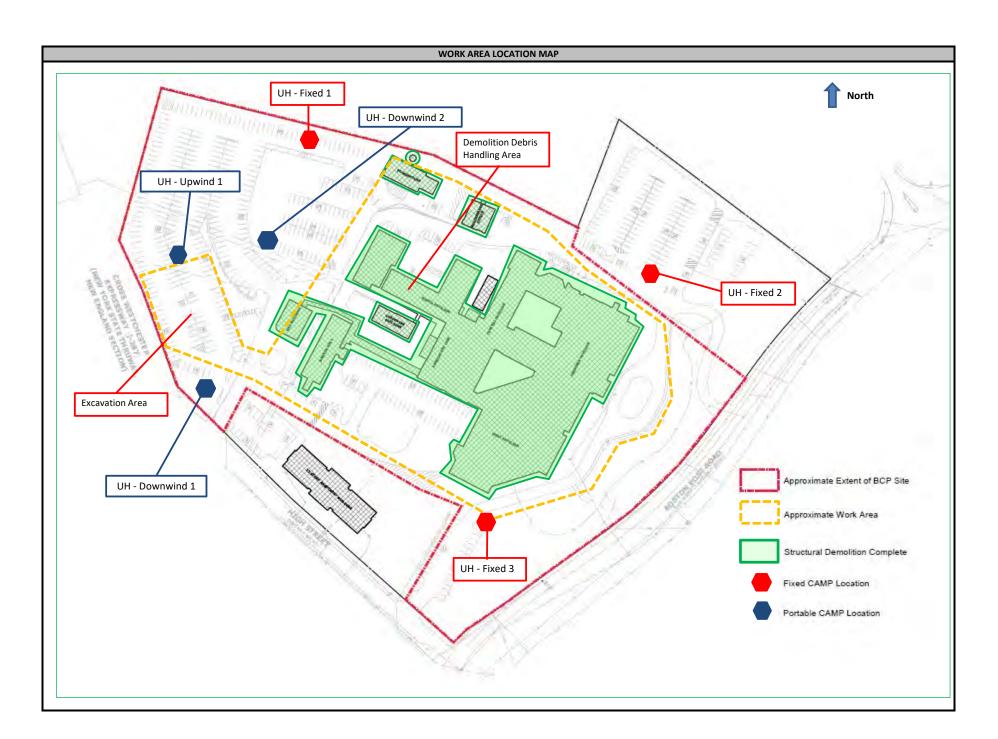


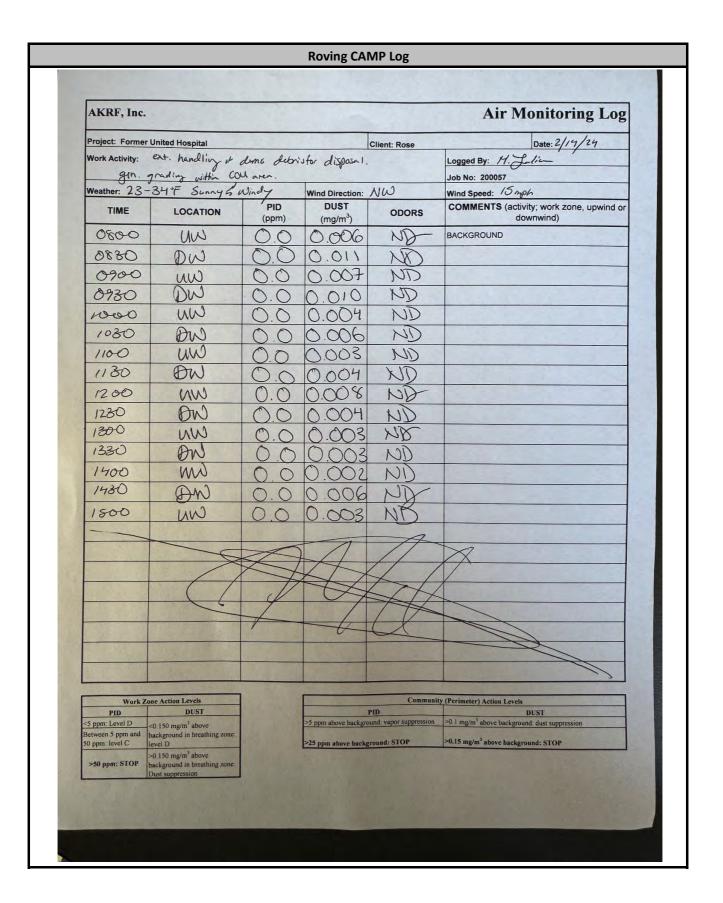


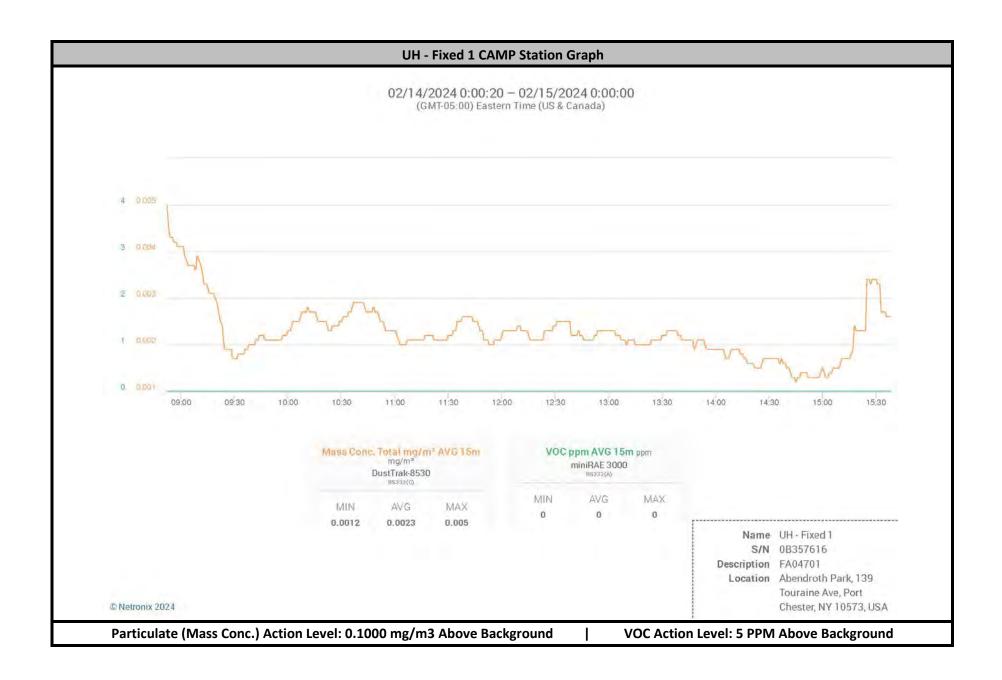


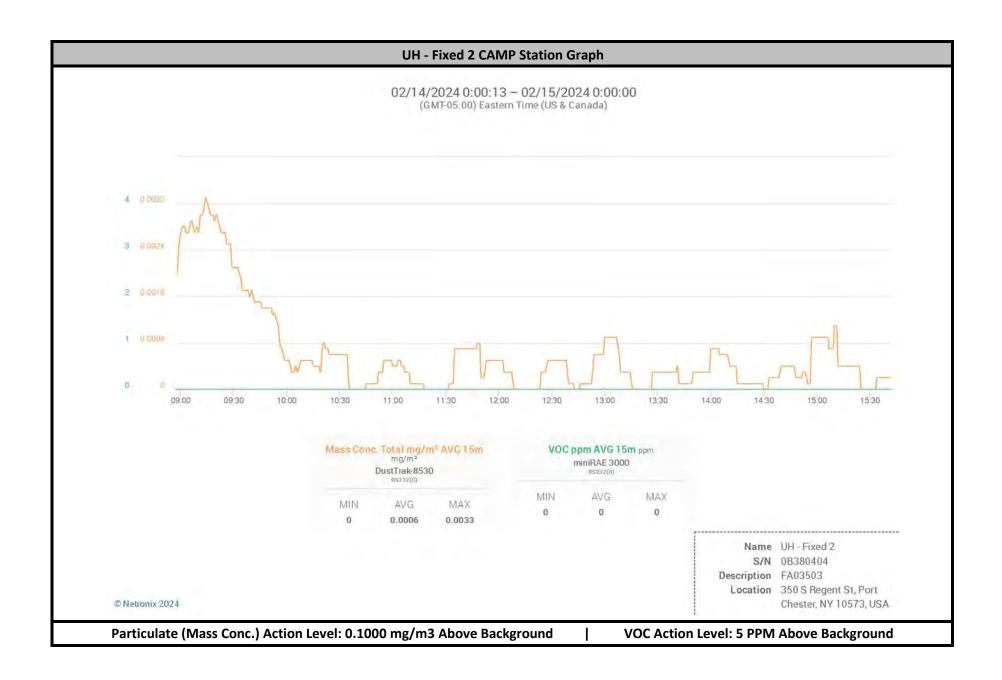

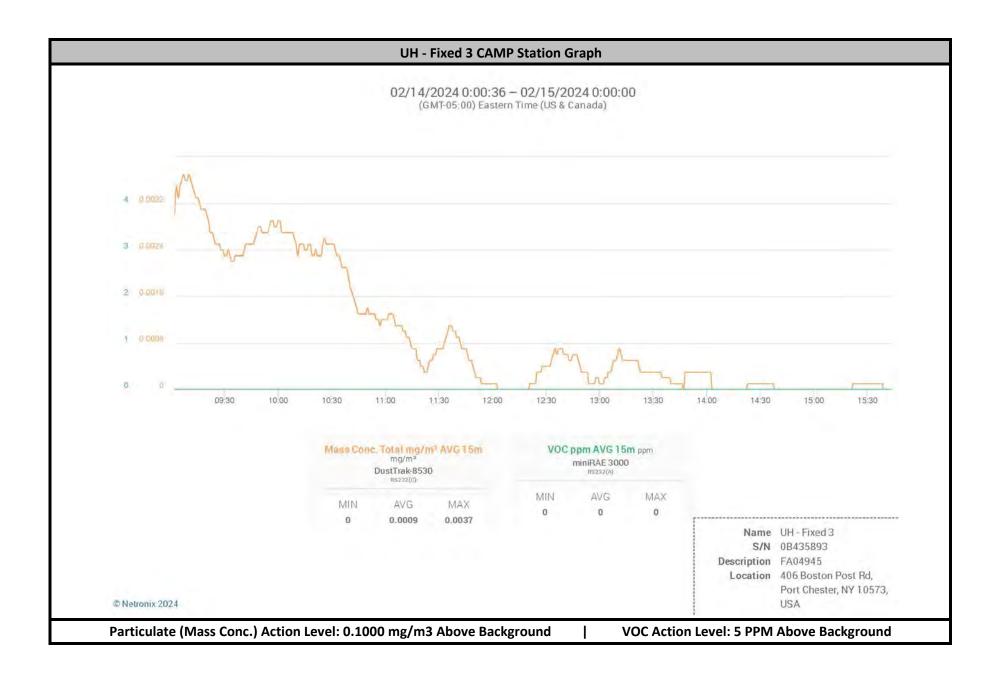

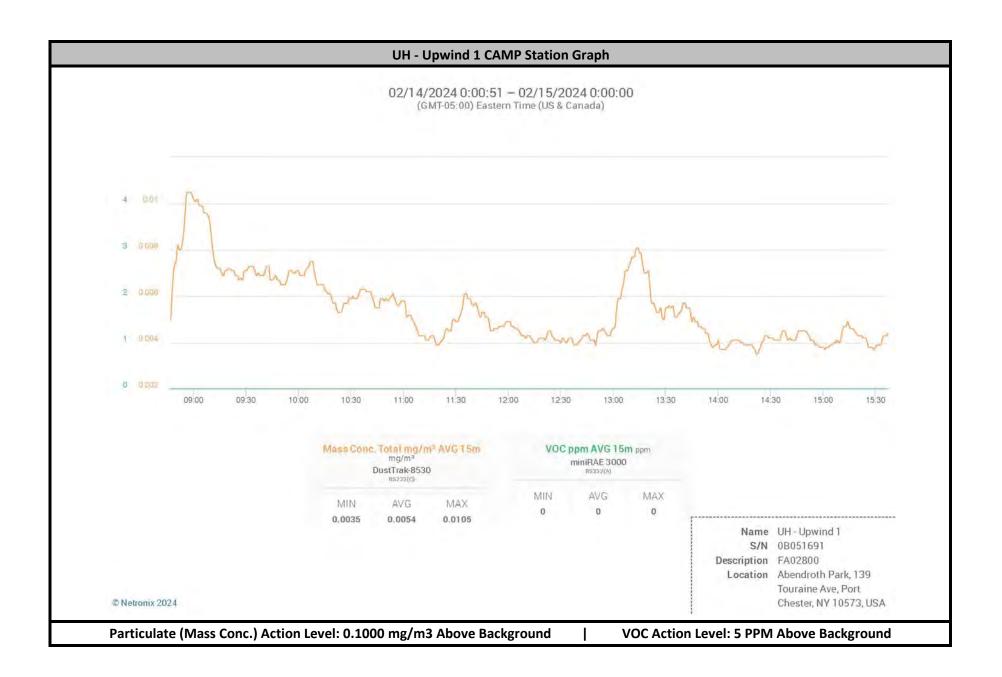

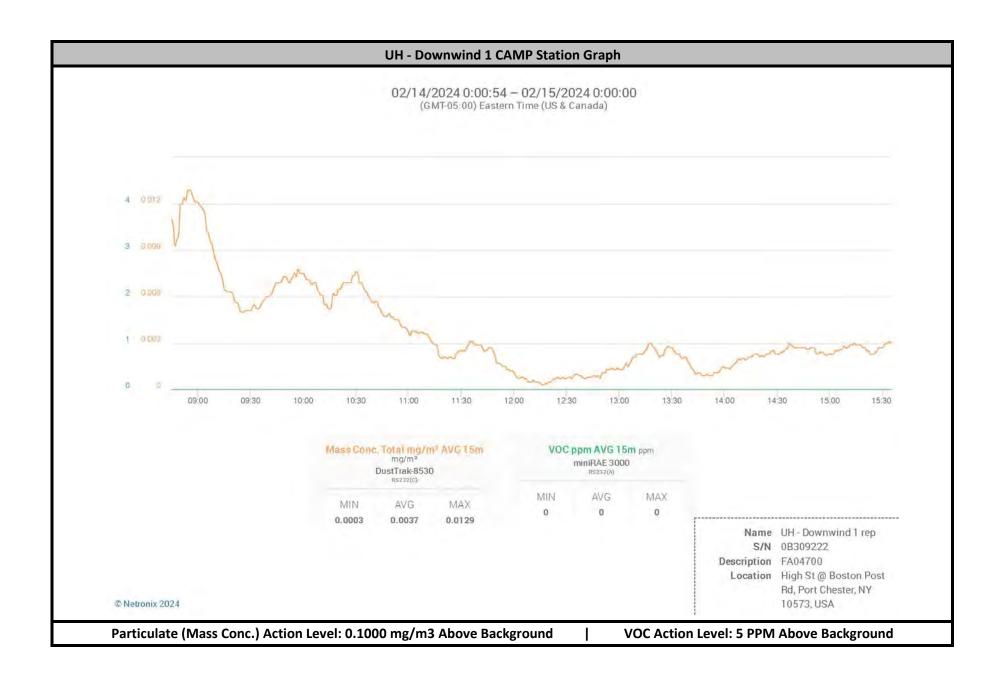


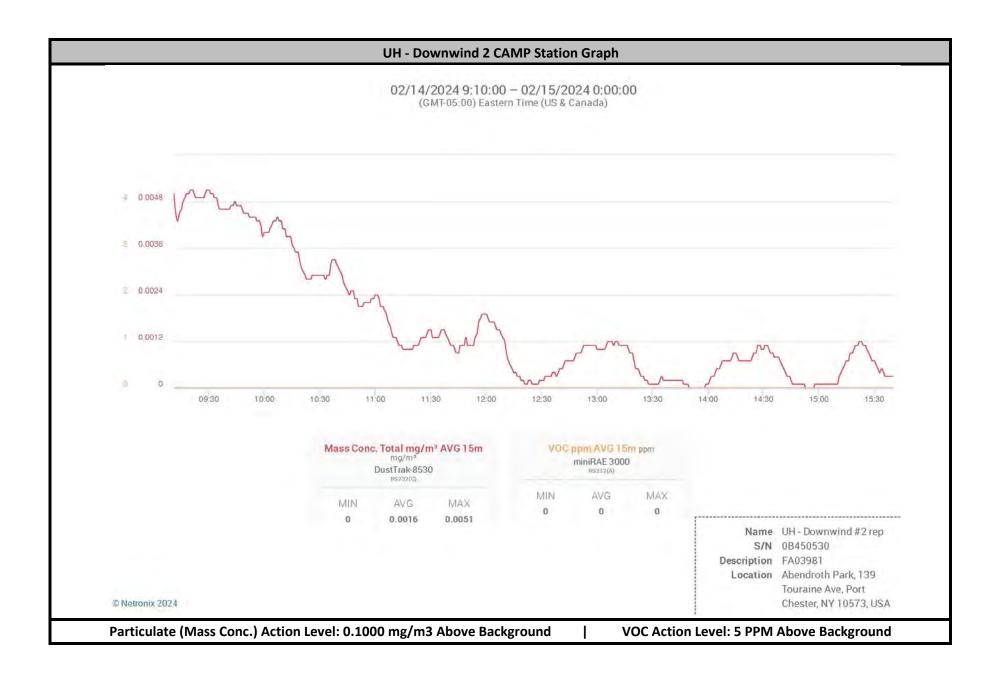



| | | Daily Activity Report Former United Hospital Port Chester, NY BCP No. C360202 | | | | | | | |
|--|---|--|------------------------|-----------------------|--------------------------|---|---------------------|------------------------------|--|
| PAKI | KF' | | | | | | | | |
| | · | | | | | | | | |
| ate: | | ı | Genera | I Site Information | Thursday, Febru | Jany 15, 2024 | | | |
| /eather: | | | | | Partly Cloudy | | | | |
| /ind Direction/Speed: KRF Personnel on Site: | | NW @ 6 mph Michael Iodice | | | | | | | |
| KRF Equipment on Site: | | 3 Fixed CAN | 1P Stations (PID & Du | ıst Monitor), 3 Porta | | | , One Handheld PID, | One Handheld Dust Monitor | |
| sitors: | | | | • | Non | | | | |
| Conti | racting Company | Contractor Information Key Personnel Equipment | | | | | | | |
| | ony Casale Inc. | Rigo Diaz Various excavation and grading equipmen | | | | | | | |
| (Excav | vation Contractor) | | Rigo | Diaz | | (e.g., ex | cavators, compactor | s, roller-compactor, etc.) | |
| | al Industries Corp. Dition Contractor) | | Joe Cia | anciulli | | Various demolition (e.g., excavators, skid steers | | | |
| | | D | escription and Locat | ion of Work Activitie | es Performed | | | | |
| e excavation contractor | installed forms for an upcoming conre | te pour, and conduct | ed general grading a | nd compaction with | in the antennae Cha | inge of Use (COU) an | ea. | | |
| ne demolition contractor | continued sorting and loading demolti | ion debris into contai | ners for off-site disp | osal. | | | | | |
| | | | Site Soil Dispo | osal Tracking Inform | ation | | | | |
| Desi | tination Facility | Daily Trucks | | Daily Approx | Daily Approx. Cubic Yds. | | te Loads | Total Approximate Cubic Yard | |
| ean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | |
| | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | |
| | | | Imported Fi | II Tracking Informati | on | | | | |
| C | Origin Facility | Daily ' | Trucks | Daily Approx | . Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yard | |
| Filcon West Nyack Quarry - West Nyack, NY ITEM #4) | | 0 | | 0 | | 64 | | 1,535 | |
| Filcon West Nyack Quarry - West Nyack, NY NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | |
| | | Daily Import (CY) | | 0 | | Total Import (CY) | | 1,580 | |
| CAN | MP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | |
| dors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | |
| OC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | |
| articulate Action Level Exc | ceedance(s) Above Background: | No | No | No | No | No | No | No | |
| | | | Additi | onal Information | | | | | |
| ctivity for Following | demolition contractor will continue so excavation contratcor will continue to | | | | _ | | | ıyer. | |
| | Particulate data from the UH - Fixed 3 CAMP station did not report to the online database from approximately 13:21 until 14:07 due to a telemetry issue; the equipment was reset, and the station was fully operational by 14:08. No elevated levels of VOCs were detected with nearby CAMP or roving equipment during the period that particulates were not reported at the UH - Fixed 3 CAMP station. | | | | | | | | |


1 of 69 C360202_Daily Report_2024.02.15


Site Photographs Boston Post Rd, United State Photograph 1 -Excavation contractor conducting general grading within the antennae COU area, view facing southwest. PAKRE Network:Feb 15, 2024 at 9:14:34 AM EST N 40° 59' 39.285", W 73° 40' 37.207" Boston Post Rd, United States Photograph 2 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north. AKRE Network:Feb 15, 2024 at 1:44:37 PM EST N 40° 59' 40.012", W 73° 40' 37.401" Boston Post Rd, United States Photograph 3 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north.

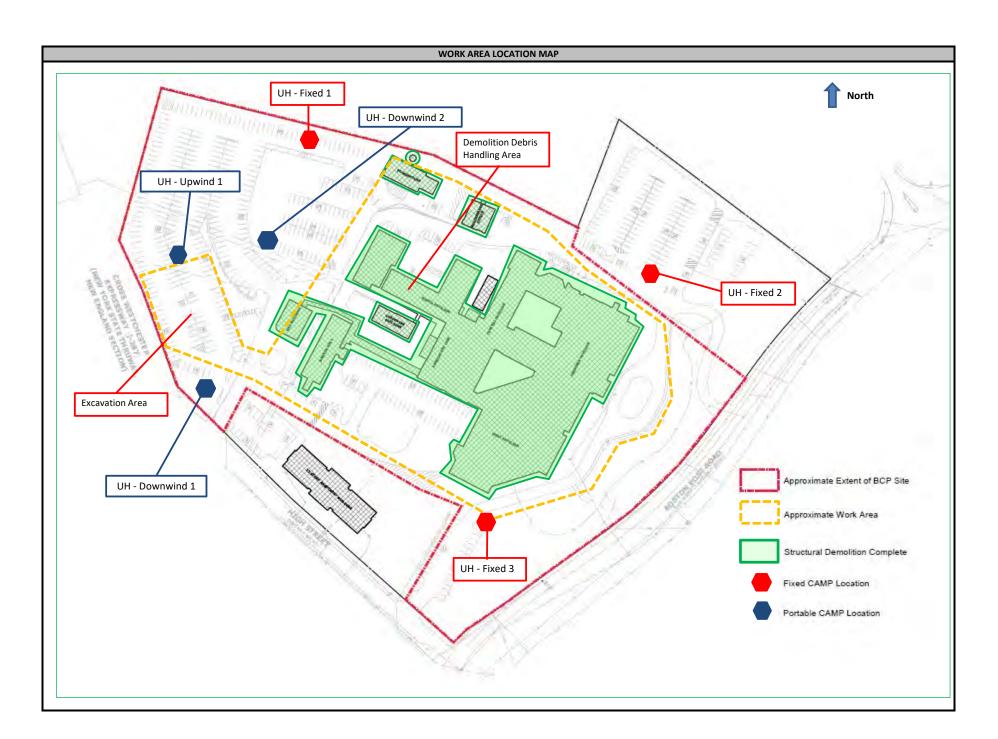


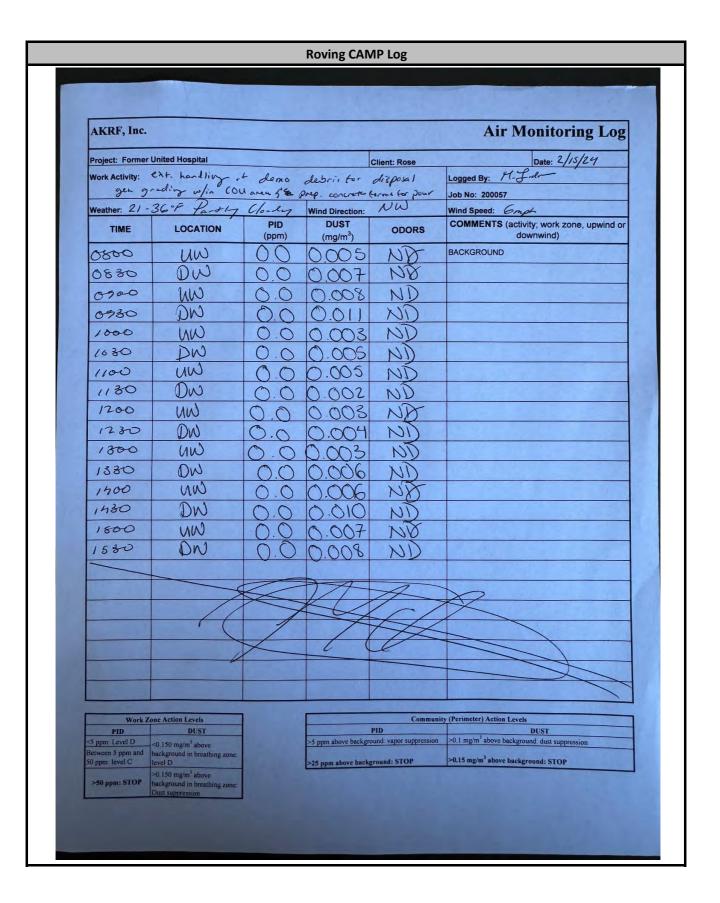


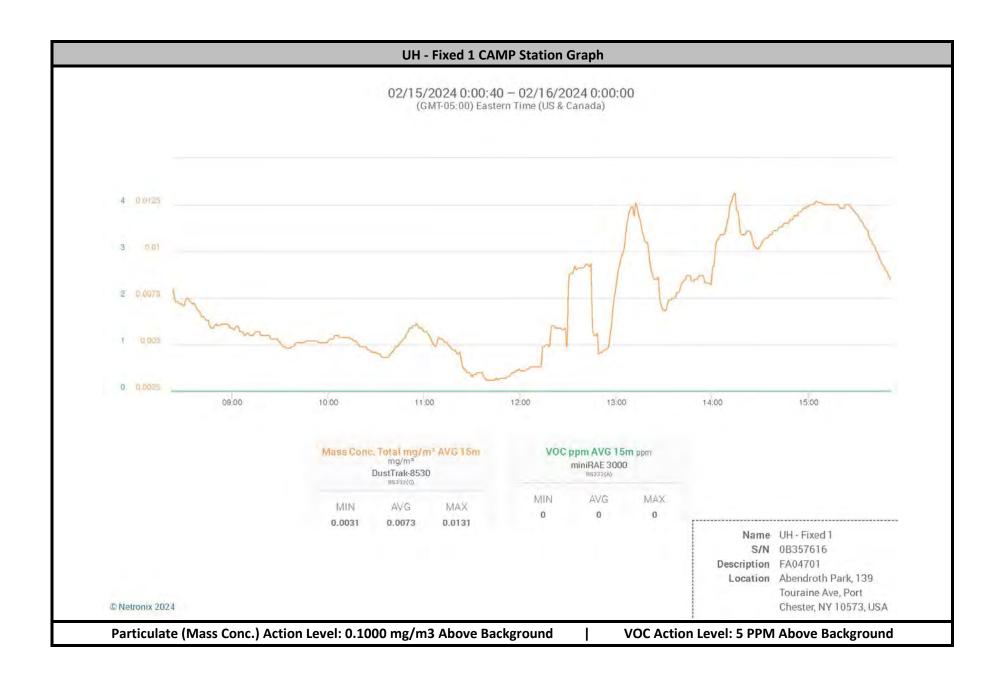


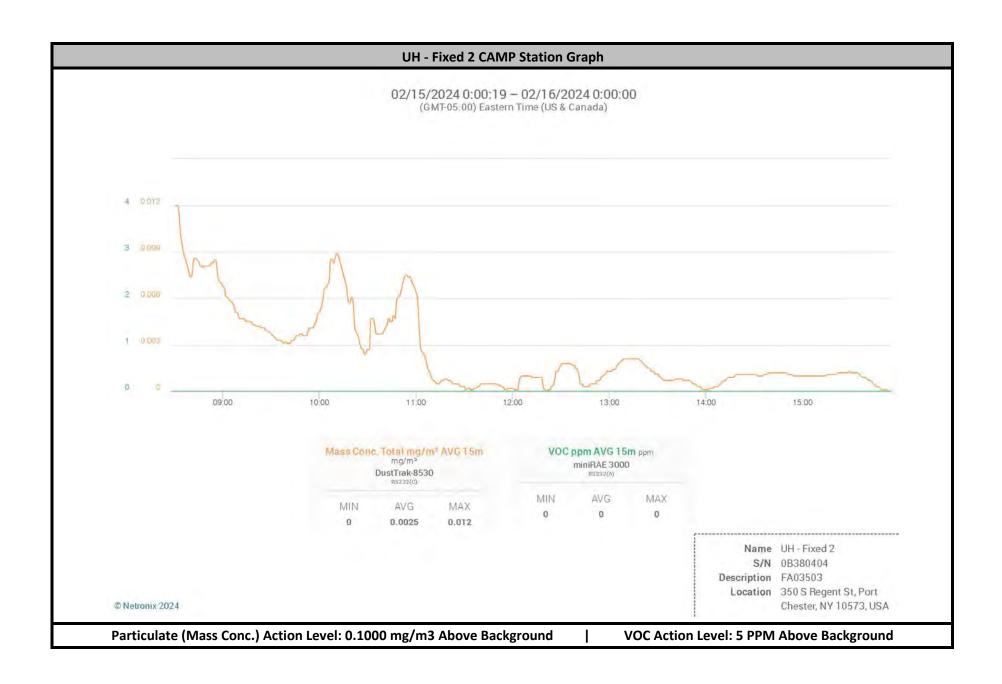

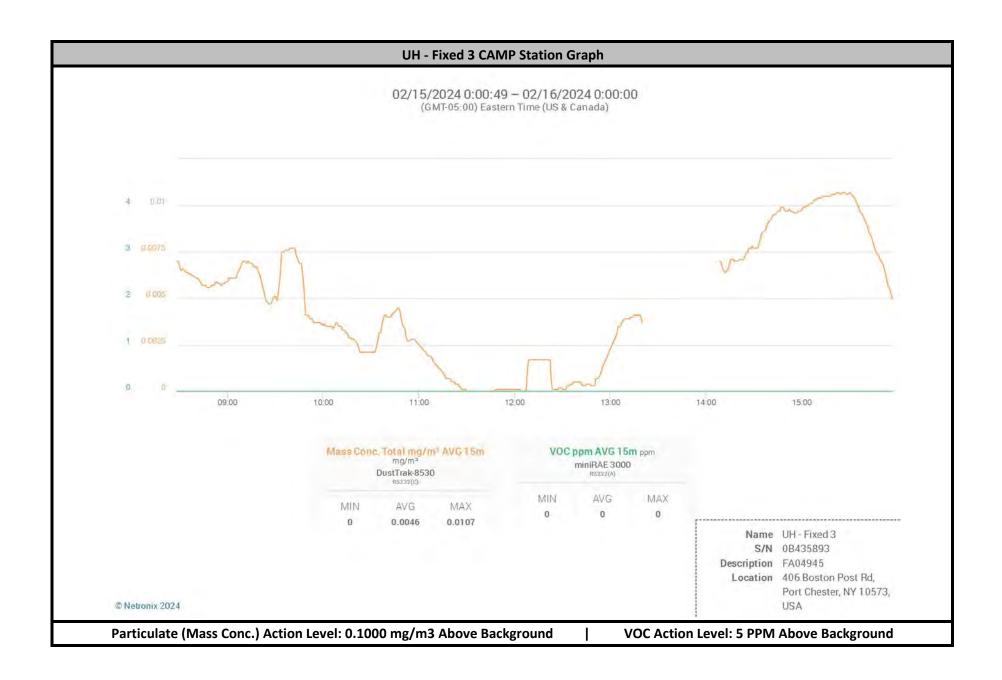

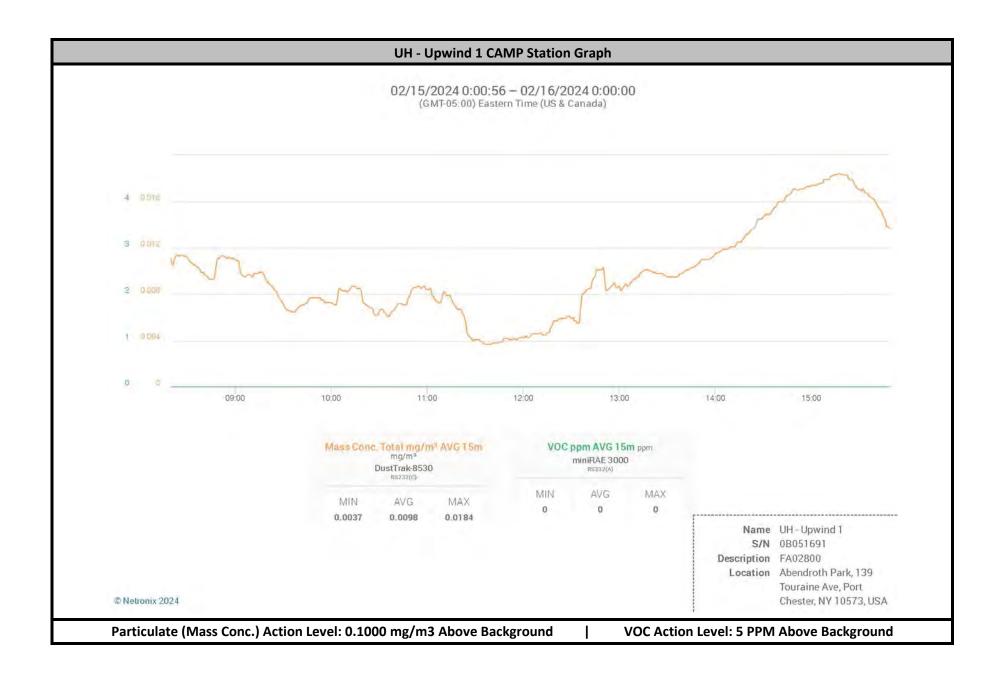


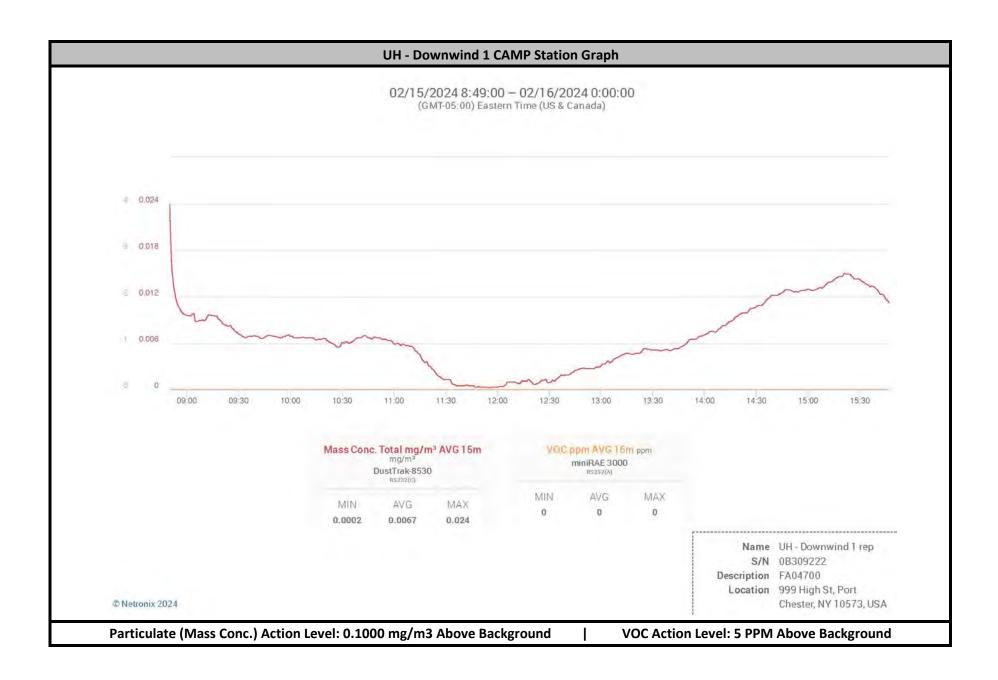


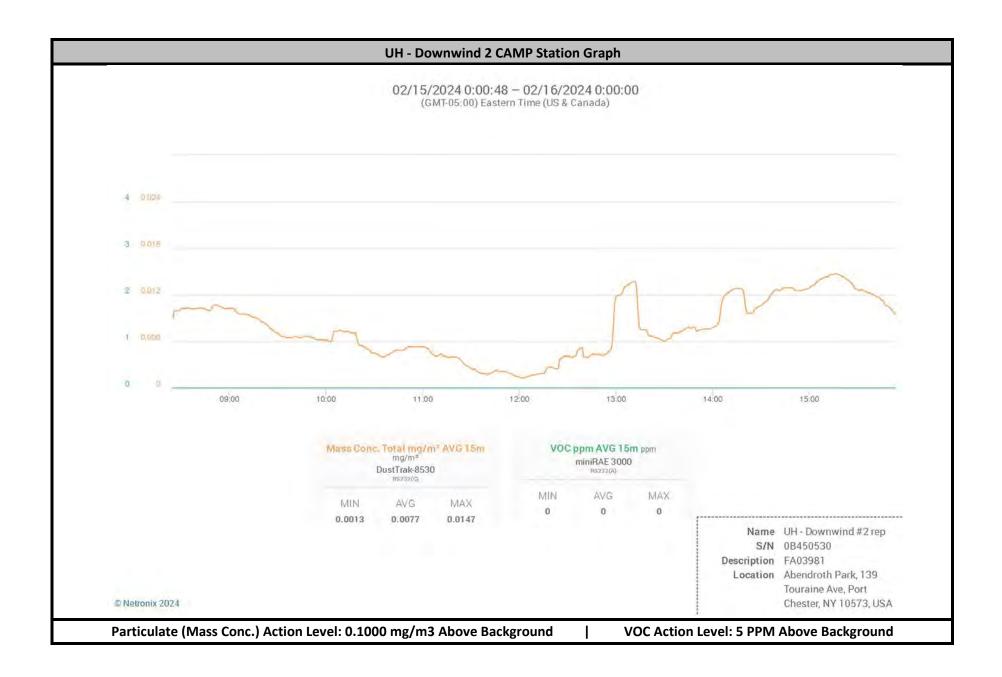



| | Daily Activity Report | | | | | | | | | |
|---|---|---|-------------------------------|-----------------------|---------------------|---|---------------------|-------------------------------|--|--|
| PAK | m RF | Former United Hospital | | | | | | | | |
| | a u | Port Chester, NY BCP No. C360202 | | | | | | | | |
| Date: | | | Genera | Site Information | Friday, Februa | rv 16. 2024 | | | | |
| Weather: | | Partly Cloudy, 30-40°F NW @ 15 mph | | | | | | | | |
| Wind Direction/Speed: AKRF Personnel on Site: | : | NW @ 15 mph Michael lodice | | | | | | | | |
| AKRF Equipment on Site | | 3 Fixed CAM | IP Stations (PID & Du | ıst Monitor), 3 Porta | ble CAMP Stations (| PID & Dust Monitor) | , One Handheld PID, | One Handheld Dust Monitor | | |
| Visitors: | | | Contra | ctor Information | Non | e | | | | |
| C | Contracting Company Key Personnel Equipment Topu Corollo Inc. Verieur open parties and good resulting and | | | | | | | | | |
| (Ex | Tony Casale Inc. cavation Contractor) | Rigo Diaz Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.) | | | | | | | | |
| Ca | pital Industries Corp. emolition Contractor) | | Joe Cia | nciulli | | Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.) | | | | |
| | | De | escription and Locati | on of Work Activitie | es Performed | | | | | |
| The excavation contract | tor prepared for and conducted a conrete | pour and general gra | ding and compaction | n within the antenna | e Change of Use (CC | DU) area. | | | | |
| The demolition contract | tor continued sorting and loading demoltic | on debris into contai | ners for off-site dispo | osal. | | | | | | |
| | | | Site Soil Dispo | sal Tracking Informa | ation | | | | | |
| | Destination Facility Daily T | | Trucks Daily Approx. Cubic Yd | | c. Cubic Yds. | Total Site Loads | | Total Approximate Cubic Yards | | |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | |
| | | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | |
| | | | Imported Fil | l Tracking Informati | on | | | | | |
| | Origin Facility | Daily ' | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards | | |
| Tilcon West Nyack Quar (ITEM #4) | rry - West Nyack, NY | 0 | | 0 | | 64 | | 1,535 | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | | |
| | | Daily Import (CY) | | 0 | | | Total Import (CY) | 1,580 | | |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| VOC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| Particulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| | | | Additi | onal Information | | | | | | |
| Activity for Following | Work The demolition contractor will continue sorting and loading of demolition debris from the former hospital buildings into containers for off-site disposal. ollowing | | | | | | | | | |
| Comments: None. | | | | | | | | | | |


1 of 69 C360202_Daily Report_2024.02.

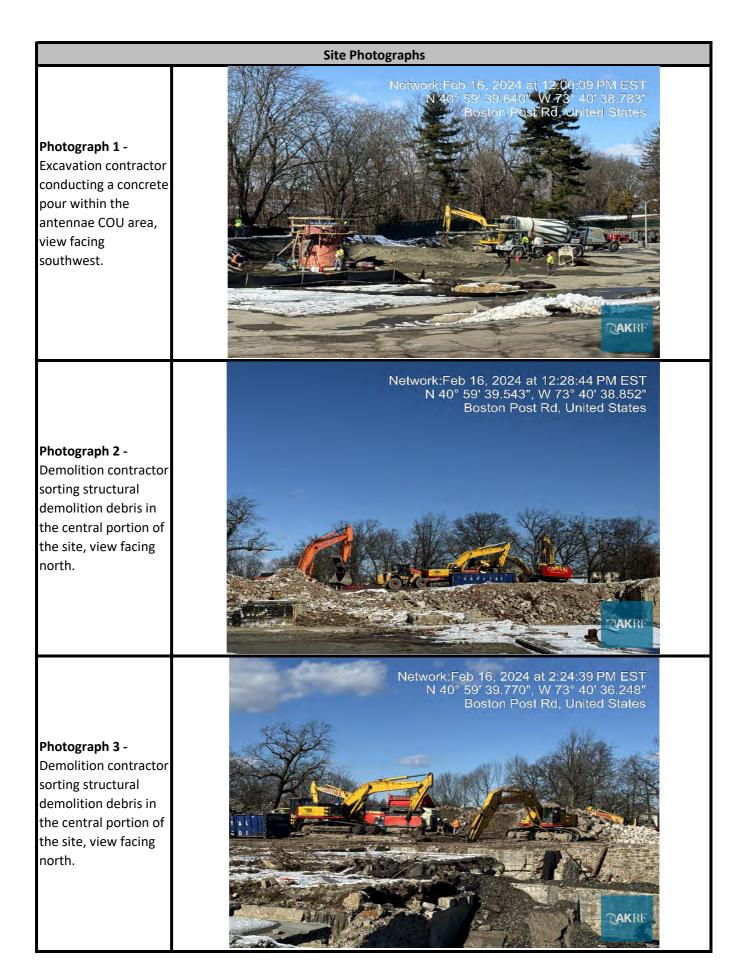


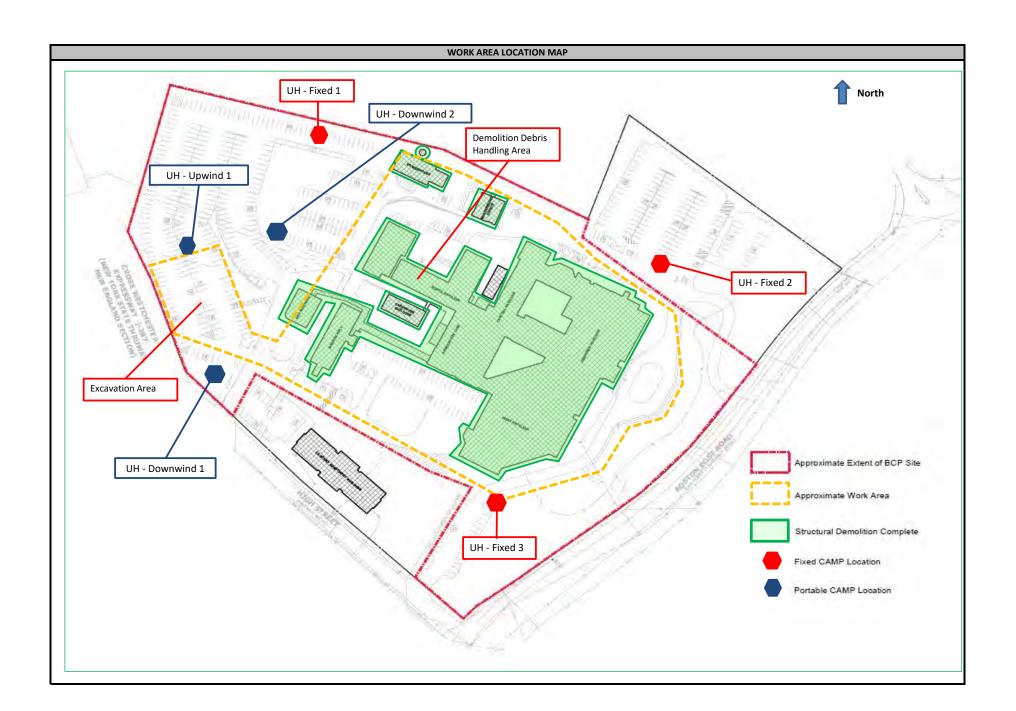


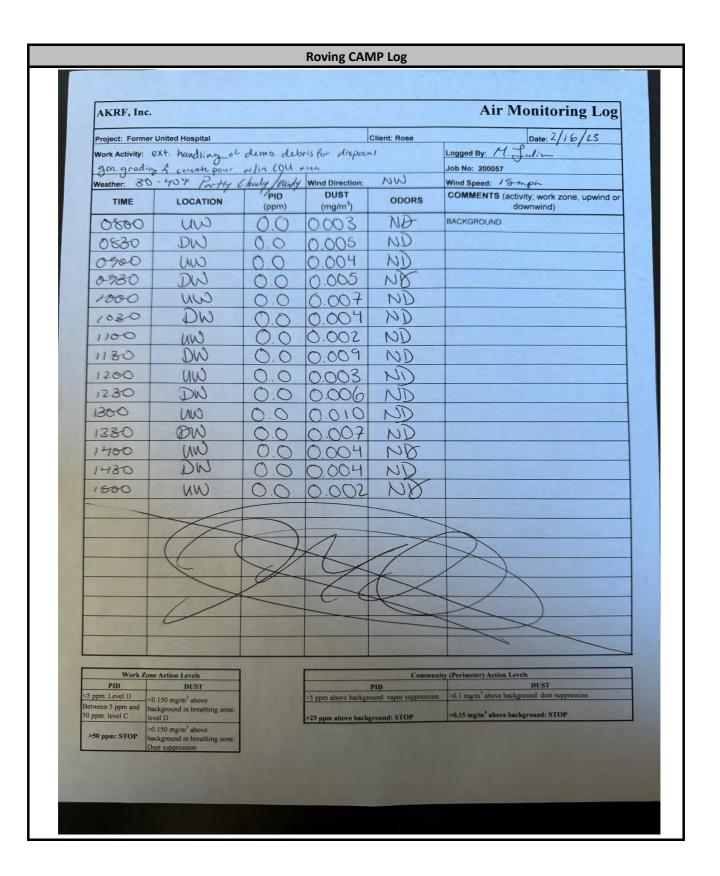


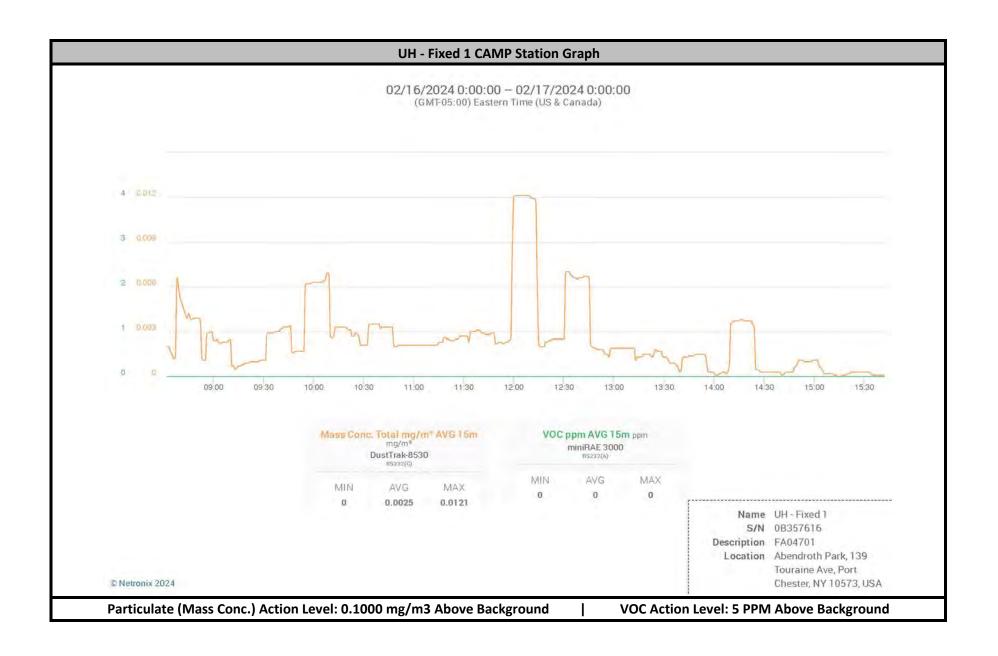


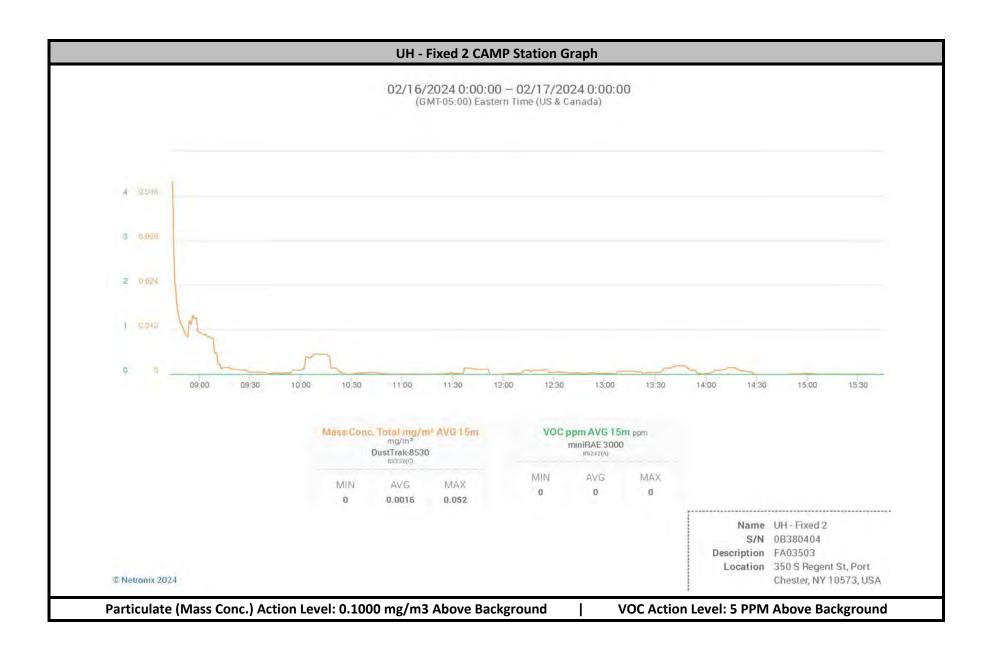

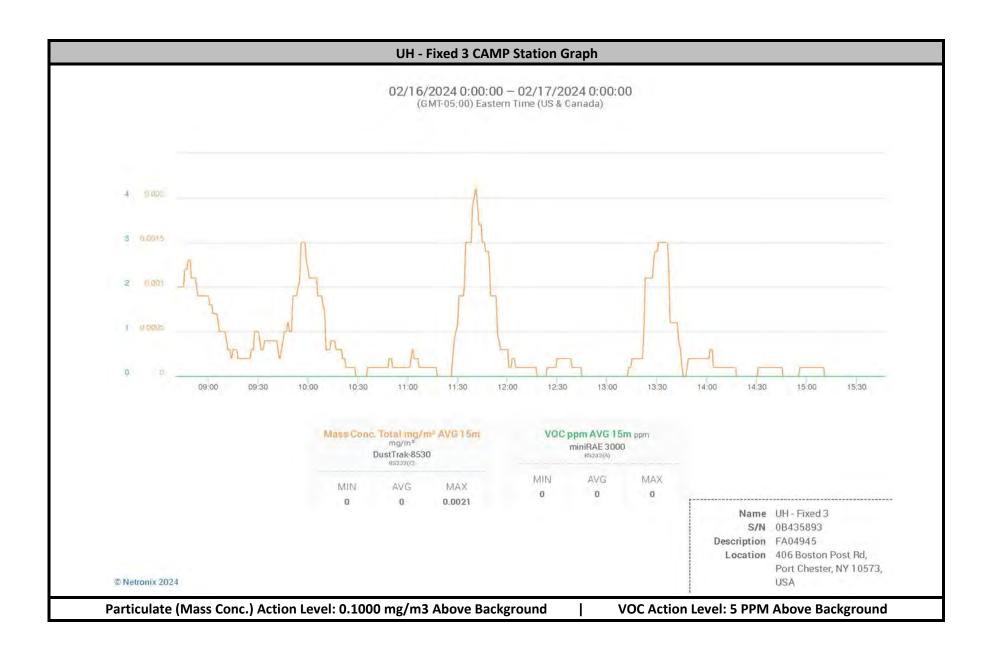

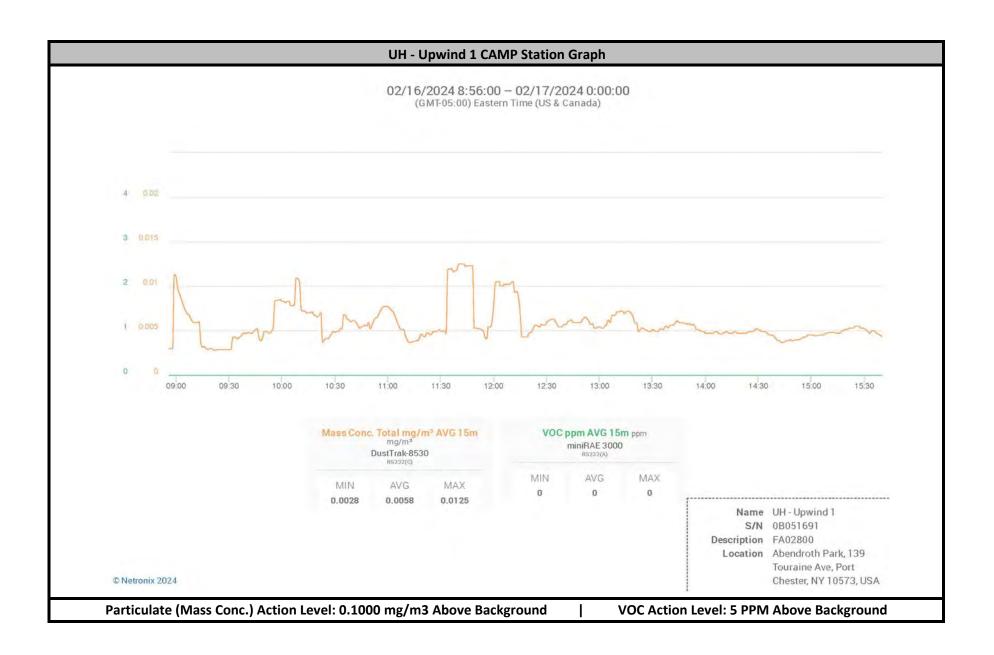


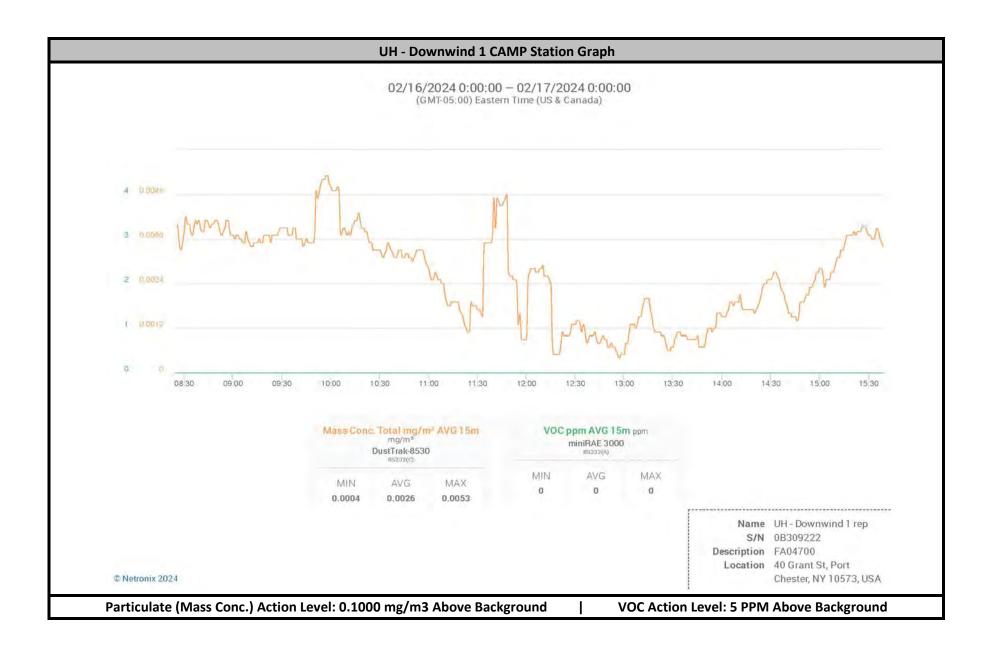


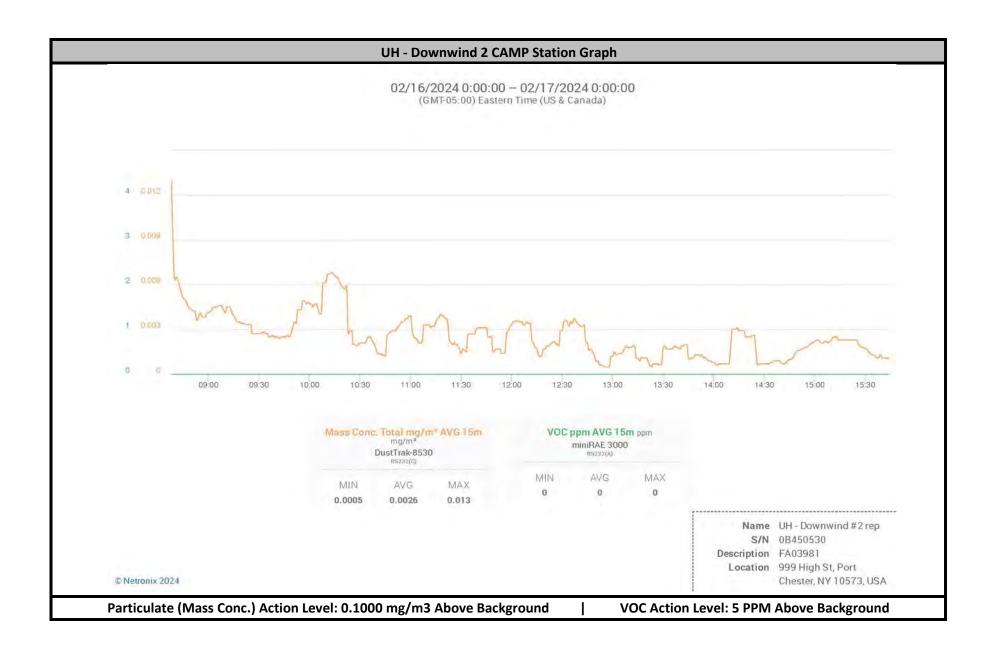



| | | Daily Activity Report | | | | | | | | | |
|---|---|---|--|--------------------------|----------------------------------|--|----------------------|-------------------------------|--|--|--|
| PAK | m RF | Former United Hospital | | | | | | | | | |
| | ıu | Port Chester, NY BCP No. C360202 | | | | | | | | | |
| | | | Genera | al Site Information | | | | | | | |
| Date: Weather: | | | | | Monday, Febru Partly Cloud | | | | | | |
| Wind Direction/Speed: | | | | | NW @ 13 | 3 mph | | | | | |
| AKRF Personnel on Site: AKRF Equipment on Site | | 3 Fixed CAN | IP Stations (PID & Du | ust Monitor), 3 Porta | Stephen S ble CAMP Stations (| | . One Handheld PID. | One Handheld Dust Monitor | | | |
| /isitors: | | 31 Med 6 W | | · · | Non | | , one nanancia i is, | one mananela base monitor | | | |
| Co | ontracting Company | Contractor Information Key Personnel Equipment | | | | | | | | | |
| | Tony Casale Inc. | | Key Personnel Equipment Various excavation and grading equipm | | | | | | | | |
| | cavation Contractor) | | Rigo | Diaz | | | | s, roller-compactor, etc.) | | | |
| | pital Industries Corp. emolition Contractor) | | Joe Cia | anciulli | | Various demolition equipment (e.g., excavators, skid steers, roll off containers, etc.) | | | | | |
| , , | , | De | secription and Locat | ion of Work Activitie | s Dorformed | 1.07 | | , , , | | | |
| he excavation contract | or imported eight (8) loads of Item #4, an | | | | | (COU) area. | | | | | |
| | | | Site Soil Dispo | osal Tracking Informa | ntion | | | | | | |
| | | | | 8 | | | | | | | |
| D | Destination Facility | Daily [·] | Trucks | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic Yards | | | |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | | |
| | | | Daily Export (CY) | | 0 | | Total Export (CY) | 710 | | | |
| | | | Imported Fi | ll Tracking Informati | on | | | | | | |
| | Origin Facility | Daily ¹ | Trucks | Daily Approx | . Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards | | | |
| Tilcon West Nyack Quar (ITEM #4) | ry - West Nyack, NY | 8 | | 0 | | 72 | | 1,735 | | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 | | | |
| | | Daily Import (CY) | | 0 | | Total Import (CY) | | 1,780 | | | |
| C | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | | |
| VOC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | | |
| Particulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | | |
| | | | Additi | onal Information | | | | | | | |
| Activity for Following | ctivity for Following | | | | | | | | | | |
| Comments: N | lone. | | | | | | | | | | |


1 of 71 C360202_Daily Report_2024.02.19

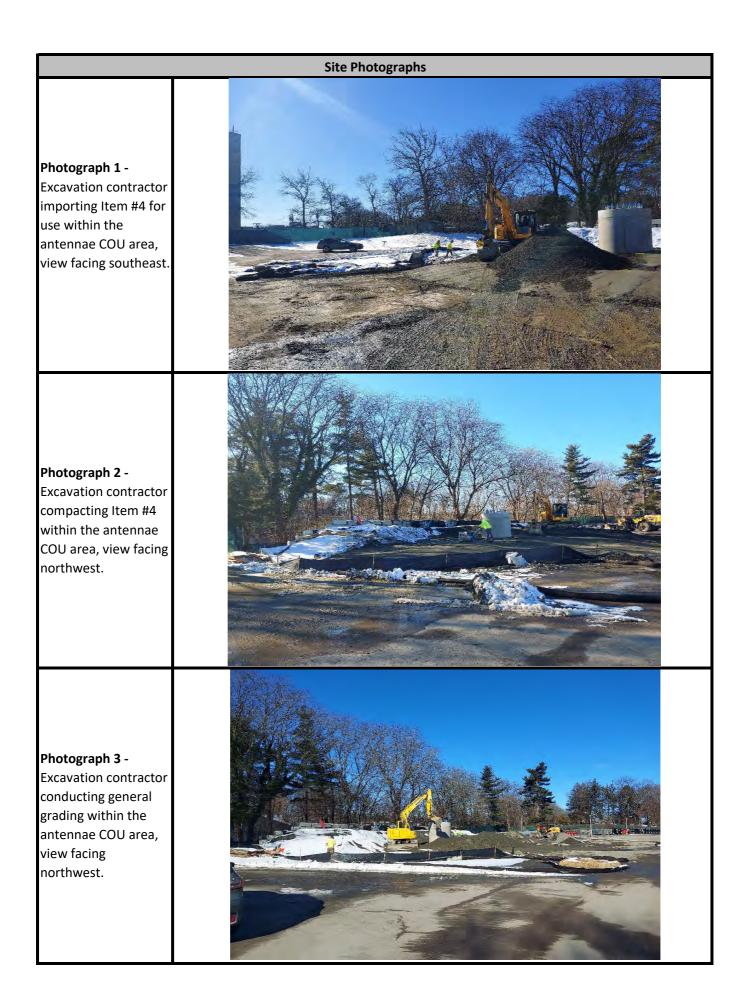


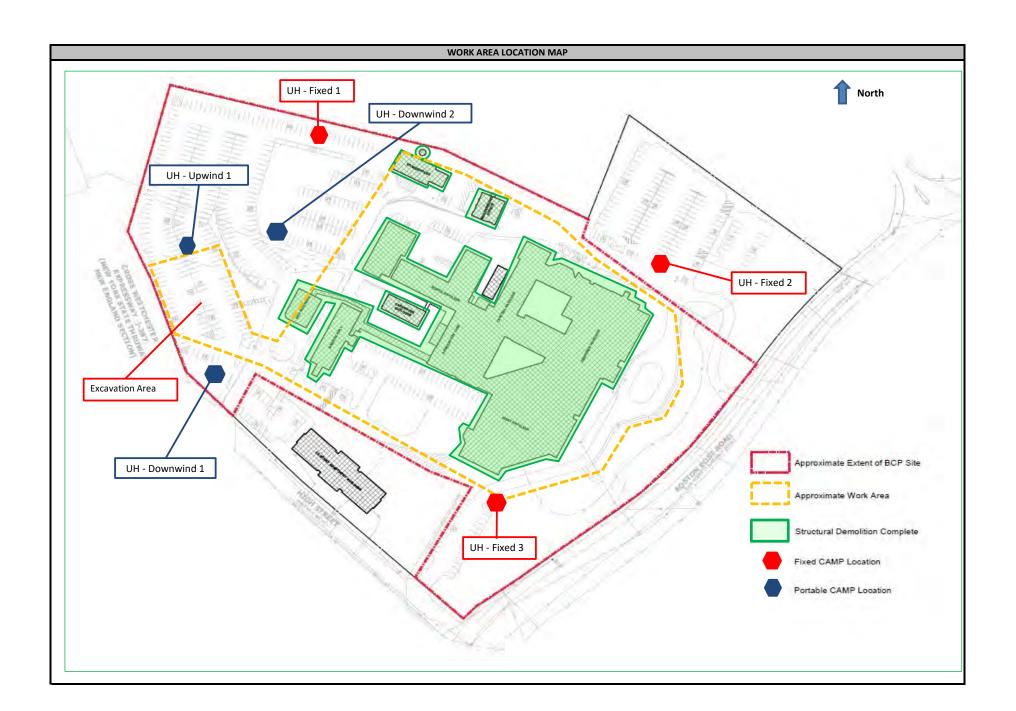


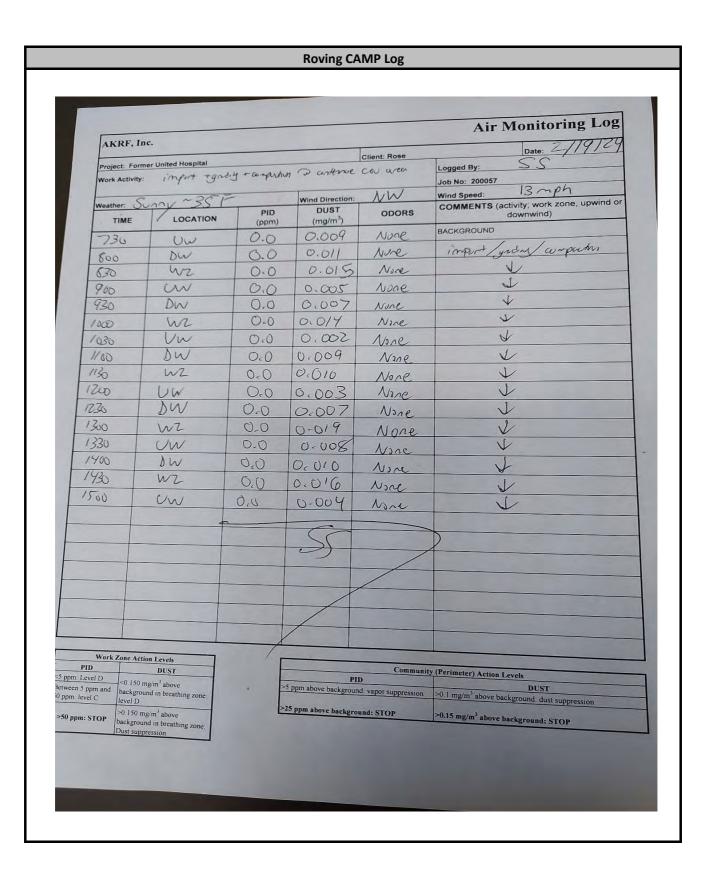


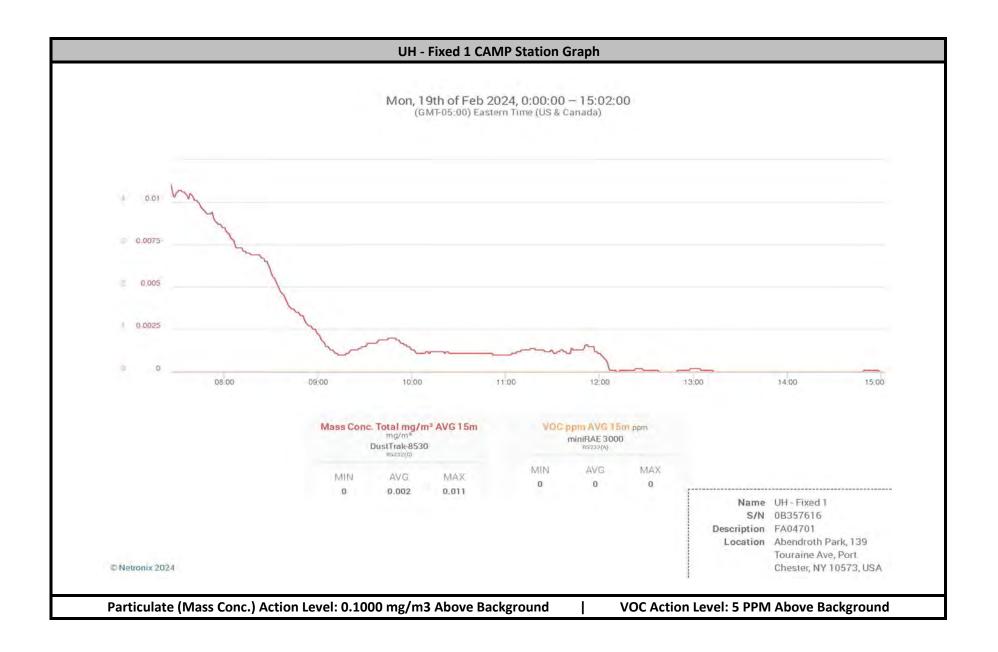


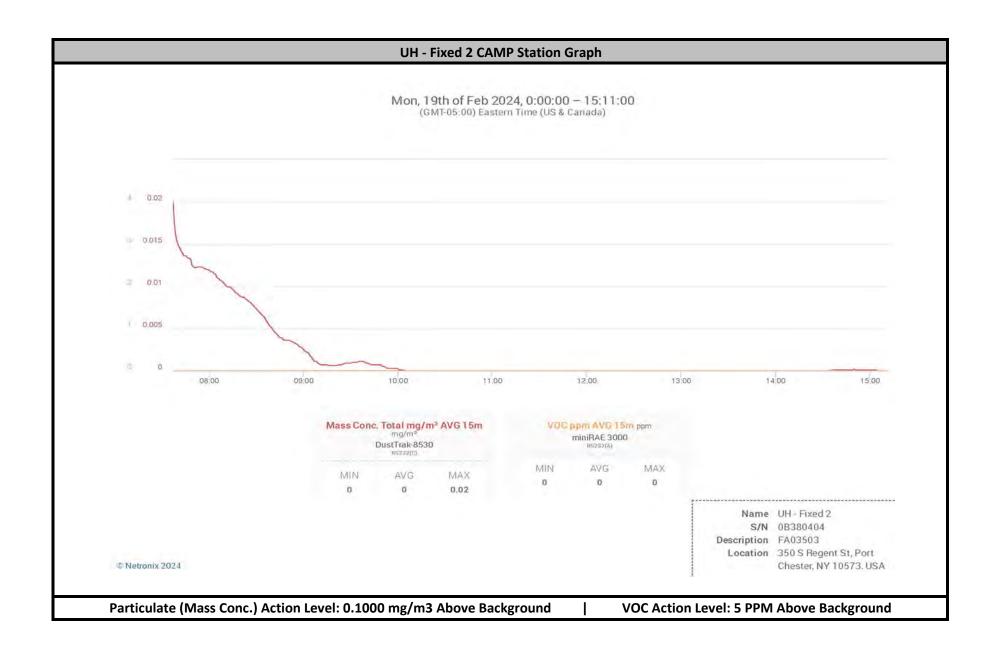

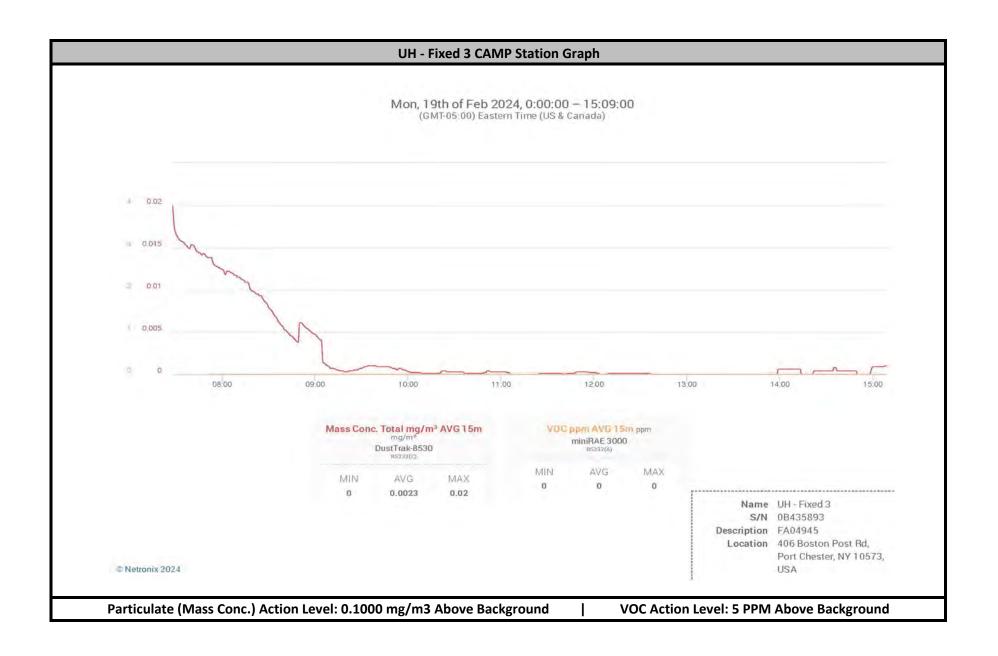

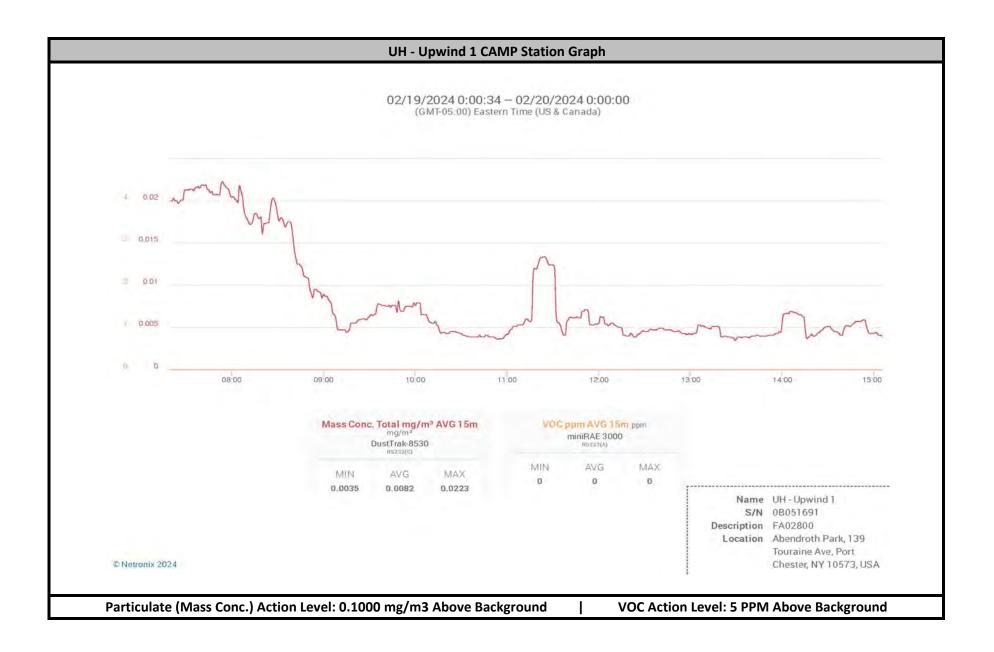

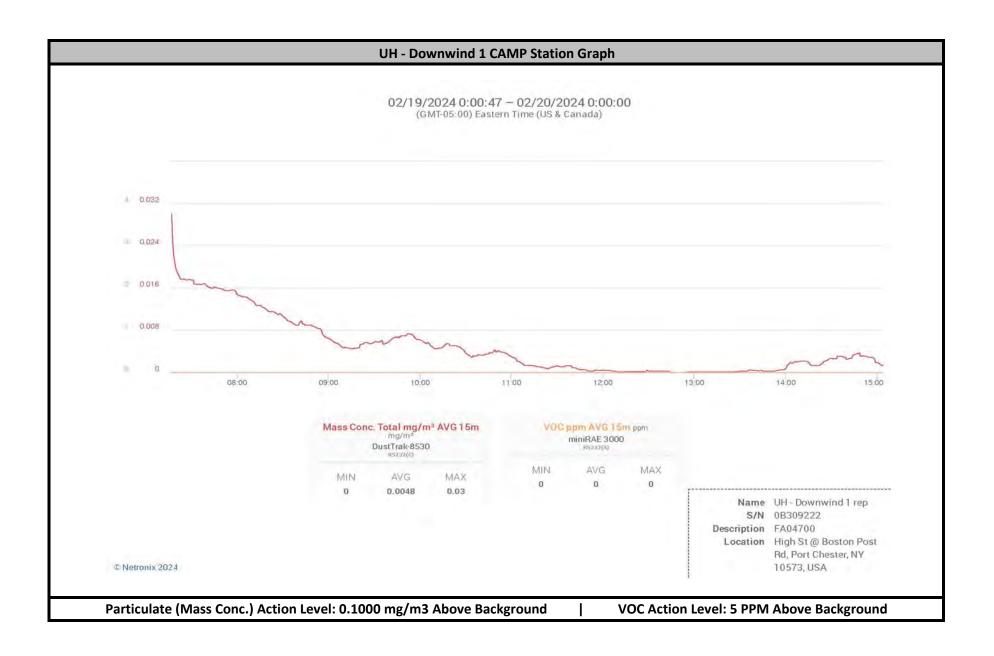

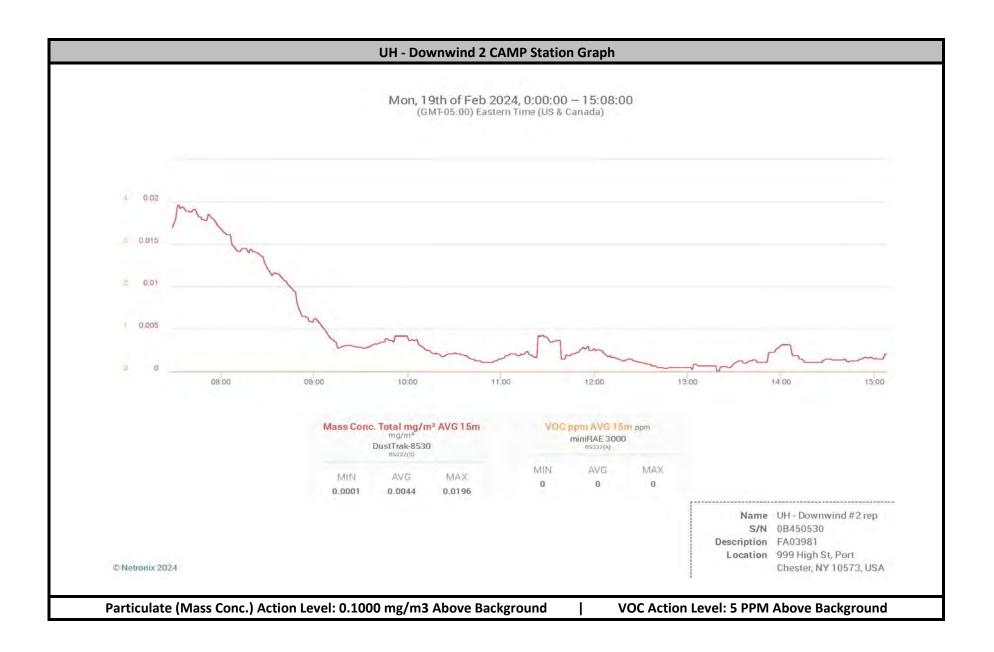

| → Λ Ι Δ | ZDE | | | ı | Daily Activi | | | |
|---|--|--|-----------------------|--------------------------|----------------------------|--|---|---|
| PAK | KF | | | | Former Unite Port Ches | | | |
| | | | Conors | al Site Information | BCP No. C | 360202 | | |
| Date: Weather: | | | Genera | ii Site information | Tuesday, Febru Sunny, 2 | | | |
| Wind Direction/Speed AKRF Personnel on Si | | | | | NW @ 6 Michael | | | |
| AKRF Equipment on S | | 3 Fixed CAN | MP Stations (PID & Du | ıst Monitor), 3 Porta | | | , One Handheld PID, | One Handheld Dust Monitor |
| Visitors: | | | Contra | actor Information | Non | e | | |
| | Contracting Company | | Key Per | | | | Equipm | ent |
| (| Tony Casale Inc. Excavation Contractor) | | Rigo | Diaz | | | rious excavation and cavators, compactors | grading equipment s, roller-compactor, etc.) |
| | Capital Industries Corp. Demolition Contractor) | | Joe Cia | nciulli | | (e.g. ex | Various demolitio | on equipment roll off containers, etc.) |
| , | | | | | | (0.87 | | , |
| The everyation center | actor conducted general grading, compaction | | escription and Locat | | | | | |
| | actor conducted general grading, compacted | | | | (COO) area. | | | |
| | | | Site Soil Dispo | osal Tracking Informa | ation | | | |
| Destination Facility | | Daily Trucks | | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic Yards |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 |
| | | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 |
| | | | Imported Fi | II Tracking Informati | on | | | |
| | Origin Facility | Daily | Trucks | Daily Approx | . Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards |
| Tilcon West Nyack Quarry - West Nyack, NY (ITEM #4) | | 17 | | 375 | | 89 | | 2,110 |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 0 | | 0 | | 2 | | 45 |
| | | Daily Import (CY) | | 375 | | Total Import (CY) | | 2,155 |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed |
| VOC Action Level Exc | eedance(s) Above Background: | No | No | No | No | No | No | No |
| Particulate Action Lev | rel Exceedance(s) Above Background: | No | No | No | No | No | No | No |
| | T | | Additi | onal Information | | | | |
| Planned Work Activity for Following Day(s): | The demolition contractor will continue so The excavation contratcor will continue to | | | | _ | | | yer. |
| Comments: | Negative particulate concentrations were station was fully operational by 13:43. No negative particulate concentrations. Negative particulate concentrations were station was fully operational by 13:26. No negative particulate concentrations. | elevated levels of par reported at the UH - | ticulates were detec | ted with nearby CAN | IP or roving equipm | ent during the perio ue to equipment ma | d that the UH - Fixed Ilfunction; the dust m | 2 CAMP station was reporting nonitor was recalibrated and the |

1 of 80 C360202_Daily Report_2024.02.20

Photograph 1 -Excavation contractor conducting general grading within the antennae COU area, view facing southwest. Photograph 2 -Excavation contractor importing Item #4 for use within the antennae





COU area, view facing west.





Photograph 3 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north.




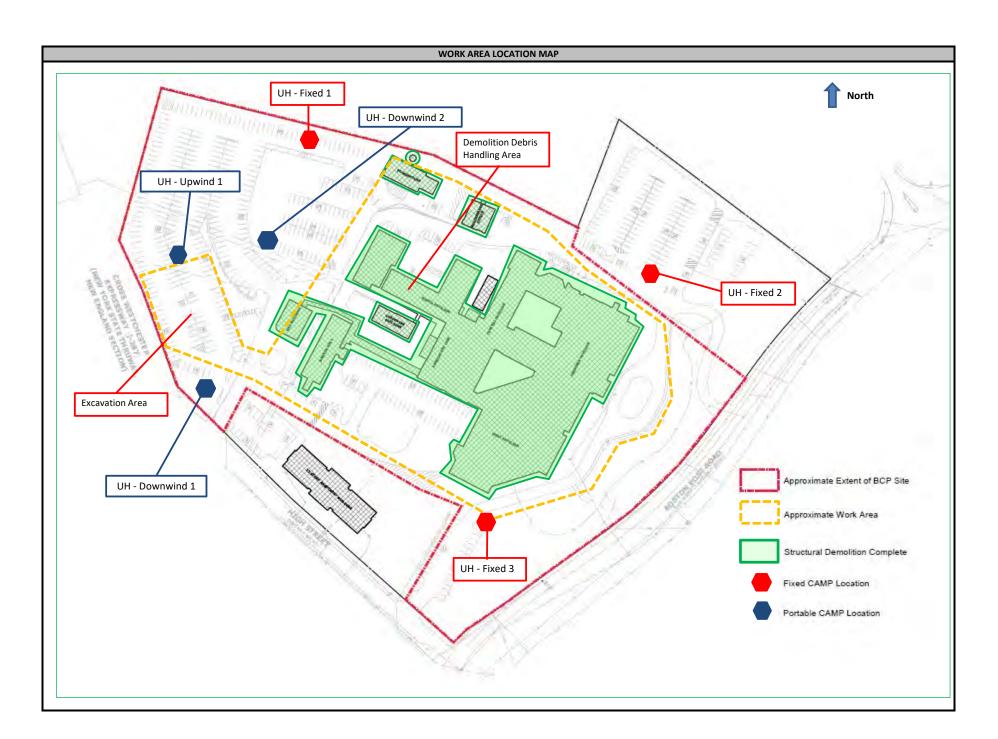


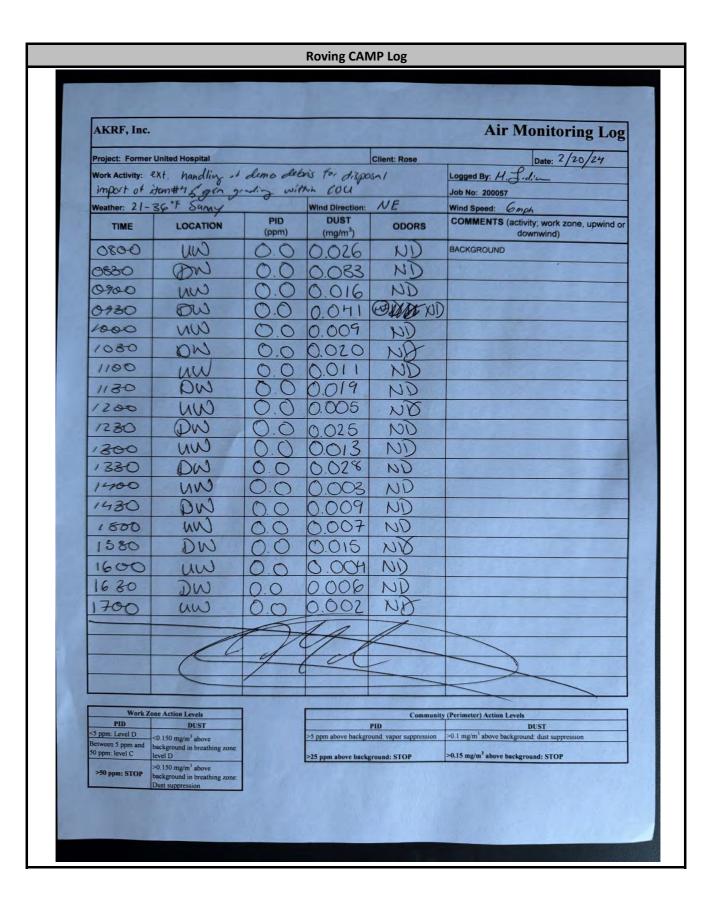


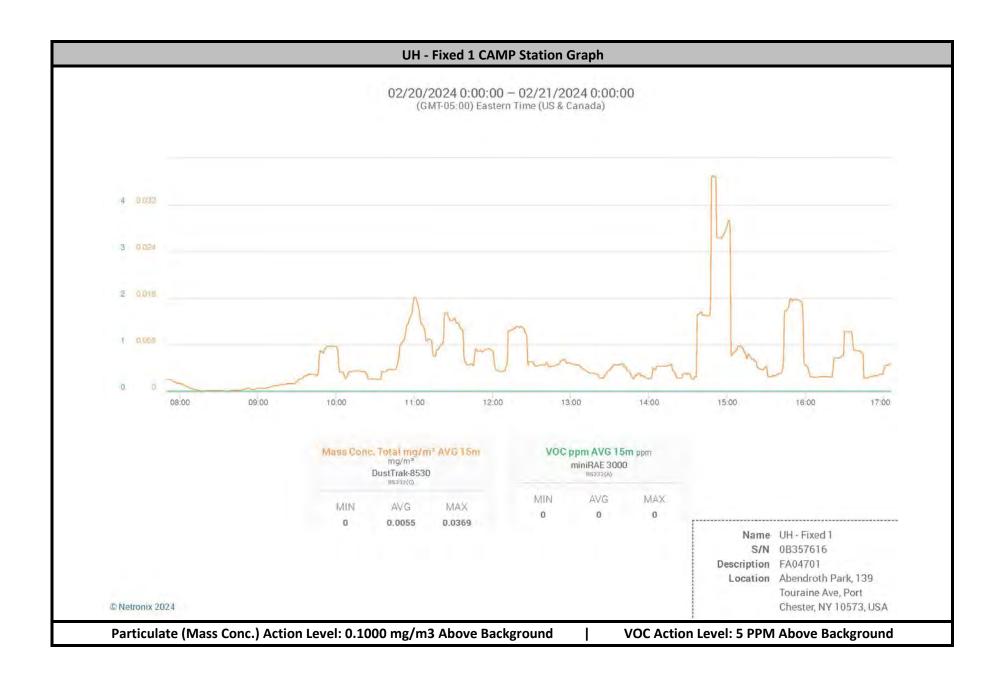


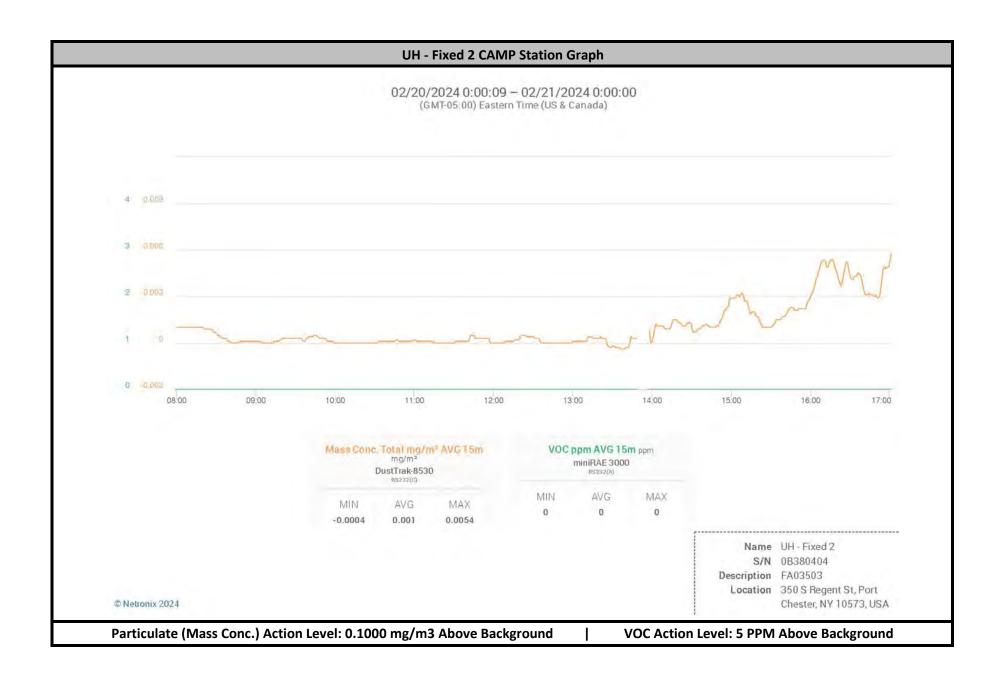

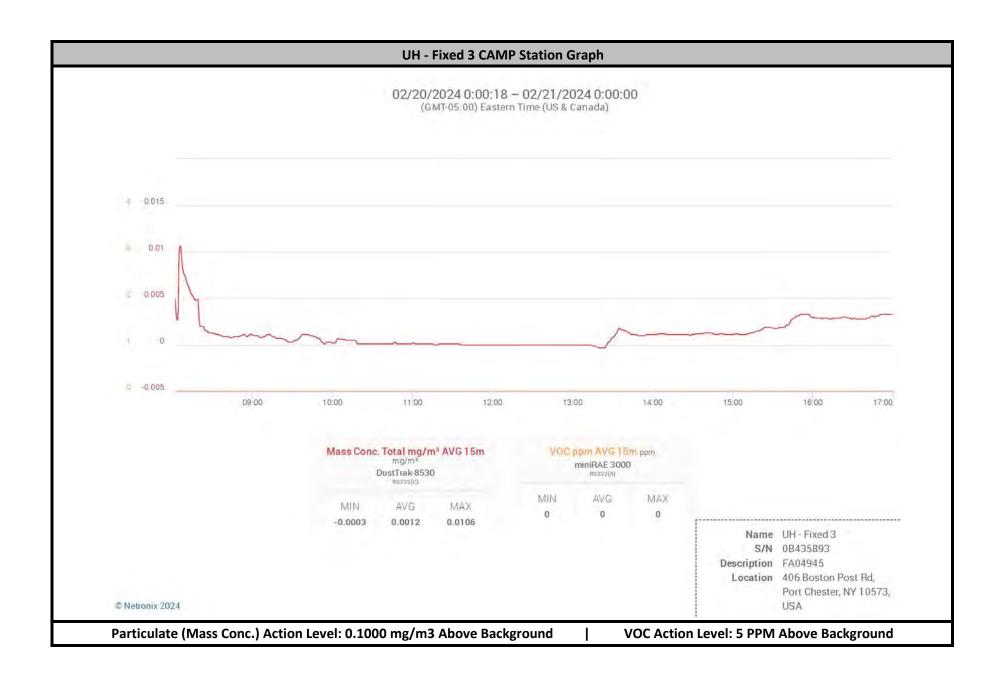

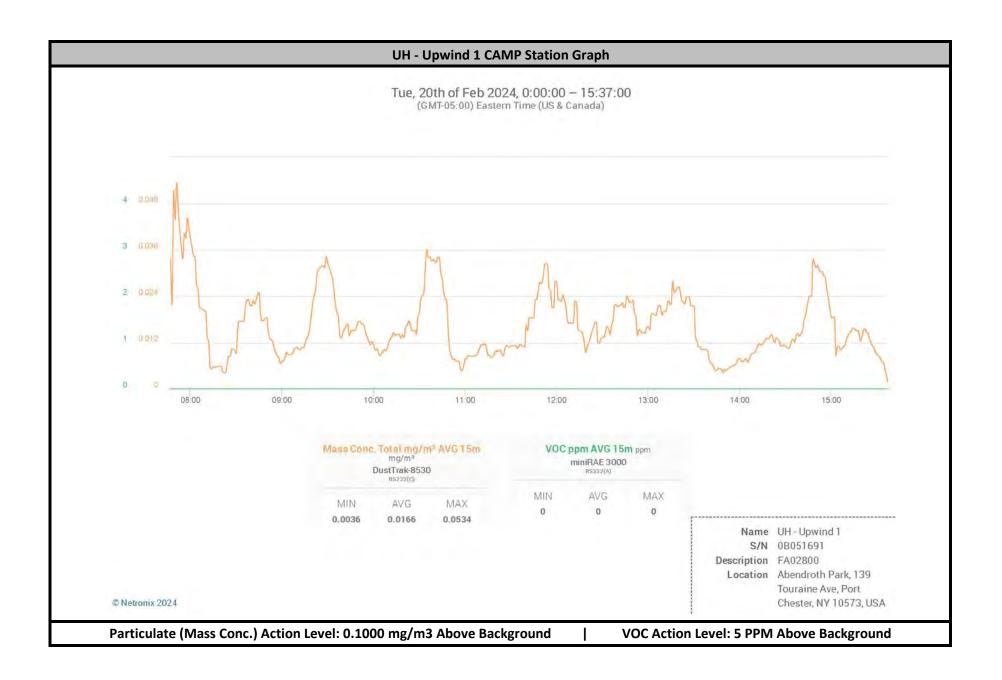

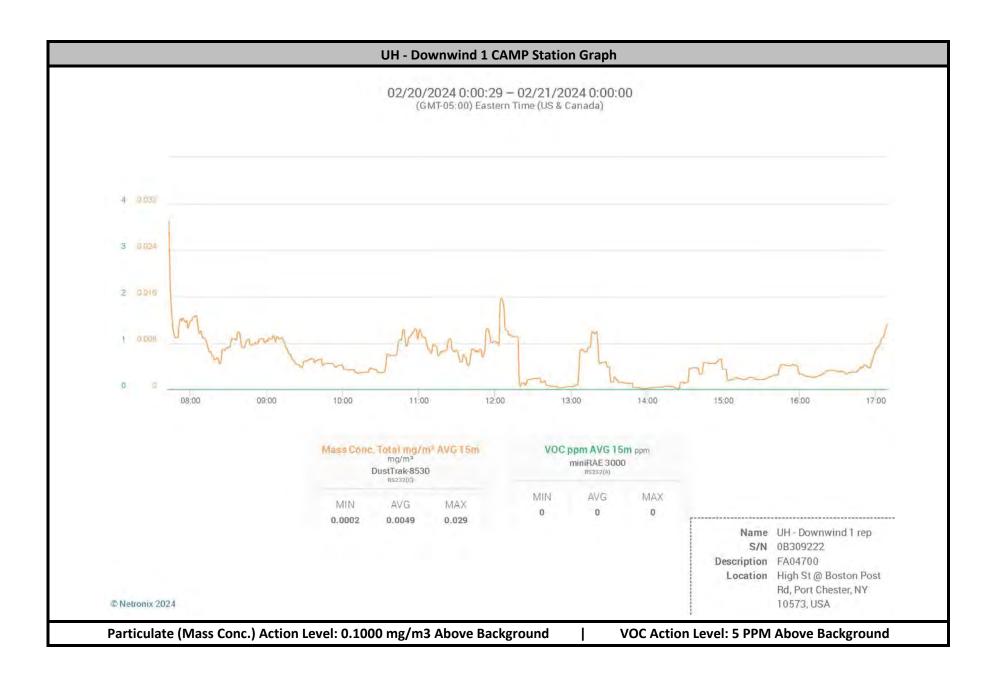

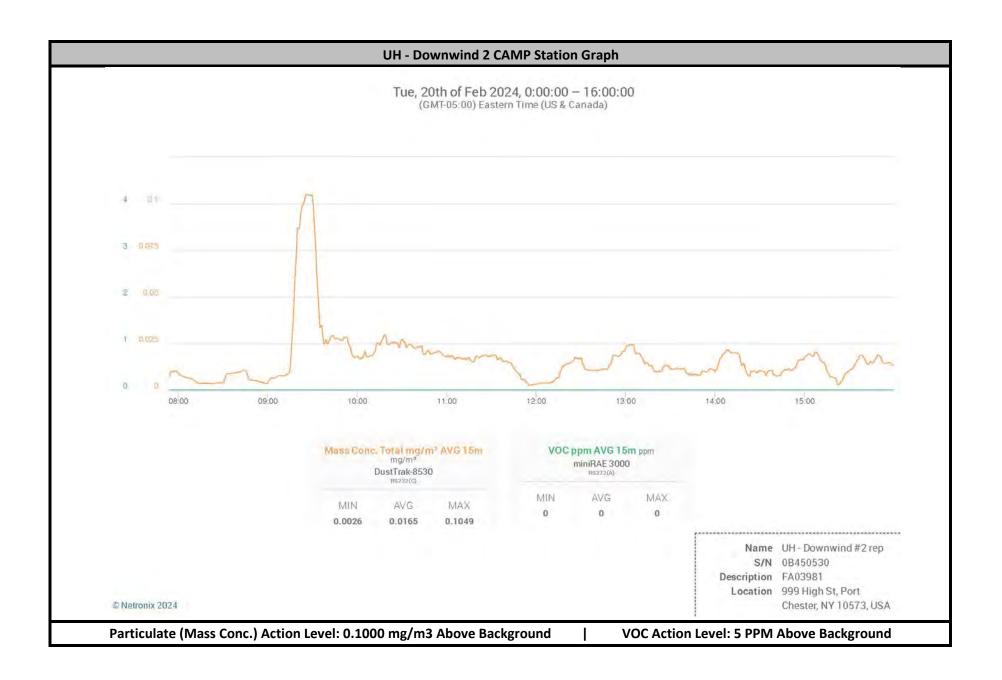

| | | | | | Daily Activi | ty Report | | |
|---|---|------------------------|-------------------------|--------------------------|----------------------------|------------------------|--|--|
| OAK | (RF | | | | Former Unite | d Hospital | | |
| | MT. | | | | Port Ches BCP No. C | | | |
| Date: | | l l | Genera | al Site Information | Wednesday, Feb | ruary 21 2024 | | |
| Weather: | | | | | Partly Cloudy | ,~25-39°F | | |
| Wind Direction/Speed AKRF Personnel on Sit | | | | | NE @ 4-9 Marco B | | | |
| AKRF Equipment on S Visitors: | ite: | 3 Fixed CAN | MP Stations (PID & Du | ust Monitor), 3 Porta | ble CAMP Stations (Non | | , One Handheld PID, | One Handheld Dust Monitor |
| | | | | actor Information | 14011 | | | |
| - | Contracting Company Tony Casale Inc. | | Key Pe | | | Va | rious excavation and | |
| (1 | Excavation Contractor) | | Rigo | Diaz | | | | s, roller-compactor, etc.) |
| | Capital Industries Corp. Demolition Contractor) | | Joe Cia | nciulli | | (e.g., ex | Various demolitic cavators, skid steers | on equipment , roll off containers, etc.) |
| | | D | escription and Locat | ion of Work Activitie | es Performed | | | |
| The excavation contra | actor imported nine (9) loads of Item #4 and | one (1) load of NY2, | /ASTM #5, and cond | ucted general gradin | g and compaction w | rithin the antennae (| Change of Use (COU) | area. |
| The demolition contra | actor continued sorting and loading demolti | on debris into contai | iners for off-site disp | osal. | | | | |
| | | | Site Soil Dispo | osal Tracking Inform | ation | | | |
| | Destination Facility | Daily [·] | Trucks | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic Yards |
| Clean Earth of Cartere | et - Carteret, NJ | (| 0 | C |) | 3 | 37 | 710 |
| | | | Daily Export (CY) | (|) | | Total Export (CY) | 710 |
| | | | Imported Fi | II Tracking Informati | ion | | | |
| | Origin Facility | Daily ' | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards |
| Tilcon West Nyack Qu (ITEM #4) | arry - West Nyack, NY | 9 | 9 | 22 | 25 | g | 98 | 2,335 |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | | 1 | | 25 | | 3 | | 70 |
| | | | Daily Import (CY) | 25 | 50 | | Total Import (CY) | 2,405 |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed |
| VOC Action Level Exce | eedance(s) Above Background: | No | No | No | No | No | No | No |
| Particulate Action Lev | rel Exceedance(s) Above Background: | No | No | No | No | No | No | No |
| | | | Addit | ional Information | | | | |
| Planned Work | The demolition contractor will continue so | rting and loading of o | demolition debris fro | m the former hospit | al buildings into con | tainers for off-site d | isposal. | |
| Activity for Following Day(s): | The excavation contratcor will continue to | import Item #4 from | Tilcon West Nyack f | or use within the ant | ennae COU area as | structural backfill ab | ove a demarcation la | ıyer. |
| Comments: | Due to a telemetry issue, the UH - Fixed 3 (station was not reporting data. | CAMP station did not | report VOC data un | til 9:47. No elevated | levels of VOCs were | detected with nearb | oy CAMP or roving ed | juipment during the time that the |

1 of 68 C360202_Daily Report_2024.02.

Site Photographs

Photograph 1 Excavation contractor importing Item #4 for use within the antennae COU area, view facing west.




Photograph 2 -

Excavation
contractor
conducting general
grading and
compacting Item #4
within the antennae
COU area, view
facing southwest.





Photograph 3 Demolition contractor exporting C&D debris, view facing northeast.



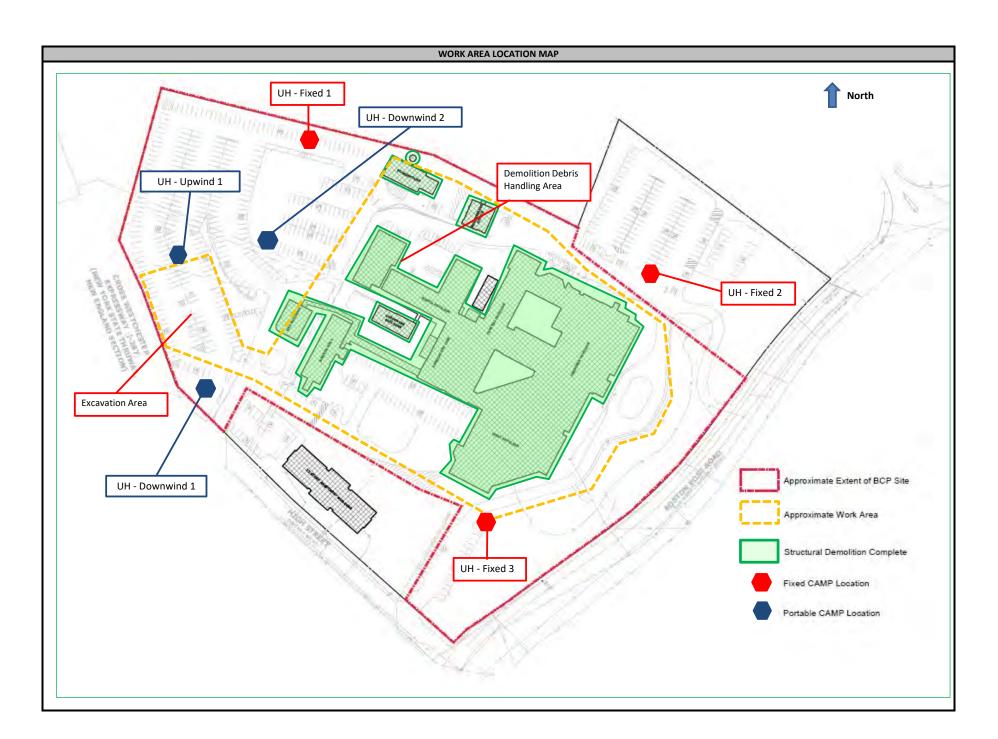



Roving CAMP Log Air Monitoring Log AKRF, Inc. Project: Former United Hospital Work Activity: + Importing of Client: Rose ITER 4 and NY#2 M. Boller Logged By: Job No: 200057 Weather: SVN 4 CLOUD (25-38/F Wind Direction: Wind Speed: PID DUST COMMENTS (activity, work zone, upwind or LOCATION TIME ODORS (ppm) (mg/m^3) downwind) NS BACKGROUND 11 NA 0.064 NA NO NO NA Community (Perimeter) Action Levels Work Zone Action Levels PID PID DUST >5 ppm above background: vapor suppression >0.1 mg/m³ above background: dust suppression <5 ppm: Level D <0.150 mg/m³ above background in breathing zone >0.15 mg/m³ above background: STOP >25 ppm above background: STOP 50 ppm: level C level D >0.150 mg/m³ above background in breathing zone >50 ppm: STOP Dust suppression

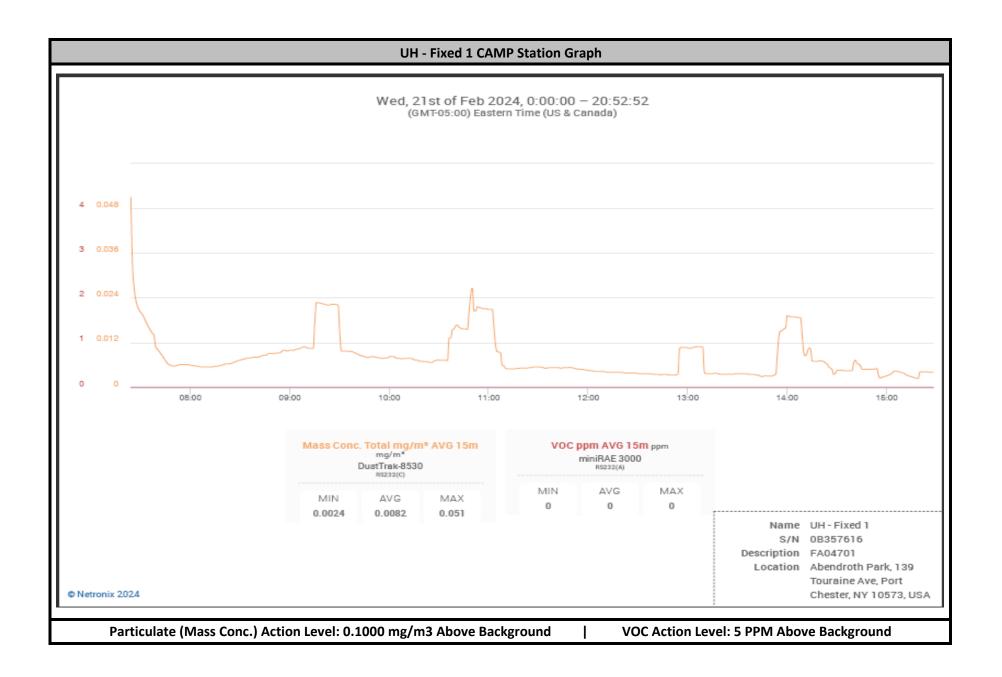


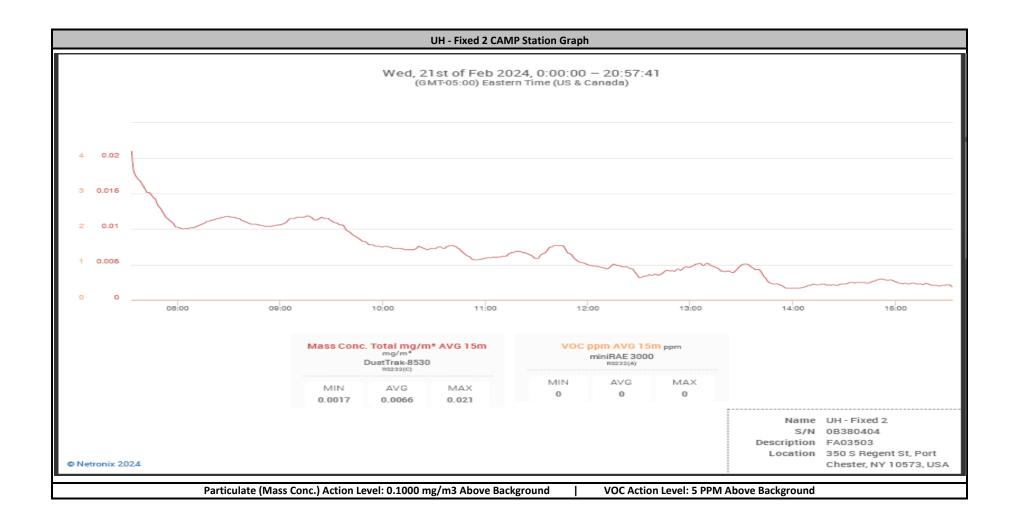


6 of 68

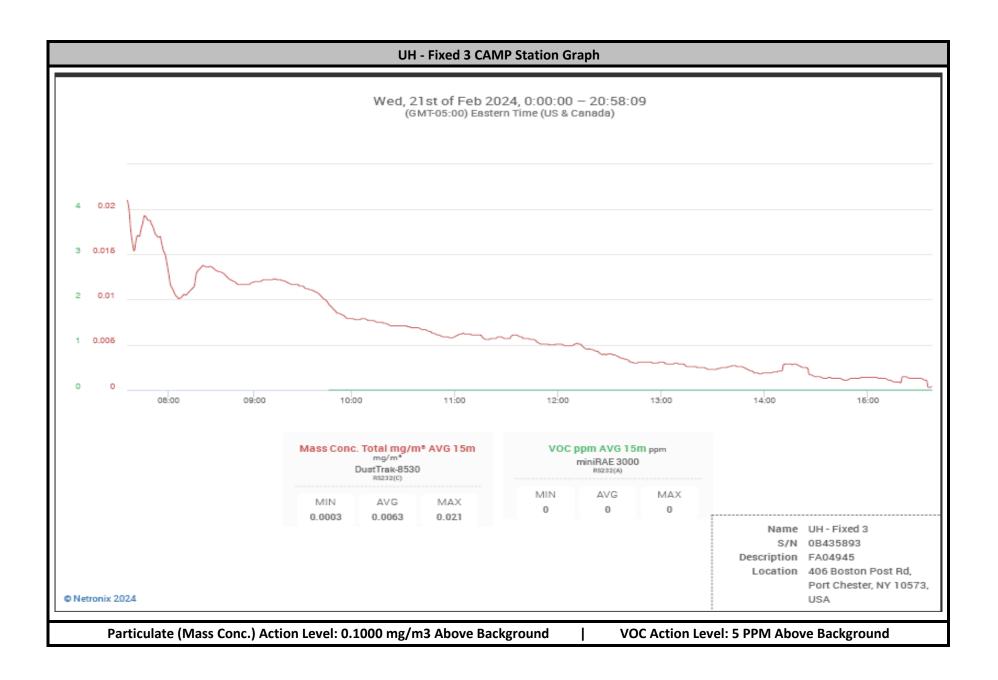

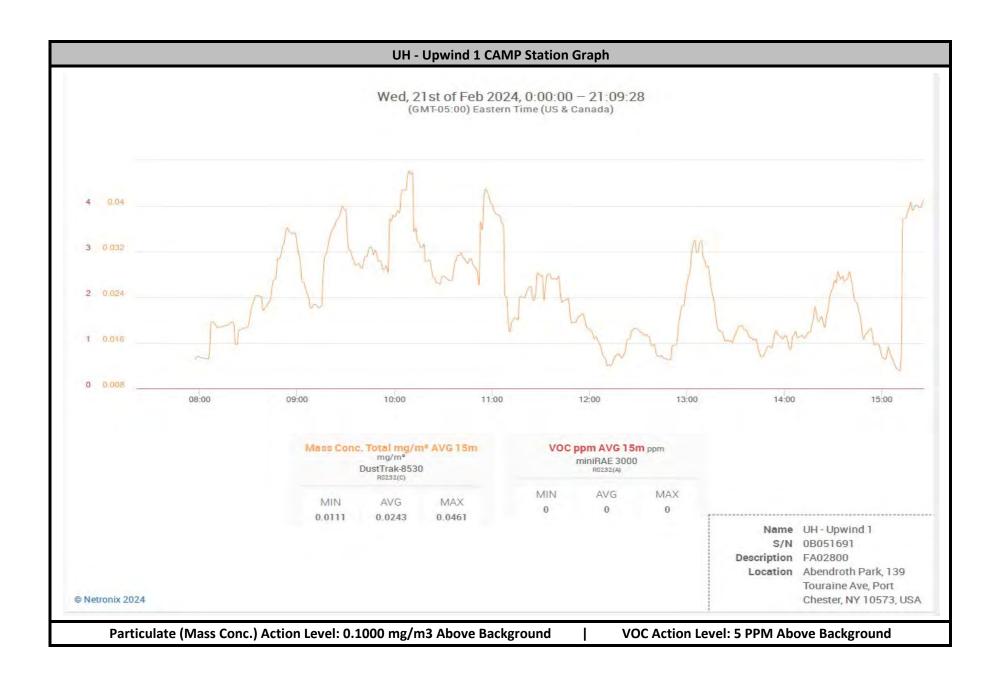

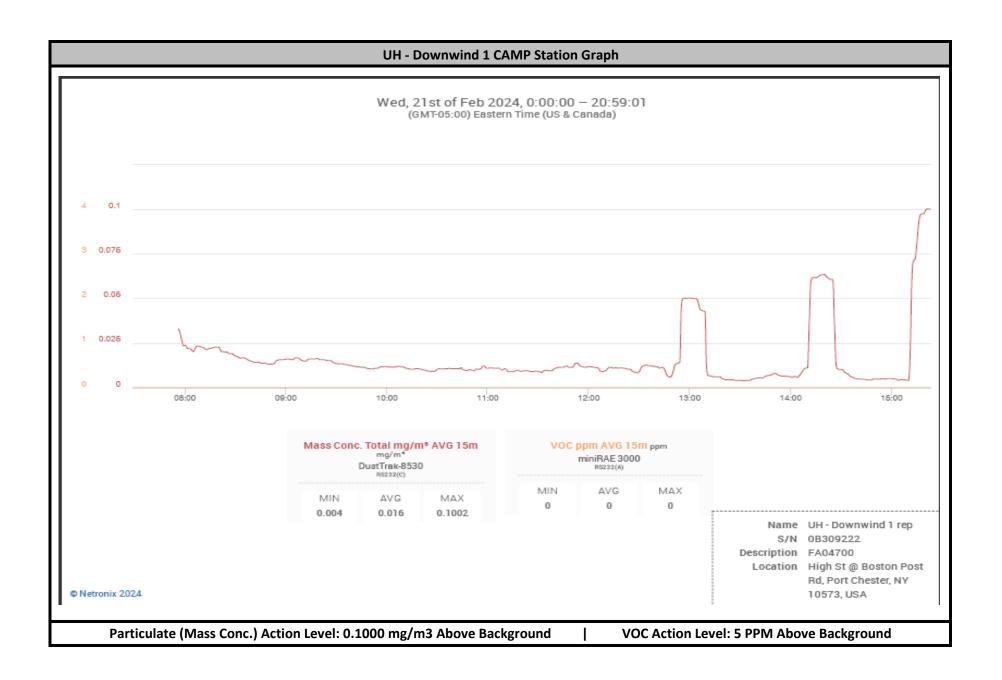

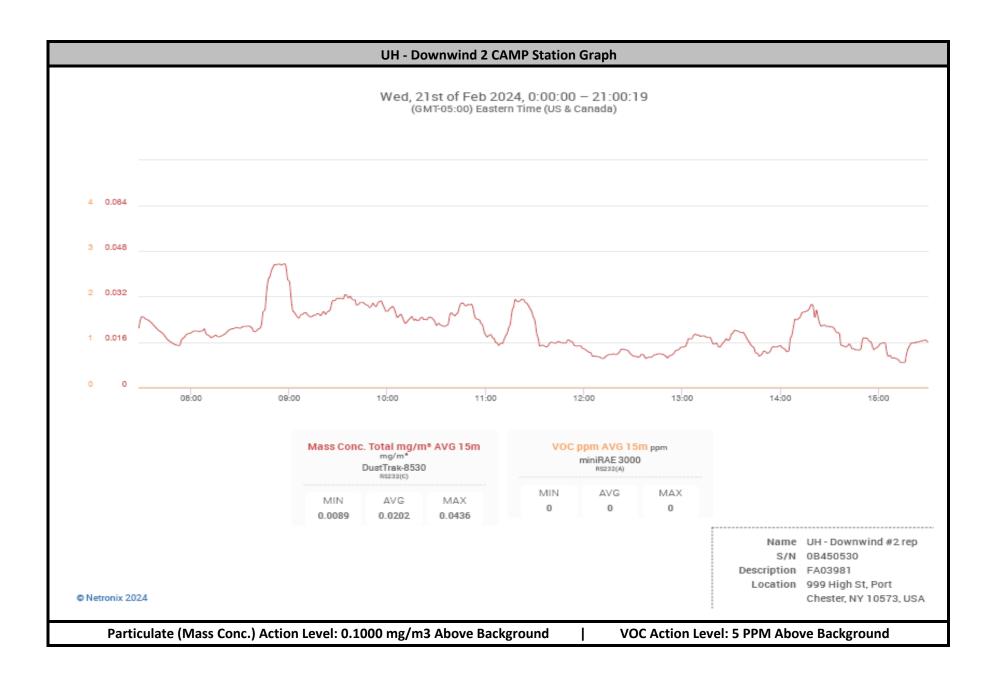

| | | | | | Daily Activi | ity Report | | | | |
|--|---|--|-------------------------|-----------------------|------------------------|--------------------|--|--|--|--|
| PAK | KF | | | | Former United Hospital | | | | | |
| | ALU. | Port Chester, NY BCP No. C360202 | | | | | | | | |
| Date: | | 1 | Genera | Site Information | Thursday, Febru | uary 22, 2024 | | | | |
| Veather: | | | | | Cloudy, ~3 | 34-45°F | | | | |
| /ind Direction/Speed KRF Personnel on Site | | | | | SE @ 3-9 Marco B | | | | | |
| KRF Equipment on Si | | 3 Fixed CAN | 1P Stations (PID & Du | ıst Monitor), 3 Porta | ble CAMP Stations (| PID & Dust Monitor | , One Handheld PID, | One Handheld Dust Monitor | | |
| sitors: | | | Contra | ctor Information | Non | e | | | | |
| (| Contracting Company | T | Key Pe | | | I | Equipm | nent | | |
| | Tony Casale Inc. | | Rigo | Diaz | | | rious excavation and | | | |
| • | Excavation Contractor) | | | | | (e.g., ex | rs, roller-compactor, etc.) | | | |
| | Capital Industries Corp. Demolition Contractor) | | Joe Cia | ınciulli | | (e.g., ex | Various demolitic cavators, skid steers | on equipment , roll off containers, etc.) | | |
| | | De | escription and Locati | ion of Work Activitie | es Performed | | | | | |
| e excavation contra | ctor imported fourteen (14) loads of Item | | | | | f Use (COU) area. | | | | |
| ne demolition contra | ctor continued sorting and loading demo | ltion debris into contai | ners for off-site dispo | osal. | | | | | | |
| | | | Site Soil Dispo | sal Tracking Informa | ation | | | | | |
| | Destination Facility | Daily | Trucks | Daily Approx | k. Cubic Yds. | Total Si | ite Loads | Total Approximate Cubic Yard | | |
| ean Earth of Cartere | t - Carteret, NJ | |) | (|) | ; | 37 | 710 | | |
| | | | Daily Export (CY) | (|) | | Total Export (CY) | 710 | | |
| | | | Innomed Si | II Tuakina Infaumati | | | | | | |
| | | 1 | | Il Tracking Informati | | Г | | | | |
| | Origin Facility | Daily | Trucks | Daily Approx | k. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yard | | |
| lcon West Nyack Qua FEM #4) | arry - West Nyack, NY | 1 | 4 | 22 | 25 | 1 | 12 | 2,560 | | |
| lcon West Nyack Qua IY2/ASTM #5 - 3/4" S | arry - West Nyack, NY Stone) | (| ס | C |) | | 3 | 70 | | |
| | | | Daily Import (CY) | 22 | 25 | | Total Import (CY) | 2,630 | | |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| dors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| OC Action Level Exce | edance(s) Above Background: | No | No | No | No | No | No | No | | |
| rticulate Action Leve | el Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| | | | Δdditi | onal Information | | | | | | |
| Discondition | The describes and a second second | and the second s | | | al building 1.1 | | | | | |
| Planned Work ctivity for Following Day(s): | The demolition contractor will continue The excavation contratcor will continue | | | | _ | | • | ayer. | | |
| Comments: | Due to battery issues; the UH - Fixed 1 CAMP station did not report particulate data after 13:20, the UH - Upwind 1 station did not report data after 11:04, the UH - Downwind 1 and UH - Downwin stations did not report data past 14:22 and 14:11, respectively. No elevated levels of particulates or VOCs were detected with nearby CAMP or roving equipment during the time that the stations w not reporting data. The equipment vendor is actively troubleshooting the battery issues and will send replacement batteries if the problem persists. | | | | | | | | | |

1 of 57 C360202_Daily Report_2024.02.22

Site Photographs

Photograph 1 -

Excavation contractor importing Item #4 for use within the antennae COU area, view facing southeast.



Photograph 2 -


Excavation contractor conducting general grading and compaction of Item #4 within the antennae COU area, view facing northwest.




Photograph 3 -


Demolition contractor exporting C&D debris, view facing northeast.




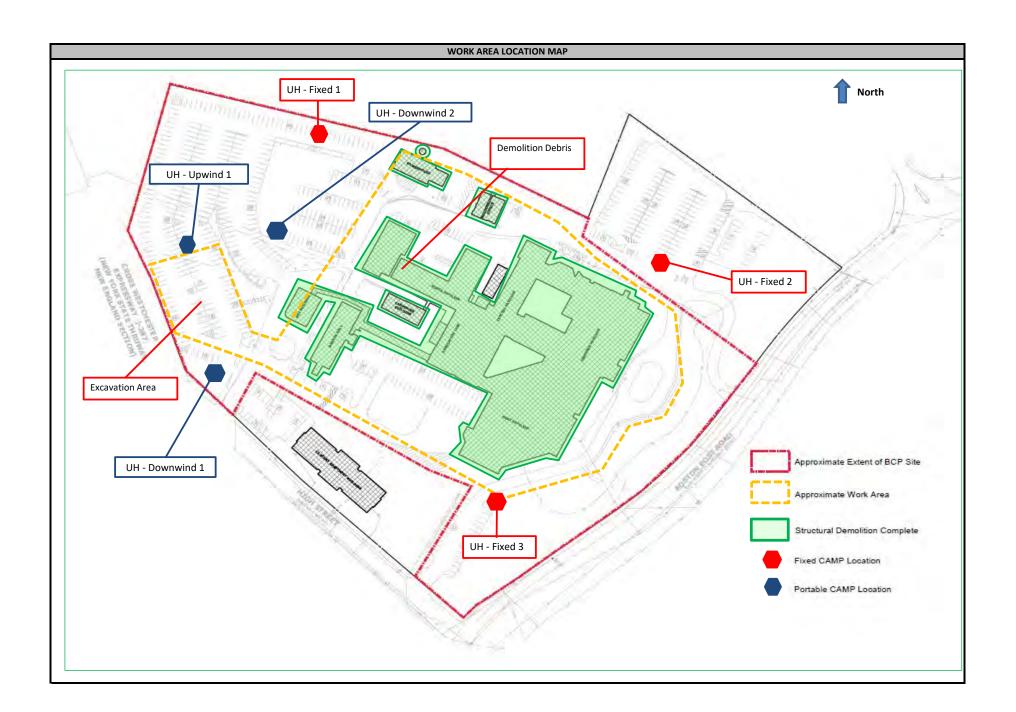



| | | | ROVING CA | AMP Log | | | |
|-------------------------|---|--------------|---|---------------------------|--|--|--|
| | , i | | 1 | | * - 0 | | |
| AKRF, Inc | | | | | Air Monitoring Log | | |
| Project: Form | er United Hospital | | | Client: Rose | Date: 0411/2014 | | |
| Work Activity: | | ITEM | | | Logged By: M. Dollo Ad | | |
| + Dognas | de Jemania | 10x 4 P | emoletion | 1 00 | Job No: 200057 | | |
| Weather: () | LOCATION 14-47 | PID (ppm) | Wind Direction: DUST (mg/m³) | ODORS | Wind Speed: (5-7) m/c COMMENTS (activity; work zone, upwind or downwind) | | |
| 730 | PF DAL Pale | 0.0 | 2.028 | LOVE | BACKGROUND | | |
| 800 | Prine | 02 | 0-247 | ((| Stores mys Ding Demolloy | | |
| B30 | Swindle Volan | 0.7 | 0-033 | (1 | 1 1 1 | | |
| PSO | Collete | 0.0 | 8.027 | 4 | 0 0 | | |
| 830 | & Sati | 0.0 | 0-040 | (1 | 11 11 | | |
| 1000 | Many | 0.0 | 0.257 | 11 | 11 11 | | |
| 1030 | White Name | 0.0 | 004 | 1 | 11 11 | | |
| 1100 | Silan latta | 20 | 0.063 | 11 | 11 11 | | |
| 1130 | SEdlife | 0,0 | 0.040 | 11 | (1) | | |
| 1200 | hours | 0.5 | 0.053 | 11 | <i>(</i> | | |
| 1230 | Nuglik | 0.0 | 0.047 | 11 | 11 11 | | |
| 1300 | il dition is | 00 | 0.763 | 11 | (1) | | |
| 1330 | salle Vha | 0.0 | 0.054 | 11 | 6 11 | | |
| 1450 | Winy | 0.0 | 0 0 63 | ((| ((() | | |
| 1430 | Stalke | 0-0 | 0.059 | (/ | 4 11 | | |
| 1500 | Cowne | 0.0 | 0.066 | 1, | 16 11 | | |
| 1530 | SELPLIE | 0.0 | 0-057 | 11 | Oschround | | |
| _ | 0 | | | | | | |
| | | | | 10 0 | 1/22/2024 | | |
| | | | 1 | 5 | 109001 | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| 260.00 | | | | | | | |
| PID | Zone Action Levels DUST | | | Commun | ity (Perimeter) Action Levels DUST | | |
| S ppm: Level D | | | >5 ppm above back | ground: vapor suppression | >0.1 mg/m³ above background: dust suppression | | |
| 50 ppm: level C level D | | | >25 ppm above background: STOP >0.15 mg/m³ above background: STOP | | | | |
| >50 ppm: STOP | >0.150 mg/m³ above background in breathing zone: Dust suppression | | | | | | |

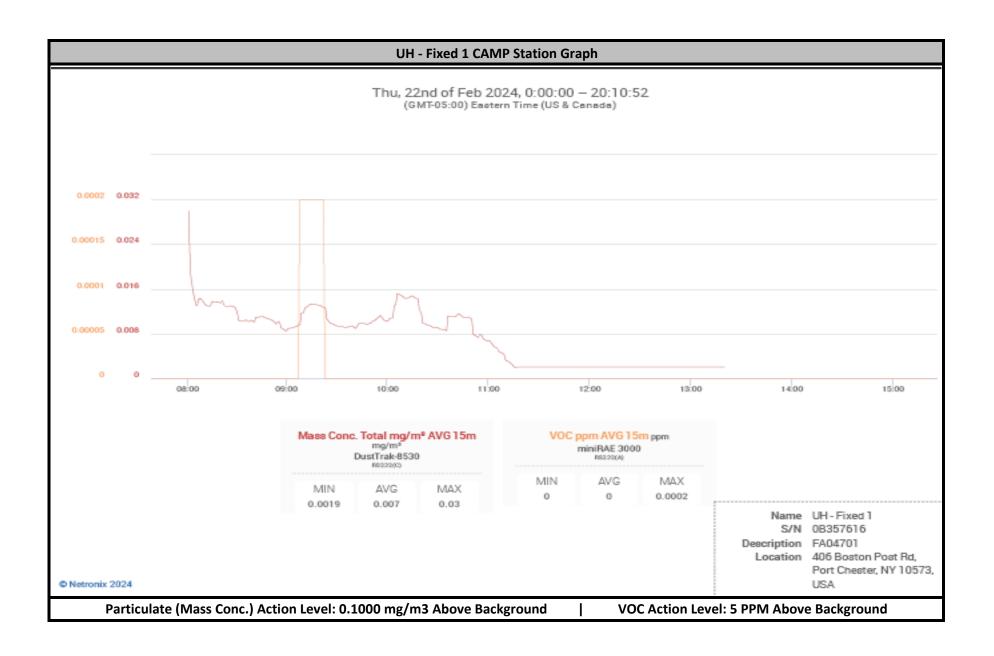


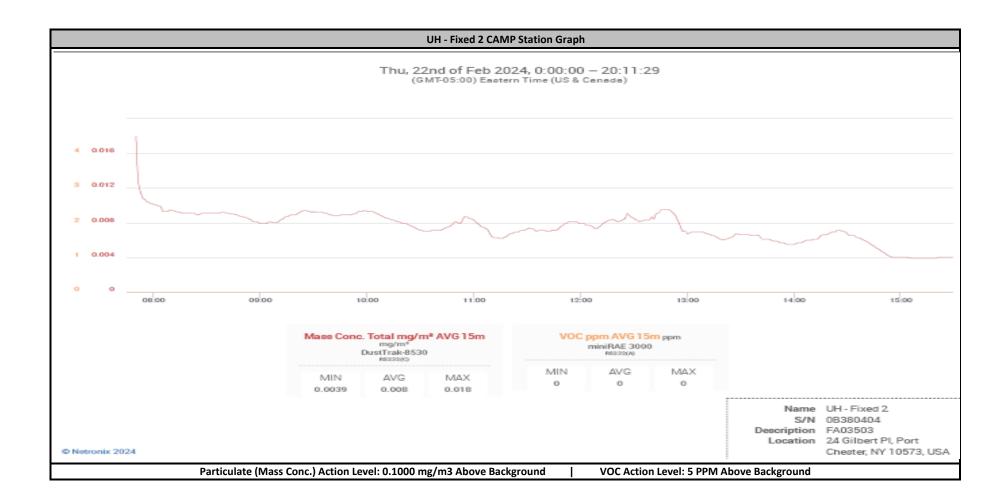

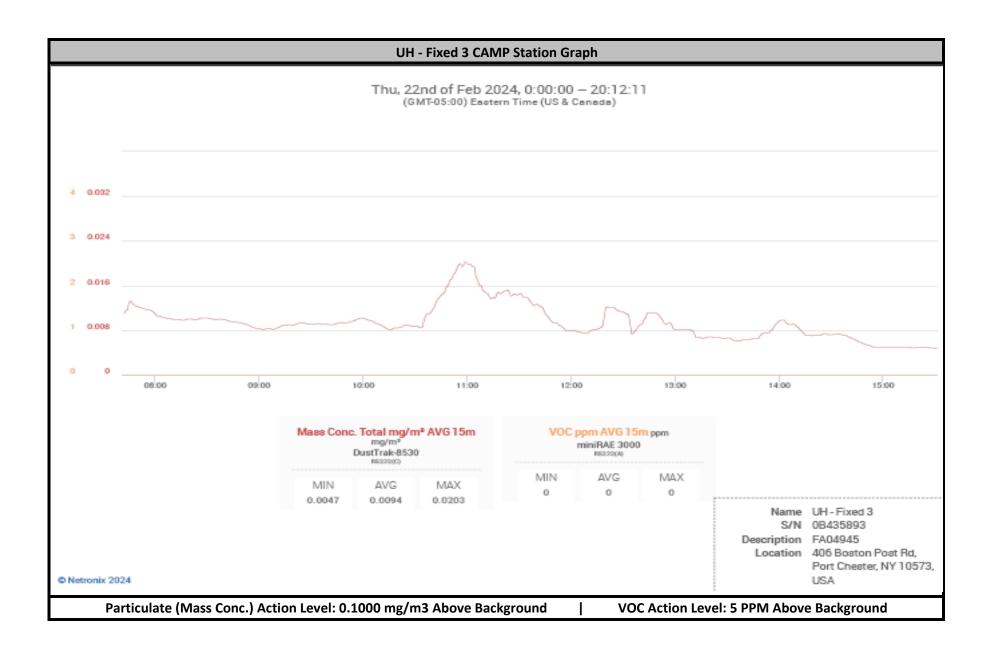

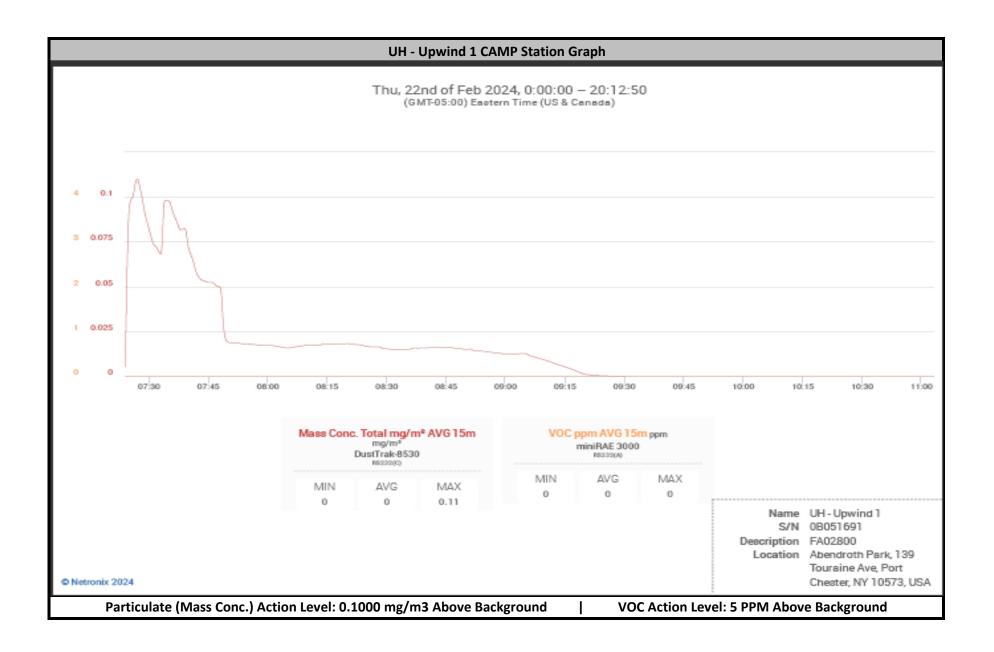

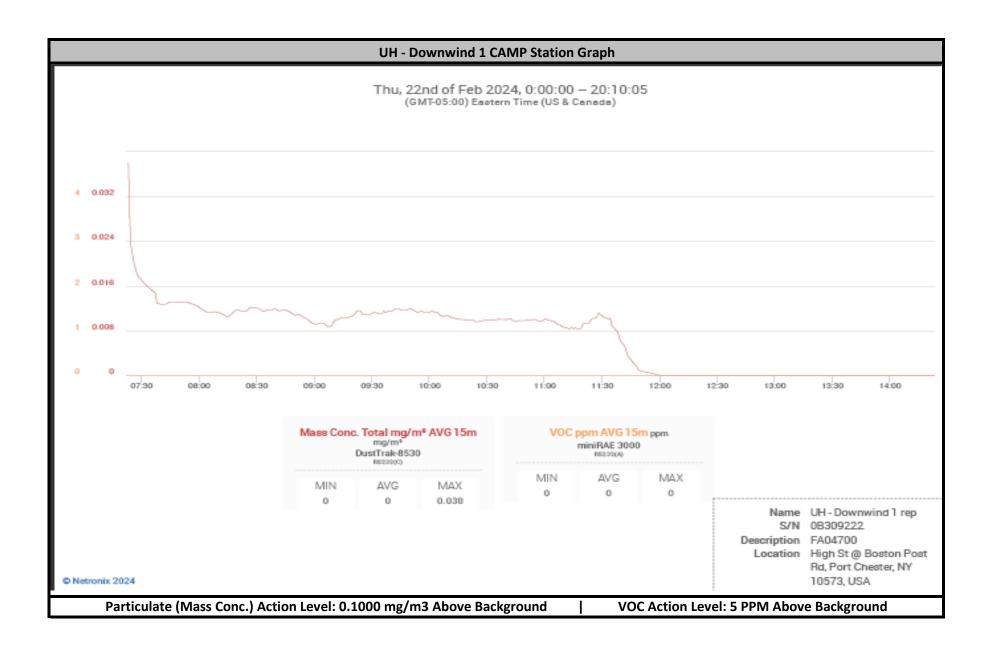

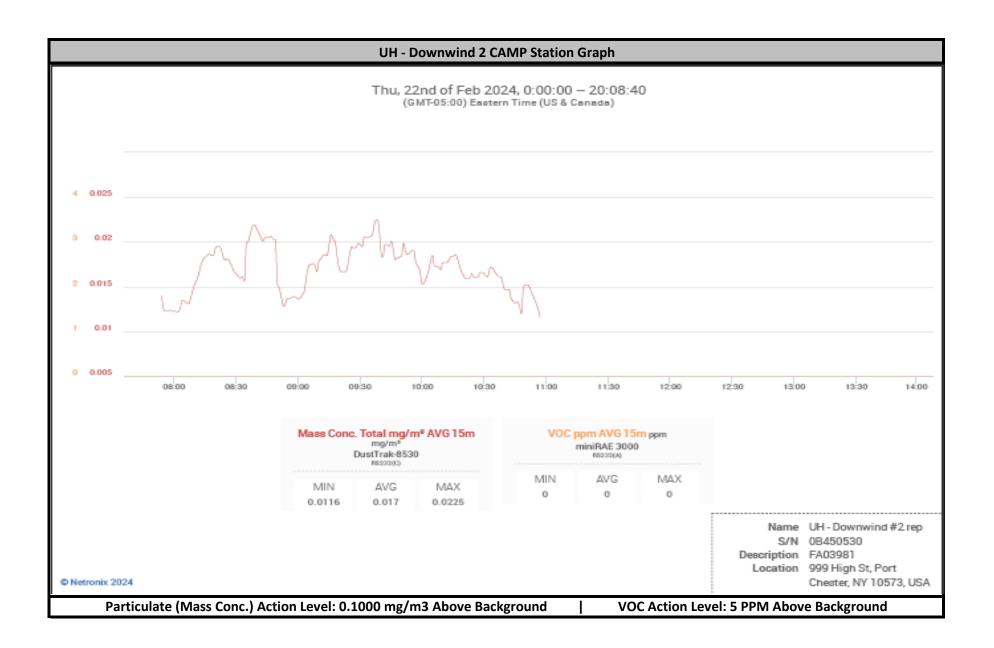

| | Z DE | Daily Activity Report | | | | | | | | |
|--|---|---|-----------------------------|--------------------------|-----------------------------|------------------------|--|---|--|--|
| OAK | KI | Former United Hospital Port Chester, NY BCP No. C360202 | | | | | | | | |
| | | | Genera | al Site Information | | | | | | |
| Date: Weather: | | | | | Friday, Februa Foggy, 37 | 7-47°F | | | | |
| Wind Direction/Spee AKRF Personnel on Si | | | West @ 4 mph Michael lodice | | | | | | | |
| AKRF Equipment on S | | 3 Fixe | ed CAMP Stations (PID | & Dust Monitor), 3 Por | table CAMP Stations (| PID & Dust Monitor), C | one Handheld PID, One | Handheld Dust Monitor | | |
| /isitors: | | | Contra | actor Information | Non | e | | | | |
| | Contracting Company | | Key Pe | rsonnel | | | Equipm | | | |
| (| Tony Casale Inc. Excavation Contractor) | | Rigo | Diaz | | | rious excavation and cavators, compactor | grading equipment s, roller-compactor, etc.) | | |
| | Capital Industries Corp. Demolition Contractor) | | Joe Cia | anciulli | | (e.g., ex | on equipment , roll off containers, etc.) | | | |
| | | D | escription and Locat | ion of Work Activition | es Performed | | | | | |
| he excavation contra | actor imported fourteen (14) loads of Item | #4, and conducted ge | eneral grading and co | ompaction within the | antennae Change o | of Use (COU) area. | | | | |
| The electrical contrac | ctor installed two utility poles using a truck- | mounted auger drill, | no soil was generate | d during the utility p | ole installations. | | | | | |
| The demolition contr | actor continued sorting and loading demolt | tion debris into conta | iners for off-site disp | osal. | | | | | | |
| | | | Site Soil Dispo | osal Tracking Inform | ation | | | | | |
| | Destination Facility | Daily Trucks | | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic Yards | | |
| lean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | |
| | | | Daily Export (CY) | 0 | | Total Export (CY) | | 710 | | |
| | | | Imported Fi | ll Tracking Informat | ion | | | | | |
| | Origin Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yards | | |
| Tilcon West Nyack Qu (ITEM #4) | uarry - West Nyack, NY | 14 | | 350 | | 126 | | 3,035 | | |
| Tilcon West Nyack Qu (NY2/ASTM #5 - 3/4" | uarry - West Nyack, NY Stone) | 0 | | 0 | | 3 | | 70 | | |
| | | Daily Import (CY) | | 350 | | Total Import (CY) | | 3,105 | | |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| VOC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| Particulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| | | | Addit | ional Information | | | | | | |
| Planned Work Activity for Following Day(s): | tivity for Following | | | | | | | | | |
| Comments: | Due to CAMP battery issues, the UH - Upwind 1 CAMP station was unable to report to the online database until 11:30 when a replacement battery was installed in the station; the UH - Downdind 1 and UH - Downdind 2 CAMP stations did not report particulate and VOC data past 11:14 and 11:22, respectively. Replacement batteries for the UH - Downdind 1 and UH - Downdind 2 CAMP stations arrived onsite at the end of the work day. No elevated levels of VOCs or particulates were detected with nearby CAMP or roving equipment during the time that the stations were not reporting data. | | | | | | | | | |
| | The VOC data from the UH - Fixed 3 CAMP station did not report to the online database from the start of the work day until approximately 12:08 due to a faulty data communication cable; the cable was repaired and the station was fully operational by 12:12. No elevated levels of VOCs were detected with nearby CAMP equipment during the period that VOCs were not reported at the UH - Fixed CAMP station. | | | | | | | | | |

1 of 50 C360202_Daily Report_2024.02.23

Site Photographs

Photograph 1 -

Excavation contractor importing Item #4 for use within the antennae COU area, view facing southeast.



Photograph 2 -


Installation of a utility pole to provide future power to the antenna COU area, view facing southeast.





Photograph 3 -


Demolition contractor handling and sorting demolition debris for disposal, view facing northeast.




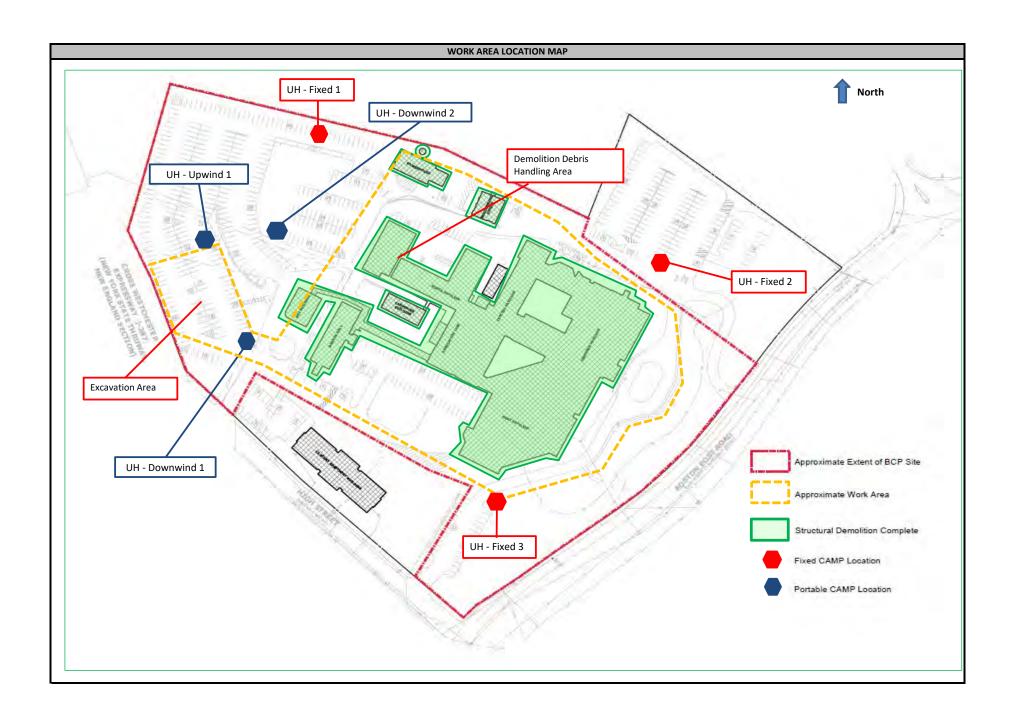


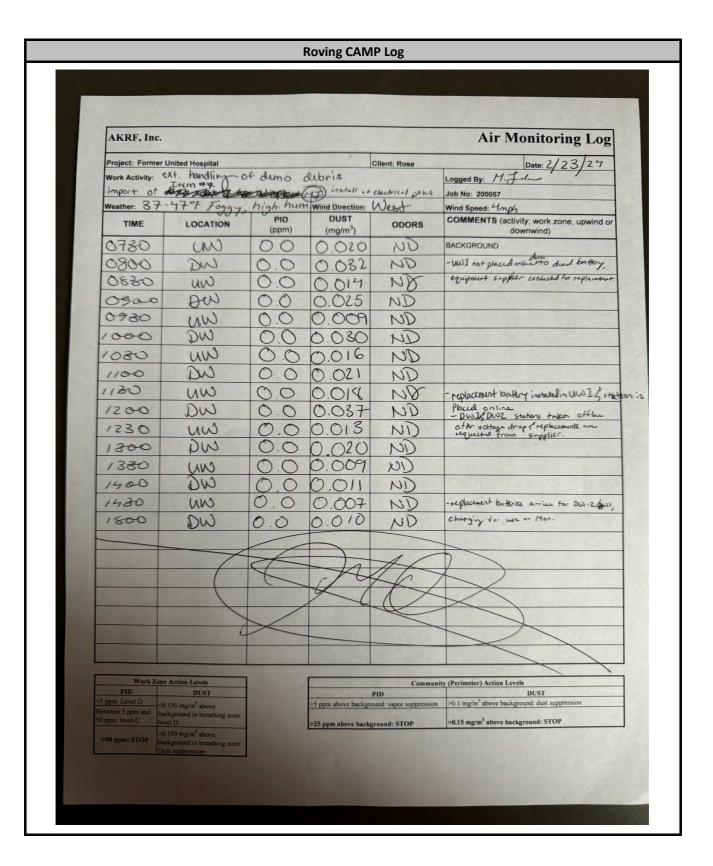


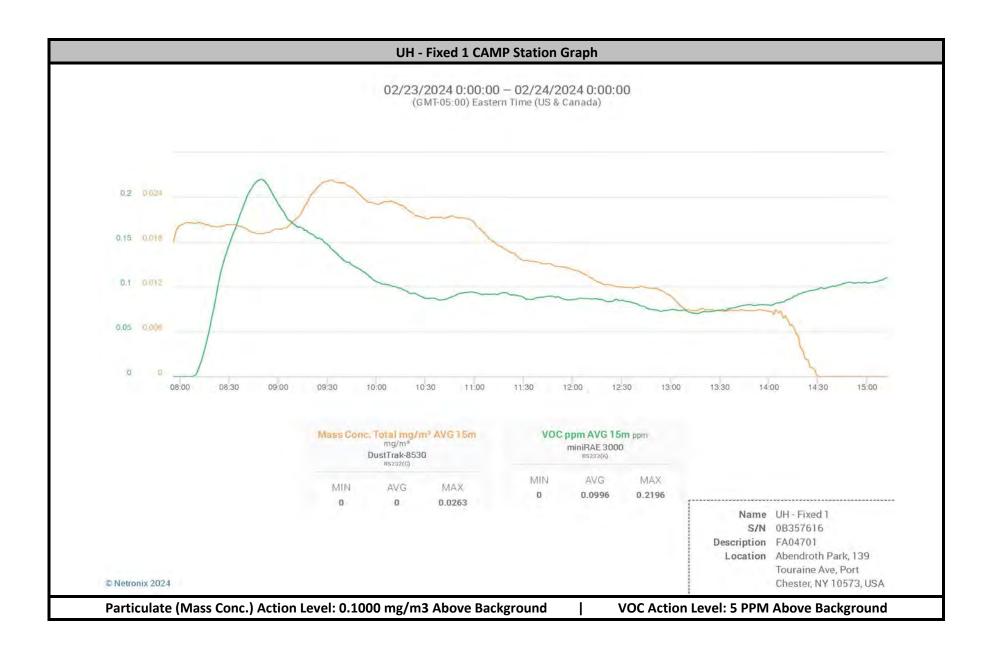


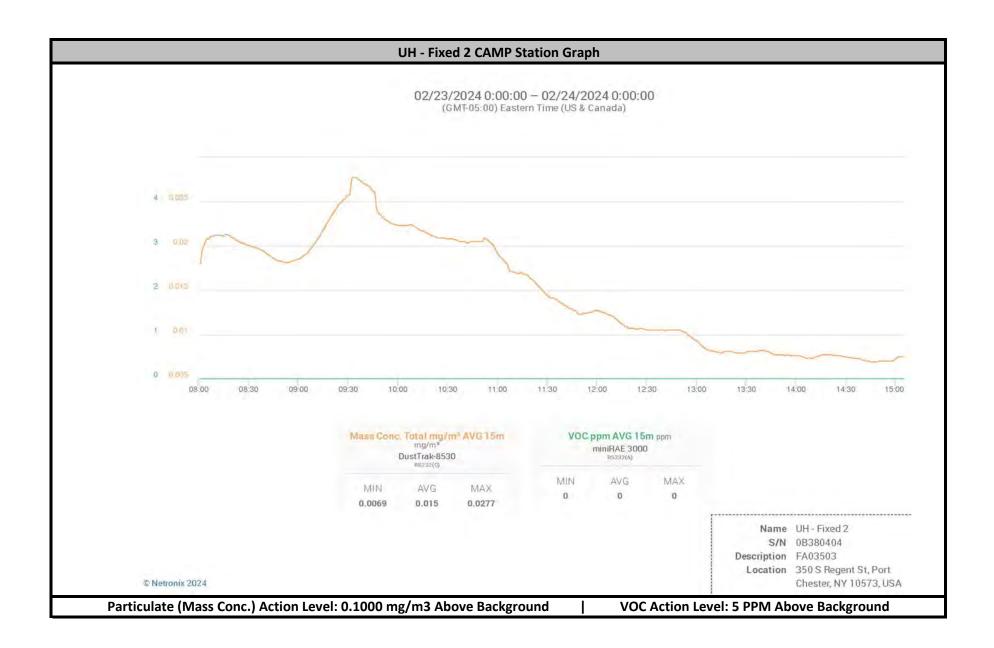

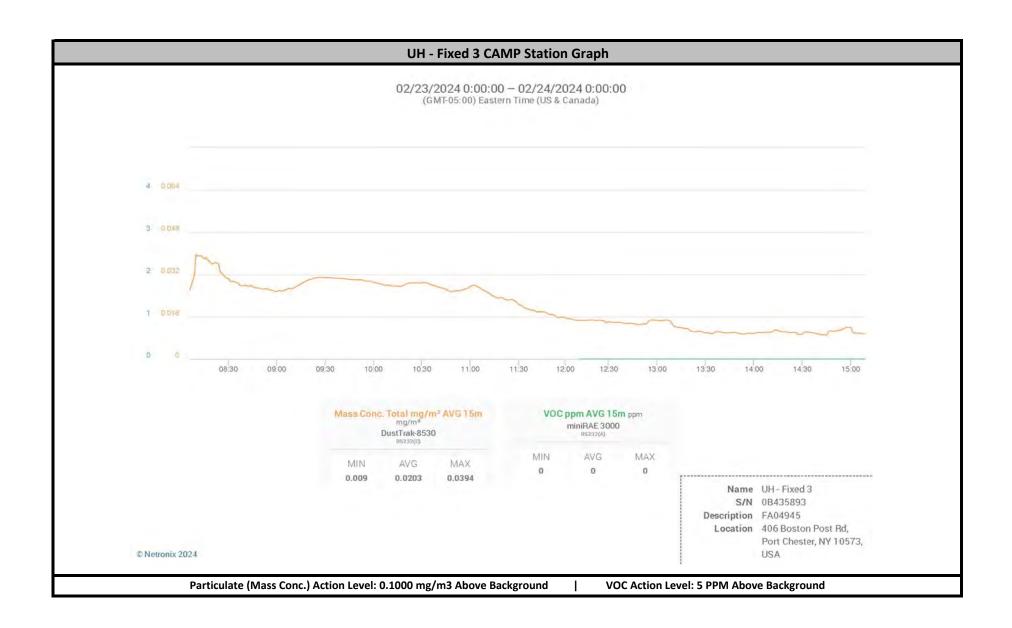

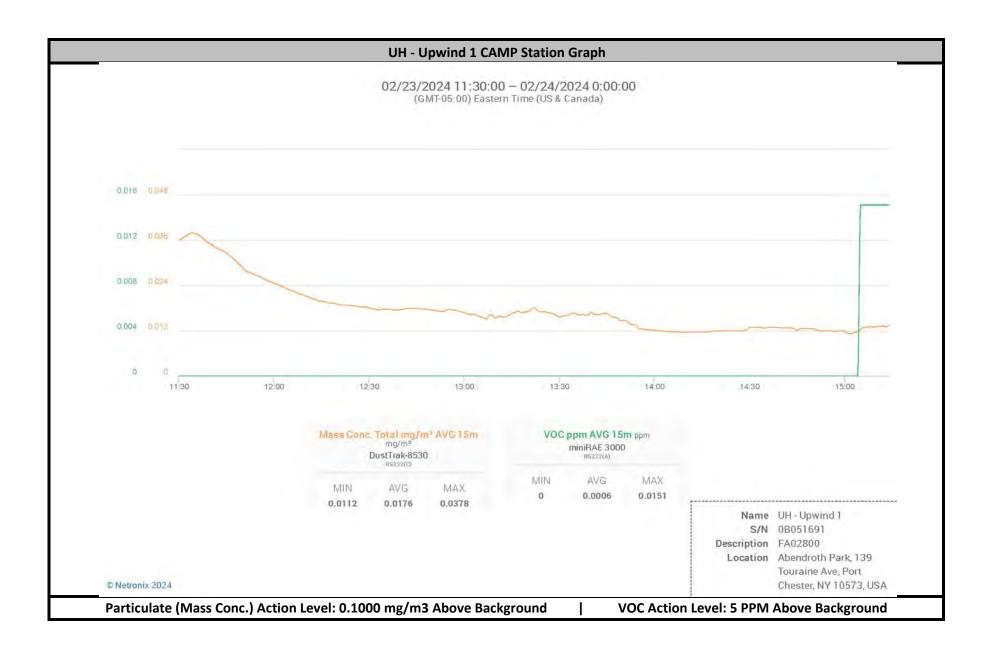

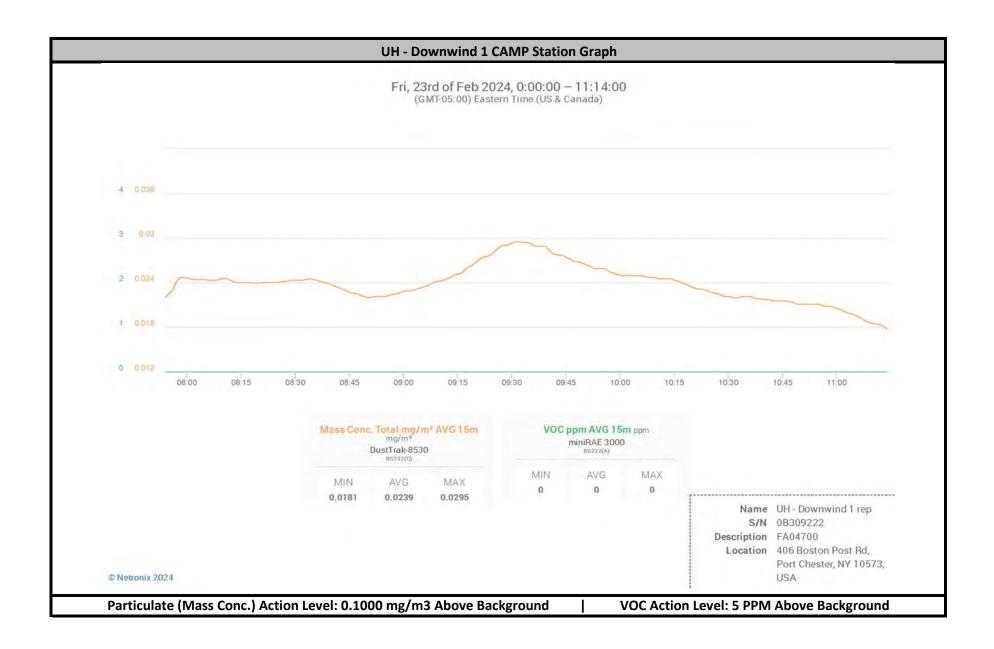


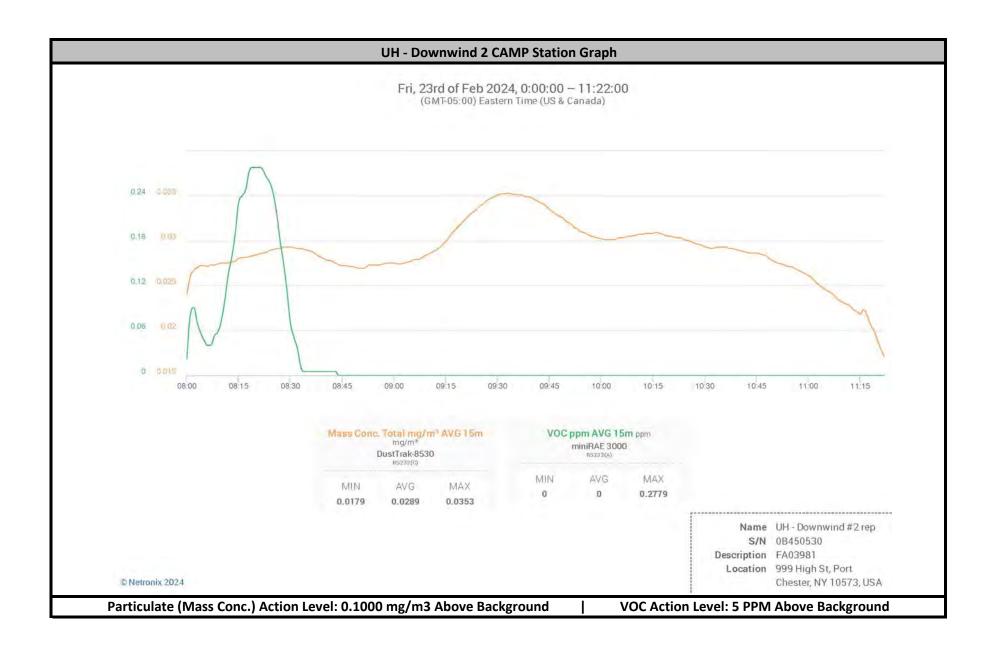



| | Daily Activity Report | | | | | | | | |
|--|---|-----------------------|-----------------------|----------------------------|-------------------|--|--|--|--|
| CAKRF | Former United Hospital Port Chester, NY | | | | | | | | |
| | | | | BCP No. C | | | | | |
| Onto. | | Genera | al Site Information | Manday Fahry | aru 26, 2024 | | | | |
| Date: Weather: | + | | | Monday, Febru Cloudy, 3 | | | | | |
| Nind Direction/Speed: | | NW @ 7 mph | | | | | | | |
| AKRF Personnel on Site: | 25: 104 | 40.01.11. (010.0.0 | | Michael | | | 0 11 11 11 0 111 11 | | |
| AKRF Equipment on Site: //isitors: | 3 Fixed CAN | 1P Stations (PID & Di | ust Monitor), 3 Porta | ble CAMP Stations (Non | |), One Handheld PID, | One Handheld Dust Monitor | | |
| 131013. | | Contra | actor Information | Non | C | | | | |
| Contracting Company | | Key Pe | rsonnel | | | Equipn | nent | | |
| Tony Casale Inc. (Excavation Contractor) | | Rigo | Diaz | | | grading equipment rs, roller-compactor, etc.) | | | |
| Capital Industries Corp. (Demolition Contractor) | | Joe Cia | anciulli | | (e.g., ex | Various demolition cavators, skid steers | on equipment , roll off containers, etc.) | | |
| | | · | ion of Work Activitie | | | | | | |
| The excavation contractor conducted general grading, compactive demonstrator contractor continued sorting and loading demonstrator contractor contr | | | | (COU) area. | | | | | |
| | | Site Soil Dispo | osal Tracking Informa | ation | | | | | |
| Destination Facility | Daily | Trucks | Daily Approx | κ. Cubic Yds. | Total Site Loads | | Total Approximate Cubic Yard | | |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | 710 | | |
| | | Daily Export (CY) | (|) | Total Export (CY) | | 710 | | |
| | | Imported Fi | II Tracking Informati | on | | | | | |
| Origin Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic Yard | | |
| Filcon West Nyack Quarry - West Nyack, NY ITEM #4) | 8 | | 200 | | 120 | | 3,235 | | |
| Tilcon West Nyack Quarry - West Nyack, NY (NY2/ASTM #5 - 3/4" Stone) | ı | 0 | | 0 | | 3 | 70 | | |
| | | Daily Import (CY) | | 200 | | Total Import (CY) | 3,305 | | |
| CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| OC Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| Particulate Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| | | Additi | ional Information | | | | | | |
| Activity for Following | Activity for Following | | | | | | | | |
| Comments: None | | | | | | | | | |


1 of 72 C360202_Daily Report_2024.02.:


Site Photographs Photograph 1 -Excavation contractor conducting general grading and compaction within the antennae COU area, view facing southwest. PAKRE etwork:Feb 26, 2024 at 12:27:58 PM EST N 40° 59' 41.045", W 73° 40' 40.971" Boston Post Rd, United States Photograph 2 -Excavation contractor importing Item #4 for use within the antennae COU area, view facing west. CAKRI Network:Feb 26, 2024 at 2:51:22 PM EST N 40° 59' 39.729", W 73° 40' 39.167" Boston Post Rd, United States Photograph 3 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north.

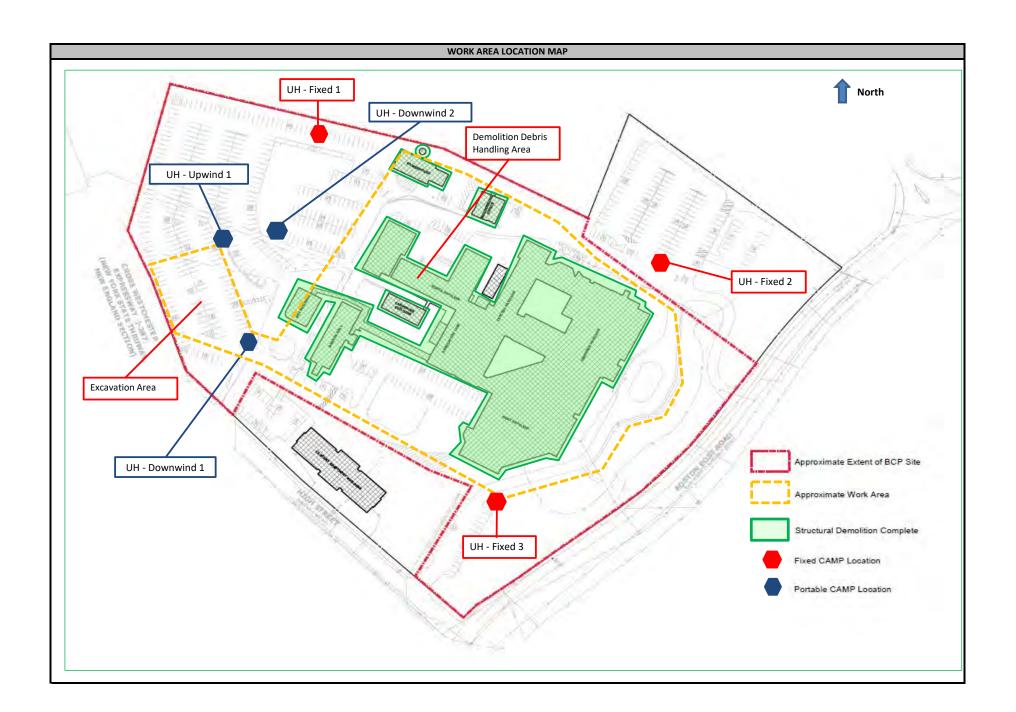


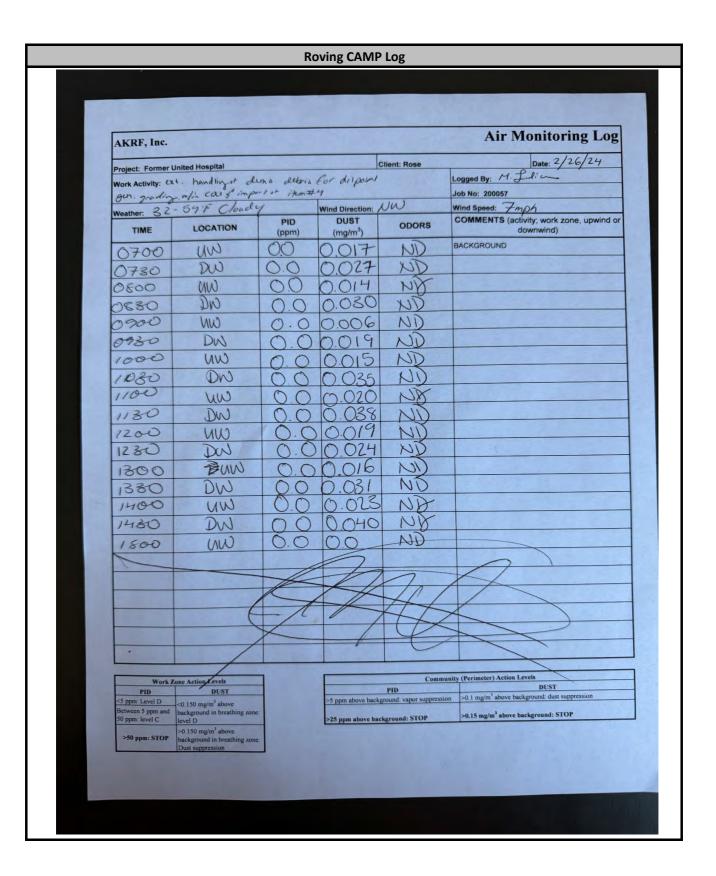


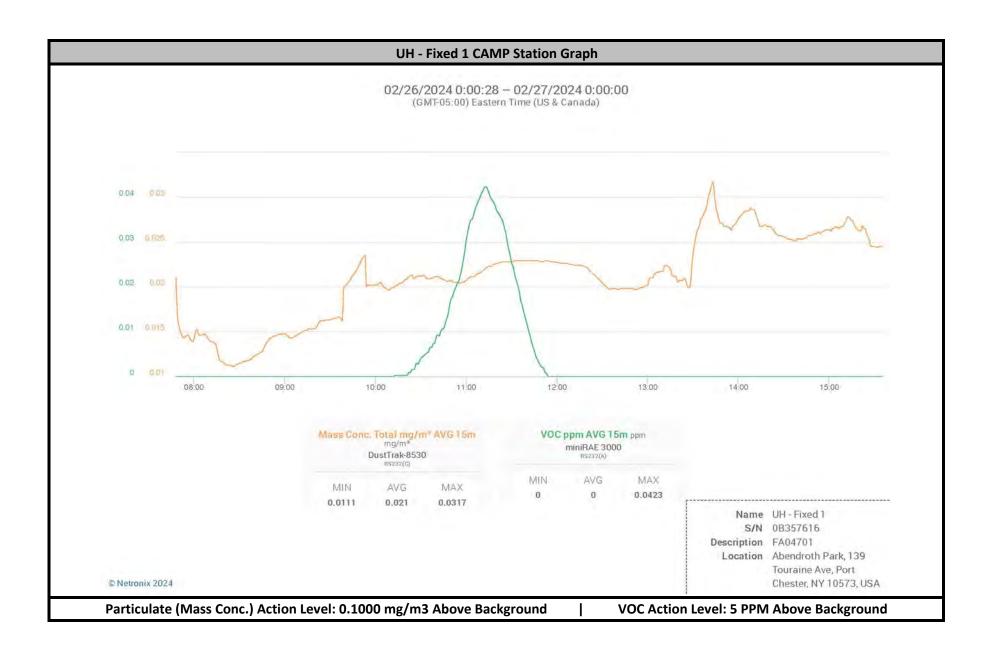


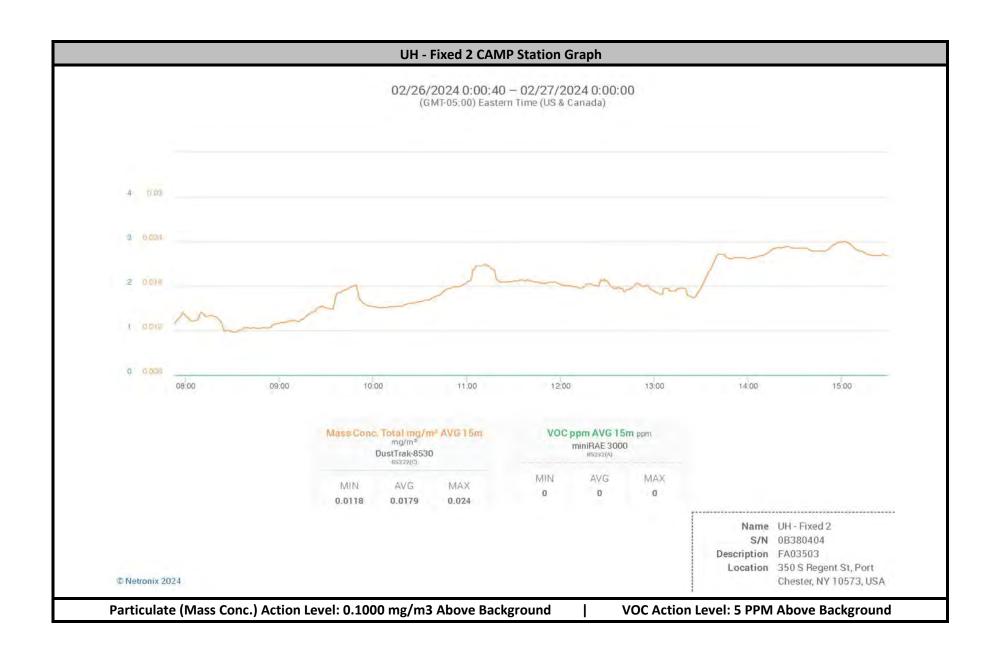

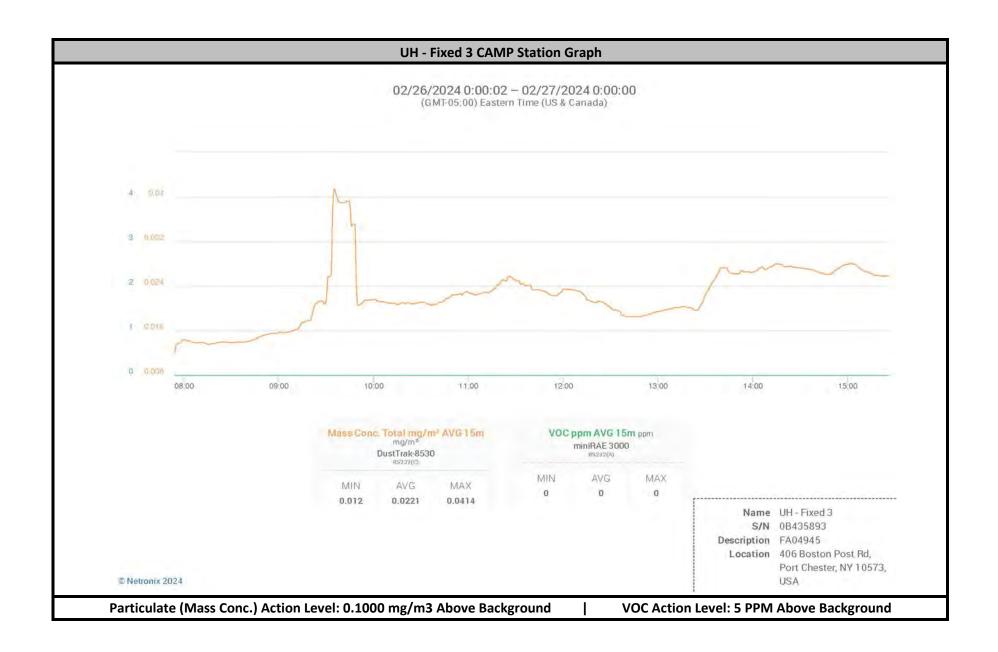

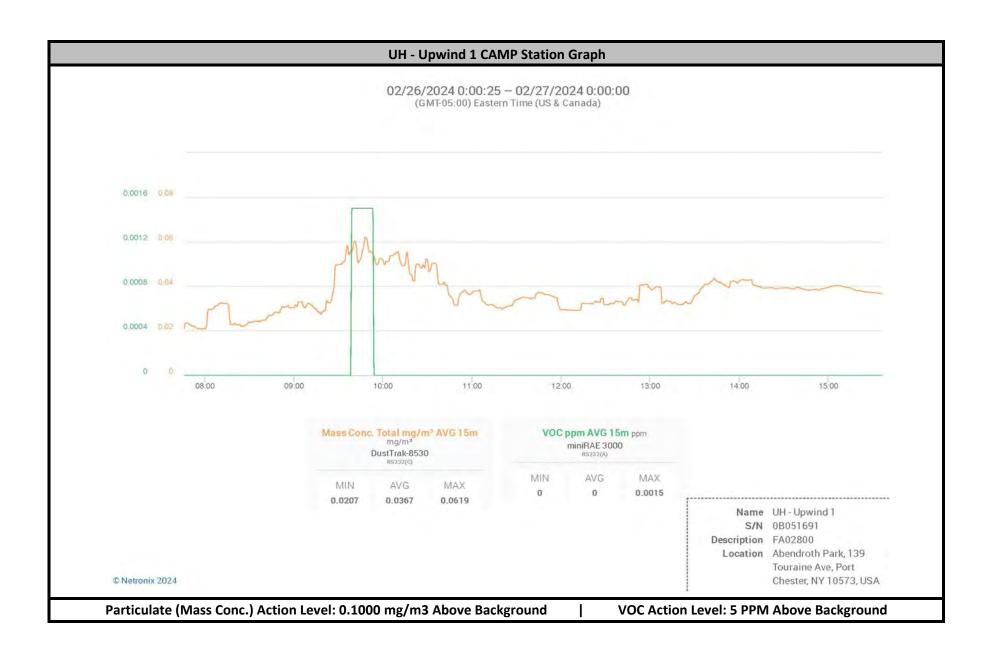

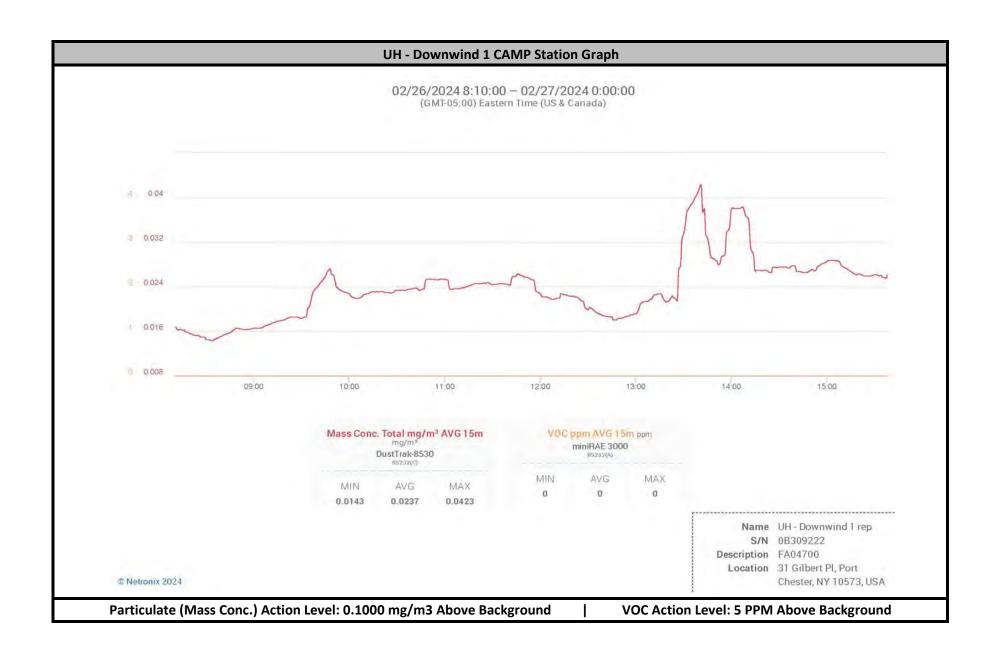

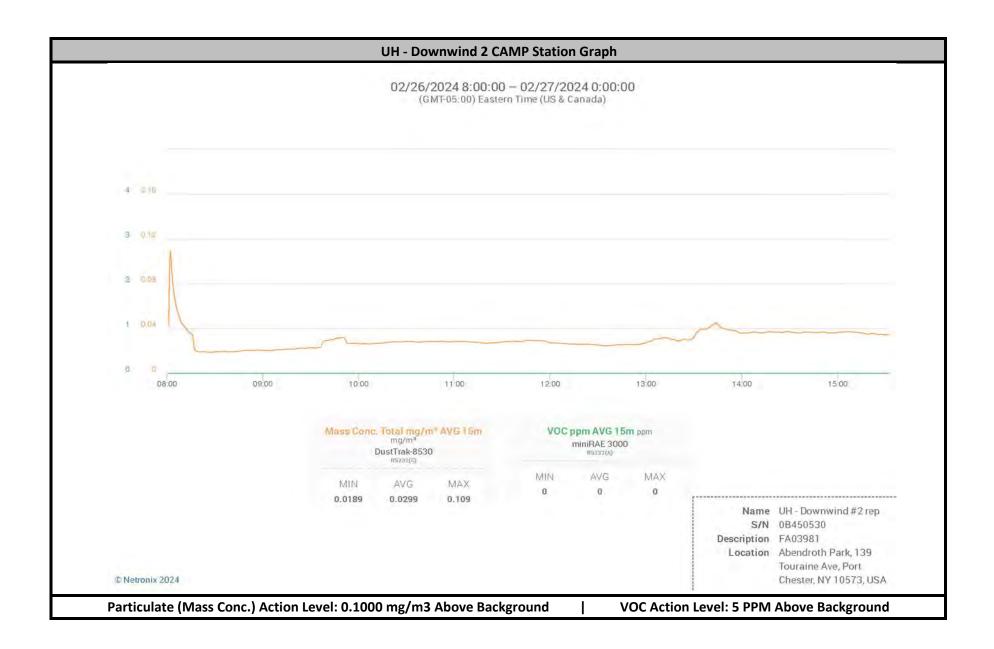

| | Daily Activity Report | | | | | | | | |
|---|---|---|-----------------------|-----------------------------------|--|-------------------------|-----------------------------|--|--|
| PAK RF | Former United Hospital Port Chester, NY BCP No. C360202 | | | | | | | | |
| | | | | | | | | | |
| | | Genera | I Site Information | BCF NO. C | 300202 | | | | |
| oate: | | | | Tuesday, Febru | | | | | |
| Veather: Vind Direction/Speed: | Cloudy, 39-57°F NE @ 4-9 mph | | | | | | | | |
| KRF Personnel on Site: | | Marco Balletta 3 Fixed CAMP Stations (PID & Dust Monitor), 3 Portable CAMP Stations (PID & Dust Monitor), One Handheld PID, One Handheld Dust Monitor | | | | | | | |
| KRF Equipment on Site: /isitors: | 3 Fixed CAN | 1P Stations (PID & Du | ust Monitor), 3 Porta | ble CAMP Stations (Non | | , One Handheld PID, | One Handheld Dust Monitor | | |
| ISITOTS: | | Contra | actor Information | NOII | e | | | | |
| Contracting Company | | Key Pe | | | | Equipm | nent | | |
| Tony Casale Inc. (Excavation Contractor) | Rigo Diaz Various excavation and gra | | | | grading equipment , roller-compactor, etc.) | | | | |
| Capital Industries Corp. | | | | | (e.g., ex | Various demolitic | | | |
| (Demolition Contractor) | | Joe Cia | anciulli | i (e.g., excavators, skid steers, | | | | | |
| | De | escription and Locat | ion of Work Activitie | es Performed | | | | | |
| he excavation contractor conducted general grading and compa | action within the ante | nnae Change of Use | (COU) area. Erosion | control mats were a | dded to completed | areas within the ante | ennae COU area. | | |
| he demolition contractor continued sorting and loading demolt | ion debris into contai | ners for off-site dispo | osal. | | | | | | |
| | | Site Soil Dispo | osal Tracking Informa | ation | | | | | |
| Destination Facility | Daily | Trucks | Daily Approx | د. Cubic Yds. | ubic Yds. Total Site Loads | | Total Approximate Cubic Yar | | |
| lean Earth of Carteret - Carteret, NJ | 0 | | 0 | | 37 | | 710 | | |
| | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | |
| | | Imported Fi | ll Tracking Informati | on | | | | | |
| Origin Facility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Si | ite Loads | Total Approximate Cubic Yar | | |
| ilcon West Nyack Quarry - West Nyack, NY TEM #4) | 0 | | 0 | | 120 | | 3,235 | | |
| ilcon West Nyack Quarry - West Nyack, NY NY2/ASTM #5 - 3/4" Stone) | 0 | | 0 | | 3 | | 70 | | |
| | Daily Import (CY) | | 0 | | Total Import (CY) | | 3,305 | | |
| CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| dors: | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| OC Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| articulate Action Level Exceedance(s) Above Background: | No | No | No | No | No | No | No | | |
| | | Additi | onal Information | | | | | | |
| Planned Work ctivity for Following | 0 | demolition debris fro | om the former hospit | Ü | | • | n activities | | |
| Day(s): The excavation contratcor will import stor | ie moini micon west N | iyack ioi use witiiin i | ine antennae COO Fa | mp area. The excava | auon contractor Will | begiii deiriobilizatioi | n acuvities. | | |
| Comments: None | | | | | | | | | |
| | | | | | | | | | |

1 of 74 C360202_Daily Report_2024.02.27

Site Photographs

Photograph 1 -

Excavation contractor conducting general grading and compaction within the antennae COU area, view facing southwest.



Photograph 2 -


Excavation contractor adding erosion control mats to completed areas within the antennae COU area, view facing northwest.




Photograph 3 -


Demolition contractor disposing of demolition debris in the central portion of the site, view facing southwest.




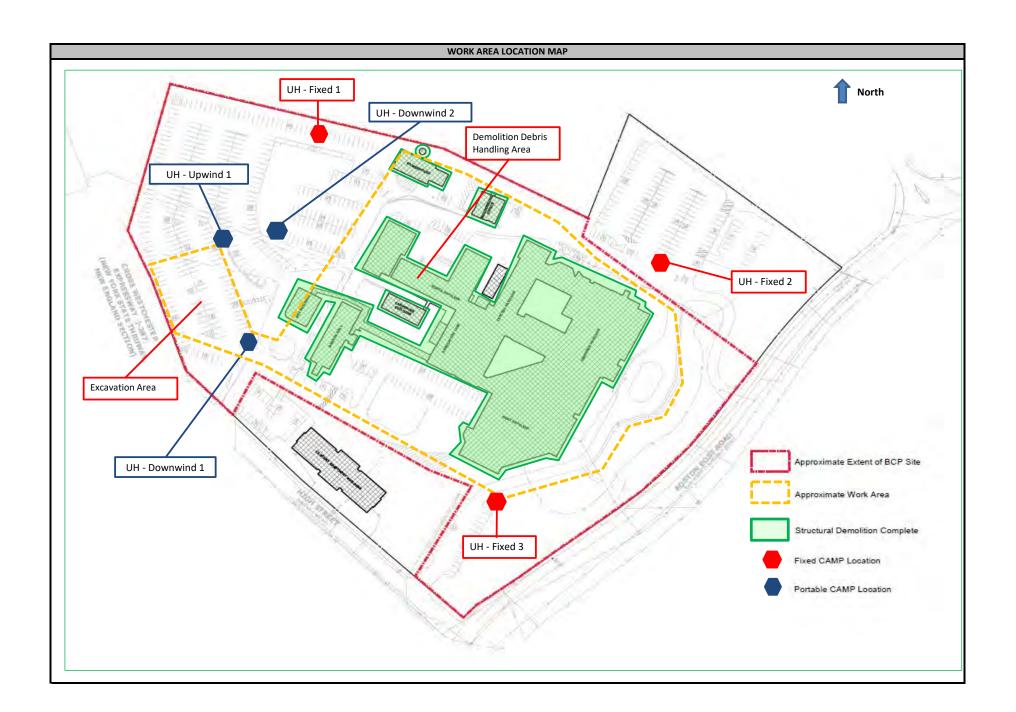



Roving CAMP Log Air Monitoring Log AKRF, Inc. 7/2021 Project: Former United Hospital Date: Client: Rose Imposed Hotered & Grading Work Activity: T Comp Dellates Trucker Logged By: Job No: 200057 (39-57/9) 4-8/mil Wind Direction: Weather: Wind Speed: DUST COMMENTS (activity; work zone, upwind or PID TIME LOCATION ODORS (mg/m^3) downwind) (ppm) lite 0.027 None BACKGROUND 0,0 madel teteral Comotion 0031 Nas 00 affore (SU) 0.057 None 0.034 None 0.029 220 None 200 0.048 None 11 11 11 0,964 11 1.20 20 30 600 0.0 0.954 Vone Det hotollomieter 0.0 0.962 Vone 1500 2.046 530 Work Zone Action Levels Community (Perimeter) Action Levels PID DUST PID DUST >5 ppm above background: vapor suppression >0.1 mg/m³ above background: dust suppression <5 ppm: Level D <0.150 mg/m¹ above Between 5 ppm and 50 ppm: level C background in breathing zone >0.15 mg/m³ above background: STOP >25 ppm above background: STOP level D >0.150 mg/m³ above >50 ppm: STOP background in breathing zone Dust suppression

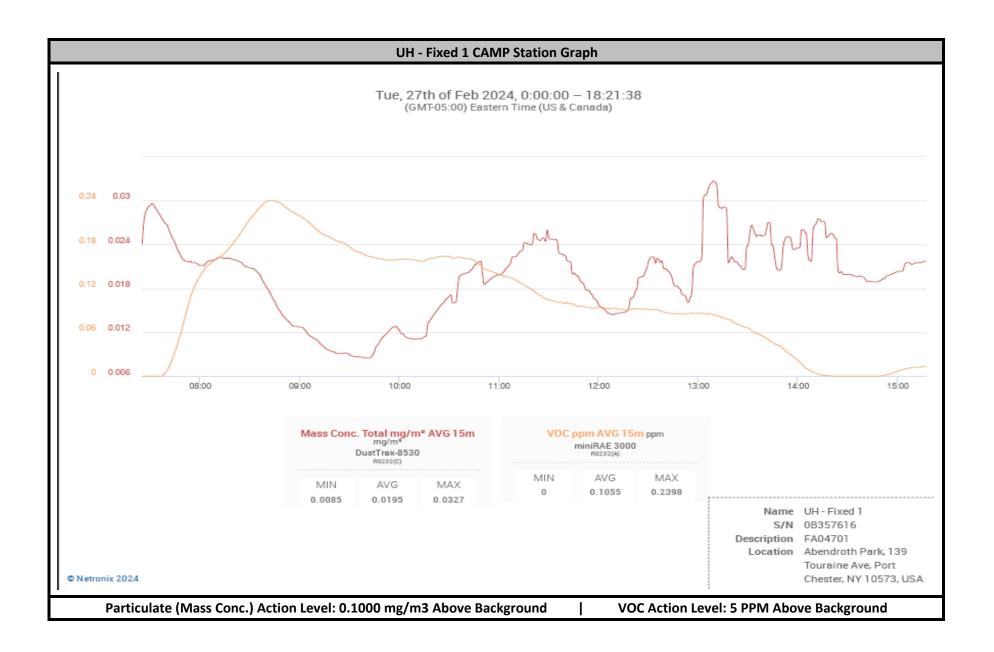


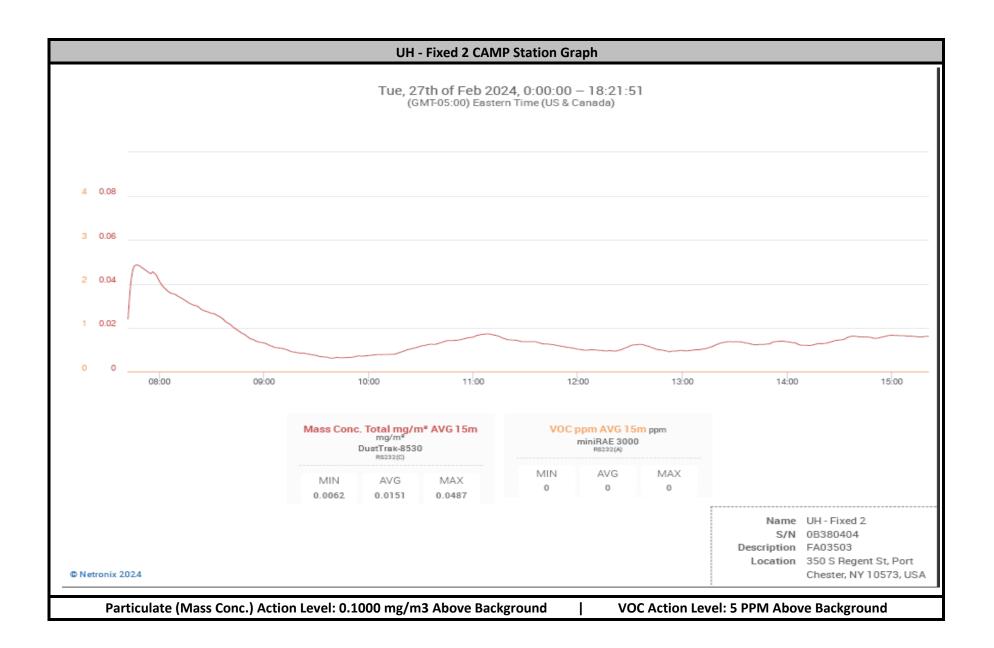

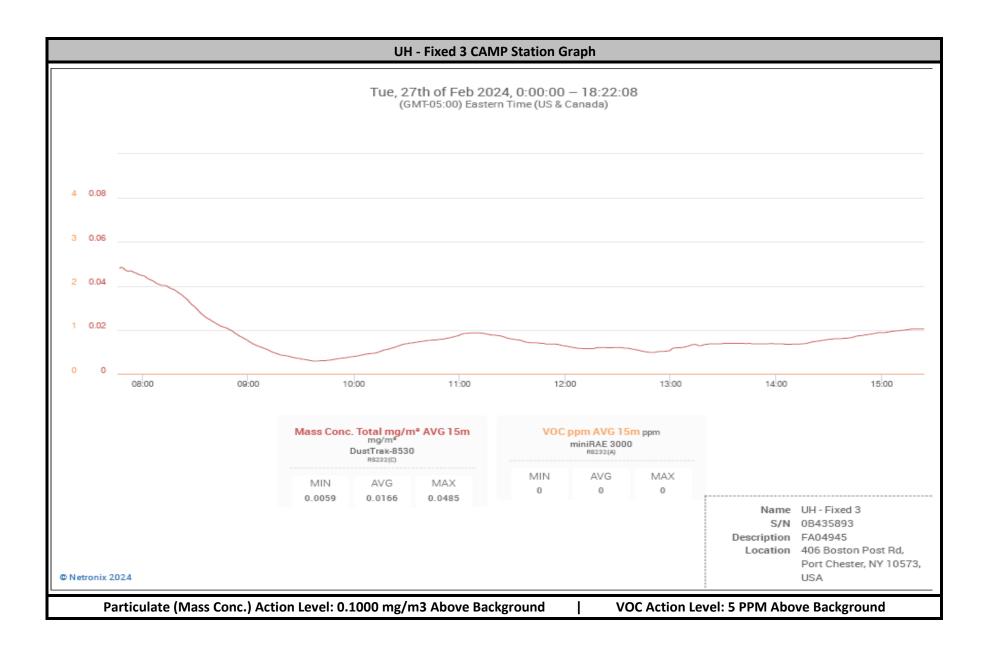

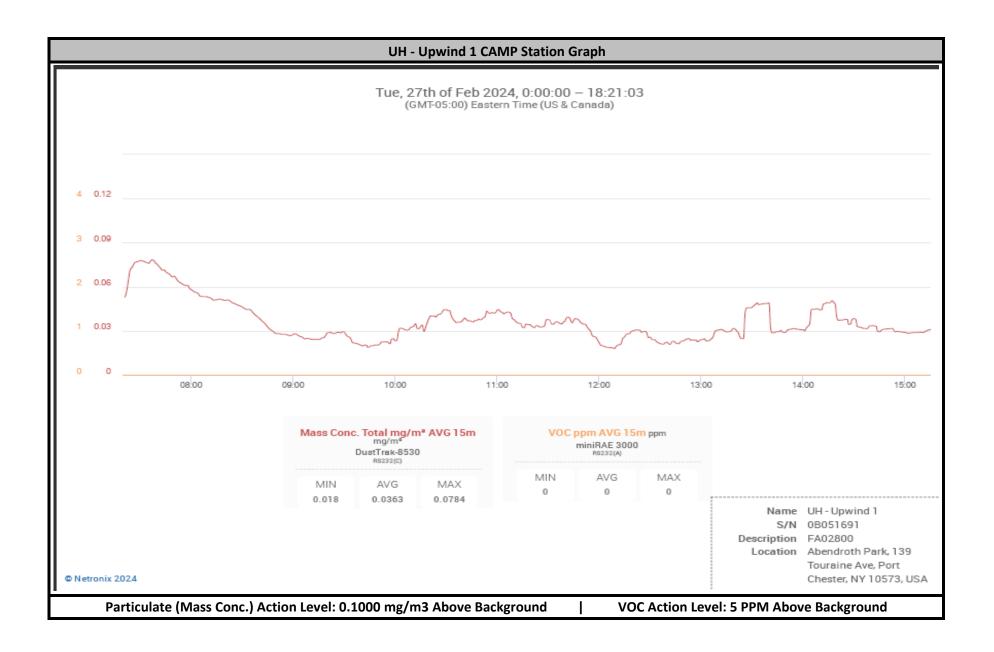

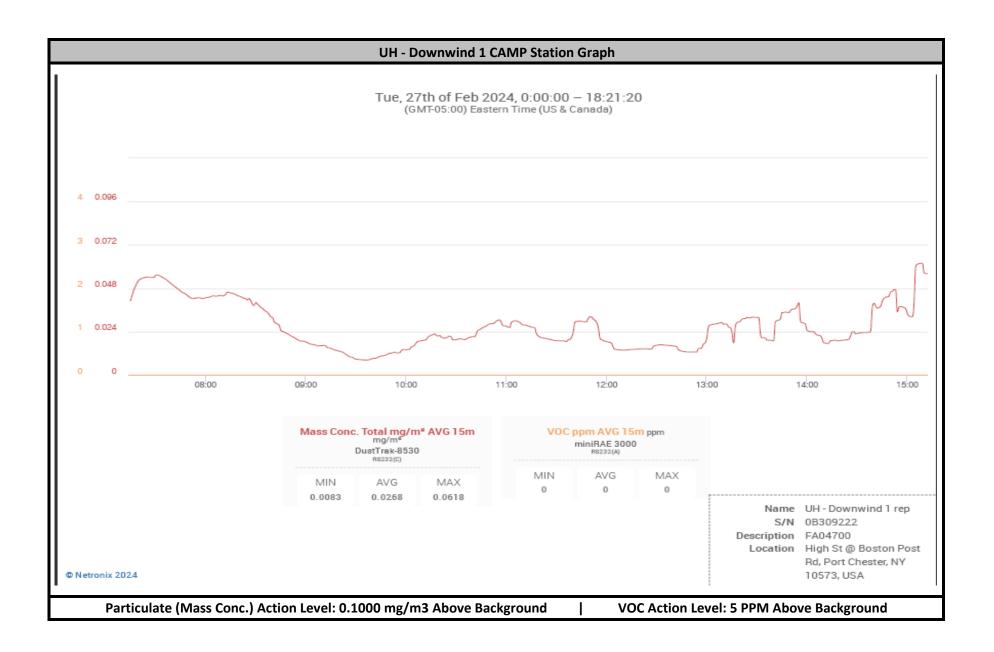


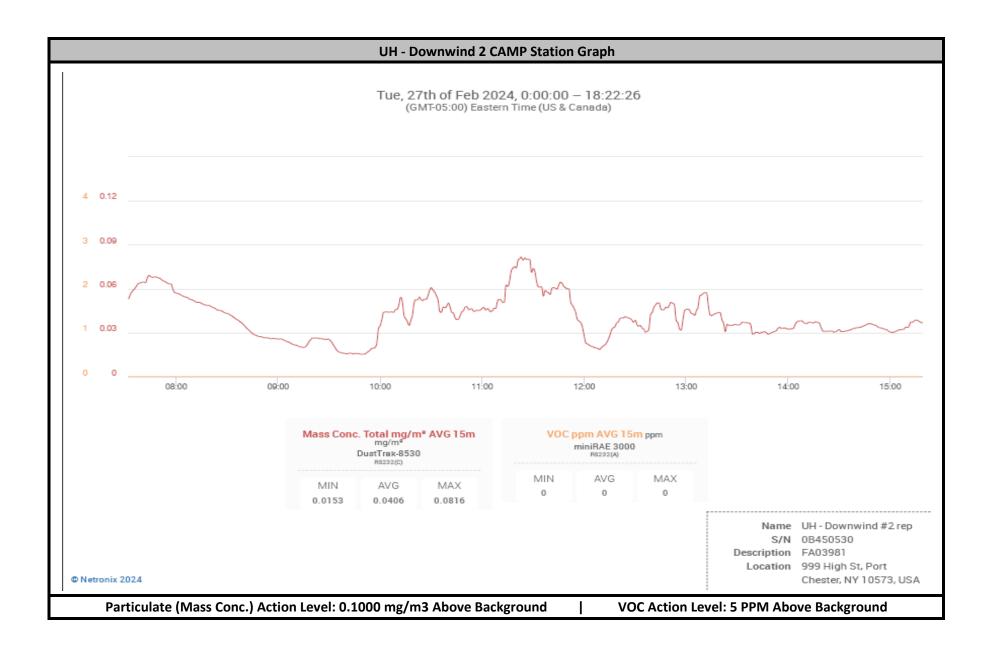


| | Daily Activity Report Former United Hospital | | | | | | | | | |
|--|--|-----------------------|--------------------------------|--|---|-------------------------------|--|--|--|--|
| PAK | Former United Hospital Port Chester, NY | | | | | | | | | |
| | | | Conora | I Site Information | BCP No. C | 360202 | | | | |
| Date: | | Τ | Genera | ii Site information | Wednesday, Febi | ruary 28, 2024 | | | | |
| Weather: | | Rain, 38-56°F | | | | | | | | |
| Wind Direction/Speed | | | South @ 11 mph Michael Iodice | | | | | | | |
| AKRF Personnel on Site AKRF Equipment on Sit | | 3 Fixed CAN | 1P Stations (PID & Du | ıst Monitor). 3 Porta | | |). One Handheld PID. | One Handheld Dust Monitor | | |
| Visitors: | | 31 /// 64 67 117 | 50000000 | 35: 11:01:11:1 | Tracy P. | | ,, one mananera ma, | one nanancia base monitor | | |
| | | | | ector Information | | | | | | |
| (| Contracting Company | | Key Pe | rsonnel | | | Equipm | | | |
| (E | Tony Casale Inc. xcavation Contractor) | Rigo Diaz | | | Various excavation and grading equipment (e.g., excavators, compactors, roller-compactor, etc.) | | | | | |
| | apital Industries Corp. emolition Contractor) | | Joe Cia | anciulli | | (e.g., ex | Various demolitic cavators, skid steers | on equipment , roll off containers, etc.) | | |
| | | De | escription and Locati | ion of Work Activitie | es Performed | | | | | |
| The excavation contrac | ctor began demobilization within the anten | nae Change of Use (C | COU) area. | | | | | | | |
| The demolition contra | ctor continued sorting and loading demolti | on debris into contai | ners for off-site dispo | osal. | | | | | | |
| | | | Site Soil Dispo | sal Tracking Informa | ation | | | | | |
| | Destination Facility | Daily [·] | Trucks | Daily Approx. Cubic Yds. Total Site Loads | | Total Approximate Cubic Yards | | | | |
| Clean Earth of Carteret - Carteret, NJ | | 0 | | 0 | | 37 | | 710 | | |
| | | Daily Export (CY) | | 0 | | Total Export (CY) | | 710 | | |
| | | | Imported Fil | ll Tracking Informati | on | | | | | |
| | Origin Facility | Daily ' | Trucks | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic Yards | | |
| Tilcon West Nyack Qua (ITEM #4) | rry - West Nyack, NY | 0 | | 0 | | 120 | | 3,235 | | |
| Tilcon West Nyack Qua (NY2/ASTM #5 - 3/4" S | | 0 | | 0 | | 3 | | 70 | | |
| | | Daily Import (CY) | | 0 | | Total Import (CY) | | 3,305 | | |
| | CAMP Information | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | | |
| Odors: | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | | |
| VOC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| Particulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | | |
| | | | Additi | onal Information | | | | | | |
| Activity for Following | The demolition contractor will continue so | | | om the former hospit | al buildings into cor | ntainers for off-site d | lisposal. | | | |
| Comments: | CAMP stations were not deployed due to i was not in use, and no fugitive dust or odc | | ersisting throughout | the workday. Visual | and olfactory monit | oring was performed | d during the period t | nat the air monitoring equipment | | |

1 of 4 C360202_Daily Report_2024.02.28

Site Photographs Network:Feb 28, 2024 at 10:59:23 AM EST N 40" 59" 39,498", W 73" 40" 37,823" Boston Post Rd, United States Photograph 1 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing north. Network:Feb 28, 2024 at 1:00:28 PM EST N 40° 59' 39.706", W 73° 40' 36.610" Boston Post Rd, United States Photograph 2 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing northeast. CAKRE Network:Feb 28, 2024 at 1:30:15 PM EST N 40° 58' 39,780", W 73° 40' 35,781" Boston Post Rd, United States Photograph 3 -Demolition contractor sorting structural demolition debris in the central portion of the site, view facing northeast.

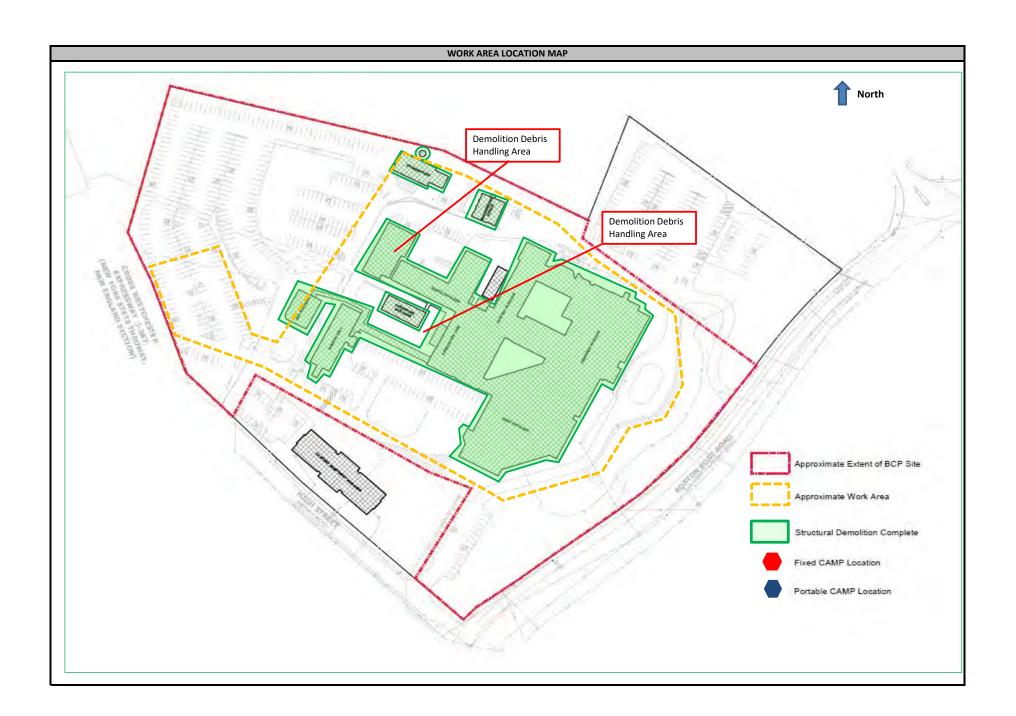

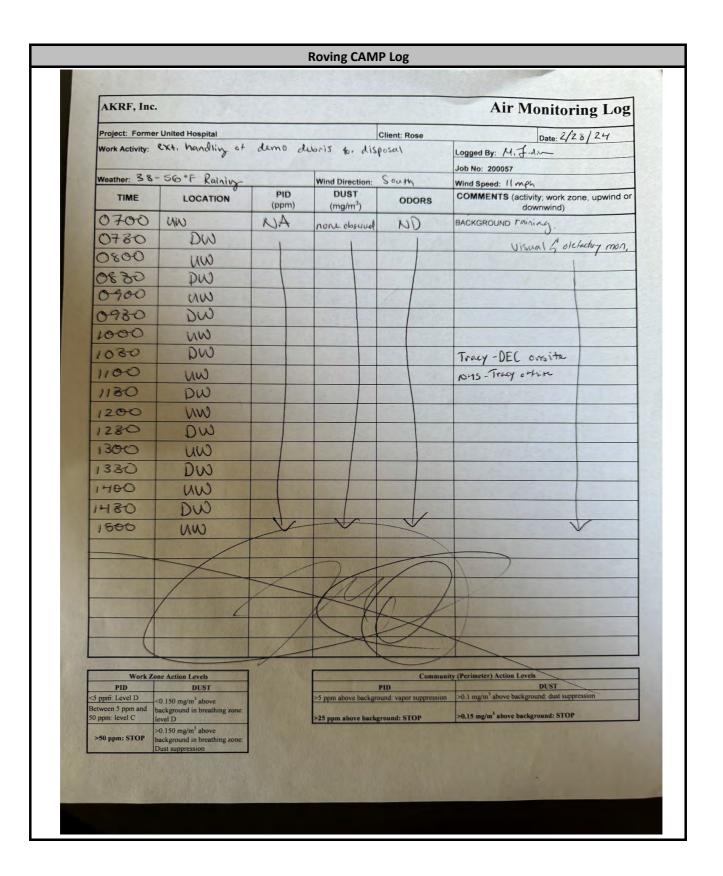

| | Daily Activity Report | | | | | | | | |
|--|--------------------------------|---|--|---|-----------------------|-----------------------|-------------------------|------------------------------|-------|
| AKRF | 1 | Former United Hospital Port Chester, NY | | | | | | | |
| | | BCP No. C360202 | | | | | | | |
| | | 1 | Genera | al Site Information | 71 5 | 20.2024 | | | |
| | | Thursday, February 29, 2024 Partly Cloudy, 28-41°F | | | | | | | |
| ection/Speed: | | | WNW @ 15-30 mph | | | | | | |
| onnel on Site: | | | | | Michael | | | | |
| ipment on Site: | | 3 Fixed CAN | //P Stations (PID & Du | ust Monitor). 3 Porta | | | . One Handheld PID. | One Handheld Dust Monito | r |
| , | | | | ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | Non | | , , | | |
| | | | Contra | actor Information | | | | | |
| Contracting Co | ompany | | Key Pe | rsonnel | | | Equipm | nent | |
| Capital Industrie | | | Joe Cianciulli Various demolition | | | | | | |
| (Demolition Con | ntractor) | | | | | (e.g., ex | cavators, skid steers | , roll off containers, etc.) | |
| | | D | escription and Locat | ion of Work Activitie | es Performed | | | | |
| lition contractor continued | d sorting and loading demolt | tion debris into conta | iners for off-site disp | osal. | | | | | |
| | | | Site Soil Dispo | osal Tracking Inform | ation | | | | |
| Destination F | acility | Daily | Trucks | Daily Approx | c. Cubic Yds. | Total Si | te Loads | Total Approximate Cubic | Yards |
| th of Carteret - Carteret, NJ | J | | 0 | 0 | | 37 | | 710 | |
| | | | Daily Export (CY) | 0 | | Total Export (CY) | | 710 | |
| | | | Imported Fi | Il Tracking Informati | ion | | | | |
| Origin Faci | Daily Trucks | | Daily Approx. Cubic Yds. | | Total Site Loads | | Total Approximate Cubic | Yards | |
| st Nyack Quarry - West Ny | rack, NY | 0 | | 0 | | 123 | | 3,300 | |
| st Nyack Quarry - West Nya M #5 - 3/4" Stone) | rack, NY | 0 | | 0 | | 5 | | 120 | |
| | | Daily Import (CY) | | 0 | | Total Import (CY) | | 3,420 | |
| CAMP Inform | nation | Roving Equipment | UH - Fixed 1 | UH - Fixed 2 | UH - Fixed 3 | UH - Upwind 1 | UH - Downwind 1 | UH - Downwind 2 | |
| | | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | None Observed | |
| VOC Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | |
| Particulate Action Level Exceedance(s) Above Background: | | No | No | No | No | No | No | No | |
| | | | Additi | ional Information | | | | | |
| ed Work The demolition | on contractor will continue so | orting and loading of | demolition dehris fro | om the former hosnit | al buildings into cor | ntainers for off-site | lisposal. | | |
| or Following | | | | | | | | | |
| | | | | | | | | | |
| VOC Action Level Exceedance(s) Above Background: Particulate Action Level Exceedance(s) Above Background: Planned Work Activity for Following Day(s): The demolition contractor will continue to the excavation contractor will continue to t | | | No Additi demolition debris fro | No ional Information om the former hospit | No | No | No | | |

1 of 70 C360202_Daily Report_2024.02.2

Site Photographs

Photograph 3 Demolition contractor sorting structural demolition debris in the central portion of the site, view facing northeast.



Photograph 3 -

Demolition contractor loading structural demolition debris in the central portion of the site for off-site disposal, view facing northeast.



Photograph 3 -

Demolition
contractor sorting
structural demolition
debris in the central
portion of the site,
view facing
northeast.



