

Project	Former Port Mobil Terminal –	Report No.	21
	IRM #1		
NYSDEC Site	#243016	Date	10/21/2024
Location	4101 Arthur Kill Road	File No.	0208988
	Staten Island, NY		
Client	NP Staten Island Industrial, LLC	Temperature	47-79°F
Contractor	Entact, Haley & Aldrich	Wind Direction	SW to NE up to 6 mph
Weather	Sunny	Personnel on Site	S. Sotomayor,
			K. O'Connor
Humidity	81%	Time on Site	6:45 am to 5:00 pm

H&A of New York Engineering and Geology, LLP (Haley & Aldrich) was present to document the implementation of the August 2024 NYSDEC-approved Interim Remedial Measures 1 Work Plan (IRM 1 Work Plan) prepared by Haley & Aldrich for the Former Port Mobil Terminal, located at 4101 Arthur Kill Road, Staten Island, NY. Site Observations are summarized below.

Daily Observations:

- Haley & Aldrich field personnel performed community air monitoring during the implementation of the activities in the approved IRM 1 Work Plan.
- Entact loaded tri-axle trucks with soil from Excavation 5 for off-Site transport and waste disposal.
- Entact continued excavation and stockpiling of soil in Excavation 5, stockpiled soil staged on tarp pad and covered.
- Entact applied odor suppressant foam in Excavation 5 at the end of the work shift.
- Entact continued pot holing inspections for utilities in Excavation 9 using the Hydro Vac Truck.
- Background PID Reading for Excavation 5: 0.0 ppm
- Stockpile PID Reading for Excavation 5: 24.9 ppm

Waste Disposal/Backfill Import Tracking:

Material Export:

• Soil/Fill disposal is summarized below:

Facility	Pure Soil Technologies Jackson, NJ						То	tal
Today:	Loads 14	Tons 280	Loads 0	Tons 0	Loads 0	Tons 0	Loads 14	Tons 280
<u>Total:</u>	<u>57</u>	1,300	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>57</u>	1,300

Note: Tonnage is approximate, executed tonnages to be included in the Construction Completion Report.



Material Import:

• Fill import is summarized below:

Facility	Mount Ho ASTM #57		То	tal
Today:	Loads 0	CY 0	Loads 0	CY 0
<u>Total:</u>	<u>14</u>	<u>401.5</u>	<u>14</u>	<u>401.5</u>

Note: 1 truckload estimated at 20 cubic yards. Quantities to be included in the Construction Completion Report.

Samples Collected:

None.

CAMP Activities:

- Background air monitoring was performed at three locations, one at the western boundary of the IRM 1 work area, one at the central location of the IRM 1 work area, and one at the eastern boundary of the IRM 1 work area, from 7:00 AM to 4:15 PM.
- No 15-minute average concentrations of VOCs or particulate matter smaller than 10 microns in diameter (PM10) exceeded the action levels. No visible dust was observed leaving the site perimeter.

Activities Planned for Coming Week:

- Entact will begin support of excavation (SOE) installation.
- Entact will continue excavating and stockpiling C&D debris for disposal.
- Entact will continue excavating soil for off-site transport and disposal.



Site Staff								
Company	Individual	Title						
Haley & Aldrich	Sebastian Sotomayor	Field Manager						
Haley & Aldrich	Kassidy O'Connor	Field Staff						
Entact	Wyatt Seel	Field Engineer						
Entact	Austin Farmerie	Field Engineer						
Entact	Brent Hayes	Field Project Manager						
Entact	Tariq Smith	SSHO						
Entact	Jeramy Leibrant	Operator						
Entact	Ross Deambrogo	Field Manager						
EA Engineering	Thomas Irvine	Site Inspector						
EA Engineering	Joe Kowalski	Site Inspector						
	Site Equipment							
Name	Contractor	Quantity						
Komatsu WA 380	Entact	1						
Caterpillar 289D Skid Steer	Entact	1						
Chicago Pneumatic Generator (CPG)	Entact	1						
Caterpillar 336E Excavator	Entact	2						
Pavement Saw	Entact	1						
Light Tower	Entact	1						
Godwin Pumps	Entact	2						
Water Truck	Entact	1						
Long Stick Caterpillar Excavator 336E	Entact	1						
Hydro Vac Truck	Entact	1						
Caterpillar Dozer D6	Entact	1						
Caterpillar Rock Truck 740	Entact	1						
Caterpillar Excavator 314	Entact	1						
United Rental Frac Tank	United Rental	1						
Rusmar Foam Machine	Entact	1						



Site Photographs:




Photo 1: View of truck wash station in IRM 1 Central Area, facing west.



Photo 2: View of soil loading onto rock truck for staging in containment area, in Excavation 5, IRM 1

Eastern Area, facing north.



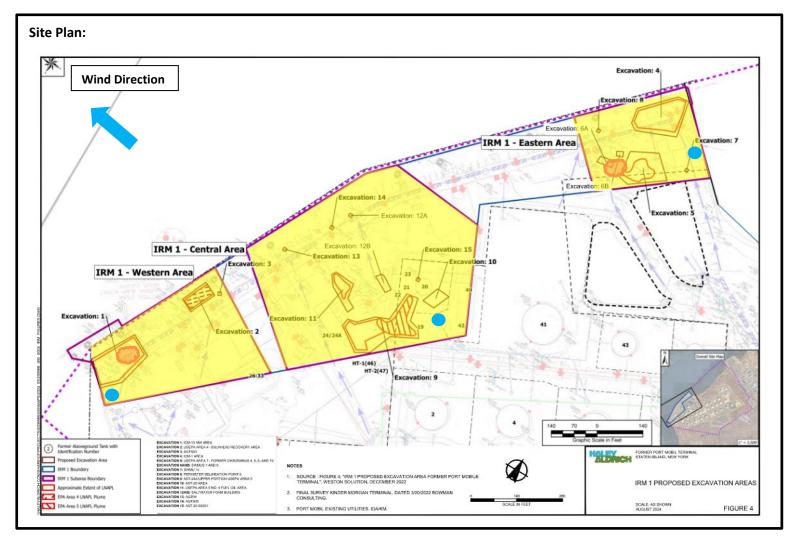

Reference: Interim Remedial Measures 1 Work Plan Figure 7B IRM-1 Central Area Proposed Excavation Area, prepared by Haley & Aldrich of New York, dated May 2024



4101 Arthur Kill Rd, Staten Island, New York, 10309

Air Monitoring Log

Date: 2024-10-21

Personnel: S. Sotomayor

Weather: Sunny, 47-79°F

Humidity: 81%

Wind Direction: SW to NE, 6 mph

Particulate Background (ug/m3): 13.657

PID Background (ppm) : 0.0

Action Levels : <u>Downwind perimeter of work area above background levels</u>

PID (ppm): > 5 ppm for the 15-min average

Dust (ug/m3): > 150 for the 15-min average

Minute of Time	Avg. PM10 (Station1)	Avg. PM10 (Station2)	Avg. PM10 (Station3)	Avg. VOC(Station1)	Avg. VOC(Station2)	Avg. VOC(Station3)	Odors	Notes Activities/ Additional Monitoring
07:00	13.477	13.657	12.050	0.0	0.0			
07:15	8.419	4.965	7.967	0.0	0.0	0.0		
07:30	7.178	6.397	7.966	0.0	0.0	0.0		
07:45	6.065	4.932	6.099	0.0	0.0	0.0		
08:00	5.553	5.949	6.462	0.0	0.0	0.1		
08:15	6.243	5.925	7.745	0.0	0.0	0.1		
08:30	7.843	4.787	8.964	0.1	0.0	0.1		
08:45	6.409	5.184	6.524	0.1	0.1	0.1		
09:00	5.689	5.297	7.705	0.1	0.0	0.1		
09:15	5.498	6.987	7.090	0.1	0.0	0.1		
09:30	5.483	5.501	6.563	0.1	0.1	0.1		
09:45	4.539	4.020	5.626	0.0	0.2	0.1		
10:00	4.241	6.413	5.941	0.0	0.0	0.1		
10:15	5.724	6.523	6.079	0.0	0.0	0.0		
10:30	4.635	6.151	6.350	0.0	0.0	0.0		
10:45	5.423	5.844	6.627	0.0	0.0	0.0		

4101 Arthur Kill Rd, Staten Island, New York, 10309

Air Monitoring Log

Minute of Time	Avg. PM10 (Station1)	Avg. PM10 (Station2)	Avg. PM10 (Station3)	Avg. VOC(Station1)	Avg. VOC(Station2)	Avg. VOC(Station3)	Odors	Notes Activities/ Additional Monitoring
11:00	4.713	4.972	5.943	0.0	0.0	0.0		
11:15	4.677	4.305	6.116	0.0	0.0	0.0		
11:30	3.803	3.978	5.551	0.0	0.0	0.0		
11:45	3.603	3.731	4.963	0.0	0.0	0.0		
12:00	3.382	3.867	4.718	0.0	0.0	0.0		
12:15	3.731	4.168	4.965	0.0	0.0	0.0		
12:30	5.119	4.186	5.047	0.0	0.0	0.0		
12:45	8.595	4.094	5.013	0.0	0.0	0.0		
13:00	4.709	4.217	5.741	0.0	0.0	0.0		
13:15	4.345	4.199	4.849	0.0	0.0	0.0		
13:30	3.990	4.210	4.985	0.0	0.0	0.0		
13:45	5.637	4.548	5.223	0.0	0.0	0.0		
14:00	7.305	4.429	5.399	0.0	0.0	0.0		
14:15	8.613	4.693	5.305	0.0	0.0	0.0		
14:30	8.914	5.386	5.958	0.0	0.0	0.0		
14:45	4.461	4.040	5.063	0.0	0.0	0.0		
15:00	7.575	3.558	4.756	0.0	0.0	0.0		
15:15	3.307	3.493	4.421	0.0	0.0	0.0		
15:30	5.289	3.819	4.571	0.0	0.1	0.0		
15:45	3.271	3.507	4.365	0.0	0.0	0.0		
16:00	2.732	3.404	4.495	0.0	0.0	0.0		
16:15	2.590	3.618	5.612	0.0	0.0	0.0		
