

## **APPENDIX H**

# **WEEKLY PROGRESS REPORTS**

**REVERE OU1 PHASE I RD/RA  
PRE-CONSTRUCTION MEETING AGENDA  
March 7, 2012**

- I. Introduce key personnel and define the authority and responsibility of each party
- II. Review work area security and safety protocols
- III. Review methods for distributing and storing documents and reports
- IV. Review methods for documenting and reporting inspection data
- V. Discuss any appropriate modifications of the workplan to ensure that project-specific considerations are addressed
- VI. Conduct a project area walk to verify that the design criteria, plans and specifications are understood and to review material and equipment storage locations
- VII. Discuss coordination of the work with the active operations of the facility

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, March 28, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Full face respirator quantitative test
  - b. Daily air monitoring commenced
  - c. ENTACT will submit air monitoring data on a weekly basis
2. Site Conditions
3. Progress Review (Week of March 19, 2012)
  - a. Continued the clearing of Containment Cell Area
  - b. Began screening and excavating hot spots within Containment Cell Area
  - c. Completed the placement of base material along entrance road to support zone and work areas
  - d. Began placing base material along clean haul roads in Eastern Fill Area
  - e. Began relocating boulders and rocks from Water –Filled Excavation
  - f. Completed the installation of silt fence in the Eastern Fill Area
  - g. Continued pumping water from the Water-Filled Excavation into storage tanks
  - h. Began the installation of clean fill road in the Eastern Fill Area
4. Schedule (Week of March 26, 2012)
  - a. Continue water pumping activities
  - b. Prep Containment Cell Area, including- de-stumping, boulder and rock removal

- c. Continue installation of clean haul road, including- placing fabric, laying base material, installing snow fence, placement of signs.
  - d. Begin laying 40mil poly for Staging Pile base
  - e. Continue screening and excavating hotspots located within the Containment Cell Area
  - f. Begin post – excavation confirmation sampling at excavated hot spots in Containment Cell Area.
5. Administrative Issues
- a. Submittals
6. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, April 4, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. ENTACT will submit air monitoring data on a weekly basis
  - c. No near losses or incidents to report.
2. Site Conditions
3. Progress Review (Week of March 26, 2012)
  - a. Continued prepping Containment Cell Area, including- de-stumping, and rock removal
  - b. Completed installation of clean haul road, including- placing fabric, laying base material, installing snow fence, and placement of signs
  - c. Completed installing 40 Mil HDPE for staging Pile Area
  - d. Completed Screening and excavating SSA hot spots in Containment Cell Area
  - e. Collected Confirmation sampling at SSA hot spots in Containment Cell Area, samples results expected Monday or Tuesday for review
  - f. Surveyor located 42 sample points for backfill mat in containment cell area
  - g. Allied Drilling closed out 9 monitoring wells.
4. Schedule (Week of April 2, 2012)
  - a. Continue water pumping activities as needed
  - b. Begin sampling on site backfill mat in Containment Cell Area
  - c. Removing Boulders from phase 1 Eastern Fill Area

- d. Begin solidification of sediment in Water Filled Excavation Area
  - e. Begin removing impacted material from cells in the Eastern Fill Area phase 1 and placing in Staging area
  - f. Expand or close SSA hot spots, pending analytical review and approval
- 5. Administrative Issues
  - a. Submittals
- 6. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, April 11, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
  - c. Air Monitor Relocation.
2. Progress Review (Week of April 2, 2012)
  - a. Continued prepping Containment Cell Area, including- de-stumping, and rock removal.
  - b. Sampled 33 out of 42 of the sample points for backfill material in Containment Cell Area.
  - c. Points not sampled because of their proximity with the SSA hot spots.
  - d. Began moving impacted material from Phase 1 cells in the Eastern Fill Area into the Water Filled Excavation for the solidification of the sediment.
  - e. Began staging impacted material from the Water Filled Excavation into the Staging pile located in the Eastern Fill Area.
  - f. Continued dewatering activities in the Water Filled Excavation.
  - g. Installed berms and sumps in the Water Filled Excavation to control ground water and run-off from the wetlands.
3. Schedule (Week of April 9, 2012)
  - a. Continue water pumping activities as needed.

- b. Continue sampling on site backfill material in Containment Cell Area based on pending SSA closure.
  - c. Continue solidification of sediment in Water Filled Excavation Area as needed.
  - d. Continue removing impacted material from cells in the Eastern Fill Area phase 1 and the Water Filled Excavation and placing into Staging area.
  - e. Expand or close SSA hot spots, pending analytical review and approval.
- 4. Administrative Issues
- 5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA  
Middletown, NY  
Weekly Meeting  
Wednesday, April 18, 2012  
10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
    - i. Personal air monitoring
  - b. Decreasing level of respiratory protection- half face respirator
  - c. No near losses or incidents to report.
2. QA/QC
  - a. Completed the sampling of SSA hot spots – SSA1, SSA2, SSA11, SSA13, SSA32 and floor sample for SSA7.
  - b. Began sampling the floors in the excavation of the Water Filled Excavation- 20, 21, 22, 24, 25, 26, 28, 29, 30, 31, 33, 34, 35, 36, 38, 39, 40, and 42.
3. Progress Review (Week of April 9, 2012)
  - a. Continued excavation of the impacted material in the Water Filled Excavation.
  - b. Continued staging impacted material from the Water Filled Excavation into the Staging Pile located in the Eastern Fill Area.
  - c. Continued dewatering activities in the Water Filled Excavation.
  - d. Managed sumps in the Water Filled Excavation to control ground water.
  - e. Began the weaving tarps together to create a tarp large enough to cover the Staging pile.
4. Schedule (Week of April 16, 2012)
  - a. Complete excavation and sampling in the Water Filled Excavation.

- b. Continue water pumping activities as needed.
  - c. Continue removing impacted material from grids in the Eastern Fill Area.
  - d. Continue sampling site backfill material in Containment Cell Area based on pending SSA hot spot analytical.
  - e. Begin sampling excavated grids in the Easter Fill Area.
- 5. Administrative Issues
  - 6. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA  
Middletown, NY  
Weekly Meeting  
Wednesday, April 25, 2012  
10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. QA/QC
  - a. Completed sampling the floors in the Water Filled Excavation Area in Grids- 17, 18, 19, 23, 27, 32, 37 and 41.
  - b. Completed sampling the sidewalls in the Water Filled Excavation Area in Grids- 16, 20, 24, 28, 32, 37, and 41.
  - c. Completed sampling the floors and sidewalls in the Eastern Fill Area in Grids- 1, 2, 11, 12, 13, 14 and 15.
  - d. Completed the backfill sampling in the Containment Cell Area.
3. Progress Review (Week of April 16, 2012)
  - a. Continued excavation of the impacted material in the Eastern Fill Area.
  - b. Continued staging impacted material from the Eastern Fill Area into the Staging Pile located in the Eastern Fill Area.
  - c. Continued dewatering activities in the Water Filled Excavation.
  - d. Managed sumps in the Water Filled Excavation to control ground water.
  - e. Continued the weaving tarps together to create a tarp large enough to cover the Staging pile.

4. Schedule (Week of April 23, 2012)
  - a. Complete excavation and sampling in the Eastern Fill Area.
  - b. Continue water pumping activities as needed.
  - c. Re-excavate SSA2 hot spot.
  - d. Continue sampling excavated grids in the Eastern Fill Area.
  - e. Begin Backfilling in the Water Filled Excavation Area.
5. Administrative Issues
6. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, May 2, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. Organic Filters for excavation of Grid#10
  - c. No near losses or incidents to report.
2. QA/QC (Week of April 23, 2012)
  - a. Samples for excavated area 2983 sent to the lab
  - b. Samples for NYSDEC150x100x1 foot cut in the Containment Cell area sent to the lab
  - c. Sampled excavated grids in the Containment Cell Area
3. Progress Review (Week of April 23, 2012)
  - a. Continued dewatering activities in the Water Filled Excavation- Rain event
  - b. Managed sumps in the Water Filled Excavation to control ground water.
  - c. Completed the excavation of the Water Filled Excavation.
  - d. Continued the excavation of the grids located in the Eastern Fill Area
  - e. Continued staging impacted material from the Water Filled Excavation and the grids in the Eastern Fill Area into the Staging Pile.
  - f. Continued weaving tarps together to create a cover large enough to for the Staging pile.
  - g. Began excavating and transporting backfill to the Water Filled Excavation
4. Schedule (Week of April 30, 2012)
  - a. Complete the excavation and sampling of all grids in the Eastern Fill Area.

- b. Continue excavating and transporting backfill to the Water Filled Excavation.
  - c. Begin the excavation and sampling of SSA hotspots SSA-19, 20, 23
  - d. Continue water pumping activities as needed.
- 5. Administrative Issues
- 6. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, May 9, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. QA/QC (Week of April 30, 2012)
  - a. Completed Sampling the Grids in the Eastern Fill Area
  - b. Completed Sampling of SSA hotspots 19, 20, 23
  - c. Report analytical for DEC 100x150x1 foot grid.
  - d. Report analytical for 2983.
3. Progress Review (Week of April 30, 2012)
  - a. Continued dewatering activities in the Water Filled Excavation- Rain event.
  - b. Completed the excavation of all impacted material for Phase 1
  - c. Completed the sampling of all excavated areas
  - d. Completed covering the Staging Pile
  - e. Continued excavating and transporting back fill to the Water Filled Excavation
4. Schedule (Week of April 30, 2012)
  - a. Continue backfilling activities of the Water Filled Excavations
  - b. Begin the backfilling of the grids in the Eastern Fill area
5. Administrative Issues
6. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, May 16, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. QA/QC (Week of May 7, 2012)
  - a. Reviewed analytical for confirmation samples collected from excavated grids in the Eastern Fill Area.
  - b. Reviewed analytical for SSA hotspots 19, 20, 23.
3. Progress Review (Week of May 7, 2012)
  - a. Continued dewatering activities in the Water Filled Excavation- As needed
  - b. Continued backfilling activities in the Water Filled Excavation and Eastern Fill Area.
4. Schedule (Week of May 14, 2012)
  - a. Continue backfilling activities of the Water Filled Excavation Area
  - b. Continue backfilling activities in the Eastern Fill area
  - c. Excavate hot spots in SSA 19 and 23.
5. Administrative Issues
6. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA  
Middletown, NY  
Weekly Meeting  
Wednesday, May 23, 2012  
10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. QA/QC (Week of May 14, 2012)
  - a. Completed confirmation sampling in SSA Hot spots 19 and 23
3. Progress Review (Week of May 14, 2012)
  - a. Continued dewatering activities in the Water Filled Excavation- As needed
  - b. Continued backfilling activities in the Water Filled Excavation and Eastern Fill Area.
  - c. Completed backfilling in SSA hot spots 19, 20 and 23
4. Schedule (Week of May 21 , 2012)
  - a. Continue backfilling activities of the Water Filled Excavation Area
  - b. Continue backfilling activities in the Eastern Fill area
  - c. Backfill hot spots in SSA 19 and 23.
5. Administrative Issues
6. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, June 6, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of May 28, 2012)
  - a. Continued dewatering activities in the Water Filled Excavation- As needed
  - b. Continued backfilling activities in the Water Filled Excavation and Eastern Fill Area.
3. Schedule (Week of June 4 , 2012)
  - a. Continue backfilling activities of the Water Filled Excavation Area
  - b. Continue backfilling activities in the Eastern Fill area
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, June 13, 2012**  
**10:00 AM**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of June 4, 2012)
  - a. Continued dewatering activities in the Water Filled Excavation- As needed
  - b. Continued backfilling activities
  - c. Continued excavating and loading backfill material in the containment cell area.
3. Schedule (Week of June 11, 2012)
  - a. Continued excavating and loading backfill material in the containment cell area.
  - b. Continue backfilling activities
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, June 27, 2012**  
**2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of June 18, 2012)
  - a. Began grading the floor of the containment cell
  - b. Began building berms along perimeter of the containment cell
3. Schedule (Week of June 26, 2012)
  - a. Continue grading floor of the containment cell.
  - b. Continue shaping perimeter berm of the containment cell.
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, July 19, 2012**  
**2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of July 9, 2012)
  - a. Continued grading the floor of the containment cell
  - b. Continued building berms along perimeter of the containment cell
3. Schedule (Week of July 16, 2012)
  - a. Continue grading floor of the containment cell.
  - b. Continue shaping perimeter berm of the containment cell.
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, August 30<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of August 27, 2012)
  - a. Continued moving clean rock pile to triangle staging area for preparation of temporary access road
  - b. Continued rinsing construction debris and laying on poly in clean area
3. Schedule (Week of September 3, 2012)
  - a. Working on final grading of the containment cell floor.
  - b. Continue shaping perimeter berm of the containment cell.
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, September 6<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 3<sup>rd</sup>, 2012)
  - a. Continued working on sub grading of containment cell
  - b. Continued working on under drain pipe
  - c. Moving office trailers to South side of tree line in preparation for temporary access road.
  - d. Continued decon of debris and placing in clean staging area
3. Schedule (Week of September 10<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Began breaking large boulders in clean area and moving to triangle staging area
  - c. Began breaking bed rock/shale in underdrain trench
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, September 13<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 10<sup>th</sup>, 2012)
  - a. Continued working on sub grading of containment cell
  - b. Continued working on under drain trench
  - c. Surveying in temp road alignment
  - d. Breaking large clean boulders and moving to triangle area
  - e. Breaking underdrain rock/shale throughout underdrain trench
3. Schedule (Week of September 17<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Knob Hill update/approval
4. Administrative Issues
5. Open Discussion
  - a. Discuss recycle/disposal of tires

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, September 20<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 17<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Continue working on underdrain trench
  - c. Start breaking larger stockpiled boulders in CAMU 4 and Rock pile
  - d. Ecological survey for access road
3. Schedule (Week of September 24<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Start importing pea gravel for underdrain and installing pipe/As-built
  - c. Knob Hill update/approval
  - d. Start As-built of underdrain
  - e. Temp. road status
  - f. Clean certifications for pea gravel (underdrain), item 4 (type 2 materials for access road) and fine stone fill (for access road). Fine stone fill is visual only 3”-5” size rock
  - g. Load out tires for recycling
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA  
Middletown, NY  
Weekly Meeting  
Thursday, September 27<sup>th</sup>, 2012  
10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 17<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Continue working on underdrain trench
  - c. Knob Hill Scrape
  - d. Loaded tires to be taken to recycling plant
  - e. State visit for temporary road
  - f. Importing Pea Gravel for underdrain status?
3. Schedule (Week of September 24<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Continue working on underdrain
  - c. Start As-built of underdrain
  - d. Temp. road status
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, October 4<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of October 1st, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Completed 300' of subgrade on underdrain trench/As-built
  - c. Importing and placing pea gravel for underdrain
  - d. Installing underdrain pipe and geotextile
  - e. Collected Knob hill samples
  - f. XRF temp. road
3. Schedule (Week of October 8<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Continue working on underdrain and installation of pipe/geotextile/As-built
  - c. Continue importing and placing pea gravel
  - d. Begin construction of temp. road
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, October 12<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.

2. Progress Review (Week of October 8<sup>th</sup>, 2012)
  - a. Continue working on sub grade of containment cell
  - b. Completed 380' of underdrain pipe and placing pea gravel
  - c. Importing pea gravel to finish underdrain trench
  - d. Installing underdrain pipe and geotextile
  - e. Completed silt fence and orange fence along temp road

Schedule (Week of October 15<sup>th</sup>, 2012)

- f. Continue working on sub grade of containment cell/as-built
  - g. Continue working on completing underdrain and installation of pipe/geotextile/As-built
  - h. Expecting results from test pits on knob hill for soil reuse in CC
3. Administrative Issues
4. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, November 8<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of November 5<sup>th</sup>, 2012)
  - a. Continue working on final grade of bedding layer
  - b. Began working on temporary road; grading, laying fabric, placing type 2 sub base
  - c. Borbas will be shooting as-built finished grade for cushion layer
  - d. Borbas will also be shooting in phase 2b pond area and sample locations of temp road
  - e. Begin digging anchor trench for liner
  - f. Preparing for liner crew, ESI, to mobilize equipment and personnel

Schedule (Week of November 12<sup>th</sup>, 2012)

  - g. ESI will begin installing containment cell liner
  - h. Continue working on temp road
  - i. Continue to bring in type 2 sub base and fine stone fill for temp road
3. Administrative Issues
4. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, November 29th, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of Nov 26th, 2012)
  - a. Completion of Containment Cell Liner
  - b. Began importing protective layer
  - c. Began soil consolidation, CAMU's 1 & 2
  - d. Completing temp road pending permit
3. Schedule (Week of Dec 3rd, 2012)
  - a. Continue importing protective layer
  - b. Continue soil consolidation, CAMU's 1 & 2
  - c. Completing temp road pending permit
  - d. Install leachate manhole in containment cell
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA  
Middletown, NY  
Weekly Meeting  
Wednesday, December 5<sup>th</sup>, 2012  
10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of December 3rd, 2012)
  - a. Install leachate manhole and have surveyor as-built it
  - b. Continue to import protective layer for CC
  - c. Finish soil consolidation, CAMU's 1 & 2 for treating area
  - d. Completing temp road pending permit
3. Schedule (Week of Dec 10th, 2012)
  - a. Continue importing protective layer
  - b. Begin pilot test
  - c. Completing temp road pending permit
  - d. Install gate at 211 entrance pending completion of temp road
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 1 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, December 12<sup>th</sup>, 2012**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of December 10<sup>th</sup>, 2012)
  - a. Began pilot test (3) 250CY piles
  - b. Continue to import protective layer for CC
  - c. Installing gate at 211 Temp Road entrance on Saturday the 15th
  - d. Complete temp road up to concrete road cut-off
3. Schedule (Week of Dec 17th, 2012)
  - a. Continue importing protective layer
  - b. As-Built protective layer
  - c. Continue treating material
  - d. Preparing for Christmas break shut-down
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, December 20<sup>th</sup>, 2012**  
**9:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of December 17<sup>th</sup>, 2012)
  - a. Continue importing protective layer
  - b. As-Built Protective Layer
  - c. XRF and Excavate SSA-29
  - d. Initial 1' scrape on knob hill for haul road
  - e. Prepare for Christmas break shut-down
3. Schedule (Dec 22<sup>nd</sup> – January 6<sup>th</sup>)
  - a. Christmas Break
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Monday, January 7<sup>th</sup>, 2013**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of January 7<sup>th</sup>, 2012)
  - a. Check all erosion and control measures around site
  - b. Unload and cover reagent from Premier
  - c. Bringing in rip rap to build rumble pad for Temp Road
  - d. Start treating material again
  - e. Finish haul road to containment cell
  - f. Start hauling material into cell
3. Schedule (Week of January 14<sup>th</sup>)
  - a. Continue treating material
  - b. Begin bringing in reagent in bulk this month
  - c. Continue to haul material into cell
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 2 RA  
Middletown, NY  
Weekly Meeting  
Thursday, January 17<sup>th</sup>, 2013  
10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of January 14<sup>th</sup>, 2012)
  - a. Continue treating material
  - b. Pending results from samples, move treated material into CC
  - c. Build haul road from treatment pad to CC
  - d. Continue pumping water in CC from snow/rain
  - e. Once treated material is in CC, pump any snow/rain water into RSR storm tanks
  - f. Move more dirty material into treatment pad to be treated
  - g. Segregate debris and rock from CAMU 4
3. Schedule (Week of January 21<sup>st</sup>)
  - a. Continue treating material
  - b. Begin bringing in reagent in bulk this month
  - c. Continue to haul material into cell
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, January 24<sup>th</sup>, 2013**  
**10:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of January 21<sup>st</sup>, 2013)
  - a. Continue treating material
  - b. Continue moving treated material into containment cell as piles pass
  - c. Continue pumping water in CC from snow/rain
  - d. Continue moving material into treatment pad as piles pass/moved to CC
3. Schedule (Week of January 28<sup>th</sup>)
  - a. Continue treating material
  - b. Continue to haul material into cell
  - c. Continue moving material into treatment pad as piles pass/moved to CC
4. Administrative Issues
5. Open Discussion
6. Notes

Treated piles PSV1 and PSV2 used on floor of treatment pad  
PSV3-PSV12 all have passed and been moved into CC  
PSV13-PSV23 waiting for results  
No failures or retreats



**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, January 31<sup>th</sup>, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of January 28<sup>th</sup>, 2013)
  - a. Continue treating impacted material
  - b. Continue moving treated material into containment cell as piles pass
  - c. Continue pumping water in CC from snow/rain events to RSR storm tanks
  - d. Continue moving impacted material into treatment pad as passing treated piles are moved to CC
3. Schedule (Week of February 4<sup>th</sup>, 2013)
  - a. Continue treating impacted material
  - b. Continue moving treated material into containment cell as piles pass
  - c. Continue moving impacted material into treatment pad as passing treated piles are moved to CC
  - d. Continue pumping water in CC from rain/snow events to RSR storm tanks
4. Administrative Issues
5. Open Discussion
6. Notes

As of 1/30/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad

PSV3-PSV22 all have passed and been moved into CC  
PSV23-PSV33 waiting for results

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, February 7, 2013<sup>th</sup>**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of February 4<sup>th</sup>, 2013)
  - a. Continue treating impacted material
  - b. Continue moving treated material into containment cell as piles pass
  - c. Continue pumping water in CC from snow/rain events to RSR storm tanks
  - d. Continue moving impacted material into treatment pad as passing treated piles are moved to CC
3. Schedule (Week of February 11<sup>th</sup>, 2013)
  - a. Continue treating impacted material
  - b. Continue moving treated material into containment cell as piles pass
  - c. Continue moving impacted material into treatment pad as passing treated piles are moved to CC
  - d. Continue pumping water in CC from rain/snow events to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - a. Temporary shutdown
6. Notes

As of 2/7/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad

PSV3-PSV35 all have passed and been moved into CC

PSV36-PSV42 waiting for results

PSV-24 retreat results pending

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, February 14, 2013<sup>th</sup>**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of February 11<sup>th</sup>, 2013)
  - a. Continue treating impacted material
  - b. Continue moving treated material into containment cell as piles pass
  - c. Continue pumping water in CC from snow/rain events to RSR storm tanks
  - d. Continue moving impacted material into treatment pad as passing treated piles are moved to CC
  - e. Preparing for temp. shutdown
3. Schedule (Week of February 18<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
4. Administrative Issues
5. Open Discussion
  - a. Temporary shutdown
  - b. Disposal of PPE
6. Notes

As of 2/12/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV41 all have passed and been moved into CC  
PSV-42 passed and is in treatment pad waiting to be moved into CC  
PSV43-PSV53 waiting for results

PSV-24 retreat passed and was placed in CC on 2/9/13

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, February 21<sup>st</sup>, 2013<sup>th</sup>**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of February 18<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Covering stock pile with poly as necessary
3. Schedule (Week of February 25<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
4. Administrative Issues
5. Open Discussion
  - a. Anticipated return date.
  - b. Weather next week
6. Notes

As of 2/12/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV55 all have passed and been moved into CC

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, February 28<sup>st</sup>, 2013<sup>th</sup>**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of February 25<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Covering stock pile with poly as necessary
3. Schedule (Week of March 4<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
4. Administrative Issues
5. Open Discussion
  - a. Anticipated return date.
  - b. Weather Forecast
6. Notes

As of 2/12/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV55 all have passed and been moved into CC



**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, March 7<sup>th</sup>, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of March 4<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Resumed treating material, loading from stock pile and placing material in treatment pad
  - d. Placing treated material into CC as pile results pass
3. Schedule (Week of March 11<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
  - c. Continue treating material
  - d. Continue placing material into CC as pile results pass
4. Administrative Issues
5. Open Discussion
6. Notes

As of 2/12/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV55 all have passed and been moved into CC  
PSV56-58 were treated and sampled on 3/5/13  
PSV59-63 will be treated and sampled on 3/6/13

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, March 14<sup>th</sup>, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of March 11<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Continue treating material, loading from stock pile and placing material in treatment pad
  - d. Placing treated material into CC as pile results pass
3. Schedule (Week of March 18<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
  - c. Continue treating material
  - d. Continue placing material into CC as pile results pass
4. Administrative Issues
5. Open Discussion
6. Notes

As of 2/12/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV58 all have passed and been moved into CC  
PSV59-70 have passed and are being moved into CC.  
PSV71-73 have been treated and are waiting for results.

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, March 21<sup>st</sup>, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of March 18<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Continue treating material, loading from stock pile and placing material in treatment pad
  - d. Placing treated material into CC as pile results pass
3. Schedule (Week of March 25<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
  - c. Continue treating material
  - d. Continue placing material into CC as pile results pass
4. Administrative Issues
5. Open Discussion
6. Notes

As of 2/12/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV73 all have passed and been moved into CC  
PSV74-88 have been treated and are waiting for results.

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, March 28<sup>th</sup>, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of March 25<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Continue treating material, loading from stock pile and placing material in treatment pad
  - d. Placing treated material into CC as pile results pass
  - e. Possibly install 700' of 2" HDPE from CC to RSR Storm Tanks
3. Schedule (Week of April 1<sup>st</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
  - c. Continue treating material
  - d. Continue placing material into CC as pile results pass
4. Administrative Issues
5. Open Discussion
6. Notes

As of 2/12/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV103 all have passed and been/will be moved into CC by end of day today  
PSV104-107 have been treated and are waiting for results.

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, April 4<sup>th</sup>, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of April 1<sup>st</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Continue treating material, loading from stock pile and placing material in treatment pad
  - d. Placing treated material into CC as pile results pass
  - e. Install 700' of 2" HDPE from CC to RSR Storm Tanks
  - f. Bring in Crusher and Excavator with hammer to crush rocks.
3. Schedule (Week of April 11<sup>th</sup>, 2013)
  - a. Pump rain water/snow from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
  - c. Continue treating material
  - d. Continue placing material into CC as pile results pass
  - e. Continue to crush rocks
4. Administrative Issues
5. Open Discussion
6. Notes

As of 4/3/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad

PSV3-PSV119 all have passed and been/will be moved into CC by end of day today

PSV120-123 have been treated and are waiting for results.

PSV-108 failed for Pb over the limit. It has been retreated and is waiting results.

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, April 18<sup>th</sup>, 2013**  
**11:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain/snow events
  - b. No near losses or incidents to report.
2. Progress Review (Week of April 15th, 2013)
  - a. Pump rain water from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Continue treating material, loading from stock pile and placing material in treatment pad
  - d. Placing treated material into CC as pile results pass
  - e. Complete crushing rock and stockpile it
3. Schedule (Week of April 22nd, 2013)
  - a. Pump rain water from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
  - c. Continue treating material
  - d. Continue placing material into CC as pile results pass
  - e. Prepare for WESP Excavation
4. Administrative Issues
5. Open Discussion
6. Notes

As of 4/18/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV138 all have passed and been moved into CC.  
PSV139-147 have been treated and are waiting for results.



**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, April 25th, 2013**  
**11:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of April 22nd, 2013)
  - a. Pump rain water from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls/BMP's
  - c. Continue treating remaining waste material, loading from final remaining piles and placing material in treatment pad
  - d. Placing treated material into CC as pile results pass
  - e. Completed crushing rock
3. Schedule (Week of April 29<sup>th</sup>, 2013)
  - a. Pump rain water from CC to RSR storm tanks
  - b. Check silt fence and all erosion/sediment controls
  - c. Finish treating any remaining waste material
  - d. Continue placing material into CC as pile results pass
  - e. Begin WESP Excavation
4. Administrative Issues
5. Open Discussion
6. Notes

As of 4/24/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad

PSV3-PSV151 all have passed and been moved into CC.

PSV152-162 have been treated and are waiting for results.

Total material left to treat is around 3,750CY.

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 2, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring – Affected by rain events
  - b. No near losses or incidents to report.
2. Progress Review (Week of April 29, 2013)
  - a. Continue to pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Completed treatment of Phase 2A impacted stockpile 4/27/13
  - d. Continued placing treated material in CC
  - e. Began WESP excavation and hauling material to impacted stockpile area
  - f. Move the last of Phase 2A treated material into CC into containment cell
  - g. Import protective layer for CC
3. Schedule (Week of May 6, 2013)
  - a. Continue to manage water/pump from CC to RSR storm tanks
  - b. Continue to manage erosion controls/BMP's
  - c. Continue WESP excavation
  - d. Treat WESP impacted excavated soils and place in CC as they pass
  - e. Place imported protective layer on CC slope
4. Administrative Issues
5. Open Discussion

Rock is ok for reuse in Eastern fill area?

6. Notes

As of 5/1/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV167 all have passed and been moved into CC.

PSV168-177 has been treated and waiting for results.

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 9, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of May 6, 2013)
  - a. Continue to pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Completed WESP excavation. Waiting for verification samples from lab
  - d. Treating WESP soil and placing into CC as piles pass
  - e. Completed installing remaining protective layer on the Northeast slope of CC
3. Schedule (Week of May 13, 2013)
  - a. Continue to manage water/pump from CC to RSR storm tanks
  - b. Continue to manage erosion controls/BMP's
  - c. Complete moving last of WESP treated soil into CC
  - d. Backfill WESP excavation/pending verification results
4. Administrative Issues
5. Open Discussion
6. Notes

As of 5/7/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad  
PSV3-PSV177 all have passed and been moved into CC.  
PSV178-188 has been treated and waiting for results.

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 16, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of May 13, 2013)
  - a. Continue to pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Completed WESP excavation and treatment of soil
  - d. Begin backfilling WESP excavation/pending results
3. Schedule (Week of May 20, 2013)
  - a. Continue to manage water/pump from CC to RSR storm tanks
  - b. Continue to manage erosion controls/BMP's
  - c. Continue backfilling WESP if needed
4. Administrative Issues
5. Open Discussion-Phase2B status?
6. Notes

As of 5/15/13

Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad

PSV3-PSV192 all have passed and been moved into the Containment cell

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 23, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of May 20, 2013)
  - a. Continue to pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Completed WESP backfilling both EAST and WEST sides 5/20/13
  - d. Begin Phase 2B excavation in grids 44-114
  - e. Mixed bentonite with clean soil for backfill (completed 5/21/13) bentonite soil has not been placed as yet
  - f. Pressure washing/deconing tires and metal
  - g. Pressure washing/deconing boulders
3. Schedule (Week of May 27, 2013)
  - a. Continue to manage water/pump water from CC to RSR storm tanks
  - b. Continue to manage erosion controls/BMP's
  - c. Continue Phase 2B excavation in grids 44-114
  - d. Backfill Phase 2B excavation in grids excavated/pending confirmation results
4. Administrative Issues
5. Open Discussion- Crushed rock reuse/backfill?
6. Notes-As of 5/15/13 Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad. WESP piles 178-192. PSV3-PSV192 all have passed and been moved into the Containment cell

**Revere Smelting & Refining Site, OU1, Phase 2 RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 30, 2013**  
**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of May 27, 2013)
  - a. Continue to pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Begin excavation of grids 44 working south 5/28
  - d. Pressure washing/deconing tires and metal
  - e. Pressure washing/deconing tires and metal
3. Schedule (Week of May 27, 2013)
  - a. Continue to manage water/pump water from CC to RSR storm tanks
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in Eastern fill area grids 44-114
  - d. Backfill Phase 2B excavation in grids excavated/pending confirmation results
  - e. Pressure washing/deconing tires and metal
  - f. Pressure washing/deconing tires and metal
4. Administrative Issues
5. Open Discussion- Crushed rock reuse/backfill?
6. Notes-As of 5/30/13 Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad.



WESP piles 178-192. PSV3-PSV192 all have passed and been moved into the Containment cell.

Eastern fill piles start at 193-Pile 193,194,195,196,197,198,199 and 200 treated and waiting results

**Revere Smelting & Refining Site, OU1, Phase 2 RA  
Middletown, NY  
Weekly Meeting**

**Thursday, June 6, 2013**

**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of June 6, 2013)
  - a. Continue to pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 44-114 (Eastern fill area )
  - d. Continue pressure washing large rocks
  - e. Continue treatment of Eastern fill soil
  - f. Hauling treated material to CC as pile pass
3. Schedule (Week of June 10, 2013)
  - a. Continue to manage water/pump water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in Eastern fill area grids 44-114 Eastern fill area)
  - d. Backfill Phase 2B excavation/grids excavated/pending confirmation results. Backfill with knob hill soil. Offsite source info coming
  - e. Continue pressure washing large rocks from excavated grids 44-114
  - f. Load lead buttons in RSR roll off box
4. Administrative Issues
5. Open Discussion

6. Notes-As of 6/5/13 Treated piles PSV1, PSV2 and PSV18 used on floor of treatment pad.

PSV3-PSV192 all have passed and been moved into the Containment cell. WESP pile 172-198

Eastern fill grids excavated and waiting verification. Eastern fill pile start at 193

44,45,46,47,48,49,52,53,54,55,58,59,60,61,64,65,66,67,68,114,113,112,111,110,108,109,105,106,  
125

Pile 193-198 have passed and will be moved into treatment cell 194-207 waiting for results.

**Revere Smelting & Refining Site, OU1, Phase 2 RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, June 12, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of June 10, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 44-114 (Eastern fill area )
  - d. Continue pressure washing large rocks
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated material to CC as piles pass
  - g. Continue loading lead buttons into RSR roll-off box
3. Schedule (Week of June 17, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in Eastern fill area grids 44-114 ( Eastern fill area)
  - d. Backfill confirmed clean grids. Approximately 400cy left of Knob hill to use then offsite soil will be imported
  - e. Continue pressure washing large rocks from excavated grids 44-114
  - f. Continue to load lead buttons in RSR roll-off box
  - g. Continue treatment of Eastern fill soil
  - h. Continue hauling treated piles to CC as piles pass

4. Administrative Issues

5. Open Discussion

6. Notes-As of 6/11/13 Eastern fill grids that have passed 44, 45, 46, 49, 53, 54, 55, 59, 61, 103, 104, 107, 18B. Waiting for result on 47, 58, 60, 64, 65, 64, 65, 66, 67, 68, 105, 108, 109, 110, 111, 112, 113, 114

Piles 208-217 have been treated and waiting results

Grids 48, 52 and 60 failed and need to be cleaned up

PSV3-PSV207 is in the Containment cell. Waiting on results for PSV208-PSV215

**Revere Smelting & Refining Site, OU1, Phase 2 RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, June 19<sup>th</sup>, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of June 17, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 44-114 (Eastern fill area )
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue loading lead buttons into RSR roll-off box, we are around half way as of this morning.
  - g. Continue pressure-washing rocks we pull out of excavation grids.
3. Schedule (Week of June 24, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in Eastern fill area grids 44-114 ( Eastern fill area)
  - d. Backfill confirmed clean grids. Approximately 400cy left of Knob hill to use then offsite soil will be imported
  - e. Continue pressure washing large rocks from excavated grids 44-114
  - f. Continue to load lead buttons in RSR roll-off box if not complete
  - g. Continue treatment of Eastern fill soil

- h. Continue hauling treated piles to CC as piles pass
- 4. Administrative Issues
- 5. Open Discussion
- 6. Notes-As of 6/19/13 Eastern fill grids that have passed 44, 45, 46, 49, 53, 54, 55, 59, 61, 103, 104, 107, 18B. Waiting for result on 47, 58, 60, 64, 65, 64, 65, 66, 67, 68, 105, 108, 109, 110, 111, 112, 113, 114

Piles 208-218 have been confirmed cleaned and are being placed in the CC

Pile 219 failed and is being retreated

Grids 48, 52 and 60 have been re-scrapped and are waiting on results.

PSV3-PSV211 is in the Containment cell. PSV212-218 is being moved into the CC today.

**Revere Smelting & Refining Site, OU1, Phase 2 RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, June 26<sup>th</sup>, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of June 24, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 76-106 (Eastern fill area )
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue loading lead buttons into RSR roll-off box, very close to completion
  - g. Continue pressure-washing large rocks.
  - h. Begin brining in fill for Eastern fill area
3. Schedule (Week of July 1st, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in Eastern fill area grids 76-106 ( Eastern fill area)
  - d. Continue pressure washing large rock
  - e. Continue to load lead buttons in RSR roll-off box if not complete
  - f. Continue treatment of Eastern fill soil
  - g. Continue hauling treated piles to CC as piles pass



h. Prepare for 4<sup>th</sup> of July Shut-Down

4. Administrative Issues

5. Open Discussion

6. Notes-As of 6/25/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 103 thru 105, 18B, 107 thru 114 Waiting on results for grids 71 thru 75.

Piles PSV219, PSV-227 thru PSV-240 have been treated and waiting on results

PSV3-PSV226 have all been treated and placed in CC excluding 219.


**EASTERN  
FILL AREA**

**SOIL  
PILE 2**


**SOIL  
PILE 3**

**WETLANDS  
BOUNDARY**

**RAILROAD  
POND**

SAMPLED =   
PASSED =   
Re-Scrape = 

**EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTH END OF CURRENT**

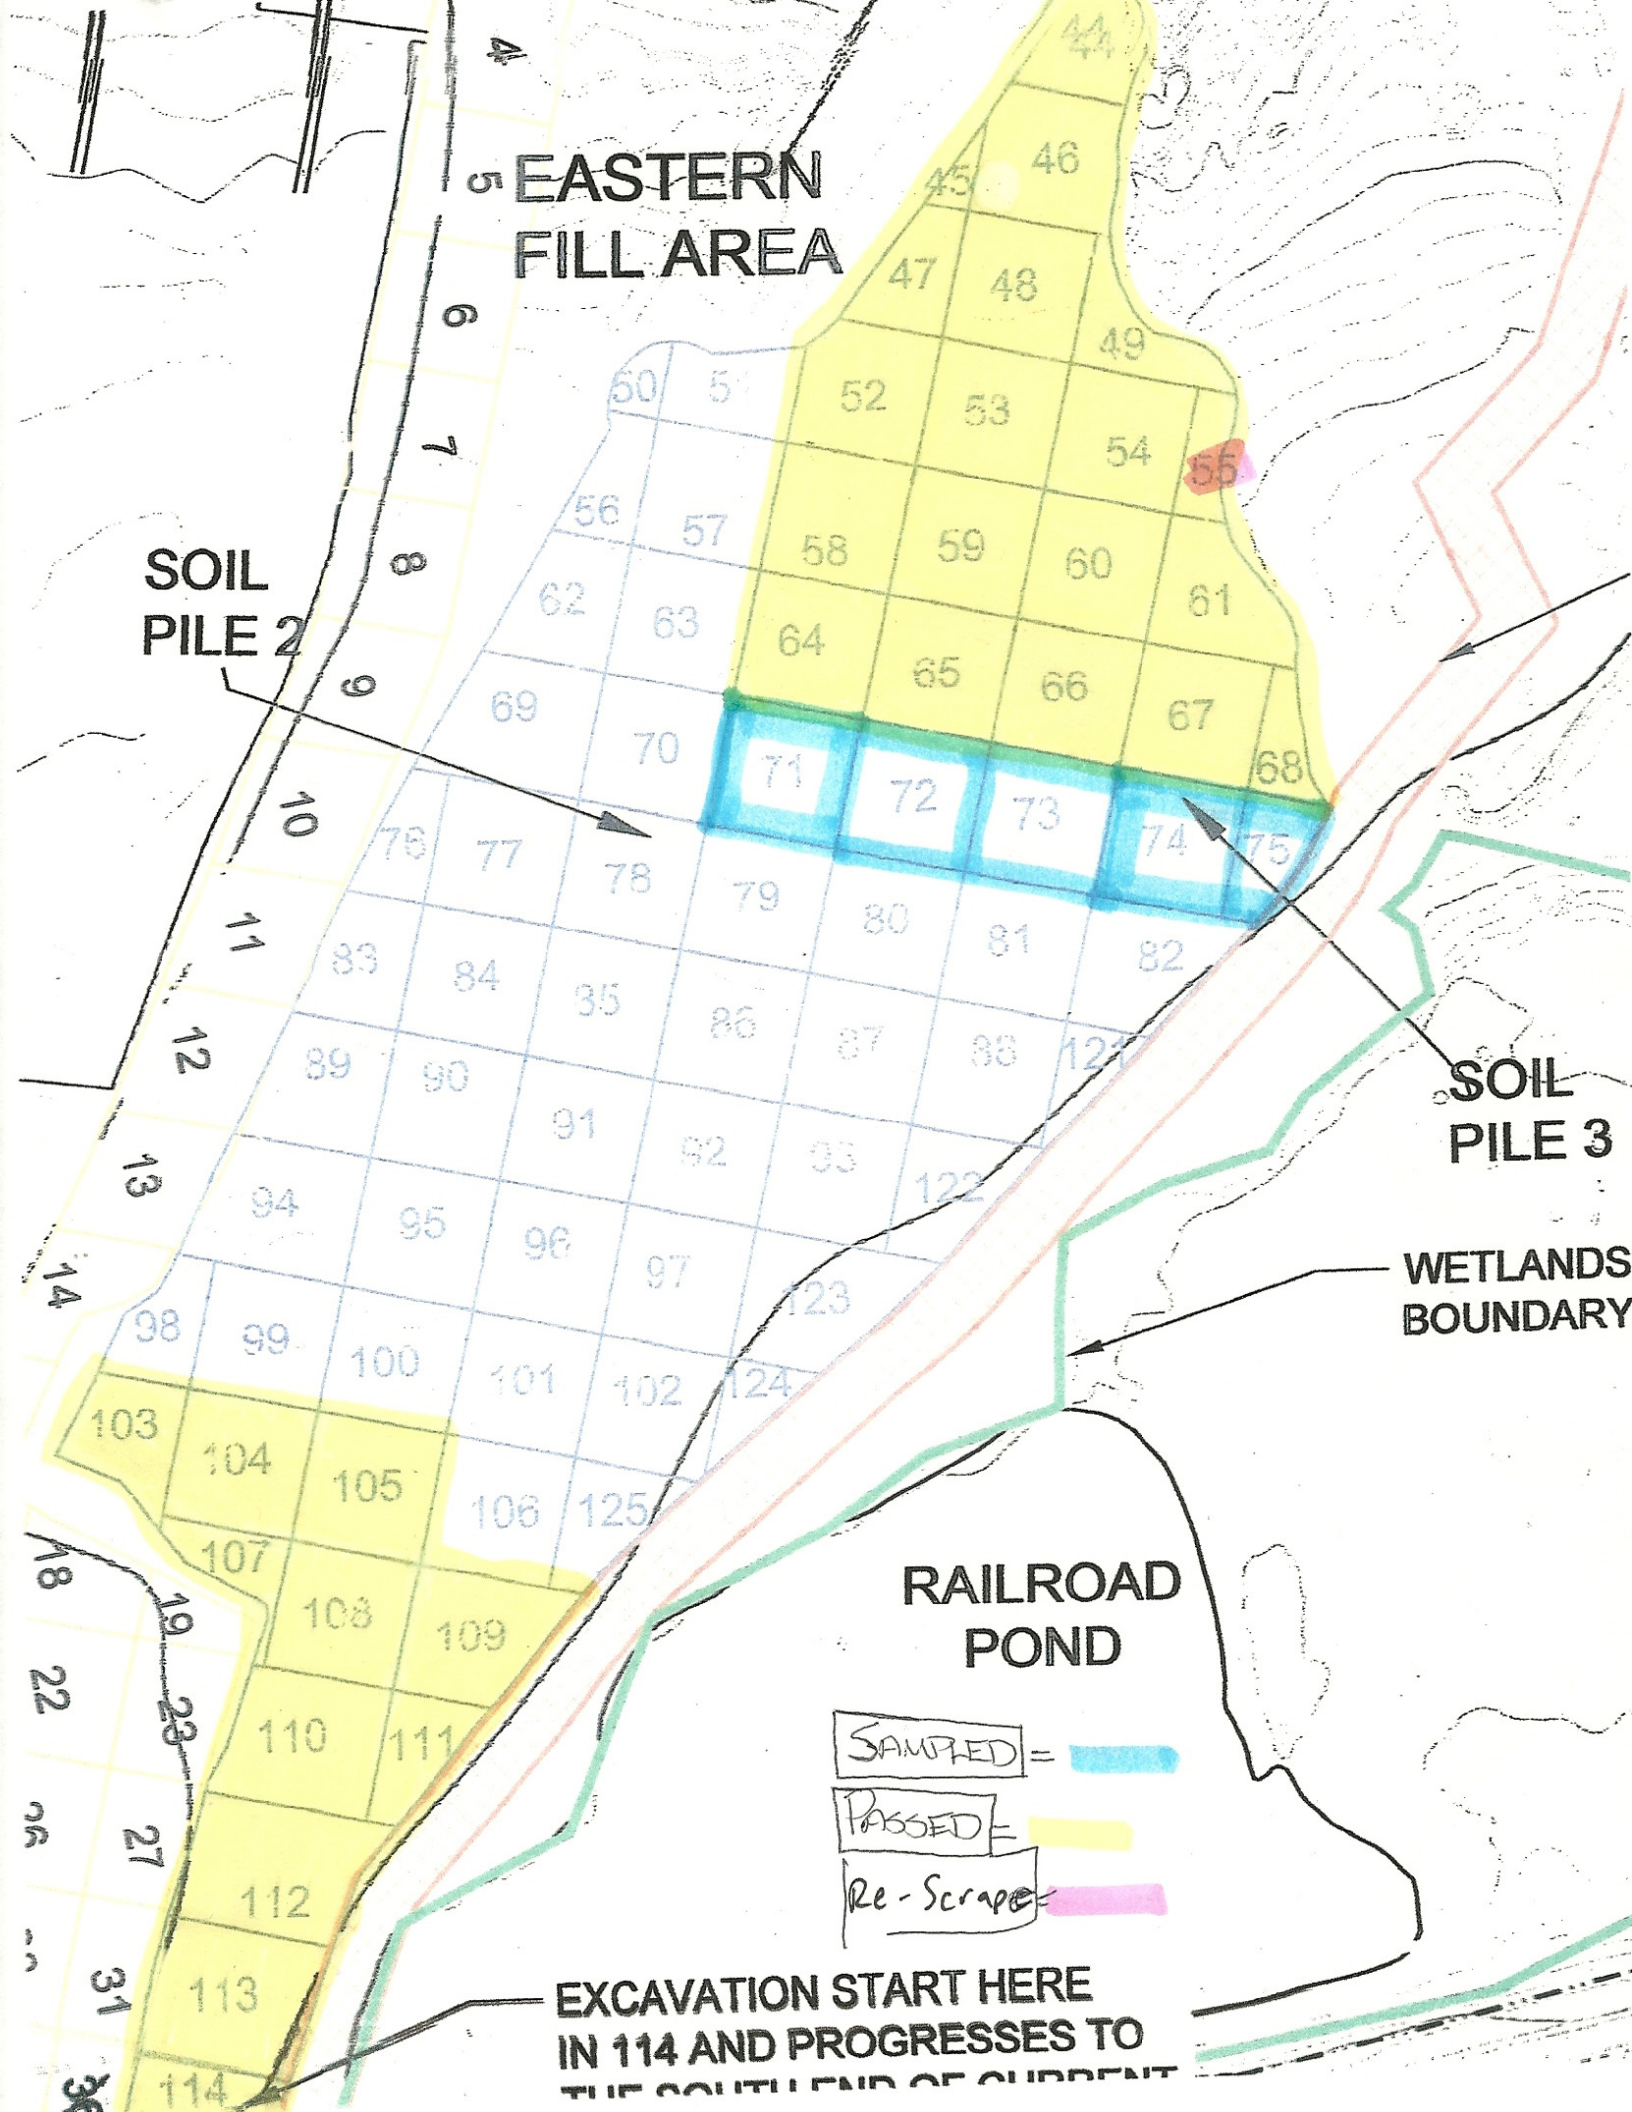

**Revere Smelting & Refining Site, OU1, Phase 2B RA**

**Middletown, NY**

**Weekly Meeting**

**Wednesday, July 10th, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of July 8th, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 76-106 (Eastern fill area ) Approx. 40 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue loading lead buttons into RSR roll-off box
  - g. Continue pressure-washing large rocks.
  - h. Continue brining in fill for Eastern fill area
3. Schedule (Week of July 15th, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in grids 76-106 ( Eastern fill area) Approx. 40 grids left to excavate
  - d. Continue pressure-washing large rocks.
  - e. Continue to load lead buttons in RSR roll-off box if not completed
  - f. Continue treatment of Eastern fill soil

g. Continue hauling treated piles to CC as piles pass

4. Administrative Issues

5. Open Discussion

6. Notes-As of 7/10/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 103 thru 105, 18B, 107 thru 114 and 71 thru 75.

Piles PSV-241PSV-247 has been treated and waiting on results.

PSV3-PSV240 have all been treated and placed in CC.




# EASTERN FILL AREA


SOIL  
PILE 2


SOIL  
PILE 3

WETLANDS  
BOUNDARY


RAILROAD  
POND

 = SAMPLED

 = PASSED

 = FAILED

EXCAVATION START HERE  
IN 114 AND PROGRESSES TO

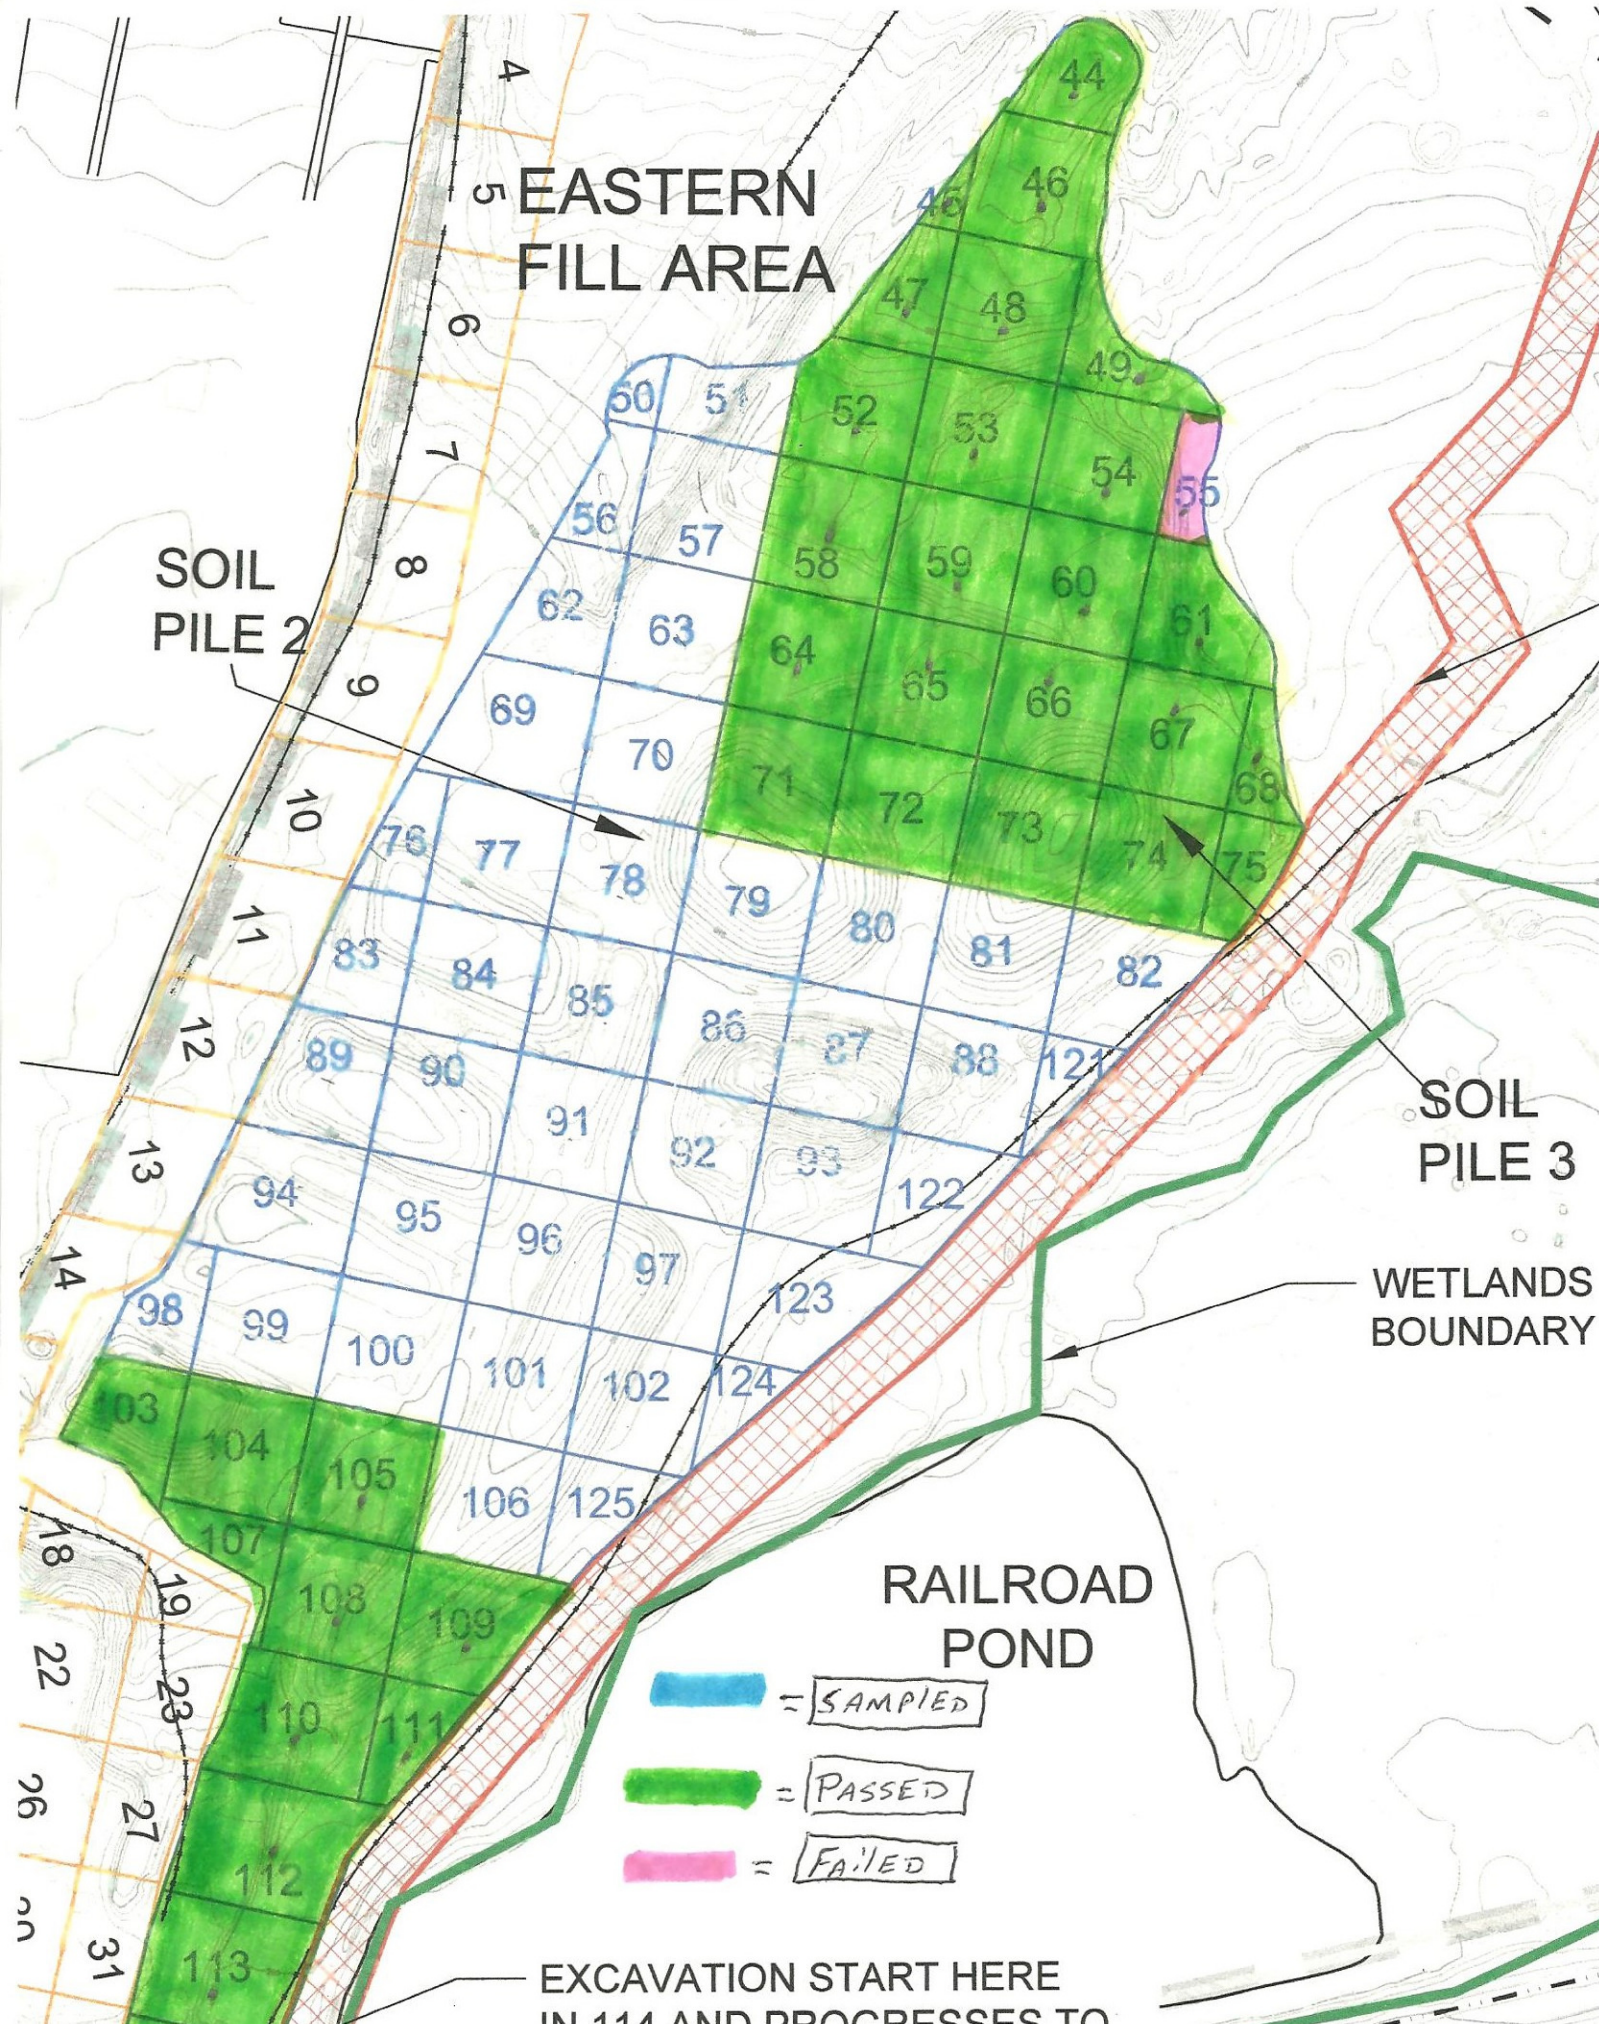

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, July 17th, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

Meeting Agenda:

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of July 15th, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 76-106 (Eastern fill area) Approx. 30 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue loading lead buttons into RSR roll-off box
  - g. Continue pressure-washing large rocks.
  - h. Continue brining in fill for Eastern fill area
3. Schedule (Week of July 22<sup>nd</sup>, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in grids 76-106 (Eastern fill area)
  - d. Continue pressure-washing large rocks.
  - e. Continue to load lead buttons in RSR roll-off box if not completed
  - f. Continue treatment of Eastern fill soil
  - g. Continue hauling treated piles to CC as piles pass

4. Administrative Issues
5. Open Discussion
6. Notes-As of 7/17/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 103 thru 105, 18B, 107 thru 114 and 71 thru 75.

Piles PSV-248-PSV-255 have been treated and verified clean. They all will be moved into CC by end of day today.

PSV3-PSV247 have all been treated and placed in CC.

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, July 24th, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of July 22<sup>nd</sup>, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 76-101 (Eastern fill area) Approx. 29 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue loading lead buttons into RSR roll-off box
  - g. Continue pressure-washing large rocks.
  - h. Continue brining in fill for Eastern fill area
3. Schedule (Week of July 29th, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in grids 76-101 (Eastern fill area)
  - d. Continue pressure-washing large rocks.
  - e. Continue to load lead buttons in RSR roll-off box if not completed
  - f. Continue treatment of Eastern fill soil
  - g. Continue hauling treated piles to CC as piles pass



4. Administrative Issues
5. Open Discussion
6. Notes-As of 7/22/13 Eastern fill grids that have passed 44 thru 49, 52 thru 54, 58 thru 61, 64 thru 68, 102 thru 106, 18B, 107 thru 114, 71 thru 75, 81, 82, 88, 121 thru 123 and 125.

Grid 97 and 55 have been re-scraped and sampled.

Grid 93 has been sampled waiting on results.

Piles PSV-256-PSV-270 have been treated and waiting on results.

PSV3-PSV-255 have all been treated and placed in CC.




# EASTERN FILL AREA

SOIL  
PILE 2


SOIL  
PILE 3

WETLANDS  
BOUNDARY

RAILROAD  
POND

-  = SAMPLED
-  = PASSED
-  = FAILED

EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTH END OF CURRENT

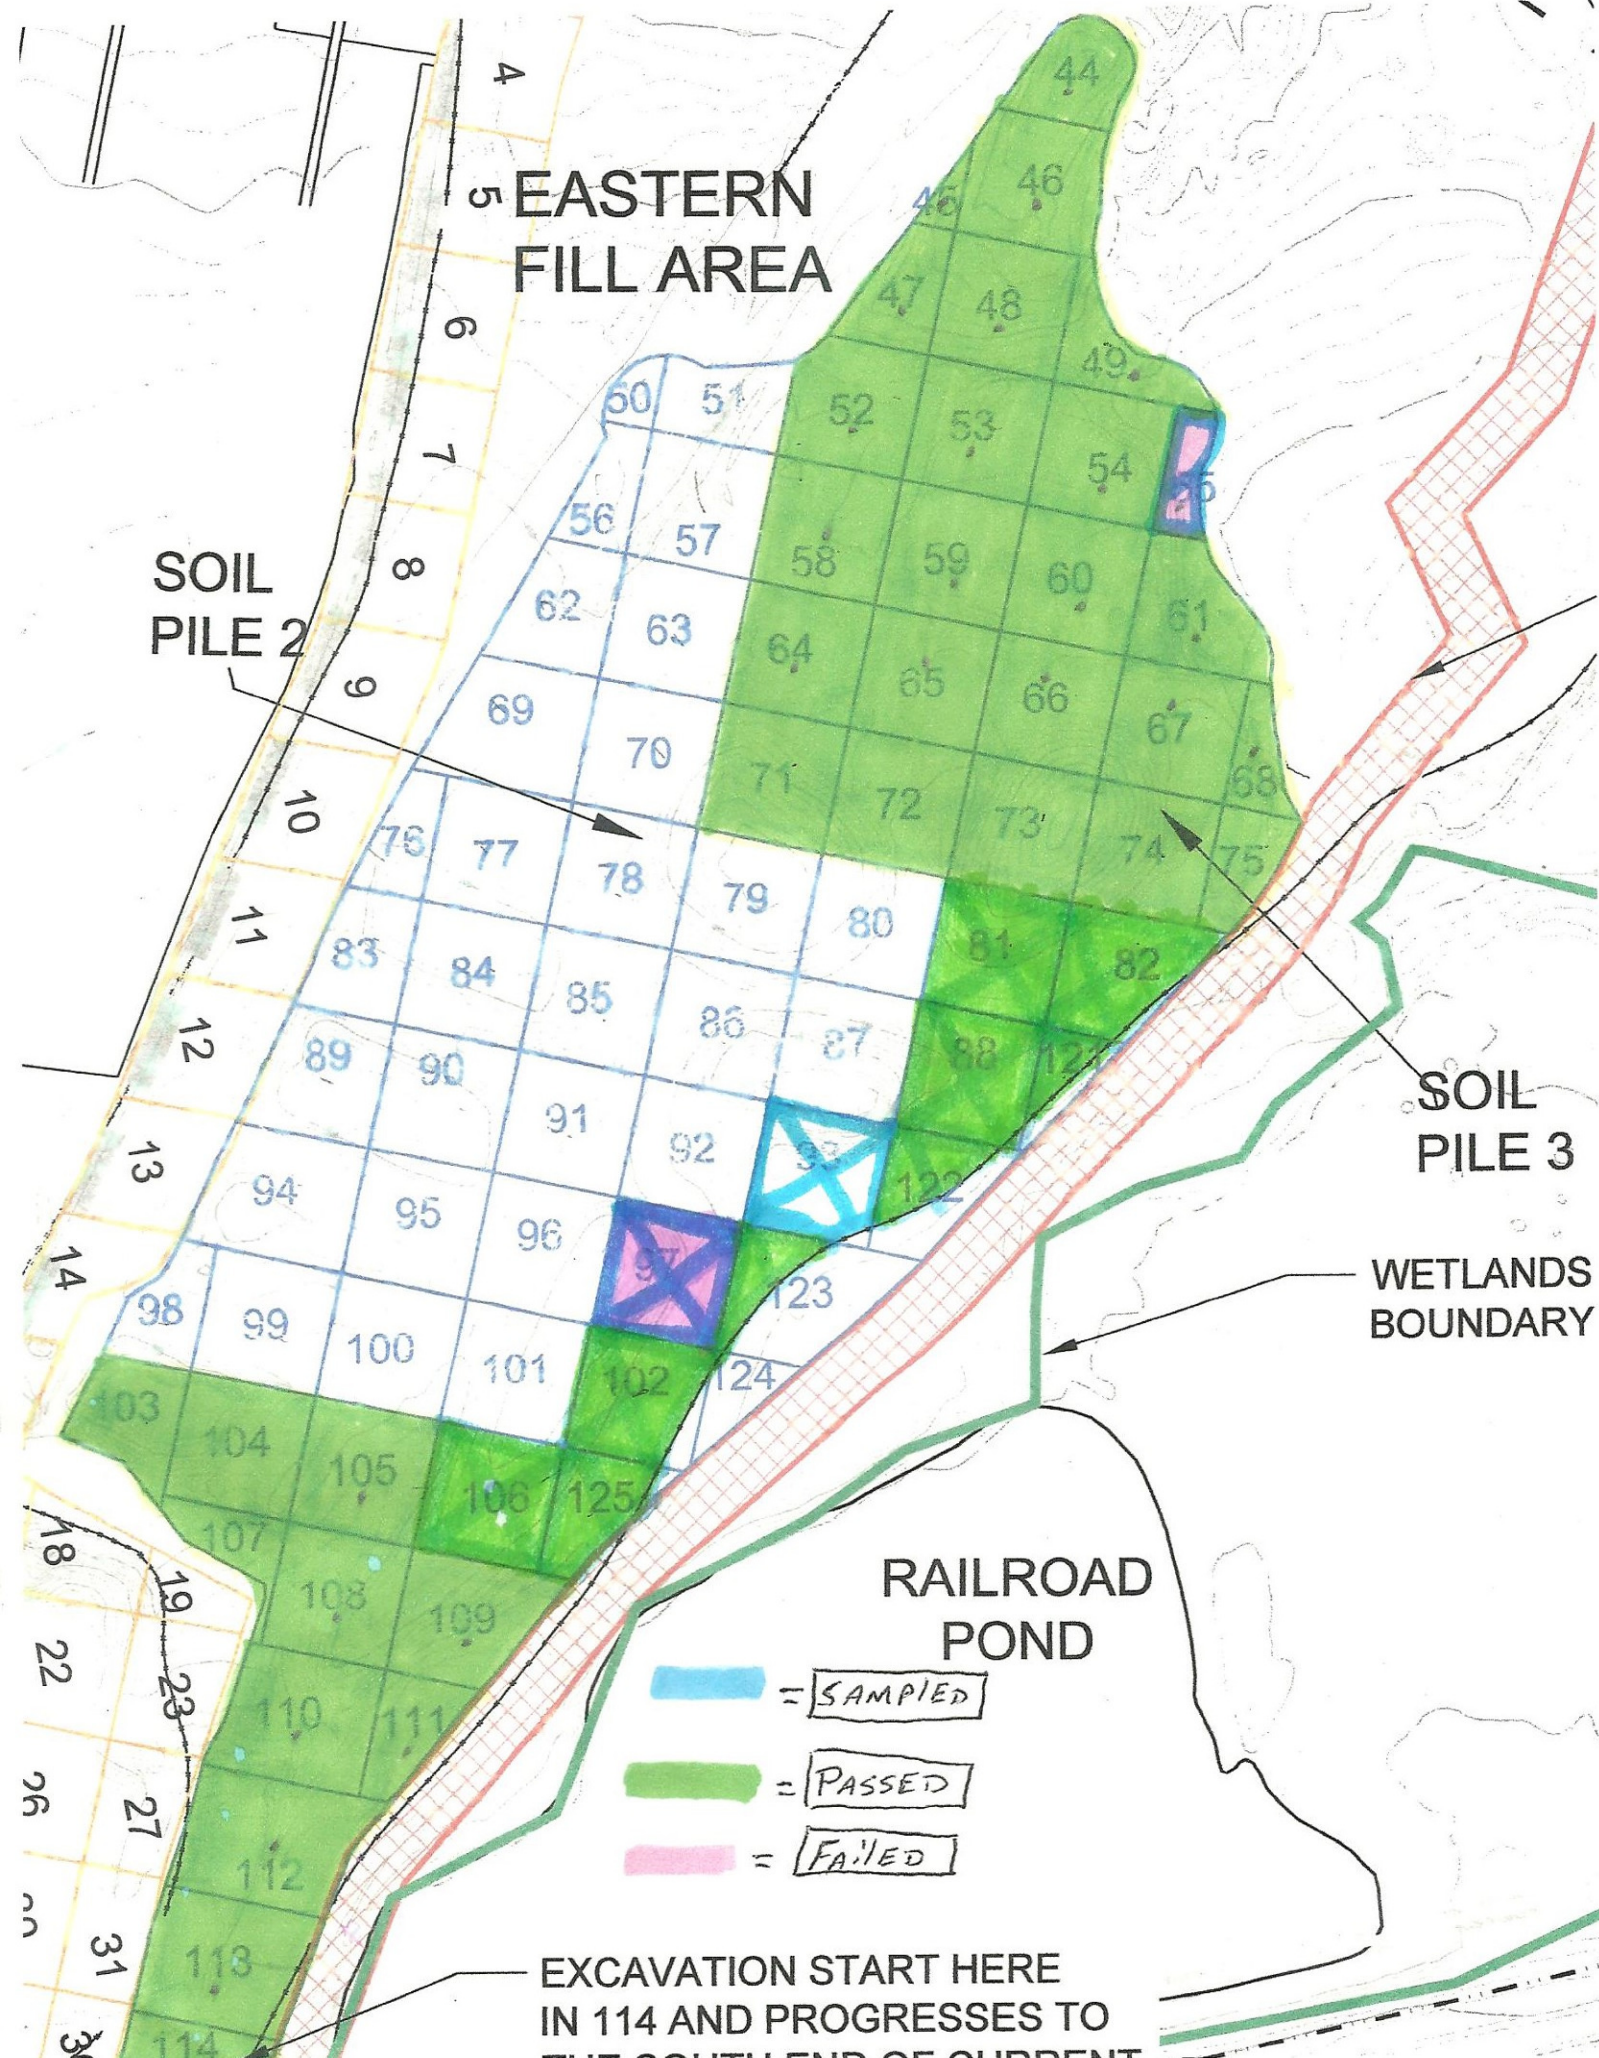

**Revere Smelting & Refining Site, OU1, Phase 2B RA**

**Middletown, NY**

**Weekly Meeting**

**Wednesday, July 31th, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317


Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of July 29<sup>th</sup>, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 50-101 (Eastern fill area) Approx. 24 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks.
  - g. Loaded metal box with clean metal from excavations
3. Schedule (Week of August 5th, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in grids 76-101 (Eastern fill area)
  - d. Continue pressure-washing large rocks.
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated piles to CC as piles pass
  - g. Begin screening crushed rock pile in eastern fill area
  - h. Remove under drain manhole

4. Administrative Issues
5. Open Discussion
6. Notes-As of 7/31/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 102 thru 106, 18B, 107 thru 114, 71 thru 75, 81, 82, 93, 97, 121 thru 123 and 125.  
  
Grids 79, 80, 86, 87 and 92 sampled and waiting confirmation results  
  
Piles PSV-271-PSV-285 have been treated and waiting on results  
  
PSV3-PSV-270 have all been treated and placed in CC.



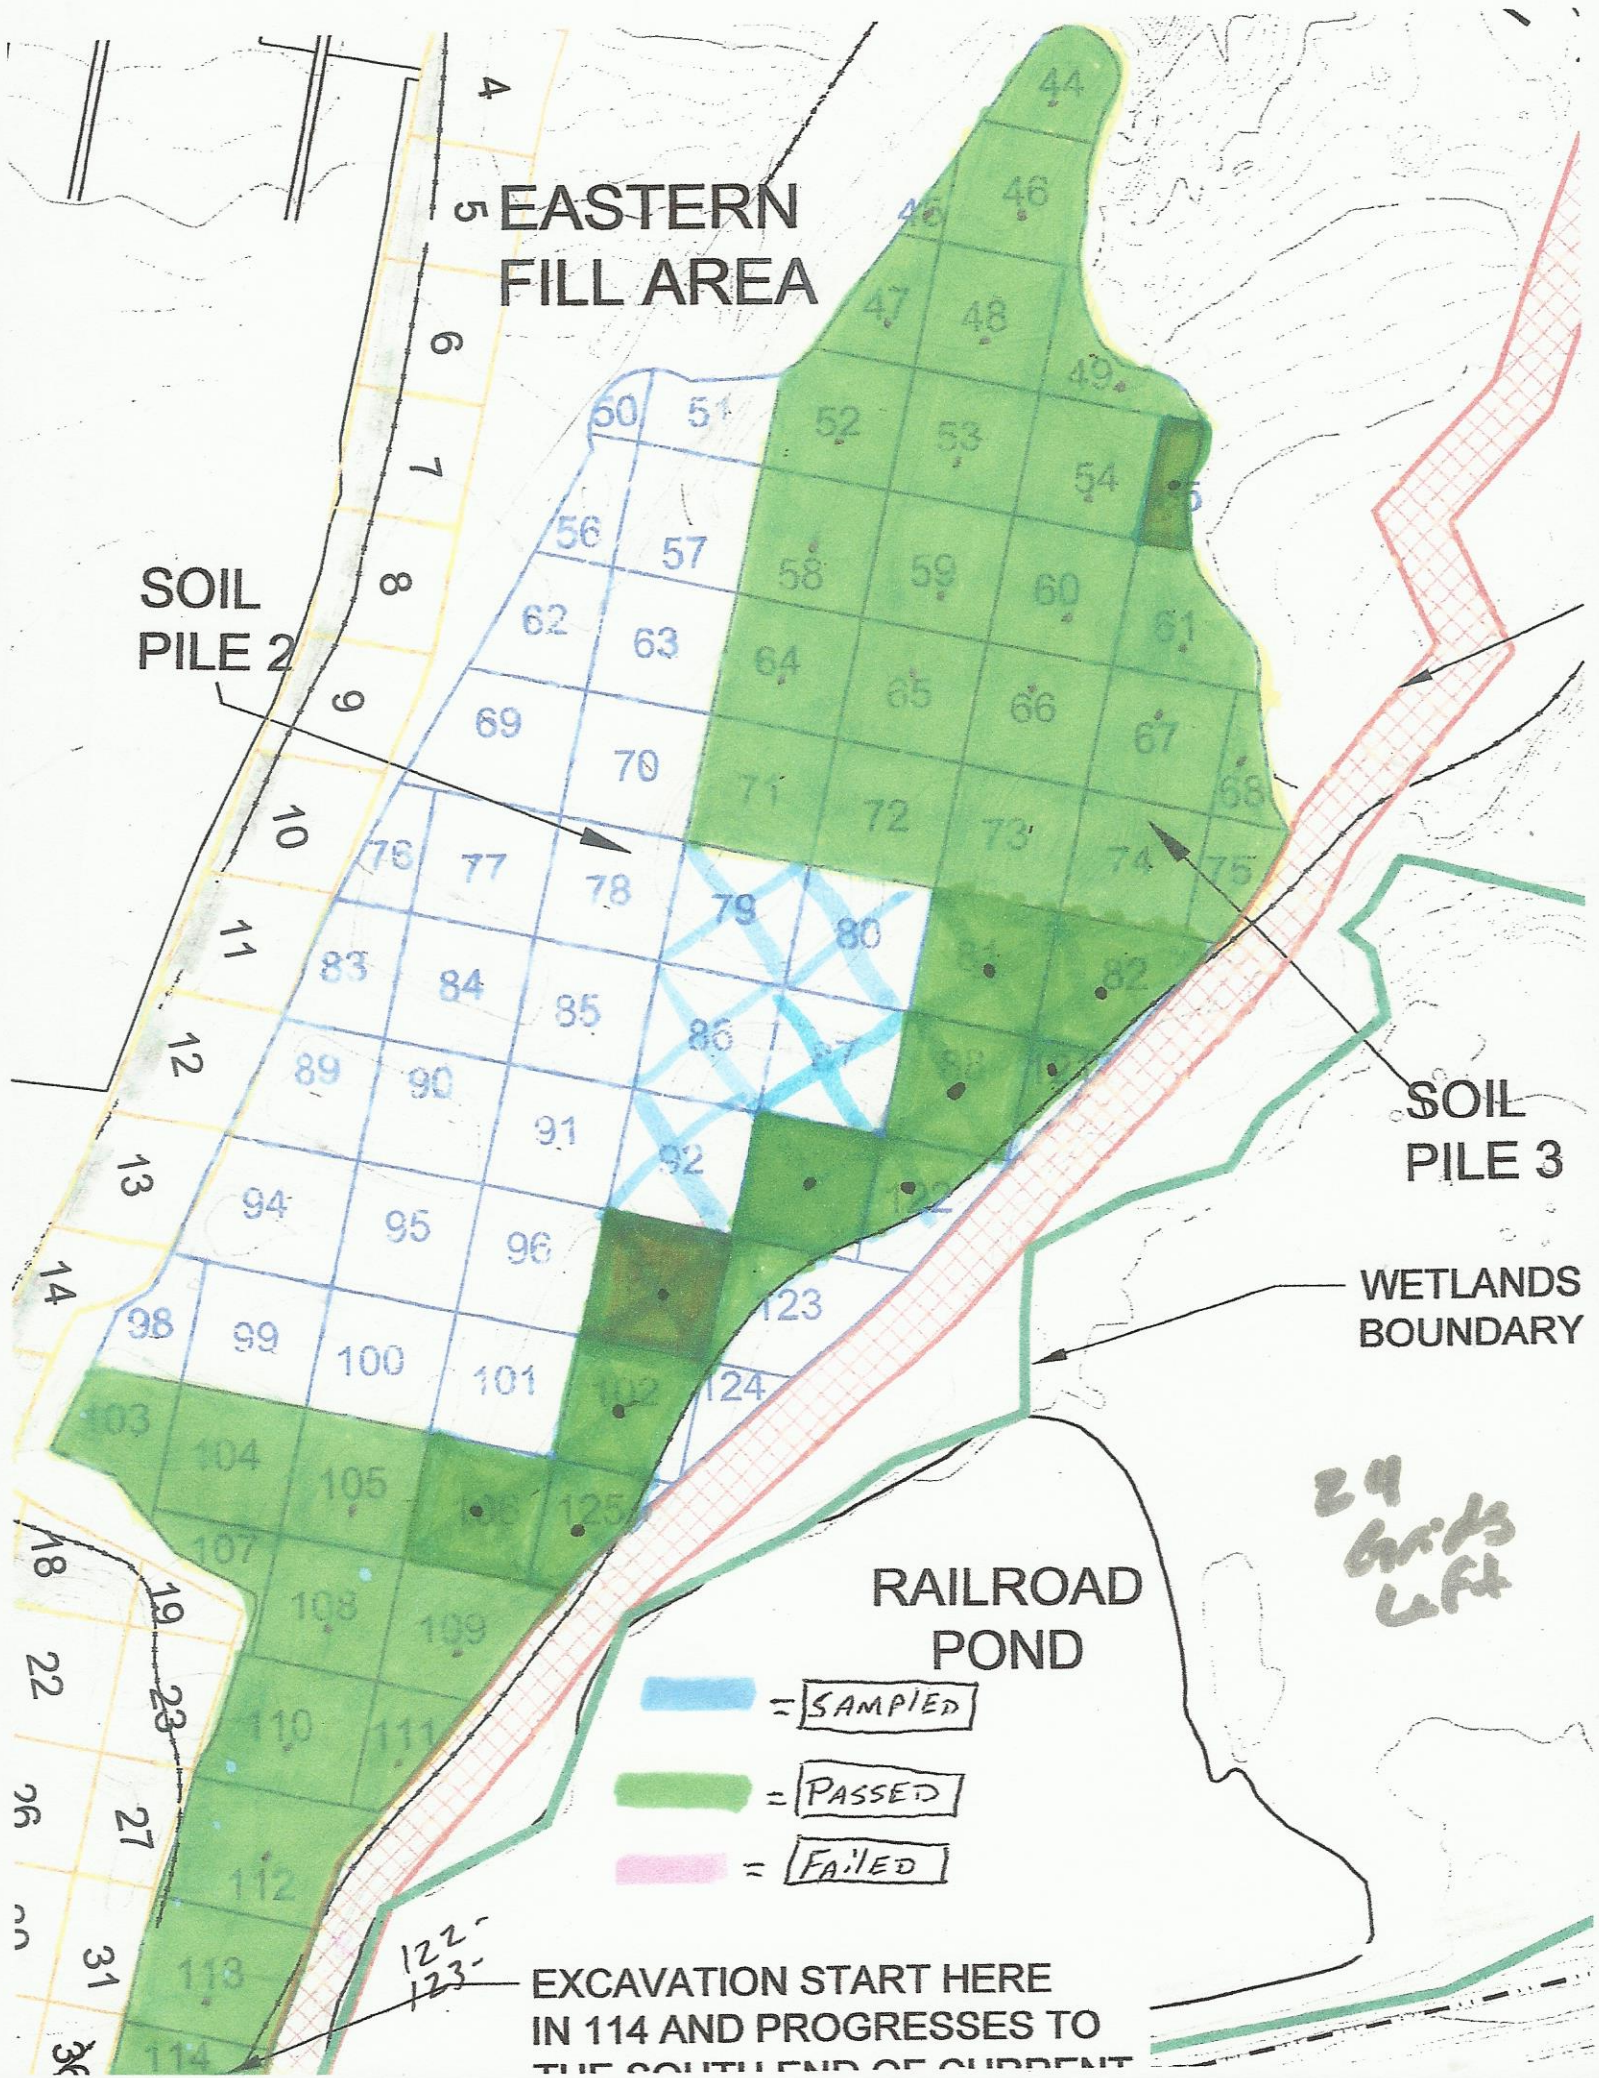

**EASTERN  
FILL AREA**




**SOIL  
PILE 2**

**SOIL  
PILE 3**

**WETLANDS  
BOUNDARY**

**RAILROAD  
POND**

29  
Grids  
Left

-  = **SAMPLED**
-  = **PASSED**
-  = **FAILED**

EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTHEAST END OF CURRENT

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Tuesday, August 6th, 2013**

**1:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of August 5<sup>th</sup>, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 50-101 (Eastern fill area) Approx. 24 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks.
  - g. Begin screening crushed rock in Eastern fill area
  - h. Retreat PSV-271 and re-excavate grid 86
  - i. Construct new treatment pad
3. Schedule (Week of August 12th, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in grids 50-101 (Eastern fill area)
  - d. Continue pressure-washing large rocks.
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated piles to CC as piles pass

g. Continue screening crushed rock pile in eastern fill area

h. Remove under drain manhole

4. Administrative Issues

5. Open Discussion- Impacted Tree's, Lead buttons?


6. Notes-As of 8/6/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 102 thru 106, 18B, 107 thru 114, 71 thru 75, 79 thru 82, 87, 88, 92, 93, 97, 121 thru 123 and 125.

Grid 86 failed and will be re-excavated

Pile PSV-271 failed and will be retreated

PSV3-PSV-285 have all been treated and placed in CC.



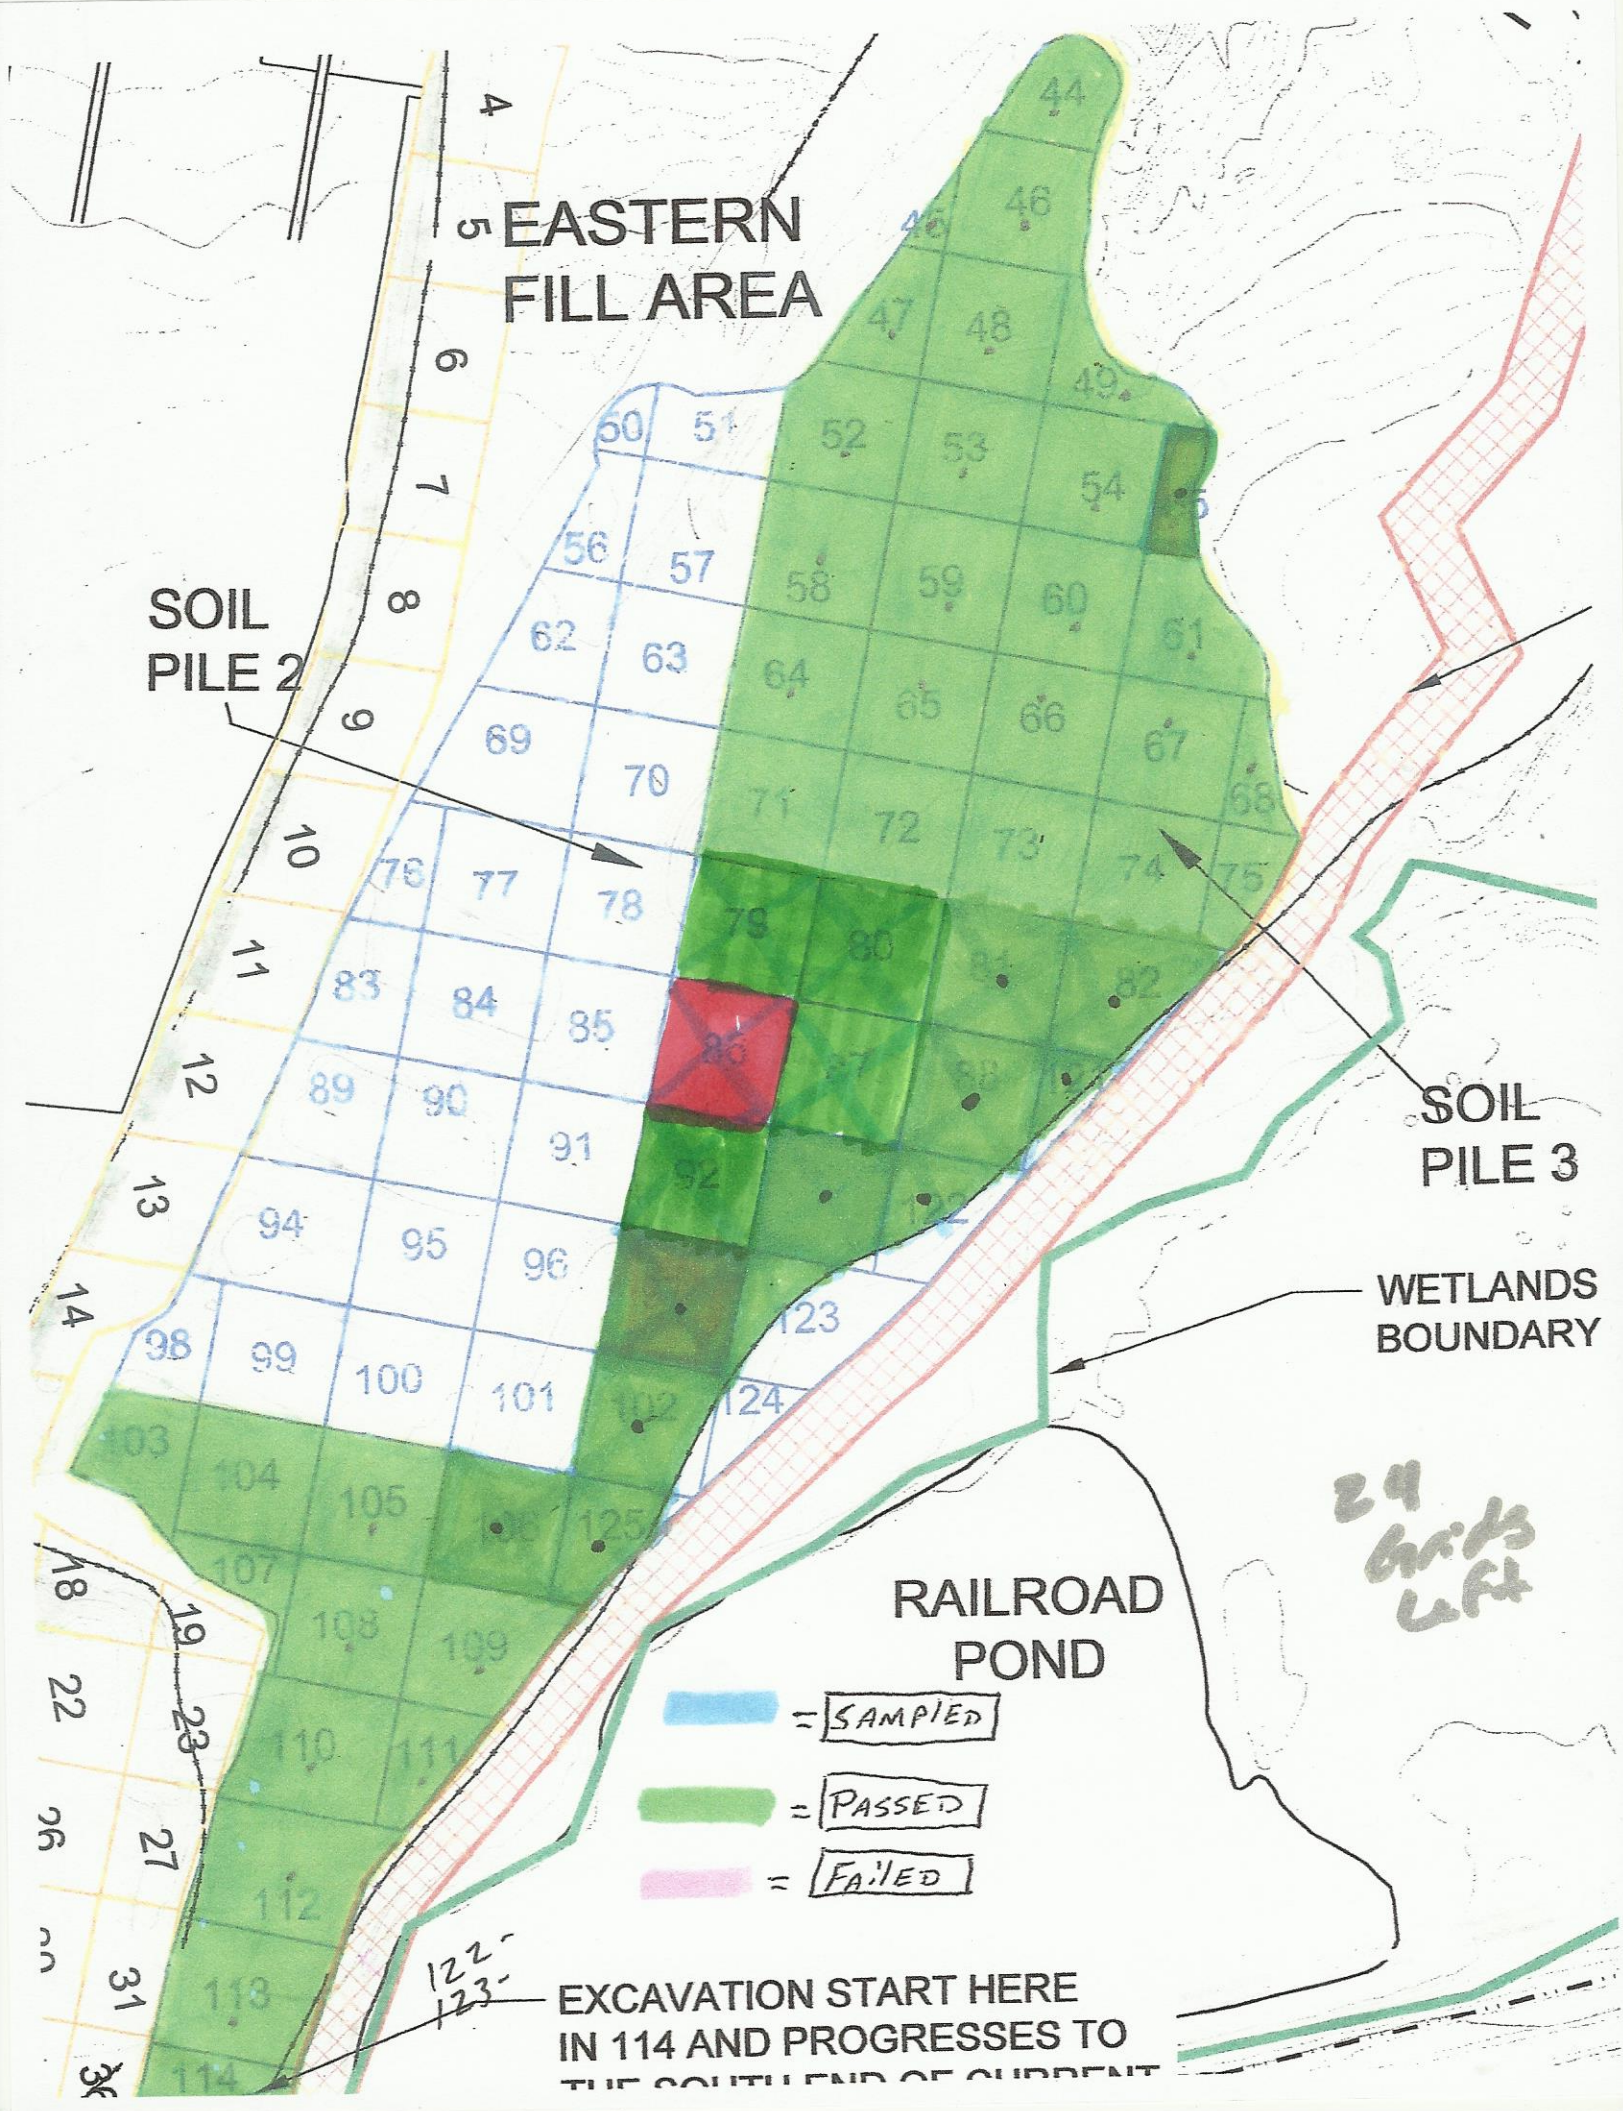



**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, August 14th, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of August 12<sup>th</sup>, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 50-101 (Eastern fill area) Approx. 24 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks.
  - g. Continue screening crushed rock in Eastern fill area
  - h. Construct new treatment pad
3. Schedule (Week of August 19th, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in grids 50-101 (Eastern fill area)
  - d. Continue pressure-washing large rocks.
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated piles to CC as piles pass
  - g. Remove under drain manhole

4. Administrative Issues
5. Open Discussion- Impacted Tree's, Lead buttons?
6. Notes-As of 8/6/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 102 thru 107, 18B, 108 thru 114, 71 thru 75, 79 thru 82, 86 thru 88, 92, 93, 97, 121 thru 123 and 125.

PSV-290 and PSV-291 have been treated and waiting on results.

PSV3-PSV-289 have all been treated and placed in CC.


# EASTERN FILL AREA


SOIL  
PILE 2

SOIL  
PILE 3

WETLANDS  
BOUNDARY


RAILROAD  
POND

 = SAMPLED

 = PASSED

 = FAILED

EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTH END OF CURRENT

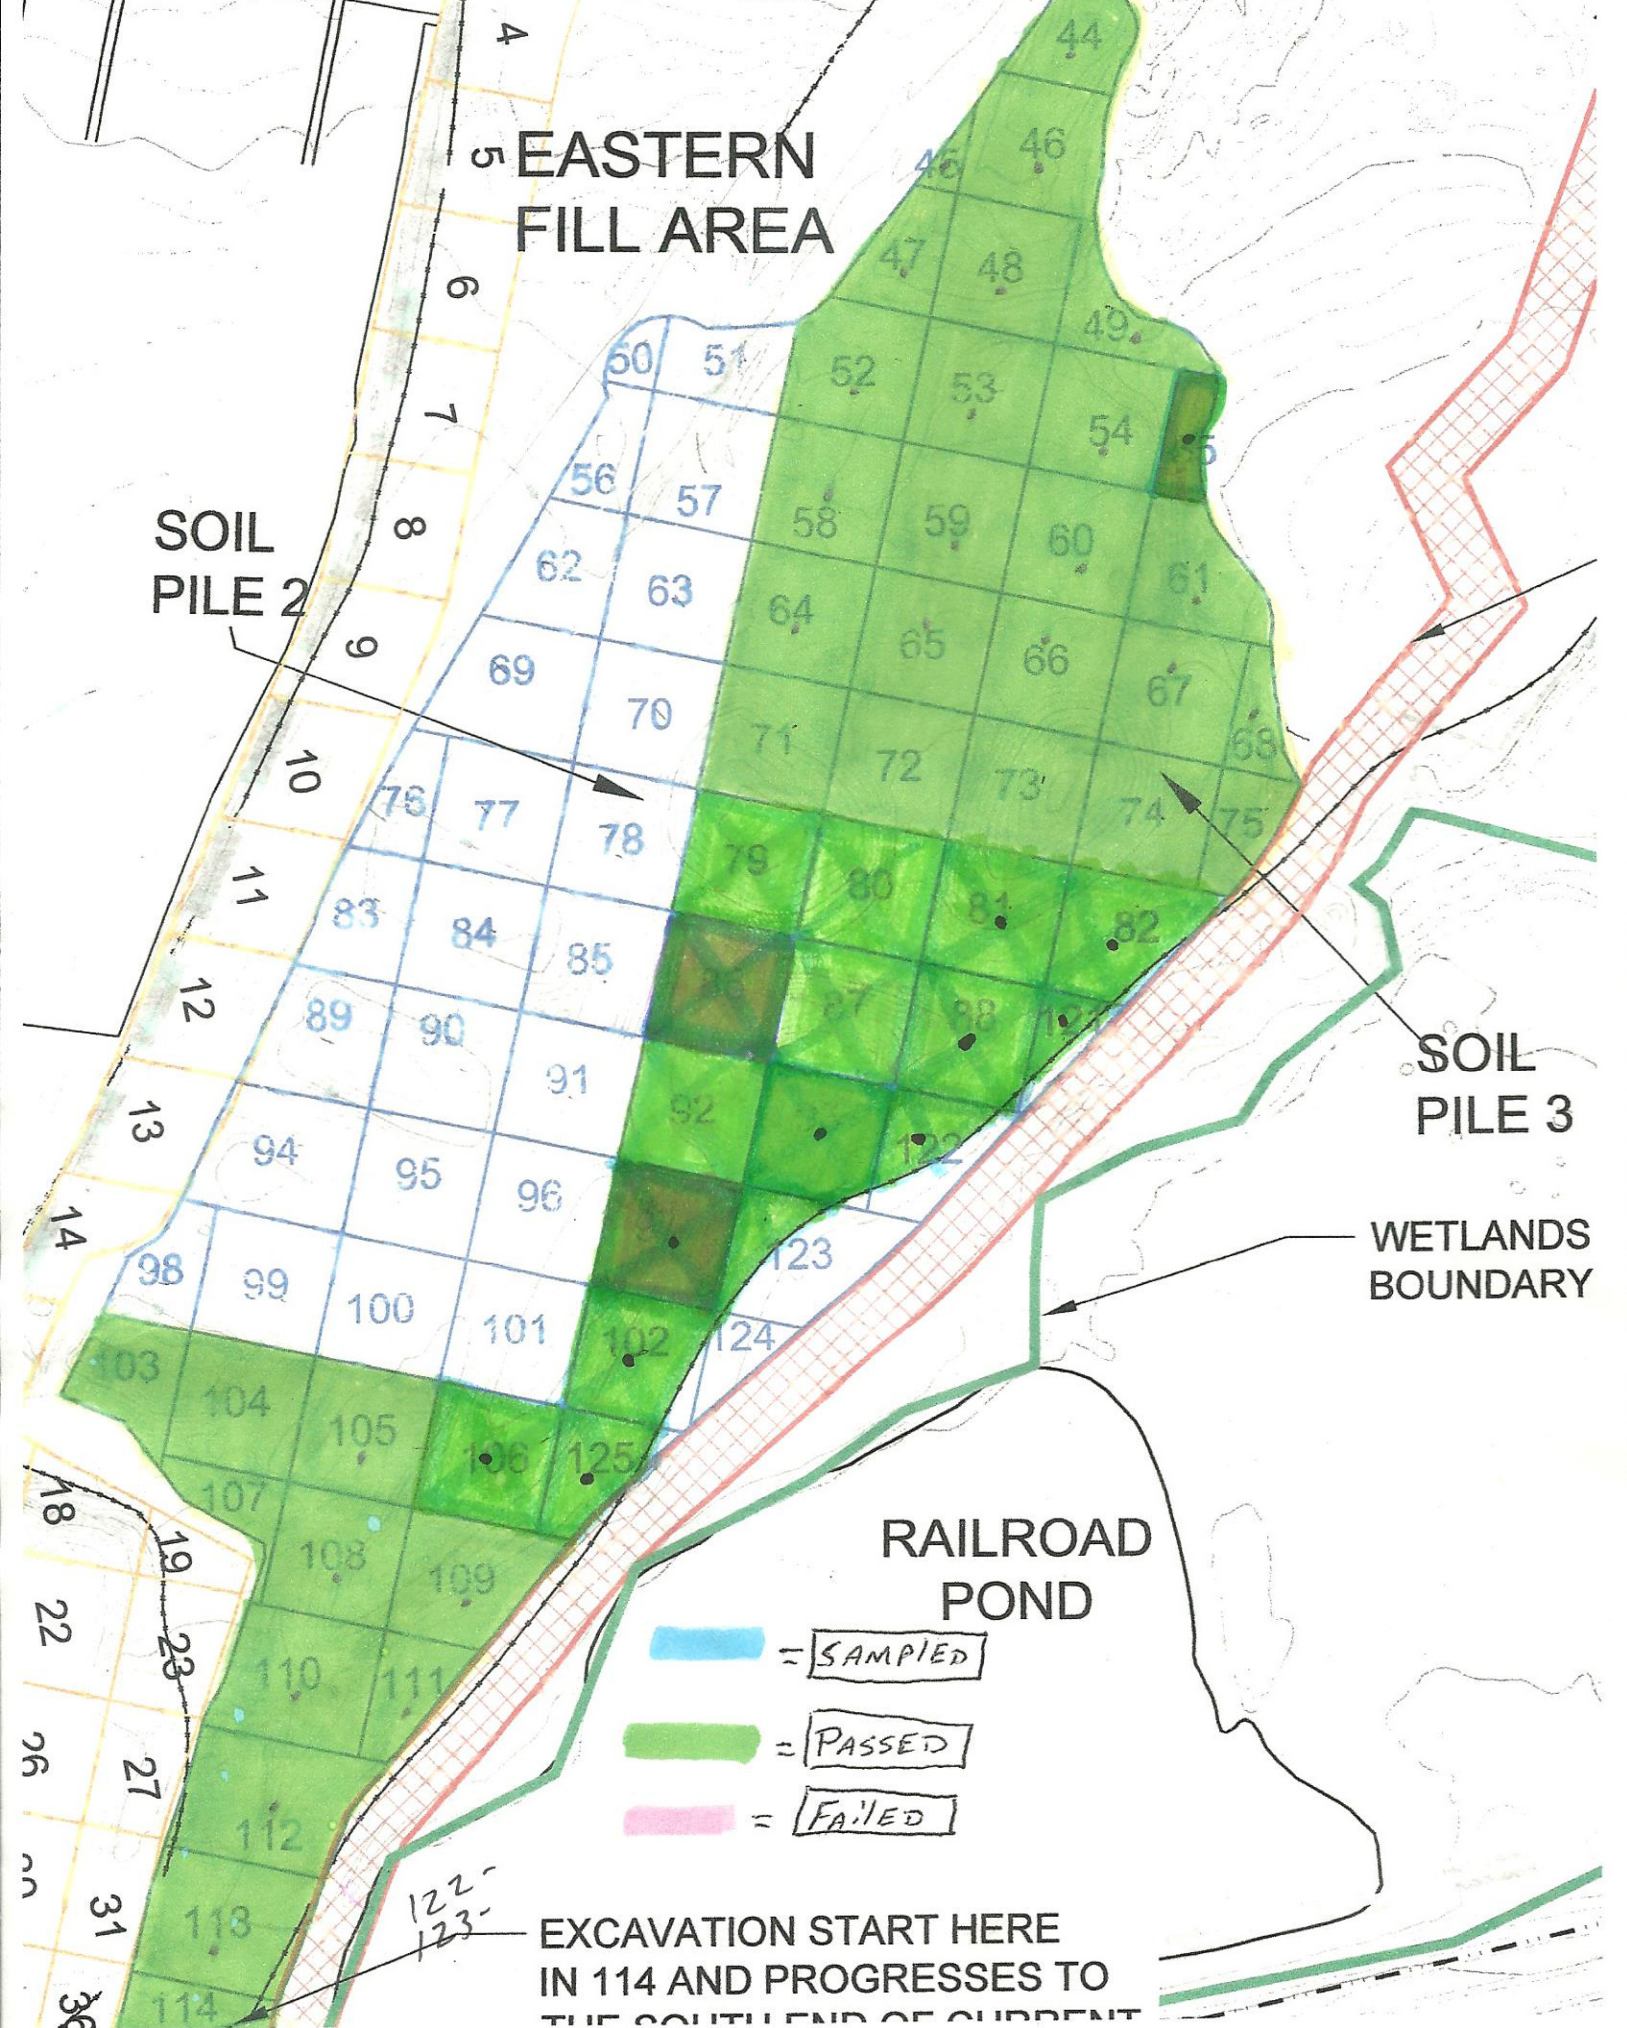

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, August 21th, 2013**

**1:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of August 19<sup>th</sup>, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 50-95 (Eastern fill area) Approx. 15 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks.
  - g. Complete construction of new treatment pad
3. Schedule (Week of August 26th, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids 50-95 (Eastern fill area)
  - d. Continue pressure-washing large rocks.
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated piles to CC as piles pass
  - g. Remove under drain manhole
  - h. Backfill excavated grids


4. Administrative Issues
5. Open Discussion- Impacted Tree's, Lead buttons?
6. Notes-As of 8/14/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 102 thru 107, 18B, 108 thru 114, 71 thru 75, 79 thru 82, 86 thru 88, 92, 93, 97, 121 thru 123 and 125.

PSV-292 thru PSV-297 has been treated and waiting on results.

PSV3-PSV-291 have all been treated and placed in CC.

Grids 70, 78, 85, 91, 96, 98, 99, 101, 100 have been sampled and waiting on confirmation results



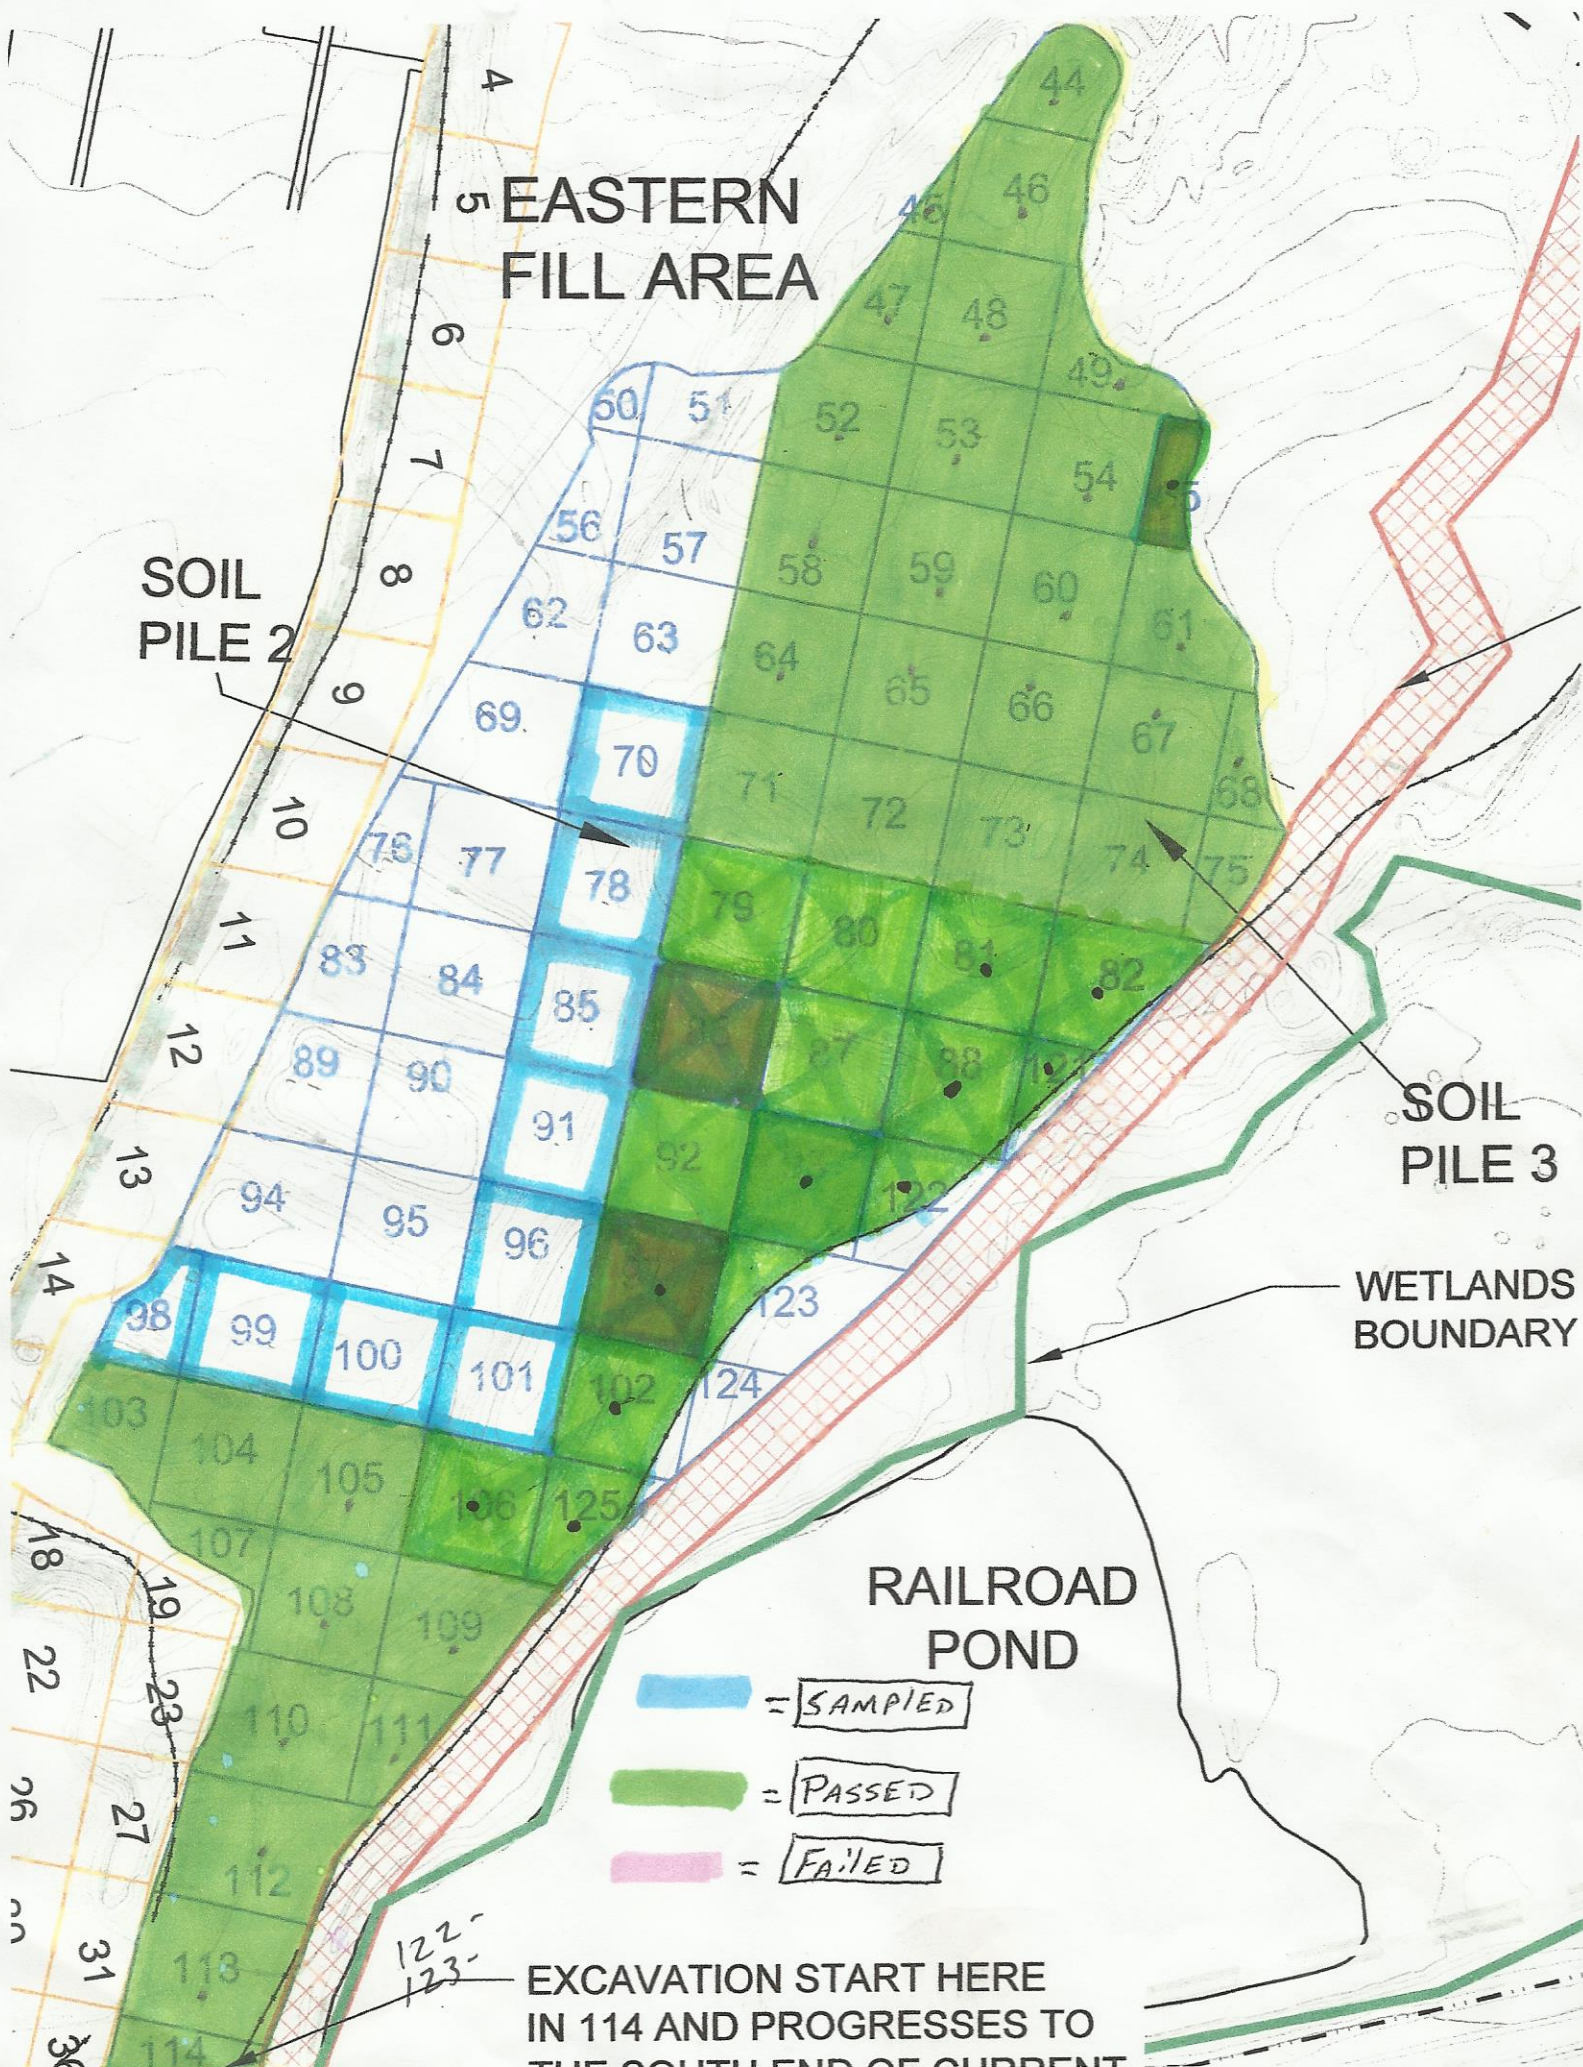

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Tuesday, August 27th, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317


Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of August 26<sup>th</sup>, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 50-95 (Eastern fill area) Approx. 14 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks.
3. Schedule (Week of September 2nd, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids 50-95 (Eastern fill area) if needed
  - d. Continue pressure-washing large rocks.
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated piles to CC as piles pass
  - g. Remove under drain manhole
  - h. Backfill excavated grids
4. Administrative Issues

5. Open Discussion- Impacted Tree's, buttons?
6. Notes-As of 8/26/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 70 thru 75, 78 thru 82,85 thru 88, 91 thru 93,97, 98 thru 114, 121 thru 123, 18B, 125.  
  
PSV1-PSV-295 have all been treated and placed in CC.  
  
PSV-296 and PSV-297 used in floor of new treatment pad  
  
PSV-298,299 and 300 have been treated and waiting results  
  
Grid 96 failed and was re-scrapped 8/24/13



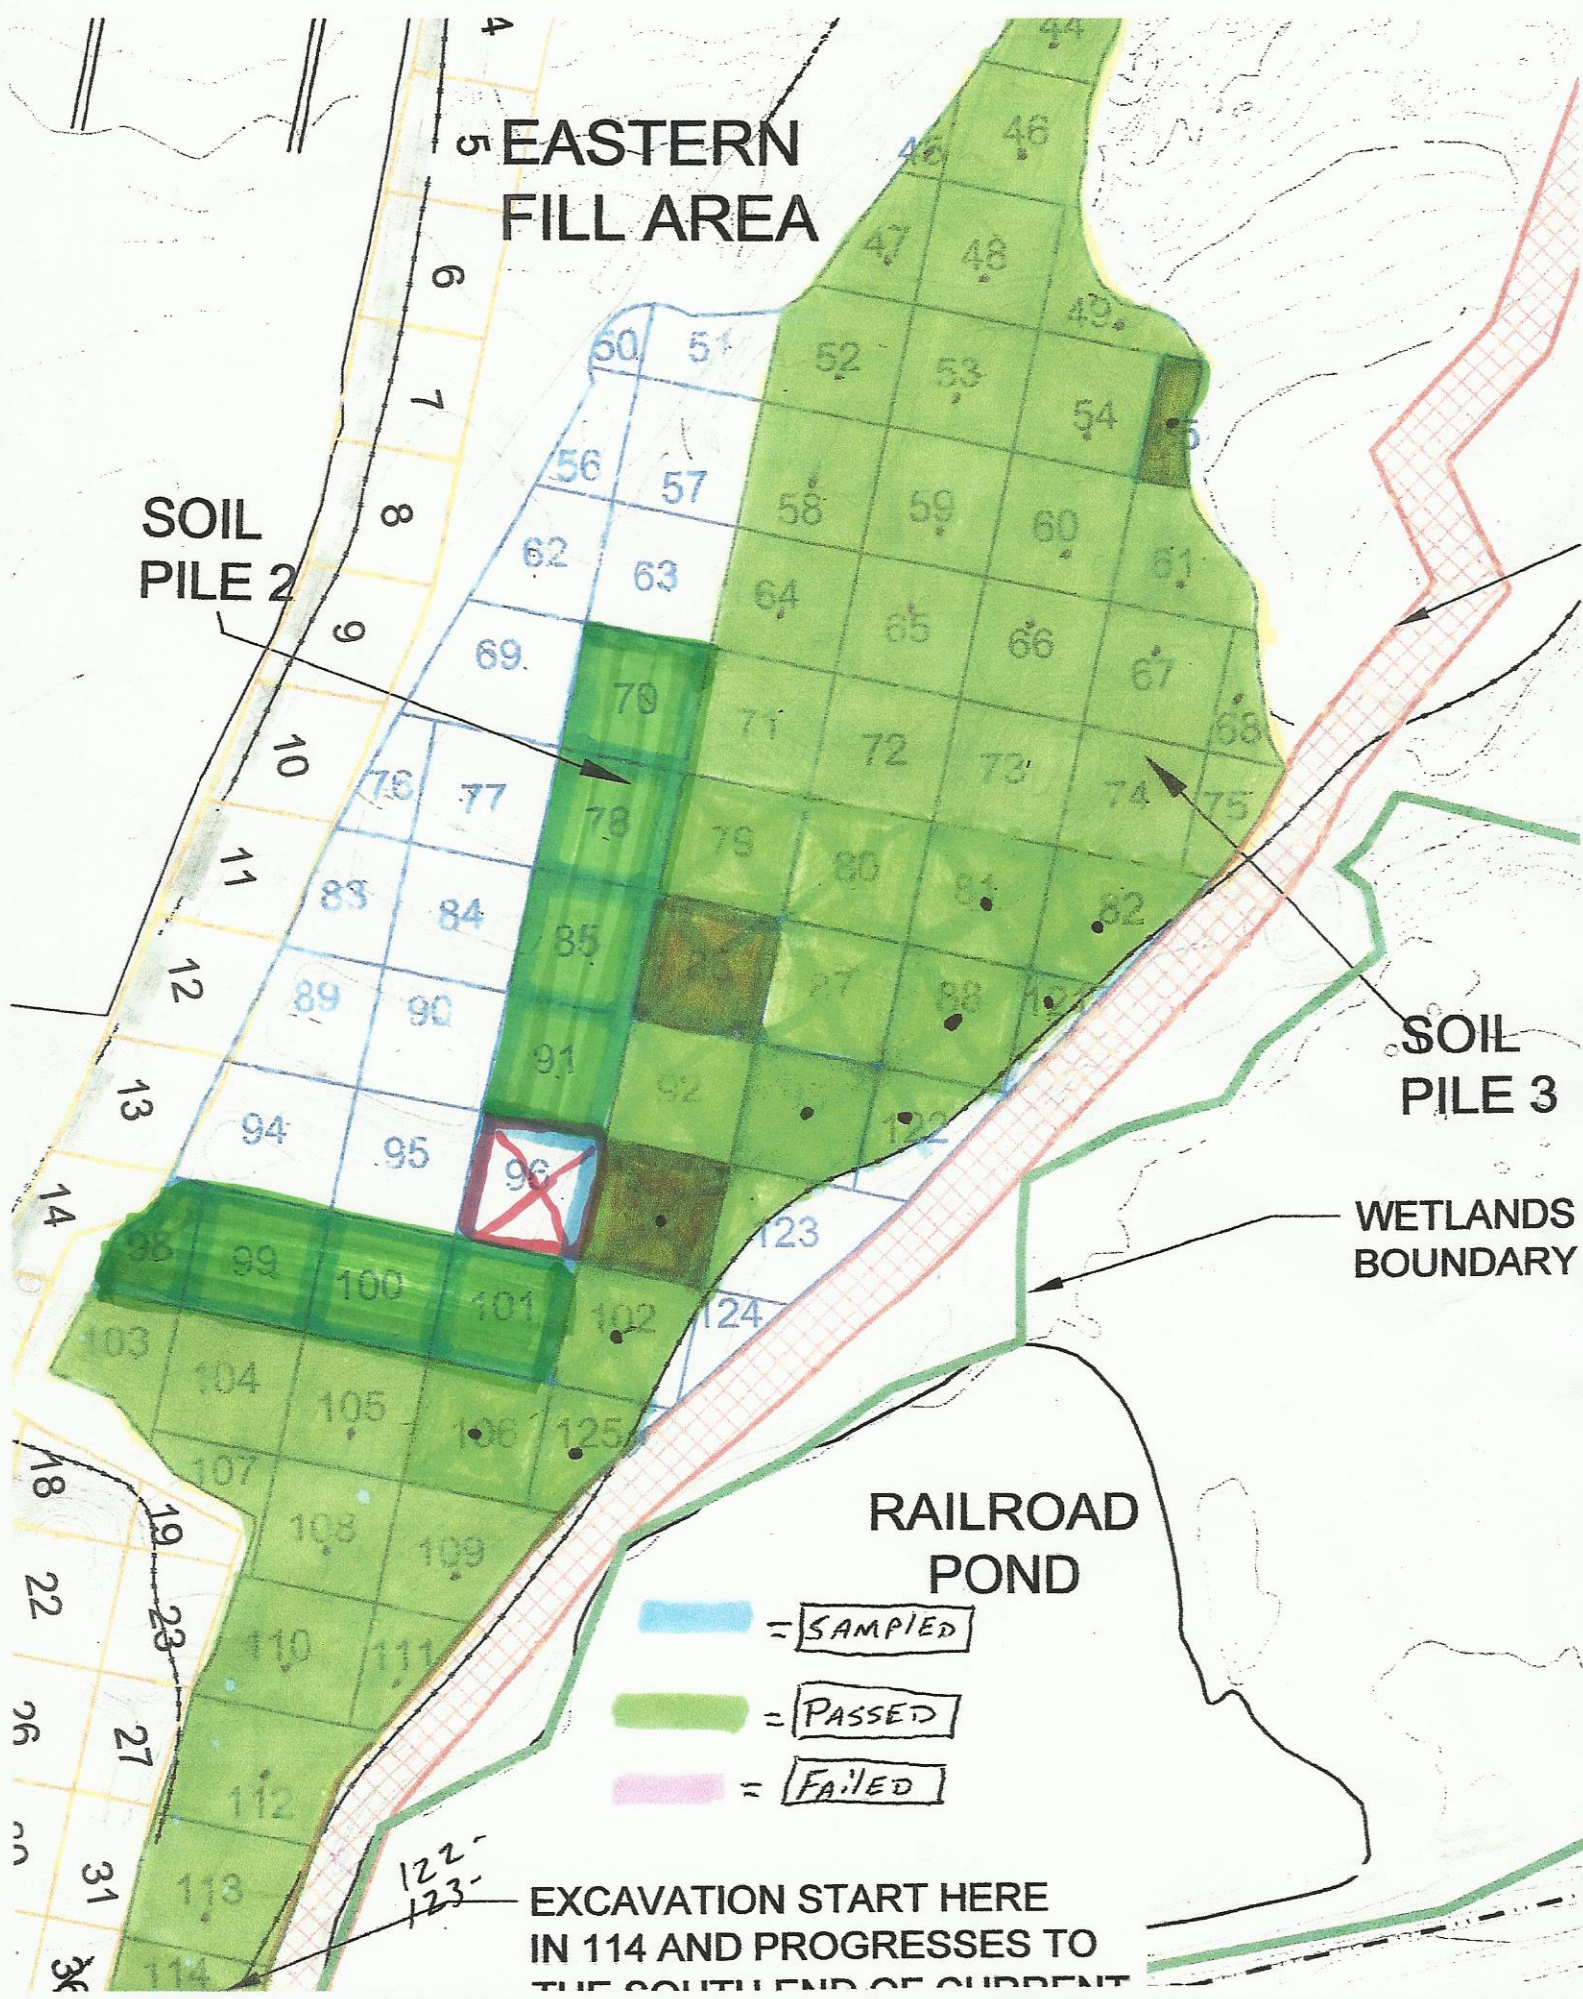

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, September 4th, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317


Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 2<sup>nd</sup>, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 50-89 (Eastern fill area) Approx. 11 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks, metal, concrete
3. Schedule (Week of September 9th, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids 50-89 (Eastern fill area) if needed
  - d. Continue pressure-washing large rocks, metal, concrete.
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated piles to CC as piles pass
  - g. Remove under drain manhole
  - h. Backfill excavated grids
  - i. Chip Impacted trees and sample?

4. Administrative Issues
5. Open Discussion- buttons?
6. Notes-As of 8/26/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 70 thru 75, 78 thru 82, 85 thru 88, 91 thru 93, 97, 98 thru 114, 121 thru 123, 18B, 125.  
  
PSV1-PSV-295 have all been treated and placed in CC.  
  
PSV-296 and PSV-297 used in floor of new treatment pad  
  
PSV-298 thru 307 passed and will be moved in the cell today  
  
Grid 96 failed and was re-scrapped 8/24/13  
  
Grids 94,95,90,84 all sampled and waiting verification



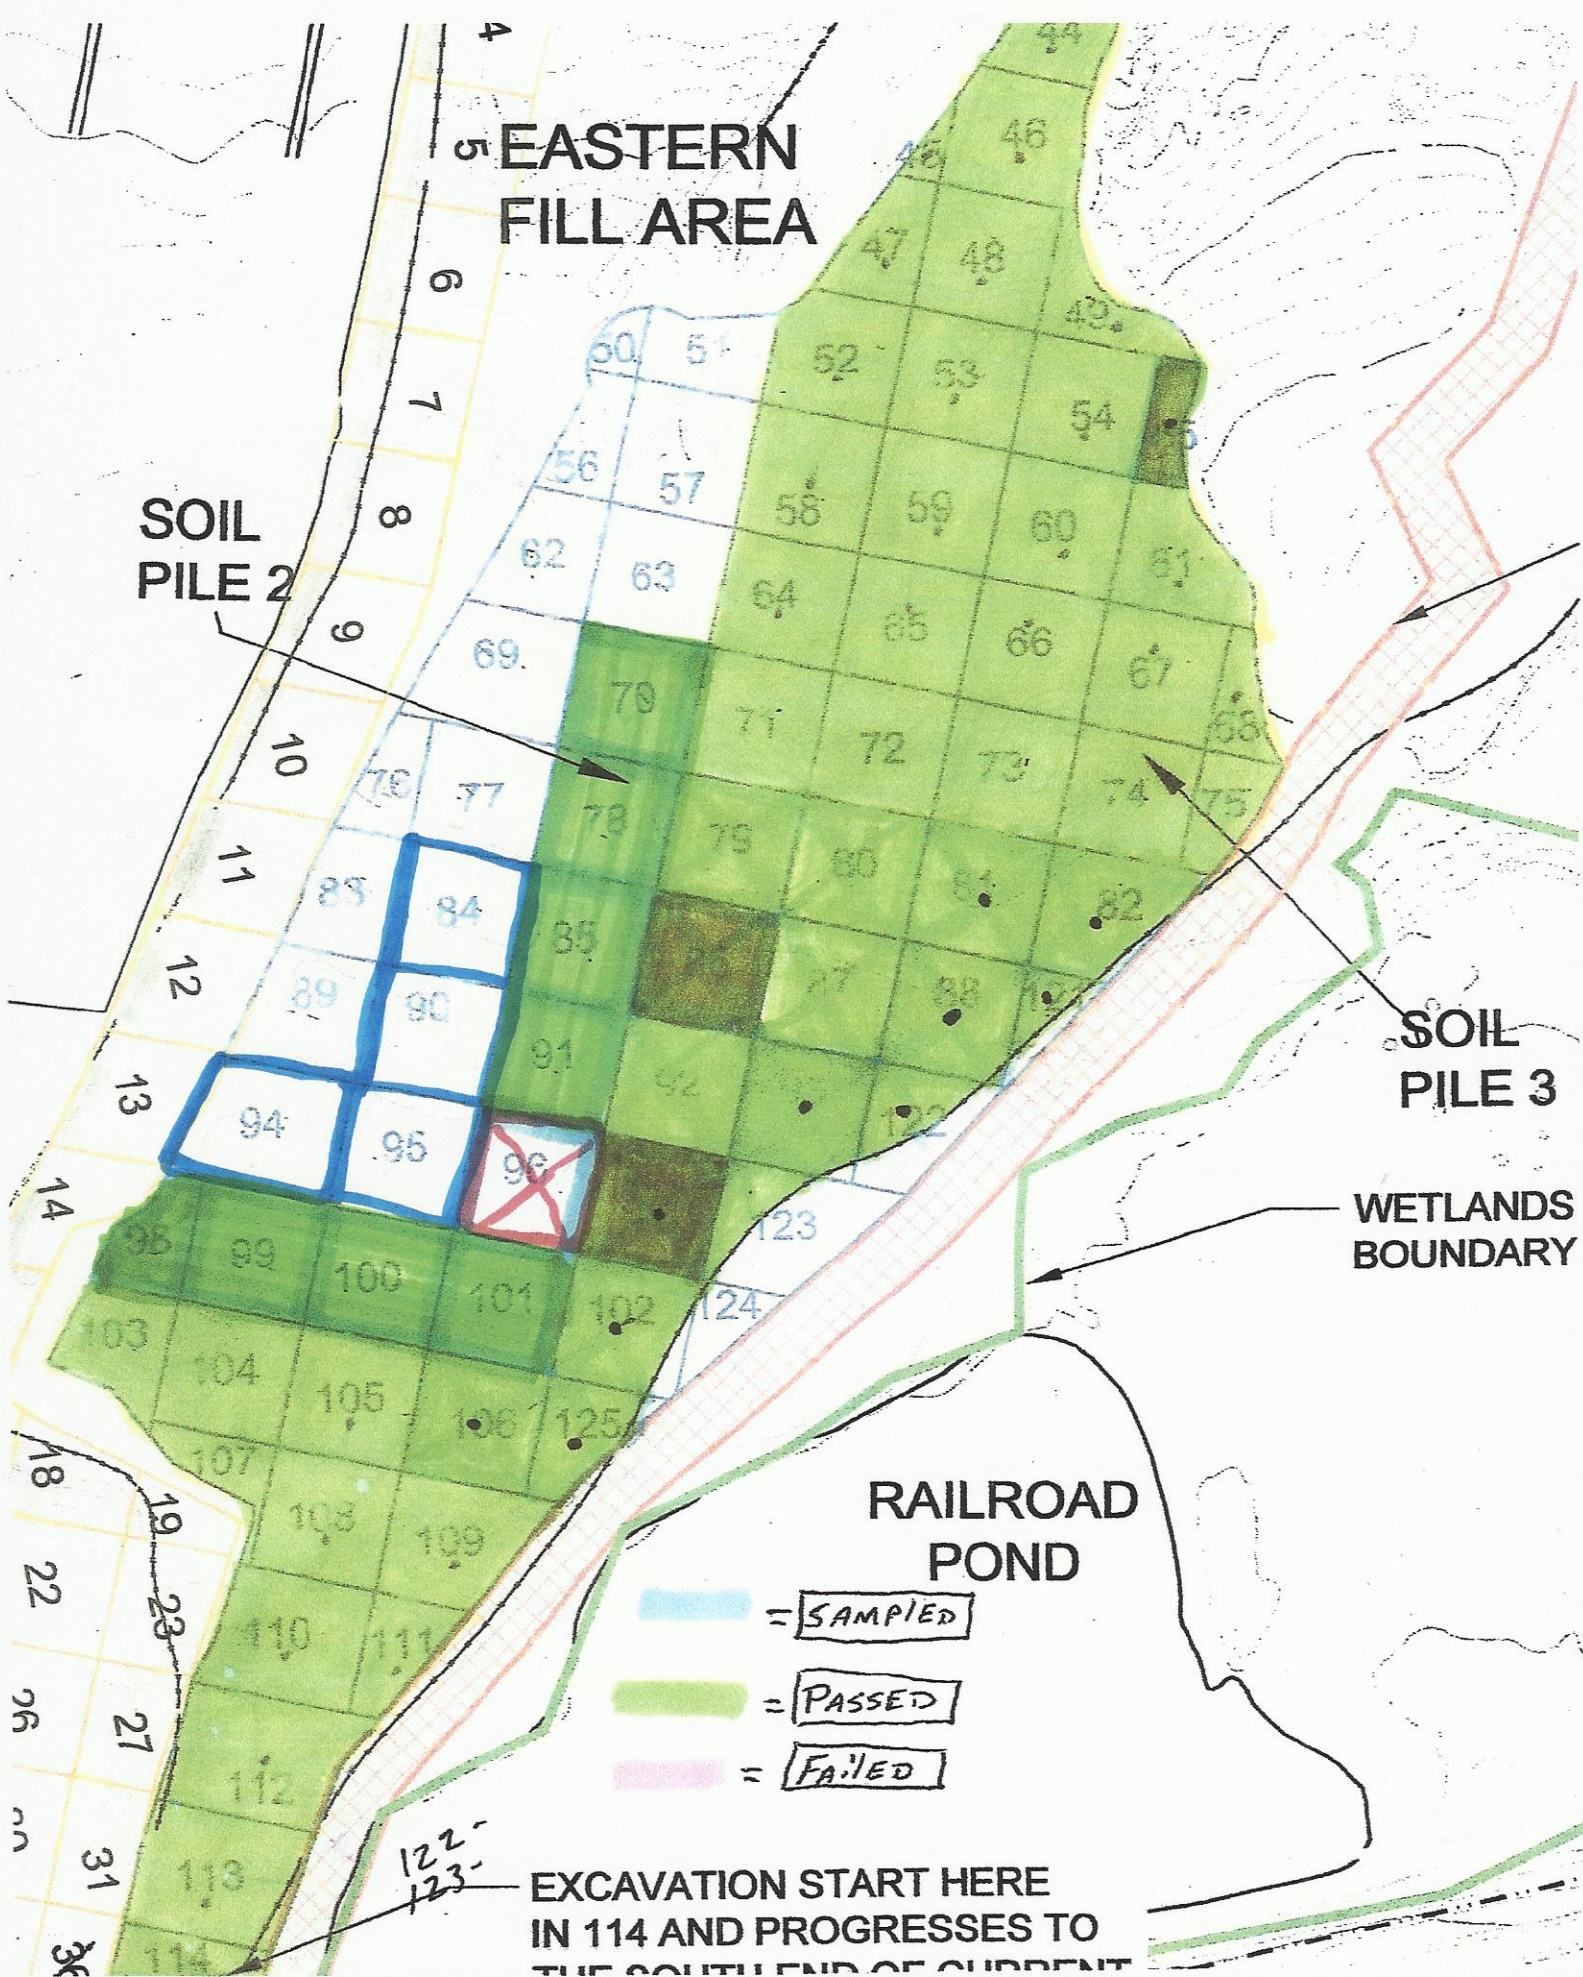




**EASTERN  
FILL AREA**

**SOIL  
PILE 2**

**SOIL  
PILE 3**

**WETLANDS  
BOUNDARY**

**RAILROAD  
POND**

-  = **SAMPLED**
-  = **PASSED**
-  = **FAILED**

**EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTHEAST END OF CURRENT**

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Tuesday, September 10th, 2013**

**10:00 a.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 9th, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids in 50-77 (Eastern fill area) Approx. 9 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks, metal, concrete
3. Schedule (Week of September 16, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage erosion controls/BMP's
  - c. Continue excavation of grids 50-77 (Eastern fill area) if needed
  - d. Continue pressure-washing large rocks, metal, concrete.
  - e. Continue treatment of Eastern fill soil
  - f. Continue hauling treated piles to CC as piles pass
  - g. Remove under drain manhole
  - h. Backfill excavated grids
  - i. Chip impacted trees and sample?

4. Administrative Issues
5. Open Discussion- lead buttons?
6. Notes-As of 9/10/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 70 thru 75, 78 thru 82, 85 thru 88, 91 thru 93, 97, 98 thru 114, 121 thru 123, 18B, 125.  
  
PSV1-PSV-307 have all been treated and placed in CC.  
  
PSV-296 and PSV-297 used in floor of new treatment pad  
  
Grid 96 failed and was re-scrapped 8/24/13 waiting for result  
  
Grids 83,84,89,94,95,90 all sampled and waiting verification  
  
Piles 308-312 have been sampled and waiting results






# EASTERN FILL AREA

SOIL  
PILE 2


SOIL  
PILE 3

WETLANDS  
BOUNDARY

RAILROAD  
POND

-  = **SAMPLED**
-  = **PASSED**
-  = **FAILED**

EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTHEAST END OF CURRENT

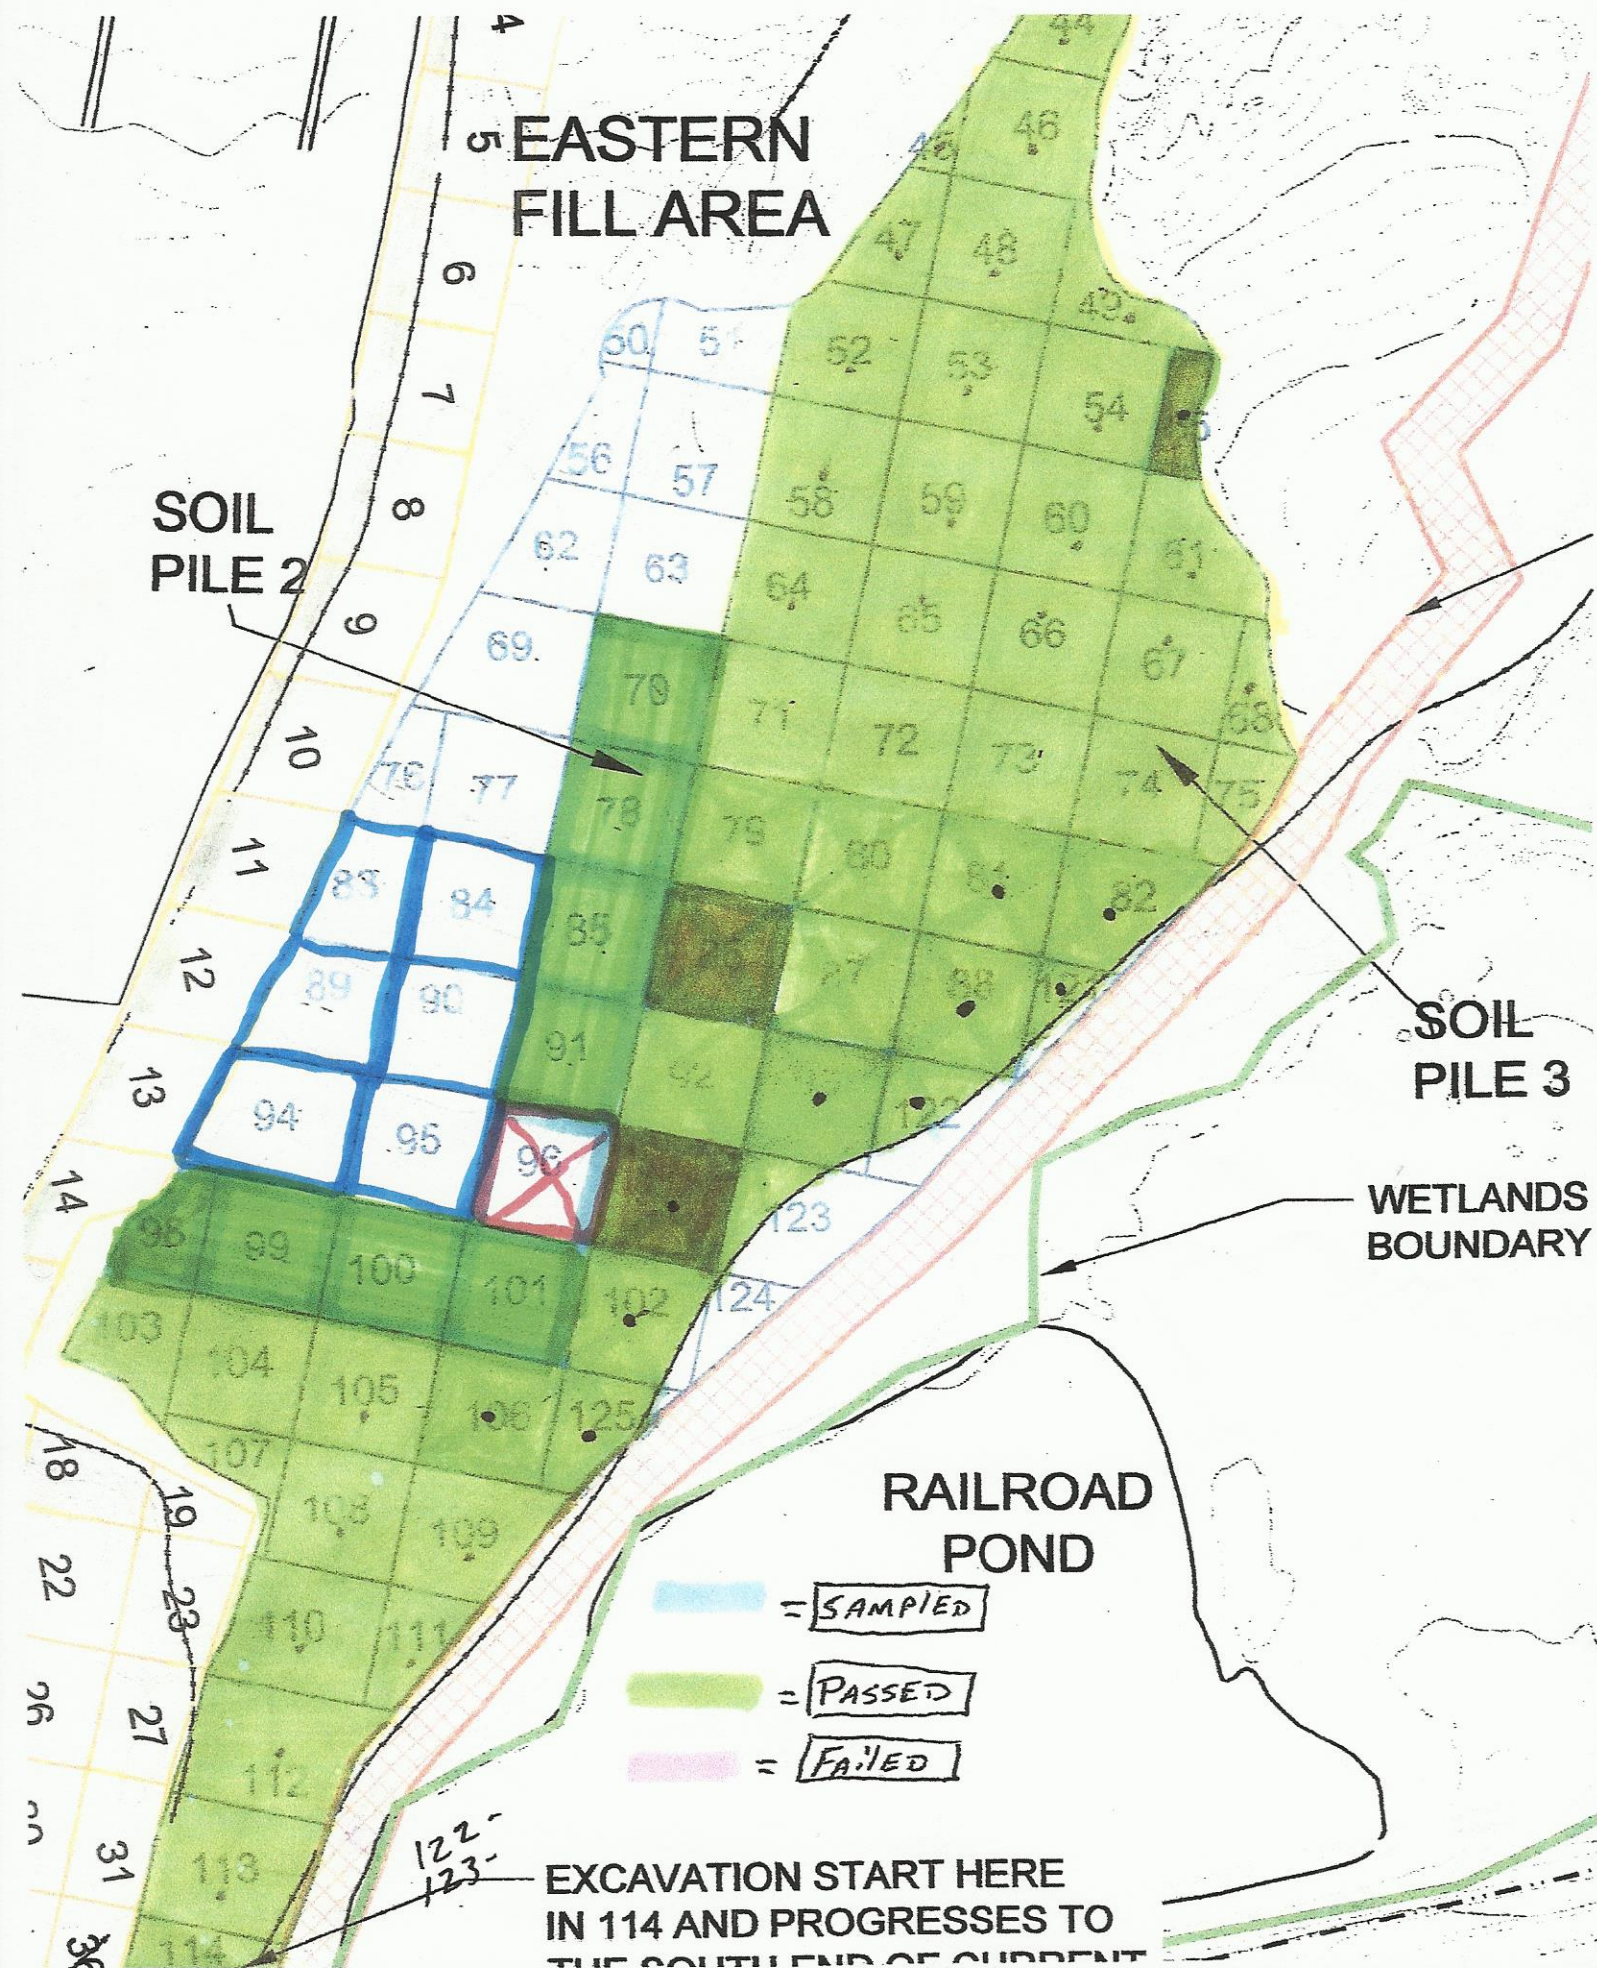

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, September 18th, 2013**

**11:00 a.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 16th, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue excavation of grids in 50,51,56,57,62,69 (Eastern fill area) 6 grids left to excavate
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated material to CC as piles pass
  - f. Continue pressure-washing large rocks, metal, concrete
  - g. Removed underdrain manhole. 9-16-13
  - h. Continue backfilling excavated grids
3. Schedule (Week of September 23rd, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
  - d. Continue treatment of Eastern fill soil
  - e. Continue hauling treated piles to CC as piles pass
  - f. Continue Backfilling excavated grids



4. Administrative Issues

5. Open Discussion

6. Notes-As of 9/18/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 64 thru 68, 70 thru 75, 78 thru 82, 83 thru 114, 121 thru 123, 18B, 125.

PSV1-PSV-307 have all been treated and placed in CC.

PSV-296 and PSV-297 used in floor of new treatment pad

Grids 77, 63, all sampled and waiting verification

Piles 308-317 passed and are being moved to the containment cell




# EASTERN FILL AREA

SOIL  
PILE 2


SOIL  
PILE 3

WETLANDS  
BOUNDARY

RAILROAD  
POND

-  = SAMPLED
-  = PASSED
-  = FAILED

EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTHEAST END OF CURRENT

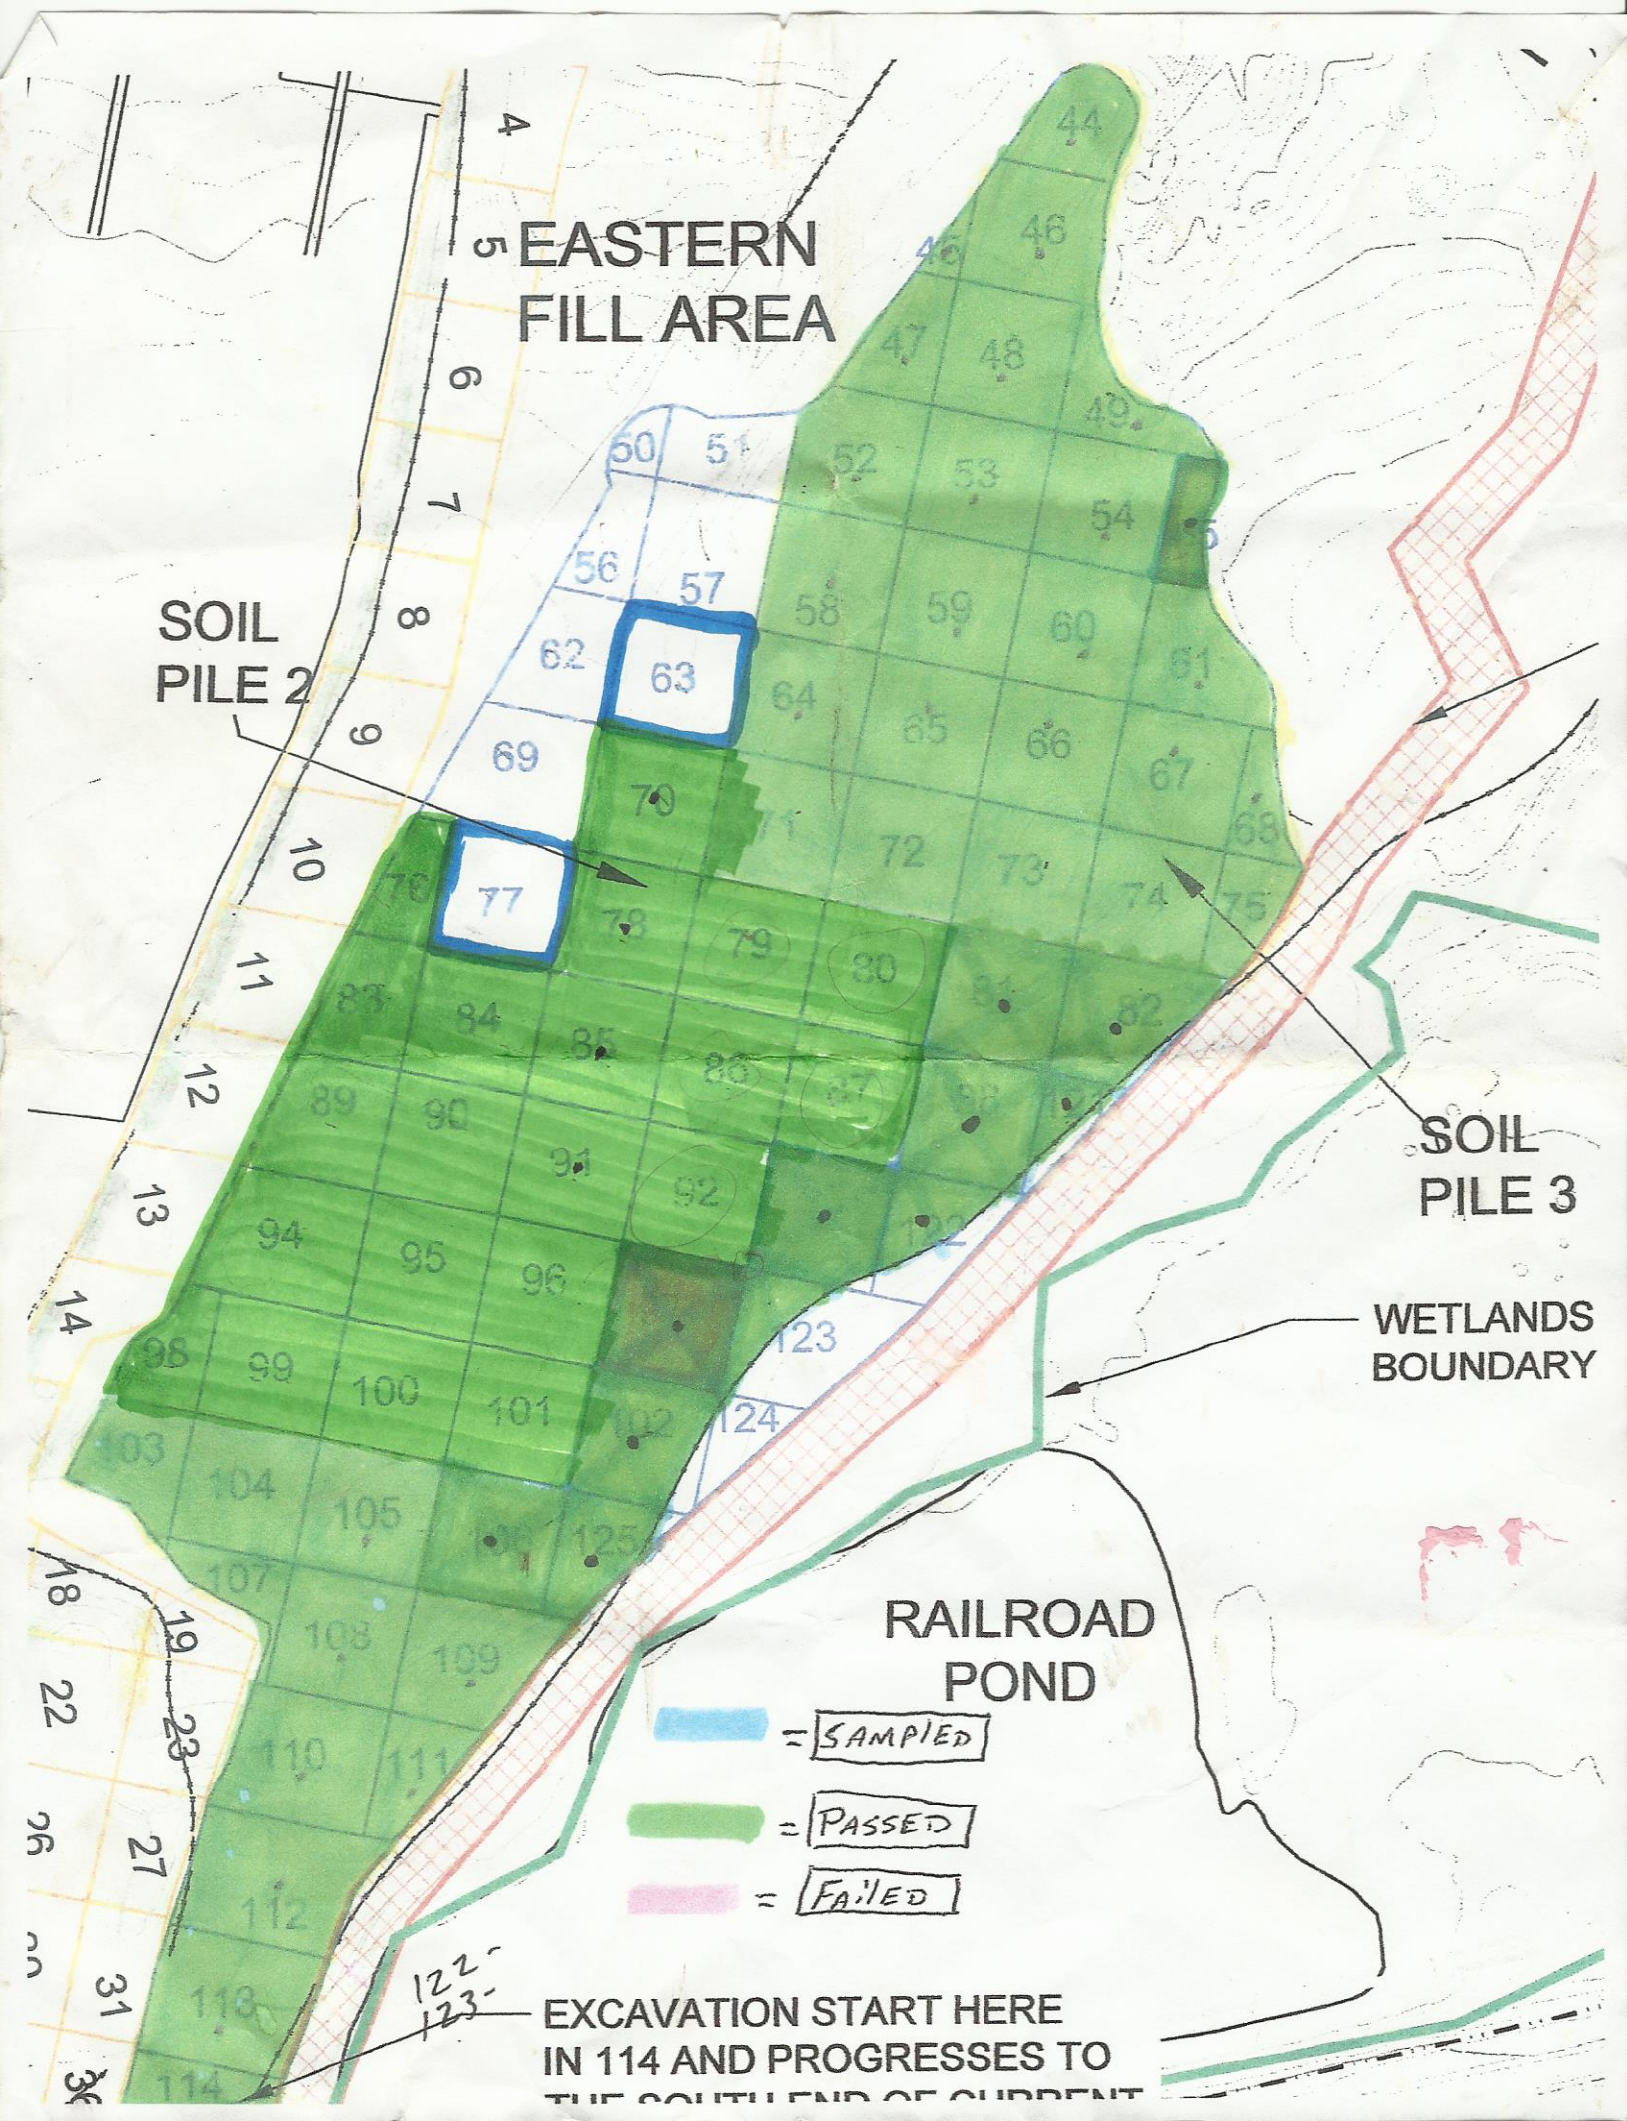

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, September 25th, 2013**

**11:30 a.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 23, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Completed Eastern fill excavation 9/20/13 (waiting for confirmation on grids 50, 52, 56, 57, 62, 69)
  - d. Continue hauling treated material to CC as piles pass (318-321 4 Piles left)
  - e. Continue pressure-washing large rocks, metal, concrete
  - f. Continue backfilling eastern fill area
3. Schedule (Week of September 30, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
  - d. Continue backfilling Eastern fill excavation
4. Administrative Issues
5. Open Discussion
6. Notes-As of 9/24/13 Eastern fill grids that have passed 44 thru 49, 52 thru 55, 58 thru 61, 63 thru 68, 70 thru 75, 76 thru 114, 121 thru 123, 18B, 125.


PSV1-PSV-317 have all been treated and placed in CC.

PSV-296 and PSV-297 used in floor of new treatment pad

Grids 50, 51, 56, 57, 62, and 69 all sampled and waiting verification

Piles 318-321 are treated and waiting on results



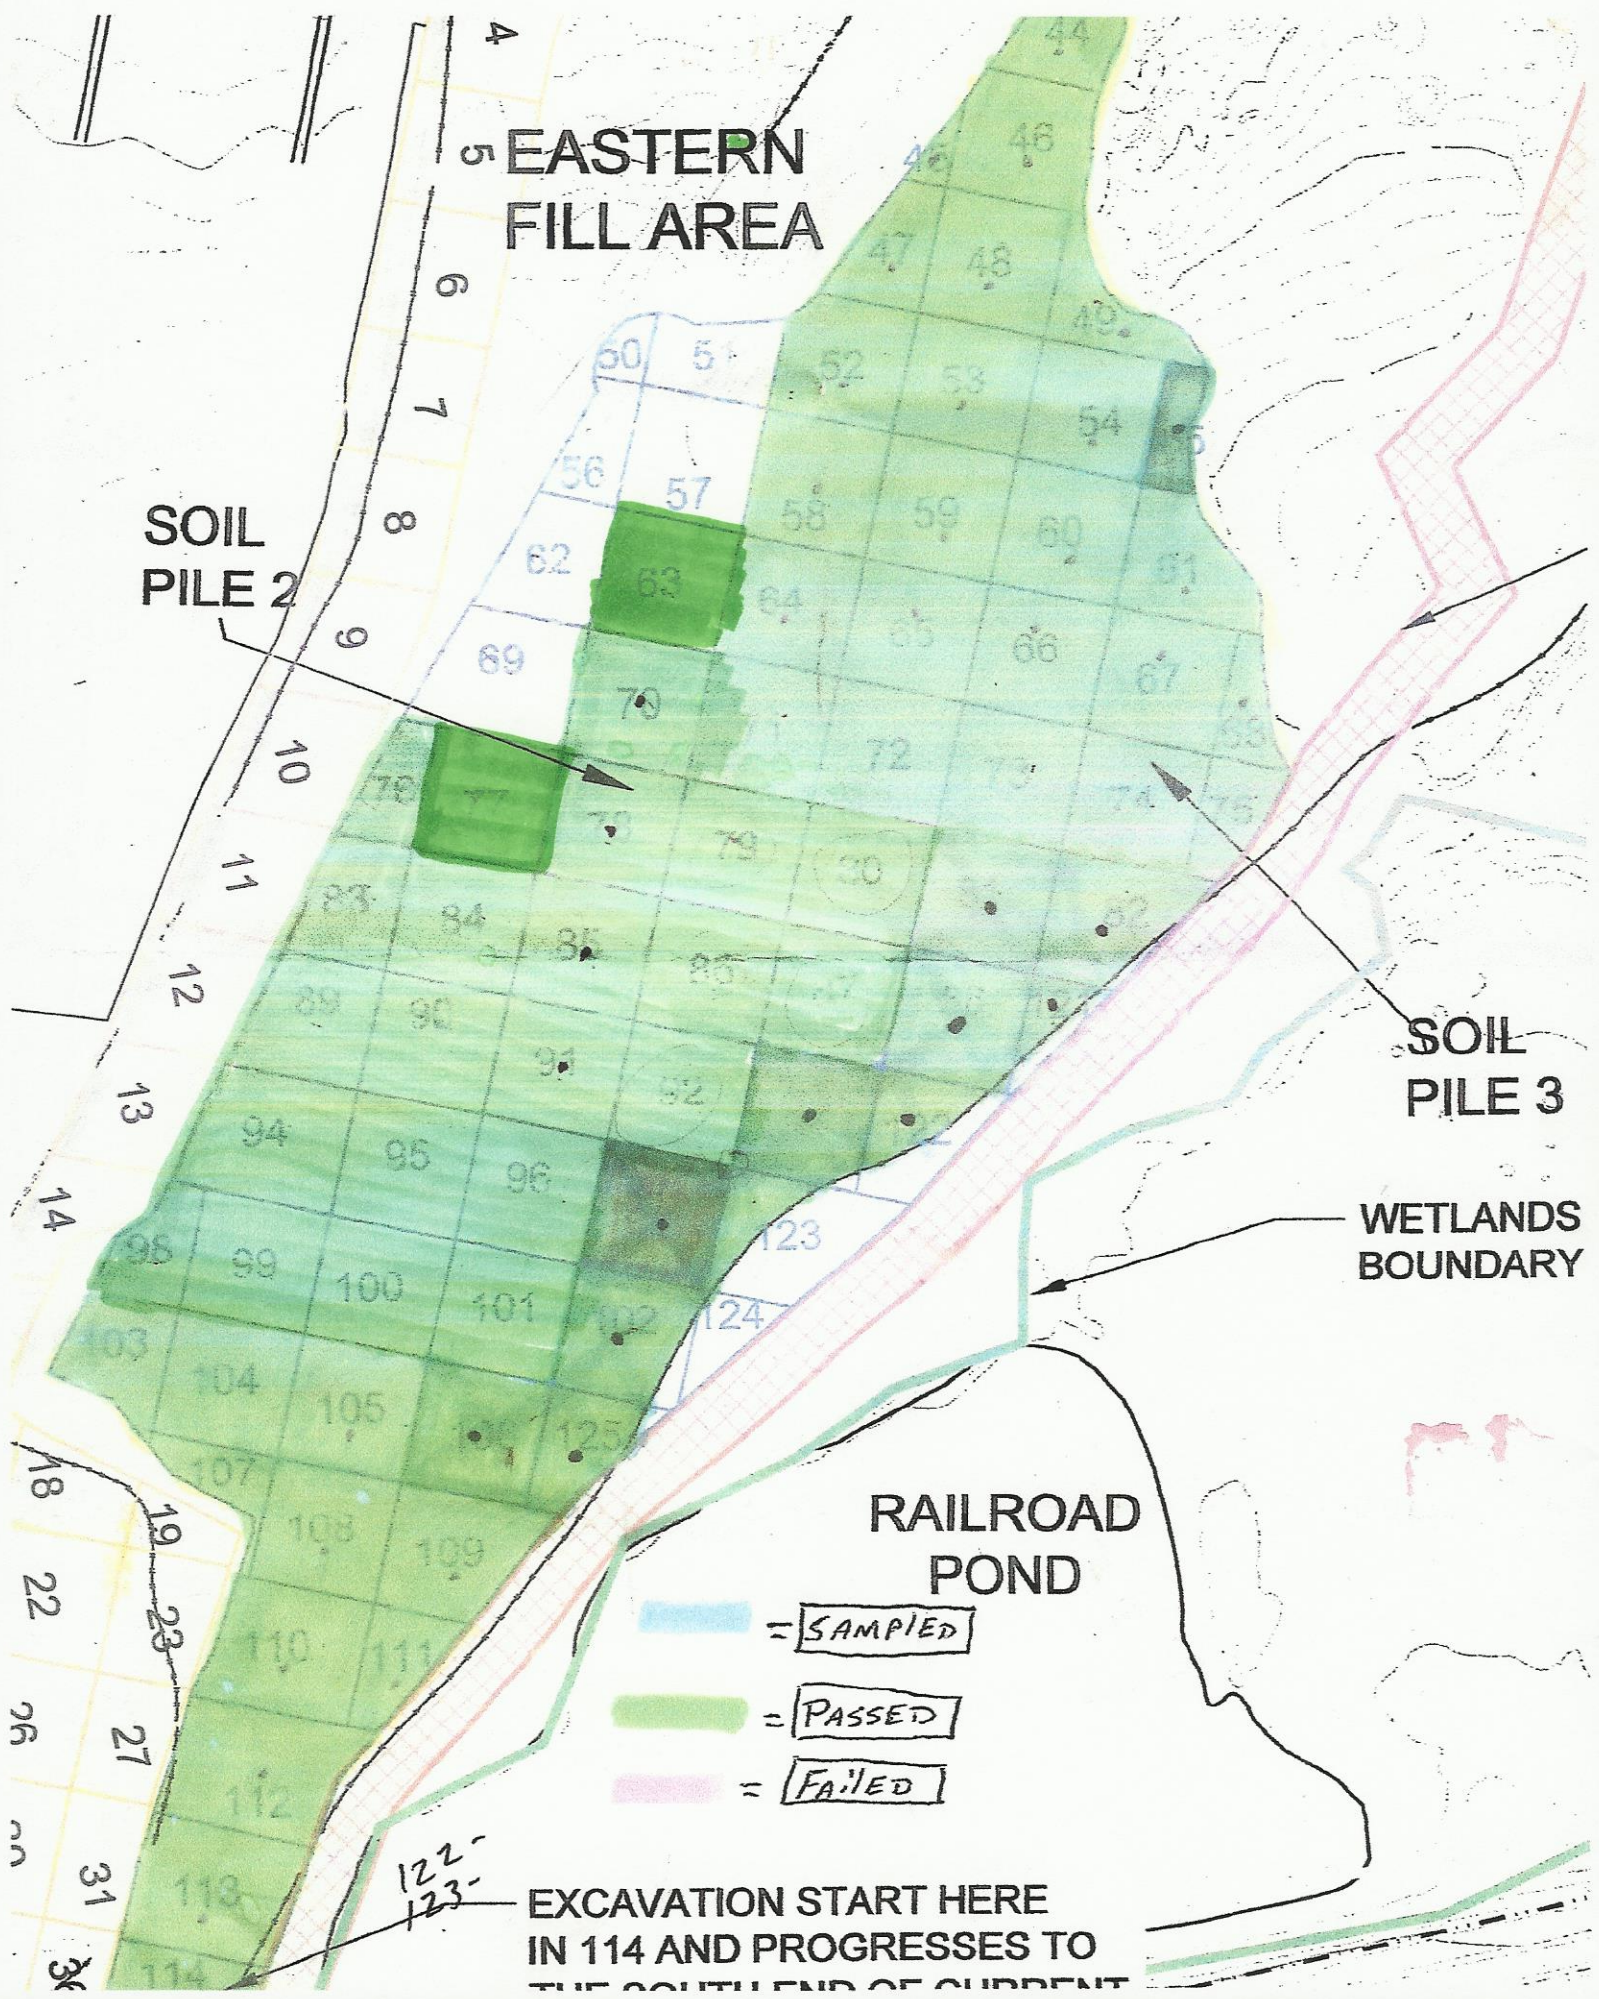

# EASTERN FILL AREA

SOIL  
PILE 2

SOIL  
PILE 3

WETLANDS  
BOUNDARY

RAILROAD  
POND

EXCAVATION START HERE  
IN 114 AND PROGRESSES TO  
THE SOUTHEAST END OF CURRENT

= SAMPLED

= PASSED

= FAILED

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, October 2, 2013**

**1:00 p.m. ET**


Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of September 30, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Re-Treating pile 318
  - d. Continue hauling treated material to CC as piles pass (moving 319-321)
  - e. Continue pressure-washing large rocks, metal, concrete
  - f. Continue backfilling eastern fill area
3. Schedule (Week of October 7, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
4. Administrative Issues
5. Open Discussion
6. Notes-As of 10/2/13 all Eastern fill grids have passed 44 thru 114, 121 thru 123, 18B, 125.  
  
PSV1-PSV-317 have all been treated and placed in CC.  
  
PSV-296 and PSV-297 used in floor of new treatment pad



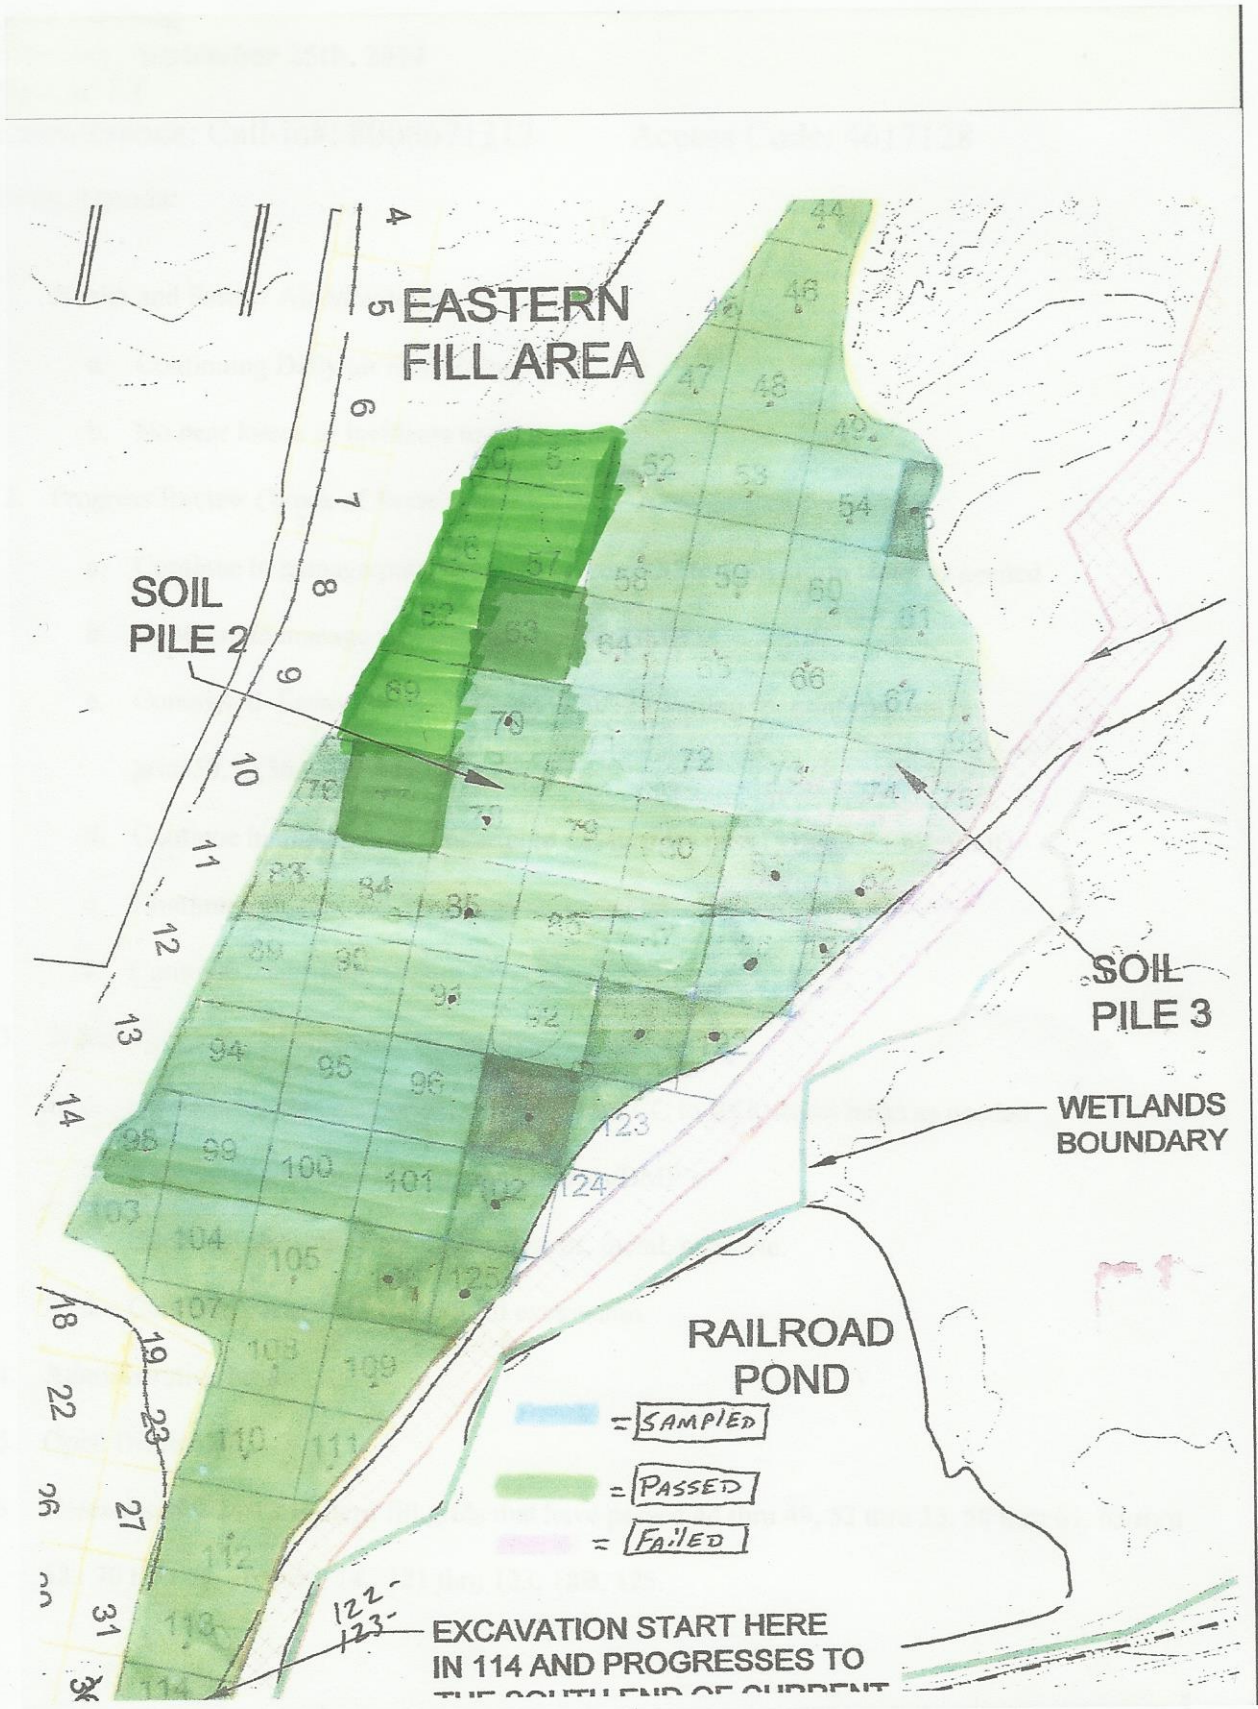

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, October 9, 2013**

**11:30 a.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of October 7, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Breaking slag buttons for disposal
  - d. Moved 319,320,321 treated material to CC
  - e. Continue pressure-washing large rocks, metal, concrete
  - f. Replace silt fence East of imported fill stockpile
  - g. Grading eastern fill area
3. Schedule (Week of October 14, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
  - d. Seed Eastern fill area and Under drain manhole area
  - e. Install silt fence around crushed rock piles
4. Administrative Issues
5. Open Discussion
6. Notes-As of 10/9/13 all Eastern fill grids have passed 44 thru 114, 121 thru 123, 18B, 125.



PSV1-PSV-317, 319-321 have all been treated and placed in CC.

PSV-296 and PSV-297 used in floor of new treatment pad

Waiting on results for Pile 318 and 322

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, October 16, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of October 14, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Slag buttons are broken up and waiting for disposal
  - d. Retreated PSV-318-R-2
  - e. Continue pressure-washing large rocks, metal, concrete
  - f. Seeding Eastern fill foot print
  - g. Installing silt fence around crushed rock pile in Eastern fill area
  - h. Haul PSV-318-R-2 to CC
3. Schedule (Week of October 21, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
4. Administrative Issues
5. Open Discussion
6. Notes-As of 10/9/13 all Eastern fill grids have passed 44 thru 114, 121 thru 123, 18B, 125.  
PSV1-PSV-317, 319-322 all have been treated and placed in CC.

PSV-296 and PSV-297 used in floor of new treatment pad.

PSV-318-R-2 waiting for result

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, October 23, 2013**

**11:30 a.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of October 21, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete
  - d. Installing silt fence around crushed rock pile in Eastern fill area
  - e. PSV-318-R-2 passed/ hauled into CC
  - f. Continue pressure-washing large rocks, metal, concrete.
3. Schedule (Week of October 28, 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
  - d. Test pits in front yard (30th )
4. Administrative Issues
5. Open Discussion
6. Notes-As of 10/23/13 all Eastern fill grids have passed 44 thru 114, 121 thru 123, 18B, 125.  
PSV1-PSV-322 all have been treated and placed in CC.  
PSV-296 and PSV-297 used in floor of new treatment pad.

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, October 30, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of October 28, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete
  - d. Loaded lead buttons for disposal
  - e. Continue pressure-washing large rocks, metal, concrete
  - f. Begin Test pitting in front yard of RSR
  - g. Begin stream work after test pits are completed
3. Schedule (Week of November 4 , 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
4. Administrative Issues
5. Open Discussion
6. Notes

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, November 6, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of November 4, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete
3. Schedule (Week of November 11 , 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
4. Administrative Issues
5. Open Discussion
6. Notes

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, November 13, 2013**

**11:30 a.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of November 11, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete
3. Schedule (Week of November 18 , 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
4. Administrative Issues
5. Open Discussion
6. Notes

**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, November 20, 2013**

**1:30 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
  - a. Continuing Daily air monitoring
  - b. No near losses or incidents to report.
2. Progress Review (Week of November 18, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete
3. Schedule (Week of November 25 , 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
4. Administrative Issues
5. Open Discussion
6. Notes



**Revere Smelting & Refining Site, OU1, Phase 2B RA  
Middletown, NY  
Weekly Meeting**

**Wednesday, December 4, 2013**

**2:00 p.m. ET**

Teleconference: Call-in#: 8008671317

Access Code: 4617128

**Meeting Agenda:**

1. Health and Safety/ Air Monitoring
2. Progress Review (Week of December 2, 2013)
  - a. Continue to manage/pump rain water from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete
3. Schedule (Week of December 9 , 2013)
  - a. Continue to manage/pump rainwater from CC to RSR storm tanks as needed
  - b. Continue to manage soil erosion controls/BMP's
  - c. Continue pressure-washing large rocks, metal, concrete.
4. Administrative Issues
5. Open Discussion
6. Notes

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, February 12, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of February 10, 2014)
  - Excavation area's cleared of trees-9,8,11,12,7,6,K-18,AZ5,5,3,21
  - Excavation area's with roads completed-11,12
  - Currently working on clearing area 2
3. Schedule (Week of February 17, 2014)
  - Building roads to area's 6,2,3,5
  - Complete roads in area's 8,7
  - Clear area 20, 13
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion-Removal of excavation area 9

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Wednesday, February 19, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
  - Foot injury incident
2. Progress Review (Week of February 17, 2014)
  - Roads built and completed this week 8, 7 and 6
  - Currently working on road to 2, 21, 3 and 5
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of February 24, 2014)
  - Building roads to area's- 3, 5 and 13
  - Complete roads in area's 3, 5 and 13
  - Clear area 20, 13
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Excavation area's cleared of trees-9, 8, 11, 12, 7, 6, K-18, AZ5, 5, 3, 21, 2
  - Excavation area's with roads completed- 11, 12, 8, 7 and 6

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, February 26, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of February 24<sup>th</sup>, 2014)
  - Roads built and completed this week 2
  - Currently working on road to 3 and 5
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of March 3<sup>rd</sup>, 2014)
  - Building roads to area's- 3, 5 and 13
  - Complete roads in area's 3, 5 and 13
  - Clear area 20, 13
  - Start clearing area's south of tracks pending approval
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Excavation area's cleared of trees-9, 8, 11, 12, 7, 6, K-18, AZ5, 5, 3, 21, 2
  - Excavation area's with roads completed- 2, 11, 12, 8, 7 and 6

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, March 5<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 3<sup>rd</sup>, 2014)
  - Roads built and completed this week were 3 and 5
  - Cleared area 20
  - Finish clearing trees for exaction area's in 3 and 5
  - Surveyor staking out Southside of tracks for roads and tree clearing
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of March 10<sup>th</sup>, 2014)
  - Surveyor staking out Southside of tracks for roads and tree clearing
  - Surveyor to place stakes in 13 for tree clearing and road
  - Start clearing area's south of tracks pending approval
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Excavation area's cleared of trees-9, 8, 11, 12, 7, 6, K-18, AZ5, 5, 3, 21, 2, 20
  - Excavation area's with roads completed- 2, 11, 12, 8, 7, 6, 3 and 5

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, March 13<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 10<sup>th</sup>, 2014)
  - Cleared area 13
  - Built Road from CC to 12 and 13
  - Surveyor finished staking out perimeter south of tracks
  - Begin clearing trees south of tracks pending access
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of March 17<sup>th</sup>, 2014)
  - Surveyor staking out area 9
  - Continue clearing trees south of tracks pending access
  - Clear area 9
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Excavation area's cleared of trees-9, 8, 11, 12, 13, 7, 6, K-18, AZ5, 5, 3, 21, 2, 20
  - Excavation area's with roads completed- 2, 11, 12, 13, 21, 8, 7, 6, 3 and 5

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Wednesday, March 19<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 17<sup>th</sup>, 2014)
  - Surveyor staked out area 19
  - Cleared area 19, 15 and 16b in front lawn
  - Begin clearing area 16a
  - Begin clearing trees south of tracks pending access
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of March 24<sup>th</sup>, 2014)
  - Continue clearing trees south of tracks pending access
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Excavation area's cleared of trees-9, 8, 11, 12, 13, 7, 6, K-18, AZ5, 5, 3, 21, 2, 20,15 , 19
  - Excavation area's with roads completed- 2, 11, 12, 13, 21, 8, 7, 6, 3 and 5

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, March 26<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 24<sup>th</sup>, 2014)
  - Cleared area's 28, 27, 38A, 25, 24, 29, 23, 38B, 29, 33, 34, 36, 37, 35 and 38D south of the tracks
  - Continue to clear roads south of the tracks and 38C south stream
  - Begin Clearing 16a front lawn North stream
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of March 31<sup>st</sup>, 2014)
  - Finish clearing any trees needing to be cut on Monday.
  - Begin constructing entrance for roads south of tracks
  - Begin building roads south of tracks
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Excavation area's cleared of trees-9, 8, 11, 12, 13, 7, 6, K-18, AZ5, 5, 3, 21, 2, 20, 15, 19, 28, 27, 38A, 25, 24, 29, 23, 38B, 29, 33, 34, 36, 37, 35, 38D.
  - Excavation area's with roads completed- 2, 11, 12, 13, 21, 8, 7, 6, 3 and 5



**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, April 2<sup>nd</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 31<sup>st</sup>, 2014)
  - Cleared area's 38C (stream), 16B (stream), 40 and 17.
  - Finished clearing trees on Southside roads.
  - Finished clearing all trees needing to be cut throughout entire site before the 31<sup>st</sup> deadline.
  - Began constructing entrances on south side of track roads.
  - Continue building roads on Southside of tracks.
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of April 7<sup>th</sup>, 2014)
  - Continue building roads Southside of tracks.
  - Build stream crossings Southside of tracks.
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - All tree clearing is finished.
  - Excavation area's with roads completed- 2, 11, 12, 13, 21, 8, 7, 6, 3, 5, and south side of tracks construction entrances are complete.

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, April 9<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of April 7<sup>th</sup>, 2014)
  - Continue building roads on Southside of tracks.
  - Completed road from Westside entrance south of tracks to area 33 and 34
  - Building road from Eastside entrance along stream 38C to area 27 and 28
  - Began building stream crossing over 38A stream into area 25
  - Delineating area 9
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of April 14<sup>th</sup>, 2014)
  - Continue building roads Southside of tracks.
  - Build stream crossings Southside of tracks.
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Approval for digging?
  - All tree clearing is finished.
  - Excavation area's with roads completed- 2, 11, 12, 13, 21, 8, 7, 6, 3, 5, and south side of tracks construction entrances are complete.

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Wednesday, April 16<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of April 14<sup>th</sup>, 2014)
  - Continue building road from Eastside entrance along stream 38C to area 27 and 28
  - Began building stream crossing over 38A stream into area 25
  - Finish delineating area 9
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of April 21<sup>st</sup>, 2014)
  - Continue building roads Southside of tracks.
  - Build stream crossings Southside of tracks.
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - All tree clearing is finished.
  - Excavation area's with roads completed- 2, 11, 12, 13, 21, 8, 7, 6, 3, 5, south side of tracks construction entrances are complete, and west side road south of tracks is complete.

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Wednesday, April 23<sup>rd</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of April 21<sup>st</sup>, 2014)
  - Stopped building roads South of railroad tracks due to wet conditions
  - Relocating concrete footing to make room for the slurry wall
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of April 28<sup>th</sup>, 2014).
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - All tree clearing is finished.
  - Excavation area's with roads completed- 2, 11, 12, 13, 21, 8, 7, 6, 3, 5, south side of tracks construction entrances are complete, and west side road south of tracks is complete.

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, April 30<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of April 28<sup>th</sup>, 2014)
  - Surveyor laid out grids 43, 115, 116 and area 2 up to wetland boundary
  - Surveyor staked out slurry wall center line
  - Relocated concrete slabs in preparation for slurry wall
  - Preparing to excavate grids 43, 115, 116 & Area 2 up to wetland boundary
  - Abandon Monitoring Wells MW-23S and MW-23D
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of May 5<sup>th</sup>, 2014)
  - Begin excavating grids 43, 115, 116 & area 2 up to wetland boundary
  - Import backfill
  - Begin mobilization slurry wall supplies and equipment
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Wednesday, May 7<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 5<sup>th</sup>, 2014)
  - Began excavating grids 43, 115, 116 & up to wetland boundary
  - Importing backfill
  - Collecting confirmation samples in grids 43, 115 & 116
  - Treating excavated material
  - Abandoned Monitoring Wells MW-23S, MW-23D and PZ-14
  - Possibly survey limits of excavation for grids 43, 115 and 116
  - Mobilizing slurry wall material and equipment
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of 12<sup>th</sup>, 2014)
  - Mobilizing PC800 for digging slurry wall trench
  - 70 Ton crane coming Tuesday to set-up PC800
  - Continue to bring in slurry wall materials
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, May 14<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 12<sup>th</sup>, 2014)
  - Finished excavating grids 43, 115, 116 up to wetland boundary
  - Importing backfill for grids 43, 115, 116 up to wetland boundary and working platform for slurry wall
  - Treated excavated material
  - Survey in south end of slurry wall alignment after working platform is complete
  - Mobilizing slurry wall material and equipment
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of 19<sup>th</sup>, 2014)
  - Begin slurry wall excavation Monday
  - Pump slurry from mixing pad to trench
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Thursday, May 22<sup>nd</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 19<sup>th</sup>, 2014)
  - Began slurry wall excavation 316+03
  - Completed slurry wall excavation from 316+03 to 315+00
  - Completed backfill from 316+03 to 315+00
  - Continue slurry wall excavation form 315+00
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of 26<sup>th</sup>, 2014)
  - No work Monday
  - Continue slurry wall excavation on 5/27/14
  - Pump slurry from mixing pad to trench
  - Backfill trench as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, May 28<sup>th</sup>, 2014**  
**1:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 26<sup>th</sup>, 2014)
  - Completed slurry wall excavation from 316+03 to 310+00
  - Completed backfill from 316+03 to 310+50
  - Continue slurry wall excavation form 310+00
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of June 2<sup>nd</sup>, 2014)
  - Continue slurry wall excavation
  - Pump slurry from mixing pad to trench
  - Backfill trench as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Wednesday, June 4<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 2<sup>nd</sup>, 2014)
  - Completed slurry wall excavation and backfill
  - Digging clay cap trench
  - Bringing in clay material for cap
  - Placing and compacting clay cap
  - Cleaning equipment and getting ready for demobilization
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of June 9<sup>th</sup>, 2014)
  - Finish clay cap if necessary
  - Demobilizing equipment needed for slurry wall
  - As-built slurry wall center line
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Wednesday, June 11<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 9<sup>th</sup>, 2014)
  - Finished Clay Cap except for WESP area
  - Surveyor to as-built slurry wall alignment
  - Surveyor to shoot elevations in WESP along slurry wall alignment
  - Electrician reconnecting power lines and trailers
  - Moved treated piles PSV-323,324,325 & 326 from treatment cell to containment cell
  - Graded out containment cell
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of June 16<sup>th</sup>, 2014)
  - Cap WESP area
  - Mobilize on road truck to continue building roads south of tracks
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA  
Middletown, NY  
Weekly Meeting  
Thursday, June 19<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 23<sup>rd</sup>, 2014)
  - Cap WESP area
  - Continue building roads south of tracks
  - Build stream crossing over stream 38A
  - Finished road over cap in boneyard and north of tanks
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of June 30<sup>th</sup>, 2014)
  - Finish cap in WESP area
  - Continue to build roads south of tracks
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, June 26<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 23<sup>rd</sup>, 2014)
  - Cap WESP area
  - Continue building roads south of tracks
  - Build stream crossing over stream 38A
  - Finished road over cap in boneyard and north of tanks
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of June 30<sup>th</sup>, 2014)
  - Finish cap in WESP area
  - Continue to build roads south of tracks
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, July 9<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 7<sup>th</sup>, 2014)
  - Finished slurry wall cap in WESP area
  - Begin installing silt fence on down gradient slopes in north areas
  - Take down fence along railroad pond stream to prepare for excavation
  - Begin laying out and grading concrete road to WESP
  - Bring in place and compact road base for concrete road to WESP
  - Continue building roads south of tracks
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of July 14<sup>th</sup>, 2014)
  - Begin digging area 2 north of rail road pond
  - Install concrete road to WESP
  - Continue to build roads south of tracks
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, July 16<sup>th</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 14<sup>th</sup>, 2014)
  - Finished installing silt fence on down gradient slopes in north areas
  - Begin excavation along railroad pond stream
  - Begin treating excavated material
  - Begin placing and compacting road base for concrete road to WESP
  - Continue building roads south of tracks
  - Begin receiving reagent for treatment of excavated material
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of July 21<sup>st</sup>, 2014)
  - Continue to excavate material along railroad pond stream
  - Continue to treat excavated material
  - Begin setting forms and pouring concrete for access road to WESP
  - Continue to build roads south of tracks
  - Pump water from CC to RSR storm tanks
  - Begin placing and compacting treated material in CC
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Wednesday, July 23<sup>rd</sup>, 2014**  
**11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 21<sup>st</sup>, 2014)
  - Began excavation along railroad pond stream
  - Began treating excavated material
  - Finish placing and compacting road base for concrete road to WESP
  - Begin placing rebar for concrete road
  - Pouring Concrete Road to WESP on Saturday
  - Continue building roads south of tracks
  - Continue receiving reagent for treatment of excavated material
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of July 28<sup>th</sup>, 2014)
  - Finish excavating material along railroad pond stream
  - Begin receiving habitat subgrade fill, wetland topsoil and upland topsoil
  - Begin placing and compacting fill and topsoil in excavated area
  - Begin excavating material in area 8
  - Continue to treat excavated material
  - Continue building roads south of tracks
  - Begin placing and compacting treated material in CC
  - Pump water from CC to RSR storm tanks



4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, July 30<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 28<sup>th</sup>, 2014)
  - Finished excavation along railroad pond stream, waiting on confirmation results
  - Finished treating excavated material, waiting on results
  - Finished concrete road to WESP
  - Continue building roads south of tracks
  - Begin hauling treated material into containment cell, pending results
  - Surveyor on-site to shoot limits of excavation, Thursday
  - Begin receiving habitat subgrade fill
  - Begin placing and compacting habitat subgrade fill in excavation along railroad pond stream
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of August 4<sup>th</sup>, 2014)
  - Continue receiving habitat subgrade fill
  - Continue placing and compacting habitat subgrade fill in excavated area
  - Begin excavating in 20
  - Continue building roads south of tracks
  - Continue placing and compacting treated material in CC
  - Pump water from CC to RSR storm tanks

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, August 6<sup>th</sup> 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 4<sup>th</sup>, 2014)
  - Begin receiving habitat subgrade fill
  - Begin placing and compacting habitat subgrade fill in excavation along railroad pond stream
  - Utility Locator on-site to identify location of water line in area 20.
  - Begin excavating area 20
  - Treat excavated material from area 20
  - Finish building roads south of the tracks
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of August 11<sup>th</sup>, 2014)
  - Continue receiving habitat subgrade fill
  - Continue placing and compacting habitat subgrade fill in excavated area
  - Finish excavating in 20
  - Continue treating excavated material from area 20
  - Bring surveyor in to shoot limits of excavation in area 20
  - Continue building roads south of tracks
  - Continue placing and compacting treated material in CC as piles pass
  - Pump water from CC to RSR storm tanks

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, August 14<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 11<sup>th</sup>, 2014)
  - Continued Backfilling Area 2 North of railroad pond stream
  - Continued placing and compacting habitat subgrade fill in Area 2 North of railroad pond stream
  - Finished excavating area 20
  - Treated excavated material from area 20 (PSV-336-338)
  - Surveyor on-site to shoot limits of excavation and sample locations in area 20
  - Begin excavating in area 11
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of August 18<sup>th</sup>, 2014)
  - Continue receiving habitat subgrade fill and begin receiving wetland topsoil
  - Continue placing and compacting habitat subgrade fill in area 2 North of railroad pond stream
  - Begin backfilling area 20 once confirmation samples are confirmed clean
  - Begin placing and compacting treated material in CC as piles pass
  - Continue building roads south of tracks
  - Pump water from CC to RSR storm tanks
4. Administrative Issues

## 5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, August 20<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 18<sup>th</sup>, 2014)
  - Finished backfilling area 2 North of the railroad tracks and building working platform
  - Finished excavating area 11
  - Moved treated piles PSV-336-338 and Area 11 material into containment cell
  - Begin backfilling, placing and compacting area 20
  - Begin excavating area 8
  - Begin backfilling area 11 pending floor confirmation results
  - Finished roads south of the tracks
  - Stockpiling Habitat Subgrade and Wetland Topsoil
  - Pumping water from CC to RSR storm tanks
3. Schedule (Week of August 25<sup>th</sup>, 2014)
  - Continue stockpiling wetland topsoil
  - Backfill area 8 pending results from confirmation samples
  - Begin excavating area 7
  - Shut-down for labor day weekend, two guys will remain on site to pump water
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, August 27<sup>th</sup>, 2014  
1:30 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 25<sup>th</sup>, 2014)
  - Finished Excavating area 7 and 6
  - Finished backfilling area 11
  - Continued stockpiling Habitat Subgrade and Wetland Topsoil
  - Pumping water from CC to RSR storm tanks
  - Surveyor on-site shooting post excavation and sample locations
  - Prepare for Labor Day shut-down
3. Schedule (Week of September 1<sup>st</sup>, 2014)
  - Move piles C-Area8-Stockpile-1&2, C-Area7-Stockpile-1, and C-Area6-Stockpile-1, pending confirmation results into CC
  - Backfill areas 8,7 & 6 pending confirmation results
  - Begin excavating areas 12 & 13
  - Begin hand digging areas AZ-5 and K-18
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, September 10<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 8<sup>th</sup>, 2014)
  - Finished backfilling area 8, 7, 13 and 12
  - Finish backfilling area 6
  - Continued stockpiling Wetland Topsoil and Upland Topsoil
  - Surveyor on-site shooting post excavation and sample locations
  - Began hand digging areas K-18 and AZ-5
  - Begin excavating area 5
  - Began backfilling and compacting WESP area with select fill
  - Treated C-Area 7-Stockpile making it PSV-339
  - Graded and compacted piles C-Area8-Stockpile-1&2 and C-Area6-Stockpile in CC
  - Move piles PSV-339, C-Area6-Stockpile-2 and C-Area12/13-Stockpile-1 into CC  
pending confirmation results
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of September 15<sup>th</sup>, 2014)
  - Begin excavating area 3
  - Begin backfilling hand dig area K-18, AZ-5 and area 5 pending confirmation results
  - Treat piles as needed
  - Finish backfilling and compacting WESP area with select fill

- Kick off-meeting with MLS
  - Surveyor on-site shooting post excavation and sample locations
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, September 17<sup>th</sup>, 2014  
2:30 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 15<sup>th</sup>, 2014)
  - Hydro Seeded area 11,8,7,6,12 & 13
  - Finished excavating area K-18, AZ-5 and area 5
  - Finish excavating area 3
  - Continued stockpiling Wetland Topsoil
  - Surveyor on-site shooting post excavation and sample locations
  - Finish backfilling and compacting WESP area with select fill
  - Begin backfilling area 5, K-18 and AZ-5
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of September 22<sup>nd</sup>, 2014)
  - Finish backfilling areas K-18, AZ-5, 5 and 3
  - Haul material from treatment pad to CC
  - Begin excavating area 2
  - Discuss stream excavation
  - Treat piles as needed
  - Surveyor on-site shooting post excavation and sample locations
  - Pump water from CC to RSR storm tanks
4. Administrative Issues

## 5. Open Discussion

- Stream excavation

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, September 24<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 22<sup>nd</sup>, 2014)
  - Finished excavating area 3
  - Finished backfilling K-18 & and 5
  - Begin backfilling AZ-5 and area 3
  - Continued stockpiling Wetland Topsoil & Habitat Subgrade
  - Surveyor on-site shooting post excavation and sample locations
  - Finished backfilling and compacting WESP area with select fill
  - Finish final grade on WESP after Chazen adds final grade stakes
  - Moved C-Area5-Stockpile-1 and C-Area3-Stockpile-1 into CC
  - Moving C-Area3-Stockpile-1&2
  - Begin excavating area 2
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of September 29<sup>th</sup>, 2014)
  - Begin excavating area 4 (stream)
  - Continue excavating area 2
  - Continue importing Wetland Topsoil and Habitat Subgrade
  - Surveyor on-site shooting post excavation and sample locations of stream
  - Pump water from CC to RSR storm tanks

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, September 30<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 29<sup>th</sup>, 2014)
  - Finished backfilling area 3 and AZ-5
  - Began excavating area 2
  - Continued stockpiling Wetland & Upland Topsoil along with Habitat Subgrade
  - Surveyor on-site shooting post excavation and sample locations
  - Setup stream pump around for area 4 pending approval
  - Begin excavating area 4 (stream) pending approval
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of October 6<sup>th</sup>, 2014)
  - MLS on-site to hydro seed areas K-18, 5, AZ-5 and 3.
  - Backfill area 4 (stream) with habitat subgrade if needed
  - MLS to restore area 4 (stream)
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC and compact
  - Surveyor on-site shooting post excavation and sample locations of stream
  - Pump water from CC to RSR storm tanks
4. Administrative Issues



## 5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, October 8<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 6<sup>th</sup>, 2014)
  - Continue excavating area 2
  - Continued stockpiling Wetland & Upland Topsoil along with Habitat Subgrade
  - Begin backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Moving stockpiles 1,2,3,4 & 5 from area 2 into CC
  - Setup stream pump around for area 4 pending approval
  - Pump water from CC to RSR storm tanks
  - Begin bringing in equipment for slurry wall extensions
3. Schedule (Week of October 13<sup>th</sup>, 2014)
  - Begin excavating area 4 pending approval
  - MLS on-site to hydro seed areas K-18, 5, AZ-5 and 3
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations of stream
  - Pump water from CC to RSR storm tanks

- Continue bringing in equipment for slurry wall extensions and begin putting together the  
PC800 Excavator
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, October 16<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 13<sup>th</sup>, 2014)
  - Excavated area 4 (stream)
  - Continuing to pump around area 4 (stream) until restored.
  - Continue excavating area 2
  - Continued stockpiling Wetland & Upland Topsoil along with Habitat Subgrade
  - Continue backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Moved stockpiles 6,7 and 8 from area 2 into CC
  - Continue moving stockpiles from area 2 and stream into CC as they pass
  - Pump water from CC to RSR storm tanks
  - Begin slurry wall tie-in under railroad tracks on Saturday 10/18/14
3. Schedule (Week of October 20<sup>th</sup>, 2014)
  - MLS on-site to hydro seed areas K-18, 5, AZ-5 and 3
  - MLS to restore area 4 (stream)
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations of stream

- Pump water from CC to RSR storm tanks
  - Begin slurry wall tie-in at RSR front gate on Saturday the 25<sup>th</sup>.
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Tuesday, October 21<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 20<sup>th</sup>, 2014)
  - Waiting on results for area 4 (stream) to backfill banks with habitat subgrade
  - Continuing to pump around area 4 (stream) until restored.
  - MLS on-site to hydro seed areas K-18, 5, AZ-5 and 3.
  - MLS to restore area 4 (stream) pending results
  - Continue excavating area 2
  - Continued stockpiling Wetland & Upland Topsoil along with Habitat Subgrade
  - Continue backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Treated stockpile 9 from area 2
  - Moved stockpile 10 from area 2 into CC
  - Waiting on results from stockpiles to move into CC
  - Pump water from CC to RSR storm tanks
  - Finished slurry wall tie-in under railroad tracks on Saturday 10/18/14
  - Begin slurry wall tie-in at RSR front gate on Saturday 10/25/14
3. Schedule (Week of October 27<sup>th</sup>, 2014)
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade

- Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations of stream
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, October 30<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 27<sup>th</sup>, 2014)
  - Waiting on decision for area4 (stream) to backfill banks with habitat subgrade
  - Continuing to pump around area 4 (stream) until restored.
  - MLS to restore area 4 (stream) pending decision
  - Continue excavating area 2
  - Continued stockpiling Wetland & Upland Topsoil along with Habitat Subgrade
  - Continue backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Treated PSV344 and PSV345 from area 2
  - Moved stockpile 12 and PSV343 from treatment pad into CC
  - Waiting on results from stockpiles to move into CC
  - Pump water from CC to RSR storm tanks
  - Finished slurry wall tie-in at front gate on Saturday 10/25/14
3. Schedule (Week of Novemebr 3<sup>rd</sup>, 2014)
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations of stream



- Pump water from CC to RSR storm tanks
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, November 5<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of November 3<sup>rd</sup>, 2014)
  - Waiting on results for area4 (stream) to backfill banks with habitat subgrade
  - Continuing to pump around area 4 (stream) until restored.
  - MLS to restore area 4 (stream) pending results
  - Continue excavating area 2
  - Continued stockpiling Wetland Topsoil and Habitat Subgrade
  - Continue backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Treated PSV346, 347, 348, 349 from area 2
  - Moved stockpile 15 from treatment pad into CC
  - Pump water from CC to RSR storm tanks
  - Begin Pumping water from pond into RSR storm tank
3. Schedule (Week of November 10<sup>th</sup>, 2014)
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations of stream
  - Pump water from CC to RSR storm tanks

- Pump water from pond to RSR storm tank.
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, November 12<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of November 10<sup>th</sup>, 2014)
  - Backfilling area 4 (stream) banks with habitat subgrade
  - MLS restoring stream
  - Continuing to pump around area 4 (stream) until restoration is complete
  - Continue excavating area 2
  - Continued stockpiling Wetland Topsoil and Habitat Subgrade
  - Continue backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Treated PSV350, 351 and 352 from area 2
  - Moved stockpiles PSV 346, 347, 348 and 349 from treatment pad into CC
  - Pump water from CC to RSR storm tanks
  - Began Pumping water from pond into RSR storm tank
3. Schedule (Week of November 17<sup>th</sup>, 2014)
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations of stream
  - Pump water from CC to RSR storm tanks

- Pump water from pond to RSR storm tank.
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, November 19<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of November 17<sup>th</sup>, 2014)
  - Finished restoring area 4 (stream)
  - Continue excavating area 2
  - Continued stockpiling Wetland Topsoil and Habitat Subgrade
  - Continue backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Treated PSV353-359 from area 2
  - Moved stockpiles PSV 350-353 from treatment pad into CC
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water from pond into RSR storm tank
3. Schedule (Week of November 24<sup>th</sup>, 2014)
  - Continue excavating area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank.
4. Administrative Issues

## 5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, December 3<sup>rd</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of December 1<sup>st</sup>, 2014)
  - Finish excavating area 2A
  - Continue backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Treated PSV360-367 from area 2
  - Moving stockpiles PSV 360-367 from treatment pad into CC
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water from pond into RSR storm tanks
3. Schedule (Week of December 8<sup>th</sup>, 2014)
  - Finish Backfilling Area 2
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, December 10<sup>th</sup>, 2014  
3:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of December 8<sup>th</sup>, 2014)
  - Finish excavating area 2
  - Finish backfilling confirmed clean grids in area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Treated PSV368 from area 2
  - Graded out CC with stockpiles from treatment pad
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water from pond into RSR storm tanks
3. Schedule (Week of December 15<sup>th</sup>, 2014)
  - Begin roads in front lawn
  - Excavate finger roads in area 2, road that leads to areas 11 & 8 and also road to 12 & 13
  - Continue importing Wetland & Upland Topsoil along with Habitat Subgrade
  - Move stockpiles into CC pending results
  - Surveyor on-site shooting post excavation and sample locations
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, December 18<sup>th</sup>, 2014  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of December 15<sup>th</sup>, 2014)
  - Finished excavating finger roads and backfilling them
  - Finish backfilling in area 2
  - Lined grid Q20 South Sidewall along rail road property and backfilled
  - MLS on-site to hydro seed finger roads, area 3 west of stream and area 2
  - Surveyor on-site shooting post excavation and sample locations
  - Graded out CC with stockpiles from treatment pad
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water from pond into RSR storm tanks
3. Schedule (Week of December 22<sup>nd</sup>, 2014)
  - Prepare for shut-down from the 23<sup>rd</sup> to the 4<sup>th</sup> of January
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, January 07, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 5<sup>th</sup>, 2015)
  - Began building roads in front lawn area
  - Moved Stockpiles PSV-368, C-Area2-Stockpiles 16 & 17 and C-Areas8,11,12,13 – Stockpile 1 into CC
  - Grading out CC with stockpiles from treatment pad
  - Surveyor on-site shooting existing grade of pond
  - Begin building haul pad for trucks in pond
  - Begin digging pond
  - Begin digging front lawn once written approval is received from the town.
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
  - Continue Pumping water from Area 2A (marsh area) to RSR storm tanks
3. Schedule (Week of January 12<sup>th</sup>, 2015)
  - Continue digging pond
  - Continue digging front lawn
  - Stockpiling/Treating piles on treatment pad
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, January 14<sup>th</sup>, 2015  
2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 12<sup>th</sup>, 2015)
  - Began digging in pond
  - Waiting for characterization results from C-Area22-Stockpiles 1 & 2
  - Grading out CC
  - Surveyor on-site shooting grids in front lawn
  - Begin digging area 15 in front lawn
  - Begin digging FLA test pit location from 25' easement
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
  - Continue Pumping water from Area 2A (marsh area) to RSR storm tanks
3. Schedule (Week of January 19<sup>th</sup>, 2015)
  - Continue digging pond
  - Continue digging front lawn & test pits
  - Stockpiling/Treating piles on treatment pad
  - Begin hauling confirmed clean stockpiles from pad to CC
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, January 22<sup>nd</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 19<sup>th</sup>, 2015)
  - Continue digging pond
  - Waiting for characterization results from C-Area22-Stockpiles 3&4, C-Area22/15-Stockpiles 1, 2, 3&4.
  - Treated C-Area22-Stockpiles 1&2 and they are now PSV-369&370.
  - Begin hauling confirmed clean stockpiles from pad to CC
  - Grading out CC
  - Surveyor on-site post excavation samples in front lawn
  - Finish area 15 and move to area 40 and Test Pits
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
  - Continue Pumping water from Area 2A (marsh area) to RSR storm tanks
3. Schedule (Week of January 26<sup>th</sup>, 2015)
  - Continue digging pond
  - Continue digging front lawn & test pits
  - Stockpiling/Treating piles on treatment pad
  - Begin hauling confirmed clean stockpiles from pad to CC
  - Pump water from CC to RSR storm tanks

- Pump water from pond to RSR storm tank
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, January 28<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 26<sup>th</sup>, 2015)
  - Continue digging pond
  - Waiting for PSV-372,373,374,375,376 & 377
  - Begin hauling confirmed clean stockpiles from pad to CC
  - Grading out CC
  - Surveyor on-site post excavation samples in front lawn
  - Finished area 15, 40 and 17
  - Digging Test Pits in between Area 17 and 18
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
  - Continue Pumping water from Area 2A (marsh area) to RSR storm tanks
3. Schedule (Week of February 2<sup>nd</sup>, 2015)
  - Continue digging pond
  - Continue digging front lawn & test pits
  - Stockpiling/Treating piles on treatment pad
  - Begin hauling confirmed clean stockpiles from pad to CC
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank



4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, February 5<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of February 2<sup>nd</sup>, 2015)
  - Continue digging pond
  - Waiting for PSV-382
  - Hauling confirmed clean stockpiles from pad to CC
  - Grading out CC
  - Surveyor on-site post excavation samples in front lawn
  - Finished backfilling areas 15, 40 and 17
  - Continue excavating Test Pits in between Area 17 and 18
  - Excavate Test Pits starting at TP-11 down along drive
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
  - Continue Pumping water from Area 2A (marsh area) to RSR storm tanks
3. Schedule (Week of February 9<sup>th</sup>, 2015)
  - Continue digging pond
  - Finish digging and backfilling front lawn
  - Stockpiling/Treating piles on treatment pad
  - Continue hauling confirmed clean stockpiles from pad to CC
  - Pump water from CC to RSR storm tanks

- Pump water from pond to RSR storm tank
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, February 12<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of February 9<sup>th</sup> 2015)
  - Continue digging pond
  - Waiting for results for PSV385
  - Hauling confirmed clean stockpiles from pad to CC
  - Grading out CC
  - Surveyor on-site for post excavation samples in front lawn and along north side of drive
  - Finish excavating test pits starting at TP-11 down along drive
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
  - Continue Pumping water from Area 2A (marsh area) to RSR storm tanks
3. Schedule (Week of February 16<sup>th</sup>, 2015)
  - Continue digging pond
  - Finish backfilling front lawn
  - Stockpiling/Treating piles on treatment pad
  - Continue hauling confirmed clean stockpiles from pad to CC
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, February 19<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of February 16th, 2015)
  - Continue digging pond
  - Waiting for PSV-385
  - Grading out CC
  - Surveyor on-site post excavation samples in front lawn
  - Finished backfilling areas Test pit area
  - Finished Excavating Test Pits starting at TP-11 down along drive
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of February 23rd, 2015)
  - Continue digging pond
  - Finish backfilling front lawn
  - Stockpiling/Treating piles on treatment pad
  - Continue hauling confirmed clean stockpiles from pad to CC
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, March 5<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 2<sup>nd</sup>, 2015)
  - Finished backfilling front lawn
  - PSV-387 on treatment pad ready to be moved to CC
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of March 9<sup>th</sup>, 2015)
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, March 19<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 16<sup>th</sup>, 2015)
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of March 23<sup>rd</sup>, 2015)
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, April 2<sup>nd</sup>, 2015  
2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 30<sup>th</sup>, 2015)
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of April 6<sup>th</sup>, 2015)
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, April 16th, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of April 13<sup>th</sup>, 2015)
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of April 20<sup>th</sup>, 2015)
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, May 7<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 4<sup>th</sup>, 2015)
  - Start pump around on Western Stream 16A
  - Begin excavating Western Stream 16A
  - Treating/Stockpiling Area 16A on treatment pad
  - Finish backfilling around trees in front lawn (soil settled since winter)
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of May 11<sup>th</sup>, 2015)
  - Finish excavating Area 16A if not complete
  - Treating/Stockpiling Area 16A on treatment pad
  - Haul confirmed clean piles from pad to CC
  - Grade CC as needed
  - Begin backfilling stream as confirmation samples come back
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, May 13<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 11<sup>th</sup>, 2015)
  - Excavated road from area 5 to stream crossing
  - Backfilled road from area 5 to stream crossing
  - Surveyor onsite shooting post excavation and sample locations in area 16a
  - Backfilling stream 16a as confirmation samples come back
  - Treating/Stockpiling Area 16A on treatment pad
  - Finished backfilling around trees in front lawn (soil settled since winter)
  - Began building road on south side of RSR driveway
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of May 18<sup>th</sup>, 2015)
  - Finish backfilling Area 16A if not complete
  - MLS on-site to restore area 16a and hydro seed front lawn
  - Begin digging test pits south of driveway
  - Begin digging area 19 along stream south of driveway
  - Haul confirmed clean piles from pad to CC
  - Grade CC as needed
  - Begin backfilling stream as confirmation samples come back

- Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, May 21<sup>st</sup>, 2015  
2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 18<sup>th</sup>, 2015)
  - Finished Backfilling Stream 16A
  - MLS on-site hydro seeding front lawn areas
  - MLS restoring stream 11+00 to 17+00
  - Remove dam when complete
  - Remove road and finish excavating Area 18
  - Backfill road and Area 18
  - Windrowed containment cell to help dry the material
  - Haul Characterization Piles, C-Area-16A-Stockpile-1&2
  - Finished building road on south side of RSR driveway
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of May 25<sup>th</sup>, 2015)
  - Begin excavating front lawn test pits along Ballard Rd
  - Begin excavating area 19 along stream south of driveway
  - Haul confirmed clean piles from pad to CC if necessary
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks

- Pump water from pond to RSR storm tank
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, May 27<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 25<sup>th</sup>, 2015)
  - Finished Stream 16A
  - Finish backfilling road north of drive and Area 18
  - Begin Excavating Test Pits in FLA
  - Begin Excavating Area 19
  - Start setting up stream pump around for stream 16B
  - Graded and compacted CC
  - Stage wetland and habitat subgrade all week
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of June 1<sup>st</sup>, 2015)
  - Continue excavating FLA test pits
  - Continue excavating area 19 along stream south of driveway
  - Haul confirmed clean piles from pad to CC if necessary
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, June 3<sup>rd</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of May 25<sup>th</sup>, 2015)
  - Finished Excavating Test Pits in FLA South of Drive
  - Continue Excavating Area 19
  - Backfill FLA Test Pits pending confirmation results
  - Set up stream pump around for stream 16B
  - Graded and compacted CC
  - Stage wetland and habitat subgrade all week
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of June 1<sup>st</sup>, 2015)
  - Continue excavating area 19 along stream south of driveway
  - Begin excavating stream 16B
  - Haul confirmed clean piles from pad to CC if necessary
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, June 10<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 8<sup>th</sup>, 2015)
  - Backfilled FLA test pits south of driveway
  - Installed dam and pump around for stream 16b
  - Began excavating stream 16b
  - Begin excavating wetland swamp area north of pond and top of pond bank
  - Graded and compacted CC
  - Bring in Enviroblend
  - Treated characterization piles C-Area19/TP Stockpile 1&4, now they are PSV-387,388
  - Stage wetland and habitat subgrade all week
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of June 15<sup>th</sup>, 2015)
  - Finish excavating stream 16b
  - Begin backfilling stream 16b
  - MLS on-site to restore stream 16b (pending confirmation results)
  - Haul confirmed clean piles from pad to CC as necessary
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks

- Pump water from pond to RSR storm tank
4. Administrative Issues
  5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, June 17<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 15<sup>th</sup>, 2015)
  - Continued excavating stream 16b
  - Finished excavating swamp area north of pond
  - Graded and compacted CC
  - Stage wetland and habitat subgrade all week
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of June 22<sup>nd</sup>, 2015)
  - Finish excavating stream 16b if necessary
  - Begin backfilling stream 16b
  - MLS on-site to restore stream 16b (pending confirmation results)
  - Begin backfilling swamp area north of pond
  - Haul confirmed clean piles from pad to CC as necessary
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, June 24<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 22<sup>nd</sup>, 2015)
  - Finish excavating stream 16b
  - Surveyor on-site shooting post excavation and sample locations
  - Backfill swamp area north of pond
  - Moved piles PSV 388-397 in CC
  - Waiting on results from PSV 398-401
  - Graded and compacted CC
  - Stage wetland and habitat subgrade all week, along with general backfill with clay mix
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of June 29<sup>th</sup>, 2015)
  - Begin backfilling stream 16b
  - MLS on-site to restore stream 16b (pending confirmation results)
  - Haul confirmed clean piles from pad to CC as necessary
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, July 1<sup>st</sup>, 2015  
2:30 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of June 29<sup>th</sup>, 2015)
  - Began backfilling stream 16b
  - MLS on-site restoring stream 16b
  - Surveyor on-site shooting post excavation and sample locations
  - Backfilled swamp area north of pond
  - Moved piles PSV 398-399 in CC
  - Waiting on results for PSV 400-403
  - Graded and compacted CC
  - Stage wetland and habitat subgrade all week, along with general backfill with clay mix
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of June 29<sup>th</sup>, 2015)
  - Finish backfilling & restoring stream 16b
  - Haul confirmed clean piles from pad to CC as necessary
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, July 8<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 6<sup>th</sup>, 2015)
  - Finish Backfilling stream 16b
  - MLS to finish restoring stream 16b
  - Remove road south of drive once MLS is finished restoring stream 16b
  - Begin setting up pond pump around filter system
  - Test pond filter system and sample
  - Moving piles PSV 400-403 in CC
  - Grad and compact CC
  - Begin staging equipment south of tracks for area 29 excavation
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of July 13<sup>th</sup>, 2015)
  - Begin pond pump around and pull sample at 500K gallons
  - Begin excavating area 29
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues

## 5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, July 15<sup>th</sup>, 2015  
1:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 13<sup>th</sup>, 2015)
  - MLS hydro seeding rest of front lawn
  - Pond pump around filter system setup ready to pump
  - Pump first 500K Gal of water through pump around and pull sample
  - Investigating between areas 12 and 13 due to confirmation samples from March
  - Grad and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond into RSR storm tanks
3. Schedule (Week of July 20<sup>th</sup>, 2015)
  - Begin excavating pond when water is gone
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, July 22<sup>nd</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 20<sup>th</sup>, 2015)
  - Began excavation of Pond
  - Backfill between areas 12 and 13
  - Grad and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
  - Continue Pumping water/recharge from pond
3. Schedule (Week of July 27<sup>th</sup>, 2015)
  - Finish excavating pond if not complete
  - Begin backfilling pond
  - MLS on-site to restore slopes in pond
  - Begin pond stream excavation
  - Stage equipment south of tracks
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
  - Pump water from pond to RSR storm tank
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, July 29<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of July 27<sup>th</sup>, 2015)
  - Finish pond excavation
  - Begin backfilling pond
  - Begin pond stream excavation
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of August 3<sup>rd</sup>, 2015)
  - Finish backfilling pond
  - MLS on-site to restore slopes in pond
  - Finish excavating pond stream
  - Backfill pond stream
  - MLS restore pond stream
  - Stage equipment south of tracks
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, August 5<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 3<sup>rd</sup>, 2015)
  - Finish railroad pond stream excavation
  - Finish backfilling pond
  - Begin staging equipment south of tracks
  - MLS on-site hydro-seeding area between 12 & 13 and restoring pond banks
  - Moved piles PSV 413-414 into cell
  - Move piles PSV 415-416 into cell
  - Waiting on results for PSV 417-422
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of August 10<sup>th</sup>, 2015)
  - Backfill railroad pond stream
  - MLS on-site to restore pond stream
  - Begin excavating south of tracks in area 28
  - Move piles into CC as needed
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, August 12<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 10<sup>th</sup>, 2015)
  - Finished backfilling pond stream
  - Finish backfilling pond
  - Begin digging in area 28 south of tracks
  - Moved piles PSV 415-422 in CC
  - Retreated PSV-420 and waiting results
  - Waiting on results for PSV 420R and 423-426
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of August 17<sup>th</sup>, 2015)
  - MLS on-site to restore pond stream and bank of pond
  - Continue excavating south of tracks in area 28
  - Move piles into CC as needed
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, August 20<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 17<sup>th</sup>, 2015)
  - Pond and pond stream restored
  - Continue excavating area 28 south of tracks
  - Retreated PSV-426 on 8/15/15
  - Waiting on results for PSV 427-430
  - Move piles into CC as needed
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of August 24<sup>th</sup>, 2015)
  - Backfill confirmed clean samples in area 28
  - Begin excavating area 29 while backfilling area 28 confirmed grids
  - Move piles into CC as needed
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion
  - Trees south of tracks, safety issues; falling on tracks, possibly falling on workers/equipment

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, August 27<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 24<sup>th</sup>, 2015)
  - Backfilling confirmed clean grids in area 28
  - Excavating area 29
  - Moved piles PSV-426-R1 and PSV 427-432 into CC
  - Waiting on results for PSV 433-434
  - Move piles into CC as needed
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of August 31<sup>th</sup>, 2015)
  - Continue Backfilling confirmed clean grids in area 28
  - Finish excavating area 29
  - Backfill area 29 as grids are confirmed clean
  - Move piles into CC as needed
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, September 2<sup>nd</sup>, 2015  
1:30 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of August 31<sup>st</sup>, 2015)
  - Backfilling confirmed clean grids in area 28 & 29
  - Finished excavating area 29 on the west side of stream
  - Continue excavating area 28 and 27
  - Moved piles PSV-433-434 into CC
  - Waiting on results for PSV 435-439
  - Move piles into CC as needed
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of September 7<sup>th</sup>, 2015)
  - Finish backfilling area 29 west of stream and confirmed clean grids
  - Continue excavating area 28 and 27
  - Continue backfilling confirmed clean grids in area 28 and 27
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks



4. Administrative Issues
5. Open Discussion
  - MLS hydro seed backfilled grids in area 28 and 29

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, September 10<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 7<sup>th</sup>, 2015)
  - Backfilling confirmed clean grids in area 28
  - MLS on-site hydro seeding completed grids in 28 and 29
  - Continue excavating area 28, 27, 24 and 25
  - Moved piles PSV-435-439 into CC
  - Waiting on results for PSV 440-442
  - Move piles into CC as needed
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of September 14<sup>th</sup>, 2015)
  - Continue excavating area 28, 27, 24 and 25
  - Continue backfilling confirmed clean grids in area 28 and 27
  - Begin excavating stream 38A (no pump around needed)
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, September 17<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 14<sup>th</sup>, 2015)
  - Re-scraped grid Area28-K27-F and re-sampled
  - Continue excavating area 28, 27, 24 and 25
  - Began digging stream 38A
  - Moving pile 440-442 into CC
  - Waiting on results for 443-447
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of September 21<sup>st</sup>, 2015)
  - Continue excavating area 28, 27, 24, 25 and 38A if not complete
  - Continue backfilling confirmed clean grids in area 28 and 27
  - Backfill stream 38A as results confirm clean
  - Begin setting up stream pump around for 38B
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, September 24<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 21<sup>st</sup>, 2015)
  - Begin backfilling pond stream 38A
  - Finish excavating area 28, 27, 25, 24 and 29 except for haul roads
  - Setup stream pump around for Western stream 38B
  - Retreated pile PSV-447
  - Moved pile PSV-446 into CC
  - Waiting on results for PSV-447 though 449
  - Grade and compact CC
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of September 28<sup>th</sup>, 2015)
  - MLS on-site to restore pond stream 38A
  - Begin excavating stream 38B
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, September 30<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of September 28<sup>th</sup>, 2015)
  - Preparing for rain from tropical storm Joaquin
  - MLS on-site to restore pond stream 38A
  - Areas 24, 25, 27, 28, 29 all excavated except for Haul road along 38B stream
  - Finish Backfilling all areas confirmed clean
  - Piles PSV-447 and PSV-448 were both retreated and waiting on results
  - Moved Pile PSV-449 into CC
  - Began grading CC to design
  - Begin excavating areas 33, 34 and 36 due to heavy rain keeping us out of the stream
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of October 5<sup>th</sup>, 2015)
  - Begin excavating stream 38B
  - Finish excavating area 33, 34 and 36
  - Backfill area 33, 34 and 36
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed

- Pump water from CC to RSR storm tanks
4. Administrative Issues
  5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, October 8<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 5<sup>th</sup>, 2015)
  - Began excavating Western Stream 38B
  - Finished excavating area 33
  - Moved Piles PSV-447R & 448R into CC
  - MLS and ERM onsite planting trees and shrubs in all areas north of tracks
  - Continue grading CC to design
  - Excavate area 2 road when ERM completes planting trees east of stream crossing
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of October 12<sup>th</sup>, 2015)
  - Continue excavating stream 38B
  - Backfill area 33 pending confirmation results
  - Begin backfilling confirmed samples in stream 38B
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, October 15<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 7<sup>th</sup>, 2015)
  - Finish excavating western stream 38B
  - Backfill western stream 38B
  - Moved Piles PSV-450-453 into CC
  - ERM finished planting trees on North side
  - Continue grading CC to design
  - Backfill area 33
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of October 14<sup>th</sup>, 2015)
  - Finish backfilling western stream 38B
  - Continue digging stream 38C
  - Finish backfilling 33
  - Excavate area 36
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks

4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, October 22<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 19<sup>th</sup>, 2015)
  - MLS on-site restoring stream section 30+00 to 36+00 in stream 38B
  - Continue excavating stream 38C from 36+00
  - Moved Piles PSV-454-456 into CC
  - Finished grading and compacting CC to design
  - Finish backfilling area 33
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of October 26<sup>th</sup>, 2015)
  - Continue digging stream 38C
  - Begin Backfilling stream 38C from 36+00 as confirmation results come back
  - Begin taking out road on west side of 38C stream and Excavate area 36
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, October 29<sup>th</sup>, 2015  
2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of October 26<sup>th</sup>, 2015)
  - MLS on-site restoring stream section 34+00 to 38+50 in stream 38B
  - Finish excavating western stream
  - Finished grading and compacting CC to design and as-built
  - Finish backfilling area 36
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of November 2<sup>nd</sup>, 2015)
  - Finish western stream if not already completed
  - Begin Backfilling stream 38C from 38+50 as confirmation results come back
  - Begin bringing in 6" protection layer for CC
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Grade CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, November 5<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of November 2<sup>nd</sup>, 2015)
  - Finished excavating western stream
  - Continue backfilling western stream
  - MLS on-site restoring stream section 38+00 to 44+00 in stream 38B
  - Begin placing 6” protection layer for CC
  - Finish backfilling area 36
  - Stage wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of November 9<sup>th</sup>, 2015)
  - Finish Backfilling Western Stream
  - MLS on-site restoring stream to completion
  - Begin installing coir logs south of tracks
  - Continue placing 6” protection layer for CC
  - Move piles into CC as needed
  - Continue staging wetland and habitat subgrade
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, November 12<sup>th</sup>, 2015  
2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of November 9<sup>th</sup>, 2015)
  - Finished backfilling western stream
  - MLS on-site completing restoration of western stream
  - Removed pump around and pipe
  - Continue placing 6" protection layer for CC
  - Begin removing road to pond stream bridge crossing
  - Backfill road for MLS to hydro seed
  - Begin installing coir logs south of tracks
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of November 16<sup>th</sup>, 2015)
  - MLS on-site hydro seeding south of tracks
  - Continue installing coir logs south of tracks
  - Finish removing road up to first stream crossing
  - Backfill road to first stream crossing
  - Excavate and sample under road in area 35
  - Move piles into CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, November 18<sup>th</sup>, 2015  
2:00 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of November 18<sup>th</sup>, 2015)
  - Continue removing roads up to first stream crossing
  - Backfill roads
  - MLS on-site hydro seeding roads
  - Finished placing 6" protection layer for CC
  - Continue installing coir logs south of tracks
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of November 23<sup>rd</sup>, 2015)
  - Finish south of tracks if not complete
  - Continue installing coir logs south of tracks if not complete
  - Move piles to CC
  - Begin removing treatment pad
  - Prepare for Thanksgiving shut-down
  - Move piles into CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, December 3<sup>rd</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of November 30<sup>th</sup>, 2015)
  - Treated Material from RSR Facility – Est. 200CY
  - Begin excavating treatment pad and Piles PSV 460 & 461
  - Placed new stone at RSR front entry
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of December 7<sup>th</sup>, 2015)
  - Finish removing treatment pad
  - Begin temp cap on 1/3 section of CC
  - Move piles into CC as needed
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, December 9<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of December 7<sup>th</sup>, 2015)
  - Finish excavating treatment pad and moved pile PSV461 into CC
  - Pressure washed all K-Rails around treatment pad
  - Stockpiled temp cap material and topsoil
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of December 14<sup>th</sup>, 2015)
  - Begin swale from containment cell to wetland pond pending approval
  - Finish temp cap on 1/3 section of CC
  - Pump water from CC to RSR storm tanks
  - Shut down for Christmas and New Year
  - Return the 3<sup>rd</sup> of January
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, December 17<sup>th</sup>, 2015  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of December 14<sup>th</sup>, 2015)
  - Finished placing 12” temporary cap cover
  - Finish placing 4” topsoil cover over temp cap
  - Built temp drainage swell from CC to 25” Eco buffer
  - Check all BMP’s
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of December 21<sup>st</sup>, 2015)
  - Shut down on the 18th for Christmas and New Year
  - Return the 3<sup>rd</sup> of January
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, January 7<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 4<sup>th</sup>, 2016)
  - Check all BMPs
  - Empty 55 Gal drums of water from MW drilling into manhole
  - Sampled MW 30 material
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of January 10<sup>th</sup>, 2016)
  - Check BMPs
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, January 14<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 11<sup>th</sup>, 2016)
  - Checking BMPs
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of January 18<sup>th</sup>, 2016)
  - Checking BMPs
  - Begin moving trees and boulders if ground is frozen
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, January 20<sup>th</sup>, 2016  
2:30 PM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 18<sup>th</sup>, 2016)
  - Checking BMPs
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of January 25<sup>th</sup>, 2016)
  - Checking BMPs
  - Begin moving trees and boulders if ground is frozen
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, January 28<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of January 25<sup>th</sup>, 2016)
  - Checking BMPs
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of February 1<sup>st</sup>, 2016)
  - Checking BMPs
  - Begin moving trees and boulders if ground is frozen
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, February 11<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of February 8<sup>th</sup>, 2016)
  - Checking BMPs
  - Begin moving trees/boulders around south of tracks
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of February 15<sup>th</sup>, 2016)
  - Checking BMPs
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, February 25<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of February 22<sup>nd</sup>, 2016)
  - Continue checking BMPs
  - Moved trees and boulders around south of tracks
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of February 29<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, March 10<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 8008671317      Access Code: 4617128

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 7<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of March 14<sup>th</sup>, 2016)
  - Continue checking BMPs
  - MLS on-site to repair wash-outs and move rocks/boulders in the streams
  - MLS will also plant trees south of the tracks, live stakes and move trees out of the pond
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, March 17<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety/Air Monitoring
2. Progress Review (Week of March 14<sup>th</sup>, 2016)
  - Continue checking BMPs
  - MLS onsite planting live stakes and repairing stream washouts
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of March 21<sup>st</sup>, 2016)
  - Continue checking BMPs
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, March 24<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety
2. Progress Review (Week of March 21<sup>st</sup>, 2016)
  - Continue checking BMPs
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of March 28<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Wednesday, April 6<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety
2. Progress Review (Week of April 4<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Stabilized stream bank south of track with large logs along bank'
  - Stabilize stream along parking lot
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of April 11<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Thursday, April 14<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety
2. Progress Review (Week of April 11<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of April 18<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Parking lot stabilization
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase II-B/III RA – Ecological & Sediment Areas  
Middletown, NY  
Weekly Meeting  
Tuesday, April 26<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety
2. Progress Review (Week of April 25<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Install Gas Vents
  - MLS on-site working on stream south of tracks, ER&M planting trees
  - Begin Anchor Trench
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of May 2<sup>nd</sup>, 2016)
  - Continue checking BMPs
  - ESI on-site installing liner
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 5<sup>th</sup>, 2016**  
**11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety
2. Progress Review (Week of May 2, 2016)
  - Continue checking BMPs
  - Liner Crew on-site – rained out and could not place GCL
  - MLS on-site planting live stakes and placing rip rap around culvert for Wakerfen Rd
  - Finished Anchor trench
  - Stabilize pond bank
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of May 9, 2016)
  - Continue checking BMPs
  - Liner crew to install cap
  - MLS – hydro seed south road after ENTACT removes and replaces with topsoil
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 12<sup>th</sup>, 2016**  
**10:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety
2. Progress Review (Week of May 9, 2016)
  - Continue checking BMPs
  - MLS on-site placing rip rap around culvert for Wakerfen Rd
  - MLS and Entact finished all tasks South of the tracks
  - Fixing erosion wash outs on Cap before GCL is placed
  - Stabilized pond bank
  - Began final grading
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of May 16, 2016)
  - Continue checking BMPs
  - Liner crew to install cap
  - Finish Final Grading
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading**  
**Middletown, NY**  
**Weekly Meeting**  
**Thursday, May 19<sup>th</sup>, 2016**  
**11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety & Air Monitoring
2. Progress Review (Week of May 16<sup>th</sup>, 2016)
  - Continue checking BMPs
  - ESI on-site installing liner cap
  - Continue bringing in fill for final grading in EFA
  - Hydro-seed stabilized pond bank
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of May 23<sup>rd</sup>, 2016)
  - Continue checking BMPs
  - ESI to finish if not complete before Sunday
  - Dig drain outfalls around cell
  - Hydro-seed EFA final grading if complete
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading  
Middletown, NY  
Weekly Meeting  
Thursday, May 26<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety & Air Monitoring
2. Progress Review (Week of May 23<sup>rd</sup>, 2016)
  - Continue checking BMPs
  - Finished Liner Installation – ESI Demob
  - Continue bringing in fill for final grading in EFA
  - Begin 24” protective cover soil layer
  - Finish Outfalls and Anchor Trench
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of May 30<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Continue protective cover soil layer until complete
  - Hydro-seed EFA final grading if complete
  - Begin Concrete Block Spillway
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading  
Middletown, NY  
Weekly Meeting  
Wednesday, June 1<sup>st</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety & Air Monitoring
2. Progress Review (Week of May 30<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Hydro Seed final grading EFA area
  - Continue 24” protective cover soil layer
  - Finish Outfalls and Anchor Trench
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of June 6<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Continue protective cover soil layer until complete
  - Begin Concrete Block Spillway
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading  
Middletown, NY  
Weekly Meeting  
Thursday, June 9<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety & Air Monitoring
2. Progress Review (Week of June 6<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Continue 24” protective cover soil layer
  - Install concrete blocks swale and drainage swale
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of June 13<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Continue protective cover soil layer until complete
  - Finish block swale
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading  
Middletown, NY  
Weekly Meeting  
Thursday, June 16<sup>th</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety & Air Monitoring
2. Progress Review (Week of June 13<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Finish and As-built 24” protective cover soil layer
  - Finish installing concrete blocks swale and drainage swale
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of June 20<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Finish Topsoil layer until complete
  - Finish block swale if not complete
  - Begin Leachate Extraction from manhole
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading  
Middletown, NY  
Weekly Meeting  
Thursday, June 23<sup>rd</sup>, 2016  
11:00 AM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Health and Safety & Air Monitoring
2. Progress Review (Week of June 20<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Finish and As-built 6" topsoil layer
  - Finish road, slopes and outfalls around cell
  - Pump water from CC to RSR storm tanks
3. Schedule (Week of June 27<sup>th</sup>, 2016)
  - Continue checking BMPs
  - Finish block swale if not complete
  - Leave Thursday for 4<sup>th</sup> of July shut-down back on the 5<sup>th</sup>.
  - Pump water from CC to RSR storm tanks
4. Administrative Issues
5. Open Discussion

**Revere Smelting & Refining Site, OU1, Phase III RA – Containment Cell Cap & Final Grading  
Middletown, NY  
Leachate Extraction Discussion  
Monday, June 27<sup>th</sup>, 2016  
2:00 PM ET**

Teleconference: Call-in#: 866-871-6537      Access Code: 2544852 #

Meeting Agenda:

1. Leachate Extraction from Manhole to RSR Storm Tanks
2. Open Discussion



**Revere Smelting & Refining Site, OU1, Phase III RA – Final Inspection Meeting**  
**Middletown, NY**  
**Wednesday, July 6, 2016**  
**2:00 PM ET**

Informal Meeting Agenda:

1. Leachate pipe discussion
2. Final inspection and punchlist item discussion
3. Site walk
