

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/2/2024

Weather: 30 deg. F, Clear/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Alba continuing groundwater treatment system and well point installation.
- 3) Export two loads (approximately 40 CY) of material from WC-26, 27 & 28 for off-Site disposal at the MSM facility.
- 4) Export of one load of mixed demolition debris (approximately 20 CY) for off-Site disposal at the Clean Earth of New Castle facility.

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

Off-Site Material Disposal				
Facility Location	Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	EE MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	BSM 75 Crows Mill Rd. Keasby, NJ 08832
Today: (CY)	0	0	40	0
Total: (CY)	1,375	0	4,385	0

Site Layout Map

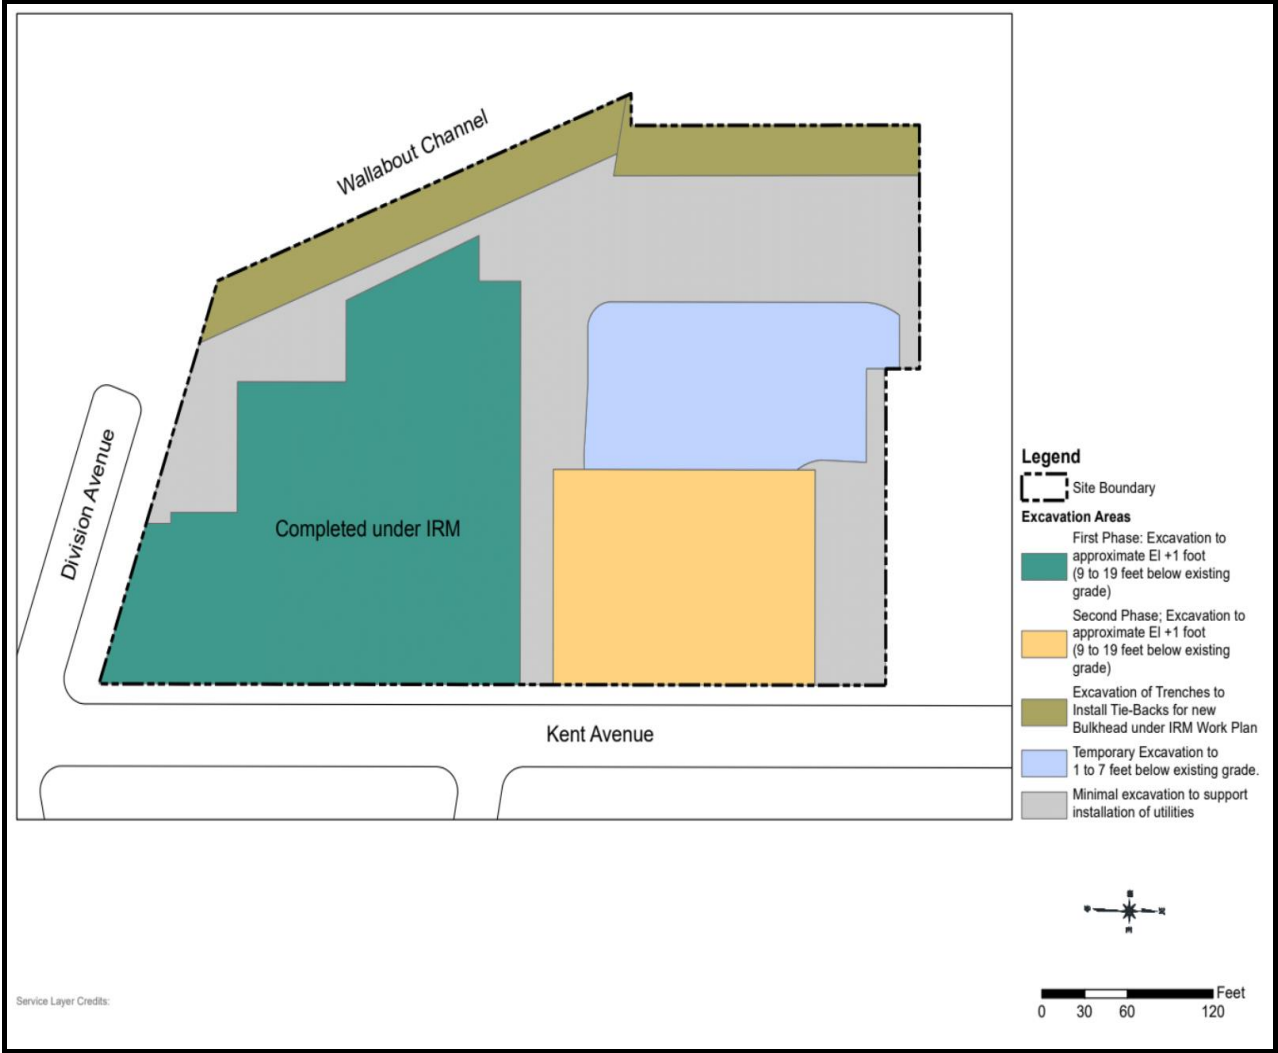


Photo 1:
View of Site conditions
facing northwest.

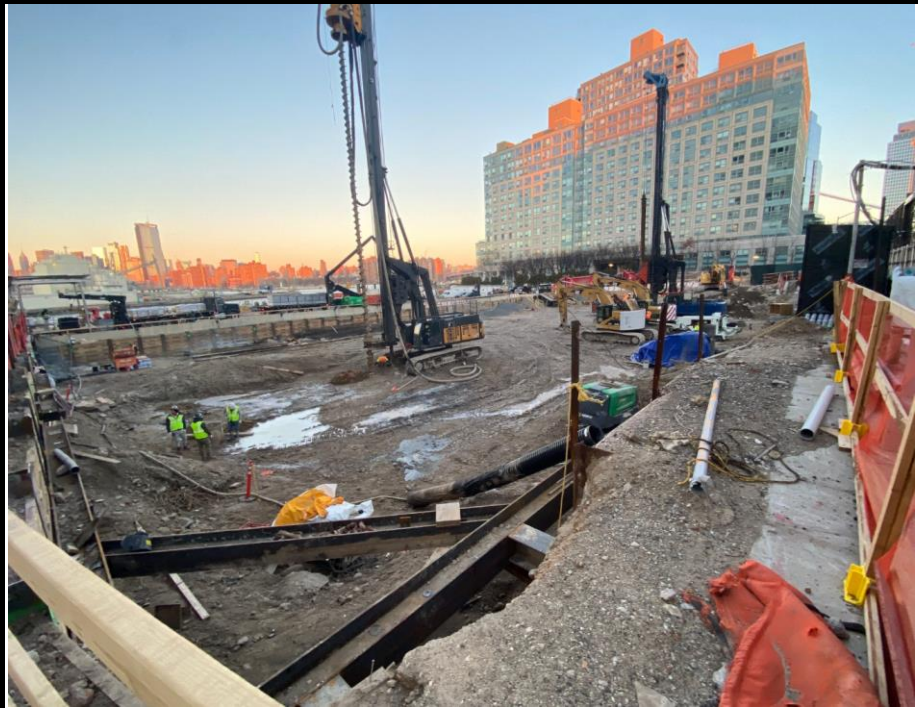


Photo 2:
View of excavation and
drilling for pile
installation and SOE
installation.



Photo 3:

View of truck loading for off-Site soil disposal.



Photo 4:


View of SOE installation.



CAMP:
Downwind
Particulates

Dust Levels


0.015 mg/m³ 0.025 mg/m³ 0.15

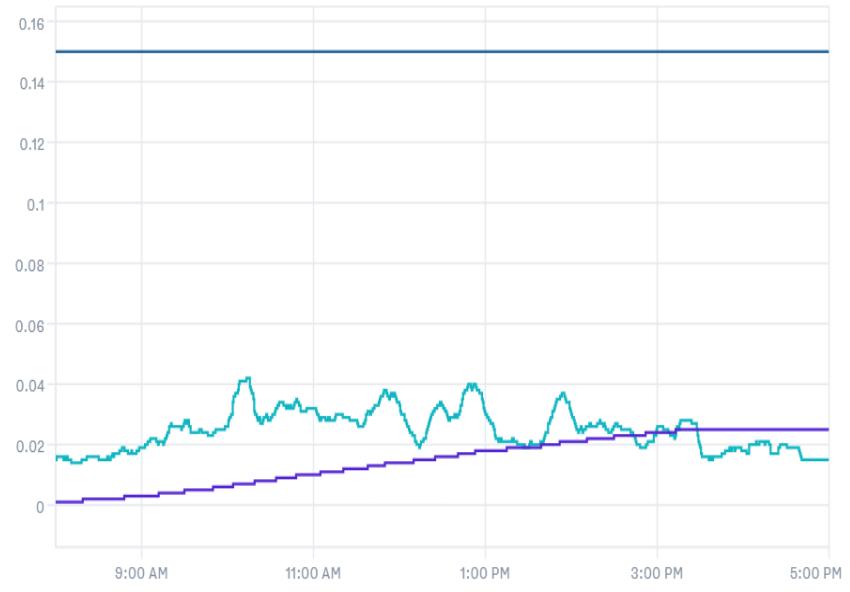

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm 5

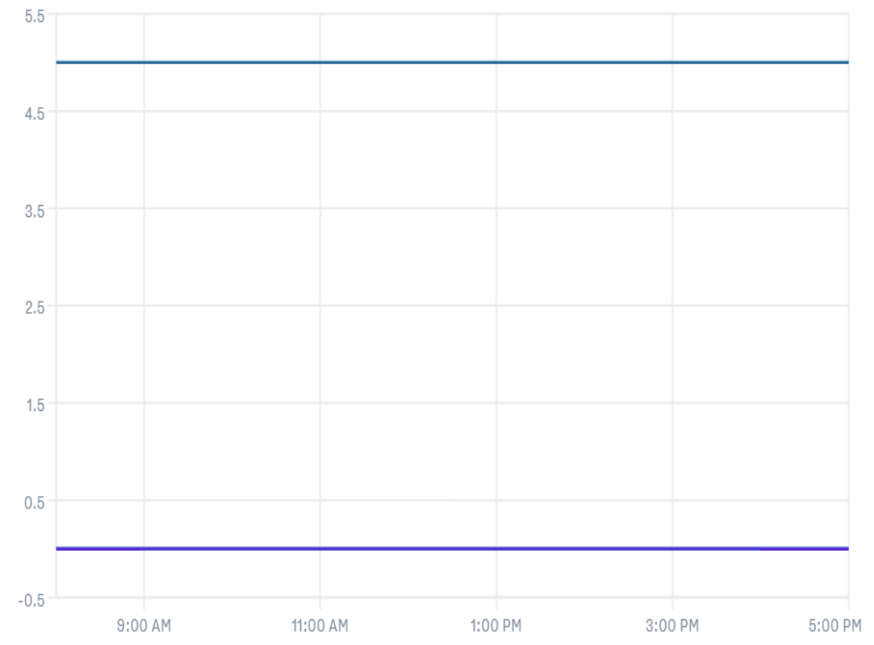

CAMP:
Upwind Particulates

Dust Levels


0.005 mg/m³ 0.014 mg/m³ 0.15

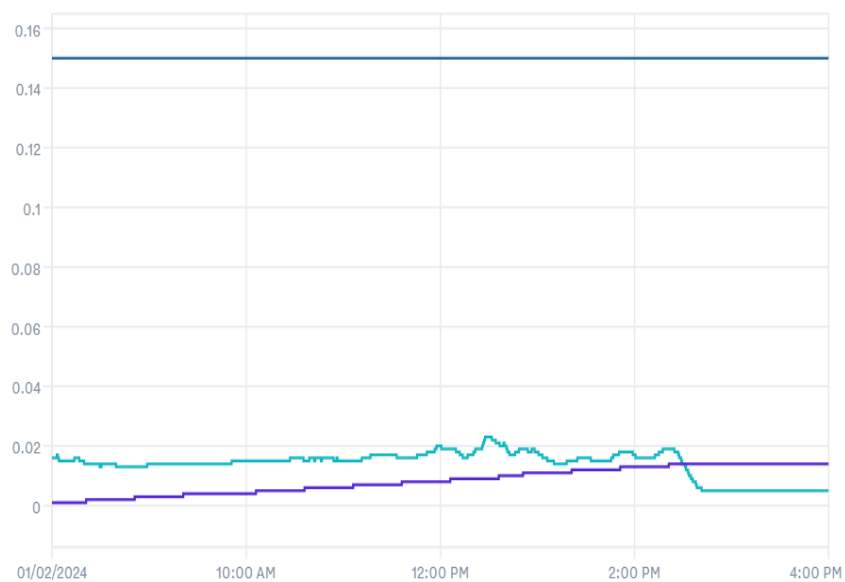

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

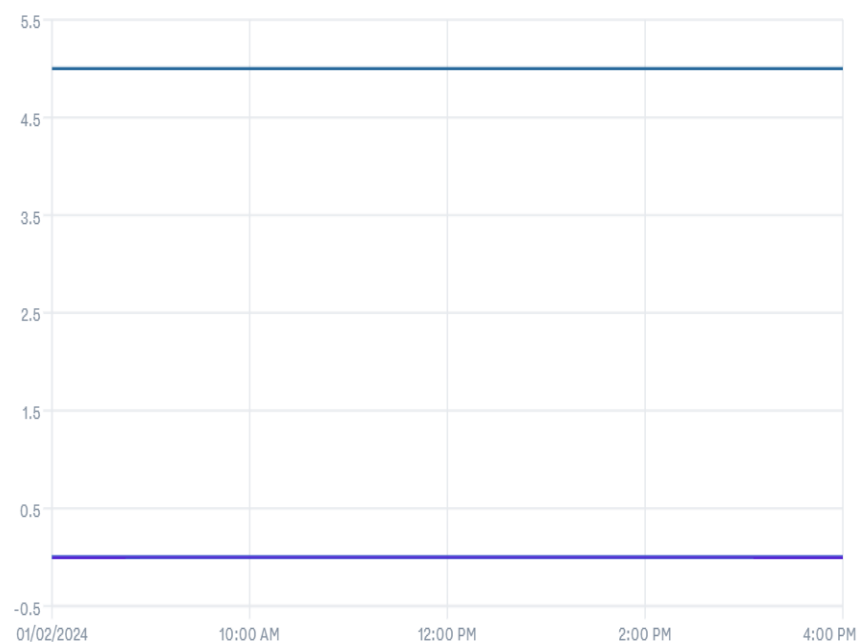

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/2/2024 8:00	1/2/2024 8:10	0.150	0.001	5	0
DW 47907	1/2/2024 8:10	1/2/2024 8:20	0.150	0.002	5	0
DW 47907	1/2/2024 8:20	1/2/2024 8:30	0.150	0.002	5	0
DW 47907	1/2/2024 8:30	1/2/2024 8:40	0.150	0.002	5	0
DW 47907	1/2/2024 8:40	1/2/2024 8:50	0.150	0.003	5	0
DW 47907	1/2/2024 8:50	1/2/2024 9:00	0.150	0.003	5	0
DW 47907	1/2/2024 9:00	1/2/2024 9:10	0.150	0.003	5	0
DW 47907	1/2/2024 9:10	1/2/2024 9:20	0.150	0.004	5	0
DW 47907	1/2/2024 9:20	1/2/2024 9:30	0.150	0.005	5	0
DW 47907	1/2/2024 9:30	1/2/2024 9:40	0.150	0.005	5	0
DW 47907	1/2/2024 9:40	1/2/2024 9:50	0.150	0.006	5	0
DW 47907	1/2/2024 9:50	1/2/2024 10:00	0.150	0.006	5	0
DW 47907	1/2/2024 10:00	1/2/2024 10:10	0.150	0.007	5	0
DW 47907	1/2/2024 10:10	1/2/2024 10:20	0.150	0.008	5	0
DW 47907	1/2/2024 10:20	1/2/2024 10:30	0.150	0.008	5	0
DW 47907	1/2/2024 10:30	1/2/2024 10:40	0.150	0.009	5	0
DW 47907	1/2/2024 10:40	1/2/2024 10:50	0.150	0.01	5	0
DW 47907	1/2/2024 10:50	1/2/2024 11:00	0.150	0.01	5	0
DW 47907	1/2/2024 11:00	1/2/2024 11:10	0.150	0.011	5	0
DW 47907	1/2/2024 11:10	1/2/2024 11:20	0.150	0.011	5	0
DW 47907	1/2/2024 11:20	1/2/2024 11:30	0.150	0.012	5	0
DW 47907	1/2/2024 11:30	1/2/2024 11:40	0.150	0.013	5	0
DW 47907	1/2/2024 11:40	1/2/2024 11:50	0.150	0.014	5	0
DW 47907	1/2/2024 11:50	1/2/2024 12:00	0.150	0.014	5	0
DW 47907	1/2/2024 12:00	1/2/2024 12:10	0.150	0.015	5	0
DW 47907	1/2/2024 12:10	1/2/2024 12:20	0.150	0.015	5	0
DW 47907	1/2/2024 12:20	1/2/2024 12:30	0.150	0.016	5	0
DW 47907	1/2/2024 12:30	1/2/2024 12:40	0.150	0.016	5	0
DW 47907	1/2/2024 12:40	1/2/2024 12:50	0.150	0.017	5	0
DW 47907	1/2/2024 12:50	1/2/2024 13:00	0.150	0.018	5	0
DW 47907	1/2/2024 13:00	1/2/2024 13:10	0.150	0.018	5	0
DW 47907	1/2/2024 13:10	1/2/2024 13:20	0.150	0.019	5	0
DW 47907	1/2/2024 13:20	1/2/2024 13:30	0.150	0.019	5	0
DW 47907	1/2/2024 13:30	1/2/2024 13:40	0.150	0.02	5	0
DW 47907	1/2/2024 13:40	1/2/2024 13:50	0.150	0.02	5	0
DW 47907	1/2/2024 13:50	1/2/2024 14:00	0.150	0.021	5	0
DW 47907	1/2/2024 14:00	1/2/2024 14:10	0.150	0.021	5	0
DW 47907	1/2/2024 14:10	1/2/2024 14:20	0.150	0.022	5	0
DW 47907	1/2/2024 14:20	1/2/2024 14:30	0.150	0.023	5	0
DW 47907	1/2/2024 14:30	1/2/2024 14:40	0.150	0.023	5	0
DW 47907	1/2/2024 14:40	1/2/2024 14:50	0.150	0.023	5	0
DW 47907	1/2/2024 14:50	1/2/2024 15:00	0.150	0.024	5	0
DW 47907	1/2/2024 15:00	1/2/2024 15:10	0.150	0.024	5	0
DW 47907	1/2/2024 15:10	1/2/2024 15:20	0.150	0.025	5	0
DW 47907	1/2/2024 15:20	1/2/2024 15:30	0.150	0.025	5	0
DW 47907	1/2/2024 15:30	1/2/2024 15:40	0.150	0.025	5	0
DW 47907	1/2/2024 15:40	1/2/2024 15:50	0.150	0.025	5	0
DW 47907	1/2/2024 15:50	1/2/2024 16:00	0.150	0.025	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/2/2024 8:00	1/2/2024 8:10	0.150	0.001	5	0
UW 212221	1/2/2024 8:10	1/2/2024 8:20	0.150	0.001	5	0
UW 212221	1/2/2024 8:20	1/2/2024 8:30	0.150	0.002	5	0
UW 212221	1/2/2024 8:30	1/2/2024 8:40	0.150	0.002	5	0
UW 212221	1/2/2024 8:40	1/2/2024 8:50	0.150	0.002	5	0
UW 212221	1/2/2024 8:50	1/2/2024 9:00	0.150	0.003	5	0
UW 212221	1/2/2024 9:00	1/2/2024 9:10	0.150	0.003	5	0
UW 212221	1/2/2024 9:10	1/2/2024 9:20	0.150	0.003	5	0
UW 212221	1/2/2024 9:20	1/2/2024 9:30	0.150	0.004	5	0
UW 212221	1/2/2024 9:30	1/2/2024 9:40	0.150	0.004	5	0
UW 212221	1/2/2024 9:40	1/2/2024 9:50	0.150	0.004	5	0
UW 212221	1/2/2024 9:50	1/2/2024 10:00	0.150	0.004	5	0
UW 212221	1/2/2024 10:00	1/2/2024 10:10	0.150	0.005	5	0
UW 212221	1/2/2024 10:10	1/2/2024 10:20	0.150	0.005	5	0
UW 212221	1/2/2024 10:20	1/2/2024 10:30	0.150	0.005	5	0
UW 212221	1/2/2024 10:30	1/2/2024 10:40	0.150	0.006	5	0
UW 212221	1/2/2024 10:40	1/2/2024 10:50	0.150	0.006	5	0
UW 212221	1/2/2024 10:50	1/2/2024 11:00	0.150	0.006	5	0
UW 212221	1/2/2024 11:00	1/2/2024 11:10	0.150	0.007	5	0
UW 212221	1/2/2024 11:10	1/2/2024 11:20	0.150	0.007	5	0
UW 212221	1/2/2024 11:20	1/2/2024 11:30	0.150	0.007	5	0
UW 212221	1/2/2024 11:30	1/2/2024 11:40	0.150	0.008	5	0
UW 212221	1/2/2024 11:40	1/2/2024 11:50	0.150	0.008	5	0
UW 212221	1/2/2024 11:50	1/2/2024 12:00	0.150	0.008	5	0
UW 212221	1/2/2024 12:00	1/2/2024 12:10	0.150	0.009	5	0
UW 212221	1/2/2024 12:10	1/2/2024 12:20	0.150	0.009	5	0
UW 212221	1/2/2024 12:20	1/2/2024 12:30	0.150	0.009	5	0
UW 212221	1/2/2024 12:30	1/2/2024 12:40	0.150	0.01	5	0
UW 212221	1/2/2024 12:40	1/2/2024 12:50	0.150	0.01	5	0
UW 212221	1/2/2024 12:50	1/2/2024 13:00	0.150	0.011	5	0
UW 212221	1/2/2024 13:00	1/2/2024 13:10	0.150	0.011	5	0
UW 212221	1/2/2024 13:10	1/2/2024 13:20	0.150	0.011	5	0
UW 212221	1/2/2024 13:20	1/2/2024 13:30	0.150	0.012	5	0
UW 212221	1/2/2024 13:30	1/2/2024 13:40	0.150	0.012	5	0
UW 212221	1/2/2024 13:40	1/2/2024 13:50	0.150	0.012	5	0
UW 212221	1/2/2024 13:50	1/2/2024 14:00	0.150	0.013	5	0
UW 212221	1/2/2024 14:00	1/2/2024 14:10	0.150	0.013	5	0
UW 212221	1/2/2024 14:10	1/2/2024 14:20	0.150	0.013	5	0
UW 212221	1/2/2024 14:20	1/2/2024 14:30	0.150	0.014	5	0
UW 212221	1/2/2024 14:30	1/2/2024 14:40	0.150	0.014	5	0
UW 212221	1/2/2024 14:40	1/2/2024 14:50	0.150	0.014	5	0
UW 212221	1/2/2024 14:50	1/2/2024 15:00	0.150	0.014	5	0
UW 212221	1/2/2024 15:00	1/2/2024 15:10	0.150	0.014	5	0
UW 212221	1/2/2024 15:10	1/2/2024 15:20	0.150	0.014	5	0
UW 212221	1/2/2024 15:20	1/2/2024 15:30	0.150	0.014	5	0
UW 212221	1/2/2024 15:30	1/2/2024 15:40	0.150	0.014	5	0
UW 212221	1/2/2024 15:40	1/2/2024 15:50	0.150	0.014	5	0
UW 212221	1/2/2024 15:50	1/2/2024 16:00	0.150	0.014	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/2/2024 8:00	1/2/2024 8:10	0.150	0.006	5	0
PER1 50057	1/2/2024 8:10	1/2/2024 8:20	0.150	0.007	5	0
PER1 50057	1/2/2024 8:20	1/2/2024 8:30	0.150	0.007	5	0
PER1 50057	1/2/2024 8:30	1/2/2024 8:40	0.150	0.008	5	0
PER1 50057	1/2/2024 8:40	1/2/2024 8:50	0.150	0.009	5	0
PER1 50057	1/2/2024 8:50	1/2/2024 9:00	0.150	0.01	5	0
PER1 50057	1/2/2024 9:00	1/2/2024 9:10	0.150	0.01	5	0
PER1 50057	1/2/2024 9:10	1/2/2024 9:20	0.150	0.011	5	0
PER1 50057	1/2/2024 9:20	1/2/2024 9:30	0.150	0.012	5	0
PER1 50057	1/2/2024 9:30	1/2/2024 9:40	0.150	0.013	5	0
PER1 50057	1/2/2024 9:40	1/2/2024 9:50	0.150	0.014	5	0
PER1 50057	1/2/2024 9:50	1/2/2024 10:00	0.150	0.016	5	0
PER1 50057	1/2/2024 10:00	1/2/2024 10:10	0.150	0.017	5	0
PER1 50057	1/2/2024 10:10	1/2/2024 10:20	0.150	0.018	5	0
PER1 50057	1/2/2024 10:20	1/2/2024 10:30	0.150	0.019	5	0
PER1 50057	1/2/2024 10:30	1/2/2024 10:40	0.150	0.019	5	0
PER1 50057	1/2/2024 10:40	1/2/2024 10:50	0.150	0.02	5	0
PER1 50057	1/2/2024 10:50	1/2/2024 11:00	0.150	0.021	5	0
PER1 50057	1/2/2024 11:00	1/2/2024 11:10	0.150	0.022	5	0
PER1 50057	1/2/2024 11:10	1/2/2024 11:20	0.150	0.026	5	0
PER1 50057	1/2/2024 11:20	1/2/2024 11:30	0.150	0.027	5	0
PER1 50057	1/2/2024 11:30	1/2/2024 11:40	0.150	0.027	5	0
PER1 50057	1/2/2024 11:40	1/2/2024 11:50	0.150	0.028	5	0
PER1 50057	1/2/2024 11:50	1/2/2024 12:00	0.150	0.029	5	0
PER1 50057	1/2/2024 12:00	1/2/2024 12:10	0.150	0.029	5	0
PER1 50057	1/2/2024 12:10	1/2/2024 12:20	0.150	0.03	5	0
PER1 50057	1/2/2024 12:20	1/2/2024 12:30	0.150	0.031	5	0
PER1 50057	1/2/2024 12:30	1/2/2024 12:40	0.150	0.032	5	0
PER1 50057	1/2/2024 12:40	1/2/2024 12:50	0.150	0.032	5	0
PER1 50057	1/2/2024 12:50	1/2/2024 13:00	0.150	0.033	5	0
PER1 50057	1/2/2024 13:00	1/2/2024 13:10	0.150	0.034	5	0
PER1 50057	1/2/2024 13:10	1/2/2024 13:20	0.150	0.034	5	0
PER1 50057	1/2/2024 13:20	1/2/2024 13:30	0.150	0.035	5	0
PER1 50057	1/2/2024 13:30	1/2/2024 13:40	0.150	0.035	5	0
PER1 50057	1/2/2024 13:40	1/2/2024 13:50	0.150	0.035	5	0
PER1 50057	1/2/2024 13:50	1/2/2024 14:00	0.150	0.036	5	0
PER1 50057	1/2/2024 14:00	1/2/2024 14:10	0.150	0.036	5	0
PER1 50057	1/2/2024 14:10	1/2/2024 14:20	0.150	0.036	5	0
PER1 50057	1/2/2024 14:20	1/2/2024 14:30	0.150	0.037	5	0
PER1 50057	1/2/2024 14:30	1/2/2024 14:40	0.150	0.038	5	0
PER1 50057	1/2/2024 14:40	1/2/2024 14:50	0.150	0.038	5	0
PER1 50057	1/2/2024 14:50	1/2/2024 15:00	0.150	0.038	5	0
PER1 50057	1/2/2024 15:00	1/2/2024 15:10	0.150	0.039	5	0
PER1 50057	1/2/2024 15:10	1/2/2024 15:20	0.150	0.039	5	0
PER1 50057	1/2/2024 15:20	1/2/2024 15:30	0.150	0.039	5	0
PER1 50057	1/2/2024 15:30	1/2/2024 15:40	0.150	0.039	5	0
PER1 50057	1/2/2024 15:40	1/2/2024 15:50	0.150	0.039	5	0
PER1 50057	1/2/2024 15:50	1/2/2024 16:00	0.150	0.039	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/2/2024 8:00	1/2/2024 8:10	0.150	0.002	5	0
PER2 46495	1/2/2024 8:10	1/2/2024 8:20	0.150	0.003	5	0
PER2 46495	1/2/2024 8:20	1/2/2024 8:30	0.150	0.004	5	0
PER2 46495	1/2/2024 8:30	1/2/2024 8:40	0.150	0.004	5	0
PER2 46495	1/2/2024 8:40	1/2/2024 8:50	0.150	0.005	5	0
PER2 46495	1/2/2024 8:50	1/2/2024 9:00	0.150	0.005	5	0
PER2 46495	1/2/2024 9:00	1/2/2024 9:10	0.150	0.005	5	0
PER2 46495	1/2/2024 9:10	1/2/2024 9:20	0.150	0.006	5	0
PER2 46495	1/2/2024 9:20	1/2/2024 9:30	0.150	0.006	5	0
PER2 46495	1/2/2024 9:30	1/2/2024 9:40	0.150	0.007	5	0
PER2 46495	1/2/2024 9:40	1/2/2024 9:50	0.150	0.007	5	0
PER2 46495	1/2/2024 9:50	1/2/2024 10:00	0.150	0.007	5	0
PER2 46495	1/2/2024 10:00	1/2/2024 10:10	0.150	0.008	5	0
PER2 46495	1/2/2024 10:10	1/2/2024 10:20	0.150	0.009	5	0
PER2 46495	1/2/2024 10:20	1/2/2024 10:30	0.150	0.009	5	0
PER2 46495	1/2/2024 10:30	1/2/2024 10:40	0.150	0.01	5	0
PER2 46495	1/2/2024 10:40	1/2/2024 10:50	0.150	0.01	5	0
PER2 46495	1/2/2024 10:50	1/2/2024 11:00	0.150	0.011	5	0
PER2 46495	1/2/2024 11:00	1/2/2024 11:10	0.150	0.011	5	0
PER2 46495	1/2/2024 11:10	1/2/2024 11:20	0.150	0.012	5	0
PER2 46495	1/2/2024 11:20	1/2/2024 11:30	0.150	0.012	5	0
PER2 46495	1/2/2024 11:30	1/2/2024 11:40	0.150	0.012	5	0
PER2 46495	1/2/2024 11:40	1/2/2024 11:50	0.150	0.013	5	0
PER2 46495	1/2/2024 11:50	1/2/2024 12:00	0.150	0.013	5	0
PER2 46495	1/2/2024 12:00	1/2/2024 12:10	0.150	0.014	5	0
PER2 46495	1/2/2024 12:10	1/2/2024 12:20	0.150	0.014	5	0
PER2 46495	1/2/2024 12:20	1/2/2024 12:30	0.150	0.015	5	0
PER2 46495	1/2/2024 12:30	1/2/2024 12:40	0.150	0.015	5	0
PER2 46495	1/2/2024 12:40	1/2/2024 12:50	0.150	0.016	5	0
PER2 46495	1/2/2024 12:50	1/2/2024 13:00	0.150	0.016	5	0
PER2 46495	1/2/2024 13:00	1/2/2024 13:10	0.150	0.016	5	0
PER2 46495	1/2/2024 13:10	1/2/2024 13:20	0.150	0.016	5	0
PER2 46495	1/2/2024 13:20	1/2/2024 13:30	0.150	0.016	5	0
PER2 46495	1/2/2024 13:30	1/2/2024 13:40	0.150	0.016	5	0
PER2 46495	1/2/2024 13:40	1/2/2024 13:50	0.150	0.016	5	0
PER2 46495	1/2/2024 13:50	1/2/2024 14:00	0.150	0.016	5	0
PER2 46495	1/2/2024 14:00	1/2/2024 14:10	0.150	0.016	5	0
PER2 46495	1/2/2024 14:10	1/2/2024 14:20	0.150	0.016	5	0
PER2 46495	1/2/2024 14:20	1/2/2024 14:30	0.150	0.016	5	0
PER2 46495	1/2/2024 14:30	1/2/2024 14:40	0.150	0.016	5	0
PER2 46495	1/2/2024 14:40	1/2/2024 14:50	0.150	0.016	5	0
PER2 46495	1/2/2024 14:50	1/2/2024 15:00	0.150	0.016	5	0
PER2 46495	1/2/2024 15:00	1/2/2024 15:10	0.150	0.016	5	0
PER2 46495	1/2/2024 15:10	1/2/2024 15:20	0.150	0.016	5	0
PER2 46495	1/2/2024 15:20	1/2/2024 15:30	0.150	0.016	5	0
PER2 46495	1/2/2024 15:30	1/2/2024 15:40	0.150	0.016	5	0
PER2 46495	1/2/2024 15:40	1/2/2024 15:50	0.150	0.016	5	0
PER2 46495	1/2/2024 15:50	1/2/2024 16:00	0.150	0.016	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/3/2024

Weather: 40 deg. F, Clear/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Alba continuing groundwater treatment system and well point installation.
- 3) ECD continuing waterfront development.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

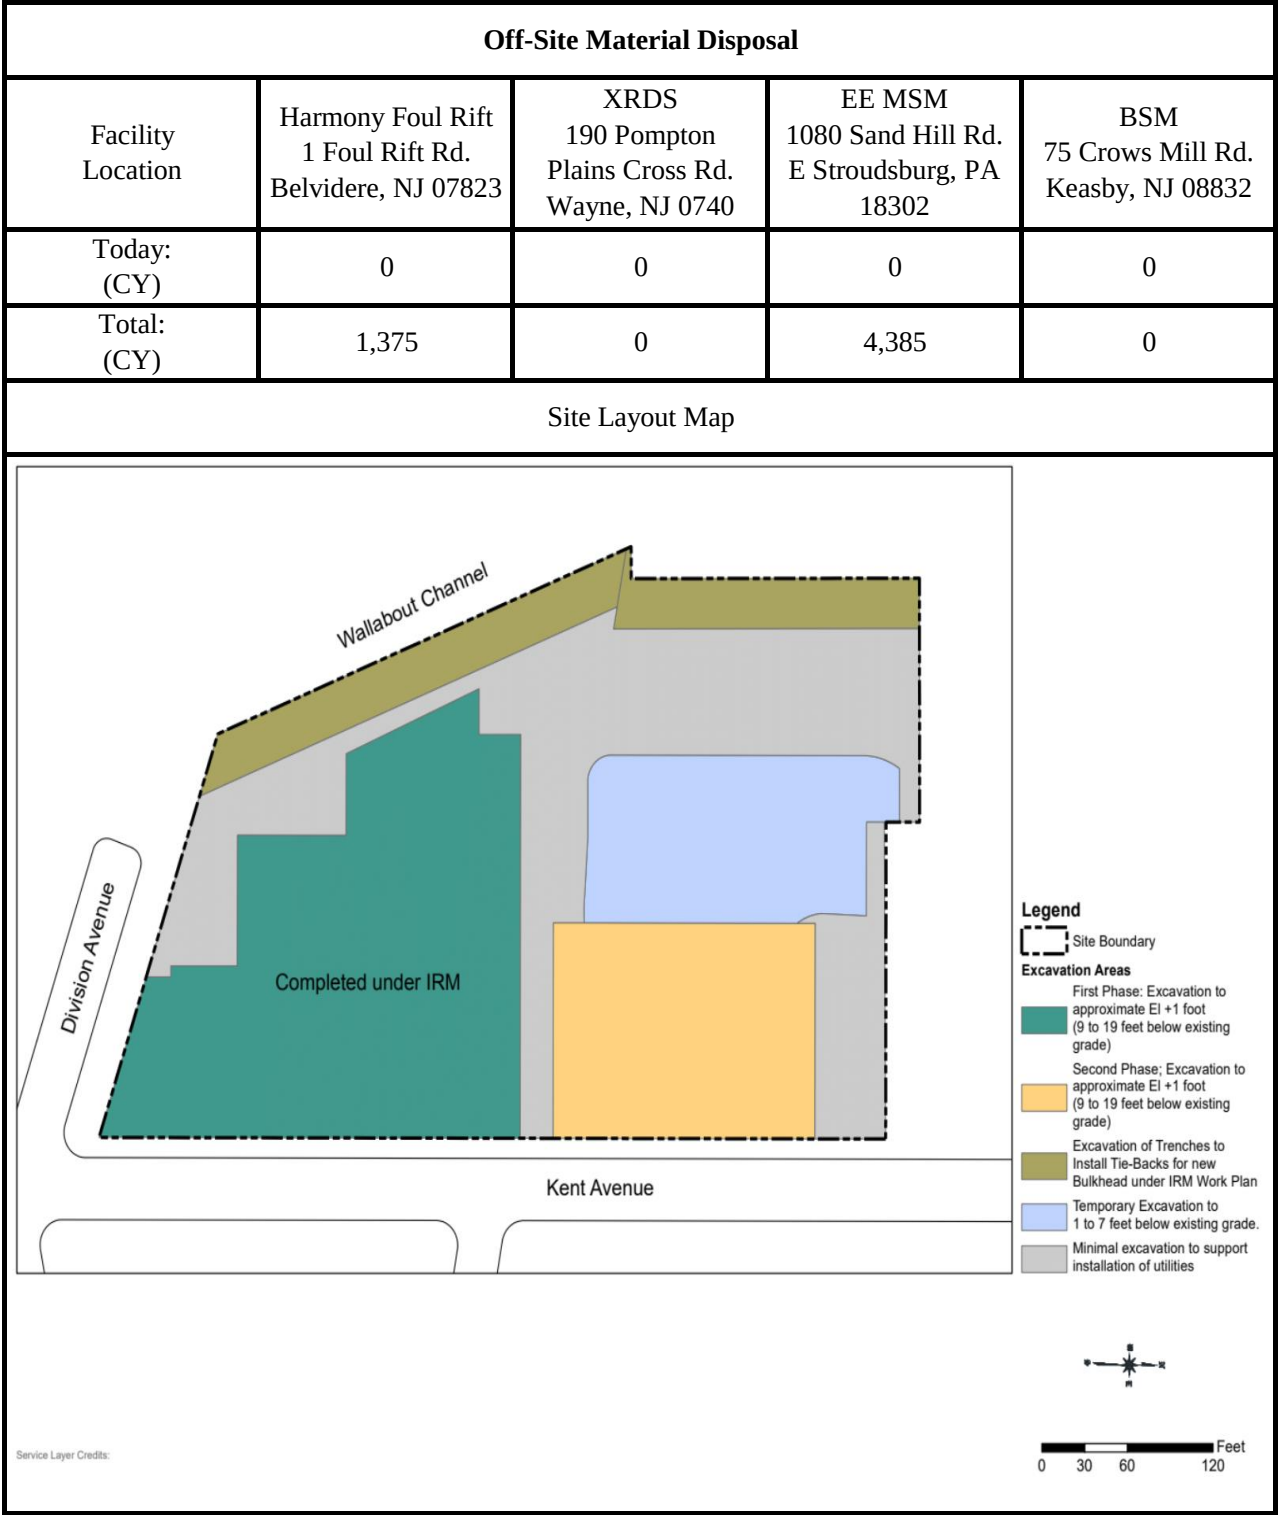


Photo 1:
View of Site conditions
facing southeast.

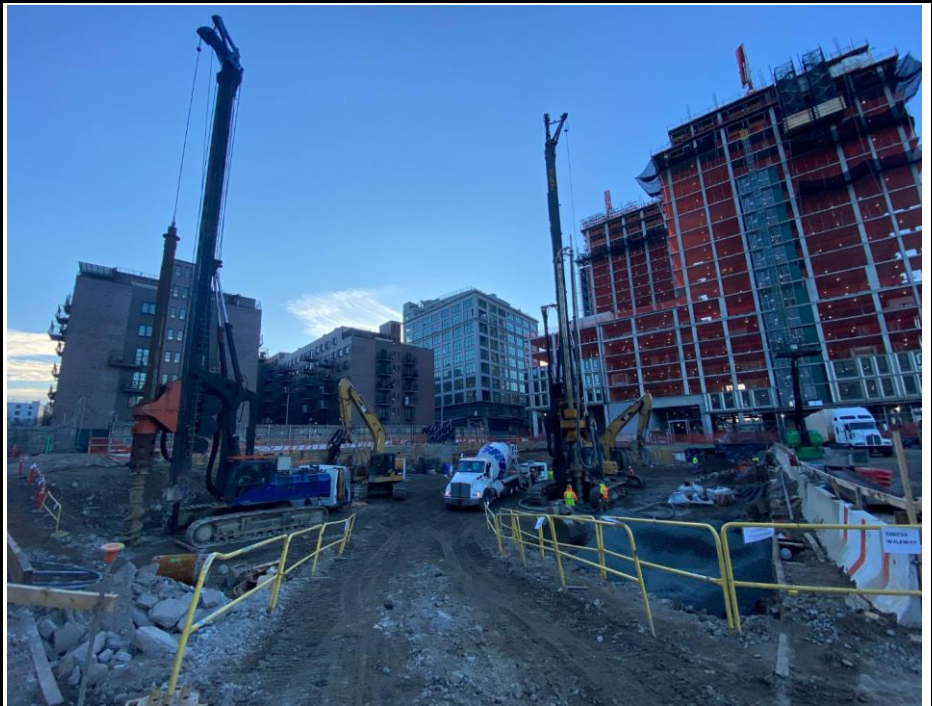



Photo 2:
View of excavation and
drilling for pile
installation and SOE
installation.




Photo 3:
View of Site
conditions facing
north.



Photo 4:
View of SOE
installation.

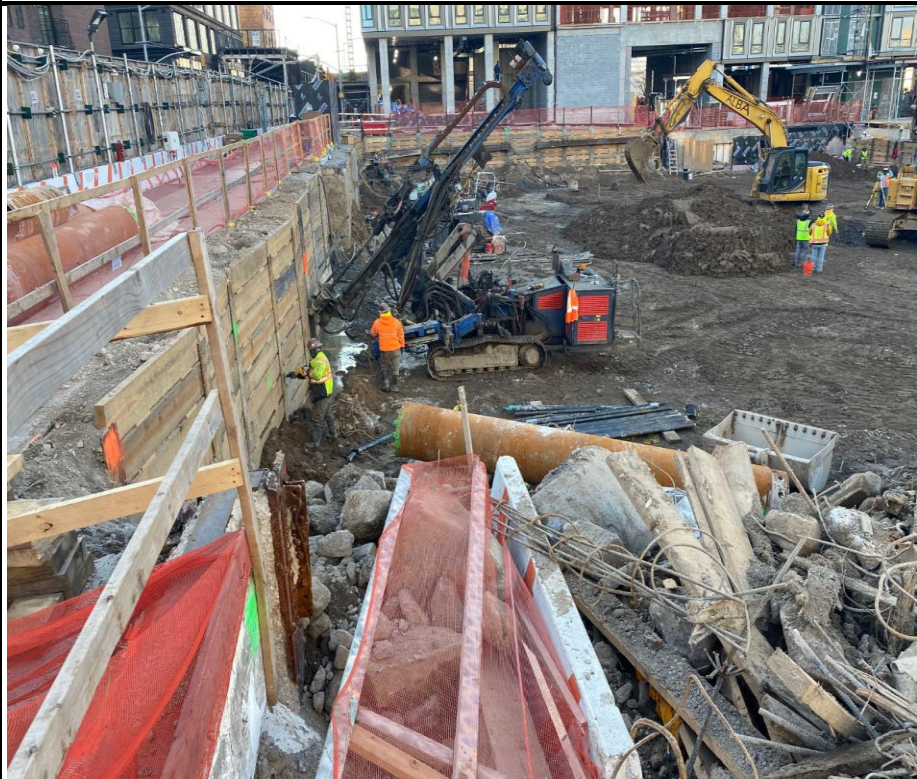


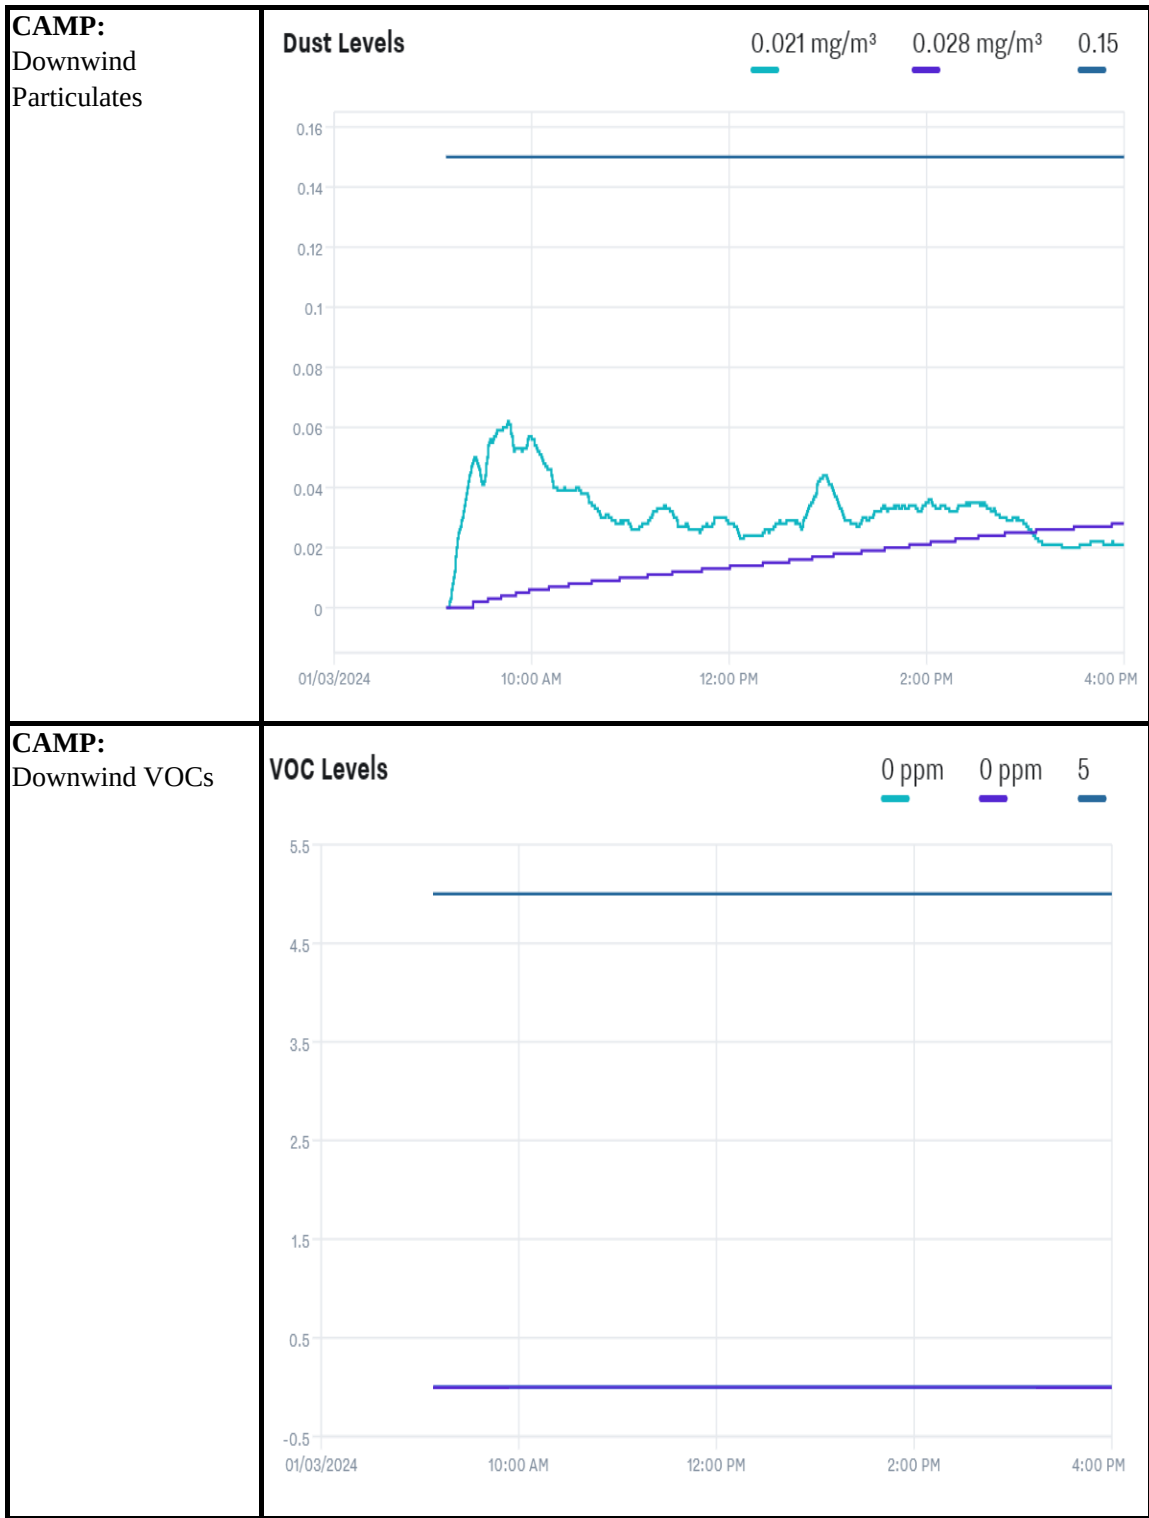

CAMP:
Upwind Particulates

Dust Levels


0.021 mg/m³ 0.021 mg/m³ 0.15

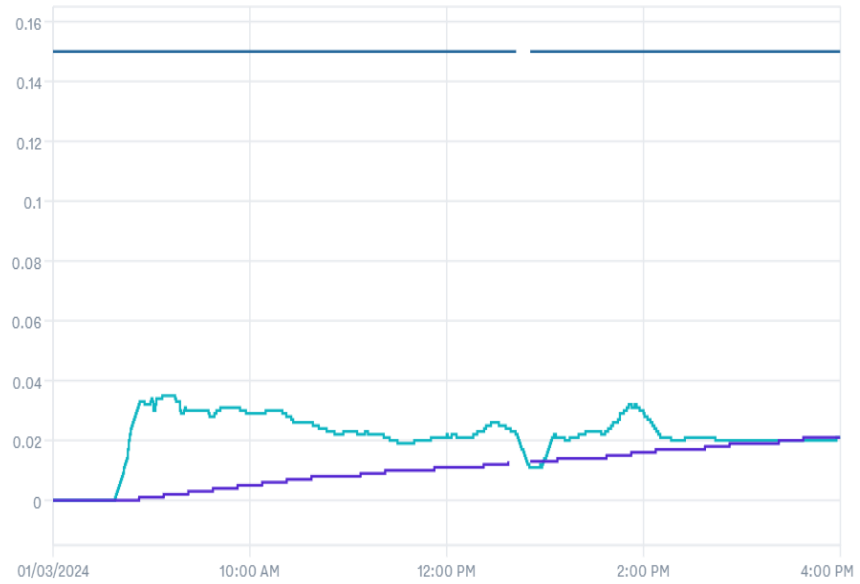

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

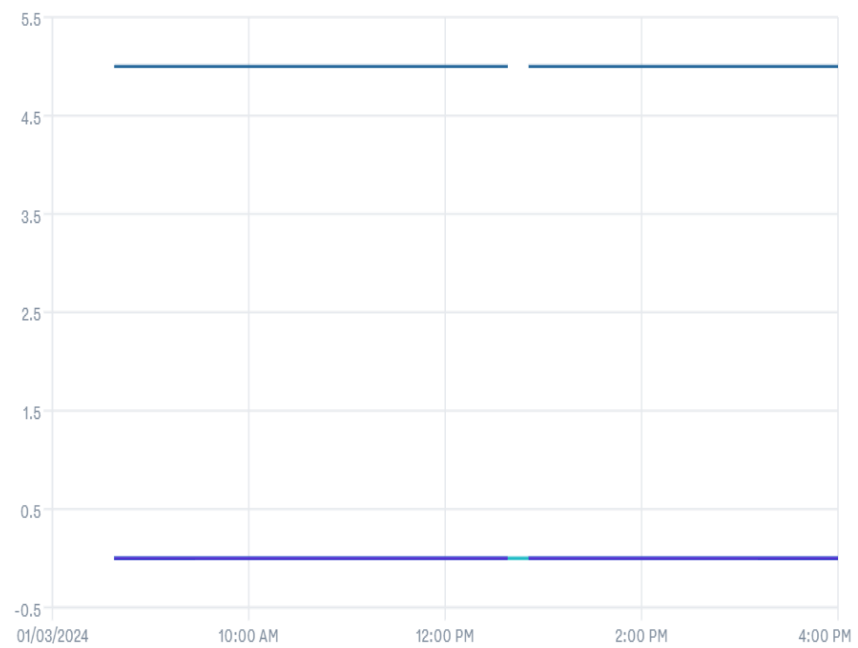

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/3/2024 8:00	1/3/2024 8:10	0.150	0.025	5	0
DW 47907	1/3/2024 8:10	1/3/2024 8:20	0.150	0.025	5	0
DW 47907	1/3/2024 8:20	1/3/2024 8:30	0.150	0.025	5	0
DW 47907	1/3/2024 8:30	1/3/2024 8:40	0.150	0.025	5	0
DW 47907	1/3/2024 8:40	1/3/2024 8:50	0.150	0.025	5	0
DW 47907	1/3/2024 8:50	1/3/2024 9:00	0.150	0.025	5	0
DW 47907	1/3/2024 9:00	1/3/2024 9:10	0.150	0	5	0
DW 47907	1/3/2024 9:10	1/3/2024 9:20	0.150	0	5	0
DW 47907	1/3/2024 9:20	1/3/2024 9:30	0.150	0.002	5	0
DW 47907	1/3/2024 9:30	1/3/2024 9:40	0.150	0.003	5	0
DW 47907	1/3/2024 9:40	1/3/2024 9:50	0.150	0.004	5	0
DW 47907	1/3/2024 9:50	1/3/2024 10:00	0.150	0.006	5	0
DW 47907	1/3/2024 10:00	1/3/2024 10:10	0.150	0.006	5	0
DW 47907	1/3/2024 10:10	1/3/2024 10:20	0.150	0.007	5	0
DW 47907	1/3/2024 10:20	1/3/2024 10:30	0.150	0.008	5	0
DW 47907	1/3/2024 10:30	1/3/2024 10:40	0.150	0.009	5	0
DW 47907	1/3/2024 10:40	1/3/2024 10:50	0.150	0.009	5	0
DW 47907	1/3/2024 10:50	1/3/2024 11:00	0.150	0.01	5	0
DW 47907	1/3/2024 11:00	1/3/2024 11:10	0.150	0.01	5	0
DW 47907	1/3/2024 11:10	1/3/2024 11:20	0.150	0.011	5	0
DW 47907	1/3/2024 11:20	1/3/2024 11:30	0.150	0.012	5	0
DW 47907	1/3/2024 11:30	1/3/2024 11:40	0.150	0.012	5	0
DW 47907	1/3/2024 11:40	1/3/2024 11:50	0.150	0.013	5	0
DW 47907	1/3/2024 11:50	1/3/2024 12:00	0.150	0.013	5	0
DW 47907	1/3/2024 12:00	1/3/2024 12:10	0.150	0.014	5	0
DW 47907	1/3/2024 12:10	1/3/2024 12:20	0.150	0.014	5	0
DW 47907	1/3/2024 12:20	1/3/2024 12:30	0.150	0.015	5	0
DW 47907	1/3/2024 12:30	1/3/2024 12:40	0.150	0.016	5	0
DW 47907	1/3/2024 12:40	1/3/2024 12:50	0.150	0.016	5	0
DW 47907	1/3/2024 12:50	1/3/2024 13:00	0.150	0.017	5	0
DW 47907	1/3/2024 13:00	1/3/2024 13:10	0.150	0.018	5	0
DW 47907	1/3/2024 13:10	1/3/2024 13:20	0.150	0.018	5	0
DW 47907	1/3/2024 13:20	1/3/2024 13:30	0.150	0.019	5	0
DW 47907	1/3/2024 13:30	1/3/2024 13:40	0.150	0.02	5	0
DW 47907	1/3/2024 13:40	1/3/2024 13:50	0.150	0.021	5	0
DW 47907	1/3/2024 13:50	1/3/2024 14:00	0.150	0.021	5	0
DW 47907	1/3/2024 14:00	1/3/2024 14:10	0.150	0.022	5	0
DW 47907	1/3/2024 14:10	1/3/2024 14:20	0.150	0.023	5	0
DW 47907	1/3/2024 14:20	1/3/2024 14:30	0.150	0.023	5	0
DW 47907	1/3/2024 14:30	1/3/2024 14:40	0.150	0.024	5	0
DW 47907	1/3/2024 14:40	1/3/2024 14:50	0.150	0.025	5	0
DW 47907	1/3/2024 14:50	1/3/2024 15:00	0.150	0.025	5	0
DW 47907	1/3/2024 15:00	1/3/2024 15:10	0.150	0.026	5	0
DW 47907	1/3/2024 15:10	1/3/2024 15:20	0.150	0.026	5	0
DW 47907	1/3/2024 15:20	1/3/2024 15:30	0.150	0.027	5	0
DW 47907	1/3/2024 15:30	1/3/2024 15:40	0.150	0.027	5	0
DW 47907	1/3/2024 15:40	1/3/2024 15:50	0.150	0.027	5	0
DW 47907	1/3/2024 15:50	1/3/2024 16:00	0.150	0.028	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/3/2024 8:00	1/3/2024 8:10	0.150	0	5	0
UW 212221	1/3/2024 8:10	1/3/2024 8:20	0.150	0	5	0
UW 212221	1/3/2024 8:20	1/3/2024 8:30	0.150	0	5	0
UW 212221	1/3/2024 8:30	1/3/2024 8:40	0.150	0	5	0
UW 212221	1/3/2024 8:40	1/3/2024 8:50	0.150	0	5	0
UW 212221	1/3/2024 8:50	1/3/2024 9:00	0.150	0.001	5	0
UW 212221	1/3/2024 9:00	1/3/2024 9:10	0.150	0.002	5	0
UW 212221	1/3/2024 9:10	1/3/2024 9:20	0.150	0.002	5	0
UW 212221	1/3/2024 9:20	1/3/2024 9:30	0.150	0.003	5	0
UW 212221	1/3/2024 9:30	1/3/2024 9:40	0.150	0.004	5	0
UW 212221	1/3/2024 9:40	1/3/2024 9:50	0.150	0.004	5	0
UW 212221	1/3/2024 9:50	1/3/2024 10:00	0.150	0.005	5	0
UW 212221	1/3/2024 10:00	1/3/2024 10:10	0.150	0.006	5	0
UW 212221	1/3/2024 10:10	1/3/2024 10:20	0.150	0.006	5	0
UW 212221	1/3/2024 10:20	1/3/2024 10:30	0.150	0.007	5	0
UW 212221	1/3/2024 10:30	1/3/2024 10:40	0.150	0.008	5	0
UW 212221	1/3/2024 10:40	1/3/2024 10:50	0.150	0.008	5	0
UW 212221	1/3/2024 10:50	1/3/2024 11:00	0.150	0.008	5	0
UW 212221	1/3/2024 11:00	1/3/2024 11:10	0.150	0.009	5	0
UW 212221	1/3/2024 11:10	1/3/2024 11:20	0.150	0.009	5	0
UW 212221	1/3/2024 11:20	1/3/2024 11:30	0.150	0.01	5	0
UW 212221	1/3/2024 11:30	1/3/2024 11:40	0.150	0.01	5	0
UW 212221	1/3/2024 11:40	1/3/2024 11:50	0.150	0.01	5	0
UW 212221	1/3/2024 11:50	1/3/2024 12:00	0.150	0.011	5	0
UW 212221	1/3/2024 12:00	1/3/2024 12:10	0.150	0.011	5	0
UW 212221	1/3/2024 12:10	1/3/2024 12:20	0.150	0.011	5	0
UW 212221	1/3/2024 12:20	1/3/2024 12:30	0.150	0.012	5	0
UW 212221	1/3/2024 12:30	1/3/2024 12:40	0.150	0.013	5	0
UW 212221	1/3/2024 12:40	1/3/2024 12:50	0.150	0.013	5	0
UW 212221	1/3/2024 12:50	1/3/2024 13:00	0.150	0.013	5	0
UW 212221	1/3/2024 13:00	1/3/2024 13:10	0.150	0.014	5	0
UW 212221	1/3/2024 13:10	1/3/2024 13:20	0.150	0.014	5	0
UW 212221	1/3/2024 13:20	1/3/2024 13:30	0.150	0.014	5	0
UW 212221	1/3/2024 13:30	1/3/2024 13:40	0.150	0.015	5	0
UW 212221	1/3/2024 13:40	1/3/2024 13:50	0.150	0.015	5	0
UW 212221	1/3/2024 13:50	1/3/2024 14:00	0.150	0.016	5	0
UW 212221	1/3/2024 14:00	1/3/2024 14:10	0.150	0.017	5	0
UW 212221	1/3/2024 14:10	1/3/2024 14:20	0.150	0.017	5	0
UW 212221	1/3/2024 14:20	1/3/2024 14:30	0.150	0.017	5	0
UW 212221	1/3/2024 14:30	1/3/2024 14:40	0.150	0.018	5	0
UW 212221	1/3/2024 14:40	1/3/2024 14:50	0.150	0.018	5	0
UW 212221	1/3/2024 14:50	1/3/2024 15:00	0.150	0.019	5	0
UW 212221	1/3/2024 15:00	1/3/2024 15:10	0.150	0.019	5	0
UW 212221	1/3/2024 15:10	1/3/2024 15:20	0.150	0.019	5	0
UW 212221	1/3/2024 15:20	1/3/2024 15:30	0.150	0.02	5	0
UW 212221	1/3/2024 15:30	1/3/2024 15:40	0.150	0.021	5	0
UW 212221	1/3/2024 15:40	1/3/2024 15:50	0.150	0.021	5	0
UW 212221	1/3/2024 15:50	1/3/2024 16:00	0.150	0.021	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/3/2024 8:00	1/3/2024 8:10	0.150	0	5	0
PER1 50057	1/3/2024 8:10	1/3/2024 8:20	0.150	0	5	0
PER1 50057	1/3/2024 8:20	1/3/2024 8:30	0.150	0	5	0
PER1 50057	1/3/2024 8:30	1/3/2024 8:40	0.150	0	5	0
PER1 50057	1/3/2024 8:40	1/3/2024 8:50	0.150	0.002	5	0
PER1 50057	1/3/2024 8:50	1/3/2024 9:00	0.150	0.003	5	0
PER1 50057	1/3/2024 9:00	1/3/2024 9:10	0.150	0.004	5	0
PER1 50057	1/3/2024 9:10	1/3/2024 9:20	0.150	0.005	5	0
PER1 50057	1/3/2024 9:20	1/3/2024 9:30	0.150	0.006	5	0
PER1 50057	1/3/2024 9:30	1/3/2024 9:40	0.150	0.007	5	0
PER1 50057	1/3/2024 9:40	1/3/2024 9:50	0.150	0.008	5	0
PER1 50057	1/3/2024 9:50	1/3/2024 10:00	0.150	0.009	5	0
PER1 50057	1/3/2024 10:00	1/3/2024 10:10	0.150	0.01	5	0
PER1 50057	1/3/2024 10:10	1/3/2024 10:20	0.150	0.01	5	0
PER1 50057	1/3/2024 10:20	1/3/2024 10:30	0.150	0.011	5	0
PER1 50057	1/3/2024 10:30	1/3/2024 10:40	0.150	0.012	5	0
PER1 50057	1/3/2024 10:40	1/3/2024 10:50	0.150	0.013	5	0
PER1 50057	1/3/2024 10:50	1/3/2024 11:00	0.150	0.013	5	0
PER1 50057	1/3/2024 11:00	1/3/2024 11:10	0.150	0.014	5	0
PER1 50057	1/3/2024 11:10	1/3/2024 11:20	0.150	0.015	5	0
PER1 50057	1/3/2024 11:20	1/3/2024 11:30	0.150	0.016	5	0
PER1 50057	1/3/2024 11:30	1/3/2024 11:40	0.150	0.016	5	0
PER1 50057	1/3/2024 11:40	1/3/2024 11:50	0.150	0.017	5	0
PER1 50057	1/3/2024 11:50	1/3/2024 12:00	0.150	0.018	5	0
PER1 50057	1/3/2024 12:00	1/3/2024 12:10	0.150	0.019	5	0
PER1 50057	1/3/2024 12:10	1/3/2024 12:20	0.150	0.02	5	0
PER1 50057	1/3/2024 12:20	1/3/2024 12:30	0.150	0.021	5	0
PER1 50057	1/3/2024 12:30	1/3/2024 12:40	0.150	0.021	5	0
PER1 50057	1/3/2024 12:40	1/3/2024 12:50	0.150	0.022	5	0
PER1 50057	1/3/2024 12:50	1/3/2024 13:00	0.150	0.023	5	0
PER1 50057	1/3/2024 13:00	1/3/2024 13:10	0.150	0.024	5	0
PER1 50057	1/3/2024 13:10	1/3/2024 13:20	0.150	0.024	5	0
PER1 50057	1/3/2024 13:20	1/3/2024 13:30	0.150	0.025	5	0
PER1 50057	1/3/2024 13:30	1/3/2024 13:40	0.150	0.025	5	0
PER1 50057	1/3/2024 13:40	1/3/2024 13:50	0.150	0.026	5	0
PER1 50057	1/3/2024 13:50	1/3/2024 14:00	0.150	0.026	5	0
PER1 50057	1/3/2024 14:00	1/3/2024 14:10	0.150	0.027	5	0
PER1 50057	1/3/2024 14:10	1/3/2024 14:20	0.150	0.028	5	0
PER1 50057	1/3/2024 14:20	1/3/2024 14:30	0.150	0.029	5	0
PER1 50057	1/3/2024 14:30	1/3/2024 14:40	0.150	0.029	5	0
PER1 50057	1/3/2024 14:40	1/3/2024 14:50	0.150	0.03	5	0
PER1 50057	1/3/2024 14:50	1/3/2024 15:00	0.150	0.031	5	0
PER1 50057	1/3/2024 15:00	1/3/2024 15:10	0.150	0.031	5	0
PER1 50057	1/3/2024 15:10	1/3/2024 15:20	0.150	0.032	5	0
PER1 50057	1/3/2024 15:20	1/3/2024 15:30	0.150	0.033	5	0
PER1 50057	1/3/2024 15:30	1/3/2024 15:40	0.150	0.033	5	0
PER1 50057	1/3/2024 15:40	1/3/2024 15:50	0.150	0.034	5	0
PER1 50057	1/3/2024 15:50	1/3/2024 16:00	0.150	0.035	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/3/2024 8:00	1/3/2024 8:10	0.150	0.016	5	0
PER2 46495	1/3/2024 8:10	1/3/2024 8:20	0.150	0.016	5	0
PER2 46495	1/3/2024 8:20	1/3/2024 8:30	0.150	0.016	5	0
PER2 46495	1/3/2024 8:30	1/3/2024 8:40	0.150	0.016	5	0
PER2 46495	1/3/2024 8:40	1/3/2024 8:50	0.150	0.016	5	0
PER2 46495	1/3/2024 8:50	1/3/2024 9:00	0.150	0.016	5	0
PER2 46495	1/3/2024 9:00	1/3/2024 9:10	0.150	0	5	0
PER2 46495	1/3/2024 9:10	1/3/2024 9:20	0.150	0.001	5	0
PER2 46495	1/3/2024 9:20	1/3/2024 9:30	0.150	0.002	5	0
PER2 46495	1/3/2024 9:30	1/3/2024 9:40	0.150	0.002	5	0
PER2 46495	1/3/2024 9:40	1/3/2024 9:50	0.150	0.003	5	0
PER2 46495	1/3/2024 9:50	1/3/2024 10:00	0.150	0.004	5	0
PER2 46495	1/3/2024 10:00	1/3/2024 10:10	0.150	0.005	5	0
PER2 46495	1/3/2024 10:10	1/3/2024 10:20	0.150	0.006	5	0
PER2 46495	1/3/2024 10:20	1/3/2024 10:30	0.150	0.006	5	0
PER2 46495	1/3/2024 10:30	1/3/2024 10:40	0.150	0.007	5	0
PER2 46495	1/3/2024 10:40	1/3/2024 10:50	0.150	0.007	5	0
PER2 46495	1/3/2024 10:50	1/3/2024 11:00	0.150	0.008	5	0
PER2 46495	1/3/2024 11:00	1/3/2024 11:10	0.150	0.008	5	0
PER2 46495	1/3/2024 11:10	1/3/2024 11:20	0.150	0.009	5	0
PER2 46495	1/3/2024 11:20	1/3/2024 11:30	0.150	0.009	5	0
PER2 46495	1/3/2024 11:30	1/3/2024 11:40	0.150	0.01	5	0
PER2 46495	1/3/2024 11:40	1/3/2024 11:50	0.150	0.01	5	0
PER2 46495	1/3/2024 11:50	1/3/2024 12:00	0.150	0.011	5	0
PER2 46495	1/3/2024 12:00	1/3/2024 12:10	0.150	0.011	5	0
PER2 46495	1/3/2024 12:10	1/3/2024 12:20	0.150	0.012	5	0
PER2 46495	1/3/2024 12:20	1/3/2024 12:30	0.150	0.012	5	0
PER2 46495	1/3/2024 12:30	1/3/2024 12:40	0.150	0.013	5	0
PER2 46495	1/3/2024 12:40	1/3/2024 12:50	0.150	0.014	5	0
PER2 46495	1/3/2024 12:50	1/3/2024 13:00	0.150	0.014	5	0
PER2 46495	1/3/2024 13:00	1/3/2024 13:10	0.150	0.014	5	0
PER2 46495	1/3/2024 13:10	1/3/2024 13:20	0.150	0.015	5	0
PER2 46495	1/3/2024 13:20	1/3/2024 13:30	0.150	0.016	5	0
PER2 46495	1/3/2024 13:30	1/3/2024 13:40	0.150	0.016	5	0
PER2 46495	1/3/2024 13:40	1/3/2024 13:50	0.150	0.017	5	0
PER2 46495	1/3/2024 13:50	1/3/2024 14:00	0.150	0.018	5	0
PER2 46495	1/3/2024 14:00	1/3/2024 14:10	0.150	0.018	5	0
PER2 46495	1/3/2024 14:10	1/3/2024 14:20	0.150	0.019	5	0
PER2 46495	1/3/2024 14:20	1/3/2024 14:30	0.150	0.019	5	0
PER2 46495	1/3/2024 14:30	1/3/2024 14:40	0.150	0.02	5	0
PER2 46495	1/3/2024 14:40	1/3/2024 14:50	0.150	0.02	5	0
PER2 46495	1/3/2024 14:50	1/3/2024 15:00	0.150	0.02	5	0
PER2 46495	1/3/2024 15:00	1/3/2024 15:10	0.150	0.021	5	0
PER2 46495	1/3/2024 15:10	1/3/2024 15:20	0.150	0.021	5	0
PER2 46495	1/3/2024 15:20	1/3/2024 15:30	0.150	0.022	5	0
PER2 46495	1/3/2024 15:30	1/3/2024 15:40	0.150	0.022	5	0
PER2 46495	1/3/2024 15:40	1/3/2024 15:50	0.150	0.023	5	0
PER2 46495	1/3/2024 15:50	1/3/2024 16:00	0.150	0.023	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/4/2024

Weather: 40 deg. F, Clear/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation, drilling piles and installing SOE in A3 building location. 2) Alba continuing groundwater treatment system and well point installation. 3) ECD continuing waterfront development.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below. The downwind CAMP battery experienced issues from approximately 11AM to 12PM and 1230PM to 115PM. The field personnel completed troubleshooting and replaced the battery.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.	

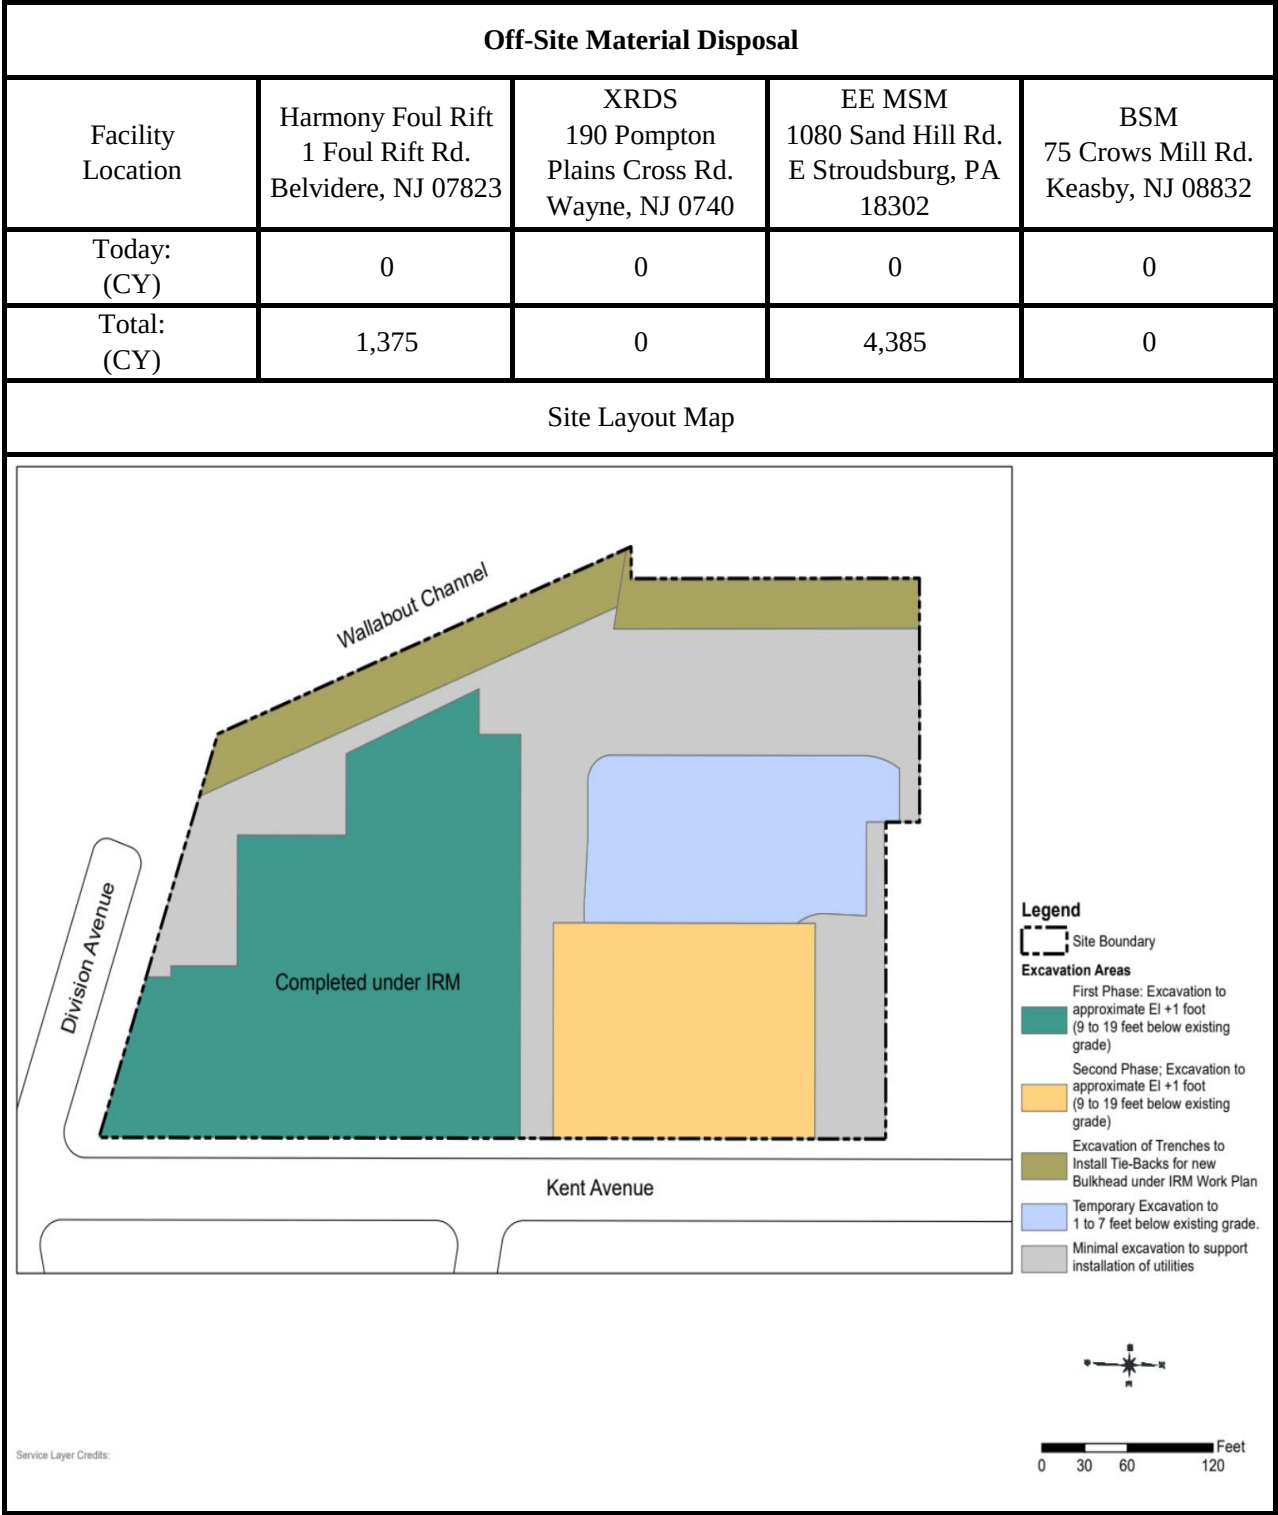


Photo 1:
View of Site conditions
facing south.

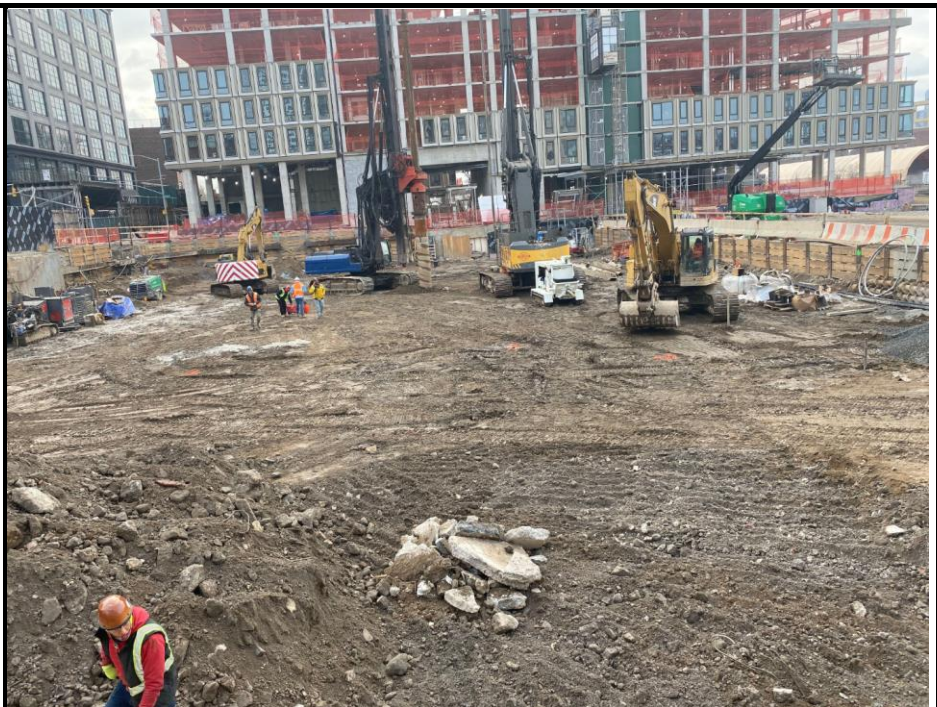


Photo 2:
View of excavation and
drilling for pile
installation and SOE
installation.



Photo 3:
View of Site
conditions facing
north.

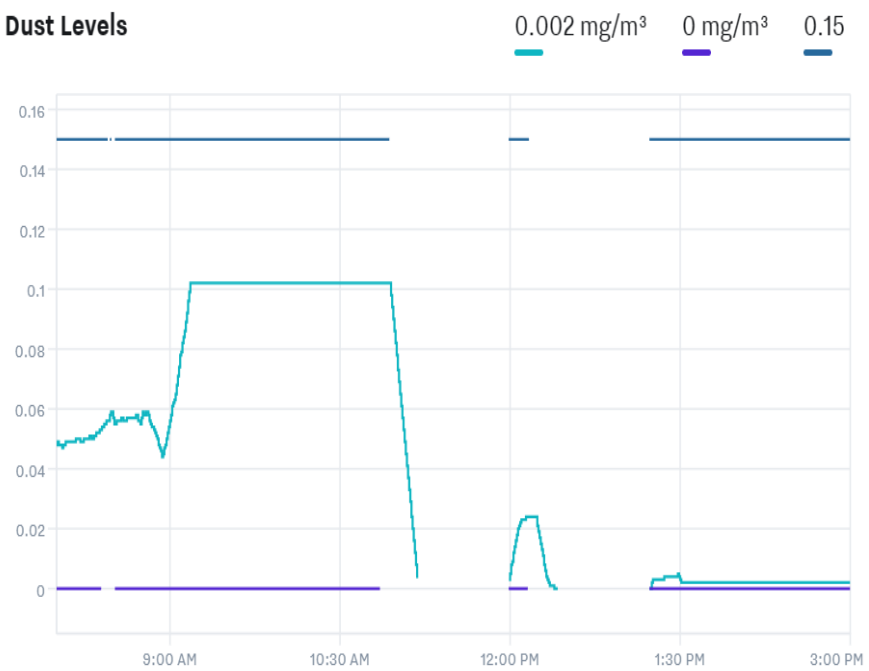


Photo 4:
View of dewatering
system equipment.




CAMP:
Downwind
Particulates


Dust Levels



CAMP:
Downwind VOCs

VOC Levels

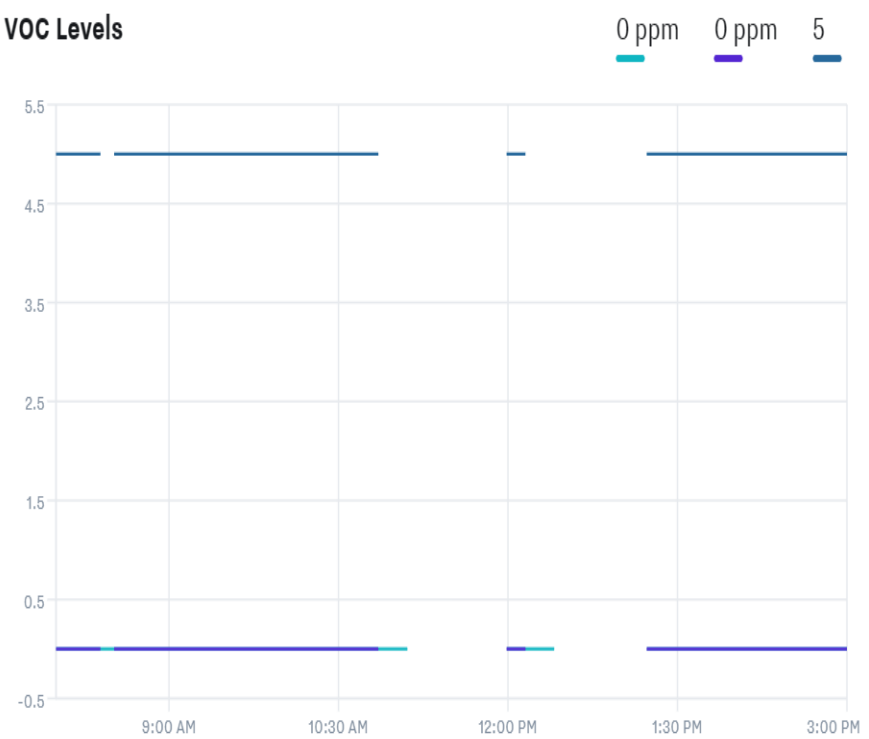

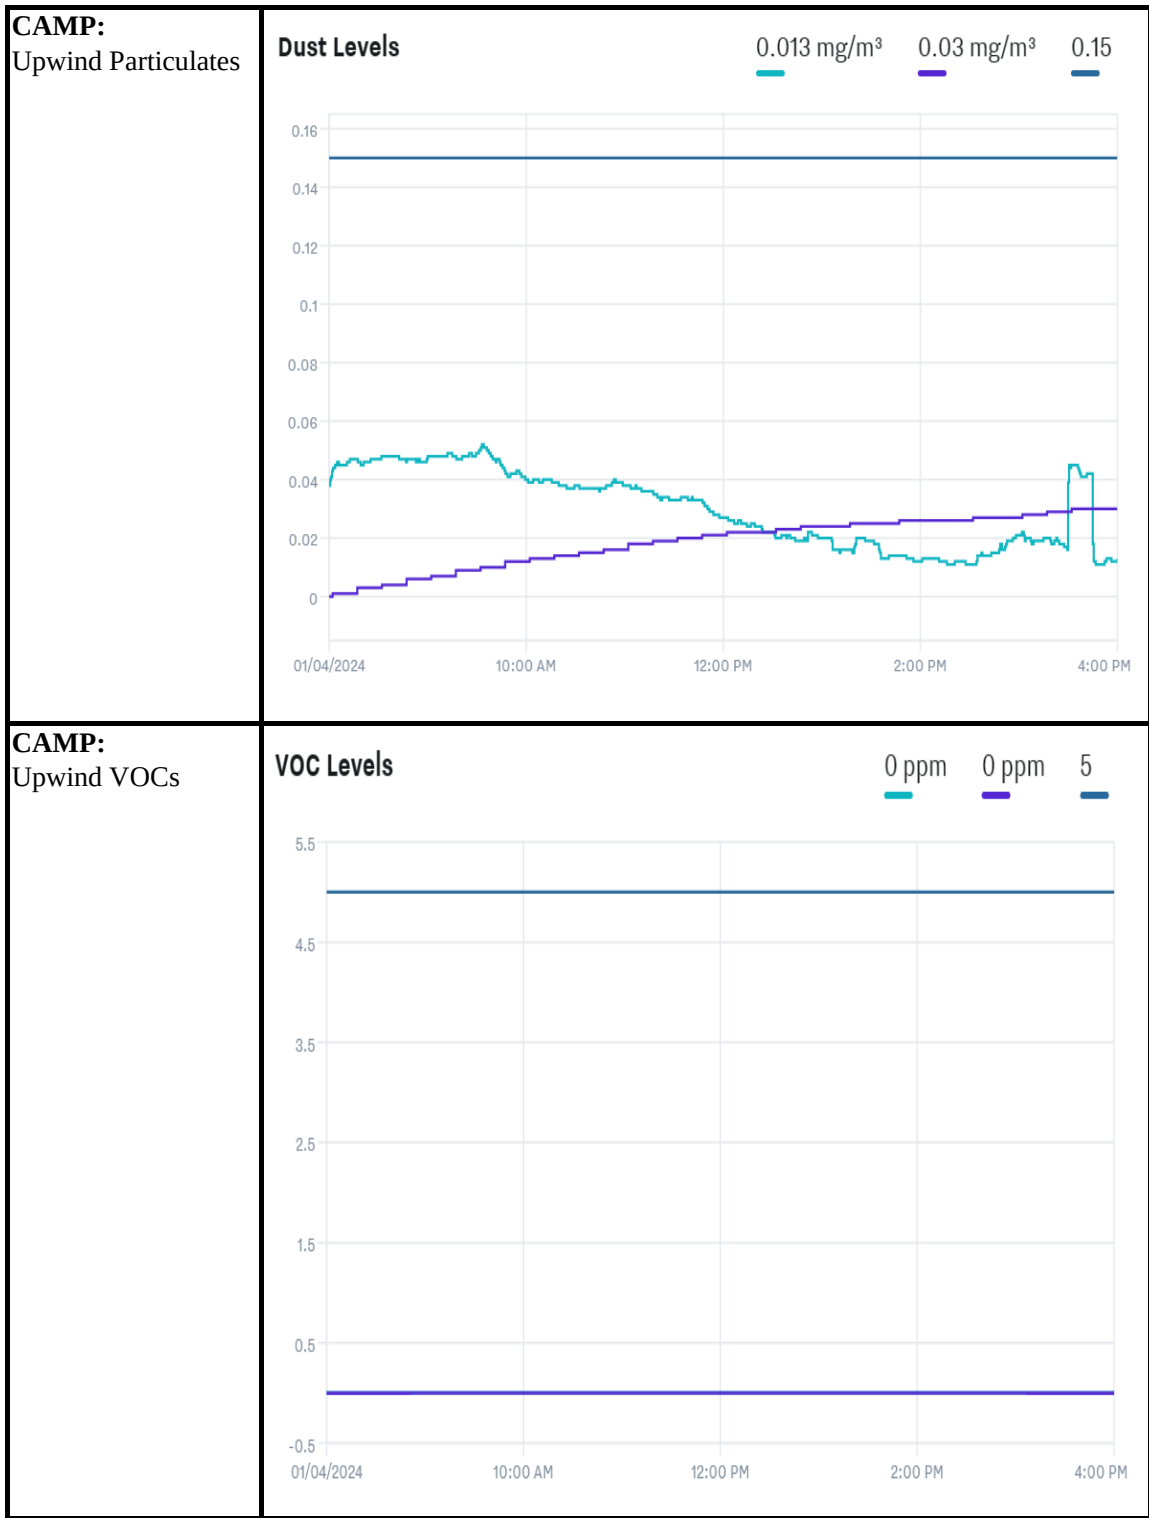

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/4/2024 8:00	1/4/2024 8:10	0.150	0	5	0
DW 47907	1/4/2024 8:10	1/4/2024 8:20	0.150	0	5	0
DW 47907	1/4/2024 8:20	1/4/2024 8:30	0.150	0	5	0
DW 47907	1/4/2024 8:30	1/4/2024 8:40	0.150	0	5	0
DW 47907	1/4/2024 8:40	1/4/2024 8:50	0.150	0	5	0
DW 47907	1/4/2024 8:50	1/4/2024 9:00	0.150	0	5	0
DW 47907	1/4/2024 9:00	1/4/2024 9:10	0.150	0	5	0
DW 47907	1/4/2024 9:10	1/4/2024 9:20	0.150	0	5	0
DW 47907	1/4/2024 9:20	1/4/2024 9:30	0.150	0	5	0
DW 47907	1/4/2024 9:30	1/4/2024 9:40	0.150	0	5	0
DW 47907	1/4/2024 9:40	1/4/2024 9:50	0.150	0	5	0
DW 47907	1/4/2024 9:50	1/4/2024 10:00	0.150	0	5	0
DW 47907	1/4/2024 10:00	1/4/2024 10:10	0.150	0	5	0
DW 47907	1/4/2024 10:10	1/4/2024 10:20	0.150	0	5	0
DW 47907	1/4/2024 10:20	1/4/2024 10:30	0.150	0	5	0
DW 47907	1/4/2024 10:30	1/4/2024 10:40	0.150	0	5	0
DW 47907	1/4/2024 10:40	1/4/2024 10:50	0.150	0	5	0
DW 47907	1/4/2024 10:50	1/4/2024 11:00	0.150	0	5	0
DW 47907	1/4/2024 11:00	1/4/2024 11:10	0.150	0	5	0
DW 47907	1/4/2024 11:10	1/4/2024 11:20	0.150	0	5	0
DW 47907	1/4/2024 11:20	1/4/2024 11:30	0.150	0	5	0
DW 47907	1/4/2024 11:30	1/4/2024 11:40	0.150	0	5	0
DW 47907	1/4/2024 11:40	1/4/2024 11:50	0.150	0	5	0
DW 47907	1/4/2024 11:50	1/4/2024 12:00	0.150	0	5	0
DW 47907	1/4/2024 12:00	1/4/2024 12:10	0.150	0	5	0
DW 47907	1/4/2024 12:10	1/4/2024 12:20	0.150	0	5	0
DW 47907	1/4/2024 12:20	1/4/2024 12:30	0.150	0	5	0
DW 47907	1/4/2024 12:30	1/4/2024 12:40	0.150	0	5	0
DW 47907	1/4/2024 12:40	1/4/2024 12:50	0.150	0	5	0
DW 47907	1/4/2024 12:50	1/4/2024 13:00	0.150	0	5	0
DW 47907	1/4/2024 13:00	1/4/2024 13:10	0.150	0	5	0
DW 47907	1/4/2024 13:10	1/4/2024 13:20	0.150	0	5	0
DW 47907	1/4/2024 13:20	1/4/2024 13:30	0.150	0	5	0
DW 47907	1/4/2024 13:30	1/4/2024 13:40	0.150	0	5	0
DW 47907	1/4/2024 13:40	1/4/2024 13:50	0.150	0	5	0
DW 47907	1/4/2024 13:50	1/4/2024 14:00	0.150	0	5	0
DW 47907	1/4/2024 14:00	1/4/2024 14:10	0.150	0	5	0
DW 47907	1/4/2024 14:10	1/4/2024 14:20	0.150	0	5	0
DW 47907	1/4/2024 14:20	1/4/2024 14:30	0.150	0	5	0
DW 47907	1/4/2024 14:30	1/4/2024 14:40	0.150	0	5	0
DW 47907	1/4/2024 14:40	1/4/2024 14:50	0.150	0	5	0
DW 47907	1/4/2024 14:50	1/4/2024 15:00	0.150	0	5	0
DW 47907	1/4/2024 15:00	1/4/2024 15:10	0.150	0	5	0
DW 47907	1/4/2024 15:10	1/4/2024 15:20	0.150	0	5	0
DW 47907	1/4/2024 15:20	1/4/2024 15:30	0.150	0	5	0
DW 47907	1/4/2024 15:30	1/4/2024 15:40	0.150	0	5	0
DW 47907	1/4/2024 15:40	1/4/2024 15:50	0.150	0	5	0
DW 47907	1/4/2024 15:50	1/4/2024 16:00	0.150	0	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/4/2024 8:00	1/4/2024 8:10	0.150	0.001	5	0
UW 212221	1/4/2024 8:10	1/4/2024 8:20	0.150	0.003	5	0
UW 212221	1/4/2024 8:20	1/4/2024 8:30	0.150	0.003	5	0
UW 212221	1/4/2024 8:30	1/4/2024 8:40	0.150	0.004	5	0
UW 212221	1/4/2024 8:40	1/4/2024 8:50	0.150	0.006	5	0
UW 212221	1/4/2024 8:50	1/4/2024 9:00	0.150	0.006	5	0
UW 212221	1/4/2024 9:00	1/4/2024 9:10	0.150	0.007	5	0
UW 212221	1/4/2024 9:10	1/4/2024 9:20	0.150	0.009	5	0
UW 212221	1/4/2024 9:20	1/4/2024 9:30	0.150	0.009	5	0
UW 212221	1/4/2024 9:30	1/4/2024 9:40	0.150	0.01	5	0
UW 212221	1/4/2024 9:40	1/4/2024 9:50	0.150	0.012	5	0
UW 212221	1/4/2024 9:50	1/4/2024 10:00	0.150	0.012	5	0
UW 212221	1/4/2024 10:00	1/4/2024 10:10	0.150	0.013	5	0
UW 212221	1/4/2024 10:10	1/4/2024 10:20	0.150	0.014	5	0
UW 212221	1/4/2024 10:20	1/4/2024 10:30	0.150	0.014	5	0
UW 212221	1/4/2024 10:30	1/4/2024 10:40	0.150	0.015	5	0
UW 212221	1/4/2024 10:40	1/4/2024 10:50	0.150	0.016	5	0
UW 212221	1/4/2024 10:50	1/4/2024 11:00	0.150	0.016	5	0
UW 212221	1/4/2024 11:00	1/4/2024 11:10	0.150	0.018	5	0
UW 212221	1/4/2024 11:10	1/4/2024 11:20	0.150	0.019	5	0
UW 212221	1/4/2024 11:20	1/4/2024 11:30	0.150	0.019	5	0
UW 212221	1/4/2024 11:30	1/4/2024 11:40	0.150	0.02	5	0
UW 212221	1/4/2024 11:40	1/4/2024 11:50	0.150	0.021	5	0
UW 212221	1/4/2024 11:50	1/4/2024 12:00	0.150	0.021	5	0
UW 212221	1/4/2024 12:00	1/4/2024 12:10	0.150	0.022	5	0
UW 212221	1/4/2024 12:10	1/4/2024 12:20	0.150	0.022	5	0
UW 212221	1/4/2024 12:20	1/4/2024 12:30	0.150	0.022	5	0
UW 212221	1/4/2024 12:30	1/4/2024 12:40	0.150	0.023	5	0
UW 212221	1/4/2024 12:40	1/4/2024 12:50	0.150	0.024	5	0
UW 212221	1/4/2024 12:50	1/4/2024 13:00	0.150	0.024	5	0
UW 212221	1/4/2024 13:00	1/4/2024 13:10	0.150	0.024	5	0
UW 212221	1/4/2024 13:10	1/4/2024 13:20	0.150	0.025	5	0
UW 212221	1/4/2024 13:20	1/4/2024 13:30	0.150	0.025	5	0
UW 212221	1/4/2024 13:30	1/4/2024 13:40	0.150	0.025	5	0
UW 212221	1/4/2024 13:40	1/4/2024 13:50	0.150	0.026	5	0
UW 212221	1/4/2024 13:50	1/4/2024 14:00	0.150	0.026	5	0
UW 212221	1/4/2024 14:00	1/4/2024 14:10	0.150	0.026	5	0
UW 212221	1/4/2024 14:10	1/4/2024 14:20	0.150	0.026	5	0
UW 212221	1/4/2024 14:20	1/4/2024 14:30	0.150	0.026	5	0
UW 212221	1/4/2024 14:30	1/4/2024 14:40	0.150	0.027	5	0
UW 212221	1/4/2024 14:40	1/4/2024 14:50	0.150	0.027	5	0
UW 212221	1/4/2024 14:50	1/4/2024 15:00	0.150	0.027	5	0
UW 212221	1/4/2024 15:00	1/4/2024 15:10	0.150	0.028	5	0
UW 212221	1/4/2024 15:10	1/4/2024 15:20	0.150	0.029	5	0
UW 212221	1/4/2024 15:20	1/4/2024 15:30	0.150	0.029	5	0
UW 212221	1/4/2024 15:30	1/4/2024 15:40	0.150	0.03	5	0
UW 212221	1/4/2024 15:40	1/4/2024 15:50	0.150	0.03	5	0
UW 212221	1/4/2024 15:50	1/4/2024 16:00	0.150	0.03	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/4/2024 8:00	1/4/2024 8:10	0.150	0.006	5	0
PER1 50057	1/4/2024 8:10	1/4/2024 8:20	0.150	0.007	5	0
PER1 50057	1/4/2024 8:20	1/4/2024 8:30	0.150	0.008	5	0
PER1 50057	1/4/2024 8:30	1/4/2024 8:40	0.150	0.01	5	0
PER1 50057	1/4/2024 8:40	1/4/2024 8:50	0.150	0.011	5	0
PER1 50057	1/4/2024 8:50	1/4/2024 9:00	0.150	0.012	5	0
PER1 50057	1/4/2024 9:00	1/4/2024 9:10	0.150	0.013	5	0
PER1 50057	1/4/2024 9:10	1/4/2024 9:20	0.150	0.015	5	0
PER1 50057	1/4/2024 9:20	1/4/2024 9:30	0.150	0.016	5	0
PER1 50057	1/4/2024 9:30	1/4/2024 9:40	0.150	0.017	5	0
PER1 50057	1/4/2024 9:40	1/4/2024 9:50	0.150	0.018	5	0
PER1 50057	1/4/2024 9:50	1/4/2024 10:00	0.150	0.02	5	0
PER1 50057	1/4/2024 10:00	1/4/2024 10:10	0.150	0.021	5	0
PER1 50057	1/4/2024 10:10	1/4/2024 10:20	0.150	0.022	5	0
PER1 50057	1/4/2024 10:20	1/4/2024 10:30	0.150	0.023	5	0
PER1 50057	1/4/2024 10:30	1/4/2024 10:40	0.150	0.024	5	0
PER1 50057	1/4/2024 10:40	1/4/2024 10:50	0.150	0.025	5	0
PER1 50057	1/4/2024 10:50	1/4/2024 11:00	0.150	0.026	5	0
PER1 50057	1/4/2024 11:00	1/4/2024 11:10	0.150	0.027	5	0
PER1 50057	1/4/2024 11:10	1/4/2024 11:20	0.150	0.028	5	0
PER1 50057	1/4/2024 11:20	1/4/2024 11:30	0.150	0.029	5	0
PER1 50057	1/4/2024 11:30	1/4/2024 11:40	0.150	0.032	5	0
PER1 50057	1/4/2024 11:40	1/4/2024 11:50	0.150	0.032	5	0
PER1 50057	1/4/2024 11:50	1/4/2024 12:00	0.150	0.033	5	0
PER1 50057	1/4/2024 12:00	1/4/2024 12:10	0.150	0.034	5	0
PER1 50057	1/4/2024 12:10	1/4/2024 12:20	0.150	0.035	5	0
PER1 50057	1/4/2024 12:20	1/4/2024 12:30	0.150	0.037	5	0
PER1 50057	1/4/2024 12:30	1/4/2024 12:40	0.150	0.038	5	0
PER1 50057	1/4/2024 12:40	1/4/2024 12:50	0.150	0.04	5	0
PER1 50057	1/4/2024 12:50	1/4/2024 13:00	0.150	0.042	5	0
PER1 50057	1/4/2024 13:00	1/4/2024 13:10	0.150	0.042	5	0
PER1 50057	1/4/2024 13:10	1/4/2024 13:20	0.150	0.043	5	0
PER1 50057	1/4/2024 13:20	1/4/2024 13:30	0.150	0.044	5	0
PER1 50057	1/4/2024 13:30	1/4/2024 13:40	0.150	0.045	5	0
PER1 50057	1/4/2024 13:40	1/4/2024 13:50	0.150	0.046	5	0
PER1 50057	1/4/2024 13:50	1/4/2024 14:00	0.150	0.046	5	0
PER1 50057	1/4/2024 14:00	1/4/2024 14:10	0.150	0.047	5	0
PER1 50057	1/4/2024 14:10	1/4/2024 14:20	0.150	0.048	5	0
PER1 50057	1/4/2024 14:20	1/4/2024 14:30	0.150	0.049	5	0
PER1 50057	1/4/2024 14:30	1/4/2024 14:40	0.150	0.049	5	0
PER1 50057	1/4/2024 14:40	1/4/2024 14:50	0.150	0.049	5	0
PER1 50057	1/4/2024 14:50	1/4/2024 15:00	0.150	0.05	5	0
PER1 50057	1/4/2024 15:00	1/4/2024 15:10	0.150	0.052	5	0
PER1 50057	1/4/2024 15:10	1/4/2024 15:20	0.150	0.052	5	0
PER1 50057	1/4/2024 15:20	1/4/2024 15:30	0.150	0.052	5	0
PER1 50057	1/4/2024 15:30	1/4/2024 15:40	0.150	0.052	5	0
PER1 50057	1/4/2024 15:40	1/4/2024 15:50	0.150	0.052	5	0
PER1 50057	1/4/2024 15:50	1/4/2024 16:00	0.150	0.052	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/4/2024 8:00	1/4/2024 8:10	0.150	0.004	5	0
PER2 46495	1/4/2024 8:10	1/4/2024 8:20	0.150	0.005	5	0
PER2 46495	1/4/2024 8:20	1/4/2024 8:30	0.150	0.007	5	0
PER2 46495	1/4/2024 8:30	1/4/2024 8:40	0.150	0.008	5	0
PER2 46495	1/4/2024 8:40	1/4/2024 8:50	0.150	0.009	5	0
PER2 46495	1/4/2024 8:50	1/4/2024 9:00	0.150	0.01	5	0
PER2 46495	1/4/2024 9:00	1/4/2024 9:10	0.150	0.011	5	0
PER2 46495	1/4/2024 9:10	1/4/2024 9:20	0.150	0.012	5	0
PER2 46495	1/4/2024 9:20	1/4/2024 9:30	0.150	0.013	5	0
PER2 46495	1/4/2024 9:30	1/4/2024 9:40	0.150	0.014	5	0
PER2 46495	1/4/2024 9:40	1/4/2024 9:50	0.150	0.015	5	0
PER2 46495	1/4/2024 9:50	1/4/2024 10:00	0.150	0.016	5	0
PER2 46495	1/4/2024 10:00	1/4/2024 10:10	0.150	0.017	5	0
PER2 46495	1/4/2024 10:10	1/4/2024 10:20	0.150	0.017	5	0
PER2 46495	1/4/2024 10:20	1/4/2024 10:30	0.150	0.018	5	0
PER2 46495	1/4/2024 10:30	1/4/2024 10:40	0.150	0.019	5	0
PER2 46495	1/4/2024 10:40	1/4/2024 10:50	0.150	0.02	5	0
PER2 46495	1/4/2024 10:50	1/4/2024 11:00	0.150	0.021	5	0
PER2 46495	1/4/2024 11:00	1/4/2024 11:10	0.150	0.021	5	0
PER2 46495	1/4/2024 11:10	1/4/2024 11:20	0.150	0.022	5	0
PER2 46495	1/4/2024 11:20	1/4/2024 11:30	0.150	0.023	5	0
PER2 46495	1/4/2024 11:30	1/4/2024 11:40	0.150	0.024	5	0
PER2 46495	1/4/2024 11:40	1/4/2024 11:50	0.150	0.024	5	0
PER2 46495	1/4/2024 11:50	1/4/2024 12:00	0.150	0.025	5	0
PER2 46495	1/4/2024 12:00	1/4/2024 12:10	0.150	0.025	5	0
PER2 46495	1/4/2024 12:10	1/4/2024 12:20	0.150	0.026	5	0
PER2 46495	1/4/2024 12:20	1/4/2024 12:30	0.150	0.026	5	0
PER2 46495	1/4/2024 12:30	1/4/2024 12:40	0.150	0.027	5	0
PER2 46495	1/4/2024 12:40	1/4/2024 12:50	0.150	0.027	5	0
PER2 46495	1/4/2024 12:50	1/4/2024 13:00	0.150	0.028	5	0
PER2 46495	1/4/2024 13:00	1/4/2024 13:10	0.150	0.028	5	0
PER2 46495	1/4/2024 13:10	1/4/2024 13:20	0.150	0.028	5	0
PER2 46495	1/4/2024 13:20	1/4/2024 13:30	0.150	0.029	5	0
PER2 46495	1/4/2024 13:30	1/4/2024 13:40	0.150	0.029	5	0
PER2 46495	1/4/2024 13:40	1/4/2024 13:50	0.150	0.029	5	0
PER2 46495	1/4/2024 13:50	1/4/2024 14:00	0.150	0.03	5	0
PER2 46495	1/4/2024 14:00	1/4/2024 14:10	0.150	0.03	5	0
PER2 46495	1/4/2024 14:10	1/4/2024 14:20	0.150	0.03	5	0
PER2 46495	1/4/2024 14:20	1/4/2024 14:30	0.150	0.03	5	0
PER2 46495	1/4/2024 14:30	1/4/2024 14:40	0.150	0.031	5	0
PER2 46495	1/4/2024 14:40	1/4/2024 14:50	0.150	0.031	5	0
PER2 46495	1/4/2024 14:50	1/4/2024 15:00	0.150	0.032	5	0
PER2 46495	1/4/2024 15:00	1/4/2024 15:10	0.150	0.032	5	0
PER2 46495	1/4/2024 15:10	1/4/2024 15:20	0.150	0.032	5	0
PER2 46495	1/4/2024 15:20	1/4/2024 15:30	0.150	0.032	5	0
PER2 46495	1/4/2024 15:30	1/4/2024 15:40	0.150	0.032	5	0
PER2 46495	1/4/2024 15:40	1/4/2024 15:50	0.150	0.032	5	0
PER2 46495	1/4/2024 15:50	1/4/2024 16:00	0.150	0.032	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/5/2024

Weather: 40 deg. F, Clear/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Alba completes the installation of the groundwater treatment system. The system was briefly run in order to collect an influent and effluent sample. Sample names are included below. The system was shut down following sampling and will be restarted for continual operation upon approval from the NYSDEC.
- 3) Import of 12 loads of previously approved soil for backfill in the marine area.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): Influent_20240105 and Effluent_20240105

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

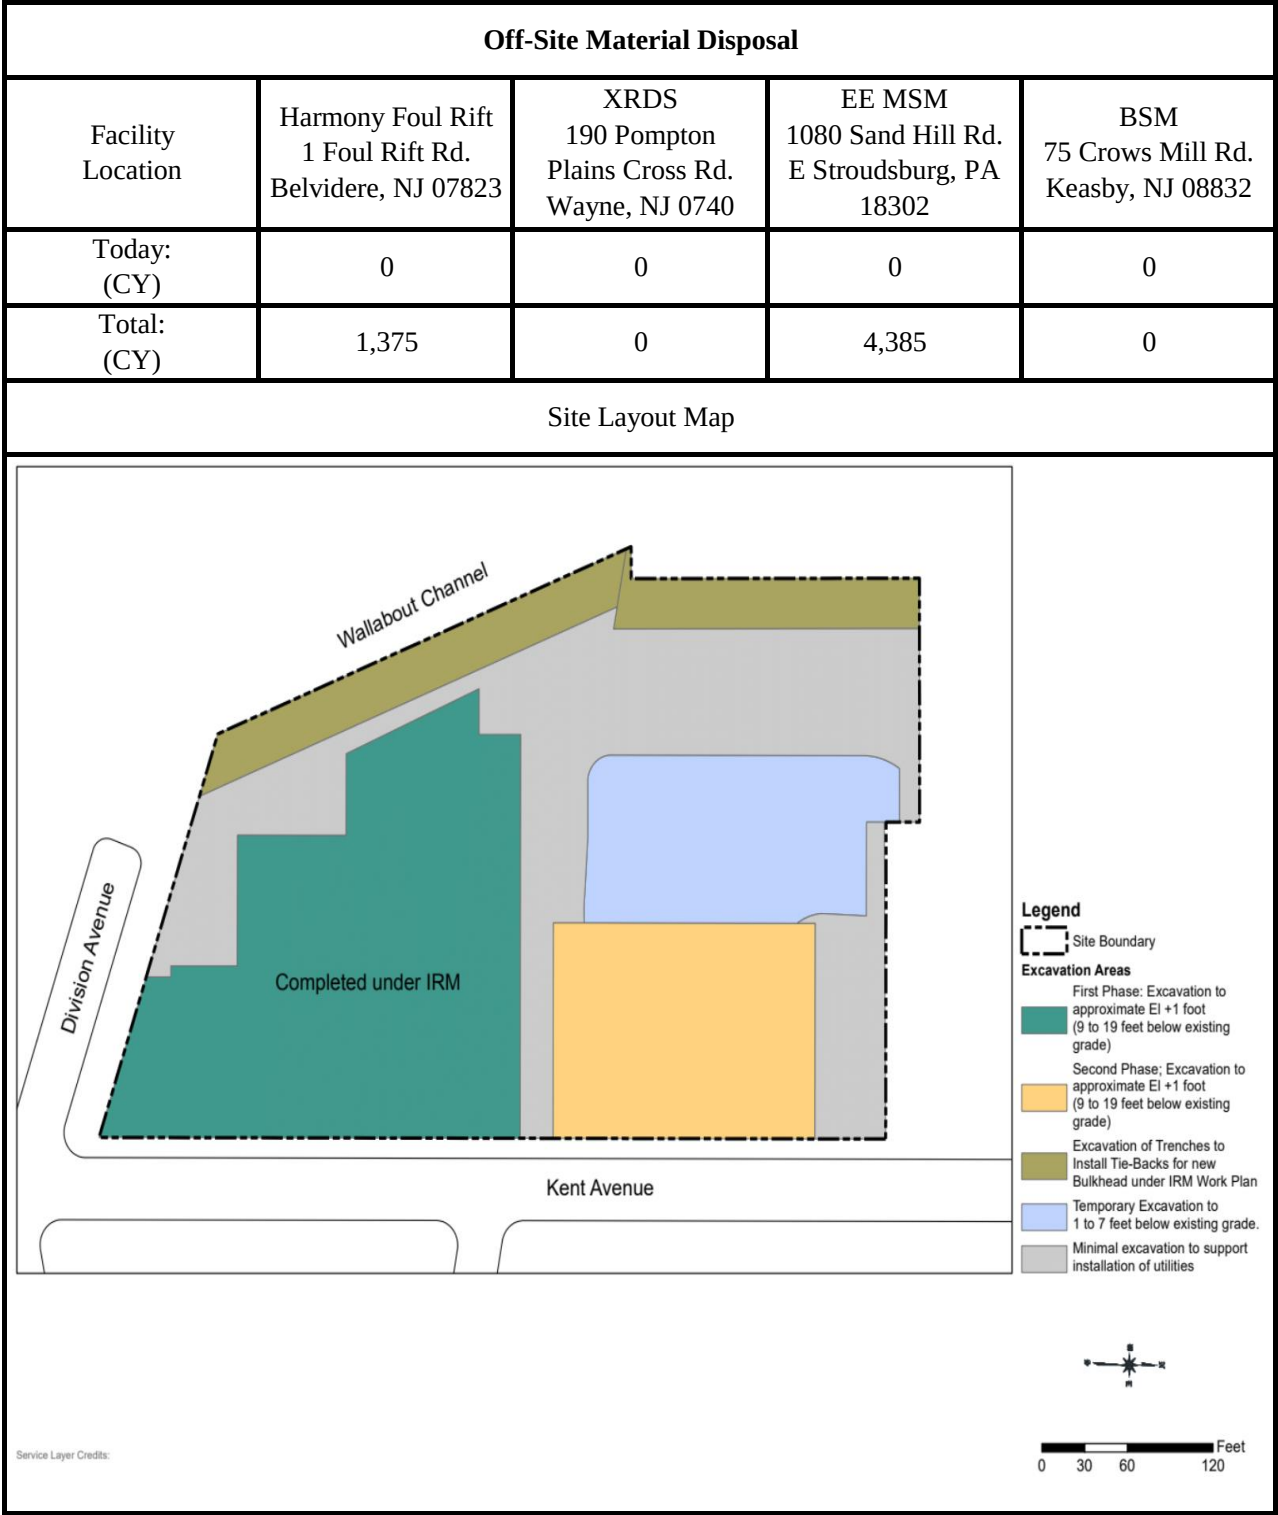


Photo 1:
View of Site conditions
facing northwest.

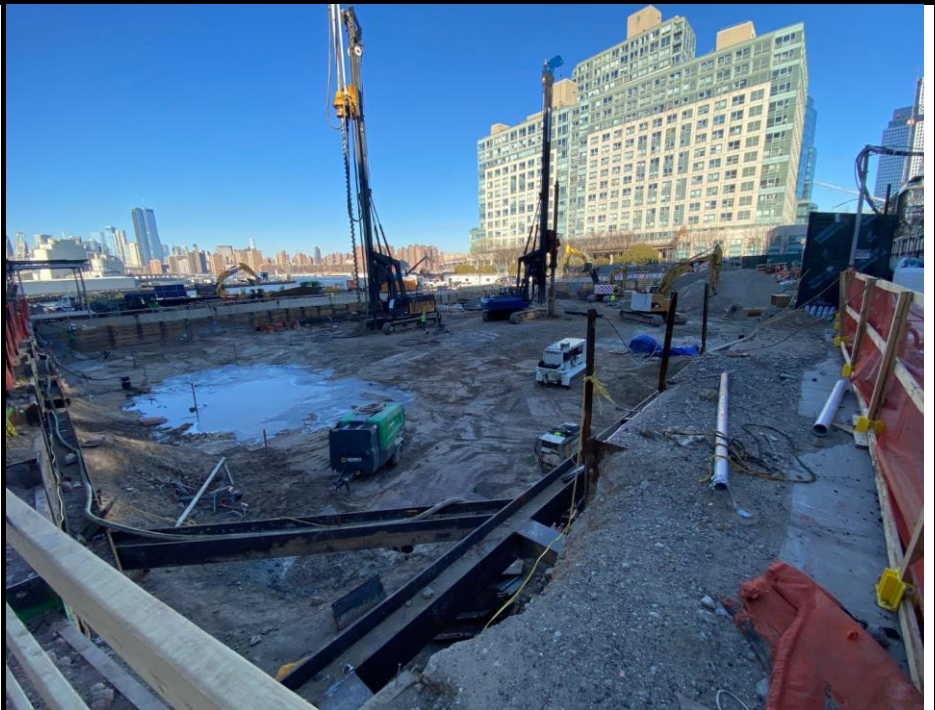


Photo 2:
View of excavation and
drilling for pile
installation and SOE
installation.



Photo 3:
View of SOE
installation.




Photo 4:
View of soil
imported for backfill
in the marine area.



CAMP:
Downwind
Particulates

Dust Levels


0.026 mg/m³ 0 mg/m³ 0.15

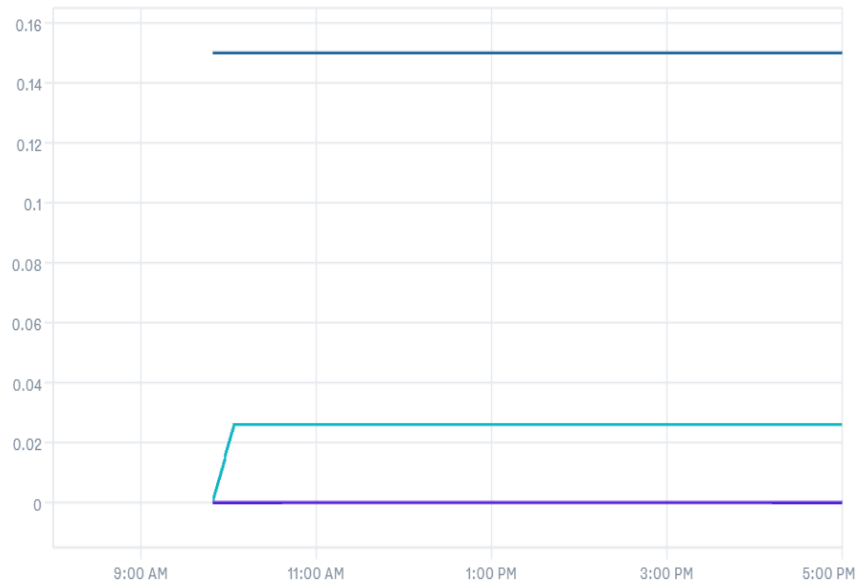

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm 5

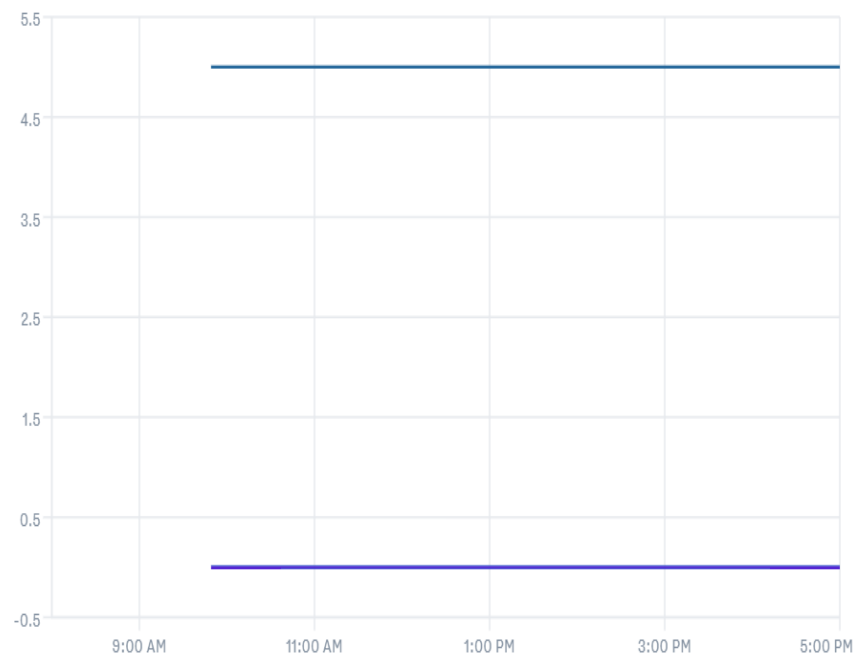

CAMP:
Upwind Particulates

Dust Levels


0 mg/m³ 0 mg/m³ 0

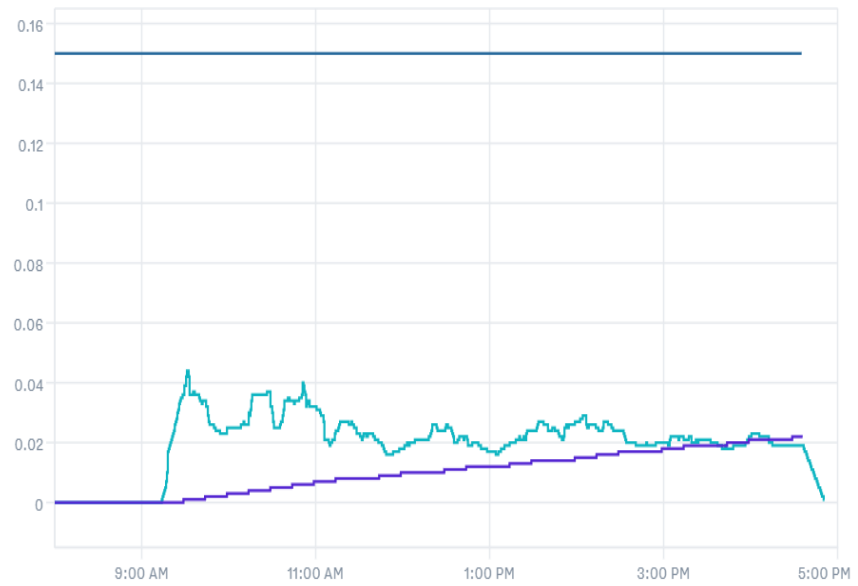

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 0

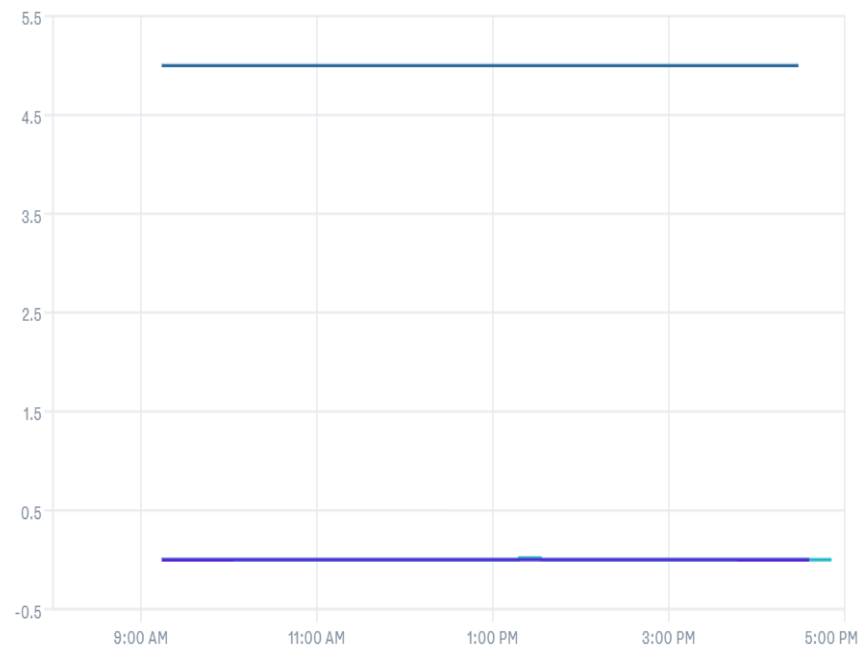

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/5/2024 8:00	1/5/2024 8:10	0.150	0	5	0
DW 47907	1/5/2024 8:10	1/5/2024 8:20	0.150	0	5	0
DW 47907	1/5/2024 8:20	1/5/2024 8:30	0.150	0	5	0
DW 47907	1/5/2024 8:30	1/5/2024 8:40	0.150	0	5	0
DW 47907	1/5/2024 8:40	1/5/2024 8:50	0.150	0	5	0
DW 47907	1/5/2024 8:50	1/5/2024 9:00	0.150	0	5	0
DW 47907	1/5/2024 9:00	1/5/2024 9:10	0.150	0	5	0
DW 47907	1/5/2024 9:10	1/5/2024 9:20	0.150	0	5	0
DW 47907	1/5/2024 9:20	1/5/2024 9:30	0.150	0	5	0
DW 47907	1/5/2024 9:30	1/5/2024 9:40	0.150	0	5	0
DW 47907	1/5/2024 9:40	1/5/2024 9:50	0.150	0	5	0
DW 47907	1/5/2024 9:50	1/5/2024 10:00	0.150	0	5	0
DW 47907	1/5/2024 10:00	1/5/2024 10:10	0.150	0	5	0
DW 47907	1/5/2024 10:10	1/5/2024 10:20	0.150	0	5	0
DW 47907	1/5/2024 10:20	1/5/2024 10:30	0.150	0	5	0
DW 47907	1/5/2024 10:30	1/5/2024 10:40	0.150	0	5	0
DW 47907	1/5/2024 10:40	1/5/2024 10:50	0.150	0	5	0
DW 47907	1/5/2024 10:50	1/5/2024 11:00	0.150	0	5	0
DW 47907	1/5/2024 11:00	1/5/2024 11:10	0.150	0	5	0
DW 47907	1/5/2024 11:10	1/5/2024 11:20	0.150	0	5	0
DW 47907	1/5/2024 11:20	1/5/2024 11:30	0.150	0	5	0
DW 47907	1/5/2024 11:30	1/5/2024 11:40	0.150	0	5	0
DW 47907	1/5/2024 11:40	1/5/2024 11:50	0.150	0	5	0
DW 47907	1/5/2024 11:50	1/5/2024 12:00	0.150	0	5	0
DW 47907	1/5/2024 12:00	1/5/2024 12:10	0.150	0	5	0
DW 47907	1/5/2024 12:10	1/5/2024 12:20	0.150	0	5	0
DW 47907	1/5/2024 12:20	1/5/2024 12:30	0.150	0	5	0
DW 47907	1/5/2024 12:30	1/5/2024 12:40	0.150	0	5	0
DW 47907	1/5/2024 12:40	1/5/2024 12:50	0.150	0	5	0
DW 47907	1/5/2024 12:50	1/5/2024 13:00	0.150	0	5	0
DW 47907	1/5/2024 13:00	1/5/2024 13:10	0.150	0	5	0
DW 47907	1/5/2024 13:10	1/5/2024 13:20	0.150	0	5	0
DW 47907	1/5/2024 13:20	1/5/2024 13:30	0.150	0	5	0
DW 47907	1/5/2024 13:30	1/5/2024 13:40	0.150	0	5	0
DW 47907	1/5/2024 13:40	1/5/2024 13:50	0.150	0	5	0
DW 47907	1/5/2024 13:50	1/5/2024 14:00	0.150	0	5	0
DW 47907	1/5/2024 14:00	1/5/2024 14:10	0.150	0	5	0
DW 47907	1/5/2024 14:10	1/5/2024 14:20	0.150	0	5	0
DW 47907	1/5/2024 14:20	1/5/2024 14:30	0.150	0	5	0
DW 47907	1/5/2024 14:30	1/5/2024 14:40	0.150	0	5	0
DW 47907	1/5/2024 14:40	1/5/2024 14:50	0.150	0	5	0
DW 47907	1/5/2024 14:50	1/5/2024 15:00	0.150	0	5	0
DW 47907	1/5/2024 15:00	1/5/2024 15:10	0.150	0	5	0
DW 47907	1/5/2024 15:10	1/5/2024 15:20	0.150	0	5	0
DW 47907	1/5/2024 15:20	1/5/2024 15:30	0.150	0	5	0
DW 47907	1/5/2024 15:30	1/5/2024 15:40	0.150	0	5	0
DW 47907	1/5/2024 15:40	1/5/2024 15:50	0.150	0	5	0
DW 47907	1/5/2024 15:50	1/5/2024 16:00	0.150	0	5	0
DW 47907	1/5/2024 16:00	1/5/2024 16:10	0.150	0	5	0
DW 47907	1/5/2024 16:10	1/5/2024 16:20	0.150	0	5	0
DW 47907	1/5/2024 16:20	1/5/2024 16:30	0.150	0	5	0
DW 47907	1/5/2024 16:30	1/5/2024 16:40	0.150	0	5	0
DW 47907	1/5/2024 16:40	1/5/2024 16:50	0.150	0	5	0
DW 47907	1/5/2024 16:50	1/5/2024 17:00	0.150	0	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/5/2024 8:00	1/5/2024 8:10	0.150	0	5	0
UW 212221	1/5/2024 8:10	1/5/2024 8:20	0.150	0	5	0
UW 212221	1/5/2024 8:20	1/5/2024 8:30	0.150	0	5	0
UW 212221	1/5/2024 8:30	1/5/2024 8:40	0.150	0	5	0
UW 212221	1/5/2024 8:40	1/5/2024 8:50	0.150	0	5	0
UW 212221	1/5/2024 8:50	1/5/2024 9:00	0.150	0	5	0
UW 212221	1/5/2024 9:00	1/5/2024 9:10	0.150	0	5	0
UW 212221	1/5/2024 9:10	1/5/2024 9:20	0.150	0	5	0
UW 212221	1/5/2024 9:20	1/5/2024 9:30	0.150	0.001	5	0
UW 212221	1/5/2024 9:30	1/5/2024 9:40	0.150	0.001	5	0
UW 212221	1/5/2024 9:40	1/5/2024 9:50	0.150	0.002	5	0
UW 212221	1/5/2024 9:50	1/5/2024 10:00	0.150	0.003	5	0
UW 212221	1/5/2024 10:00	1/5/2024 10:10	0.150	0.003	5	0
UW 212221	1/5/2024 10:10	1/5/2024 10:20	0.150	0.004	5	0
UW 212221	1/5/2024 10:20	1/5/2024 10:30	0.150	0.005	5	0
UW 212221	1/5/2024 10:30	1/5/2024 10:40	0.150	0.005	5	0
UW 212221	1/5/2024 10:40	1/5/2024 10:50	0.150	0.006	5	0
UW 212221	1/5/2024 10:50	1/5/2024 11:00	0.150	0.007	5	0
UW 212221	1/5/2024 11:00	1/5/2024 11:10	0.150	0.007	5	0
UW 212221	1/5/2024 11:10	1/5/2024 11:20	0.150	0.008	5	0
UW 212221	1/5/2024 11:20	1/5/2024 11:30	0.150	0.008	5	0
UW 212221	1/5/2024 11:30	1/5/2024 11:40	0.150	0.008	5	0
UW 212221	1/5/2024 11:40	1/5/2024 11:50	0.150	0.009	5	0
UW 212221	1/5/2024 11:50	1/5/2024 12:00	0.150	0.01	5	0
UW 212221	1/5/2024 12:00	1/5/2024 12:10	0.150	0.01	5	0
UW 212221	1/5/2024 12:10	1/5/2024 12:20	0.150	0.01	5	0
UW 212221	1/5/2024 12:20	1/5/2024 12:30	0.150	0.011	5	0
UW 212221	1/5/2024 12:30	1/5/2024 12:40	0.150	0.011	5	0
UW 212221	1/5/2024 12:40	1/5/2024 12:50	0.150	0.012	5	0
UW 212221	1/5/2024 12:50	1/5/2024 13:00	0.150	0.012	5	0
UW 212221	1/5/2024 13:00	1/5/2024 13:10	0.150	0.012	5	0
UW 212221	1/5/2024 13:10	1/5/2024 13:20	0.150	0.013	5	0
UW 212221	1/5/2024 13:20	1/5/2024 13:30	0.150	0.014	5	0
UW 212221	1/5/2024 13:30	1/5/2024 13:40	0.150	0.014	5	0
UW 212221	1/5/2024 13:40	1/5/2024 13:50	0.150	0.014	5	0
UW 212221	1/5/2024 13:50	1/5/2024 14:00	0.150	0.015	5	0
UW 212221	1/5/2024 14:00	1/5/2024 14:10	0.150	0.015	5	0
UW 212221	1/5/2024 14:10	1/5/2024 14:20	0.150	0.016	5	0
UW 212221	1/5/2024 14:20	1/5/2024 14:30	0.150	0.017	5	0
UW 212221	1/5/2024 14:30	1/5/2024 14:40	0.150	0.017	5	0
UW 212221	1/5/2024 14:40	1/5/2024 14:50	0.150	0.017	5	0
UW 212221	1/5/2024 14:50	1/5/2024 15:00	0.150	0.018	5	0
UW 212221	1/5/2024 15:00	1/5/2024 15:10	0.150	0.018	5	0
UW 212221	1/5/2024 15:10	1/5/2024 15:20	0.150	0.019	5	0
UW 212221	1/5/2024 15:20	1/5/2024 15:30	0.150	0.019	5	0
UW 212221	1/5/2024 15:30	1/5/2024 15:40	0.150	0.019	5	0
UW 212221	1/5/2024 15:40	1/5/2024 15:50	0.150	0.02	5	0
UW 212221	1/5/2024 15:50	1/5/2024 16:00	0.150	0.021	5	0
UW 212221	1/5/2024 16:00	1/5/2024 16:10	0.150	0.021	5	0
UW 212221	1/5/2024 16:10	1/5/2024 16:20	0.150	0.021	5	0
UW 212221	1/5/2024 16:20	1/5/2024 16:30	0.150	0.022	5	0
UW 212221	1/5/2024 16:30	1/5/2024 16:40	0.150	0.022	5	0
UW 212221	1/5/2024 16:40	1/5/2024 16:50	0.150	0	5	0
UW 212221	1/5/2024 16:50	1/5/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/5/2024 8:00	1/5/2024 8:10	0.150	0	5	0
PER1 50057	1/5/2024 8:10	1/5/2024 8:20	0.150	0	5	0
PER1 50057	1/5/2024 8:20	1/5/2024 8:30	0.150	0	5	0
PER1 50057	1/5/2024 8:30	1/5/2024 8:40	0.150	0	5	0
PER1 50057	1/5/2024 8:40	1/5/2024 8:50	0.150	0	5	0
PER1 50057	1/5/2024 8:50	1/5/2024 9:00	0.150	0.002	5	0
PER1 50057	1/5/2024 9:00	1/5/2024 9:10	0.150	0.004	5	0
PER1 50057	1/5/2024 9:10	1/5/2024 9:20	0.150	0.005	5	0
PER1 50057	1/5/2024 9:20	1/5/2024 9:30	0.150	0.006	5	0
PER1 50057	1/5/2024 9:30	1/5/2024 9:40	0.150	0.008	5	0
PER1 50057	1/5/2024 9:40	1/5/2024 9:50	0.150	0.009	5	0
PER1 50057	1/5/2024 9:50	1/5/2024 10:00	0.150	0.011	5	0
PER1 50057	1/5/2024 10:00	1/5/2024 10:10	0.150	0.012	5	0
PER1 50057	1/5/2024 10:10	1/5/2024 10:20	0.150	0.014	5	0
PER1 50057	1/5/2024 10:20	1/5/2024 10:30	0.150	0.016	5	0
PER1 50057	1/5/2024 10:30	1/5/2024 10:40	0.150	0.017	5	0
PER1 50057	1/5/2024 10:40	1/5/2024 10:50	0.150	0.018	5	0
PER1 50057	1/5/2024 10:50	1/5/2024 11:00	0.150	0.019	5	0
PER1 50057	1/5/2024 11:00	1/5/2024 11:10	0.150	0.019	5	0
PER1 50057	1/5/2024 11:10	1/5/2024 11:20	0.150	0.021	5	0
PER1 50057	1/5/2024 11:20	1/5/2024 11:30	0.150	0.022	5	0
PER1 50057	1/5/2024 11:30	1/5/2024 11:40	0.150	0.023	5	0
PER1 50057	1/5/2024 11:40	1/5/2024 11:50	0.150	0.023	5	0
PER1 50057	1/5/2024 11:50	1/5/2024 12:00	0.150	0.025	5	0
PER1 50057	1/5/2024 12:00	1/5/2024 12:10	0.150	0.026	5	0
PER1 50057	1/5/2024 12:10	1/5/2024 12:20	0.150	0.026	5	0
PER1 50057	1/5/2024 12:20	1/5/2024 12:30	0.150	0.028	5	0
PER1 50057	1/5/2024 12:30	1/5/2024 12:40	0.150	0.029	5	0
PER1 50057	1/5/2024 12:40	1/5/2024 12:50	0.150	0.03	5	0
PER1 50057	1/5/2024 12:50	1/5/2024 13:00	0.150	0.03	5	0
PER1 50057	1/5/2024 13:00	1/5/2024 13:10	0.150	0.031	5	0
PER1 50057	1/5/2024 13:10	1/5/2024 13:20	0.150	0.032	5	0
PER1 50057	1/5/2024 13:20	1/5/2024 13:30	0.150	0.032	5	0
PER1 50057	1/5/2024 13:30	1/5/2024 13:40	0.150	0.033	5	0
PER1 50057	1/5/2024 13:40	1/5/2024 13:50	0.150	0.034	5	0
PER1 50057	1/5/2024 13:50	1/5/2024 14:00	0.150	0.034	5	0
PER1 50057	1/5/2024 14:00	1/5/2024 14:10	0.150	0.036	5	0
PER1 50057	1/5/2024 14:10	1/5/2024 14:20	0.150	0.036	5	0
PER1 50057	1/5/2024 14:20	1/5/2024 14:30	0.150	0.036	5	0
PER1 50057	1/5/2024 14:30	1/5/2024 14:40	0.150	0.037	5	0
PER1 50057	1/5/2024 14:40	1/5/2024 14:50	0.150	0.037	5	0
PER1 50057	1/5/2024 14:50	1/5/2024 15:00	0.150	0.038	5	0
PER1 50057	1/5/2024 15:00	1/5/2024 15:10	0.150	0.038	5	0
PER1 50057	1/5/2024 15:10	1/5/2024 15:20	0.150	0.039	5	0
PER1 50057	1/5/2024 15:20	1/5/2024 15:30	0.150	0.039	5	0
PER1 50057	1/5/2024 15:30	1/5/2024 15:40	0.150	0.04	5	0
PER1 50057	1/5/2024 15:40	1/5/2024 15:50	0.150	0.04	5	0
PER1 50057	1/5/2024 15:50	1/5/2024 16:00	0.150	0	5	0
PER1 50057	1/5/2024 16:00	1/5/2024 16:10	0.150	0	5	0
PER1 50057	1/5/2024 16:10	1/5/2024 16:20	0.150	0	5	0
PER1 50057	1/5/2024 16:20	1/5/2024 16:30	0.150	0	5	0
PER1 50057	1/5/2024 16:30	1/5/2024 16:40	0.150	0	5	0
PER1 50057	1/5/2024 16:40	1/5/2024 16:50	0.150	0	5	0
PER1 50057	1/5/2024 16:50	1/5/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/5/2024 8:00	1/5/2024 8:10	0.150	0.032	5	0
PER2 46495	1/5/2024 8:10	1/5/2024 8:20	0.150	0.032	5	0
PER2 46495	1/5/2024 8:20	1/5/2024 8:30	0.150	0.032	5	0
PER2 46495	1/5/2024 8:30	1/5/2024 8:40	0.150	0.032	5	0
PER2 46495	1/5/2024 8:40	1/5/2024 8:50	0.150	0.032	5	0
PER2 46495	1/5/2024 8:50	1/5/2024 9:00	0.150	0.032	5	0
PER2 46495	1/5/2024 9:00	1/5/2024 9:10	0.150	0.032	5	0
PER2 46495	1/5/2024 9:10	1/5/2024 9:20	0.150	0.032	5	0
PER2 46495	1/5/2024 9:20	1/5/2024 9:30	0.150	0.032	5	0
PER2 46495	1/5/2024 9:30	1/5/2024 9:40	0.150	0.032	5	0
PER2 46495	1/5/2024 9:40	1/5/2024 9:50	0.150	0.032	5	0
PER2 46495	1/5/2024 9:50	1/5/2024 10:00	0.150	0	5	0
PER2 46495	1/5/2024 10:00	1/5/2024 10:10	0.150	0.001	5	0
PER2 46495	1/5/2024 10:10	1/5/2024 10:20	0.150	0.002	5	0
PER2 46495	1/5/2024 10:20	1/5/2024 10:30	0.150	0.002	5	0
PER2 46495	1/5/2024 10:30	1/5/2024 10:40	0.150	0.003	5	0
PER2 46495	1/5/2024 10:40	1/5/2024 10:50	0.150	0.004	5	0
PER2 46495	1/5/2024 10:50	1/5/2024 11:00	0.150	0.004	5	0
PER2 46495	1/5/2024 11:00	1/5/2024 11:10	0.150	0.004	5	0
PER2 46495	1/5/2024 11:10	1/5/2024 11:20	0.150	0.005	5	0
PER2 46495	1/5/2024 11:20	1/5/2024 11:30	0.150	0.005	5	0
PER2 46495	1/5/2024 11:30	1/5/2024 11:40	0.150	0.006	5	0
PER2 46495	1/5/2024 11:40	1/5/2024 11:50	0.150	0.006	5	0
PER2 46495	1/5/2024 11:50	1/5/2024 12:00	0.150	0.006	5	0
PER2 46495	1/5/2024 12:00	1/5/2024 12:10	0.150	0.007	5	0
PER2 46495	1/5/2024 12:10	1/5/2024 12:20	0.150	0.007	5	0
PER2 46495	1/5/2024 12:20	1/5/2024 12:30	0.150	0.008	5	0
PER2 46495	1/5/2024 12:30	1/5/2024 12:40	0.150	0.008	5	0
PER2 46495	1/5/2024 12:40	1/5/2024 12:50	0.150	0.009	5	0
PER2 46495	1/5/2024 12:50	1/5/2024 13:00	0.150	0.009	5	0
PER2 46495	1/5/2024 13:00	1/5/2024 13:10	0.150	0.009	5	0
PER2 46495	1/5/2024 13:10	1/5/2024 13:20	0.150	0.01	5	0
PER2 46495	1/5/2024 13:20	1/5/2024 13:30	0.150	0.01	5	0
PER2 46495	1/5/2024 13:30	1/5/2024 13:40	0.150	0.011	5	0
PER2 46495	1/5/2024 13:40	1/5/2024 13:50	0.150	0.011	5	0
PER2 46495	1/5/2024 13:50	1/5/2024 14:00	0.150	0.012	5	0
PER2 46495	1/5/2024 14:00	1/5/2024 14:10	0.150	0.012	5	0
PER2 46495	1/5/2024 14:10	1/5/2024 14:20	0.150	0.013	5	0
PER2 46495	1/5/2024 14:20	1/5/2024 14:30	0.150	0.014	5	0
PER2 46495	1/5/2024 14:30	1/5/2024 14:40	0.150	0.014	5	0
PER2 46495	1/5/2024 14:40	1/5/2024 14:50	0.150	0.014	5	0
PER2 46495	1/5/2024 14:50	1/5/2024 15:00	0.150	0.015	5	0
PER2 46495	1/5/2024 15:00	1/5/2024 15:10	0.150	0.015	5	0
PER2 46495	1/5/2024 15:10	1/5/2024 15:20	0.150	0.016	5	0
PER2 46495	1/5/2024 15:20	1/5/2024 15:30	0.150	0.016	5	0
PER2 46495	1/5/2024 15:30	1/5/2024 15:40	0.150	0.017	5	0
PER2 46495	1/5/2024 15:40	1/5/2024 15:50	0.150	0.017	5	0
PER2 46495	1/5/2024 15:50	1/5/2024 16:00	0.150	0.017	5	0
PER2 46495	1/5/2024 16:00	1/5/2024 16:10	0.150	0.017	5	0
PER2 46495	1/5/2024 16:10	1/5/2024 16:20	0.150	0.017	5	0
PER2 46495	1/5/2024 16:20	1/5/2024 16:30	0.150	0.017	5	0
PER2 46495	1/5/2024 16:30	1/5/2024 16:40	0.150	0.017	5	0
PER2 46495	1/5/2024 16:40	1/5/2024 16:50	0.150	0.017	5	0
PER2 46495	1/5/2024 16:50	1/5/2024 17:00	0.150	0.017	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/8/2024

Weather: 35 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) ECD continuing grading in the marine area.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

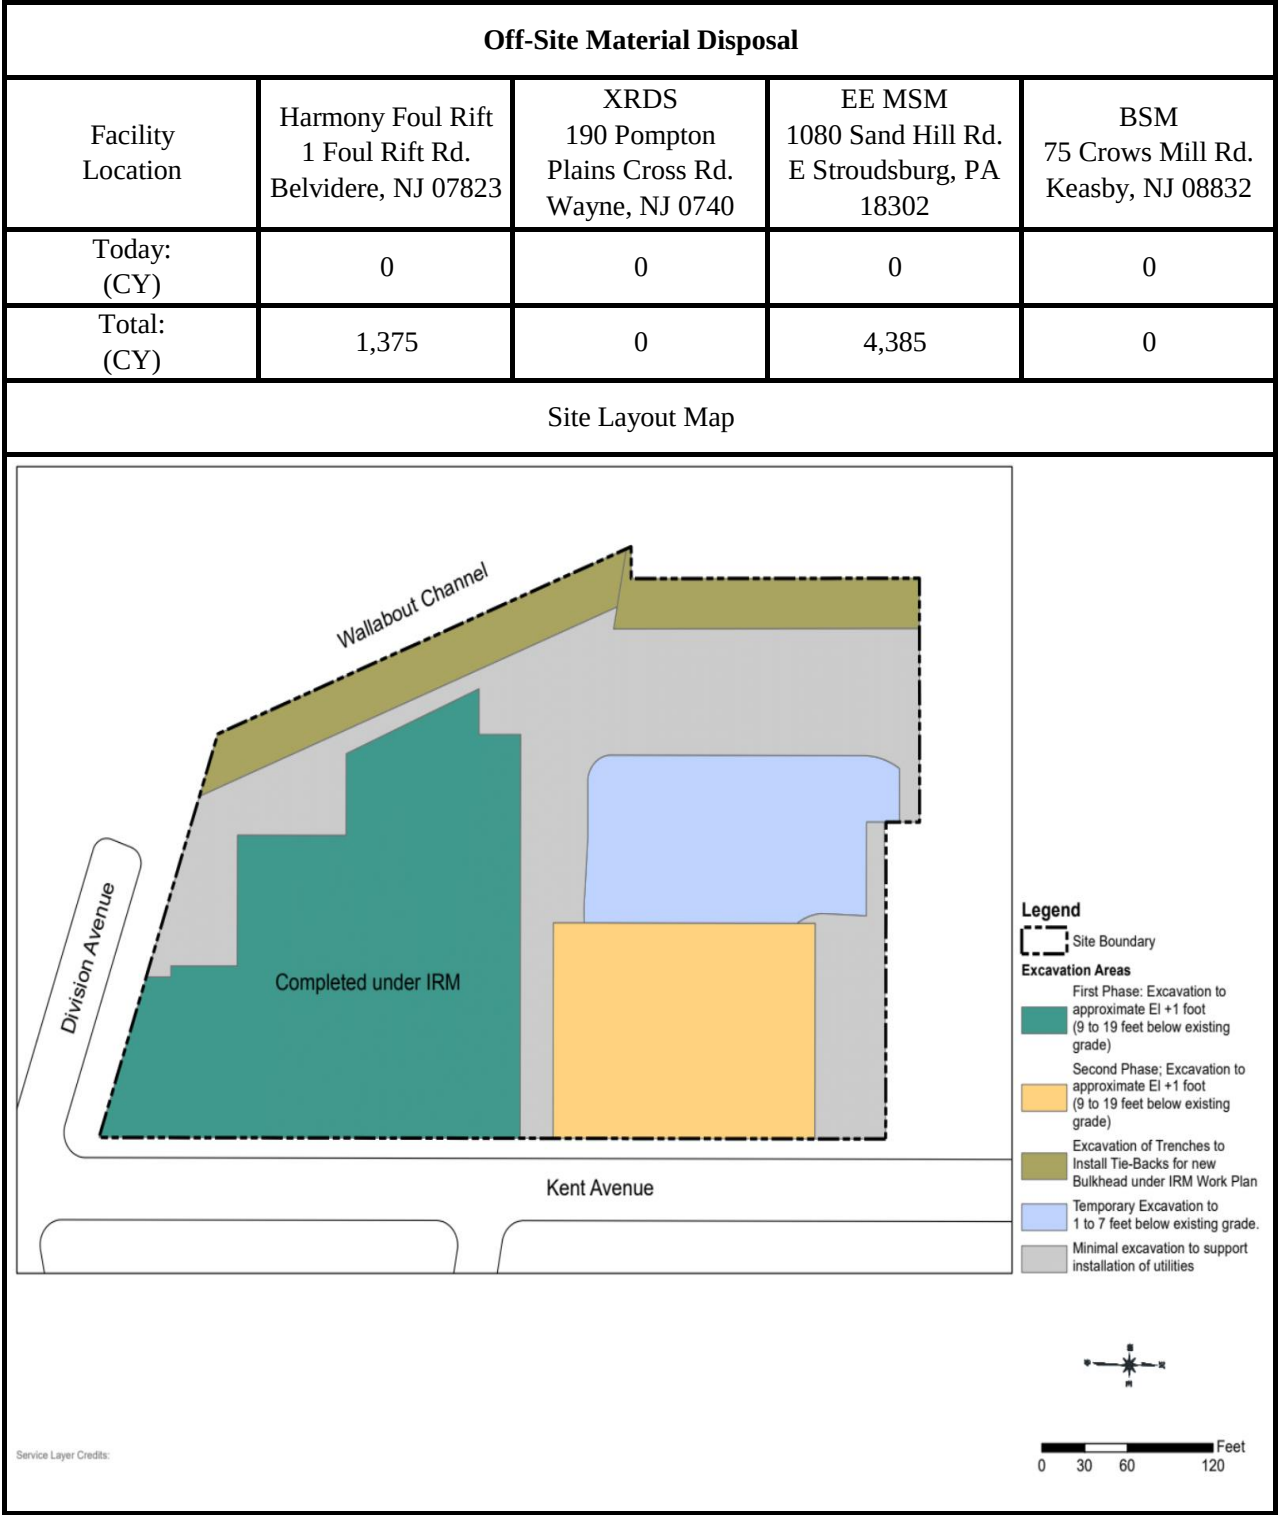


Photo 1:

View of Site conditions facing north.



Photo 2:

View of excavation and drilling for pile installation and SOE installation.


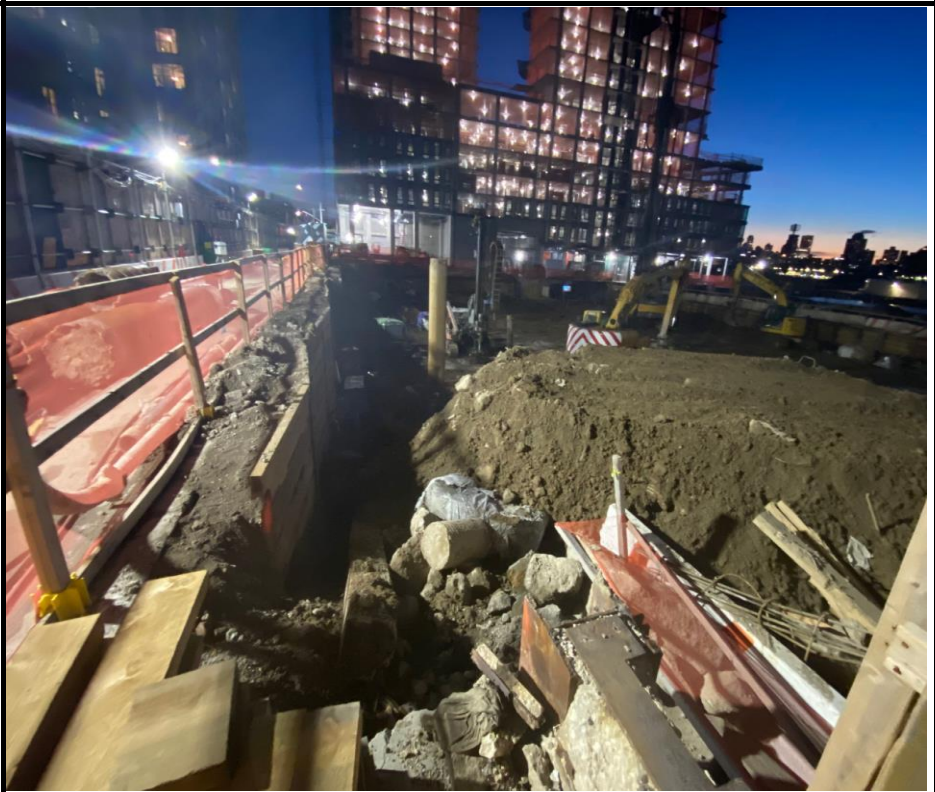


Photo 3:
View of site
conditions facing
southeast.




Photo 4:
View of site
conditions facing
southwest.

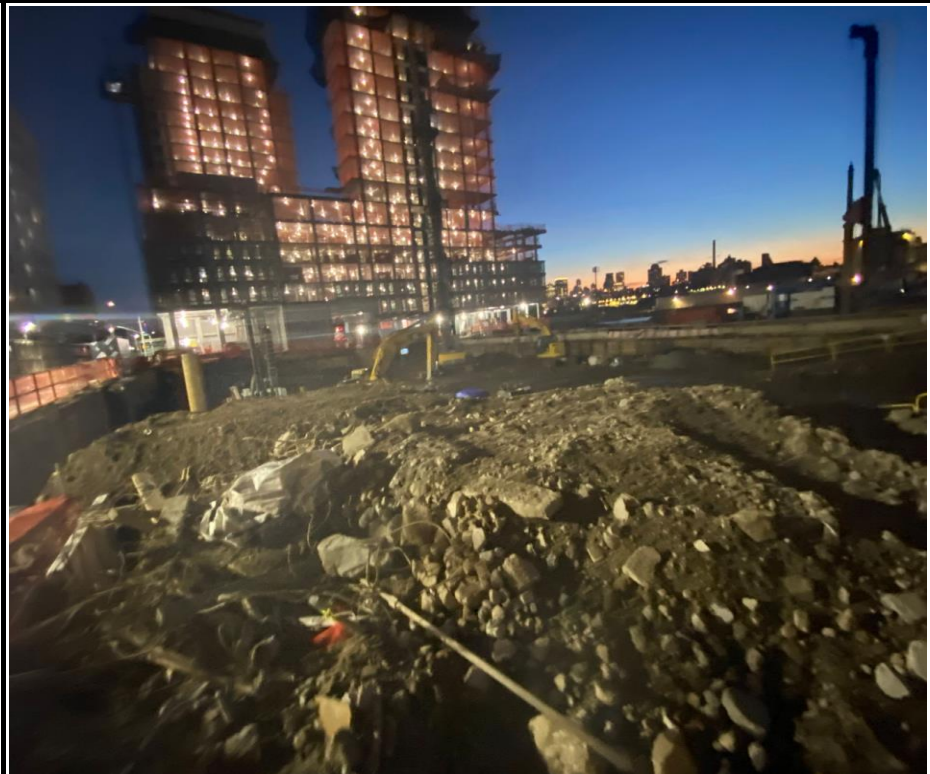

CAMP:
Downwind
Particulates

Dust Levels


0.013 mg/m³ 0.012 mg/m³ 0.15

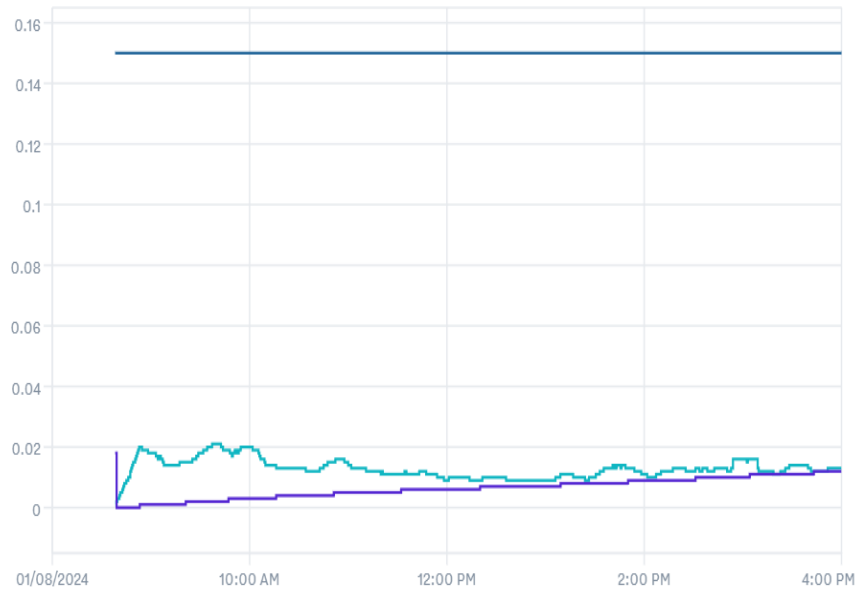


CAMP:
Downwind VOCs

VOC Levels

0 ppm 0 ppm 5

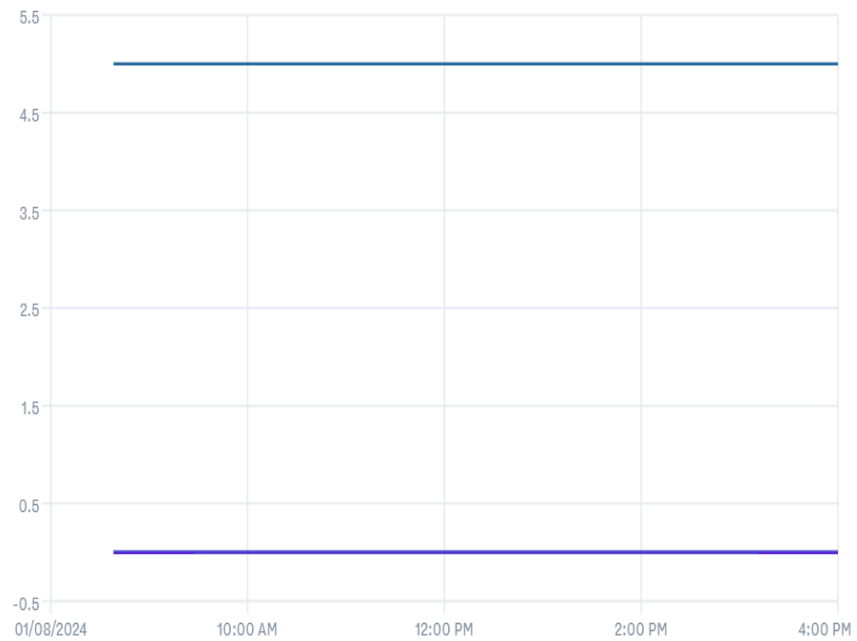

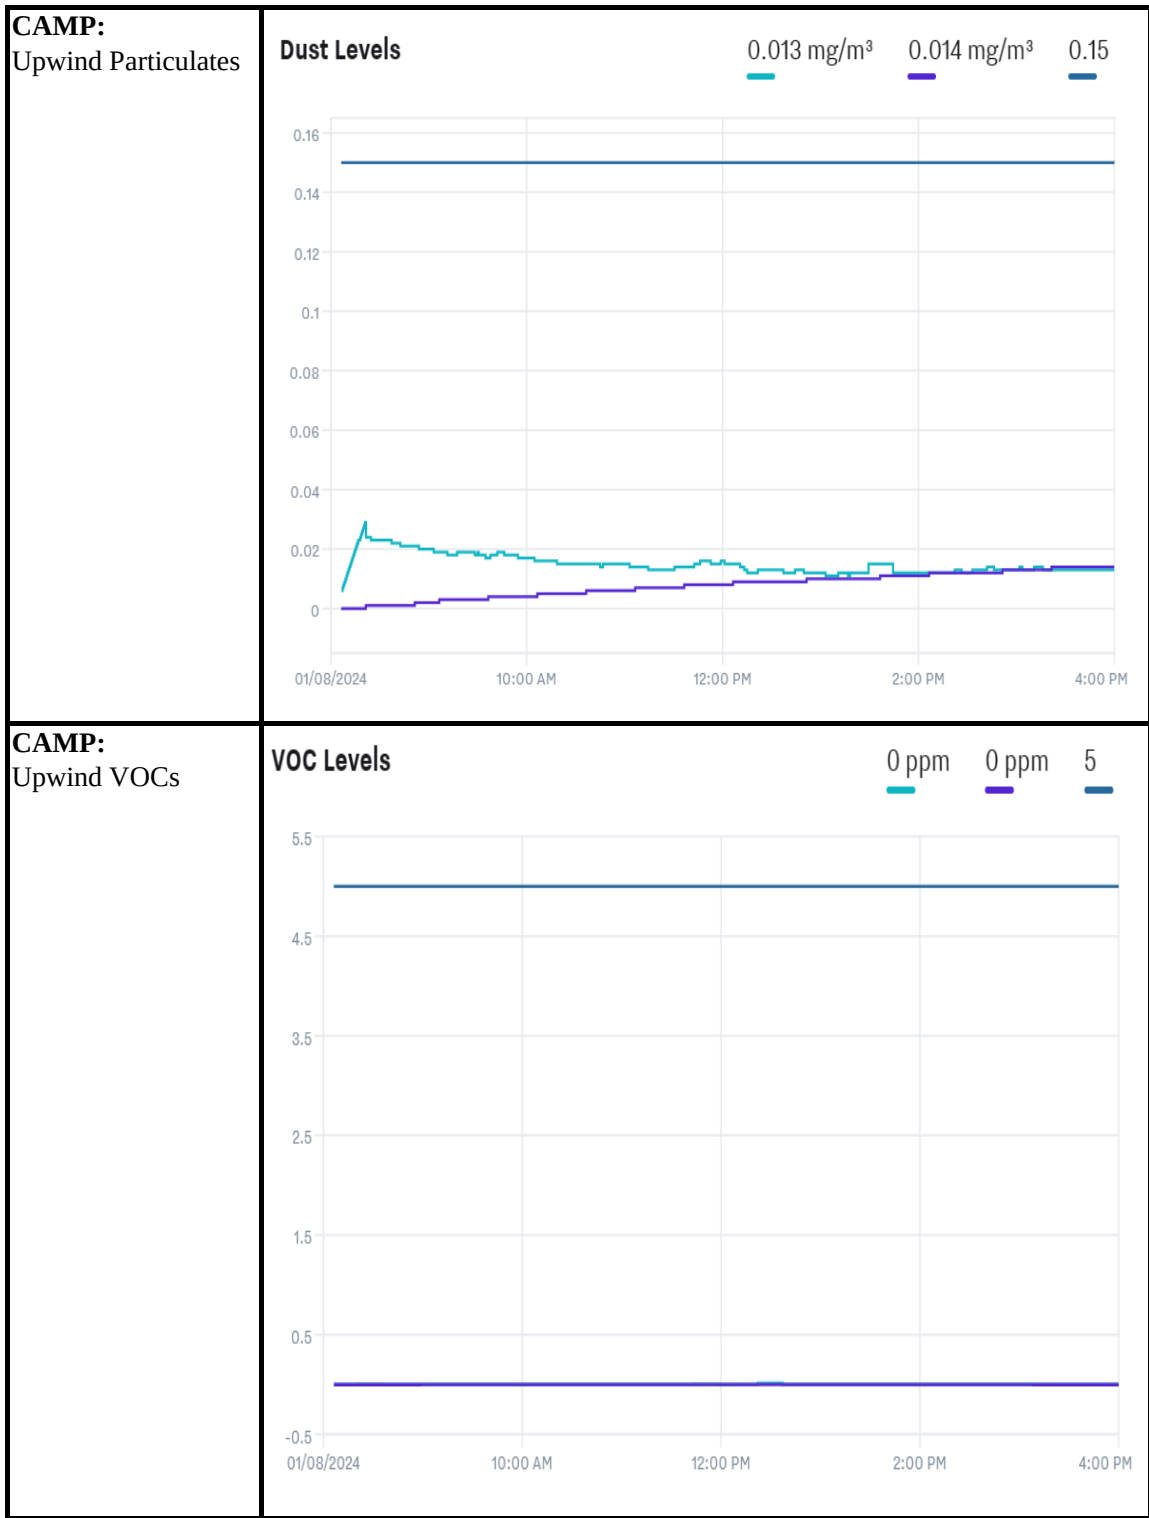

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/8/2024 8:00	1/8/2024 8:10	0.150	0	5	0
DW 47907	1/8/2024 8:10	1/8/2024 8:20	0.150	0	5	0
DW 47907	1/8/2024 8:20	1/8/2024 8:30	0.150	0	5	0
DW 47907	1/8/2024 8:30	1/8/2024 8:40	0.150	0.018	5	0
DW 47907	1/8/2024 8:40	1/8/2024 8:50	0.150	0	5	0
DW 47907	1/8/2024 8:50	1/8/2024 9:00	0.150	0.001	5	0
DW 47907	1/8/2024 9:00	1/8/2024 9:10	0.150	0.001	5	0
DW 47907	1/8/2024 9:10	1/8/2024 9:20	0.150	0.001	5	0
DW 47907	1/8/2024 9:20	1/8/2024 9:30	0.150	0.002	5	0
DW 47907	1/8/2024 9:30	1/8/2024 9:40	0.150	0.002	5	0
DW 47907	1/8/2024 9:40	1/8/2024 9:50	0.150	0.003	5	0
DW 47907	1/8/2024 9:50	1/8/2024 10:00	0.150	0.003	5	0
DW 47907	1/8/2024 10:00	1/8/2024 10:10	0.150	0.003	5	0
DW 47907	1/8/2024 10:10	1/8/2024 10:20	0.150	0.004	5	0
DW 47907	1/8/2024 10:20	1/8/2024 10:30	0.150	0.004	5	0
DW 47907	1/8/2024 10:30	1/8/2024 10:40	0.150	0.004	5	0
DW 47907	1/8/2024 10:40	1/8/2024 10:50	0.150	0.004	5	0
DW 47907	1/8/2024 10:50	1/8/2024 11:00	0.150	0.005	5	0
DW 47907	1/8/2024 11:00	1/8/2024 11:10	0.150	0.005	5	0
DW 47907	1/8/2024 11:10	1/8/2024 11:20	0.150	0.005	5	0
DW 47907	1/8/2024 11:20	1/8/2024 11:30	0.150	0.005	5	0
DW 47907	1/8/2024 11:30	1/8/2024 11:40	0.150	0.006	5	0
DW 47907	1/8/2024 11:40	1/8/2024 11:50	0.150	0.006	5	0
DW 47907	1/8/2024 11:50	1/8/2024 12:00	0.150	0.006	5	0
DW 47907	1/8/2024 12:00	1/8/2024 12:10	0.150	0.006	5	0
DW 47907	1/8/2024 12:10	1/8/2024 12:20	0.150	0.006	5	0
DW 47907	1/8/2024 12:20	1/8/2024 12:30	0.150	0.007	5	0
DW 47907	1/8/2024 12:30	1/8/2024 12:40	0.150	0.007	5	0
DW 47907	1/8/2024 12:40	1/8/2024 12:50	0.150	0.007	5	0
DW 47907	1/8/2024 12:50	1/8/2024 13:00	0.150	0.007	5	0
DW 47907	1/8/2024 13:00	1/8/2024 13:10	0.150	0.008	5	0
DW 47907	1/8/2024 13:10	1/8/2024 13:20	0.150	0.008	5	0
DW 47907	1/8/2024 13:20	1/8/2024 13:30	0.150	0.008	5	0
DW 47907	1/8/2024 13:30	1/8/2024 13:40	0.150	0.008	5	0
DW 47907	1/8/2024 13:40	1/8/2024 13:50	0.150	0.008	5	0
DW 47907	1/8/2024 13:50	1/8/2024 14:00	0.150	0.009	5	0
DW 47907	1/8/2024 14:00	1/8/2024 14:10	0.150	0.009	5	0
DW 47907	1/8/2024 14:10	1/8/2024 14:20	0.150	0.009	5	0
DW 47907	1/8/2024 14:20	1/8/2024 14:30	0.150	0.009	5	0
DW 47907	1/8/2024 14:30	1/8/2024 14:40	0.150	0.01	5	0
DW 47907	1/8/2024 14:40	1/8/2024 14:50	0.150	0.01	5	0
DW 47907	1/8/2024 14:50	1/8/2024 15:00	0.150	0.01	5	0
DW 47907	1/8/2024 15:00	1/8/2024 15:10	0.150	0.011	5	0
DW 47907	1/8/2024 15:10	1/8/2024 15:20	0.150	0.011	5	0
DW 47907	1/8/2024 15:20	1/8/2024 15:30	0.150	0.011	5	0
DW 47907	1/8/2024 15:30	1/8/2024 15:40	0.150	0.011	5	0
DW 47907	1/8/2024 15:40	1/8/2024 15:50	0.150	0.012	5	0
DW 47907	1/8/2024 15:50	1/8/2024 16:00	0.150	0.012	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/8/2024 8:00	1/8/2024 8:10	0.150	0	5	0
UW 212221	1/8/2024 8:10	1/8/2024 8:20	0.150	0	5	0
UW 212221	1/8/2024 8:20	1/8/2024 8:30	0.150	0.001	5	0
UW 212221	1/8/2024 8:30	1/8/2024 8:40	0.150	0.001	5	0
UW 212221	1/8/2024 8:40	1/8/2024 8:50	0.150	0.001	5	0
UW 212221	1/8/2024 8:50	1/8/2024 9:00	0.150	0.002	5	0
UW 212221	1/8/2024 9:00	1/8/2024 9:10	0.150	0.003	5	0
UW 212221	1/8/2024 9:10	1/8/2024 9:20	0.150	0.003	5	0
UW 212221	1/8/2024 9:20	1/8/2024 9:30	0.150	0.003	5	0
UW 212221	1/8/2024 9:30	1/8/2024 9:40	0.150	0.004	5	0
UW 212221	1/8/2024 9:40	1/8/2024 9:50	0.150	0.004	5	0
UW 212221	1/8/2024 9:50	1/8/2024 10:00	0.150	0.004	5	0
UW 212221	1/8/2024 10:00	1/8/2024 10:10	0.150	0.005	5	0
UW 212221	1/8/2024 10:10	1/8/2024 10:20	0.150	0.005	5	0
UW 212221	1/8/2024 10:20	1/8/2024 10:30	0.150	0.005	5	0
UW 212221	1/8/2024 10:30	1/8/2024 10:40	0.150	0.006	5	0
UW 212221	1/8/2024 10:40	1/8/2024 10:50	0.150	0.006	5	0
UW 212221	1/8/2024 10:50	1/8/2024 11:00	0.150	0.006	5	0
UW 212221	1/8/2024 11:00	1/8/2024 11:10	0.150	0.007	5	0
UW 212221	1/8/2024 11:10	1/8/2024 11:20	0.150	0.007	5	0
UW 212221	1/8/2024 11:20	1/8/2024 11:30	0.150	0.007	5	0
UW 212221	1/8/2024 11:30	1/8/2024 11:40	0.150	0.008	5	0
UW 212221	1/8/2024 11:40	1/8/2024 11:50	0.150	0.008	5	0
UW 212221	1/8/2024 11:50	1/8/2024 12:00	0.150	0.008	5	0
UW 212221	1/8/2024 12:00	1/8/2024 12:10	0.150	0.009	5	0
UW 212221	1/8/2024 12:10	1/8/2024 12:20	0.150	0.009	5	0
UW 212221	1/8/2024 12:20	1/8/2024 12:30	0.150	0.009	5	0
UW 212221	1/8/2024 12:30	1/8/2024 12:40	0.150	0.009	5	0
UW 212221	1/8/2024 12:40	1/8/2024 12:50	0.150	0.009	5	0
UW 212221	1/8/2024 12:50	1/8/2024 13:00	0.150	0.01	5	0
UW 212221	1/8/2024 13:00	1/8/2024 13:10	0.150	0.01	5	0
UW 212221	1/8/2024 13:10	1/8/2024 13:20	0.150	0.01	5	0
UW 212221	1/8/2024 13:20	1/8/2024 13:30	0.150	0.01	5	0
UW 212221	1/8/2024 13:30	1/8/2024 13:40	0.150	0.011	5	0
UW 212221	1/8/2024 13:40	1/8/2024 13:50	0.150	0.011	5	0
UW 212221	1/8/2024 13:50	1/8/2024 14:00	0.150	0.011	5	0
UW 212221	1/8/2024 14:00	1/8/2024 14:10	0.150	0.012	5	0
UW 212221	1/8/2024 14:10	1/8/2024 14:20	0.150	0.012	5	0
UW 212221	1/8/2024 14:20	1/8/2024 14:30	0.150	0.012	5	0
UW 212221	1/8/2024 14:30	1/8/2024 14:40	0.150	0.012	5	0
UW 212221	1/8/2024 14:40	1/8/2024 14:50	0.150	0.012	5	0
UW 212221	1/8/2024 14:50	1/8/2024 15:00	0.150	0.013	5	0
UW 212221	1/8/2024 15:00	1/8/2024 15:10	0.150	0.013	5	0
UW 212221	1/8/2024 15:10	1/8/2024 15:20	0.150	0.013	5	0
UW 212221	1/8/2024 15:20	1/8/2024 15:30	0.150	0.014	5	0
UW 212221	1/8/2024 15:30	1/8/2024 15:40	0.150	0.014	5	0
UW 212221	1/8/2024 15:40	1/8/2024 15:50	0.150	0.014	5	0
UW 212221	1/8/2024 15:50	1/8/2024 16:00	0.150	0.014	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/8/2024 8:00	1/8/2024 8:10	0.150	0	5	0
PER1 50057	1/8/2024 8:10	1/8/2024 8:20	0.150	0	5	0
PER1 50057	1/8/2024 8:20	1/8/2024 8:30	0.150	0	5	0
PER1 50057	1/8/2024 8:30	1/8/2024 8:40	0.150	0	5	0
PER1 50057	1/8/2024 8:40	1/8/2024 8:50	0.150	0.001	5	0
PER1 50057	1/8/2024 8:50	1/8/2024 9:00	0.150	0.002	5	0
PER1 50057	1/8/2024 9:00	1/8/2024 9:10	0.150	0.003	5	0
PER1 50057	1/8/2024 9:10	1/8/2024 9:20	0.150	0.003	5	0
PER1 50057	1/8/2024 9:20	1/8/2024 9:30	0.150	0.004	5	0
PER1 50057	1/8/2024 9:30	1/8/2024 9:40	0.150	0.005	5	0
PER1 50057	1/8/2024 9:40	1/8/2024 9:50	0.150	0.005	5	0
PER1 50057	1/8/2024 9:50	1/8/2024 10:00	0.150	0.006	5	0
PER1 50057	1/8/2024 10:00	1/8/2024 10:10	0.150	0.006	5	0
PER1 50057	1/8/2024 10:10	1/8/2024 10:20	0.150	0.007	5	0
PER1 50057	1/8/2024 10:20	1/8/2024 10:30	0.150	0.007	5	0
PER1 50057	1/8/2024 10:30	1/8/2024 10:40	0.150	0.007	5	0
PER1 50057	1/8/2024 10:40	1/8/2024 10:50	0.150	0.008	5	0
PER1 50057	1/8/2024 10:50	1/8/2024 11:00	0.150	0.008	5	0
PER1 50057	1/8/2024 11:00	1/8/2024 11:10	0.150	0.008	5	0
PER1 50057	1/8/2024 11:10	1/8/2024 11:20	0.150	0.009	5	0
PER1 50057	1/8/2024 11:20	1/8/2024 11:30	0.150	0.009	5	0
PER1 50057	1/8/2024 11:30	1/8/2024 11:40	0.150	0.009	5	0
PER1 50057	1/8/2024 11:40	1/8/2024 11:50	0.150	0.01	5	0
PER1 50057	1/8/2024 11:50	1/8/2024 12:00	0.150	0.01	5	0
PER1 50057	1/8/2024 12:00	1/8/2024 12:10	0.150	0.01	5	0
PER1 50057	1/8/2024 12:10	1/8/2024 12:20	0.150	0.011	5	0
PER1 50057	1/8/2024 12:20	1/8/2024 12:30	0.150	0.011	5	0
PER1 50057	1/8/2024 12:30	1/8/2024 12:40	0.150	0.011	5	0
PER1 50057	1/8/2024 12:40	1/8/2024 12:50	0.150	0.012	5	0
PER1 50057	1/8/2024 12:50	1/8/2024 13:00	0.150	0.012	5	0
PER1 50057	1/8/2024 13:00	1/8/2024 13:10	0.150	0.012	5	0
PER1 50057	1/8/2024 13:10	1/8/2024 13:20	0.150	0.012	5	0
PER1 50057	1/8/2024 13:20	1/8/2024 13:30	0.150	0.013	5	0
PER1 50057	1/8/2024 13:30	1/8/2024 13:40	0.150	0.013	5	0
PER1 50057	1/8/2024 13:40	1/8/2024 13:50	0.150	0.013	5	0
PER1 50057	1/8/2024 13:50	1/8/2024 14:00	0.150	0.014	5	0
PER1 50057	1/8/2024 14:00	1/8/2024 14:10	0.150	0.014	5	0
PER1 50057	1/8/2024 14:10	1/8/2024 14:20	0.150	0.014	5	0
PER1 50057	1/8/2024 14:20	1/8/2024 14:30	0.150	0.014	5	0
PER1 50057	1/8/2024 14:30	1/8/2024 14:40	0.150	0.015	5	0
PER1 50057	1/8/2024 14:40	1/8/2024 14:50	0.150	0.015	5	0
PER1 50057	1/8/2024 14:50	1/8/2024 15:00	0.150	0.015	5	0
PER1 50057	1/8/2024 15:00	1/8/2024 15:10	0.150	0.015	5	0
PER1 50057	1/8/2024 15:10	1/8/2024 15:20	0.150	0.015	5	0
PER1 50057	1/8/2024 15:20	1/8/2024 15:30	0.150	0.016	5	0
PER1 50057	1/8/2024 15:30	1/8/2024 15:40	0.150	0.016	5	0
PER1 50057	1/8/2024 15:40	1/8/2024 15:50	0.150	0.016	5	0
PER1 50057	1/8/2024 15:50	1/8/2024 16:00	0.150	0.016	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/8/2024 8:00	1/8/2024 8:10	0.150	0.017	5	0
PER2 46495	1/8/2024 8:10	1/8/2024 8:20	0.150	0.017	5	0
PER2 46495	1/8/2024 8:20	1/8/2024 8:30	0.150	0.017	5	0
PER2 46495	1/8/2024 8:30	1/8/2024 8:40	0.150	0.017	5	0
PER2 46495	1/8/2024 8:40	1/8/2024 8:50	0.150	0	5	0
PER2 46495	1/8/2024 8:50	1/8/2024 9:00	0.150	0.001	5	0
PER2 46495	1/8/2024 9:00	1/8/2024 9:10	0.150	0.001	5	0
PER2 46495	1/8/2024 9:10	1/8/2024 9:20	0.150	0.002	5	0
PER2 46495	1/8/2024 9:20	1/8/2024 9:30	0.150	0.002	5	0
PER2 46495	1/8/2024 9:30	1/8/2024 9:40	0.150	0.003	5	0
PER2 46495	1/8/2024 9:40	1/8/2024 9:50	0.150	0.003	5	0
PER2 46495	1/8/2024 9:50	1/8/2024 10:00	0.150	0.004	5	0
PER2 46495	1/8/2024 10:00	1/8/2024 10:10	0.150	0.004	5	0
PER2 46495	1/8/2024 10:10	1/8/2024 10:20	0.150	0.004	5	0
PER2 46495	1/8/2024 10:20	1/8/2024 10:30	0.150	0.005	5	0
PER2 46495	1/8/2024 10:30	1/8/2024 10:40	0.150	0.005	5	0
PER2 46495	1/8/2024 10:40	1/8/2024 10:50	0.150	0.005	5	0
PER2 46495	1/8/2024 10:50	1/8/2024 11:00	0.150	0.006	5	0
PER2 46495	1/8/2024 11:00	1/8/2024 11:10	0.150	0.006	5	0
PER2 46495	1/8/2024 11:10	1/8/2024 11:20	0.150	0.007	5	0
PER2 46495	1/8/2024 11:20	1/8/2024 11:30	0.150	0.007	5	0
PER2 46495	1/8/2024 11:30	1/8/2024 11:40	0.150	0.008	5	0
PER2 46495	1/8/2024 11:40	1/8/2024 11:50	0.150	0.008	5	0
PER2 46495	1/8/2024 11:50	1/8/2024 12:00	0.150	0.008	5	0
PER2 46495	1/8/2024 12:00	1/8/2024 12:10	0.150	0.008	5	0
PER2 46495	1/8/2024 12:10	1/8/2024 12:20	0.150	0.009	5	0
PER2 46495	1/8/2024 12:20	1/8/2024 12:30	0.150	0.009	5	0
PER2 46495	1/8/2024 12:30	1/8/2024 12:40	0.150	0.009	5	0
PER2 46495	1/8/2024 12:40	1/8/2024 12:50	0.150	0.009	5	0
PER2 46495	1/8/2024 12:50	1/8/2024 13:00	0.150	0.01	5	0
PER2 46495	1/8/2024 13:00	1/8/2024 13:10	0.150	0.01	5	0
PER2 46495	1/8/2024 13:10	1/8/2024 13:20	0.150	0.01	5	0
PER2 46495	1/8/2024 13:20	1/8/2024 13:30	0.150	0.011	5	0
PER2 46495	1/8/2024 13:30	1/8/2024 13:40	0.150	0.011	5	0
PER2 46495	1/8/2024 13:40	1/8/2024 13:50	0.150	0.011	5	0
PER2 46495	1/8/2024 13:50	1/8/2024 14:00	0.150	0.011	5	0
PER2 46495	1/8/2024 14:00	1/8/2024 14:10	0.150	0.012	5	0
PER2 46495	1/8/2024 14:10	1/8/2024 14:20	0.150	0.012	5	0
PER2 46495	1/8/2024 14:20	1/8/2024 14:30	0.150	0.013	5	0
PER2 46495	1/8/2024 14:30	1/8/2024 14:40	0.150	0.013	5	0
PER2 46495	1/8/2024 14:40	1/8/2024 14:50	0.150	0.013	5	0
PER2 46495	1/8/2024 14:50	1/8/2024 15:00	0.150	0.013	5	0
PER2 46495	1/8/2024 15:00	1/8/2024 15:10	0.150	0.014	5	0
PER2 46495	1/8/2024 15:10	1/8/2024 15:20	0.150	0.014	5	0
PER2 46495	1/8/2024 15:20	1/8/2024 15:30	0.150	0.014	5	0
PER2 46495	1/8/2024 15:30	1/8/2024 15:40	0.150	0.014	5	0
PER2 46495	1/8/2024 15:40	1/8/2024 15:50	0.150	0.015	5	0
PER2 46495	1/8/2024 15:50	1/8/2024 16:00	0.150	0.015	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/9/2024

Weather: 50 deg. F, Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) ECD continuing grading in the marine area.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to heavy rain.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

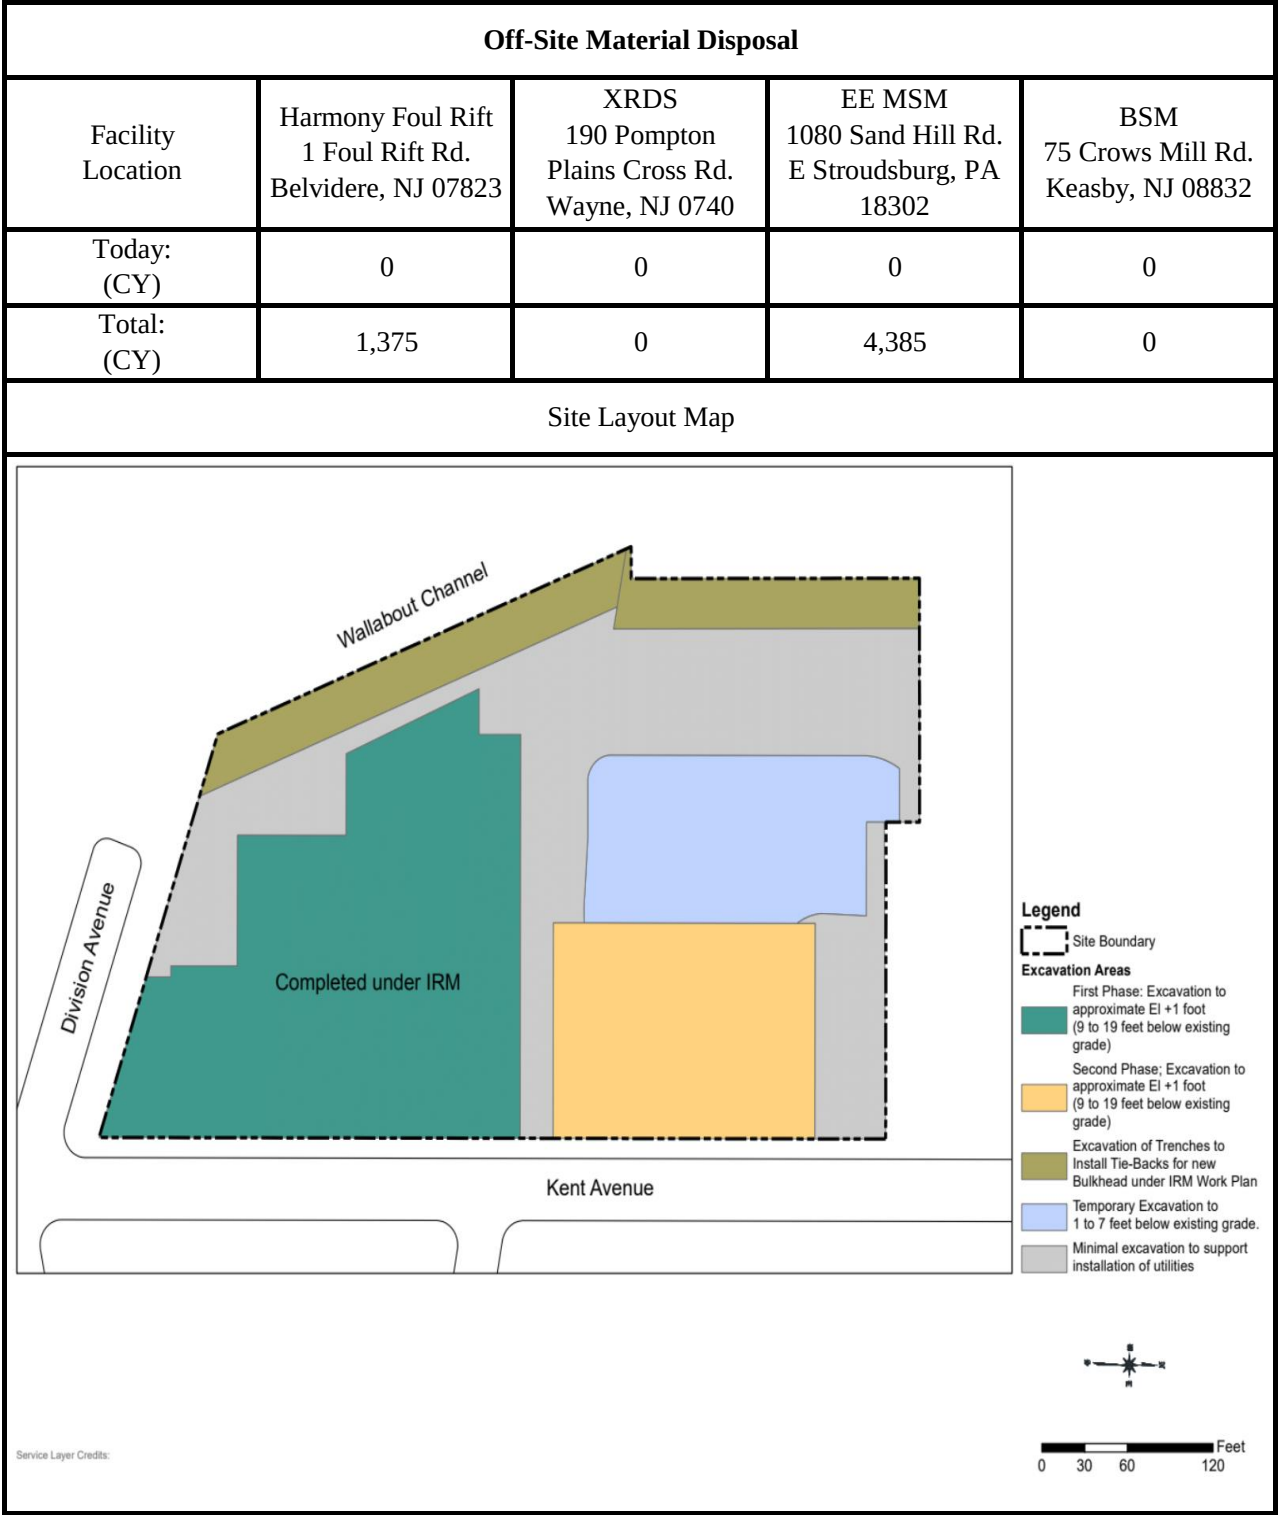


Photo 1:

View of Site conditions facing southeast.



Photo 2:

View of excavation and drilling for pile installation and SOE installation facing southwest.



Photo 3:

View of material grading in the marine area.



Photo 4:

View of site conditions facing south.



CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/10/2024

Weather: 40 deg. F, Rain/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) ECD continuing grading in the marine area.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.
CAMP stations were turned on at approximately 11AM due to rain in the morning.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

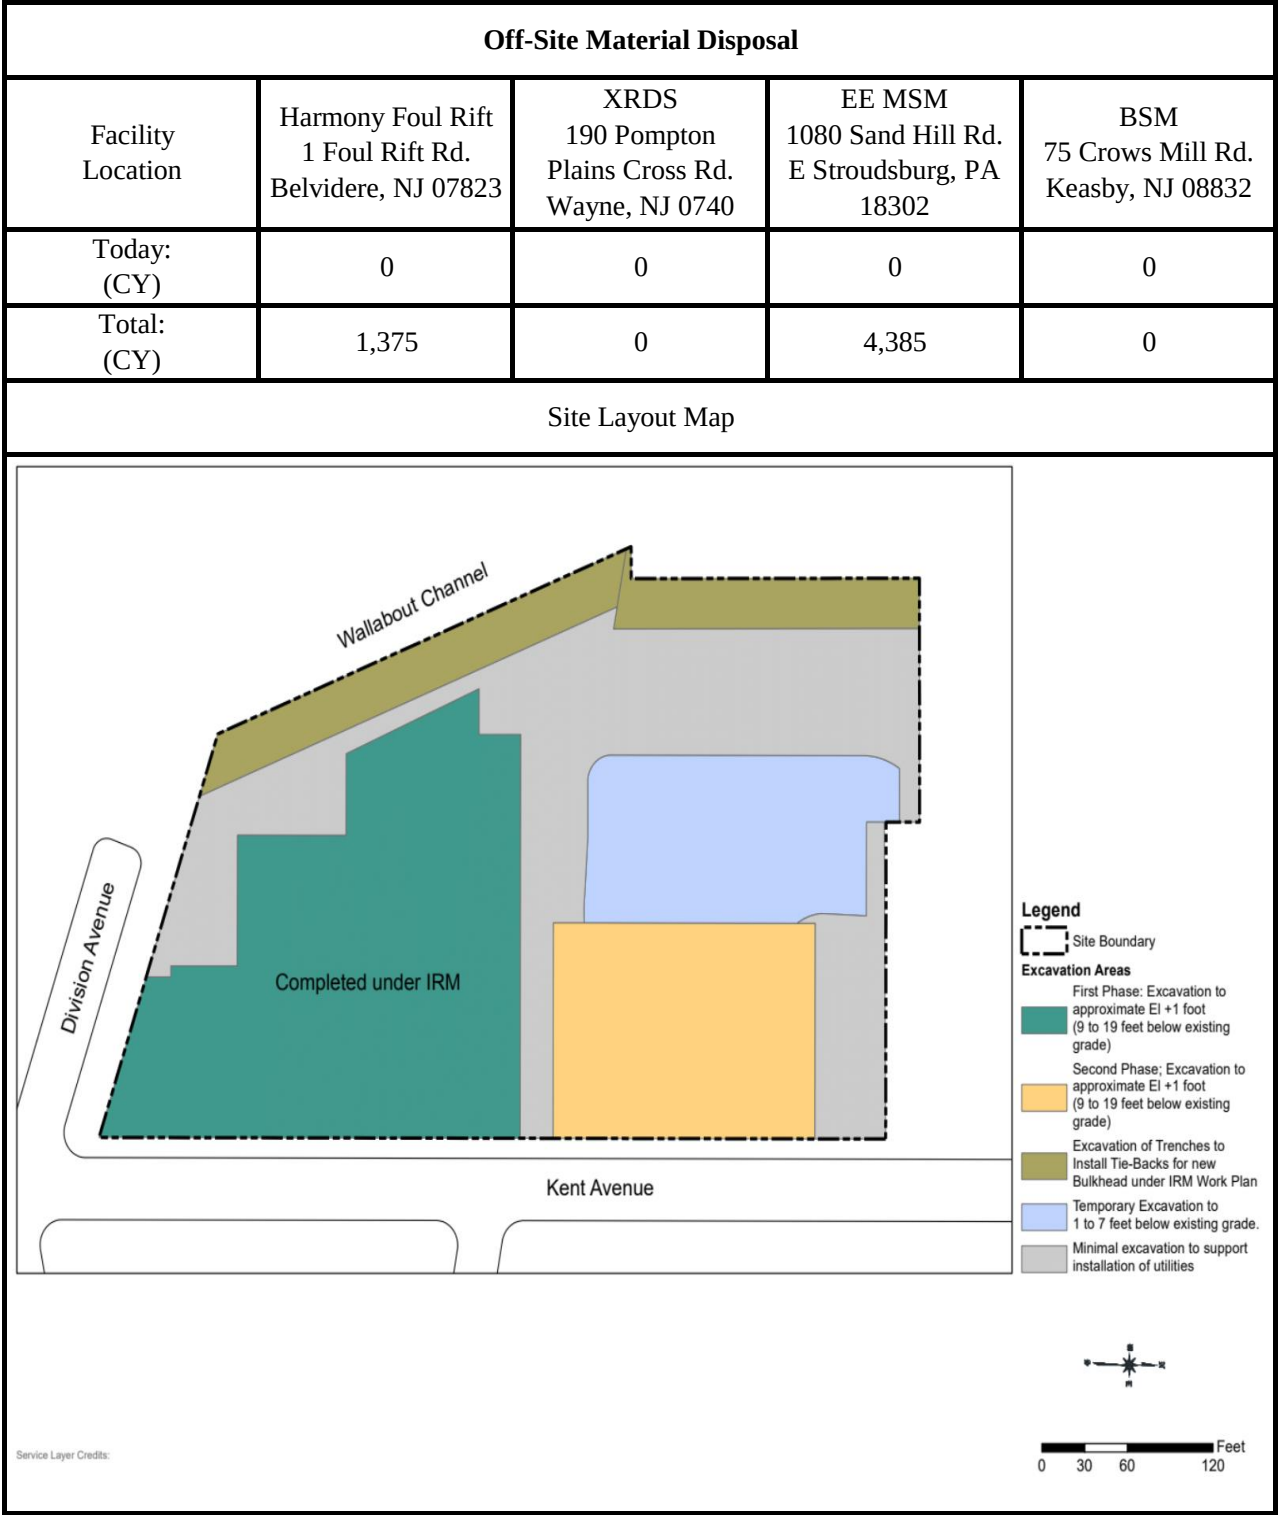


Photo 1:

View of soil excavation and stockpiling facing north.



Photo 2:

View of excavation and drilling for pile installation and SOE installation facing southwest.

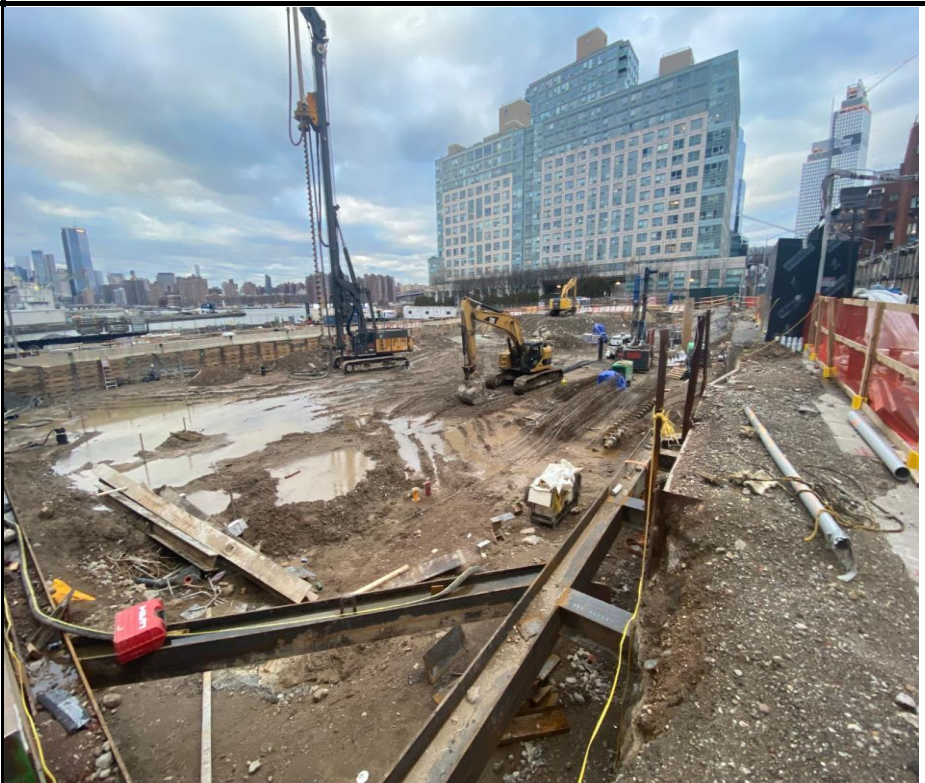


Photo 3:

View of material stockpiling in preparation for off-site disposal.



Photo 4:


View of site conditions facing south.



CAMP:
Downwind
Particulates

Dust Levels


0.005 mg/m³ 0.005 mg/m³ 0.15

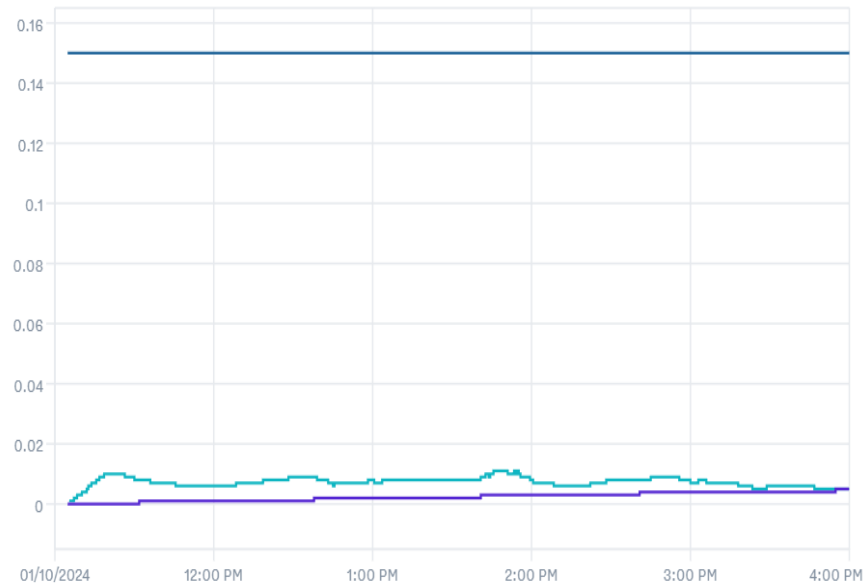

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm 5

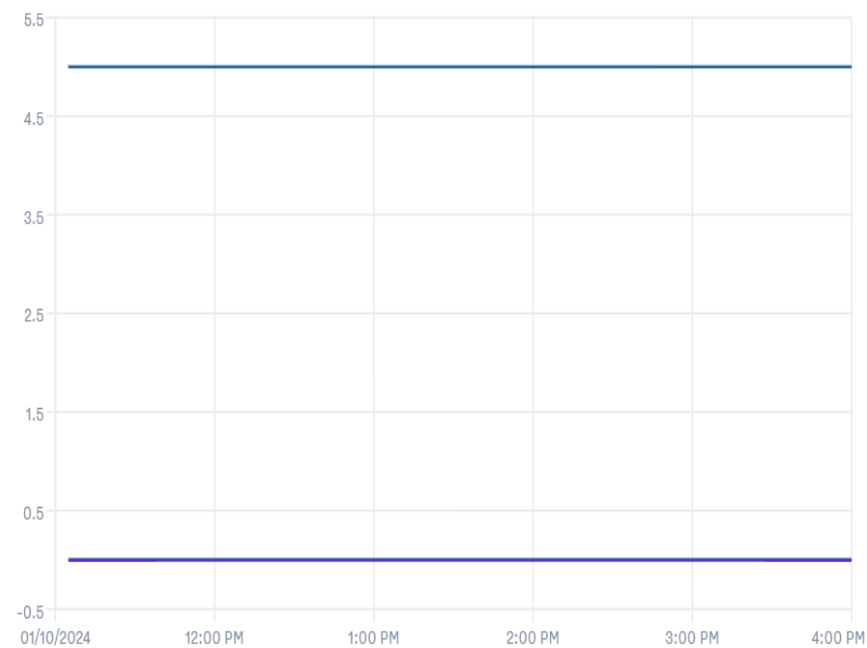

CAMP:
Upwind Particulates

Dust Levels


0.009 mg/m³ 0.007 mg/m³ 0.15

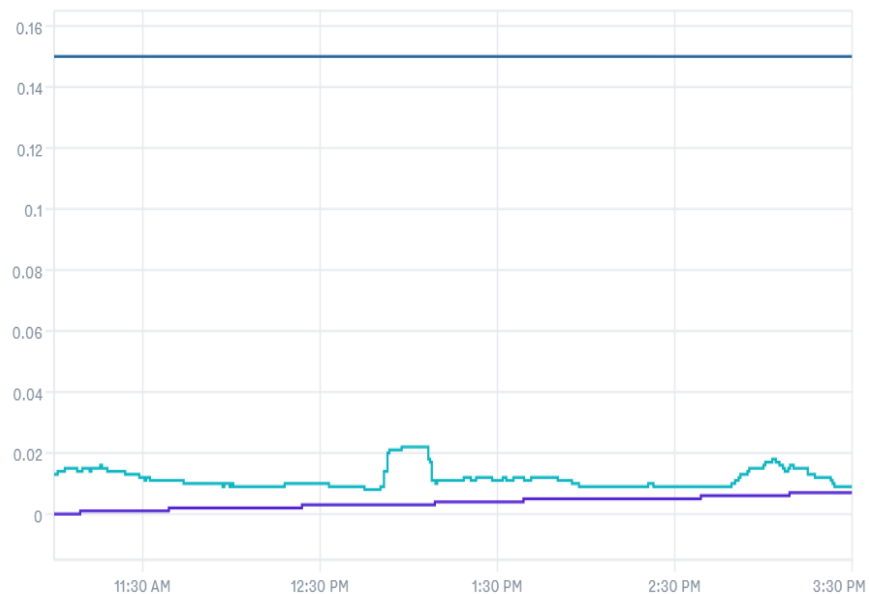

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0.001 ppm 5

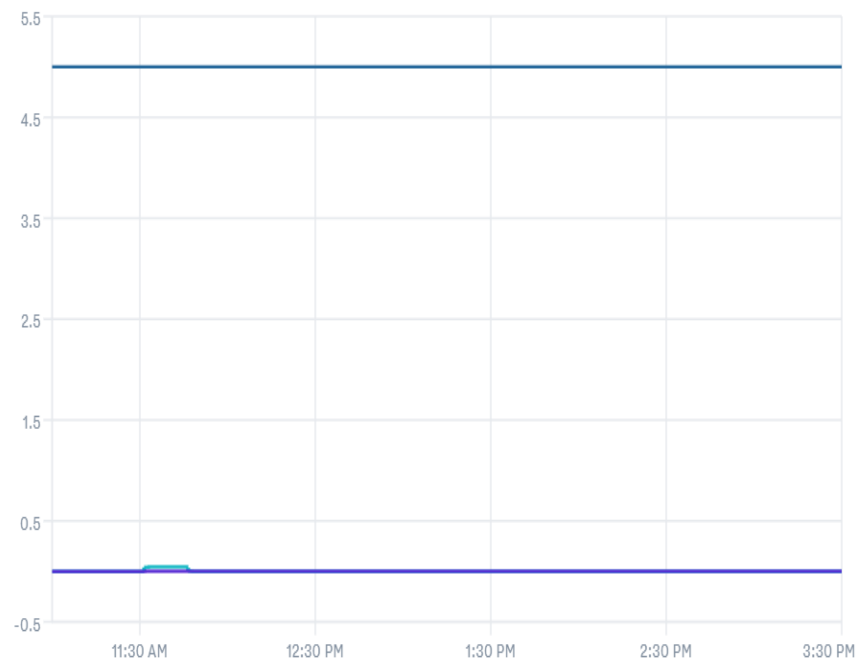

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/10/2024 11:00	1/10/2024 11:10	0.150	0	5	0
DW 47907	1/10/2024 11:10	1/10/2024 11:20	0.150	0	5	0
DW 47907	1/10/2024 11:20	1/10/2024 11:30	0.150	0	5	0
DW 47907	1/10/2024 11:30	1/10/2024 11:40	0.150	0.001	5	0
DW 47907	1/10/2024 11:40	1/10/2024 11:50	0.150	0.001	5	0
DW 47907	1/10/2024 11:50	1/10/2024 12:00	0.150	0.001	5	0
DW 47907	1/10/2024 12:00	1/10/2024 12:10	0.150	0.001	5	0
DW 47907	1/10/2024 12:10	1/10/2024 12:20	0.150	0.001	5	0
DW 47907	1/10/2024 12:20	1/10/2024 12:30	0.150	0.001	5	0
DW 47907	1/10/2024 12:30	1/10/2024 12:40	0.150	0.002	5	0
DW 47907	1/10/2024 12:40	1/10/2024 12:50	0.150	0.002	5	0
DW 47907	1/10/2024 12:50	1/10/2024 13:00	0.150	0.002	5	0
DW 47907	1/10/2024 13:00	1/10/2024 13:10	0.150	0.002	5	0
DW 47907	1/10/2024 13:10	1/10/2024 13:20	0.150	0.002	5	0
DW 47907	1/10/2024 13:20	1/10/2024 13:30	0.150	0.002	5	0
DW 47907	1/10/2024 13:30	1/10/2024 13:40	0.150	0.002	5	0
DW 47907	1/10/2024 13:40	1/10/2024 13:50	0.150	0.003	5	0
DW 47907	1/10/2024 13:50	1/10/2024 14:00	0.150	0.003	5	0
DW 47907	1/10/2024 14:00	1/10/2024 14:10	0.150	0.003	5	0
DW 47907	1/10/2024 14:10	1/10/2024 14:20	0.150	0.003	5	0
DW 47907	1/10/2024 14:20	1/10/2024 14:30	0.150	0.003	5	0
DW 47907	1/10/2024 14:30	1/10/2024 14:40	0.150	0.003	5	0
DW 47907	1/10/2024 14:40	1/10/2024 14:50	0.150	0.004	5	0
DW 47907	1/10/2024 14:50	1/10/2024 15:00	0.150	0.004	5	0
DW 47907	1/10/2024 15:00	1/10/2024 15:10	0.150	0.004	5	0
DW 47907	1/10/2024 15:10	1/10/2024 15:20	0.150	0.004	5	0
DW 47907	1/10/2024 15:20	1/10/2024 15:30	0.150	0.004	5	0
DW 47907	1/10/2024 15:30	1/10/2024 15:40	0.150	0.004	5	0
DW 47907	1/10/2024 15:40	1/10/2024 15:50	0.150	0.004	5	0
DW 47907	1/10/2024 15:50	1/10/2024 16:00	0.150	0.005	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/10/2024 11:00	1/10/2024 11:10	0.150	0.001	5	0
UW 212221	1/10/2024 11:10	1/10/2024 11:20	0.150	0.001	5	0
UW 212221	1/10/2024 11:20	1/10/2024 11:30	0.150	0.001	5	0
UW 212221	1/10/2024 11:30	1/10/2024 11:40	0.150	0.002	5	0
UW 212221	1/10/2024 11:40	1/10/2024 11:50	0.150	0.002	5	0
UW 212221	1/10/2024 11:50	1/10/2024 12:00	0.150	0.002	5	0
UW 212221	1/10/2024 12:00	1/10/2024 12:10	0.150	0.002	5	0
UW 212221	1/10/2024 12:10	1/10/2024 12:20	0.150	0.002	5	0
UW 212221	1/10/2024 12:20	1/10/2024 12:30	0.150	0.003	5	0
UW 212221	1/10/2024 12:30	1/10/2024 12:40	0.150	0.003	5	0
UW 212221	1/10/2024 12:40	1/10/2024 12:50	0.150	0.003	5	0
UW 212221	1/10/2024 12:50	1/10/2024 13:00	0.150	0.003	5	0
UW 212221	1/10/2024 13:00	1/10/2024 13:10	0.150	0.004	5	0
UW 212221	1/10/2024 13:10	1/10/2024 13:20	0.150	0.004	5	0
UW 212221	1/10/2024 13:20	1/10/2024 13:30	0.150	0.004	5	0
UW 212221	1/10/2024 13:30	1/10/2024 13:40	0.150	0.005	5	0
UW 212221	1/10/2024 13:40	1/10/2024 13:50	0.150	0.005	5	0
UW 212221	1/10/2024 13:50	1/10/2024 14:00	0.150	0.005	5	0
UW 212221	1/10/2024 14:00	1/10/2024 14:10	0.150	0.005	5	0
UW 212221	1/10/2024 14:10	1/10/2024 14:20	0.150	0.005	5	0
UW 212221	1/10/2024 14:20	1/10/2024 14:30	0.150	0.005	5	0
UW 212221	1/10/2024 14:30	1/10/2024 14:40	0.150	0.006	5	0
UW 212221	1/10/2024 14:40	1/10/2024 14:50	0.150	0.006	5	0
UW 212221	1/10/2024 14:50	1/10/2024 15:00	0.150	0.006	5	0
UW 212221	1/10/2024 15:00	1/10/2024 15:10	0.150	0.007	5	0
UW 212221	1/10/2024 15:10	1/10/2024 15:20	0.150	0.007	5	0
UW 212221	1/10/2024 15:20	1/10/2024 15:30	0.150	0.007	5	0
UW 212221	1/10/2024 15:30	1/10/2024 15:40	0.150	0.007	5	0
UW 212221	1/10/2024 15:40	1/10/2024 15:50	0.150	0.007	5	0
UW 212221	1/10/2024 15:50	1/10/2024 16:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/10/2024 11:00	1/10/2024 11:10	0.150	0	5	0
PER1 50057	1/10/2024 11:10	1/10/2024 11:20	0.150	0	5	0
PER1 50057	1/10/2024 11:20	1/10/2024 11:30	0.150	0.001	5	0
PER1 50057	1/10/2024 11:30	1/10/2024 11:40	0.150	0.001	5	0
PER1 50057	1/10/2024 11:40	1/10/2024 11:50	0.150	0.001	5	0
PER1 50057	1/10/2024 11:50	1/10/2024 12:00	0.150	0.001	5	0
PER1 50057	1/10/2024 12:00	1/10/2024 12:10	0.150	0.002	5	0
PER1 50057	1/10/2024 12:10	1/10/2024 12:20	0.150	0.002	5	0
PER1 50057	1/10/2024 12:20	1/10/2024 12:30	0.150	0.002	5	0
PER1 50057	1/10/2024 12:30	1/10/2024 12:40	0.150	0.002	5	0
PER1 50057	1/10/2024 12:40	1/10/2024 12:50	0.150	0.003	5	0
PER1 50057	1/10/2024 12:50	1/10/2024 13:00	0.150	0.003	5	0
PER1 50057	1/10/2024 13:00	1/10/2024 13:10	0.150	0.003	5	0
PER1 50057	1/10/2024 13:10	1/10/2024 13:20	0.150	0.003	5	0
PER1 50057	1/10/2024 13:20	1/10/2024 13:30	0.150	0.003	5	0
PER1 50057	1/10/2024 13:30	1/10/2024 13:40	0.150	0.004	5	0
PER1 50057	1/10/2024 13:40	1/10/2024 13:50	0.150	0.004	5	0
PER1 50057	1/10/2024 13:50	1/10/2024 14:00	0.150	0.004	5	0
PER1 50057	1/10/2024 14:00	1/10/2024 14:10	0.150	0.004	5	0
PER1 50057	1/10/2024 14:10	1/10/2024 14:20	0.150	0.005	5	0
PER1 50057	1/10/2024 14:20	1/10/2024 14:30	0.150	0.005	5	0
PER1 50057	1/10/2024 14:30	1/10/2024 14:40	0.150	0.005	5	0
PER1 50057	1/10/2024 14:40	1/10/2024 14:50	0.150	0.005	5	0
PER1 50057	1/10/2024 14:50	1/10/2024 15:00	0.150	0.006	5	0
PER1 50057	1/10/2024 15:00	1/10/2024 15:10	0.150	0.006	5	0
PER1 50057	1/10/2024 15:10	1/10/2024 15:20	0.150	0.006	5	0
PER1 50057	1/10/2024 15:20	1/10/2024 15:30	0.150	0.006	5	0
PER1 50057	1/10/2024 15:30	1/10/2024 15:40	0.150	0.006	5	0
PER1 50057	1/10/2024 15:40	1/10/2024 15:50	0.150	0.006	5	0
PER1 50057	1/10/2024 15:50	1/10/2024 16:00	0.150	0.006	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/10/2024 11:00	1/10/2024 11:10	0.150	0	5	0
PER2 46495	1/10/2024 11:10	1/10/2024 11:20	0.150	0.01	5	0
PER2 46495	1/10/2024 11:20	1/10/2024 11:30	0.150	0.01	5	0
PER2 46495	1/10/2024 11:30	1/10/2024 11:40	0.150	0.011	5	0
PER2 46495	1/10/2024 11:40	1/10/2024 11:50	0.150	0.011	5	0
PER2 46495	1/10/2024 11:50	1/10/2024 12:00	0.150	0.011	5	0
PER2 46495	1/10/2024 12:00	1/10/2024 12:10	0.150	0.011	5	0
PER2 46495	1/10/2024 12:10	1/10/2024 12:20	0.150	0.012	5	0
PER2 46495	1/10/2024 12:20	1/10/2024 12:30	0.150	0.012	5	0
PER2 46495	1/10/2024 12:30	1/10/2024 12:40	0.150	0.012	5	0
PER2 46495	1/10/2024 12:40	1/10/2024 12:50	0.150	0.012	5	0
PER2 46495	1/10/2024 12:50	1/10/2024 13:00	0.150	0.013	5	0
PER2 46495	1/10/2024 13:00	1/10/2024 13:10	0.150	0.013	5	0
PER2 46495	1/10/2024 13:10	1/10/2024 13:20	0.150	0.013	5	0
PER2 46495	1/10/2024 13:20	1/10/2024 13:30	0.150	0.013	5	0
PER2 46495	1/10/2024 13:30	1/10/2024 13:40	0.150	0.014	5	0
PER2 46495	1/10/2024 13:40	1/10/2024 13:50	0.150	0.014	5	0
PER2 46495	1/10/2024 13:50	1/10/2024 14:00	0.150	0.014	5	0
PER2 46495	1/10/2024 14:00	1/10/2024 14:10	0.150	0.014	5	0
PER2 46495	1/10/2024 14:10	1/10/2024 14:20	0.150	0.015	5	0
PER2 46495	1/10/2024 14:20	1/10/2024 14:30	0.150	0.015	5	0
PER2 46495	1/10/2024 14:30	1/10/2024 14:40	0.150	0.015	5	0
PER2 46495	1/10/2024 14:40	1/10/2024 14:50	0.150	0.015	5	0
PER2 46495	1/10/2024 14:50	1/10/2024 15:00	0.150	0.015	5	0
PER2 46495	1/10/2024 15:00	1/10/2024 15:10	0.150	0.016	5	0
PER2 46495	1/10/2024 15:10	1/10/2024 15:20	0.150	0.016	5	0
PER2 46495	1/10/2024 15:20	1/10/2024 15:30	0.150	0.016	5	0
PER2 46495	1/10/2024 15:30	1/10/2024 15:40	0.150	0.016	5	0
PER2 46495	1/10/2024 15:40	1/10/2024 15:50	0.150	0.016	5	0
PER2 46495	1/10/2024 15:50	1/10/2024 16:00	0.150	0.017	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/11/2024

Weather: 40 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) ECD continuing grading in the marine area.
- 3) Export of 20 loads (approximately 400 CY) of soil from WC-23 to the Bayshore Soil Management facility.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

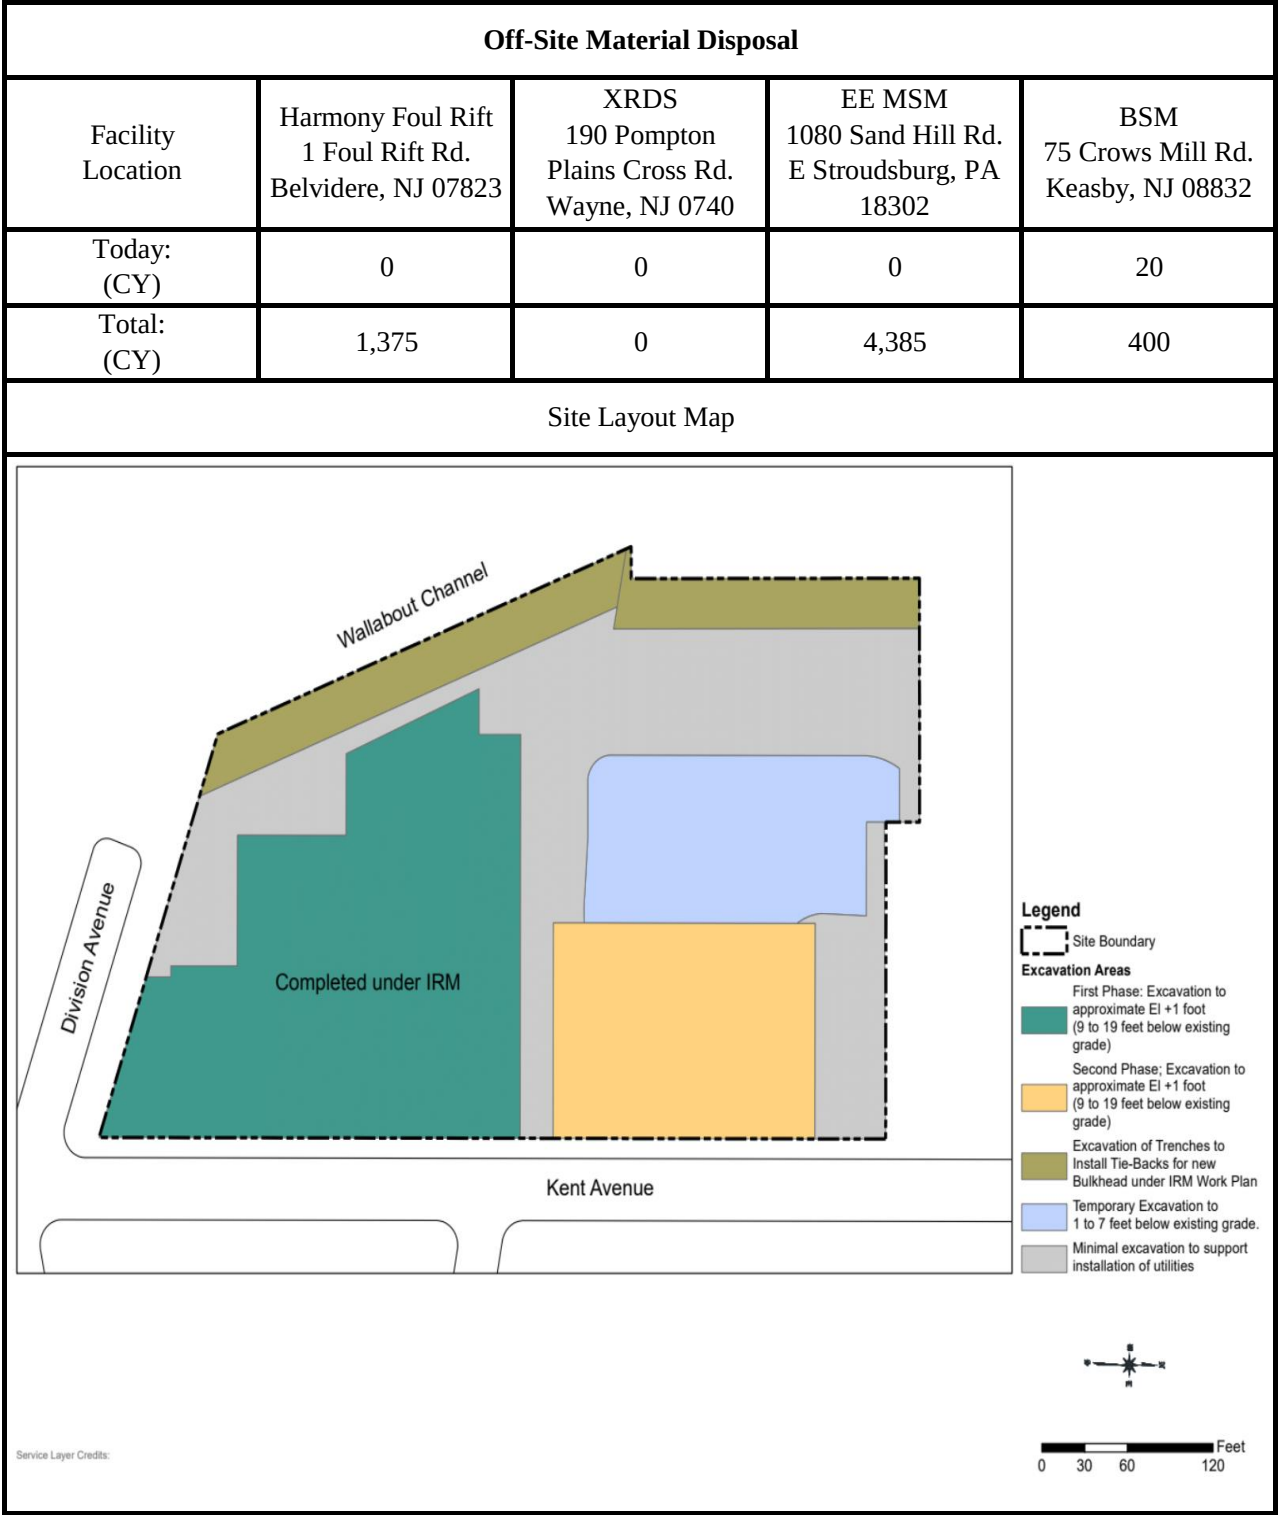


Photo 1:

View of soil excavation, pile installation and site conditions facing west.

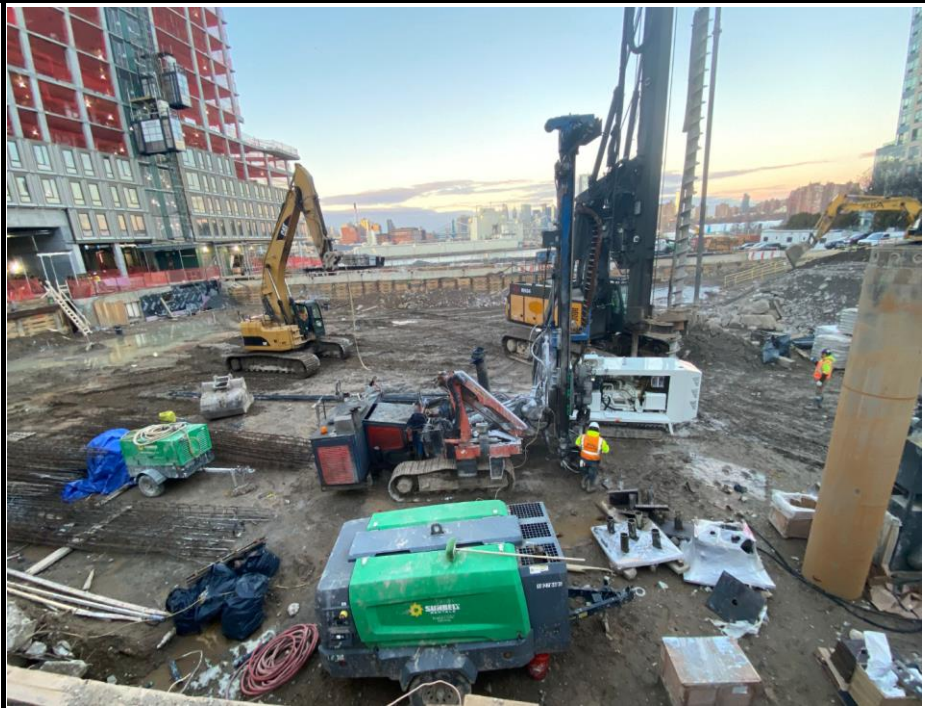


Photo 2:

View of excavation and truck loading for off-site soil disposal.




Photo 3:

View of soil excavation, pile installation and site conditions facing northwest.



Photo 4:


View of site conditions facing southwest.

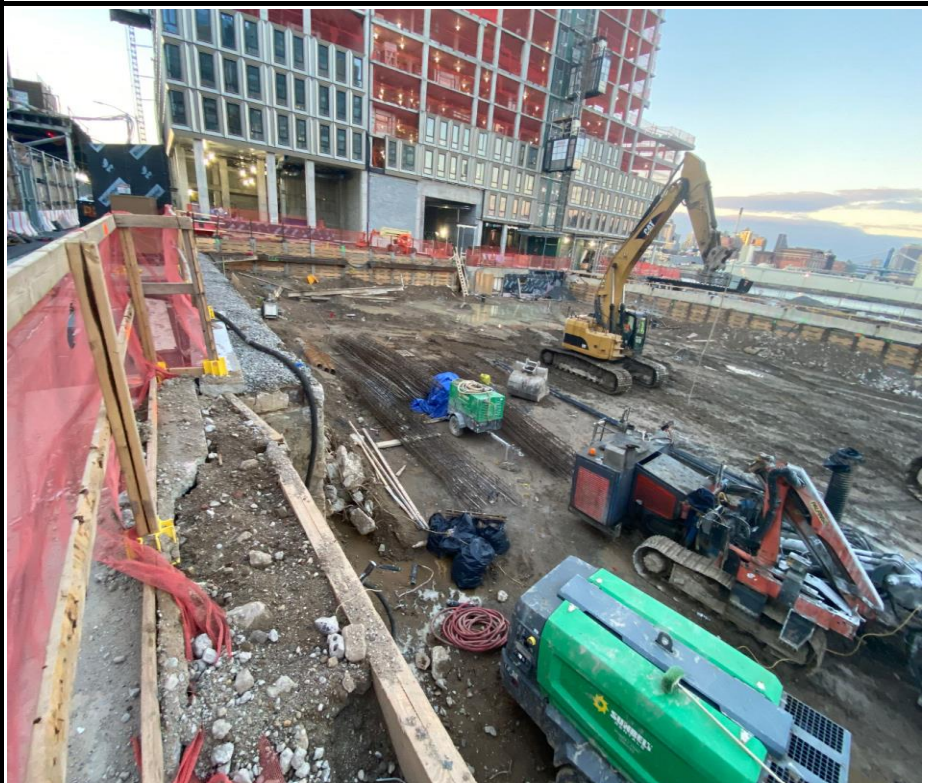

CAMP:
Downwind
Particulates

Dust Levels


0.022 mg/m³ 0.024 mg/m³ 0.15

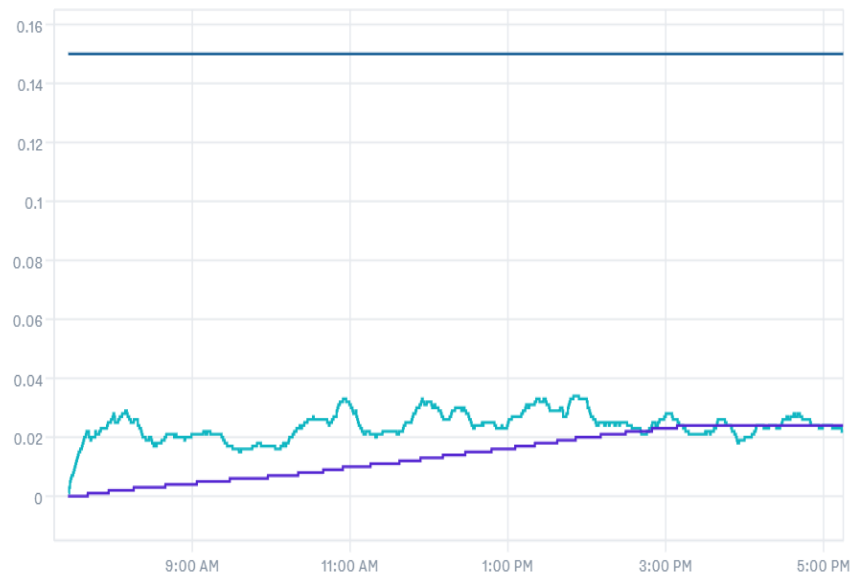


CAMP:
Downwind VOCs

VOC Levels

0 ppm 0 ppm 5

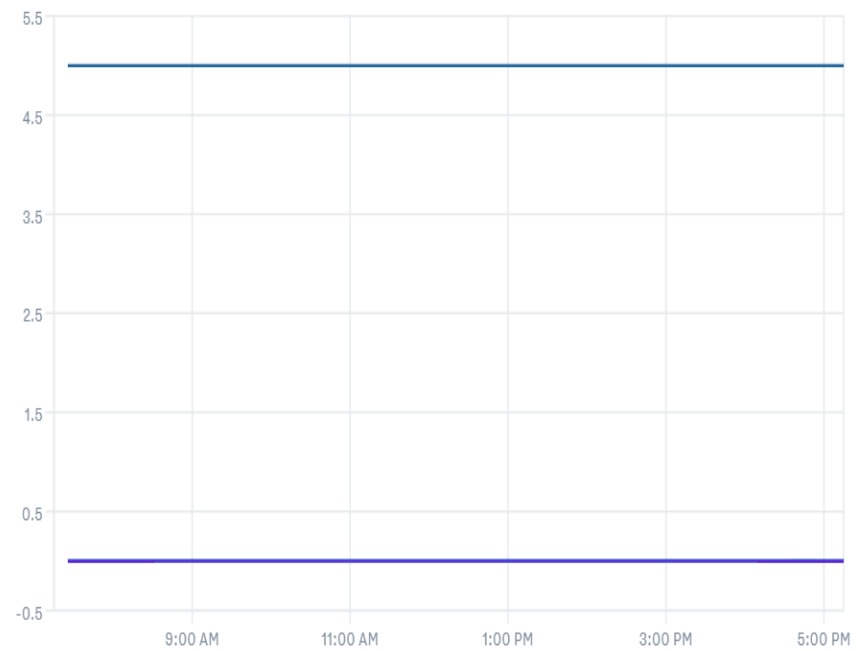

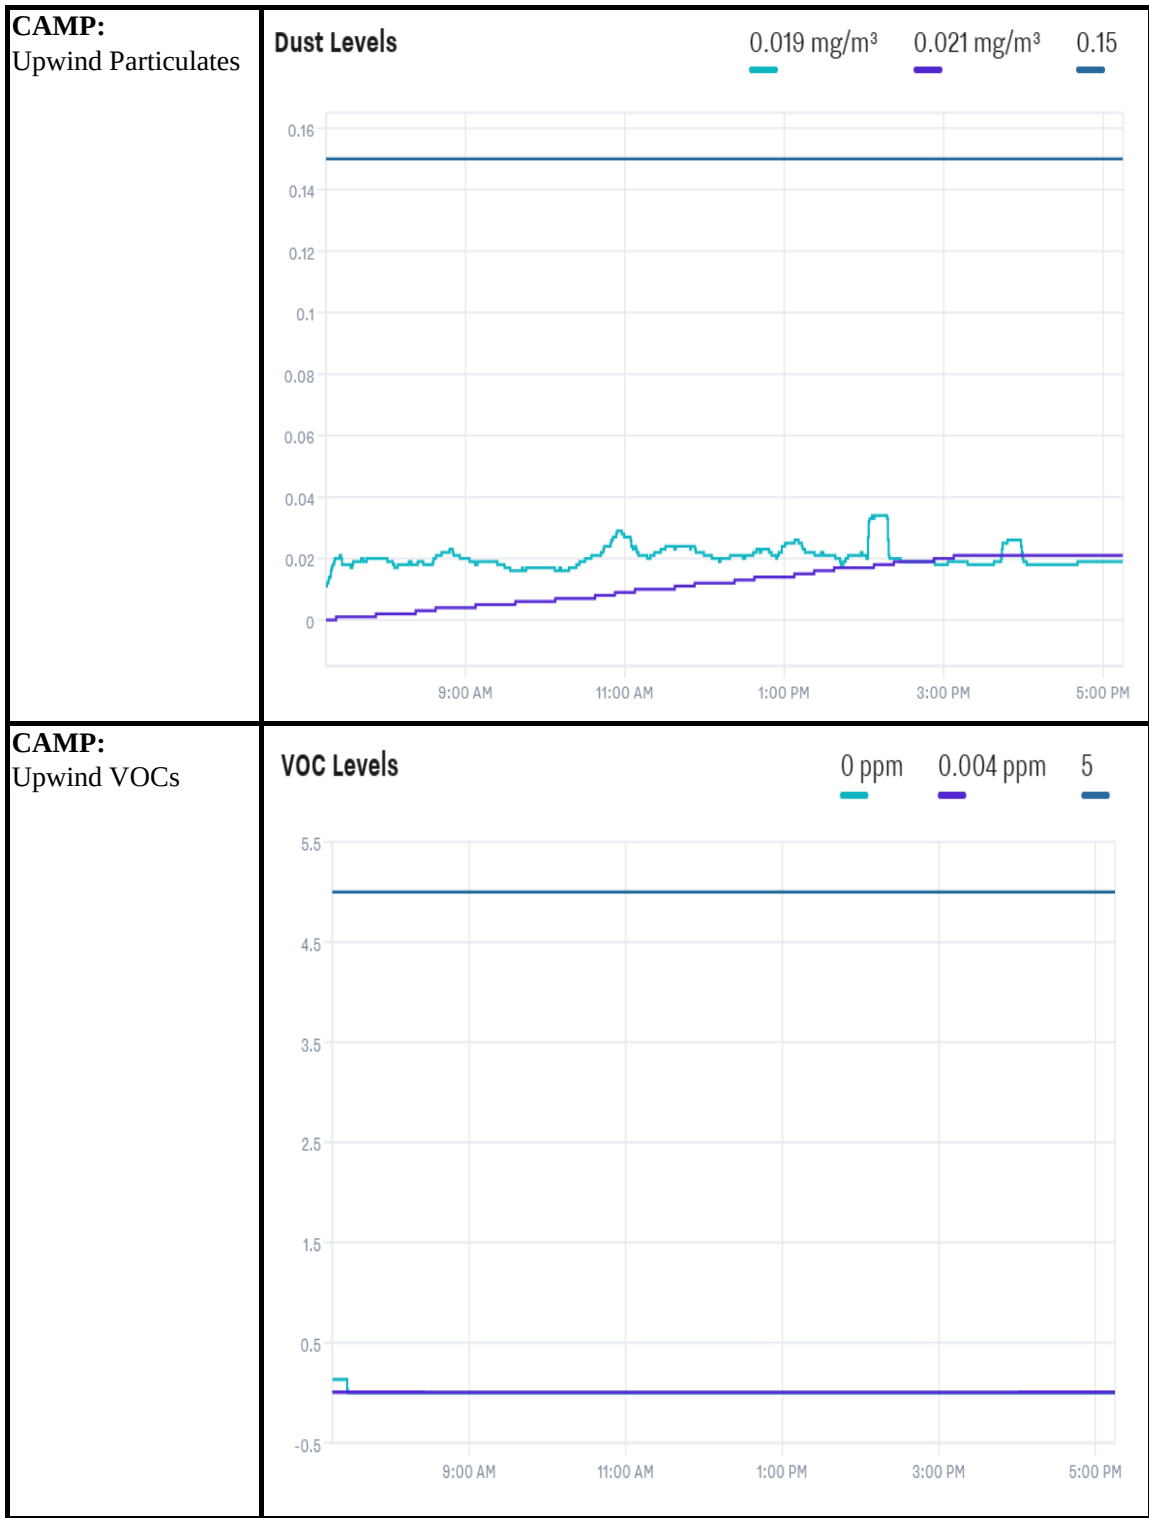

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/11/2024 7:15	1/11/2024 7:25	0.150	0.005	5	0
DW 47907	1/11/2024 7:25	1/11/2024 7:35	0.150	0	5	0
DW 47907	1/11/2024 7:35	1/11/2024 7:45	0.150	0.001	5	0
DW 47907	1/11/2024 7:45	1/11/2024 7:55	0.150	0.001	5	0
DW 47907	1/11/2024 7:55	1/11/2024 8:05	0.150	0.002	5	0
DW 47907	1/11/2024 8:05	1/11/2024 8:15	0.150	0.002	5	0
DW 47907	1/11/2024 8:15	1/11/2024 8:25	0.150	0.003	5	0
DW 47907	1/11/2024 8:25	1/11/2024 8:35	0.150	0.003	5	0
DW 47907	1/11/2024 8:35	1/11/2024 8:45	0.150	0.004	5	0
DW 47907	1/11/2024 8:45	1/11/2024 8:55	0.150	0.004	5	0
DW 47907	1/11/2024 8:55	1/11/2024 9:05	0.150	0.005	5	0
DW 47907	1/11/2024 9:05	1/11/2024 9:15	0.150	0.005	5	0
DW 47907	1/11/2024 9:15	1/11/2024 9:25	0.150	0.005	5	0
DW 47907	1/11/2024 9:25	1/11/2024 9:35	0.150	0.006	5	0
DW 47907	1/11/2024 9:35	1/11/2024 9:45	0.150	0.006	5	0
DW 47907	1/11/2024 9:45	1/11/2024 9:55	0.150	0.006	5	0
DW 47907	1/11/2024 9:55	1/11/2024 10:05	0.150	0.007	5	0
DW 47907	1/11/2024 10:05	1/11/2024 10:15	0.150	0.007	5	0
DW 47907	1/11/2024 10:15	1/11/2024 10:25	0.150	0.008	5	0
DW 47907	1/11/2024 10:25	1/11/2024 10:35	0.150	0.008	5	0
DW 47907	1/11/2024 10:35	1/11/2024 10:45	0.150	0.009	5	0
DW 47907	1/11/2024 10:45	1/11/2024 10:55	0.150	0.01	5	0
DW 47907	1/11/2024 10:55	1/11/2024 11:05	0.150	0.01	5	0
DW 47907	1/11/2024 11:05	1/11/2024 11:15	0.150	0.01	5	0
DW 47907	1/11/2024 11:15	1/11/2024 11:25	0.150	0.011	5	0
DW 47907	1/11/2024 11:25	1/11/2024 11:35	0.150	0.011	5	0
DW 47907	1/11/2024 11:35	1/11/2024 11:45	0.150	0.012	5	0
DW 47907	1/11/2024 11:45	1/11/2024 11:55	0.150	0.013	5	0
DW 47907	1/11/2024 11:55	1/11/2024 12:05	0.150	0.013	5	0
DW 47907	1/11/2024 12:05	1/11/2024 12:15	0.150	0.014	5	0
DW 47907	1/11/2024 12:15	1/11/2024 12:25	0.150	0.014	5	0
DW 47907	1/11/2024 12:25	1/11/2024 12:35	0.150	0.015	5	0
DW 47907	1/11/2024 12:35	1/11/2024 12:45	0.150	0.015	5	0
DW 47907	1/11/2024 12:45	1/11/2024 12:55	0.150	0.016	5	0
DW 47907	1/11/2024 12:55	1/11/2024 13:05	0.150	0.016	5	0
DW 47907	1/11/2024 13:05	1/11/2024 13:15	0.150	0.017	5	0
DW 47907	1/11/2024 13:15	1/11/2024 13:25	0.150	0.018	5	0
DW 47907	1/11/2024 13:25	1/11/2024 13:35	0.150	0.018	5	0
DW 47907	1/11/2024 13:35	1/11/2024 13:45	0.150	0.019	5	0
DW 47907	1/11/2024 13:45	1/11/2024 13:55	0.150	0.02	5	0
DW 47907	1/11/2024 13:55	1/11/2024 14:05	0.150	0.02	5	0
DW 47907	1/11/2024 14:05	1/11/2024 14:15	0.150	0.021	5	0
DW 47907	1/11/2024 14:15	1/11/2024 14:25	0.150	0.021	5	0
DW 47907	1/11/2024 14:25	1/11/2024 14:35	0.150	0.022	5	0
DW 47907	1/11/2024 14:35	1/11/2024 14:45	0.150	0.022	5	0
DW 47907	1/11/2024 14:45	1/11/2024 14:55	0.150	0.023	5	0
DW 47907	1/11/2024 14:55	1/11/2024 15:05	0.150	0.023	5	0
DW 47907	1/11/2024 15:05	1/11/2024 15:15	0.150	0.024	5	0
DW 47907	1/11/2024 15:15	1/11/2024 15:25	0.150	0.024	5	0
DW 47907	1/11/2024 15:25	1/11/2024 15:35	0.150	0.024	5	0
DW 47907	1/11/2024 15:35	1/11/2024 15:45	0.150	0.024	5	0
DW 47907	1/11/2024 15:45	1/11/2024 15:55	0.150	0.024	5	0
DW 47907	1/11/2024 15:55	1/11/2024 16:05	0.150	0.024	5	0
DW 47907	1/11/2024 16:05	1/11/2024 16:15	0.150	0.024	5	0
DW 47907	1/11/2024 16:15	1/11/2024 16:25	0.150	0.024	5	0
DW 47907	1/11/2024 16:25	1/11/2024 16:35	0.150	0.024	5	0
DW 47907	1/11/2024 16:35	1/11/2024 16:45	0.150	0.024	5	0
DW 47907	1/11/2024 16:45	1/11/2024 16:55	0.150	0.024	5	0
DW 47907	1/11/2024 16:55	1/11/2024 17:05	0.150	0.024	5	0
DW 47907	1/11/2024 17:05	1/11/2024 17:15	0.150	0.024	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/11/2024 7:15	1/11/2024 7:25	0.150	0.001	5	0.004
UW 212221	1/11/2024 7:25	1/11/2024 7:35	0.150	0.001	5	0.004
UW 212221	1/11/2024 7:35	1/11/2024 7:45	0.150	0.001	5	0.004
UW 212221	1/11/2024 7:45	1/11/2024 7:55	0.150	0.002	5	0.004
UW 212221	1/11/2024 7:55	1/11/2024 8:05	0.150	0.002	5	0.004
UW 212221	1/11/2024 8:05	1/11/2024 8:15	0.150	0.002	5	0.004
UW 212221	1/11/2024 8:15	1/11/2024 8:25	0.150	0.003	5	0.004
UW 212221	1/11/2024 8:25	1/11/2024 8:35	0.150	0.003	5	0.004
UW 212221	1/11/2024 8:35	1/11/2024 8:45	0.150	0.004	5	0.004
UW 212221	1/11/2024 8:45	1/11/2024 8:55	0.150	0.004	5	0.004
UW 212221	1/11/2024 8:55	1/11/2024 9:05	0.150	0.004	5	0.004
UW 212221	1/11/2024 9:05	1/11/2024 9:15	0.150	0.005	5	0.004
UW 212221	1/11/2024 9:15	1/11/2024 9:25	0.150	0.005	5	0.004
UW 212221	1/11/2024 9:25	1/11/2024 9:35	0.150	0.005	5	0.004
UW 212221	1/11/2024 9:35	1/11/2024 9:45	0.150	0.006	5	0.004
UW 212221	1/11/2024 9:45	1/11/2024 9:55	0.150	0.006	5	0.004
UW 212221	1/11/2024 9:55	1/11/2024 10:05	0.150	0.006	5	0.004
UW 212221	1/11/2024 10:05	1/11/2024 10:15	0.150	0.007	5	0.004
UW 212221	1/11/2024 10:15	1/11/2024 10:25	0.150	0.007	5	0.004
UW 212221	1/11/2024 10:25	1/11/2024 10:35	0.150	0.007	5	0.004
UW 212221	1/11/2024 10:35	1/11/2024 10:45	0.150	0.008	5	0.004
UW 212221	1/11/2024 10:45	1/11/2024 10:55	0.150	0.009	5	0.004
UW 212221	1/11/2024 10:55	1/11/2024 11:05	0.150	0.009	5	0.004
UW 212221	1/11/2024 11:05	1/11/2024 11:15	0.150	0.01	5	0.004
UW 212221	1/11/2024 11:15	1/11/2024 11:25	0.150	0.01	5	0.004
UW 212221	1/11/2024 11:25	1/11/2024 11:35	0.150	0.01	5	0.004
UW 212221	1/11/2024 11:35	1/11/2024 11:45	0.150	0.011	5	0.004
UW 212221	1/11/2024 11:45	1/11/2024 11:55	0.150	0.012	5	0.004
UW 212221	1/11/2024 11:55	1/11/2024 12:05	0.150	0.012	5	0.004
UW 212221	1/11/2024 12:05	1/11/2024 12:15	0.150	0.012	5	0.004
UW 212221	1/11/2024 12:15	1/11/2024 12:25	0.150	0.013	5	0.004
UW 212221	1/11/2024 12:25	1/11/2024 12:35	0.150	0.013	5	0.004
UW 212221	1/11/2024 12:35	1/11/2024 12:45	0.150	0.014	5	0.004
UW 212221	1/11/2024 12:45	1/11/2024 12:55	0.150	0.014	5	0.004
UW 212221	1/11/2024 12:55	1/11/2024 13:05	0.150	0.014	5	0.004
UW 212221	1/11/2024 13:05	1/11/2024 13:15	0.150	0.015	5	0.004
UW 212221	1/11/2024 13:15	1/11/2024 13:25	0.150	0.016	5	0.004
UW 212221	1/11/2024 13:25	1/11/2024 13:35	0.150	0.016	5	0.004
UW 212221	1/11/2024 13:35	1/11/2024 13:45	0.150	0.017	5	0.004
UW 212221	1/11/2024 13:45	1/11/2024 13:55	0.150	0.017	5	0.004
UW 212221	1/11/2024 13:55	1/11/2024 14:05	0.150	0.017	5	0.004
UW 212221	1/11/2024 14:05	1/11/2024 14:15	0.150	0.018	5	0.004
UW 212221	1/11/2024 14:15	1/11/2024 14:25	0.150	0.019	5	0.004
UW 212221	1/11/2024 14:25	1/11/2024 14:35	0.150	0.019	5	0.004
UW 212221	1/11/2024 14:35	1/11/2024 14:45	0.150	0.019	5	0.004
UW 212221	1/11/2024 14:45	1/11/2024 14:55	0.150	0.02	5	0.004
UW 212221	1/11/2024 14:55	1/11/2024 15:05	0.150	0.02	5	0.004
UW 212221	1/11/2024 15:05	1/11/2024 15:15	0.150	0.021	5	0.004
UW 212221	1/11/2024 15:15	1/11/2024 15:25	0.150	0.021	5	0.004
UW 212221	1/11/2024 15:25	1/11/2024 15:35	0.150	0.021	5	0.004
UW 212221	1/11/2024 15:35	1/11/2024 15:45	0.150	0.021	5	0.004
UW 212221	1/11/2024 15:45	1/11/2024 15:55	0.150	0.021	5	0.004
UW 212221	1/11/2024 15:55	1/11/2024 16:05	0.150	0.021	5	0.004
UW 212221	1/11/2024 16:05	1/11/2024 16:15	0.150	0.021	5	0.004
UW 212221	1/11/2024 16:15	1/11/2024 16:25	0.150	0.021	5	0.004
UW 212221	1/11/2024 16:25	1/11/2024 16:35	0.150	0.021	5	0.004
UW 212221	1/11/2024 16:35	1/11/2024 16:45	0.150	0.021	5	0.004
UW 212221	1/11/2024 16:45	1/11/2024 16:55	0.150	0.021	5	0.004
UW 212221	1/11/2024 16:55	1/11/2024 17:05	0.150	0.021	5	0.004
UW 212221	1/11/2024 17:05	1/11/2024 17:15	0.150	0.021	5	0.004

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/11/2024 7:15	1/11/2024 7:25	0.150	0	5	0
PER1 50057	1/11/2024 7:25	1/11/2024 7:35	0.150	0.001	5	0
PER1 50057	1/11/2024 7:35	1/11/2024 7:45	0.150	0.002	5	0
PER1 50057	1/11/2024 7:45	1/11/2024 7:55	0.150	0.003	5	0
PER1 50057	1/11/2024 7:55	1/11/2024 8:05	0.150	0.003	5	0
PER1 50057	1/11/2024 8:05	1/11/2024 8:15	0.150	0.004	5	0
PER1 50057	1/11/2024 8:15	1/11/2024 8:25	0.150	0.005	5	0
PER1 50057	1/11/2024 8:25	1/11/2024 8:35	0.150	0.005	5	0
PER1 50057	1/11/2024 8:35	1/11/2024 8:45	0.150	0.006	5	0
PER1 50057	1/11/2024 8:45	1/11/2024 8:55	0.150	0.007	5	0
PER1 50057	1/11/2024 8:55	1/11/2024 9:05	0.150	0.007	5	0
PER1 50057	1/11/2024 9:05	1/11/2024 9:15	0.150	0.008	5	0
PER1 50057	1/11/2024 9:15	1/11/2024 9:25	0.150	0.008	5	0
PER1 50057	1/11/2024 9:25	1/11/2024 9:35	0.150	0.009	5	0
PER1 50057	1/11/2024 9:35	1/11/2024 9:45	0.150	0.009	5	0
PER1 50057	1/11/2024 9:45	1/11/2024 9:55	0.150	0.01	5	0
PER1 50057	1/11/2024 9:55	1/11/2024 10:05	0.150	0.01	5	0
PER1 50057	1/11/2024 10:05	1/11/2024 10:15	0.150	0.011	5	0
PER1 50057	1/11/2024 10:15	1/11/2024 10:25	0.150	0.011	5	0
PER1 50057	1/11/2024 10:25	1/11/2024 10:35	0.150	0.011	5	0
PER1 50057	1/11/2024 10:35	1/11/2024 10:45	0.150	0.012	5	0
PER1 50057	1/11/2024 10:45	1/11/2024 10:55	0.150	0.013	5	0
PER1 50057	1/11/2024 10:55	1/11/2024 11:05	0.150	0.013	5	0
PER1 50057	1/11/2024 11:05	1/11/2024 11:15	0.150	0.013	5	0
PER1 50057	1/11/2024 11:15	1/11/2024 11:25	0.150	0.014	5	0
PER1 50057	1/11/2024 11:25	1/11/2024 11:35	0.150	0.014	5	0
PER1 50057	1/11/2024 11:35	1/11/2024 11:45	0.150	0.015	5	0
PER1 50057	1/11/2024 11:45	1/11/2024 11:55	0.150	0.016	5	0
PER1 50057	1/11/2024 11:55	1/11/2024 12:05	0.150	0.016	5	0
PER1 50057	1/11/2024 12:05	1/11/2024 12:15	0.150	0.017	5	0
PER1 50057	1/11/2024 12:15	1/11/2024 12:25	0.150	0.017	5	0
PER1 50057	1/11/2024 12:25	1/11/2024 12:35	0.150	0.018	5	0
PER1 50057	1/11/2024 12:35	1/11/2024 12:45	0.150	0.018	5	0
PER1 50057	1/11/2024 12:45	1/11/2024 12:55	0.150	0.019	5	0
PER1 50057	1/11/2024 12:55	1/11/2024 13:05	0.150	0.02	5	0
PER1 50057	1/11/2024 13:05	1/11/2024 13:15	0.150	0.02	5	0
PER1 50057	1/11/2024 13:15	1/11/2024 13:25	0.150	0.021	5	0
PER1 50057	1/11/2024 13:25	1/11/2024 13:35	0.150	0.021	5	0
PER1 50057	1/11/2024 13:35	1/11/2024 13:45	0.150	0.022	5	0
PER1 50057	1/11/2024 13:45	1/11/2024 13:55	0.150	0.022	5	0
PER1 50057	1/11/2024 13:55	1/11/2024 14:05	0.150	0.023	5	0
PER1 50057	1/11/2024 14:05	1/11/2024 14:15	0.150	0.023	5	0
PER1 50057	1/11/2024 14:15	1/11/2024 14:25	0.150	0.023	5	0
PER1 50057	1/11/2024 14:25	1/11/2024 14:35	0.150	0.024	5	0
PER1 50057	1/11/2024 14:35	1/11/2024 14:45	0.150	0.024	5	0
PER1 50057	1/11/2024 14:45	1/11/2024 14:55	0.150	0.024	5	0
PER1 50057	1/11/2024 14:55	1/11/2024 15:05	0.150	0.025	5	0
PER1 50057	1/11/2024 15:05	1/11/2024 15:15	0.150	0.025	5	0
PER1 50057	1/11/2024 15:15	1/11/2024 15:25	0.150	0.025	5	0
PER1 50057	1/11/2024 15:25	1/11/2024 15:35	0.150	0.025	5	0
PER1 50057	1/11/2024 15:35	1/11/2024 15:45	0.150	0.025	5	0
PER1 50057	1/11/2024 15:45	1/11/2024 15:55	0.150	0.025	5	0
PER1 50057	1/11/2024 15:55	1/11/2024 16:05	0.150	0.025	5	0
PER1 50057	1/11/2024 16:05	1/11/2024 16:15	0.150	0.025	5	0
PER1 50057	1/11/2024 16:15	1/11/2024 16:25	0.150	0.025	5	0
PER1 50057	1/11/2024 16:25	1/11/2024 16:35	0.150	0.025	5	0
PER1 50057	1/11/2024 16:35	1/11/2024 16:45	0.150	0.025	5	0
PER1 50057	1/11/2024 16:45	1/11/2024 16:55	0.150	0.025	5	0
PER1 50057	1/11/2024 16:55	1/11/2024 17:05	0.150	0.025	5	0
PER1 50057	1/11/2024 17:05	1/11/2024 17:15	0.150	0.025	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/11/2024 7:15	1/11/2024 7:25	0.150	0	5	0
PER2 46495	1/11/2024 7:25	1/11/2024 7:35	0.150	0	5	0
PER2 46495	1/11/2024 7:35	1/11/2024 7:45	0.150	0.002	5	0
PER2 46495	1/11/2024 7:45	1/11/2024 7:55	0.150	0.002	5	0
PER2 46495	1/11/2024 7:55	1/11/2024 8:05	0.150	0.003	5	0
PER2 46495	1/11/2024 8:05	1/11/2024 8:15	0.150	0.003	5	0
PER2 46495	1/11/2024 8:15	1/11/2024 8:25	0.150	0.003	5	0
PER2 46495	1/11/2024 8:25	1/11/2024 8:35	0.150	0.004	5	0
PER2 46495	1/11/2024 8:35	1/11/2024 8:45	0.150	0.004	5	0
PER2 46495	1/11/2024 8:45	1/11/2024 8:55	0.150	0.005	5	0
PER2 46495	1/11/2024 8:55	1/11/2024 9:05	0.150	0.005	5	0
PER2 46495	1/11/2024 9:05	1/11/2024 9:15	0.150	0.006	5	0
PER2 46495	1/11/2024 9:15	1/11/2024 9:25	0.150	0.006	5	0
PER2 46495	1/11/2024 9:25	1/11/2024 9:35	0.150	0.006	5	0
PER2 46495	1/11/2024 9:35	1/11/2024 9:45	0.150	0.007	5	0
PER2 46495	1/11/2024 9:45	1/11/2024 9:55	0.150	0.007	5	0
PER2 46495	1/11/2024 9:55	1/11/2024 10:05	0.150	0.008	5	0
PER2 46495	1/11/2024 10:05	1/11/2024 10:15	0.150	0.008	5	0
PER2 46495	1/11/2024 10:15	1/11/2024 10:25	0.150	0.009	5	0
PER2 46495	1/11/2024 10:25	1/11/2024 10:35	0.150	0.009	5	0
PER2 46495	1/11/2024 10:35	1/11/2024 10:45	0.150	0.01	5	0
PER2 46495	1/11/2024 10:45	1/11/2024 10:55	0.150	0.01	5	0
PER2 46495	1/11/2024 10:55	1/11/2024 11:05	0.150	0.011	5	0
PER2 46495	1/11/2024 11:05	1/11/2024 11:15	0.150	0.011	5	0
PER2 46495	1/11/2024 11:15	1/11/2024 11:25	0.150	0.012	5	0
PER2 46495	1/11/2024 11:25	1/11/2024 11:35	0.150	0.012	5	0
PER2 46495	1/11/2024 11:35	1/11/2024 11:45	0.150	0.013	5	0
PER2 46495	1/11/2024 11:45	1/11/2024 11:55	0.150	0.013	5	0
PER2 46495	1/11/2024 11:55	1/11/2024 12:05	0.150	0.014	5	0
PER2 46495	1/11/2024 12:05	1/11/2024 12:15	0.150	0.014	5	0
PER2 46495	1/11/2024 12:15	1/11/2024 12:25	0.150	0.014	5	0
PER2 46495	1/11/2024 12:25	1/11/2024 12:35	0.150	0.015	5	0
PER2 46495	1/11/2024 12:35	1/11/2024 12:45	0.150	0.015	5	0
PER2 46495	1/11/2024 12:45	1/11/2024 12:55	0.150	0.016	5	0
PER2 46495	1/11/2024 12:55	1/11/2024 13:05	0.150	0.016	5	0
PER2 46495	1/11/2024 13:05	1/11/2024 13:15	0.150	0.017	5	0
PER2 46495	1/11/2024 13:15	1/11/2024 13:25	0.150	0.017	5	0
PER2 46495	1/11/2024 13:25	1/11/2024 13:35	0.150	0.018	5	0
PER2 46495	1/11/2024 13:35	1/11/2024 13:45	0.150	0.018	5	0
PER2 46495	1/11/2024 13:45	1/11/2024 13:55	0.150	0.019	5	0
PER2 46495	1/11/2024 13:55	1/11/2024 14:05	0.150	0.019	5	0
PER2 46495	1/11/2024 14:05	1/11/2024 14:15	0.150	0.02	5	0
PER2 46495	1/11/2024 14:15	1/11/2024 14:25	0.150	0.02	5	0
PER2 46495	1/11/2024 14:25	1/11/2024 14:35	0.150	0.021	5	0
PER2 46495	1/11/2024 14:35	1/11/2024 14:45	0.150	0.022	5	0
PER2 46495	1/11/2024 14:45	1/11/2024 14:55	0.150	0.022	5	0
PER2 46495	1/11/2024 14:55	1/11/2024 15:05	0.150	0.023	5	0
PER2 46495	1/11/2024 15:05	1/11/2024 15:15	0.150	0.023	5	0
PER2 46495	1/11/2024 15:15	1/11/2024 15:25	0.150	0.024	5	0
PER2 46495	1/11/2024 15:25	1/11/2024 15:35	0.150	0.024	5	0
PER2 46495	1/11/2024 15:35	1/11/2024 15:45	0.150	0.024	5	0
PER2 46495	1/11/2024 15:45	1/11/2024 15:55	0.150	0.024	5	0
PER2 46495	1/11/2024 15:55	1/11/2024 16:05	0.150	0.024	5	0
PER2 46495	1/11/2024 16:05	1/11/2024 16:15	0.150	0.024	5	0
PER2 46495	1/11/2024 16:15	1/11/2024 16:25	0.150	0.024	5	0
PER2 46495	1/11/2024 16:25	1/11/2024 16:35	0.150	0.024	5	0
PER2 46495	1/11/2024 16:35	1/11/2024 16:45	0.150	0.024	5	0
PER2 46495	1/11/2024 16:45	1/11/2024 16:55	0.150	0.024	5	0
PER2 46495	1/11/2024 16:55	1/11/2024 17:05	0.150	0.024	5	0
PER2 46495	1/11/2024 17:05	1/11/2024 17:15	0.150	0.024	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/12/2024

Weather: 40 deg. F, Clear/ Cloudy

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) ECD continuing grading in the marine area.
- 3) Export of 10 loads (approximately 200 CY) of soil from WC-23 to the Bayshore Soil Management facility.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

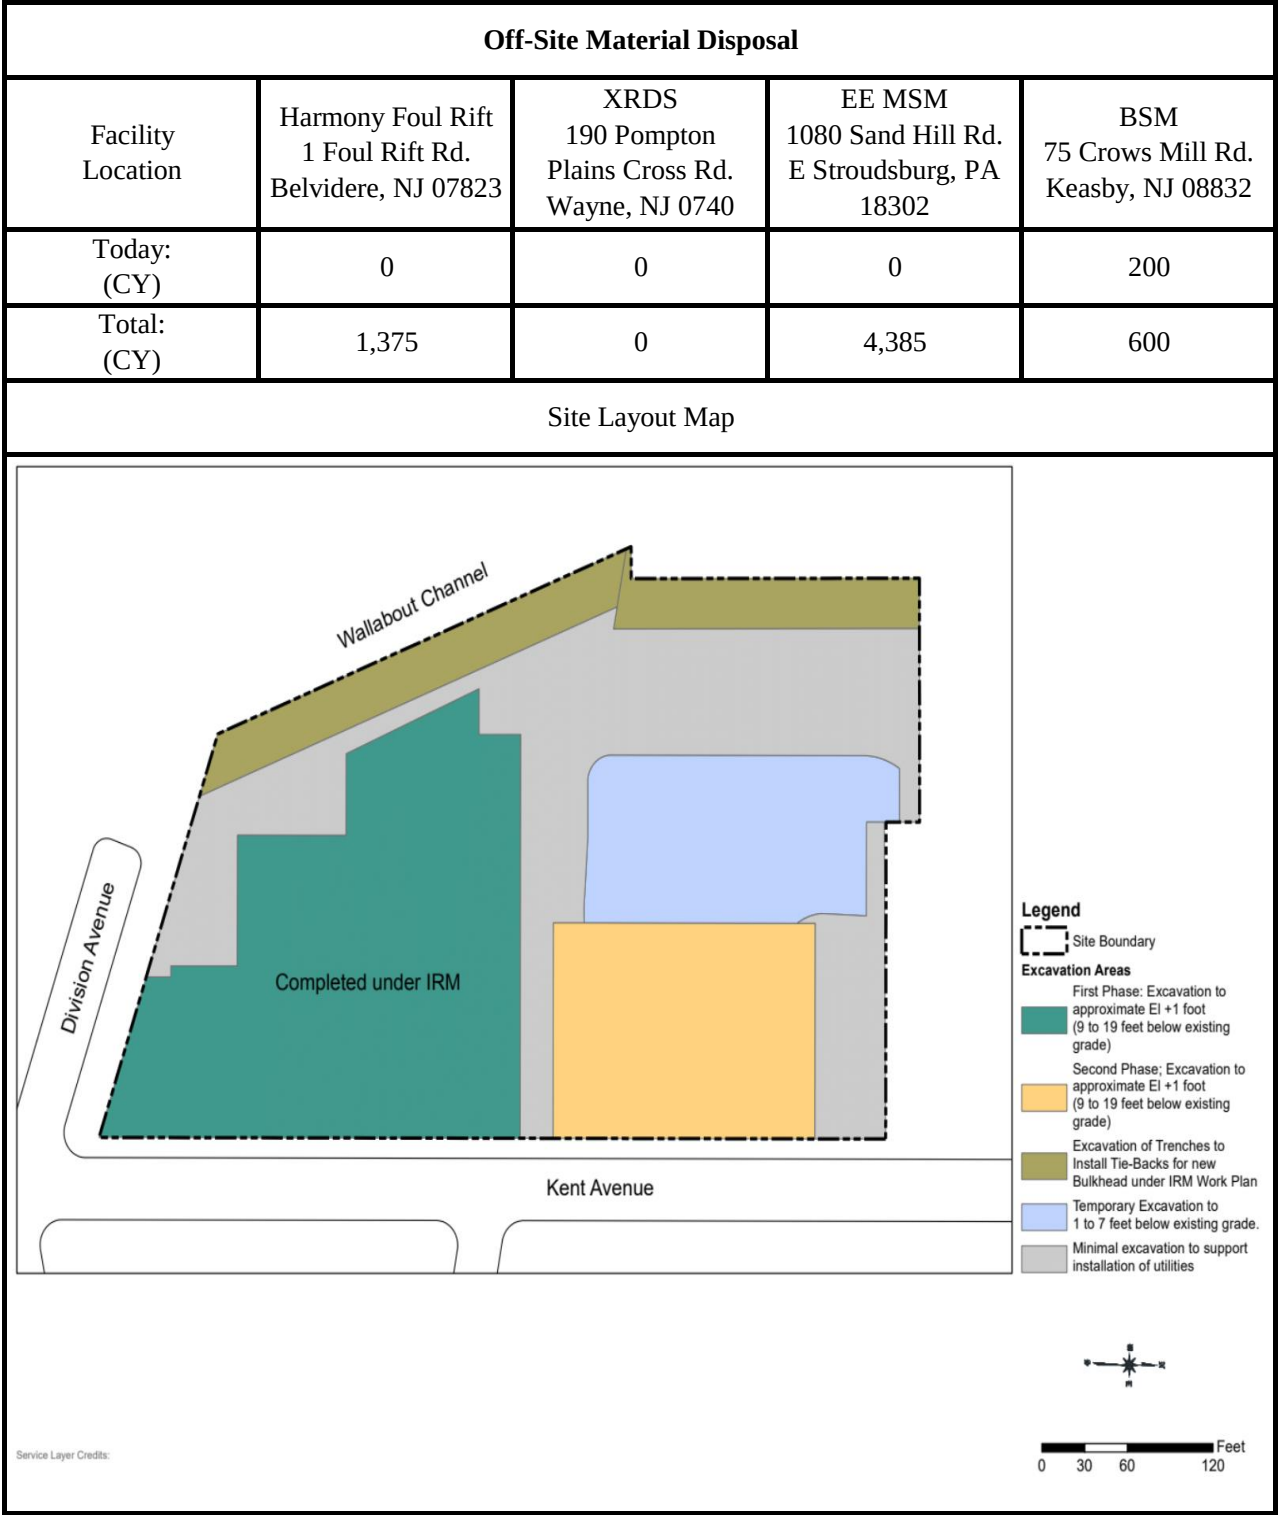


Photo 1:

View of soil excavation and truck loading for off-site soil disposal, pile installation and site conditions facing east.



Photo 2:

View of soil excavation, pile installation and site conditions facing east. of excavation and truck loading for off-site soil disposal.



Photo 3:
View of soil
excavation facing
southwest.




Photo 4:
View of site
conditions facing
southwest.



CAMP:
Downwind
Particulates

Dust Levels


0.022 mg/m³ 0.027 mg/m³ 0.15

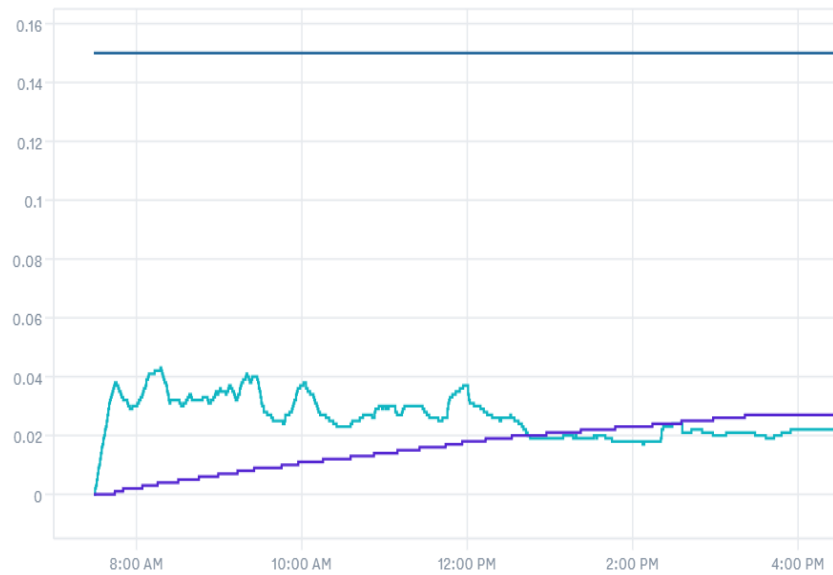


CAMP:
Downwind VOCs

VOC Levels

0 ppm 0 ppm 5

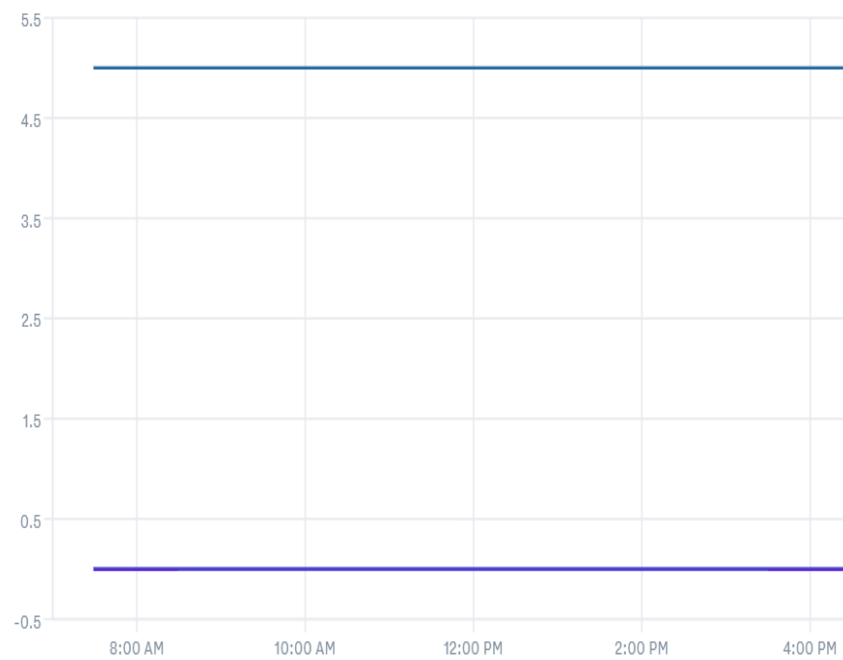

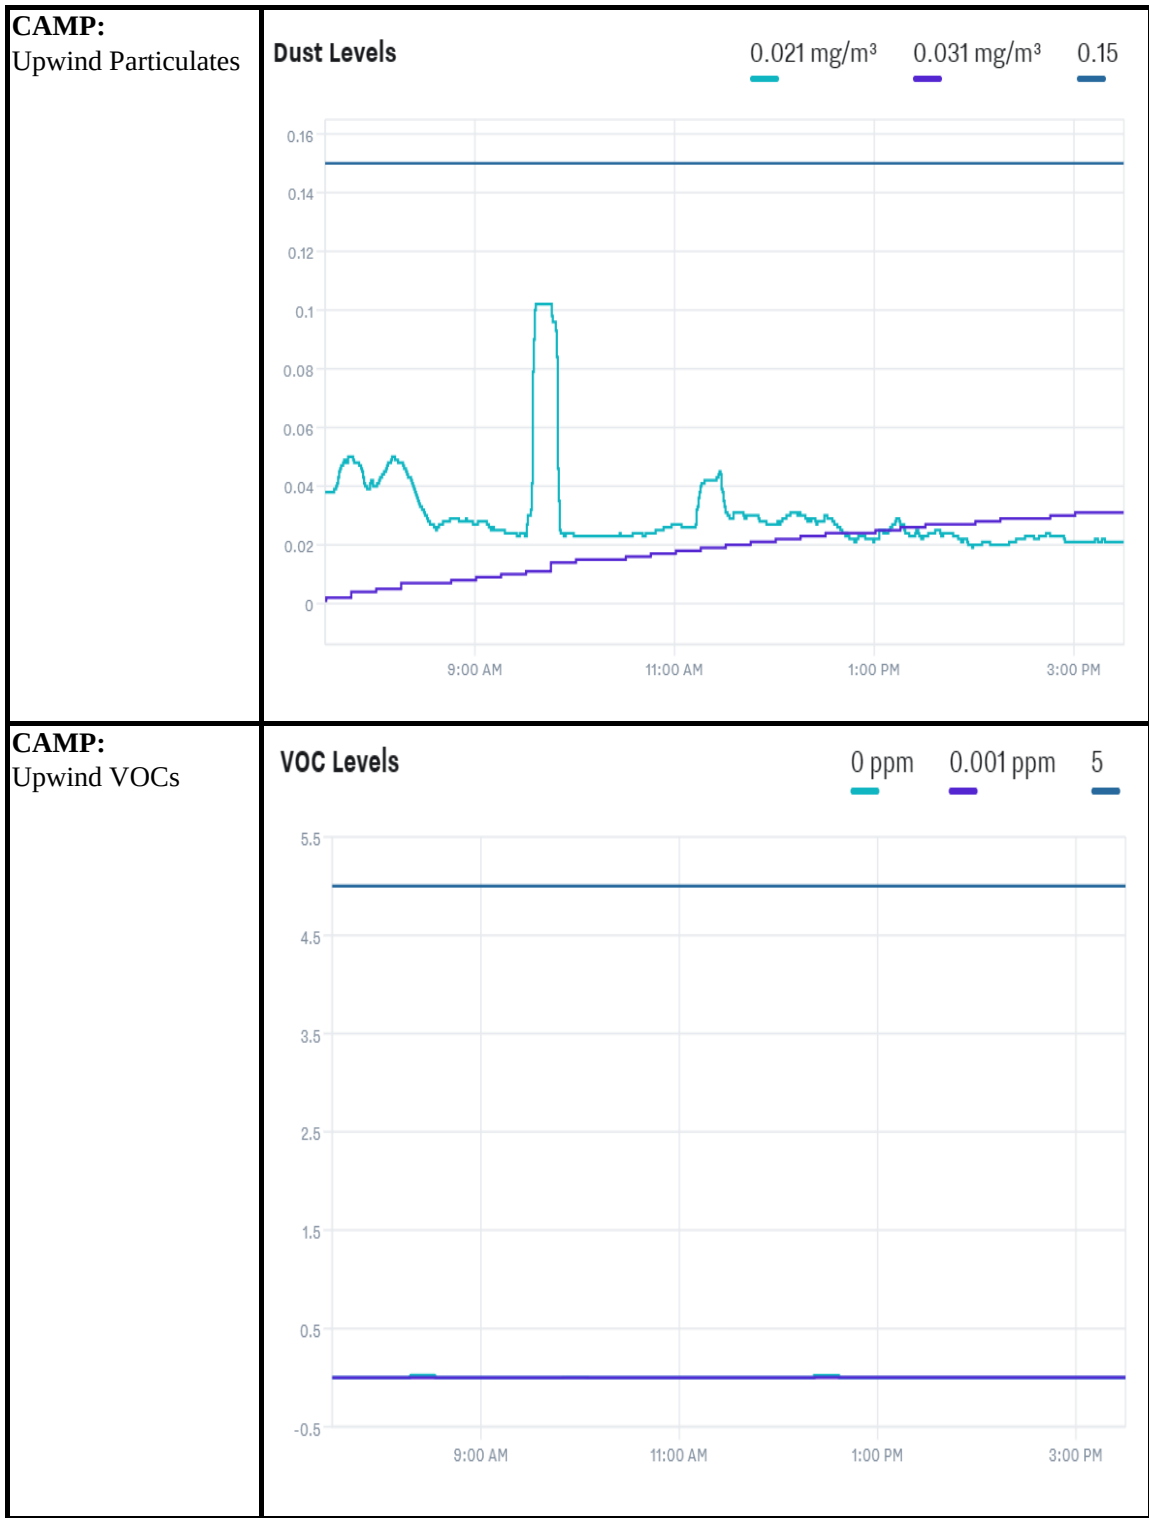

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/12/2024 8:00	1/12/2024 8:10	0.150	0.003	5	0
DW 47907	1/12/2024 8:10	1/12/2024 8:20	0.150	0.004	5	0
DW 47907	1/12/2024 8:20	1/12/2024 8:30	0.150	0.004	5	0
DW 47907	1/12/2024 8:30	1/12/2024 8:40	0.150	0.005	5	0
DW 47907	1/12/2024 8:40	1/12/2024 8:50	0.150	0.006	5	0
DW 47907	1/12/2024 8:50	1/12/2024 9:00	0.150	0.007	5	0
DW 47907	1/12/2024 9:00	1/12/2024 9:10	0.150	0.007	5	0
DW 47907	1/12/2024 9:10	1/12/2024 9:20	0.150	0.008	5	0
DW 47907	1/12/2024 9:20	1/12/2024 9:30	0.150	0.009	5	0
DW 47907	1/12/2024 9:30	1/12/2024 9:40	0.150	0.009	5	0
DW 47907	1/12/2024 9:40	1/12/2024 9:50	0.150	0.01	5	0
DW 47907	1/12/2024 9:50	1/12/2024 10:00	0.150	0.011	5	0
DW 47907	1/12/2024 10:00	1/12/2024 10:10	0.150	0.011	5	0
DW 47907	1/12/2024 10:10	1/12/2024 10:20	0.150	0.012	5	0
DW 47907	1/12/2024 10:20	1/12/2024 10:30	0.150	0.012	5	0
DW 47907	1/12/2024 10:30	1/12/2024 10:40	0.150	0.013	5	0
DW 47907	1/12/2024 10:40	1/12/2024 10:50	0.150	0.013	5	0
DW 47907	1/12/2024 10:50	1/12/2024 11:00	0.150	0.014	5	0
DW 47907	1/12/2024 11:00	1/12/2024 11:10	0.150	0.015	5	0
DW 47907	1/12/2024 11:10	1/12/2024 11:20	0.150	0.015	5	0
DW 47907	1/12/2024 11:20	1/12/2024 11:30	0.150	0.016	5	0
DW 47907	1/12/2024 11:30	1/12/2024 11:40	0.150	0.016	5	0
DW 47907	1/12/2024 11:40	1/12/2024 11:50	0.150	0.017	5	0
DW 47907	1/12/2024 11:50	1/12/2024 12:00	0.150	0.018	5	0
DW 47907	1/12/2024 12:00	1/12/2024 12:10	0.150	0.018	5	0
DW 47907	1/12/2024 12:10	1/12/2024 12:20	0.150	0.019	5	0
DW 47907	1/12/2024 12:20	1/12/2024 12:30	0.150	0.019	5	0
DW 47907	1/12/2024 12:30	1/12/2024 12:40	0.150	0.02	5	0
DW 47907	1/12/2024 12:40	1/12/2024 12:50	0.150	0.02	5	0
DW 47907	1/12/2024 12:50	1/12/2024 13:00	0.150	0.021	5	0
DW 47907	1/12/2024 13:00	1/12/2024 13:10	0.150	0.021	5	0
DW 47907	1/12/2024 13:10	1/12/2024 13:20	0.150	0.021	5	0
DW 47907	1/12/2024 13:20	1/12/2024 13:30	0.150	0.022	5	0
DW 47907	1/12/2024 13:30	1/12/2024 13:40	0.150	0.022	5	0
DW 47907	1/12/2024 13:40	1/12/2024 13:50	0.150	0.023	5	0
DW 47907	1/12/2024 13:50	1/12/2024 14:00	0.150	0.023	5	0
DW 47907	1/12/2024 14:00	1/12/2024 14:10	0.150	0.023	5	0
DW 47907	1/12/2024 14:10	1/12/2024 14:20	0.150	0.024	5	0
DW 47907	1/12/2024 14:20	1/12/2024 14:30	0.150	0.024	5	0
DW 47907	1/12/2024 14:30	1/12/2024 14:40	0.150	0.025	5	0
DW 47907	1/12/2024 14:40	1/12/2024 14:50	0.150	0.025	5	0
DW 47907	1/12/2024 14:50	1/12/2024 15:00	0.150	0.026	5	0
DW 47907	1/12/2024 15:00	1/12/2024 15:10	0.150	0.026	5	0
DW 47907	1/12/2024 15:10	1/12/2024 15:20	0.150	0.026	5	0
DW 47907	1/12/2024 15:20	1/12/2024 15:30	0.150	0.027	5	0
DW 47907	1/12/2024 15:30	1/12/2024 15:40	0.150	0.027	5	0
DW 47907	1/12/2024 15:40	1/12/2024 15:50	0.150	0.027	5	0
DW 47907	1/12/2024 15:50	1/12/2024 16:00	0.150	0.027	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/12/2024 8:00	1/12/2024 8:10	0.150	0.005	5	0
UW 212221	1/12/2024 8:10	1/12/2024 8:20	0.150	0.007	5	0
UW 212221	1/12/2024 8:20	1/12/2024 8:30	0.150	0.007	5	0
UW 212221	1/12/2024 8:30	1/12/2024 8:40	0.150	0.007	5	0
UW 212221	1/12/2024 8:40	1/12/2024 8:50	0.150	0.008	5	0
UW 212221	1/12/2024 8:50	1/12/2024 9:00	0.150	0.008	5	0
UW 212221	1/12/2024 9:00	1/12/2024 9:10	0.150	0.009	5	0
UW 212221	1/12/2024 9:10	1/12/2024 9:20	0.150	0.01	5	0
UW 212221	1/12/2024 9:20	1/12/2024 9:30	0.150	0.01	5	0
UW 212221	1/12/2024 9:30	1/12/2024 9:40	0.150	0.011	5	0
UW 212221	1/12/2024 9:40	1/12/2024 9:50	0.150	0.014	5	0
UW 212221	1/12/2024 9:50	1/12/2024 10:00	0.150	0.014	5	0
UW 212221	1/12/2024 10:00	1/12/2024 10:10	0.150	0.015	5	0
UW 212221	1/12/2024 10:10	1/12/2024 10:20	0.150	0.015	5	0
UW 212221	1/12/2024 10:20	1/12/2024 10:30	0.150	0.015	5	0
UW 212221	1/12/2024 10:30	1/12/2024 10:40	0.150	0.016	5	0
UW 212221	1/12/2024 10:40	1/12/2024 10:50	0.150	0.017	5	0
UW 212221	1/12/2024 10:50	1/12/2024 11:00	0.150	0.017	5	0
UW 212221	1/12/2024 11:00	1/12/2024 11:10	0.150	0.018	5	0
UW 212221	1/12/2024 11:10	1/12/2024 11:20	0.150	0.019	5	0
UW 212221	1/12/2024 11:20	1/12/2024 11:30	0.150	0.019	5	0
UW 212221	1/12/2024 11:30	1/12/2024 11:40	0.150	0.02	5	0
UW 212221	1/12/2024 11:40	1/12/2024 11:50	0.150	0.021	5	0
UW 212221	1/12/2024 11:50	1/12/2024 12:00	0.150	0.021	5	0
UW 212221	1/12/2024 12:00	1/12/2024 12:10	0.150	0.022	5	0
UW 212221	1/12/2024 12:10	1/12/2024 12:20	0.150	0.023	5	0
UW 212221	1/12/2024 12:20	1/12/2024 12:30	0.150	0.023	5	0.001
UW 212221	1/12/2024 12:30	1/12/2024 12:40	0.150	0.024	5	0.001
UW 212221	1/12/2024 12:40	1/12/2024 12:50	0.150	0.024	5	0.001
UW 212221	1/12/2024 12:50	1/12/2024 13:00	0.150	0.024	5	0.001
UW 212221	1/12/2024 13:00	1/12/2024 13:10	0.150	0.025	5	0.001
UW 212221	1/12/2024 13:10	1/12/2024 13:20	0.150	0.026	5	0.001
UW 212221	1/12/2024 13:20	1/12/2024 13:30	0.150	0.026	5	0.001
UW 212221	1/12/2024 13:30	1/12/2024 13:40	0.150	0.027	5	0.001
UW 212221	1/12/2024 13:40	1/12/2024 13:50	0.150	0.027	5	0.001
UW 212221	1/12/2024 13:50	1/12/2024 14:00	0.150	0.027	5	0.001
UW 212221	1/12/2024 14:00	1/12/2024 14:10	0.150	0.028	5	0.001
UW 212221	1/12/2024 14:10	1/12/2024 14:20	0.150	0.029	5	0.001
UW 212221	1/12/2024 14:20	1/12/2024 14:30	0.150	0.029	5	0.001
UW 212221	1/12/2024 14:30	1/12/2024 14:40	0.150	0.029	5	0.001
UW 212221	1/12/2024 14:40	1/12/2024 14:50	0.150	0.03	5	0.001
UW 212221	1/12/2024 14:50	1/12/2024 15:00	0.150	0.03	5	0.001
UW 212221	1/12/2024 15:00	1/12/2024 15:10	0.150	0.031	5	0.001
UW 212221	1/12/2024 15:10	1/12/2024 15:20	0.150	0.031	5	0.001
UW 212221	1/12/2024 15:20	1/12/2024 15:30	0.150	0.031	5	0.001
UW 212221	1/12/2024 15:30	1/12/2024 15:40	0.150	0.031	5	0
UW 212221	1/12/2024 15:40	1/12/2024 15:50	0.150	0	5	0
UW 212221	1/12/2024 15:50	1/12/2024 16:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/12/2024 8:00	1/12/2024 8:10	0.150	0.005	5	0
PER1 50057	1/12/2024 8:10	1/12/2024 8:20	0.150	0.006	5	0
PER1 50057	1/12/2024 8:20	1/12/2024 8:30	0.150	0.006	5	0
PER1 50057	1/12/2024 8:30	1/12/2024 8:40	0.150	0.007	5	0
PER1 50057	1/12/2024 8:40	1/12/2024 8:50	0.150	0.008	5	0
PER1 50057	1/12/2024 8:50	1/12/2024 9:00	0.150	0.009	5	0
PER1 50057	1/12/2024 9:00	1/12/2024 9:10	0.150	0.009	5	0
PER1 50057	1/12/2024 9:10	1/12/2024 9:20	0.150	0.01	5	0
PER1 50057	1/12/2024 9:20	1/12/2024 9:30	0.150	0.011	5	0
PER1 50057	1/12/2024 9:30	1/12/2024 9:40	0.150	0.011	5	0
PER1 50057	1/12/2024 9:40	1/12/2024 9:50	0.150	0.012	5	0
PER1 50057	1/12/2024 9:50	1/12/2024 10:00	0.150	0.012	5	0
PER1 50057	1/12/2024 10:00	1/12/2024 10:10	0.150	0.013	5	0
PER1 50057	1/12/2024 10:10	1/12/2024 10:20	0.150	0.014	5	0
PER1 50057	1/12/2024 10:20	1/12/2024 10:30	0.150	0.014	5	0
PER1 50057	1/12/2024 10:30	1/12/2024 10:40	0.150	0.015	5	0
PER1 50057	1/12/2024 10:40	1/12/2024 10:50	0.150	0.015	5	0
PER1 50057	1/12/2024 10:50	1/12/2024 11:00	0.150	0.016	5	0
PER1 50057	1/12/2024 11:00	1/12/2024 11:10	0.150	0.017	5	0
PER1 50057	1/12/2024 11:10	1/12/2024 11:20	0.150	0.018	5	0
PER1 50057	1/12/2024 11:20	1/12/2024 11:30	0.150	0.019	5	0
PER1 50057	1/12/2024 11:30	1/12/2024 11:40	0.150	0.02	5	0
PER1 50057	1/12/2024 11:40	1/12/2024 11:50	0.150	0.02	5	0
PER1 50057	1/12/2024 11:50	1/12/2024 12:00	0.150	0.021	5	0
PER1 50057	1/12/2024 12:00	1/12/2024 12:10	0.150	0.022	5	0
PER1 50057	1/12/2024 12:10	1/12/2024 12:20	0.150	0.022	5	0
PER1 50057	1/12/2024 12:20	1/12/2024 12:30	0.150	0.023	5	0
PER1 50057	1/12/2024 12:30	1/12/2024 12:40	0.150	0.023	5	0
PER1 50057	1/12/2024 12:40	1/12/2024 12:50	0.150	0.024	5	0
PER1 50057	1/12/2024 12:50	1/12/2024 13:00	0.150	0.024	5	0
PER1 50057	1/12/2024 13:00	1/12/2024 13:10	0.150	0.025	5	0
PER1 50057	1/12/2024 13:10	1/12/2024 13:20	0.150	0.025	5	0
PER1 50057	1/12/2024 13:20	1/12/2024 13:30	0.150	0.026	5	0
PER1 50057	1/12/2024 13:30	1/12/2024 13:40	0.150	0.026	5	0
PER1 50057	1/12/2024 13:40	1/12/2024 13:50	0.150	0.026	5	0
PER1 50057	1/12/2024 13:50	1/12/2024 14:00	0.150	0.027	5	0
PER1 50057	1/12/2024 14:00	1/12/2024 14:10	0.150	0.027	5	0
PER1 50057	1/12/2024 14:10	1/12/2024 14:20	0.150	0.027	5	0
PER1 50057	1/12/2024 14:20	1/12/2024 14:30	0.150	0.028	5	0
PER1 50057	1/12/2024 14:30	1/12/2024 14:40	0.150	0.028	5	0
PER1 50057	1/12/2024 14:40	1/12/2024 14:50	0.150	0.028	5	0
PER1 50057	1/12/2024 14:50	1/12/2024 15:00	0.150	0.029	5	0
PER1 50057	1/12/2024 15:00	1/12/2024 15:10	0.150	0.029	5	0
PER1 50057	1/12/2024 15:10	1/12/2024 15:20	0.150	0.03	5	0
PER1 50057	1/12/2024 15:20	1/12/2024 15:30	0.150	0.03	5	0
PER1 50057	1/12/2024 15:30	1/12/2024 15:40	0.150	0.03	5	0
PER1 50057	1/12/2024 15:40	1/12/2024 15:50	0.150	0	5	0
PER1 50057	1/12/2024 15:50	1/12/2024 16:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/12/2024 8:00	1/12/2024 8:10	0.150	0.003	5	0
PER2 46495	1/12/2024 8:10	1/12/2024 8:20	0.150	0.004	5	0
PER2 46495	1/12/2024 8:20	1/12/2024 8:30	0.150	0.005	5	0
PER2 46495	1/12/2024 8:30	1/12/2024 8:40	0.150	0.006	5	0
PER2 46495	1/12/2024 8:40	1/12/2024 8:50	0.150	0.006	5	0
PER2 46495	1/12/2024 8:50	1/12/2024 9:00	0.150	0.007	5	0
PER2 46495	1/12/2024 9:00	1/12/2024 9:10	0.150	0.008	5	0
PER2 46495	1/12/2024 9:10	1/12/2024 9:20	0.150	0.009	5	0
PER2 46495	1/12/2024 9:20	1/12/2024 9:30	0.150	0.009	5	0
PER2 46495	1/12/2024 9:30	1/12/2024 9:40	0.150	0.01	5	0
PER2 46495	1/12/2024 9:40	1/12/2024 9:50	0.150	0.01	5	0
PER2 46495	1/12/2024 9:50	1/12/2024 10:00	0.150	0.011	5	0
PER2 46495	1/12/2024 10:00	1/12/2024 10:10	0.150	0.011	5	0
PER2 46495	1/12/2024 10:10	1/12/2024 10:20	0.150	0.012	5	0
PER2 46495	1/12/2024 10:20	1/12/2024 10:30	0.150	0.013	5	0
PER2 46495	1/12/2024 10:30	1/12/2024 10:40	0.150	0.013	5	0
PER2 46495	1/12/2024 10:40	1/12/2024 10:50	0.150	0.014	5	0
PER2 46495	1/12/2024 10:50	1/12/2024 11:00	0.150	0.015	5	0
PER2 46495	1/12/2024 11:00	1/12/2024 11:10	0.150	0.016	5	0
PER2 46495	1/12/2024 11:10	1/12/2024 11:20	0.150	0.017	5	0
PER2 46495	1/12/2024 11:20	1/12/2024 11:30	0.150	0.018	5	0
PER2 46495	1/12/2024 11:30	1/12/2024 11:40	0.150	0.019	5	0
PER2 46495	1/12/2024 11:40	1/12/2024 11:50	0.150	0.02	5	0
PER2 46495	1/12/2024 11:50	1/12/2024 12:00	0.150	0.02	5	0
PER2 46495	1/12/2024 12:00	1/12/2024 12:10	0.150	0.021	5	0
PER2 46495	1/12/2024 12:10	1/12/2024 12:20	0.150	0.022	5	0
PER2 46495	1/12/2024 12:20	1/12/2024 12:30	0.150	0.022	5	0
PER2 46495	1/12/2024 12:30	1/12/2024 12:40	0.150	0.023	5	0
PER2 46495	1/12/2024 12:40	1/12/2024 12:50	0.150	0.023	5	0
PER2 46495	1/12/2024 12:50	1/12/2024 13:00	0.150	0.024	5	0
PER2 46495	1/12/2024 13:00	1/12/2024 13:10	0.150	0.024	5	0
PER2 46495	1/12/2024 13:10	1/12/2024 13:20	0.150	0.025	5	0
PER2 46495	1/12/2024 13:20	1/12/2024 13:30	0.150	0.025	5	0
PER2 46495	1/12/2024 13:30	1/12/2024 13:40	0.150	0.026	5	0
PER2 46495	1/12/2024 13:40	1/12/2024 13:50	0.150	0.026	5	0
PER2 46495	1/12/2024 13:50	1/12/2024 14:00	0.150	0.026	5	0
PER2 46495	1/12/2024 14:00	1/12/2024 14:10	0.150	0.027	5	0
PER2 46495	1/12/2024 14:10	1/12/2024 14:20	0.150	0.027	5	0
PER2 46495	1/12/2024 14:20	1/12/2024 14:30	0.150	0.028	5	0
PER2 46495	1/12/2024 14:30	1/12/2024 14:40	0.150	0.028	5	0
PER2 46495	1/12/2024 14:40	1/12/2024 14:50	0.150	0.029	5	0
PER2 46495	1/12/2024 14:50	1/12/2024 15:00	0.150	0.029	5	0
PER2 46495	1/12/2024 15:00	1/12/2024 15:10	0.150	0.029	5	0
PER2 46495	1/12/2024 15:10	1/12/2024 15:20	0.150	0.03	5	0
PER2 46495	1/12/2024 15:20	1/12/2024 15:30	0.150	0.03	5	0
PER2 46495	1/12/2024 15:30	1/12/2024 15:40	0.150	0.03	5	0
PER2 46495	1/12/2024 15:40	1/12/2024 15:50	0.150	0.03	5	0
PER2 46495	1/12/2024 15:50	1/12/2024 16:00	0.150	0.03	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/15/2024

Weather: 30 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) ECD continuing grading in the marine area.
- 3) Export of 28 loads (approximately 560 CY) of soil from WC-25 and 27 for off-site disposal to the HFM facility.
- 4) Export of 2 loads (approximately 40 CY) of soil from WC-29 for off-site disposal to the MSM facility.
- 5) NYC DEP on-site for SWPPP inspection.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

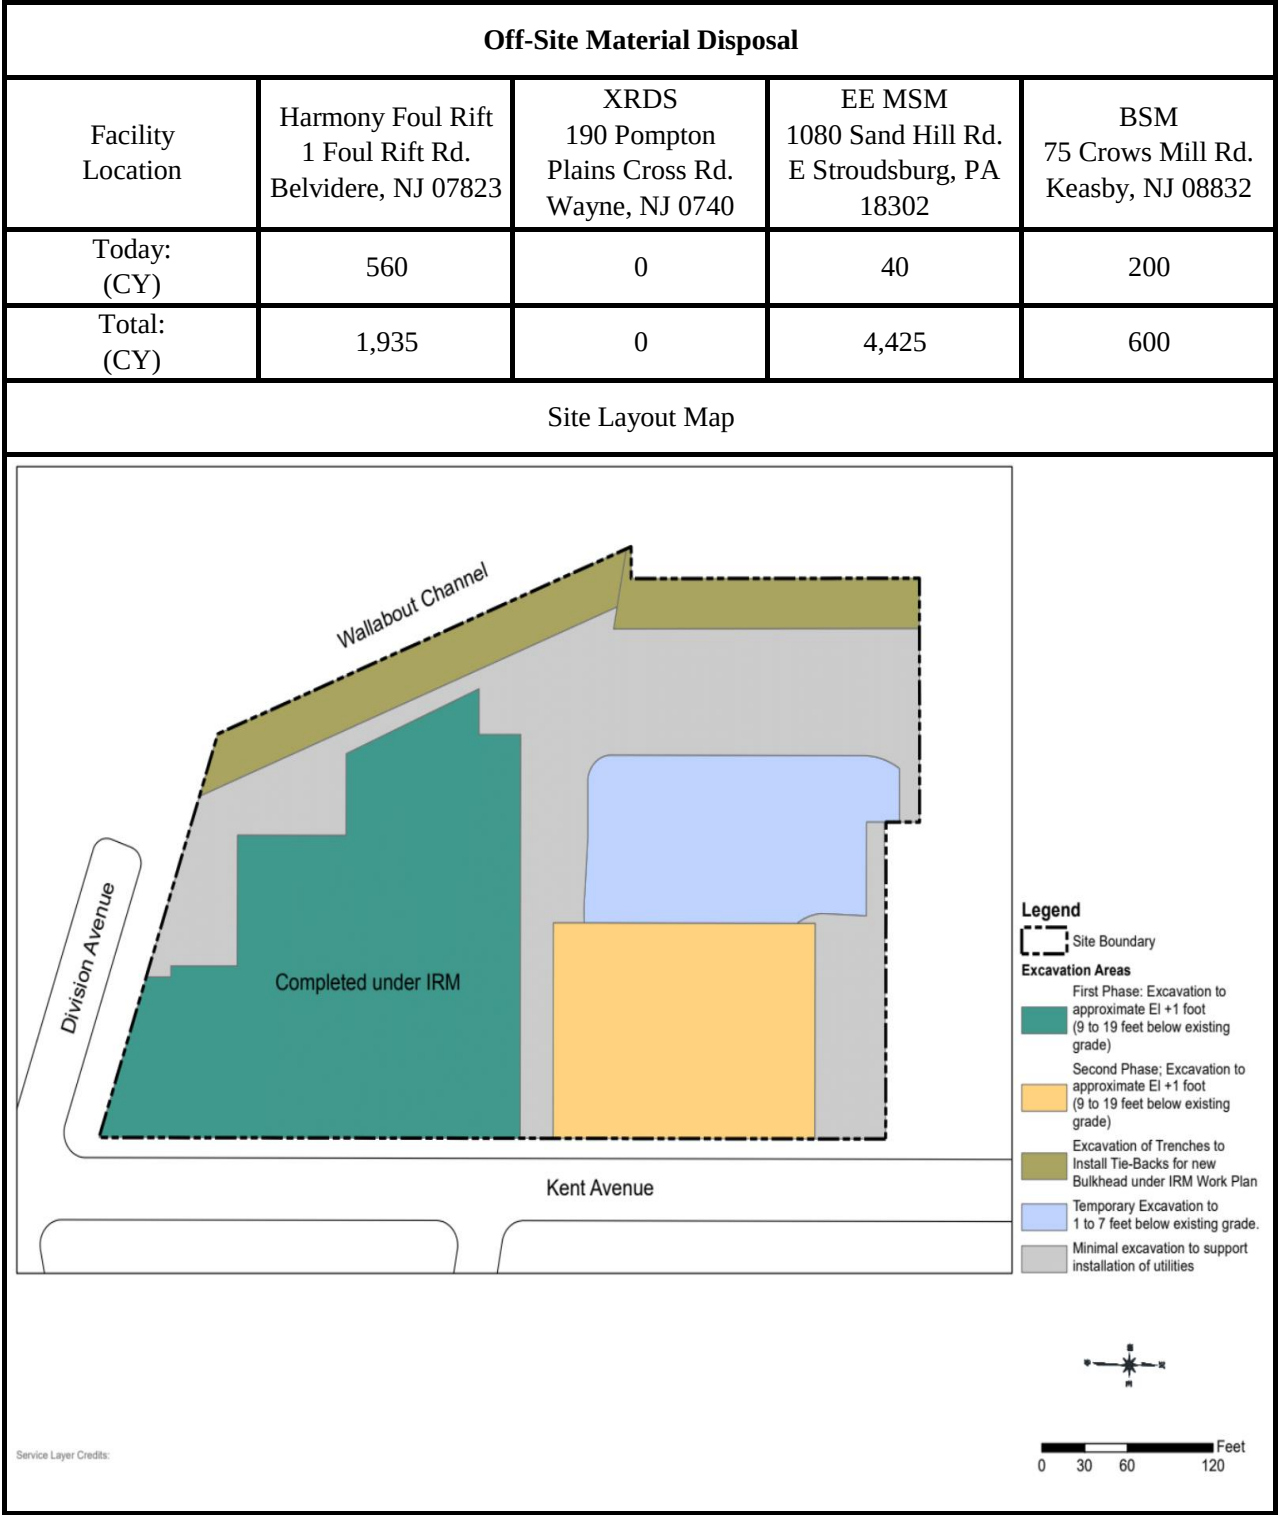


Photo 1:

View of soil excavation, pile installation and site conditions facing northwest.

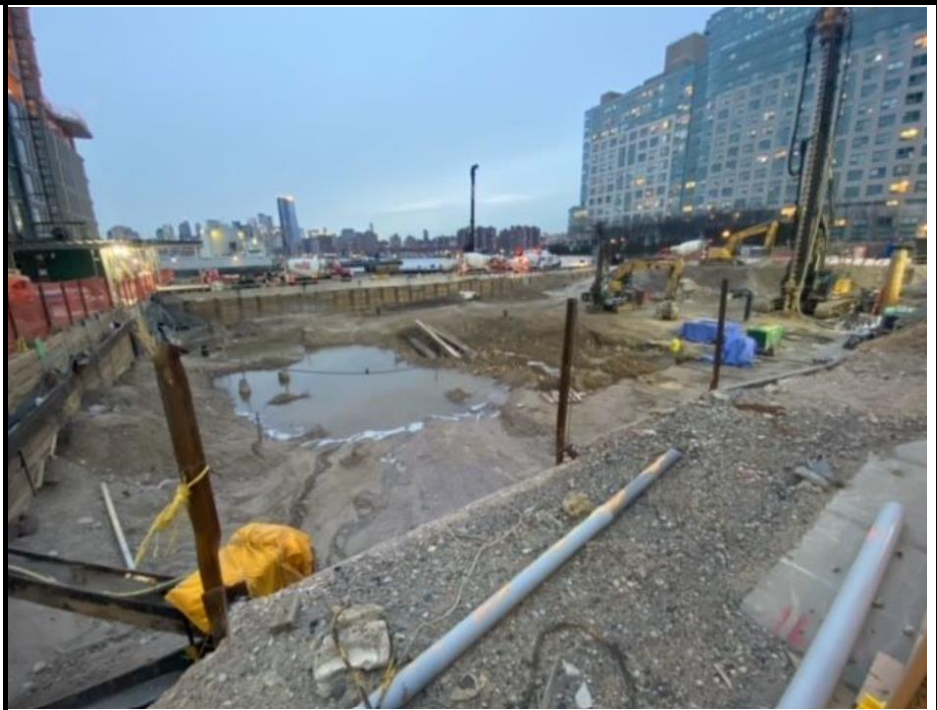


Photo 2:

View of site conditions facing southwest.

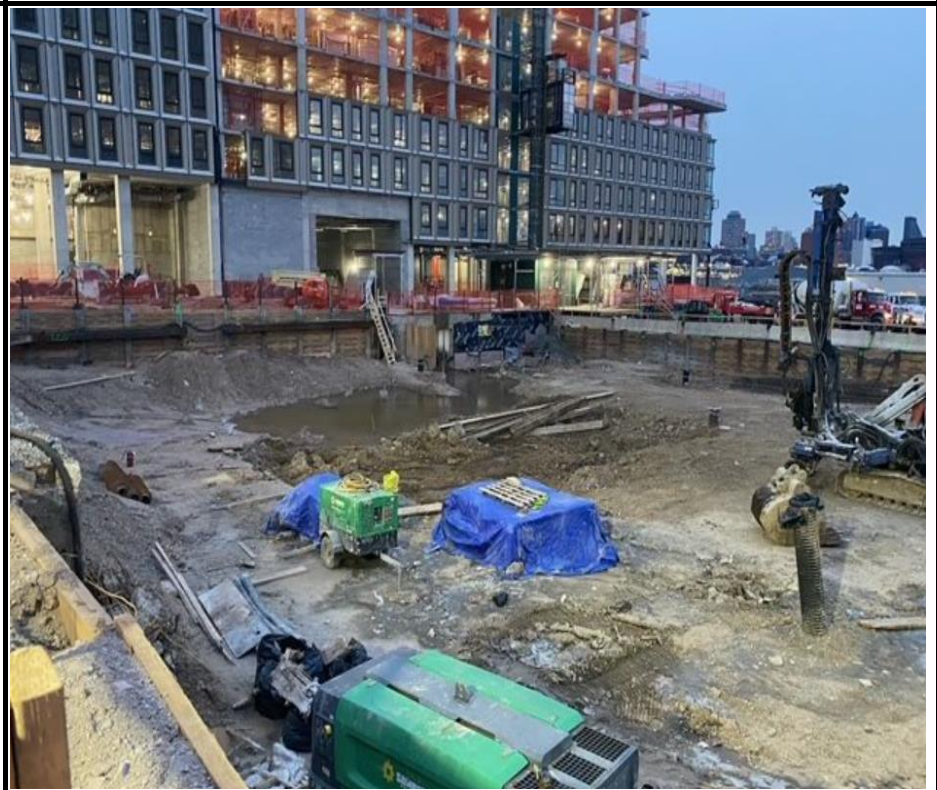


Photo 3:

View of Site
conditions facing
north.

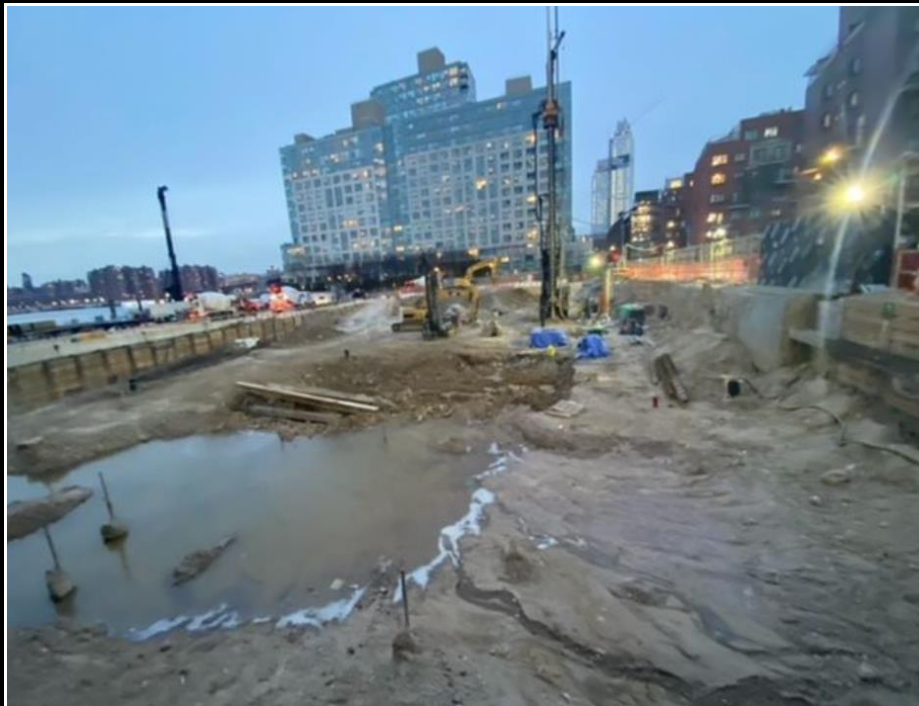


Photo 4:


View of structure
development facing
north.



CAMP:
Downwind
Particulates

Dust Levels


0.016 mg/m³ 0.026 mg/m³ 0.15

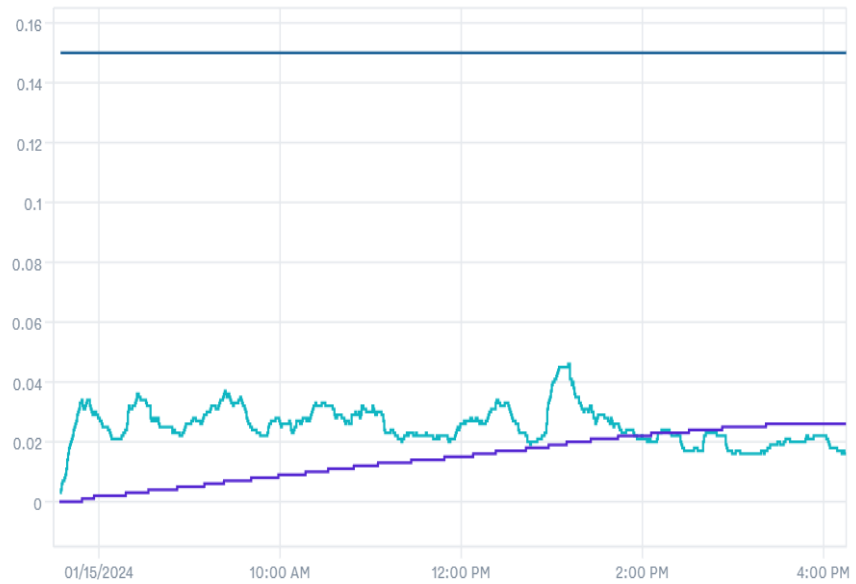


CAMP:
Downwind VOCs

VOC Levels

0 ppm 0 ppm 5

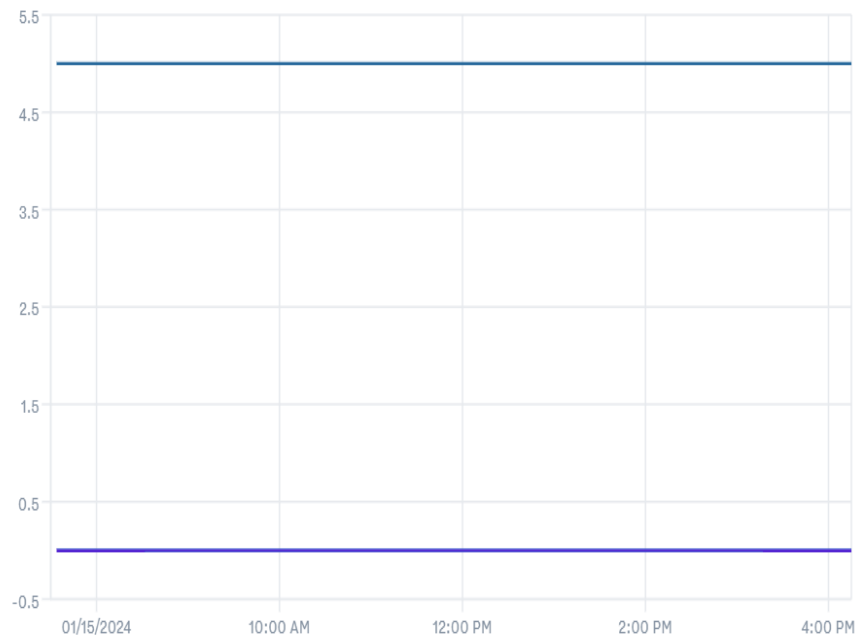

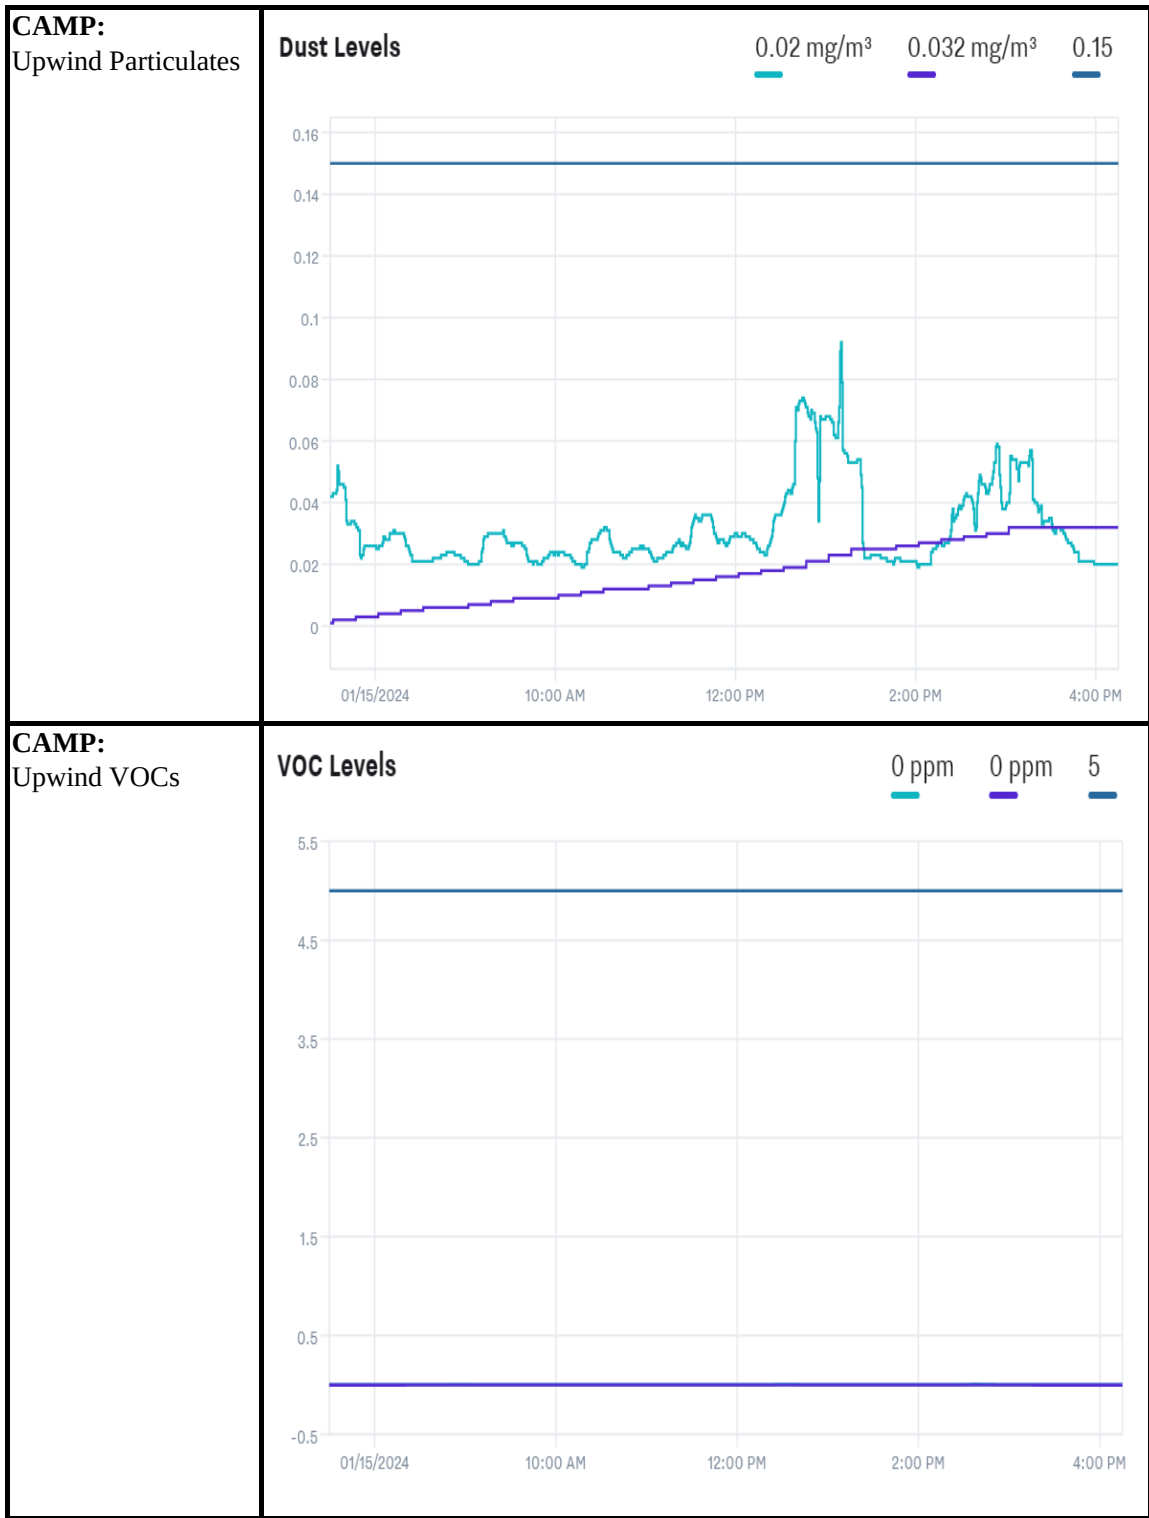

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/15/2024 8:00	1/15/2024 8:10	0.150	0.002	5	0
DW 47907	1/15/2024 8:10	1/15/2024 8:20	0.150	0.003	5	0
DW 47907	1/15/2024 8:20	1/15/2024 8:30	0.150	0.003	5	0
DW 47907	1/15/2024 8:30	1/15/2024 8:40	0.150	0.004	5	0
DW 47907	1/15/2024 8:40	1/15/2024 8:50	0.150	0.004	5	0
DW 47907	1/15/2024 8:50	1/15/2024 9:00	0.150	0.005	5	0
DW 47907	1/15/2024 9:00	1/15/2024 9:10	0.150	0.006	5	0
DW 47907	1/15/2024 9:10	1/15/2024 9:20	0.150	0.006	5	0
DW 47907	1/15/2024 9:20	1/15/2024 9:30	0.150	0.007	5	0
DW 47907	1/15/2024 9:30	1/15/2024 9:40	0.150	0.007	5	0
DW 47907	1/15/2024 9:40	1/15/2024 9:50	0.150	0.008	5	0
DW 47907	1/15/2024 9:50	1/15/2024 10:00	0.150	0.009	5	0
DW 47907	1/15/2024 10:00	1/15/2024 10:10	0.150	0.009	5	0
DW 47907	1/15/2024 10:10	1/15/2024 10:20	0.150	0.01	5	0
DW 47907	1/15/2024 10:20	1/15/2024 10:30	0.150	0.01	5	0
DW 47907	1/15/2024 10:30	1/15/2024 10:40	0.150	0.011	5	0
DW 47907	1/15/2024 10:40	1/15/2024 10:50	0.150	0.012	5	0
DW 47907	1/15/2024 10:50	1/15/2024 11:00	0.150	0.012	5	0
DW 47907	1/15/2024 11:00	1/15/2024 11:10	0.150	0.013	5	0
DW 47907	1/15/2024 11:10	1/15/2024 11:20	0.150	0.013	5	0
DW 47907	1/15/2024 11:20	1/15/2024 11:30	0.150	0.014	5	0
DW 47907	1/15/2024 11:30	1/15/2024 11:40	0.150	0.014	5	0
DW 47907	1/15/2024 11:40	1/15/2024 11:50	0.150	0.015	5	0
DW 47907	1/15/2024 11:50	1/15/2024 12:00	0.150	0.015	5	0
DW 47907	1/15/2024 12:00	1/15/2024 12:10	0.150	0.016	5	0
DW 47907	1/15/2024 12:10	1/15/2024 12:20	0.150	0.016	5	0
DW 47907	1/15/2024 12:20	1/15/2024 12:30	0.150	0.017	5	0
DW 47907	1/15/2024 12:30	1/15/2024 12:40	0.150	0.017	5	0
DW 47907	1/15/2024 12:40	1/15/2024 12:50	0.150	0.018	5	0
DW 47907	1/15/2024 12:50	1/15/2024 13:00	0.150	0.019	5	0
DW 47907	1/15/2024 13:00	1/15/2024 13:10	0.150	0.02	5	0
DW 47907	1/15/2024 13:10	1/15/2024 13:20	0.150	0.02	5	0
DW 47907	1/15/2024 13:20	1/15/2024 13:30	0.150	0.021	5	0
DW 47907	1/15/2024 13:30	1/15/2024 13:40	0.150	0.021	5	0
DW 47907	1/15/2024 13:40	1/15/2024 13:50	0.150	0.022	5	0
DW 47907	1/15/2024 13:50	1/15/2024 14:00	0.150	0.022	5	0
DW 47907	1/15/2024 14:00	1/15/2024 14:10	0.150	0.023	5	0
DW 47907	1/15/2024 14:10	1/15/2024 14:20	0.150	0.023	5	0
DW 47907	1/15/2024 14:20	1/15/2024 14:30	0.150	0.023	5	0
DW 47907	1/15/2024 14:30	1/15/2024 14:40	0.150	0.024	5	0
DW 47907	1/15/2024 14:40	1/15/2024 14:50	0.150	0.024	5	0
DW 47907	1/15/2024 14:50	1/15/2024 15:00	0.150	0.025	5	0
DW 47907	1/15/2024 15:00	1/15/2024 15:10	0.150	0.025	5	0
DW 47907	1/15/2024 15:10	1/15/2024 15:20	0.150	0.025	5	0
DW 47907	1/15/2024 15:20	1/15/2024 15:30	0.150	0.026	5	0
DW 47907	1/15/2024 15:30	1/15/2024 15:40	0.150	0.026	5	0
DW 47907	1/15/2024 15:40	1/15/2024 15:50	0.150	0.026	5	0
DW 47907	1/15/2024 15:50	1/15/2024 16:00	0.150	0.026	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/15/2024 8:00	1/15/2024 8:10	0.150	0.004	5	0
UW 212221	1/15/2024 8:10	1/15/2024 8:20	0.150	0.005	5	0
UW 212221	1/15/2024 8:20	1/15/2024 8:30	0.150	0.005	5	0
UW 212221	1/15/2024 8:30	1/15/2024 8:40	0.150	0.006	5	0
UW 212221	1/15/2024 8:40	1/15/2024 8:50	0.150	0.006	5	0
UW 212221	1/15/2024 8:50	1/15/2024 9:00	0.150	0.006	5	0
UW 212221	1/15/2024 9:00	1/15/2024 9:10	0.150	0.007	5	0
UW 212221	1/15/2024 9:10	1/15/2024 9:20	0.150	0.008	5	0
UW 212221	1/15/2024 9:20	1/15/2024 9:30	0.150	0.008	5	0
UW 212221	1/15/2024 9:30	1/15/2024 9:40	0.150	0.009	5	0
UW 212221	1/15/2024 9:40	1/15/2024 9:50	0.150	0.009	5	0
UW 212221	1/15/2024 9:50	1/15/2024 10:00	0.150	0.009	5	0
UW 212221	1/15/2024 10:00	1/15/2024 10:10	0.150	0.01	5	0
UW 212221	1/15/2024 10:10	1/15/2024 10:20	0.150	0.011	5	0
UW 212221	1/15/2024 10:20	1/15/2024 10:30	0.150	0.011	5	0
UW 212221	1/15/2024 10:30	1/15/2024 10:40	0.150	0.012	5	0
UW 212221	1/15/2024 10:40	1/15/2024 10:50	0.150	0.012	5	0
UW 212221	1/15/2024 10:50	1/15/2024 11:00	0.150	0.012	5	0
UW 212221	1/15/2024 11:00	1/15/2024 11:10	0.150	0.013	5	0
UW 212221	1/15/2024 11:10	1/15/2024 11:20	0.150	0.014	5	0
UW 212221	1/15/2024 11:20	1/15/2024 11:30	0.150	0.014	5	0
UW 212221	1/15/2024 11:30	1/15/2024 11:40	0.150	0.015	5	0
UW 212221	1/15/2024 11:40	1/15/2024 11:50	0.150	0.016	5	0
UW 212221	1/15/2024 11:50	1/15/2024 12:00	0.150	0.016	5	0
UW 212221	1/15/2024 12:00	1/15/2024 12:10	0.150	0.017	5	0
UW 212221	1/15/2024 12:10	1/15/2024 12:20	0.150	0.018	5	0
UW 212221	1/15/2024 12:20	1/15/2024 12:30	0.150	0.018	5	0
UW 212221	1/15/2024 12:30	1/15/2024 12:40	0.150	0.019	5	0
UW 212221	1/15/2024 12:40	1/15/2024 12:50	0.150	0.021	5	0
UW 212221	1/15/2024 12:50	1/15/2024 13:00	0.150	0.021	5	0
UW 212221	1/15/2024 13:00	1/15/2024 13:10	0.150	0.023	5	0
UW 212221	1/15/2024 13:10	1/15/2024 13:20	0.150	0.025	5	0
UW 212221	1/15/2024 13:20	1/15/2024 13:30	0.150	0.025	5	0
UW 212221	1/15/2024 13:30	1/15/2024 13:40	0.150	0.025	5	0
UW 212221	1/15/2024 13:40	1/15/2024 13:50	0.150	0.026	5	0
UW 212221	1/15/2024 13:50	1/15/2024 14:00	0.150	0.026	5	0
UW 212221	1/15/2024 14:00	1/15/2024 14:10	0.150	0.027	5	0
UW 212221	1/15/2024 14:10	1/15/2024 14:20	0.150	0.028	5	0
UW 212221	1/15/2024 14:20	1/15/2024 14:30	0.150	0.028	5	0
UW 212221	1/15/2024 14:30	1/15/2024 14:40	0.150	0.029	5	0
UW 212221	1/15/2024 14:40	1/15/2024 14:50	0.150	0.03	5	0
UW 212221	1/15/2024 14:50	1/15/2024 15:00	0.150	0.03	5	0
UW 212221	1/15/2024 15:00	1/15/2024 15:10	0.150	0.032	5	0
UW 212221	1/15/2024 15:10	1/15/2024 15:20	0.150	0.032	5	0
UW 212221	1/15/2024 15:20	1/15/2024 15:30	0.150	0.032	5	0
UW 212221	1/15/2024 15:30	1/15/2024 15:40	0.150	0.032	5	0
UW 212221	1/15/2024 15:40	1/15/2024 15:50	0.150	0.032	5	0
UW 212221	1/15/2024 15:50	1/15/2024 16:00	0.150	0.032	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/15/2024 8:00	1/15/2024 8:10	0.150	0.006	5	0
PER1 50057	1/15/2024 8:10	1/15/2024 8:20	0.150	0.007	5	0
PER1 50057	1/15/2024 8:20	1/15/2024 8:30	0.150	0.007	5	0
PER1 50057	1/15/2024 8:30	1/15/2024 8:40	0.150	0.008	5	0
PER1 50057	1/15/2024 8:40	1/15/2024 8:50	0.150	0.009	5	0
PER1 50057	1/15/2024 8:50	1/15/2024 9:00	0.150	0.01	5	0
PER1 50057	1/15/2024 9:00	1/15/2024 9:10	0.150	0.011	5	0
PER1 50057	1/15/2024 9:10	1/15/2024 9:20	0.150	0.012	5	0
PER1 50057	1/15/2024 9:20	1/15/2024 9:30	0.150	0.012	5	0
PER1 50057	1/15/2024 9:30	1/15/2024 9:40	0.150	0.013	5	0
PER1 50057	1/15/2024 9:40	1/15/2024 9:50	0.150	0.014	5	0
PER1 50057	1/15/2024 9:50	1/15/2024 10:00	0.150	0.015	5	0
PER1 50057	1/15/2024 10:00	1/15/2024 10:10	0.150	0.015	5	0
PER1 50057	1/15/2024 10:10	1/15/2024 10:20	0.150	0.016	5	0
PER1 50057	1/15/2024 10:20	1/15/2024 10:30	0.150	0.016	5	0
PER1 50057	1/15/2024 10:30	1/15/2024 10:40	0.150	0.017	5	0
PER1 50057	1/15/2024 10:40	1/15/2024 10:50	0.150	0.018	5	0
PER1 50057	1/15/2024 10:50	1/15/2024 11:00	0.150	0.018	5	0
PER1 50057	1/15/2024 11:00	1/15/2024 11:10	0.150	0.019	5	0
PER1 50057	1/15/2024 11:10	1/15/2024 11:20	0.150	0.019	5	0
PER1 50057	1/15/2024 11:20	1/15/2024 11:30	0.150	0.02	5	0
PER1 50057	1/15/2024 11:30	1/15/2024 11:40	0.150	0.021	5	0
PER1 50057	1/15/2024 11:40	1/15/2024 11:50	0.150	0.021	5	0
PER1 50057	1/15/2024 11:50	1/15/2024 12:00	0.150	0.022	5	0
PER1 50057	1/15/2024 12:00	1/15/2024 12:10	0.150	0.023	5	0
PER1 50057	1/15/2024 12:10	1/15/2024 12:20	0.150	0.023	5	0
PER1 50057	1/15/2024 12:20	1/15/2024 12:30	0.150	0.023	5	0
PER1 50057	1/15/2024 12:30	1/15/2024 12:40	0.150	0.023	5	0
PER1 50057	1/15/2024 12:40	1/15/2024 12:50	0.150	0.023	5	0
PER1 50057	1/15/2024 12:50	1/15/2024 13:00	0.150	0.023	5	0
PER1 50057	1/15/2024 13:00	1/15/2024 13:10	0.150	0.027	5	0
PER1 50057	1/15/2024 13:10	1/15/2024 13:20	0.150	0.027	5	0
PER1 50057	1/15/2024 13:20	1/15/2024 13:30	0.150	0.028	5	0
PER1 50057	1/15/2024 13:30	1/15/2024 13:40	0.150	0.028	5	0
PER1 50057	1/15/2024 13:40	1/15/2024 13:50	0.150	0.029	5	0
PER1 50057	1/15/2024 13:50	1/15/2024 14:00	0.150	0.03	5	0
PER1 50057	1/15/2024 14:00	1/15/2024 14:10	0.150	0.03	5	0
PER1 50057	1/15/2024 14:10	1/15/2024 14:20	0.150	0.031	5	0
PER1 50057	1/15/2024 14:20	1/15/2024 14:30	0.150	0.032	5	0
PER1 50057	1/15/2024 14:30	1/15/2024 14:40	0.150	0.032	5	0
PER1 50057	1/15/2024 14:40	1/15/2024 14:50	0.150	0.033	5	0
PER1 50057	1/15/2024 14:50	1/15/2024 15:00	0.150	0.034	5	0
PER1 50057	1/15/2024 15:00	1/15/2024 15:10	0.150	0.035	5	0
PER1 50057	1/15/2024 15:10	1/15/2024 15:20	0.150	0.035	5	0
PER1 50057	1/15/2024 15:20	1/15/2024 15:30	0.150	0.035	5	0
PER1 50057	1/15/2024 15:30	1/15/2024 15:40	0.150	0.035	5	0
PER1 50057	1/15/2024 15:40	1/15/2024 15:50	0.150	0.035	5	0
PER1 50057	1/15/2024 15:50	1/15/2024 16:00	0.150	0.035	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/15/2024 8:00	1/15/2024 8:10	0.150	0.003	5	0
PER2 46495	1/15/2024 8:10	1/15/2024 8:20	0.150	0.003	5	0
PER2 46495	1/15/2024 8:20	1/15/2024 8:30	0.150	0.004	5	0
PER2 46495	1/15/2024 8:30	1/15/2024 8:40	0.150	0.005	5	0
PER2 46495	1/15/2024 8:40	1/15/2024 8:50	0.150	0.005	5	0
PER2 46495	1/15/2024 8:50	1/15/2024 9:00	0.150	0.006	5	0
PER2 46495	1/15/2024 9:00	1/15/2024 9:10	0.150	0.007	5	0
PER2 46495	1/15/2024 9:10	1/15/2024 9:20	0.150	0.007	5	0
PER2 46495	1/15/2024 9:20	1/15/2024 9:30	0.150	0.008	5	0
PER2 46495	1/15/2024 9:30	1/15/2024 9:40	0.150	0.009	5	0
PER2 46495	1/15/2024 9:40	1/15/2024 9:50	0.150	0.009	5	0
PER2 46495	1/15/2024 9:50	1/15/2024 10:00	0.150	0.01	5	0
PER2 46495	1/15/2024 10:00	1/15/2024 10:10	0.150	0.01	5	0
PER2 46495	1/15/2024 10:10	1/15/2024 10:20	0.150	0.011	5	0
PER2 46495	1/15/2024 10:20	1/15/2024 10:30	0.150	0.012	5	0
PER2 46495	1/15/2024 10:30	1/15/2024 10:40	0.150	0.012	5	0
PER2 46495	1/15/2024 10:40	1/15/2024 10:50	0.150	0.013	5	0
PER2 46495	1/15/2024 10:50	1/15/2024 11:00	0.150	0.013	5	0
PER2 46495	1/15/2024 11:00	1/15/2024 11:10	0.150	0.014	5	0
PER2 46495	1/15/2024 11:10	1/15/2024 11:20	0.150	0.014	5	0
PER2 46495	1/15/2024 11:20	1/15/2024 11:30	0.150	0.015	5	0
PER2 46495	1/15/2024 11:30	1/15/2024 11:40	0.150	0.015	5	0
PER2 46495	1/15/2024 11:40	1/15/2024 11:50	0.150	0.016	5	0
PER2 46495	1/15/2024 11:50	1/15/2024 12:00	0.150	0.017	5	0
PER2 46495	1/15/2024 12:00	1/15/2024 12:10	0.150	0.017	5	0
PER2 46495	1/15/2024 12:10	1/15/2024 12:20	0.150	0.018	5	0
PER2 46495	1/15/2024 12:20	1/15/2024 12:30	0.150	0.018	5	0
PER2 46495	1/15/2024 12:30	1/15/2024 12:40	0.150	0.019	5	0
PER2 46495	1/15/2024 12:40	1/15/2024 12:50	0.150	0.019	5	0
PER2 46495	1/15/2024 12:50	1/15/2024 13:00	0.150	0.02	5	0
PER2 46495	1/15/2024 13:00	1/15/2024 13:10	0.150	0.02	5	0
PER2 46495	1/15/2024 13:10	1/15/2024 13:20	0.150	0.021	5	0
PER2 46495	1/15/2024 13:20	1/15/2024 13:30	0.150	0.022	5	0
PER2 46495	1/15/2024 13:30	1/15/2024 13:40	0.150	0.022	5	0
PER2 46495	1/15/2024 13:40	1/15/2024 13:50	0.150	0.023	5	0
PER2 46495	1/15/2024 13:50	1/15/2024 14:00	0.150	0.023	5	0
PER2 46495	1/15/2024 14:00	1/15/2024 14:10	0.150	0.024	5	0
PER2 46495	1/15/2024 14:10	1/15/2024 14:20	0.150	0.024	5	0
PER2 46495	1/15/2024 14:20	1/15/2024 14:30	0.150	0.025	5	0
PER2 46495	1/15/2024 14:30	1/15/2024 14:40	0.150	0.025	5	0
PER2 46495	1/15/2024 14:40	1/15/2024 14:50	0.150	0.026	5	0
PER2 46495	1/15/2024 14:50	1/15/2024 15:00	0.150	0.027	5	0
PER2 46495	1/15/2024 15:00	1/15/2024 15:10	0.150	0.027	5	0
PER2 46495	1/15/2024 15:10	1/15/2024 15:20	0.150	0.028	5	0
PER2 46495	1/15/2024 15:20	1/15/2024 15:30	0.150	0.028	5	0
PER2 46495	1/15/2024 15:30	1/15/2024 15:40	0.150	0.028	5	0
PER2 46495	1/15/2024 15:40	1/15/2024 15:50	0.150	0.028	5	0
PER2 46495	1/15/2024 15:50	1/15/2024 16:00	0.150	0.028	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/16/2024

Weather: 20 deg. F, Snow/rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

1) Alba continues excavation, drilling piles and installing SOE in A3 building location.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to mix of snow and rain.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

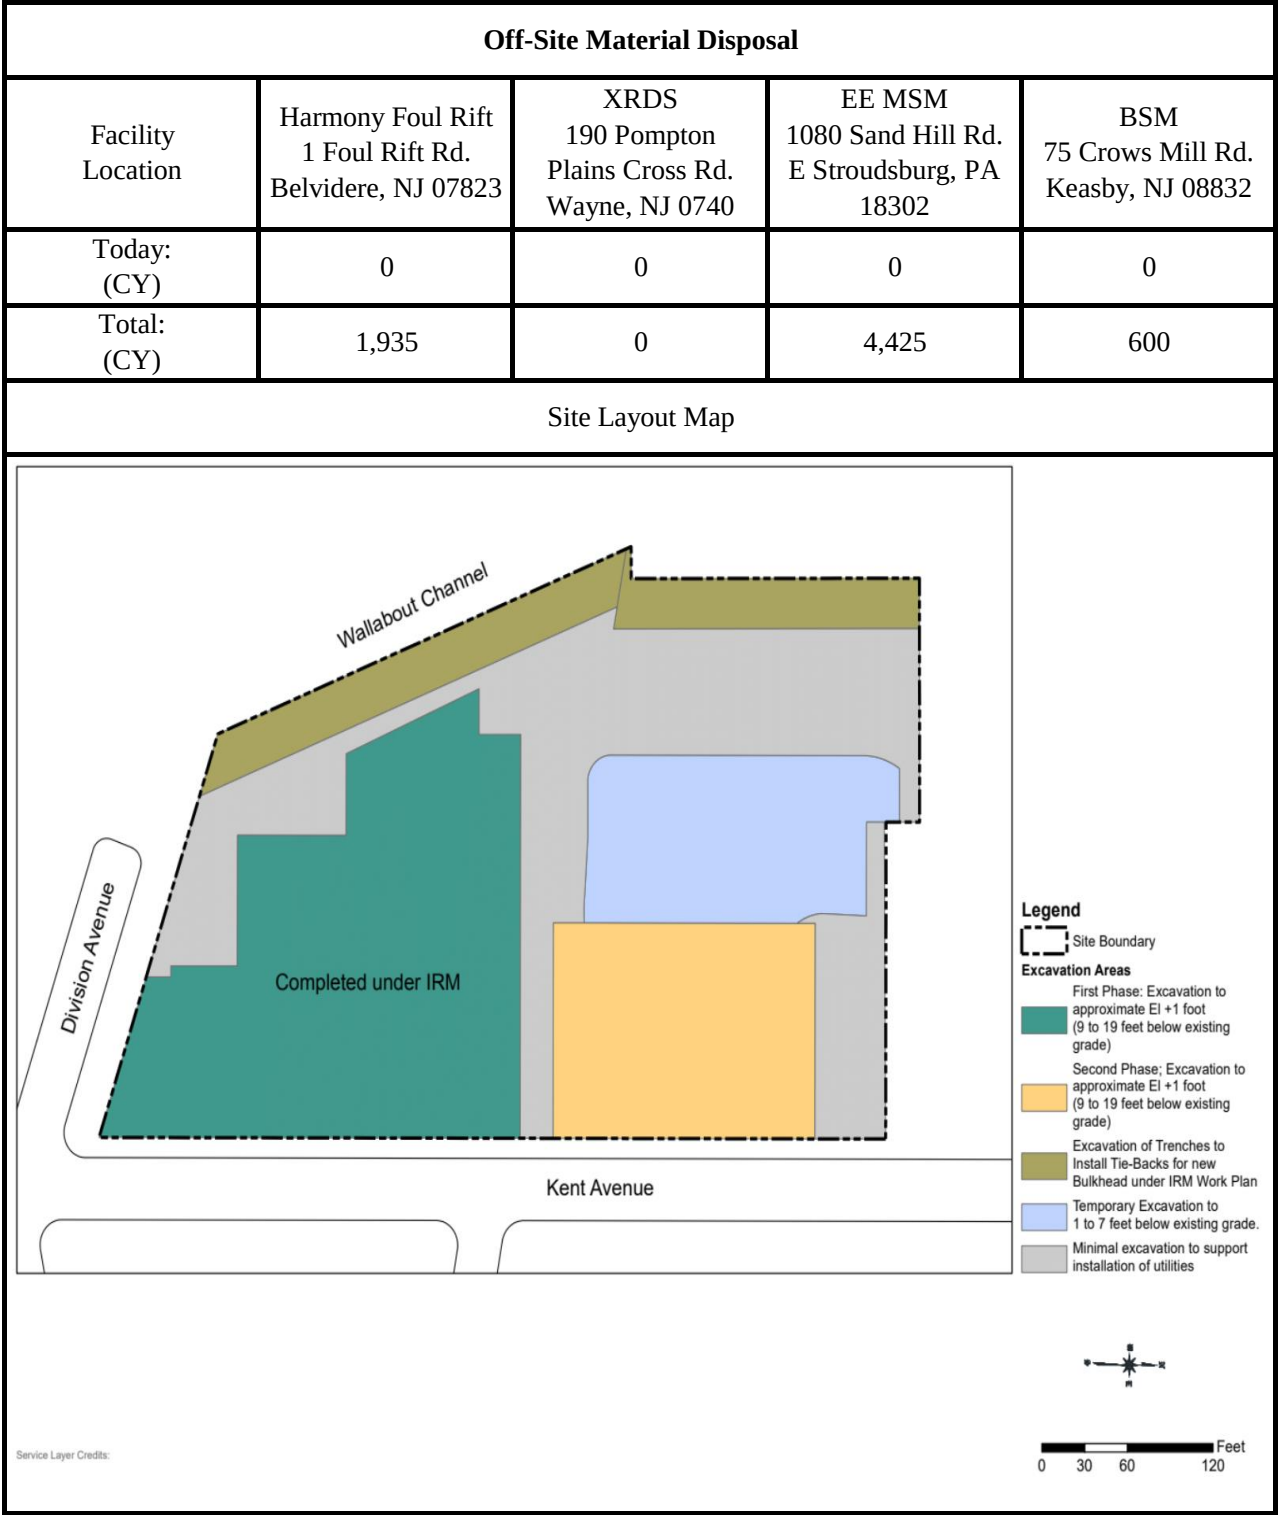


Photo 1:

View of soil excavation, pile installation and site conditions facing south.



Photo 2:

View of drilling and site conditions facing southeast.



Photo 3:

View of SOE
installation and Site
conditions facing
east.



Photo 4:

View of marine water
front area facing
north.



CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/17/2024

Weather: 25 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Export of 21 loads (approximately 420 CY) of material from WC-25 and 27 for off-site disposal at the HFR facility.
- 3) Import of 1 load of 2.5" stone to refresh trucking pad along Kent Avenue.
- 4) Tenen submitted the Notice to Commence groundwater treatment on Monday January 22, 2024 to the NYSDEC Department of Water.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

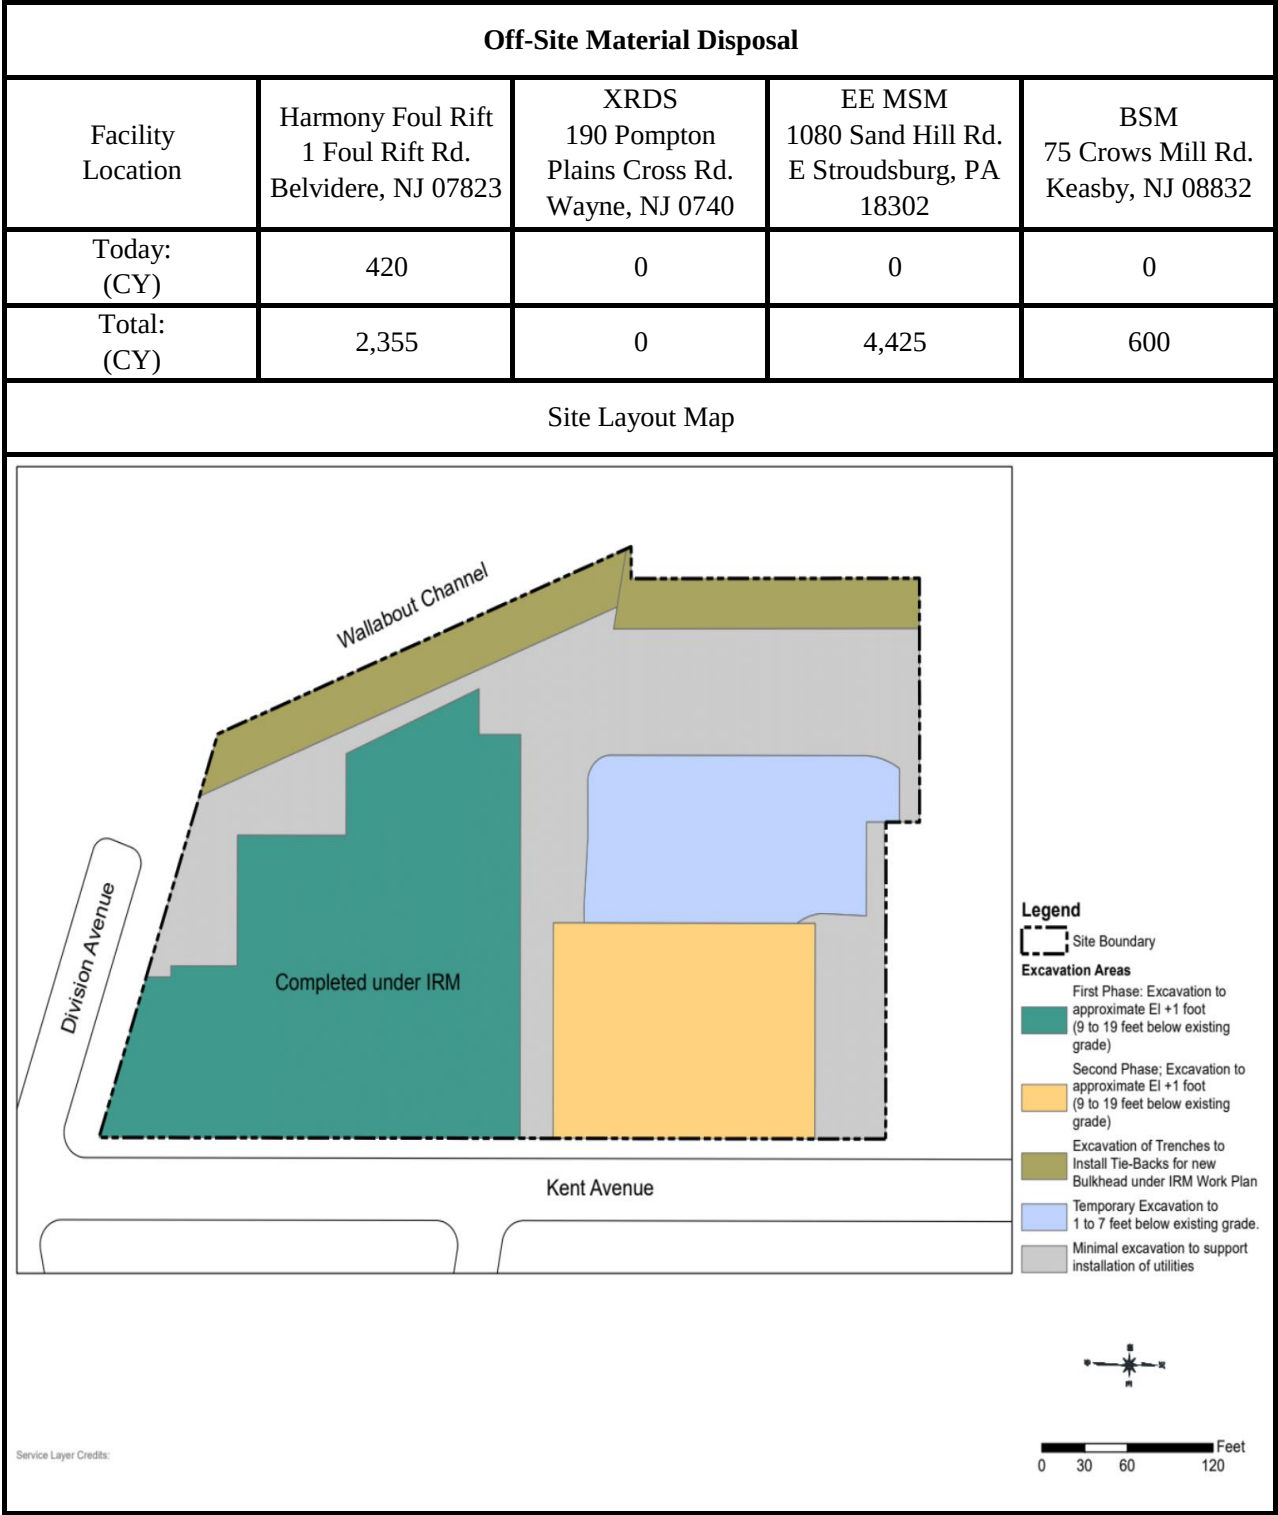


Photo 1:

View of soil excavation, pile installation and truck loading for off-site soil disposal facing southeast.



Photo 2:

View of drilling and site conditions facing north.



Photo 3:

View of truck loading for off-site soil disposal and Site conditions facing east.



Photo 4:


View of truck loading for off-site soil disposal and Site conditions facing north.



CAMP:
Downwind
Particulates

Dust Levels


0.015 mg/m³ 0.019 mg/m³ 0.15

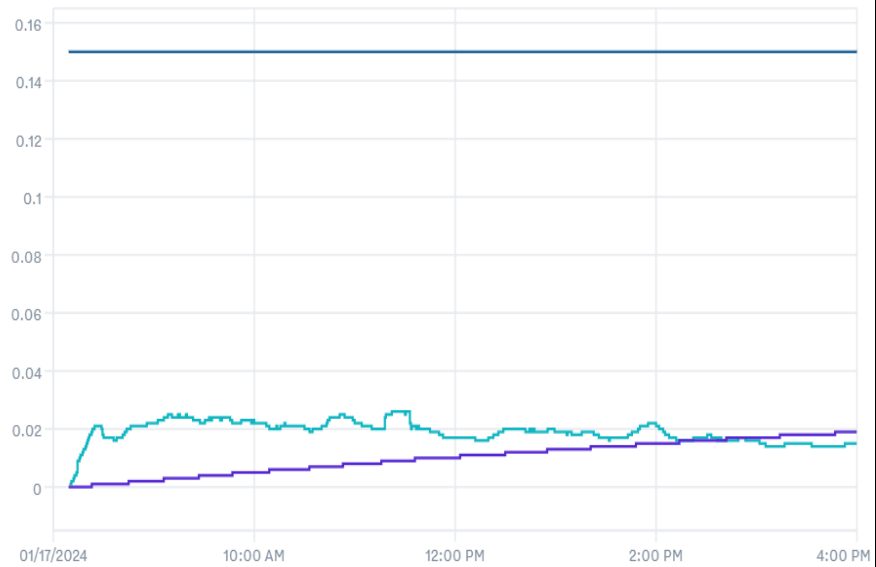


CAMP:
Downwind VOCs

VOC Levels

0 ppm 0 ppm 5

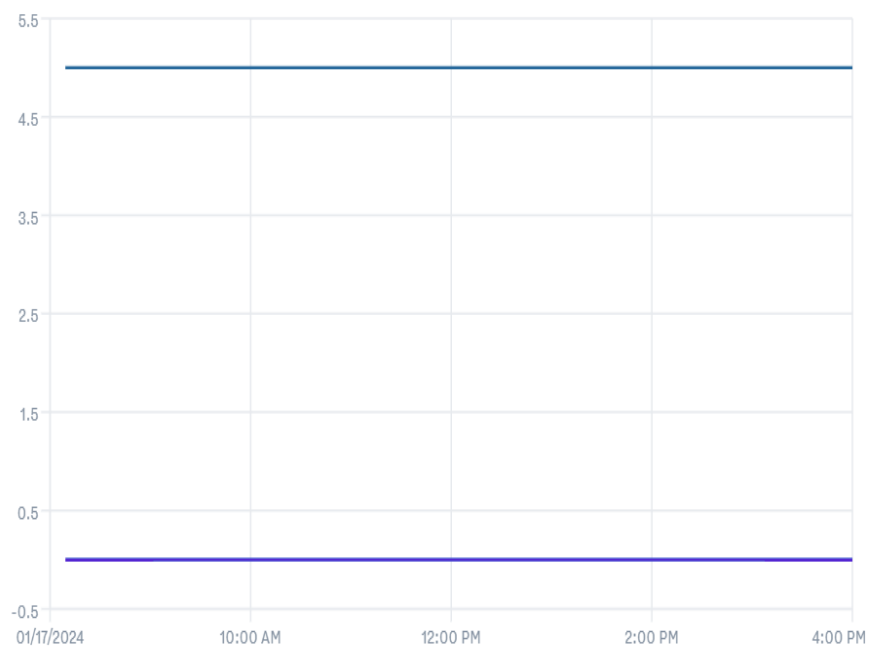

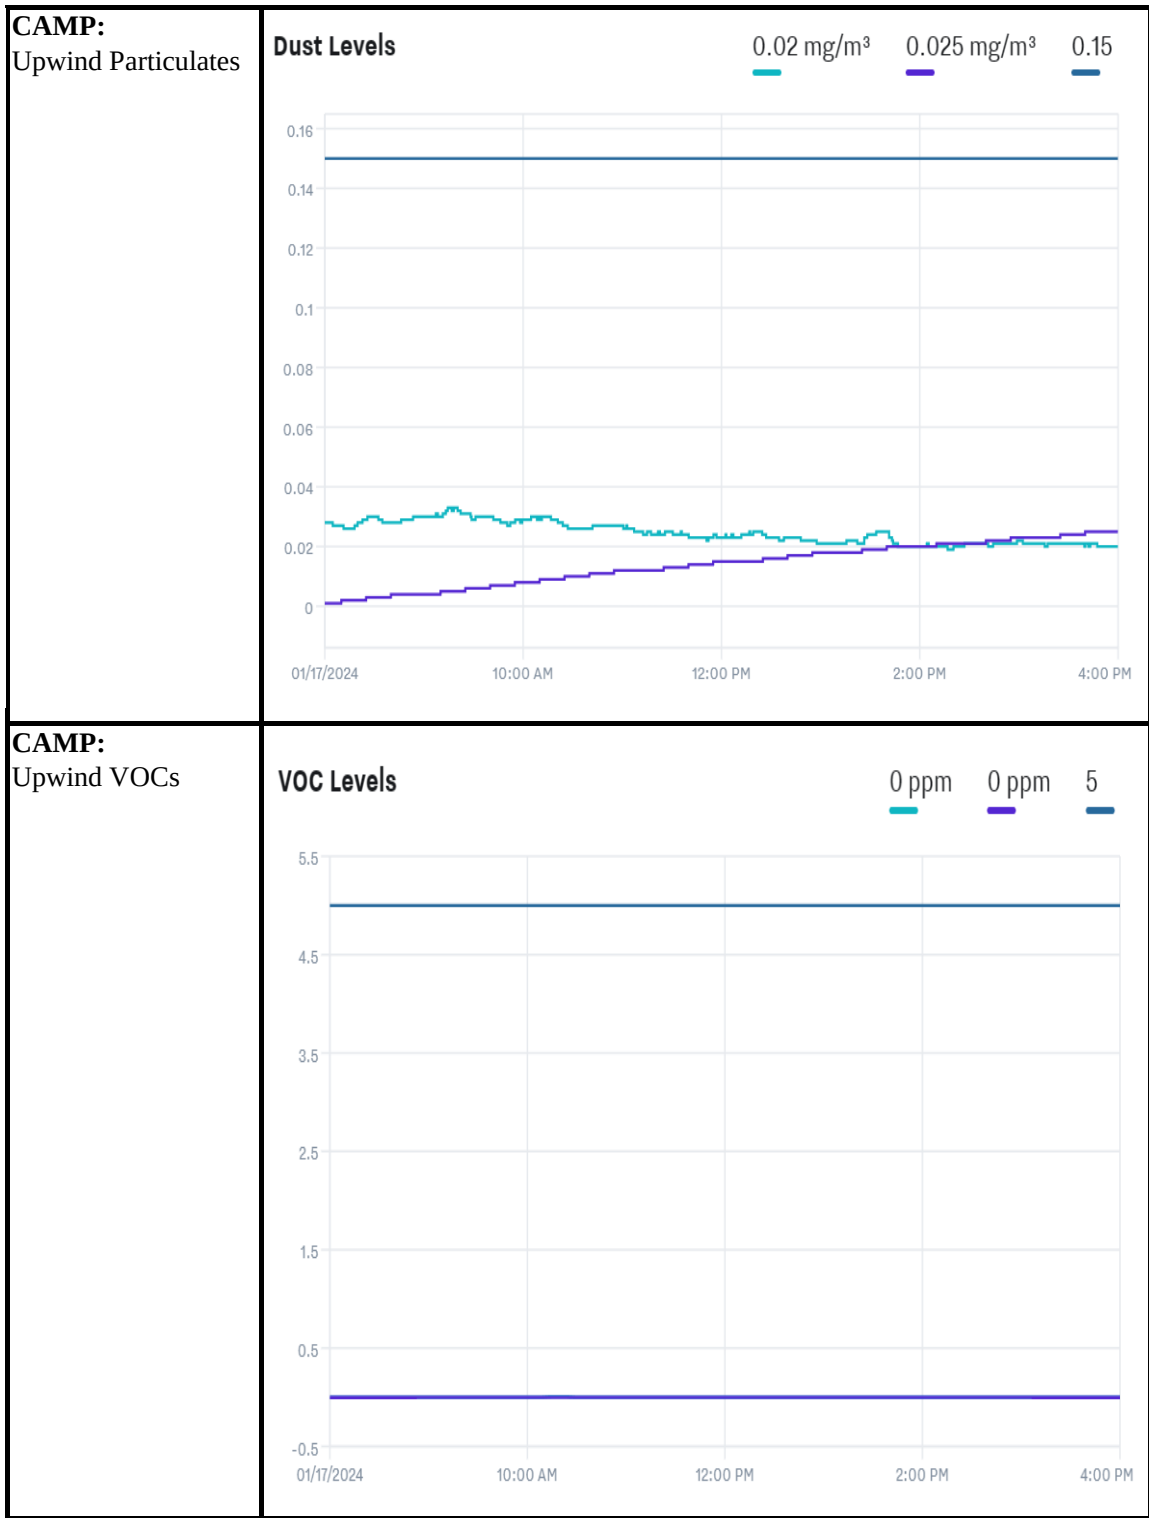

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/17/2024 8:00	1/17/2024 8:10	0.150	0	5	0
DW 47907	1/17/2024 8:10	1/17/2024 8:20	0.150	0	5	0
DW 47907	1/17/2024 8:20	1/17/2024 8:30	0.150	0.001	5	0
DW 47907	1/17/2024 8:30	1/17/2024 8:40	0.150	0.001	5	0
DW 47907	1/17/2024 8:40	1/17/2024 8:50	0.150	0.002	5	0
DW 47907	1/17/2024 8:50	1/17/2024 9:00	0.150	0.002	5	0
DW 47907	1/17/2024 9:00	1/17/2024 9:10	0.150	0.003	5	0
DW 47907	1/17/2024 9:10	1/17/2024 9:20	0.150	0.003	5	0
DW 47907	1/17/2024 9:20	1/17/2024 9:30	0.150	0.004	5	0
DW 47907	1/17/2024 9:30	1/17/2024 9:40	0.150	0.004	5	0
DW 47907	1/17/2024 9:40	1/17/2024 9:50	0.150	0.005	5	0
DW 47907	1/17/2024 9:50	1/17/2024 10:00	0.150	0.005	5	0
DW 47907	1/17/2024 10:00	1/17/2024 10:10	0.150	0.006	5	0
DW 47907	1/17/2024 10:10	1/17/2024 10:20	0.150	0.006	5	0
DW 47907	1/17/2024 10:20	1/17/2024 10:30	0.150	0.006	5	0
DW 47907	1/17/2024 10:30	1/17/2024 10:40	0.150	0.007	5	0
DW 47907	1/17/2024 10:40	1/17/2024 10:50	0.150	0.007	5	0
DW 47907	1/17/2024 10:50	1/17/2024 11:00	0.150	0.008	5	0
DW 47907	1/17/2024 11:00	1/17/2024 11:10	0.150	0.008	5	0
DW 47907	1/17/2024 11:10	1/17/2024 11:20	0.150	0.009	5	0
DW 47907	1/17/2024 11:20	1/17/2024 11:30	0.150	0.009	5	0
DW 47907	1/17/2024 11:30	1/17/2024 11:40	0.150	0.01	5	0
DW 47907	1/17/2024 11:40	1/17/2024 11:50	0.150	0.01	5	0
DW 47907	1/17/2024 11:50	1/17/2024 12:00	0.150	0.01	5	0
DW 47907	1/17/2024 12:00	1/17/2024 12:10	0.150	0.011	5	0
DW 47907	1/17/2024 12:10	1/17/2024 12:20	0.150	0.011	5	0
DW 47907	1/17/2024 12:20	1/17/2024 12:30	0.150	0.012	5	0
DW 47907	1/17/2024 12:30	1/17/2024 12:40	0.150	0.012	5	0
DW 47907	1/17/2024 12:40	1/17/2024 12:50	0.150	0.012	5	0
DW 47907	1/17/2024 12:50	1/17/2024 13:00	0.150	0.013	5	0
DW 47907	1/17/2024 13:00	1/17/2024 13:10	0.150	0.013	5	0
DW 47907	1/17/2024 13:10	1/17/2024 13:20	0.150	0.013	5	0
DW 47907	1/17/2024 13:20	1/17/2024 13:30	0.150	0.014	5	0
DW 47907	1/17/2024 13:30	1/17/2024 13:40	0.150	0.014	5	0
DW 47907	1/17/2024 13:40	1/17/2024 13:50	0.150	0.015	5	0
DW 47907	1/17/2024 13:50	1/17/2024 14:00	0.150	0.015	5	0
DW 47907	1/17/2024 14:00	1/17/2024 14:10	0.150	0.015	5	0
DW 47907	1/17/2024 14:10	1/17/2024 14:20	0.150	0.016	5	0
DW 47907	1/17/2024 14:20	1/17/2024 14:30	0.150	0.016	5	0
DW 47907	1/17/2024 14:30	1/17/2024 14:40	0.150	0.016	5	0
DW 47907	1/17/2024 14:40	1/17/2024 14:50	0.150	0.017	5	0
DW 47907	1/17/2024 14:50	1/17/2024 15:00	0.150	0.017	5	0
DW 47907	1/17/2024 15:00	1/17/2024 15:10	0.150	0.017	5	0
DW 47907	1/17/2024 15:10	1/17/2024 15:20	0.150	0.018	5	0
DW 47907	1/17/2024 15:20	1/17/2024 15:30	0.150	0.018	5	0
DW 47907	1/17/2024 15:30	1/17/2024 15:40	0.150	0.018	5	0
DW 47907	1/17/2024 15:40	1/17/2024 15:50	0.150	0.019	5	0
DW 47907	1/17/2024 15:50	1/17/2024 16:00	0.150	0.019	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/17/2024 8:00	1/17/2024 8:10	0.150	0.002	5	0
UW 212221	1/17/2024 8:10	1/17/2024 8:20	0.150	0.002	5	0
UW 212221	1/17/2024 8:20	1/17/2024 8:30	0.150	0.003	5	0
UW 212221	1/17/2024 8:30	1/17/2024 8:40	0.150	0.003	5	0
UW 212221	1/17/2024 8:40	1/17/2024 8:50	0.150	0.004	5	0
UW 212221	1/17/2024 8:50	1/17/2024 9:00	0.150	0.004	5	0
UW 212221	1/17/2024 9:00	1/17/2024 9:10	0.150	0.005	5	0
UW 212221	1/17/2024 9:10	1/17/2024 9:20	0.150	0.005	5	0
UW 212221	1/17/2024 9:20	1/17/2024 9:30	0.150	0.006	5	0
UW 212221	1/17/2024 9:30	1/17/2024 9:40	0.150	0.006	5	0
UW 212221	1/17/2024 9:40	1/17/2024 9:50	0.150	0.007	5	0
UW 212221	1/17/2024 9:50	1/17/2024 10:00	0.150	0.008	5	0
UW 212221	1/17/2024 10:00	1/17/2024 10:10	0.150	0.008	5	0
UW 212221	1/17/2024 10:10	1/17/2024 10:20	0.150	0.009	5	0
UW 212221	1/17/2024 10:20	1/17/2024 10:30	0.150	0.01	5	0
UW 212221	1/17/2024 10:30	1/17/2024 10:40	0.150	0.01	5	0
UW 212221	1/17/2024 10:40	1/17/2024 10:50	0.150	0.011	5	0
UW 212221	1/17/2024 10:50	1/17/2024 11:00	0.150	0.012	5	0
UW 212221	1/17/2024 11:00	1/17/2024 11:10	0.150	0.012	5	0
UW 212221	1/17/2024 11:10	1/17/2024 11:20	0.150	0.012	5	0
UW 212221	1/17/2024 11:20	1/17/2024 11:30	0.150	0.013	5	0
UW 212221	1/17/2024 11:30	1/17/2024 11:40	0.150	0.013	5	0
UW 212221	1/17/2024 11:40	1/17/2024 11:50	0.150	0.014	5	0
UW 212221	1/17/2024 11:50	1/17/2024 12:00	0.150	0.015	5	0
UW 212221	1/17/2024 12:00	1/17/2024 12:10	0.150	0.015	5	0
UW 212221	1/17/2024 12:10	1/17/2024 12:20	0.150	0.015	5	0
UW 212221	1/17/2024 12:20	1/17/2024 12:30	0.150	0.016	5	0
UW 212221	1/17/2024 12:30	1/17/2024 12:40	0.150	0.016	5	0
UW 212221	1/17/2024 12:40	1/17/2024 12:50	0.150	0.017	5	0
UW 212221	1/17/2024 12:50	1/17/2024 13:00	0.150	0.018	5	0
UW 212221	1/17/2024 13:00	1/17/2024 13:10	0.150	0.018	5	0
UW 212221	1/17/2024 13:10	1/17/2024 13:20	0.150	0.018	5	0
UW 212221	1/17/2024 13:20	1/17/2024 13:30	0.150	0.019	5	0
UW 212221	1/17/2024 13:30	1/17/2024 13:40	0.150	0.019	5	0
UW 212221	1/17/2024 13:40	1/17/2024 13:50	0.150	0.02	5	0
UW 212221	1/17/2024 13:50	1/17/2024 14:00	0.150	0.02	5	0
UW 212221	1/17/2024 14:00	1/17/2024 14:10	0.150	0.02	5	0
UW 212221	1/17/2024 14:10	1/17/2024 14:20	0.150	0.021	5	0
UW 212221	1/17/2024 14:20	1/17/2024 14:30	0.150	0.021	5	0
UW 212221	1/17/2024 14:30	1/17/2024 14:40	0.150	0.021	5	0
UW 212221	1/17/2024 14:40	1/17/2024 14:50	0.150	0.022	5	0
UW 212221	1/17/2024 14:50	1/17/2024 15:00	0.150	0.023	5	0
UW 212221	1/17/2024 15:00	1/17/2024 15:10	0.150	0.023	5	0
UW 212221	1/17/2024 15:10	1/17/2024 15:20	0.150	0.023	5	0
UW 212221	1/17/2024 15:20	1/17/2024 15:30	0.150	0.024	5	0
UW 212221	1/17/2024 15:30	1/17/2024 15:40	0.150	0.024	5	0
UW 212221	1/17/2024 15:40	1/17/2024 15:50	0.150	0.025	5	0
UW 212221	1/17/2024 15:50	1/17/2024 16:00	0.150	0.025	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/17/2024 8:00	1/17/2024 8:10	0.150	0.004	5	0
PER1 50057	1/17/2024 8:10	1/17/2024 8:20	0.150	0.004	5	0
PER1 50057	1/17/2024 8:20	1/17/2024 8:30	0.150	0.005	5	0
PER1 50057	1/17/2024 8:30	1/17/2024 8:40	0.150	0.006	5	0
PER1 50057	1/17/2024 8:40	1/17/2024 8:50	0.150	0.007	5	0
PER1 50057	1/17/2024 8:50	1/17/2024 9:00	0.150	0.008	5	0
PER1 50057	1/17/2024 9:00	1/17/2024 9:10	0.150	0.009	5	0
PER1 50057	1/17/2024 9:10	1/17/2024 9:20	0.150	0.01	5	0
PER1 50057	1/17/2024 9:20	1/17/2024 9:30	0.150	0.011	5	0
PER1 50057	1/17/2024 9:30	1/17/2024 9:40	0.150	0.011	5	0
PER1 50057	1/17/2024 9:40	1/17/2024 9:50	0.150	0.012	5	0
PER1 50057	1/17/2024 9:50	1/17/2024 10:00	0.150	0.013	5	0
PER1 50057	1/17/2024 10:00	1/17/2024 10:10	0.150	0.014	5	0
PER1 50057	1/17/2024 10:10	1/17/2024 10:20	0.150	0.014	5	0
PER1 50057	1/17/2024 10:20	1/17/2024 10:30	0.150	0.015	5	0
PER1 50057	1/17/2024 10:30	1/17/2024 10:40	0.150	0.015	5	0
PER1 50057	1/17/2024 10:40	1/17/2024 10:50	0.150	0.016	5	0
PER1 50057	1/17/2024 10:50	1/17/2024 11:00	0.150	0.017	5	0
PER1 50057	1/17/2024 11:00	1/17/2024 11:10	0.150	0.017	5	0
PER1 50057	1/17/2024 11:10	1/17/2024 11:20	0.150	0.018	5	0
PER1 50057	1/17/2024 11:20	1/17/2024 11:30	0.150	0.019	5	0
PER1 50057	1/17/2024 11:30	1/17/2024 11:40	0.150	0.019	5	0
PER1 50057	1/17/2024 11:40	1/17/2024 11:50	0.150	0.02	5	0
PER1 50057	1/17/2024 11:50	1/17/2024 12:00	0.150	0.021	5	0
PER1 50057	1/17/2024 12:00	1/17/2024 12:10	0.150	0.021	5	0
PER1 50057	1/17/2024 12:10	1/17/2024 12:20	0.150	0.022	5	0
PER1 50057	1/17/2024 12:20	1/17/2024 12:30	0.150	0.022	5	0
PER1 50057	1/17/2024 12:30	1/17/2024 12:40	0.150	0.023	5	0
PER1 50057	1/17/2024 12:40	1/17/2024 12:50	0.150	0.024	5	0
PER1 50057	1/17/2024 12:50	1/17/2024 13:00	0.150	0.024	5	0
PER1 50057	1/17/2024 13:00	1/17/2024 13:10	0.150	0.025	5	0
PER1 50057	1/17/2024 13:10	1/17/2024 13:20	0.150	0.026	5	0
PER1 50057	1/17/2024 13:20	1/17/2024 13:30	0.150	0.026	5	0
PER1 50057	1/17/2024 13:30	1/17/2024 13:40	0.150	0.027	5	0
PER1 50057	1/17/2024 13:40	1/17/2024 13:50	0.150	0.027	5	0
PER1 50057	1/17/2024 13:50	1/17/2024 14:00	0.150	0.028	5	0
PER1 50057	1/17/2024 14:00	1/17/2024 14:10	0.150	0.028	5	0
PER1 50057	1/17/2024 14:10	1/17/2024 14:20	0.150	0.029	5	0
PER1 50057	1/17/2024 14:20	1/17/2024 14:30	0.150	0.029	5	0
PER1 50057	1/17/2024 14:30	1/17/2024 14:40	0.150	0.03	5	0
PER1 50057	1/17/2024 14:40	1/17/2024 14:50	0.150	0.03	5	0
PER1 50057	1/17/2024 14:50	1/17/2024 15:00	0.150	0.031	5	0
PER1 50057	1/17/2024 15:00	1/17/2024 15:10	0.150	0.031	5	0
PER1 50057	1/17/2024 15:10	1/17/2024 15:20	0.150	0.032	5	0
PER1 50057	1/17/2024 15:20	1/17/2024 15:30	0.150	0.032	5	0
PER1 50057	1/17/2024 15:30	1/17/2024 15:40	0.150	0.032	5	0
PER1 50057	1/17/2024 15:40	1/17/2024 15:50	0.150	0.032	5	0
PER1 50057	1/17/2024 15:50	1/17/2024 16:00	0.150	0.032	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/17/2024 8:00	1/17/2024 8:10	0.150	0	5	0
PER2 46495	1/17/2024 8:10	1/17/2024 8:20	0.150	0	5	0
PER2 46495	1/17/2024 8:20	1/17/2024 8:30	0.150	0.002	5	0
PER2 46495	1/17/2024 8:30	1/17/2024 8:40	0.150	0.003	5	0
PER2 46495	1/17/2024 8:40	1/17/2024 8:50	0.150	0.003	5	0
PER2 46495	1/17/2024 8:50	1/17/2024 9:00	0.150	0.004	5	0
PER2 46495	1/17/2024 9:00	1/17/2024 9:10	0.150	0.005	5	0
PER2 46495	1/17/2024 9:10	1/17/2024 9:20	0.150	0.006	5	0
PER2 46495	1/17/2024 9:20	1/17/2024 9:30	0.150	0.006	5	0
PER2 46495	1/17/2024 9:30	1/17/2024 9:40	0.150	0.007	5	0
PER2 46495	1/17/2024 9:40	1/17/2024 9:50	0.150	0.008	5	0
PER2 46495	1/17/2024 9:50	1/17/2024 10:00	0.150	0.009	5	0
PER2 46495	1/17/2024 10:00	1/17/2024 10:10	0.150	0.009	5	0
PER2 46495	1/17/2024 10:10	1/17/2024 10:20	0.150	0.01	5	0
PER2 46495	1/17/2024 10:20	1/17/2024 10:30	0.150	0.011	5	0
PER2 46495	1/17/2024 10:30	1/17/2024 10:40	0.150	0.011	5	0
PER2 46495	1/17/2024 10:40	1/17/2024 10:50	0.150	0.012	5	0
PER2 46495	1/17/2024 10:50	1/17/2024 11:00	0.150	0.013	5	0
PER2 46495	1/17/2024 11:00	1/17/2024 11:10	0.150	0.014	5	0
PER2 46495	1/17/2024 11:10	1/17/2024 11:20	0.150	0.014	5	0
PER2 46495	1/17/2024 11:20	1/17/2024 11:30	0.150	0.015	5	0
PER2 46495	1/17/2024 11:30	1/17/2024 11:40	0.150	0.016	5	0
PER2 46495	1/17/2024 11:40	1/17/2024 11:50	0.150	0.016	5	0
PER2 46495	1/17/2024 11:50	1/17/2024 12:00	0.150	0.017	5	0
PER2 46495	1/17/2024 12:00	1/17/2024 12:10	0.150	0.017	5	0
PER2 46495	1/17/2024 12:10	1/17/2024 12:20	0.150	0.018	5	0
PER2 46495	1/17/2024 12:20	1/17/2024 12:30	0.150	0.019	5	0
PER2 46495	1/17/2024 12:30	1/17/2024 12:40	0.150	0.019	5	0
PER2 46495	1/17/2024 12:40	1/17/2024 12:50	0.150	0.02	5	0
PER2 46495	1/17/2024 12:50	1/17/2024 13:00	0.150	0.021	5	0
PER2 46495	1/17/2024 13:00	1/17/2024 13:10	0.150	0.021	5	0
PER2 46495	1/17/2024 13:10	1/17/2024 13:20	0.150	0.022	5	0
PER2 46495	1/17/2024 13:20	1/17/2024 13:30	0.150	0.023	5	0
PER2 46495	1/17/2024 13:30	1/17/2024 13:40	0.150	0.023	5	0
PER2 46495	1/17/2024 13:40	1/17/2024 13:50	0.150	0.024	5	0
PER2 46495	1/17/2024 13:50	1/17/2024 14:00	0.150	0.024	5	0
PER2 46495	1/17/2024 14:00	1/17/2024 14:10	0.150	0.025	5	0
PER2 46495	1/17/2024 14:10	1/17/2024 14:20	0.150	0.026	5	0
PER2 46495	1/17/2024 14:20	1/17/2024 14:30	0.150	0.026	5	0
PER2 46495	1/17/2024 14:30	1/17/2024 14:40	0.150	0.027	5	0
PER2 46495	1/17/2024 14:40	1/17/2024 14:50	0.150	0.027	5	0
PER2 46495	1/17/2024 14:50	1/17/2024 15:00	0.150	0.028	5	0
PER2 46495	1/17/2024 15:00	1/17/2024 15:10	0.150	0.028	5	0
PER2 46495	1/17/2024 15:10	1/17/2024 15:20	0.150	0.029	5	0
PER2 46495	1/17/2024 15:20	1/17/2024 15:30	0.150	0.03	5	0
PER2 46495	1/17/2024 15:30	1/17/2024 15:40	0.150	0.03	5	0
PER2 46495	1/17/2024 15:40	1/17/2024 15:50	0.150	0.031	5	0
PER2 46495	1/17/2024 15:50	1/17/2024 16:00	0.150	0.031	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/18/2024

Weather: 25 deg. F, Overcast/Snow

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Tenen's C. Zaccheo & M. Carroll on-site for Site visit.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure work; preparation to complete remedial excavation along the waterfront; continue A3 building foundation excavation and pile installation.

Off-Site Material Disposal				
Facility Location	Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	EE MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	BSM 75 Crows Mill Rd. Keasby, NJ 08832
Today: (CY)	0	0	0	0
Total: (CY)	2,355	0	4,425	600

Site Layout Map

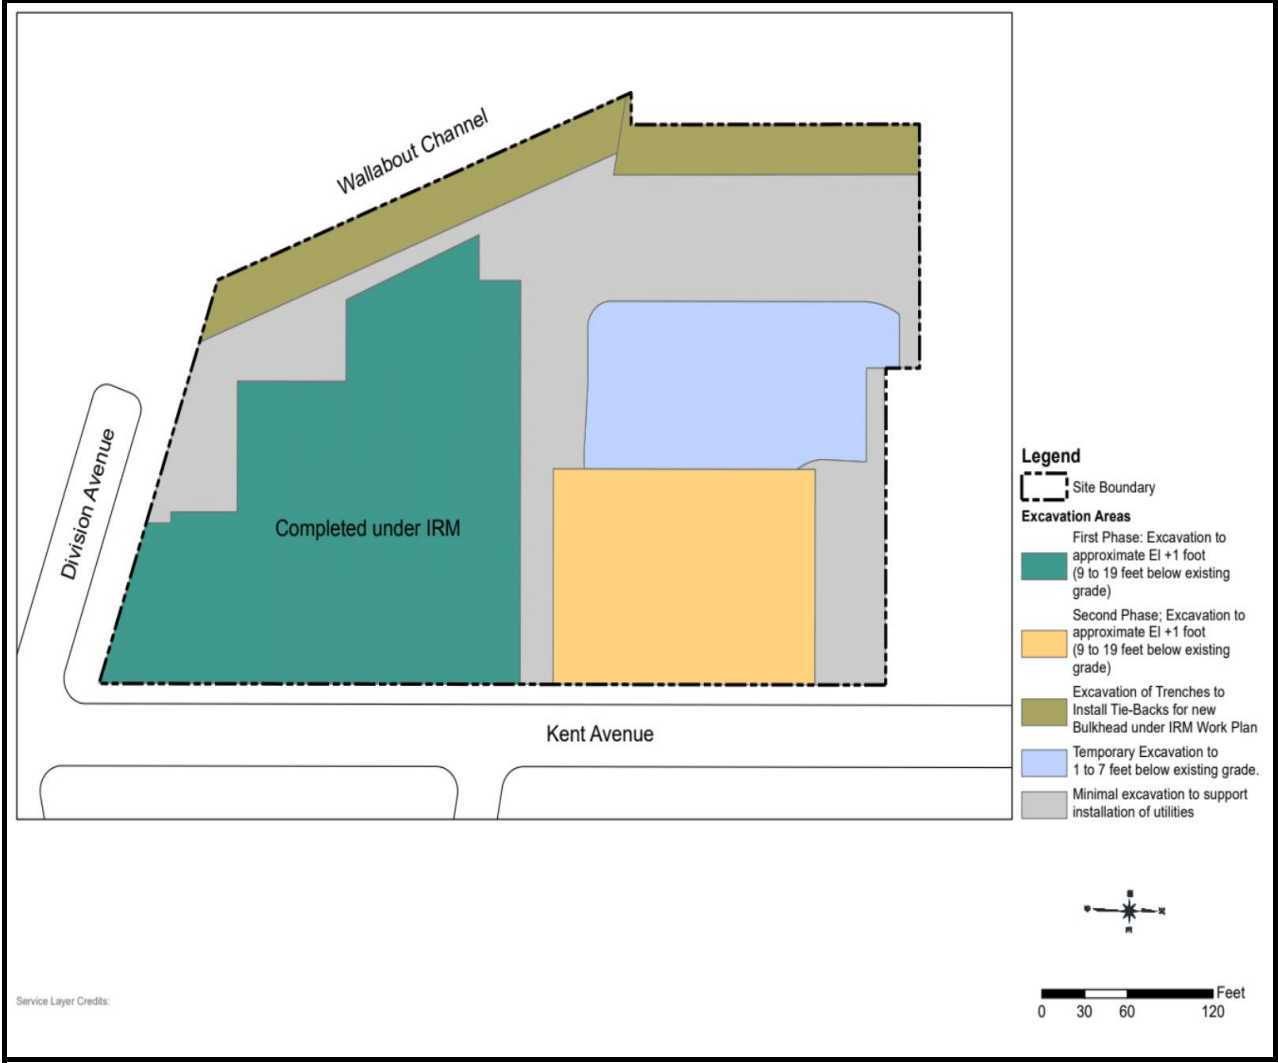


Photo 1:

View of soil excavation,
pile installation facing
northwest.



Photo 2:

View of soil excavation
and site conditions facing
west.



Photo 3:

View of Site
conditions and soil
excavation facing
north.

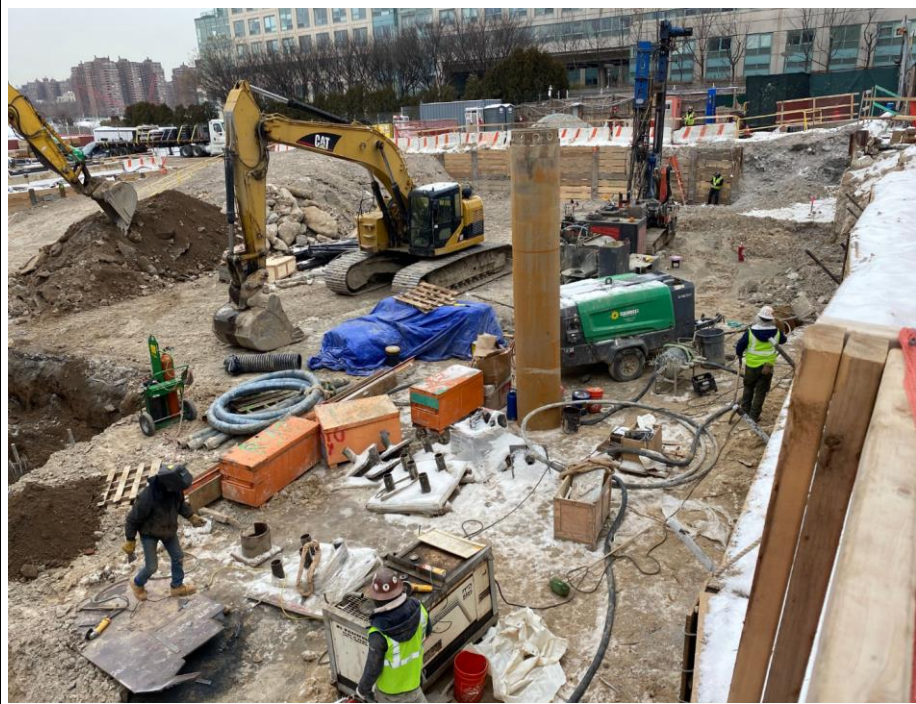


Photo 4:


View of Site
conditons and
exposed piles after
soil excavation.



CAMP:
Downwind
Particulates

Dust Levels


0.027 mg/m³ 0.018 mg/m³ 0.15

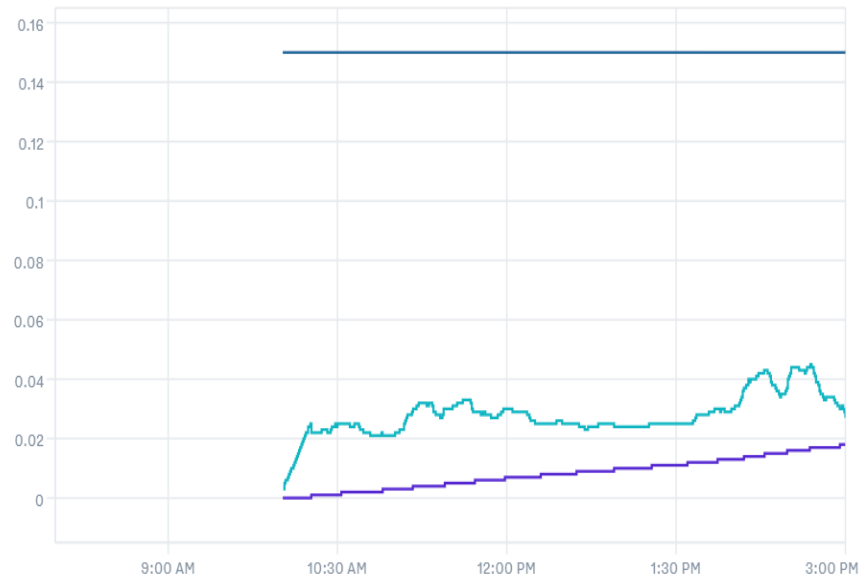


CAMP:
Downwind VOCs

VOC Levels

0 ppm 0 ppm 5

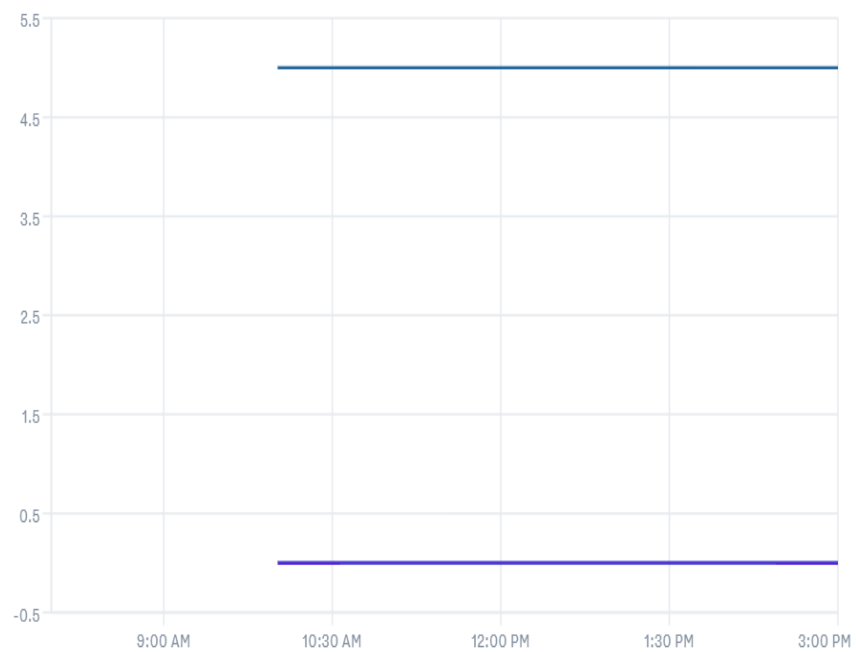

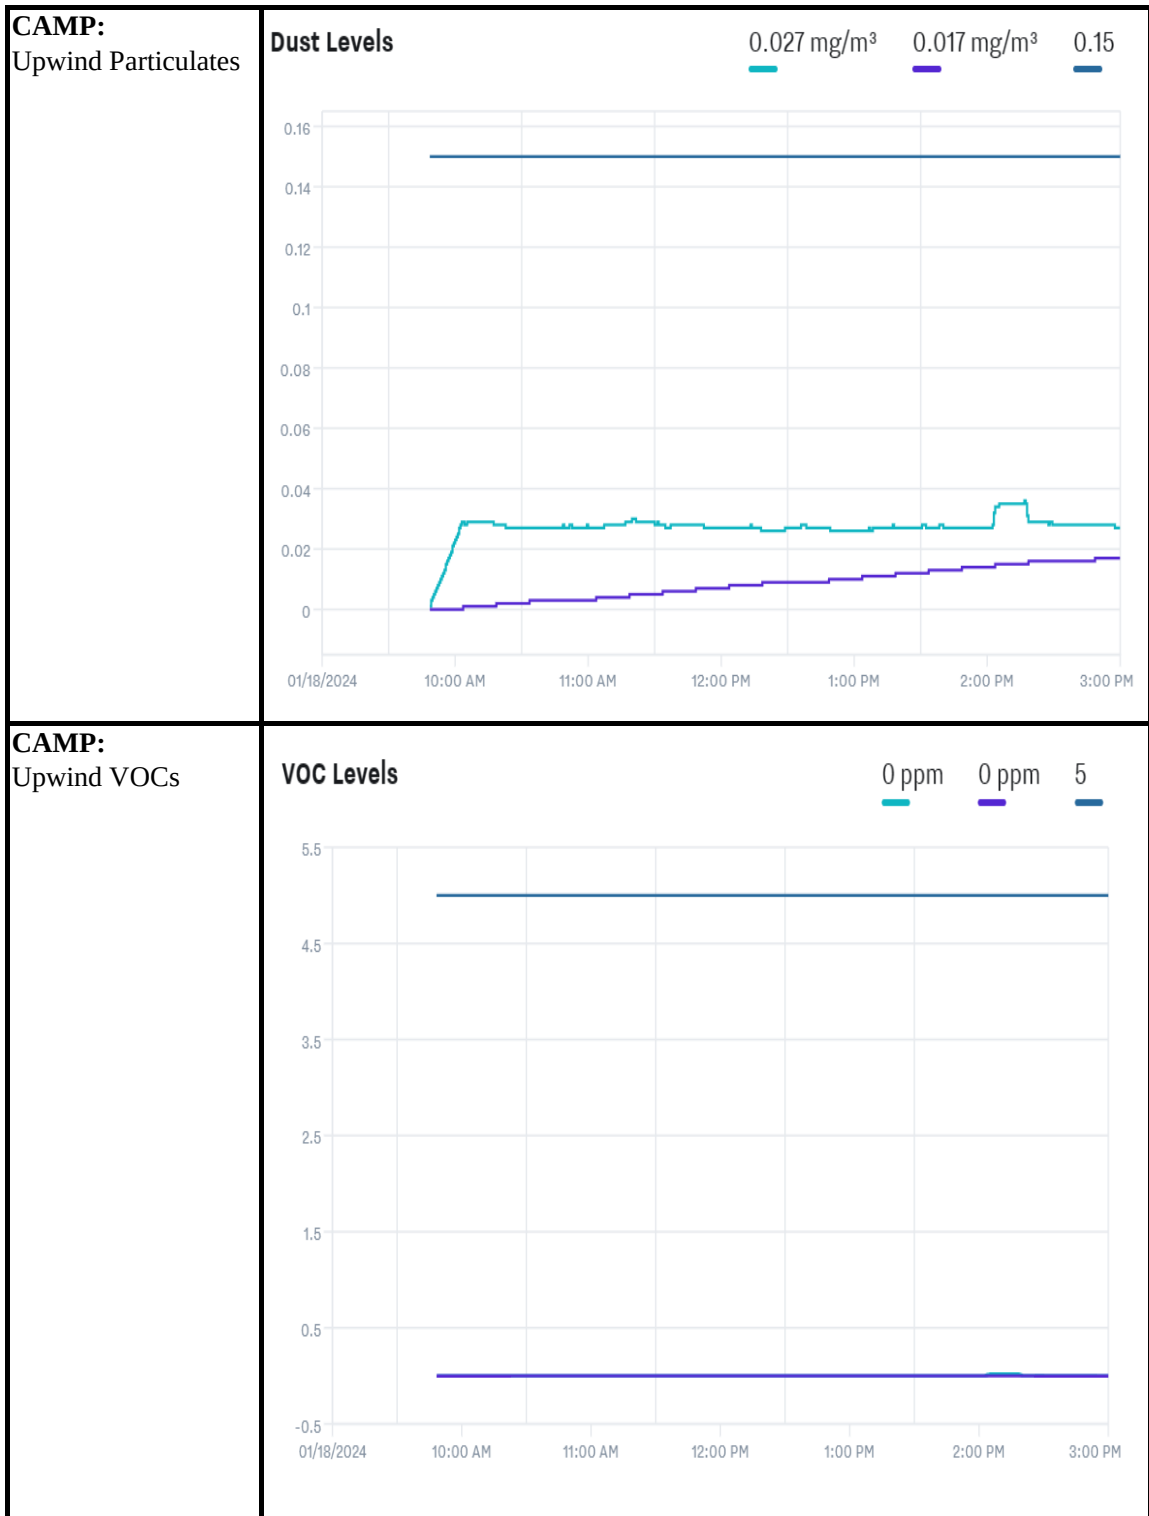

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/18/2024 8:00	1/18/2024 8:10	0.150	0.019	5	0
DW 47907	1/18/2024 8:10	1/18/2024 8:20	0.150	0.019	5	0
DW 47907	1/18/2024 8:20	1/18/2024 8:30	0.150	0.019	5	0
DW 47907	1/18/2024 8:30	1/18/2024 8:40	0.150	0.019	5	0
DW 47907	1/18/2024 8:40	1/18/2024 8:50	0.150	0.019	5	0
DW 47907	1/18/2024 8:50	1/18/2024 9:00	0.150	0.019	5	0
DW 47907	1/18/2024 9:00	1/18/2024 9:10	0.150	0.019	5	0
DW 47907	1/18/2024 9:10	1/18/2024 9:20	0.150	0.019	5	0
DW 47907	1/18/2024 9:20	1/18/2024 9:30	0.150	0.019	5	0
DW 47907	1/18/2024 9:30	1/18/2024 9:40	0.150	0.019	5	0
DW 47907	1/18/2024 9:40	1/18/2024 9:50	0.150	0.019	5	0
DW 47907	1/18/2024 9:50	1/18/2024 10:00	0.150	0.019	5	0
DW 47907	1/18/2024 10:00	1/18/2024 10:10	0.150	0	5	0
DW 47907	1/18/2024 10:10	1/18/2024 10:20	0.150	0.001	5	0
DW 47907	1/18/2024 10:20	1/18/2024 10:30	0.150	0.001	5	0
DW 47907	1/18/2024 10:30	1/18/2024 10:40	0.150	0.002	5	0
DW 47907	1/18/2024 10:40	1/18/2024 10:50	0.150	0.002	5	0
DW 47907	1/18/2024 10:50	1/18/2024 11:00	0.150	0.003	5	0
DW 47907	1/18/2024 11:00	1/18/2024 11:10	0.150	0.003	5	0
DW 47907	1/18/2024 11:10	1/18/2024 11:20	0.150	0.004	5	0
DW 47907	1/18/2024 11:20	1/18/2024 11:30	0.150	0.005	5	0
DW 47907	1/18/2024 11:30	1/18/2024 11:40	0.150	0.005	5	0
DW 47907	1/18/2024 11:40	1/18/2024 11:50	0.150	0.006	5	0
DW 47907	1/18/2024 11:50	1/18/2024 12:00	0.150	0.007	5	0
DW 47907	1/18/2024 12:00	1/18/2024 12:10	0.150	0.007	5	0
DW 47907	1/18/2024 12:10	1/18/2024 12:20	0.150	0.008	5	0
DW 47907	1/18/2024 12:20	1/18/2024 12:30	0.150	0.008	5	0
DW 47907	1/18/2024 12:30	1/18/2024 12:40	0.150	0.009	5	0
DW 47907	1/18/2024 12:40	1/18/2024 12:50	0.150	0.009	5	0
DW 47907	1/18/2024 12:50	1/18/2024 13:00	0.150	0.01	5	0
DW 47907	1/18/2024 13:00	1/18/2024 13:10	0.150	0.01	5	0
DW 47907	1/18/2024 13:10	1/18/2024 13:20	0.150	0.011	5	0
DW 47907	1/18/2024 13:20	1/18/2024 13:30	0.150	0.011	5	0
DW 47907	1/18/2024 13:30	1/18/2024 13:40	0.150	0.012	5	0
DW 47907	1/18/2024 13:40	1/18/2024 13:50	0.150	0.012	5	0
DW 47907	1/18/2024 13:50	1/18/2024 14:00	0.150	0.013	5	0
DW 47907	1/18/2024 14:00	1/18/2024 14:10	0.150	0.014	5	0
DW 47907	1/18/2024 14:10	1/18/2024 14:20	0.150	0.015	5	0
DW 47907	1/18/2024 14:20	1/18/2024 14:30	0.150	0.016	5	0
DW 47907	1/18/2024 14:30	1/18/2024 14:40	0.150	0.016	5	0
DW 47907	1/18/2024 14:40	1/18/2024 14:50	0.150	0.017	5	0
DW 47907	1/18/2024 14:50	1/18/2024 15:00	0.150	0.018	5	0
DW 47907	1/18/2024 15:00	1/18/2024 15:10	0.150	0.018	5	0
DW 47907	1/18/2024 15:10	1/18/2024 15:20	0.150	0.019	5	0
DW 47907	1/18/2024 15:20	1/18/2024 15:30	0.150	0.019	5	0
DW 47907	1/18/2024 15:30	1/18/2024 15:40	0.150	0.019	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/18/2024 8:00	1/18/2024 8:10	0.150	0	5	0
UW 212221	1/18/2024 8:10	1/18/2024 8:20	0.150	0	5	0
UW 212221	1/18/2024 8:20	1/18/2024 8:30	0.150	0	5	0
UW 212221	1/18/2024 8:30	1/18/2024 8:40	0.150	0	5	0
UW 212221	1/18/2024 8:40	1/18/2024 8:50	0.150	0	5	0
UW 212221	1/18/2024 8:50	1/18/2024 9:00	0.150	0	5	0
UW 212221	1/18/2024 9:00	1/18/2024 9:10	0.150	0	5	0
UW 212221	1/18/2024 9:10	1/18/2024 9:20	0.150	0	5	0
UW 212221	1/18/2024 9:20	1/18/2024 9:30	0.150	0	5	0
UW 212221	1/18/2024 9:30	1/18/2024 9:40	0.150	0	5	0
UW 212221	1/18/2024 9:40	1/18/2024 9:50	0.150	0	5	0
UW 212221	1/18/2024 9:50	1/18/2024 10:00	0.150	0	5	0
UW 212221	1/18/2024 10:00	1/18/2024 10:10	0.150	0.001	5	0
UW 212221	1/18/2024 10:10	1/18/2024 10:20	0.150	0.002	5	0
UW 212221	1/18/2024 10:20	1/18/2024 10:30	0.150	0.002	5	0
UW 212221	1/18/2024 10:30	1/18/2024 10:40	0.150	0.003	5	0
UW 212221	1/18/2024 10:40	1/18/2024 10:50	0.150	0.003	5	0
UW 212221	1/18/2024 10:50	1/18/2024 11:00	0.150	0.003	5	0
UW 212221	1/18/2024 11:00	1/18/2024 11:10	0.150	0.004	5	0
UW 212221	1/18/2024 11:10	1/18/2024 11:20	0.150	0.005	5	0
UW 212221	1/18/2024 11:20	1/18/2024 11:30	0.150	0.005	5	0
UW 212221	1/18/2024 11:30	1/18/2024 11:40	0.150	0.006	5	0
UW 212221	1/18/2024 11:40	1/18/2024 11:50	0.150	0.007	5	0
UW 212221	1/18/2024 11:50	1/18/2024 12:00	0.150	0.007	5	0
UW 212221	1/18/2024 12:00	1/18/2024 12:10	0.150	0.008	5	0
UW 212221	1/18/2024 12:10	1/18/2024 12:20	0.150	0.009	5	0
UW 212221	1/18/2024 12:20	1/18/2024 12:30	0.150	0.009	5	0
UW 212221	1/18/2024 12:30	1/18/2024 12:40	0.150	0.009	5	0
UW 212221	1/18/2024 12:40	1/18/2024 12:50	0.150	0.01	5	0
UW 212221	1/18/2024 12:50	1/18/2024 13:00	0.150	0.01	5	0
UW 212221	1/18/2024 13:00	1/18/2024 13:10	0.150	0.011	5	0
UW 212221	1/18/2024 13:10	1/18/2024 13:20	0.150	0.012	5	0
UW 212221	1/18/2024 13:20	1/18/2024 13:30	0.150	0.012	5	0
UW 212221	1/18/2024 13:30	1/18/2024 13:40	0.150	0.013	5	0
UW 212221	1/18/2024 13:40	1/18/2024 13:50	0.150	0.014	5	0
UW 212221	1/18/2024 13:50	1/18/2024 14:00	0.150	0.014	5	0
UW 212221	1/18/2024 14:00	1/18/2024 14:10	0.150	0.015	5	0
UW 212221	1/18/2024 14:10	1/18/2024 14:20	0.150	0.016	5	0
UW 212221	1/18/2024 14:20	1/18/2024 14:30	0.150	0.016	5	0
UW 212221	1/18/2024 14:30	1/18/2024 14:40	0.150	0.016	5	0
UW 212221	1/18/2024 14:40	1/18/2024 14:50	0.150	0.017	5	0
UW 212221	1/18/2024 14:50	1/18/2024 15:00	0.150	0.017	5	0
UW 212221	1/18/2024 15:00	1/18/2024 15:10	0.150	0.018	5	0
UW 212221	1/18/2024 15:10	1/18/2024 15:20	0.150	0.019	5	0
UW 212221	1/18/2024 15:20	1/18/2024 15:30	0.150	0.019	5	0
UW 212221	1/18/2024 15:30	1/18/2024 15:40	0.150	0.02	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/18/2024 8:00	1/18/2024 8:10	0.150	0	5	0
PER1 50057	1/18/2024 8:10	1/18/2024 8:20	0.150	0	5	0
PER1 50057	1/18/2024 8:20	1/18/2024 8:30	0.150	0	5	0
PER1 50057	1/18/2024 8:30	1/18/2024 8:40	0.150	0	5	0
PER1 50057	1/18/2024 8:40	1/18/2024 8:50	0.150	0	5	0
PER1 50057	1/18/2024 8:50	1/18/2024 9:00	0.150	0	5	0
PER1 50057	1/18/2024 9:00	1/18/2024 9:10	0.150	0	5	0
PER1 50057	1/18/2024 9:10	1/18/2024 9:20	0.150	0	5	0
PER1 50057	1/18/2024 9:20	1/18/2024 9:30	0.150	0	5	0
PER1 50057	1/18/2024 9:30	1/18/2024 9:40	0.150	0	5	0
PER1 50057	1/18/2024 9:40	1/18/2024 9:50	0.150	0.002	5	0
PER1 50057	1/18/2024 9:50	1/18/2024 10:00	0.150	0.003	5	0
PER1 50057	1/18/2024 10:00	1/18/2024 10:10	0.150	0.004	5	0
PER1 50057	1/18/2024 10:10	1/18/2024 10:20	0.150	0.004	5	0
PER1 50057	1/18/2024 10:20	1/18/2024 10:30	0.150	0.005	5	0
PER1 50057	1/18/2024 10:30	1/18/2024 10:40	0.150	0.006	5	0
PER1 50057	1/18/2024 10:40	1/18/2024 10:50	0.150	0.007	5	0
PER1 50057	1/18/2024 10:50	1/18/2024 11:00	0.150	0.008	5	0
PER1 50057	1/18/2024 11:00	1/18/2024 11:10	0.150	0.009	5	0
PER1 50057	1/18/2024 11:10	1/18/2024 11:20	0.150	0.01	5	0
PER1 50057	1/18/2024 11:20	1/18/2024 11:30	0.150	0.011	5	0
PER1 50057	1/18/2024 11:30	1/18/2024 11:40	0.150	0.012	5	0
PER1 50057	1/18/2024 11:40	1/18/2024 11:50	0.150	0.013	5	0
PER1 50057	1/18/2024 11:50	1/18/2024 12:00	0.150	0.013	5	0
PER1 50057	1/18/2024 12:00	1/18/2024 12:10	0.150	0.014	5	0
PER1 50057	1/18/2024 12:10	1/18/2024 12:20	0.150	0.015	5	0
PER1 50057	1/18/2024 12:20	1/18/2024 12:30	0.150	0.016	5	0
PER1 50057	1/18/2024 12:30	1/18/2024 12:40	0.150	0.016	5	0
PER1 50057	1/18/2024 12:40	1/18/2024 12:50	0.150	0.017	5	0
PER1 50057	1/18/2024 12:50	1/18/2024 13:00	0.150	0.018	5	0
PER1 50057	1/18/2024 13:00	1/18/2024 13:10	0.150	0.019	5	0
PER1 50057	1/18/2024 13:10	1/18/2024 13:20	0.150	0.019	5	0
PER1 50057	1/18/2024 13:20	1/18/2024 13:30	0.150	0.02	5	0
PER1 50057	1/18/2024 13:30	1/18/2024 13:40	0.150	0.021	5	0
PER1 50057	1/18/2024 13:40	1/18/2024 13:50	0.150	0.021	5	0
PER1 50057	1/18/2024 13:50	1/18/2024 14:00	0.150	0.022	5	0
PER1 50057	1/18/2024 14:00	1/18/2024 14:10	0.150	0.023	5	0
PER1 50057	1/18/2024 14:10	1/18/2024 14:20	0.150	0.024	5	0
PER1 50057	1/18/2024 14:20	1/18/2024 14:30	0.150	0.025	5	0
PER1 50057	1/18/2024 14:30	1/18/2024 14:40	0.150	0.025	5	0
PER1 50057	1/18/2024 14:40	1/18/2024 14:50	0.150	0.026	5	0
PER1 50057	1/18/2024 14:50	1/18/2024 15:00	0.150	0.027	5	0
PER1 50057	1/18/2024 15:00	1/18/2024 15:10	0.150	0.027	5	0
PER1 50057	1/18/2024 15:10	1/18/2024 15:20	0.150	0.028	5	0
PER1 50057	1/18/2024 15:20	1/18/2024 15:30	0.150	0.029	5	0
PER1 50057	1/18/2024 15:30	1/18/2024 15:40	0.150	0.029	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/18/2024 8:00	1/18/2024 8:10	0.150	0.032	5	0
PER2 46495	1/18/2024 8:10	1/18/2024 8:20	0.150	0.032	5	0
PER2 46495	1/18/2024 8:20	1/18/2024 8:30	0.150	0.032	5	0
PER2 46495	1/18/2024 8:30	1/18/2024 8:40	0.150	0.032	5	0
PER2 46495	1/18/2024 8:40	1/18/2024 8:50	0.150	0.032	5	0
PER2 46495	1/18/2024 8:50	1/18/2024 9:00	0.150	0.032	5	0
PER2 46495	1/18/2024 9:00	1/18/2024 9:10	0.150	0.032	5	0
PER2 46495	1/18/2024 9:10	1/18/2024 9:20	0.150	0.032	5	0
PER2 46495	1/18/2024 9:20	1/18/2024 9:30	0.150	0.032	5	0
PER2 46495	1/18/2024 9:30	1/18/2024 9:40	0.150	0.032	5	0
PER2 46495	1/18/2024 9:40	1/18/2024 9:50	0.150	0.032	5	0
PER2 46495	1/18/2024 9:50	1/18/2024 10:00	0.150	0	5	0
PER2 46495	1/18/2024 10:00	1/18/2024 10:10	0.150	0	5	0
PER2 46495	1/18/2024 10:10	1/18/2024 10:20	0.150	0.002	5	0
PER2 46495	1/18/2024 10:20	1/18/2024 10:30	0.150	0.002	5	0
PER2 46495	1/18/2024 10:30	1/18/2024 10:40	0.150	0.003	5	0
PER2 46495	1/18/2024 10:40	1/18/2024 10:50	0.150	0.004	5	0
PER2 46495	1/18/2024 10:50	1/18/2024 11:00	0.150	0.004	5	0
PER2 46495	1/18/2024 11:00	1/18/2024 11:10	0.150	0.005	5	0
PER2 46495	1/18/2024 11:10	1/18/2024 11:20	0.150	0.006	5	0
PER2 46495	1/18/2024 11:20	1/18/2024 11:30	0.150	0.007	5	0
PER2 46495	1/18/2024 11:30	1/18/2024 11:40	0.150	0.007	5	0
PER2 46495	1/18/2024 11:40	1/18/2024 11:50	0.150	0.008	5	0
PER2 46495	1/18/2024 11:50	1/18/2024 12:00	0.150	0.009	5	0
PER2 46495	1/18/2024 12:00	1/18/2024 12:10	0.150	0.009	5	0
PER2 46495	1/18/2024 12:10	1/18/2024 12:20	0.150	0.01	5	0
PER2 46495	1/18/2024 12:20	1/18/2024 12:30	0.150	0.011	5	0
PER2 46495	1/18/2024 12:30	1/18/2024 12:40	0.150	0.011	5	0
PER2 46495	1/18/2024 12:40	1/18/2024 12:50	0.150	0.012	5	0
PER2 46495	1/18/2024 12:50	1/18/2024 13:00	0.150	0.013	5	0
PER2 46495	1/18/2024 13:00	1/18/2024 13:10	0.150	0.013	5	0
PER2 46495	1/18/2024 13:10	1/18/2024 13:20	0.150	0.014	5	0
PER2 46495	1/18/2024 13:20	1/18/2024 13:30	0.150	0.014	5	0
PER2 46495	1/18/2024 13:30	1/18/2024 13:40	0.150	0.015	5	0
PER2 46495	1/18/2024 13:40	1/18/2024 13:50	0.150	0.016	5	0
PER2 46495	1/18/2024 13:50	1/18/2024 14:00	0.150	0.016	5	0
PER2 46495	1/18/2024 14:00	1/18/2024 14:10	0.150	0.017	5	0
PER2 46495	1/18/2024 14:10	1/18/2024 14:20	0.150	0.018	5	0
PER2 46495	1/18/2024 14:20	1/18/2024 14:30	0.150	0.018	5	0
PER2 46495	1/18/2024 14:30	1/18/2024 14:40	0.150	0.019	5	0
PER2 46495	1/18/2024 14:40	1/18/2024 14:50	0.150	0.02	5	0
PER2 46495	1/18/2024 14:50	1/18/2024 15:00	0.150	0.02	5	0
PER2 46495	1/18/2024 15:00	1/18/2024 15:10	0.150	0.021	5	0
PER2 46495	1/18/2024 15:10	1/18/2024 15:20	0.150	0.022	5	0
PER2 46495	1/18/2024 15:20	1/18/2024 15:30	0.150	0.022	5	0
PER2 46495	1/18/2024 15:30	1/18/2024 15:40	0.150	0.023	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/19/2024

Weather: 25 deg. F, Snow

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Prepare to commence dewatering system operation on the following work day, Monday, January 22nd.

Is the dewatering system operating: YES **NO**

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA


Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to snow.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

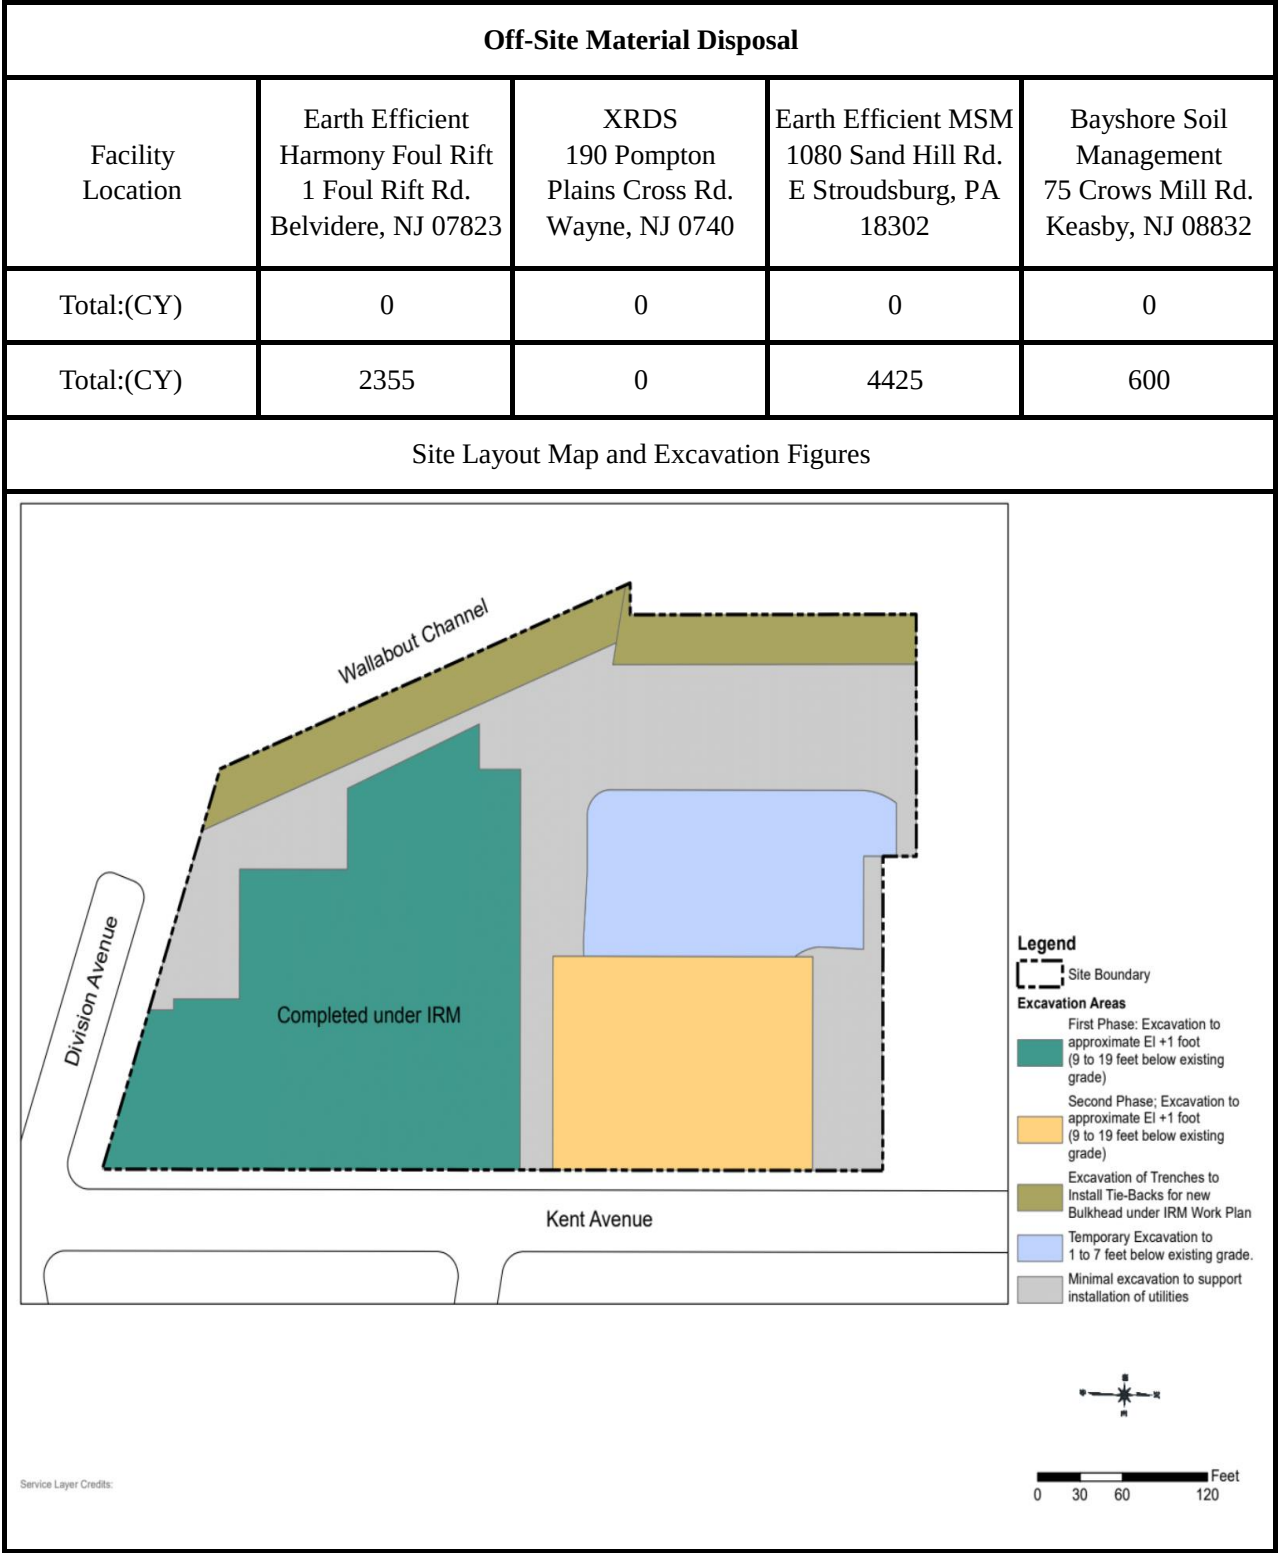

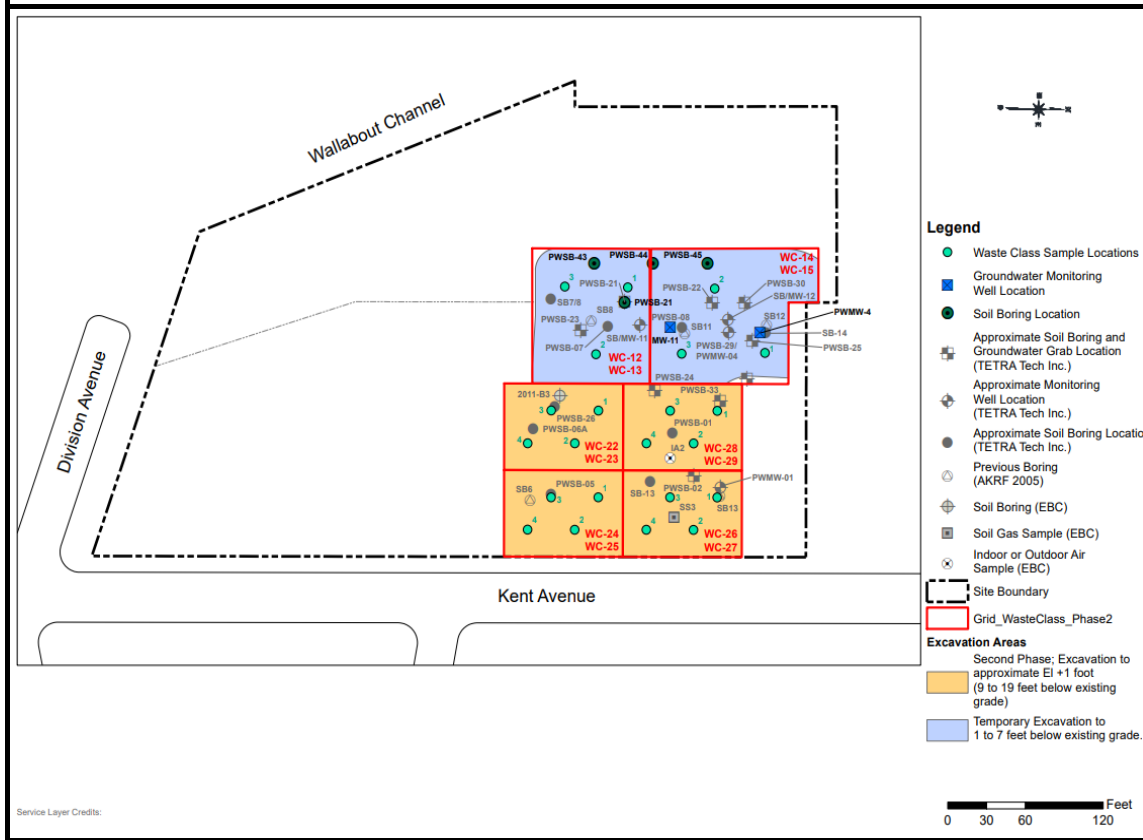
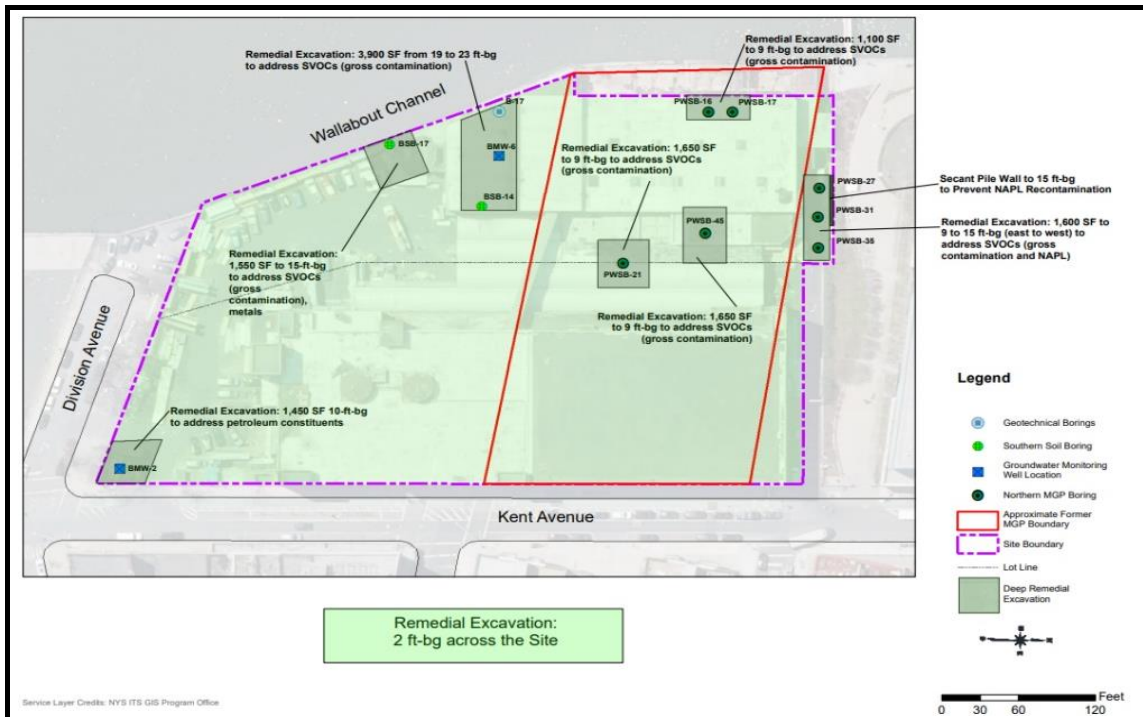


Photo 1:

View of soil excavation facing northwest.



Photo 2:

View of pile installation and site conditions facing southwest.



Photo 3:

View of Site
conditions facing
north.



Photo 4:

View of Site
conditons and
exposed piles after
soil excavation facing
west.



CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/22/2024

Weather: 35 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Commence full scale operation of dewatering system.
- 3) Export of 27 loads (approximately 540 CY) of material from WC-25 & 27 for off-site disposal to the Harmony Foul Rift disposal facility.
- 4) Export of 1 load (approximately 20 CY) of material from WC-29 for off-site disposal to MSM facility.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA


Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

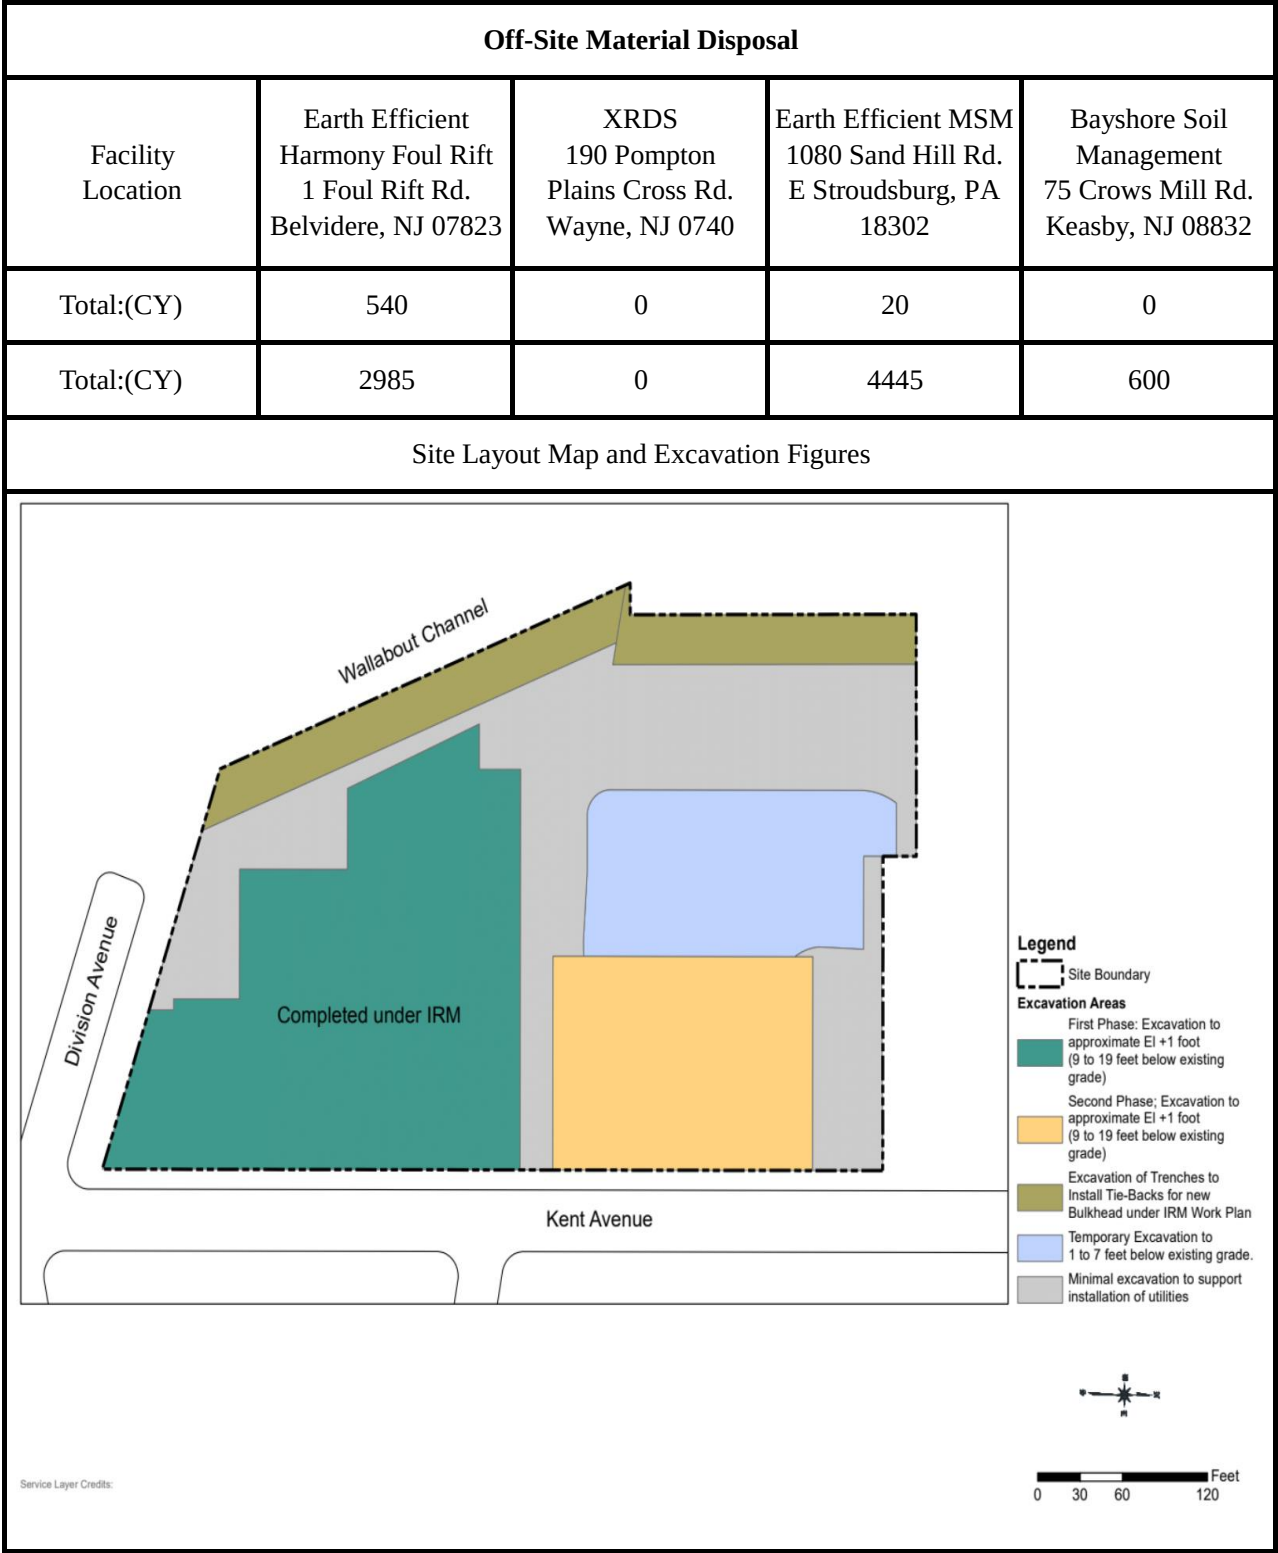

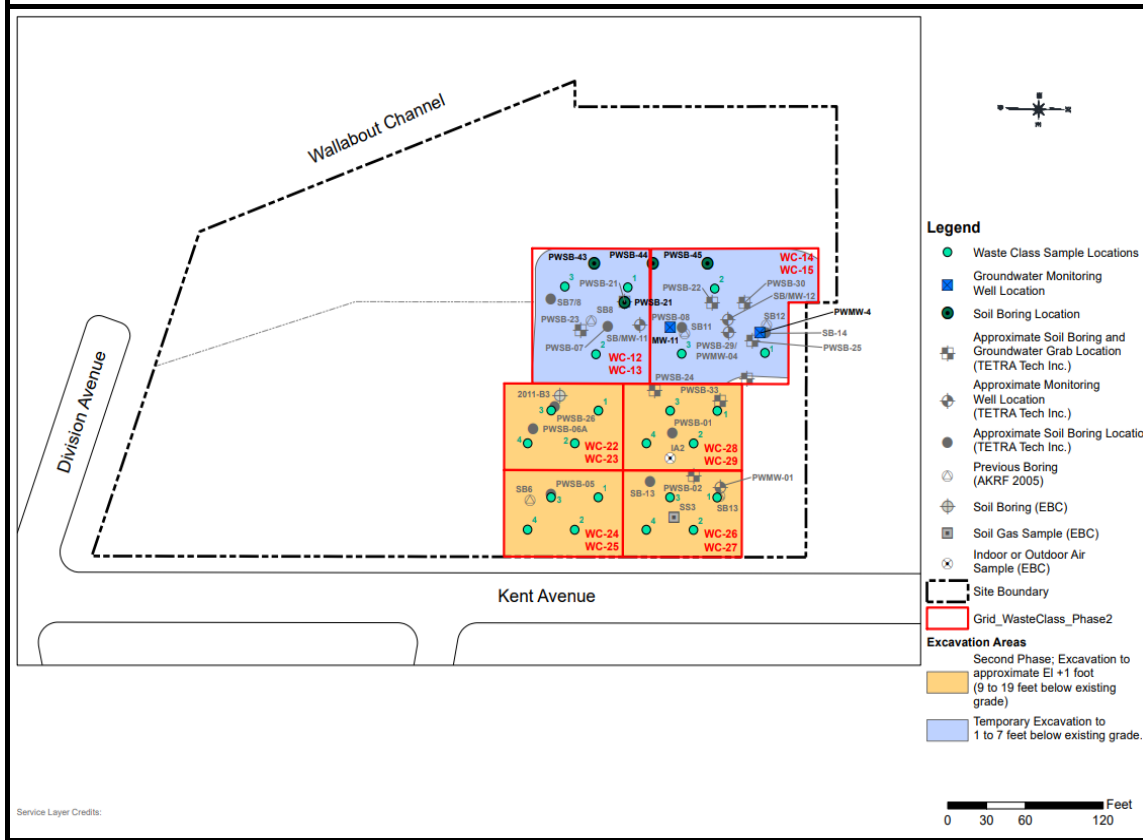
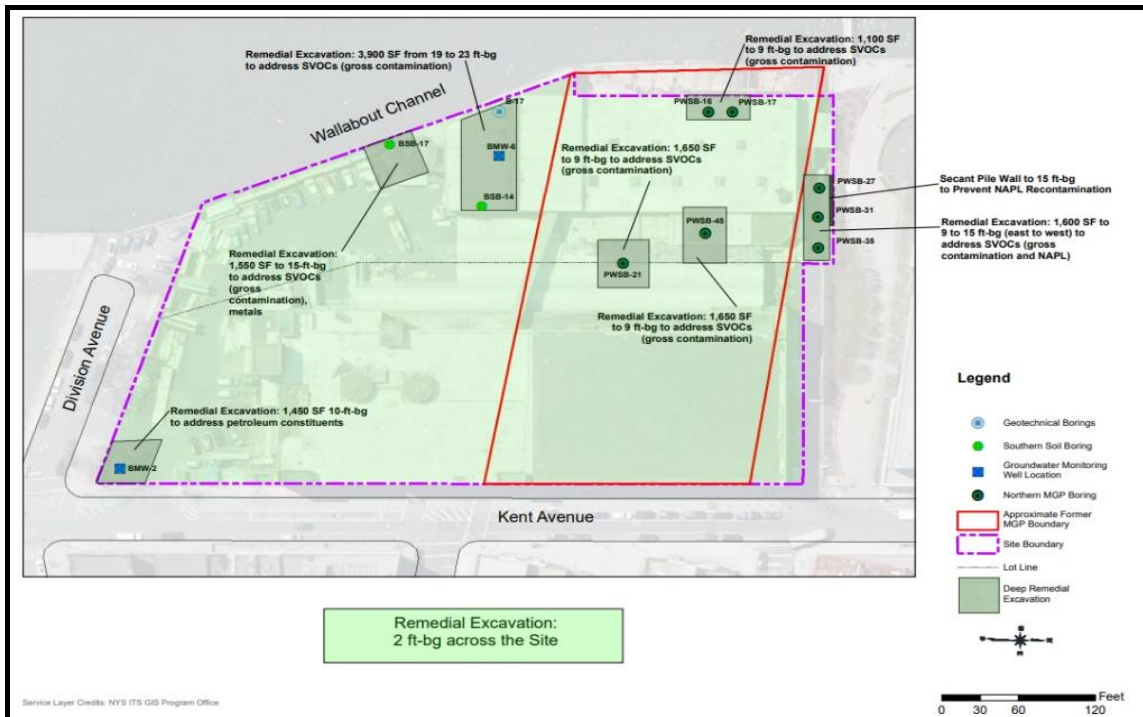


Photo 1:

View of pile installaton
and soil excavation
facing south.



Photo 2:

View of pile installation
and site conditions facing
west.

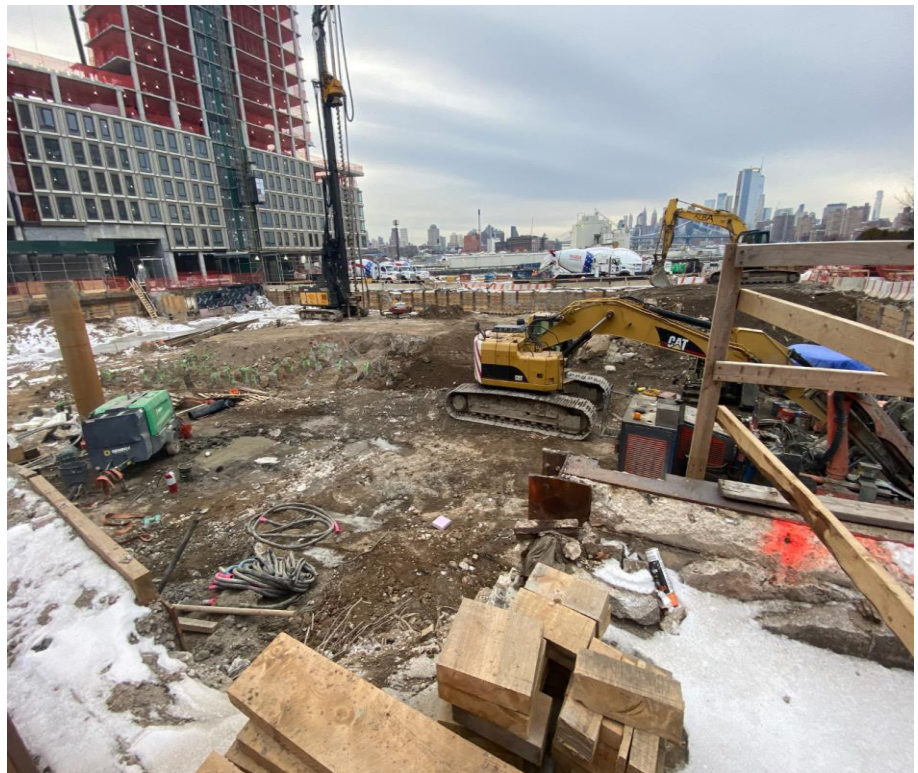


Photo 3:
View of Site
conditions facing
east.



Photo 4:
View of Site
conditons and
activities facing
southeast.



CAMP:
Downwind
Particulates

Dust Levels


0.021 mg/m³ 0.03 mg/m³ 0.15



CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm 5

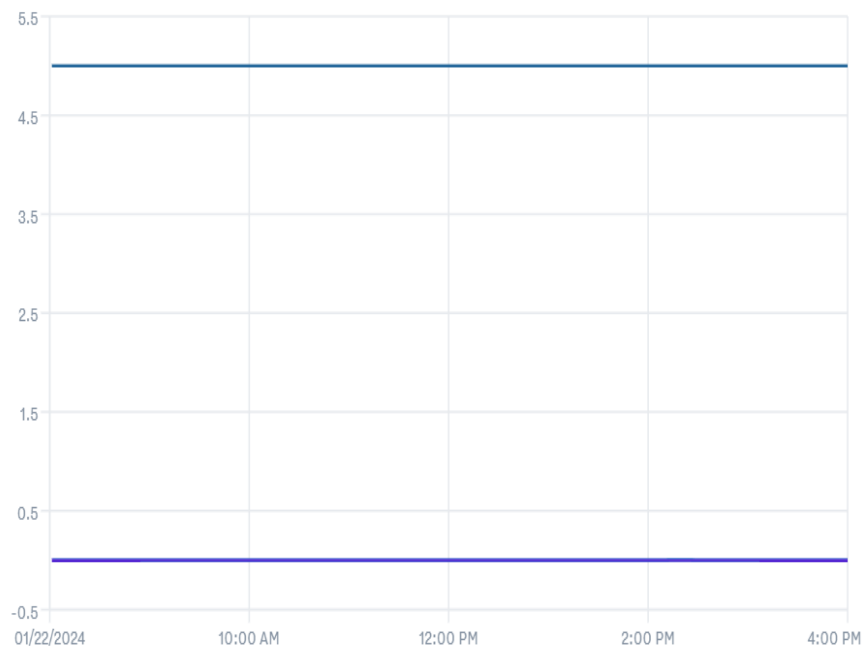

CAMP:
Upwind Particulates

Dust Levels


0.028 mg/m³ 0.029 mg/m³ 0.15

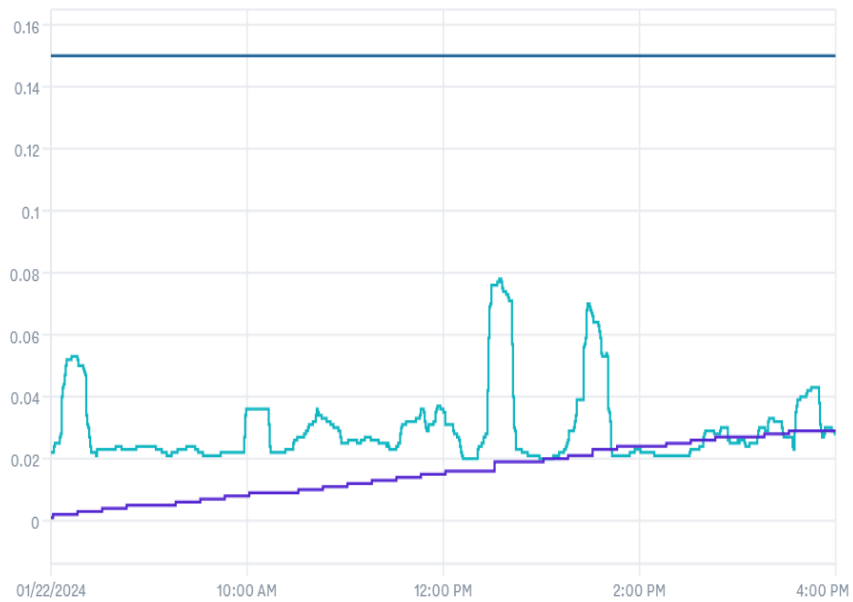

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

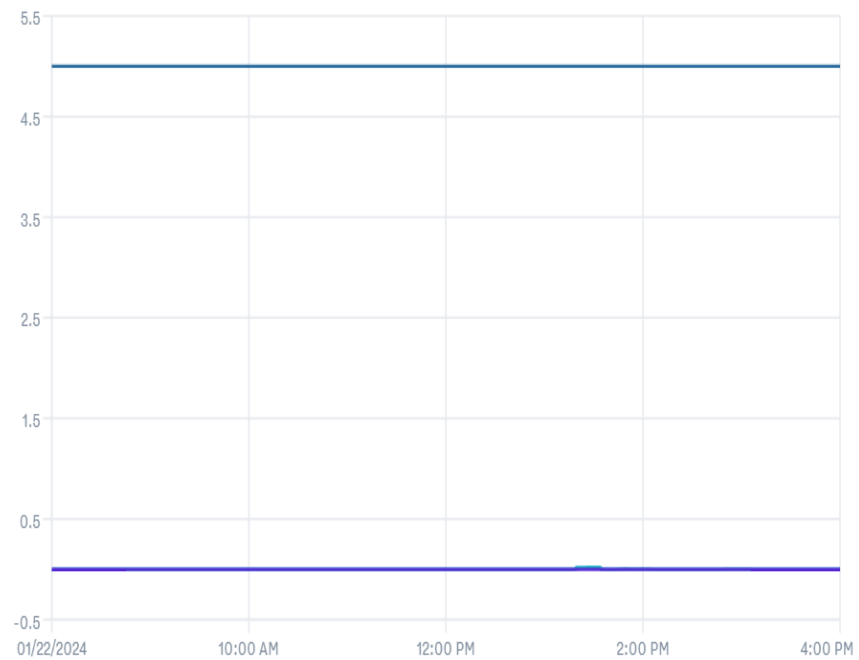

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/22/2024 8:00	1/22/2024 8:10	0.150	0	5	0
DW 47907	1/22/2024 8:10	1/22/2024 8:20	0.150	0.001	5	0
DW 47907	1/22/2024 8:20	1/22/2024 8:30	0.150	0.001	5	0
DW 47907	1/22/2024 8:30	1/22/2024 8:40	0.150	0.002	5	0
DW 47907	1/22/2024 8:40	1/22/2024 8:50	0.150	0.003	5	0
DW 47907	1/22/2024 8:50	1/22/2024 9:00	0.150	0.003	5	0
DW 47907	1/22/2024 9:00	1/22/2024 9:10	0.150	0.003	5	0
DW 47907	1/22/2024 9:10	1/22/2024 9:20	0.150	0.004	5	0
DW 47907	1/22/2024 9:20	1/22/2024 9:30	0.150	0.004	5	0
DW 47907	1/22/2024 9:30	1/22/2024 9:40	0.150	0.005	5	0
DW 47907	1/22/2024 9:40	1/22/2024 9:50	0.150	0.005	5	0
DW 47907	1/22/2024 9:50	1/22/2024 10:00	0.150	0.005	5	0
DW 47907	1/22/2024 10:00	1/22/2024 10:10	0.150	0.007	5	0
DW 47907	1/22/2024 10:10	1/22/2024 10:20	0.150	0.008	5	0
DW 47907	1/22/2024 10:20	1/22/2024 10:30	0.150	0.008	5	0
DW 47907	1/22/2024 10:30	1/22/2024 10:40	0.150	0.009	5	0
DW 47907	1/22/2024 10:40	1/22/2024 10:50	0.150	0.01	5	0
DW 47907	1/22/2024 10:50	1/22/2024 11:00	0.150	0.011	5	0
DW 47907	1/22/2024 11:00	1/22/2024 11:10	0.150	0.011	5	0
DW 47907	1/22/2024 11:10	1/22/2024 11:20	0.150	0.012	5	0
DW 47907	1/22/2024 11:20	1/22/2024 11:30	0.150	0.013	5	0
DW 47907	1/22/2024 11:30	1/22/2024 11:40	0.150	0.013	5	0
DW 47907	1/22/2024 11:40	1/22/2024 11:50	0.150	0.014	5	0
DW 47907	1/22/2024 11:50	1/22/2024 12:00	0.150	0.015	5	0
DW 47907	1/22/2024 12:00	1/22/2024 12:10	0.150	0.015	5	0
DW 47907	1/22/2024 12:10	1/22/2024 12:20	0.150	0.016	5	0
DW 47907	1/22/2024 12:20	1/22/2024 12:30	0.150	0.017	5	0
DW 47907	1/22/2024 12:30	1/22/2024 12:40	0.150	0.017	5	0
DW 47907	1/22/2024 12:40	1/22/2024 12:50	0.150	0.018	5	0
DW 47907	1/22/2024 12:50	1/22/2024 13:00	0.150	0.018	5	0
DW 47907	1/22/2024 13:00	1/22/2024 13:10	0.150	0.019	5	0
DW 47907	1/22/2024 13:10	1/22/2024 13:20	0.150	0.02	5	0
DW 47907	1/22/2024 13:20	1/22/2024 13:30	0.150	0.021	5	0
DW 47907	1/22/2024 13:30	1/22/2024 13:40	0.150	0.022	5	0
DW 47907	1/22/2024 13:40	1/22/2024 13:50	0.150	0.023	5	0
DW 47907	1/22/2024 13:50	1/22/2024 14:00	0.150	0.024	5	0
DW 47907	1/22/2024 14:00	1/22/2024 14:10	0.150	0.025	5	0
DW 47907	1/22/2024 14:10	1/22/2024 14:20	0.150	0.025	5	0
DW 47907	1/22/2024 14:20	1/22/2024 14:30	0.150	0.026	5	0
DW 47907	1/22/2024 14:30	1/22/2024 14:40	0.150	0.027	5	0
DW 47907	1/22/2024 14:40	1/22/2024 14:50	0.150	0.027	5	0
DW 47907	1/22/2024 14:50	1/22/2024 15:00	0.150	0.028	5	0
DW 47907	1/22/2024 15:00	1/22/2024 15:10	0.150	0.028	5	0
DW 47907	1/22/2024 15:10	1/22/2024 15:20	0.150	0.029	5	0
DW 47907	1/22/2024 15:20	1/22/2024 15:30	0.150	0.029	5	0
DW 47907	1/22/2024 15:30	1/22/2024 15:40	0.150	0.03	5	0
DW 47907	1/22/2024 15:40	1/22/2024 15:50	0.150	0.03	5	0
DW 47907	1/22/2024 15:50	1/22/2024 16:00	0.150	0.03	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/22/2024 8:00	1/22/2024 8:10	0.150	0.002	5	0
UW 212221	1/22/2024 8:10	1/22/2024 8:20	0.150	0.003	5	0
UW 212221	1/22/2024 8:20	1/22/2024 8:30	0.150	0.003	5	0
UW 212221	1/22/2024 8:30	1/22/2024 8:40	0.150	0.004	5	0
UW 212221	1/22/2024 8:40	1/22/2024 8:50	0.150	0.005	5	0
UW 212221	1/22/2024 8:50	1/22/2024 9:00	0.150	0.005	5	0
UW 212221	1/22/2024 9:00	1/22/2024 9:10	0.150	0.005	5	0
UW 212221	1/22/2024 9:10	1/22/2024 9:20	0.150	0.006	5	0
UW 212221	1/22/2024 9:20	1/22/2024 9:30	0.150	0.006	5	0
UW 212221	1/22/2024 9:30	1/22/2024 9:40	0.150	0.007	5	0
UW 212221	1/22/2024 9:40	1/22/2024 9:50	0.150	0.008	5	0
UW 212221	1/22/2024 9:50	1/22/2024 10:00	0.150	0.008	5	0
UW 212221	1/22/2024 10:00	1/22/2024 10:10	0.150	0.009	5	0
UW 212221	1/22/2024 10:10	1/22/2024 10:20	0.150	0.009	5	0
UW 212221	1/22/2024 10:20	1/22/2024 10:30	0.150	0.009	5	0
UW 212221	1/22/2024 10:30	1/22/2024 10:40	0.150	0.01	5	0
UW 212221	1/22/2024 10:40	1/22/2024 10:50	0.150	0.011	5	0
UW 212221	1/22/2024 10:50	1/22/2024 11:00	0.150	0.011	5	0
UW 212221	1/22/2024 11:00	1/22/2024 11:10	0.150	0.012	5	0
UW 212221	1/22/2024 11:10	1/22/2024 11:20	0.150	0.013	5	0
UW 212221	1/22/2024 11:20	1/22/2024 11:30	0.150	0.013	5	0
UW 212221	1/22/2024 11:30	1/22/2024 11:40	0.150	0.014	5	0
UW 212221	1/22/2024 11:40	1/22/2024 11:50	0.150	0.015	5	0
UW 212221	1/22/2024 11:50	1/22/2024 12:00	0.150	0.015	5	0
UW 212221	1/22/2024 12:00	1/22/2024 12:10	0.150	0.016	5	0
UW 212221	1/22/2024 12:10	1/22/2024 12:20	0.150	0.016	5	0
UW 212221	1/22/2024 12:20	1/22/2024 12:30	0.150	0.016	5	0
UW 212221	1/22/2024 12:30	1/22/2024 12:40	0.150	0.019	5	0
UW 212221	1/22/2024 12:40	1/22/2024 12:50	0.150	0.019	5	0
UW 212221	1/22/2024 12:50	1/22/2024 13:00	0.150	0.019	5	0
UW 212221	1/22/2024 13:00	1/22/2024 13:10	0.150	0.02	5	0
UW 212221	1/22/2024 13:10	1/22/2024 13:20	0.150	0.021	5	0
UW 212221	1/22/2024 13:20	1/22/2024 13:30	0.150	0.021	5	0
UW 212221	1/22/2024 13:30	1/22/2024 13:40	0.150	0.023	5	0
UW 212221	1/22/2024 13:40	1/22/2024 13:50	0.150	0.024	5	0
UW 212221	1/22/2024 13:50	1/22/2024 14:00	0.150	0.024	5	0
UW 212221	1/22/2024 14:00	1/22/2024 14:10	0.150	0.024	5	0
UW 212221	1/22/2024 14:10	1/22/2024 14:20	0.150	0.025	5	0
UW 212221	1/22/2024 14:20	1/22/2024 14:30	0.150	0.025	5	0
UW 212221	1/22/2024 14:30	1/22/2024 14:40	0.150	0.026	5	0
UW 212221	1/22/2024 14:40	1/22/2024 14:50	0.150	0.027	5	0
UW 212221	1/22/2024 14:50	1/22/2024 15:00	0.150	0.027	5	0
UW 212221	1/22/2024 15:00	1/22/2024 15:10	0.150	0.027	5	0
UW 212221	1/22/2024 15:10	1/22/2024 15:20	0.150	0.028	5	0
UW 212221	1/22/2024 15:20	1/22/2024 15:30	0.150	0.028	5	0
UW 212221	1/22/2024 15:30	1/22/2024 15:40	0.150	0.029	5	0
UW 212221	1/22/2024 15:40	1/22/2024 15:50	0.150	0.029	5	0
UW 212221	1/22/2024 15:50	1/22/2024 16:00	0.150	0.029	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/22/2024 8:00	1/22/2024 8:10	0.150	0.003	5	0
PER1 50057	1/22/2024 8:10	1/22/2024 8:20	0.150	0.004	5	0
PER1 50057	1/22/2024 8:20	1/22/2024 8:30	0.150	0.004	5	0
PER1 50057	1/22/2024 8:30	1/22/2024 8:40	0.150	0.005	5	0
PER1 50057	1/22/2024 8:40	1/22/2024 8:50	0.150	0.006	5	0
PER1 50057	1/22/2024 8:50	1/22/2024 9:00	0.150	0.007	5	0
PER1 50057	1/22/2024 9:00	1/22/2024 9:10	0.150	0.007	5	0
PER1 50057	1/22/2024 9:10	1/22/2024 9:20	0.150	0.008	5	0
PER1 50057	1/22/2024 9:20	1/22/2024 9:30	0.150	0.009	5	0
PER1 50057	1/22/2024 9:30	1/22/2024 9:40	0.150	0.009	5	0
PER1 50057	1/22/2024 9:40	1/22/2024 9:50	0.150	0.01	5	0
PER1 50057	1/22/2024 9:50	1/22/2024 10:00	0.150	0.01	5	0
PER1 50057	1/22/2024 10:00	1/22/2024 10:10	0.150	0.011	5	0
PER1 50057	1/22/2024 10:10	1/22/2024 10:20	0.150	0.012	5	0
PER1 50057	1/22/2024 10:20	1/22/2024 10:30	0.150	0.012	5	0
PER1 50057	1/22/2024 10:30	1/22/2024 10:40	0.150	0.013	5	0
PER1 50057	1/22/2024 10:40	1/22/2024 10:50	0.150	0.014	5	0
PER1 50057	1/22/2024 10:50	1/22/2024 11:00	0.150	0.014	5	0
PER1 50057	1/22/2024 11:00	1/22/2024 11:10	0.150	0.015	5	0
PER1 50057	1/22/2024 11:10	1/22/2024 11:20	0.150	0.016	5	0
PER1 50057	1/22/2024 11:20	1/22/2024 11:30	0.150	0.016	5	0
PER1 50057	1/22/2024 11:30	1/22/2024 11:40	0.150	0.017	5	0
PER1 50057	1/22/2024 11:40	1/22/2024 11:50	0.150	0.018	5	0
PER1 50057	1/22/2024 11:50	1/22/2024 12:00	0.150	0.018	5	0
PER1 50057	1/22/2024 12:00	1/22/2024 12:10	0.150	0.019	5	0
PER1 50057	1/22/2024 12:10	1/22/2024 12:20	0.150	0.019	5	0.001
PER1 50057	1/22/2024 12:20	1/22/2024 12:30	0.150	0.02	5	0.001
PER1 50057	1/22/2024 12:30	1/22/2024 12:40	0.150	0.021	5	0.001
PER1 50057	1/22/2024 12:40	1/22/2024 12:50	0.150	0.021	5	0.001
PER1 50057	1/22/2024 12:50	1/22/2024 13:00	0.150	0.022	5	0.001
PER1 50057	1/22/2024 13:00	1/22/2024 13:10	0.150	0.022	5	0.001
PER1 50057	1/22/2024 13:10	1/22/2024 13:20	0.150	0.023	5	0.001
PER1 50057	1/22/2024 13:20	1/22/2024 13:30	0.150	0.023	5	0.001
PER1 50057	1/22/2024 13:30	1/22/2024 13:40	0.150	0.024	5	0.001
PER1 50057	1/22/2024 13:40	1/22/2024 13:50	0.150	0.024	5	0.001
PER1 50057	1/22/2024 13:50	1/22/2024 14:00	0.150	0.025	5	0.001
PER1 50057	1/22/2024 14:00	1/22/2024 14:10	0.150	0.025	5	0.001
PER1 50057	1/22/2024 14:10	1/22/2024 14:20	0.150	0.026	5	0.001
PER1 50057	1/22/2024 14:20	1/22/2024 14:30	0.150	0.026	5	0.001
PER1 50057	1/22/2024 14:30	1/22/2024 14:40	0.150	0.027	5	0.001
PER1 50057	1/22/2024 14:40	1/22/2024 14:50	0.150	0.027	5	0.001
PER1 50057	1/22/2024 14:50	1/22/2024 15:00	0.150	0.027	5	0.001
PER1 50057	1/22/2024 15:00	1/22/2024 15:10	0.150	0.028	5	0.001
PER1 50057	1/22/2024 15:10	1/22/2024 15:20	0.150	0.028	5	0.001
PER1 50057	1/22/2024 15:20	1/22/2024 15:30	0.150	0.029	5	0.001
PER1 50057	1/22/2024 15:30	1/22/2024 15:40	0.150	0.029	5	0.001
PER1 50057	1/22/2024 15:40	1/22/2024 15:50	0.150	0.029	5	0.001
PER1 50057	1/22/2024 15:50	1/22/2024 16:00	0.150	0.029	5	0.001

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/22/2024 8:00	1/22/2024 8:10	0.150	0.001	5	0
PER2 46495	1/22/2024 8:10	1/22/2024 8:20	0.150	0.002	5	0
PER2 46495	1/22/2024 8:20	1/22/2024 8:30	0.150	0.002	5	0
PER2 46495	1/22/2024 8:30	1/22/2024 8:40	0.150	0.003	5	0
PER2 46495	1/22/2024 8:40	1/22/2024 8:50	0.150	0.004	5	0
PER2 46495	1/22/2024 8:50	1/22/2024 9:00	0.150	0.004	5	0
PER2 46495	1/22/2024 9:00	1/22/2024 9:10	0.150	0.005	5	0
PER2 46495	1/22/2024 9:10	1/22/2024 9:20	0.150	0.006	5	0
PER2 46495	1/22/2024 9:20	1/22/2024 9:30	0.150	0.006	5	0
PER2 46495	1/22/2024 9:30	1/22/2024 9:40	0.150	0.007	5	0
PER2 46495	1/22/2024 9:40	1/22/2024 9:50	0.150	0.007	5	0
PER2 46495	1/22/2024 9:50	1/22/2024 10:00	0.150	0.008	5	0
PER2 46495	1/22/2024 10:00	1/22/2024 10:10	0.150	0.009	5	0
PER2 46495	1/22/2024 10:10	1/22/2024 10:20	0.150	0.009	5	0
PER2 46495	1/22/2024 10:20	1/22/2024 10:30	0.150	0.01	5	0
PER2 46495	1/22/2024 10:30	1/22/2024 10:40	0.150	0.01	5	0
PER2 46495	1/22/2024 10:40	1/22/2024 10:50	0.150	0.011	5	0
PER2 46495	1/22/2024 10:50	1/22/2024 11:00	0.150	0.012	5	0
PER2 46495	1/22/2024 11:00	1/22/2024 11:10	0.150	0.012	5	0
PER2 46495	1/22/2024 11:10	1/22/2024 11:20	0.150	0.013	5	0
PER2 46495	1/22/2024 11:20	1/22/2024 11:30	0.150	0.014	5	0
PER2 46495	1/22/2024 11:30	1/22/2024 11:40	0.150	0.014	5	0
PER2 46495	1/22/2024 11:40	1/22/2024 11:50	0.150	0.015	5	0
PER2 46495	1/22/2024 11:50	1/22/2024 12:00	0.150	0.015	5	0
PER2 46495	1/22/2024 12:00	1/22/2024 12:10	0.150	0.016	5	0
PER2 46495	1/22/2024 12:10	1/22/2024 12:20	0.150	0.016	5	0
PER2 46495	1/22/2024 12:20	1/22/2024 12:30	0.150	0.017	5	0
PER2 46495	1/22/2024 12:30	1/22/2024 12:40	0.150	0.017	5	0
PER2 46495	1/22/2024 12:40	1/22/2024 12:50	0.150	0.018	5	0
PER2 46495	1/22/2024 12:50	1/22/2024 13:00	0.150	0.019	5	0
PER2 46495	1/22/2024 13:00	1/22/2024 13:10	0.150	0.019	5	0
PER2 46495	1/22/2024 13:10	1/22/2024 13:20	0.150	0.02	5	0
PER2 46495	1/22/2024 13:20	1/22/2024 13:30	0.150	0.02	5	0
PER2 46495	1/22/2024 13:30	1/22/2024 13:40	0.150	0.021	5	0
PER2 46495	1/22/2024 13:40	1/22/2024 13:50	0.150	0.022	5	0
PER2 46495	1/22/2024 13:50	1/22/2024 14:00	0.150	0.022	5	0
PER2 46495	1/22/2024 14:00	1/22/2024 14:10	0.150	0.023	5	0
PER2 46495	1/22/2024 14:10	1/22/2024 14:20	0.150	0.023	5	0
PER2 46495	1/22/2024 14:20	1/22/2024 14:30	0.150	0.024	5	0
PER2 46495	1/22/2024 14:30	1/22/2024 14:40	0.150	0.024	5	0
PER2 46495	1/22/2024 14:40	1/22/2024 14:50	0.150	0.025	5	0
PER2 46495	1/22/2024 14:50	1/22/2024 15:00	0.150	0.025	5	0
PER2 46495	1/22/2024 15:00	1/22/2024 15:10	0.150	0.026	5	0
PER2 46495	1/22/2024 15:10	1/22/2024 15:20	0.150	0.026	5	0
PER2 46495	1/22/2024 15:20	1/22/2024 15:30	0.150	0.027	5	0
PER2 46495	1/22/2024 15:30	1/22/2024 15:40	0.150	0.028	5	0
PER2 46495	1/22/2024 15:40	1/22/2024 15:50	0.150	0.028	5	0
PER2 46495	1/22/2024 15:50	1/22/2024 16:00	0.150	0.028	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/23/2024

Weather: 35 deg. F, Overcast/Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

1) Alba continues excavation, drilling piles and installing SOE in A3 building location.

Is the dewatering system operating: **YES** NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA


Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up until approximately 10AM due to rain.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

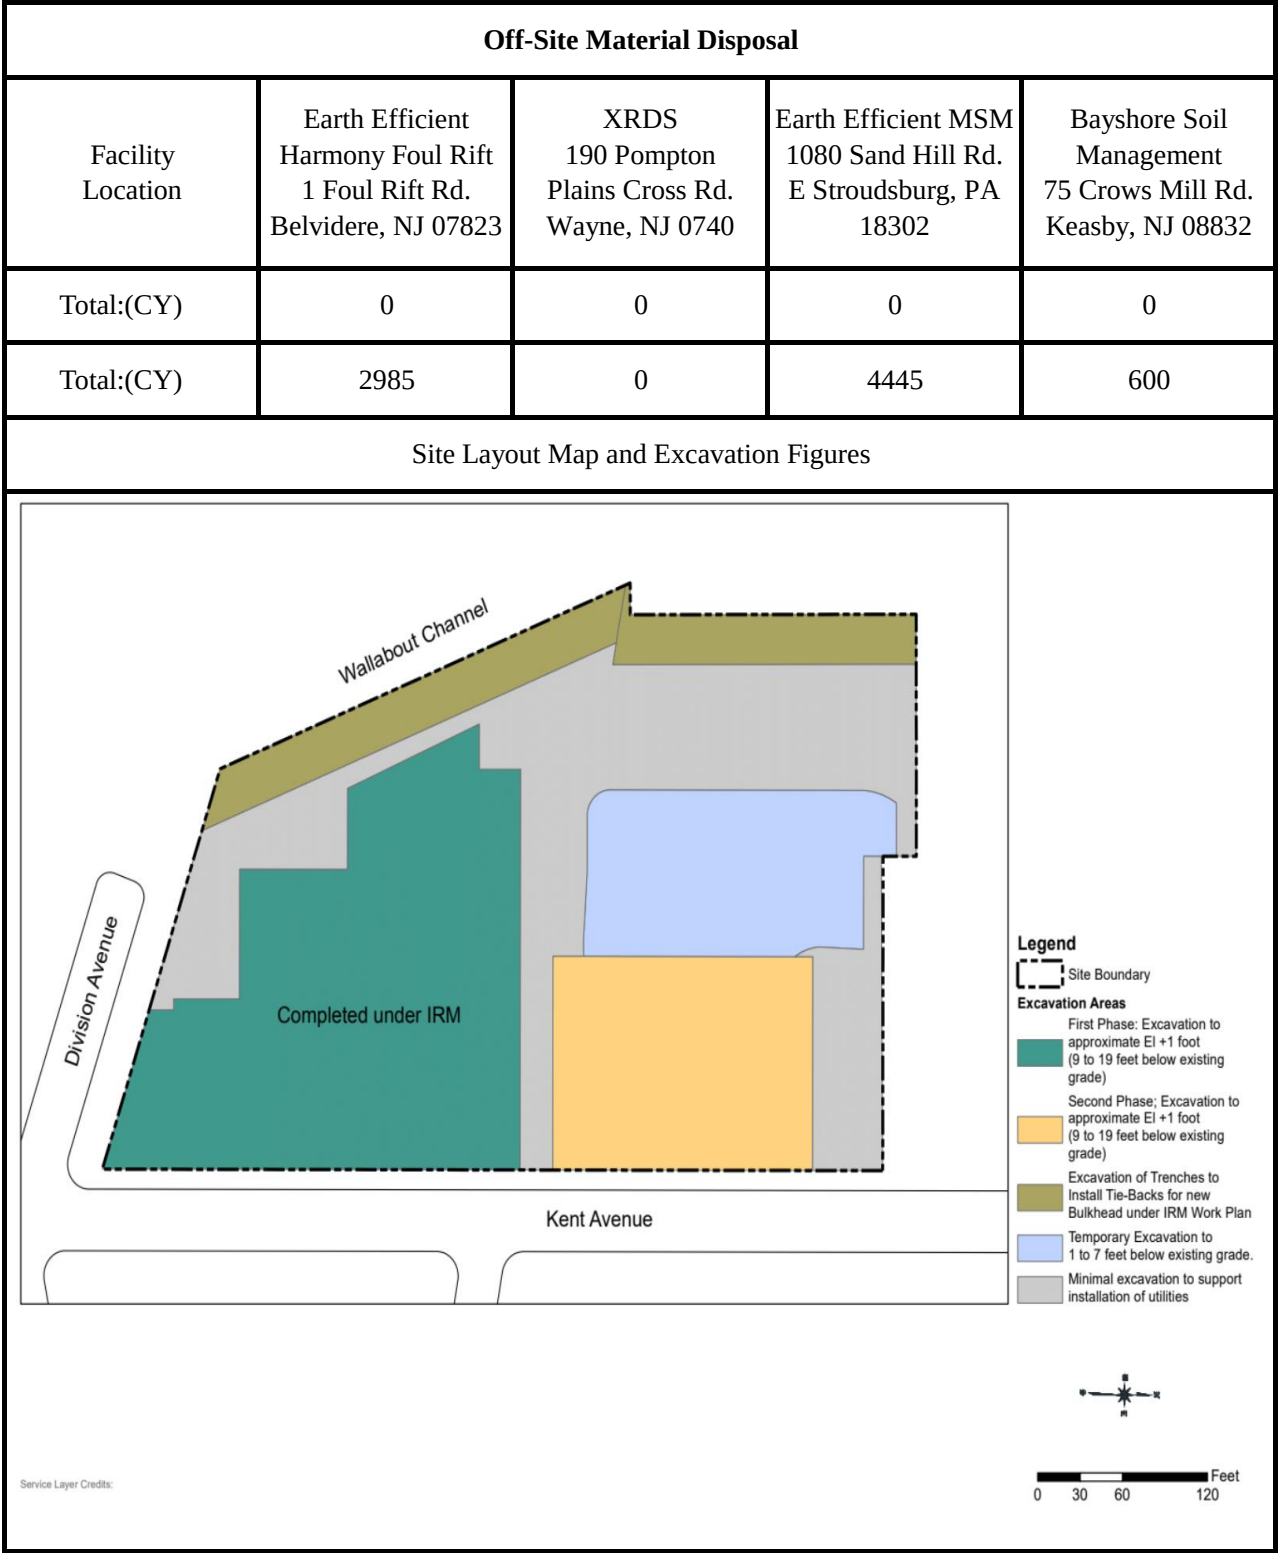

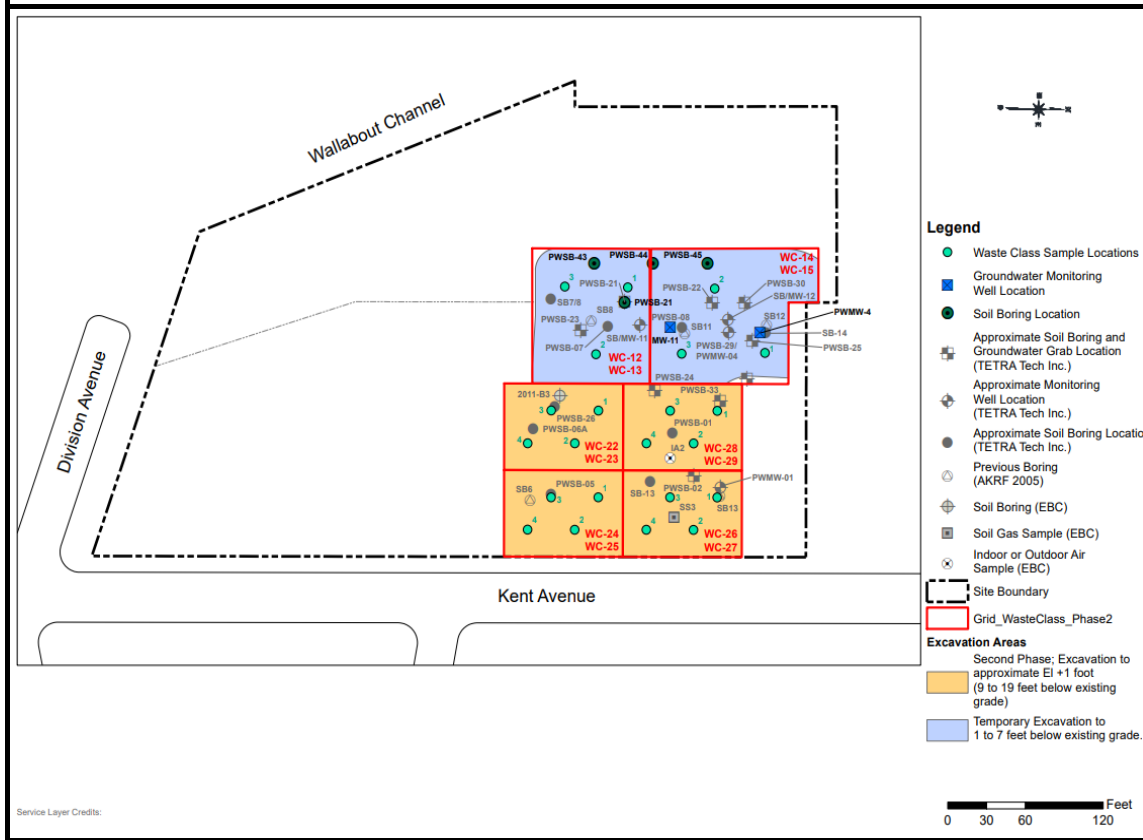
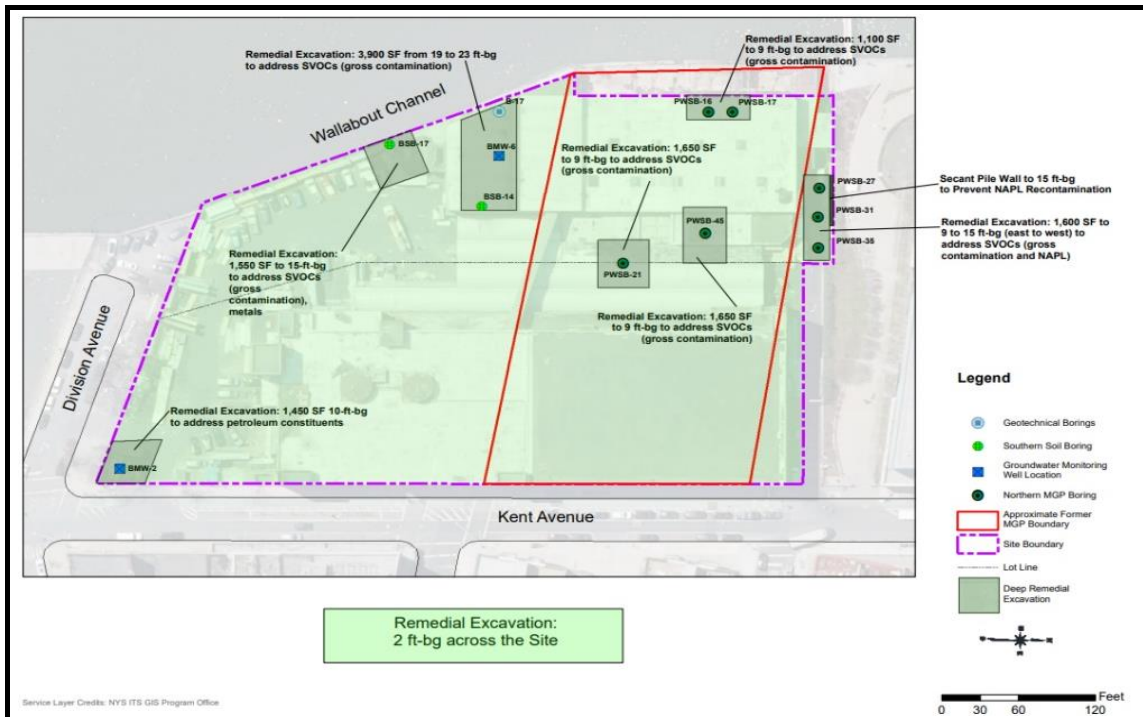


Photo 1:

View of pile installation and soil excavation facing southeast.



Photo 2:

View of pile installation and site conditions facing south.

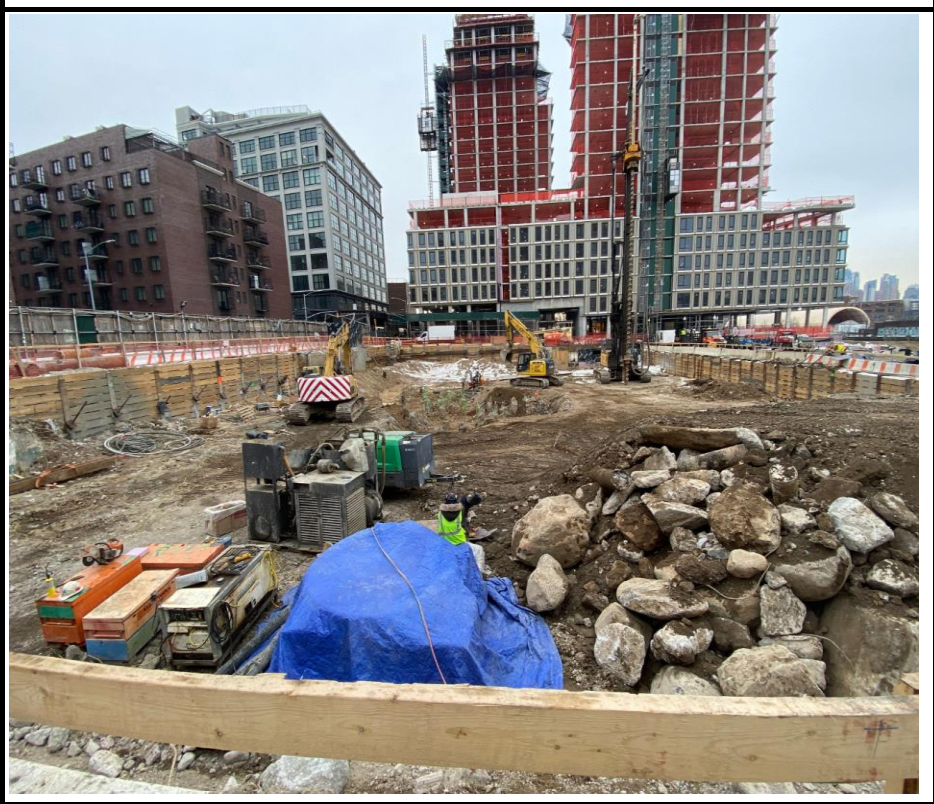


Photo 3:
View of soil
excavation facing
southeast.




Photo 4:
View of Site
conditions and
activities facing
northeast.



CAMP:
Downwind
Particulates

Dust Levels


0.031 mg/m³ 0.032 mg/m³ 0.15

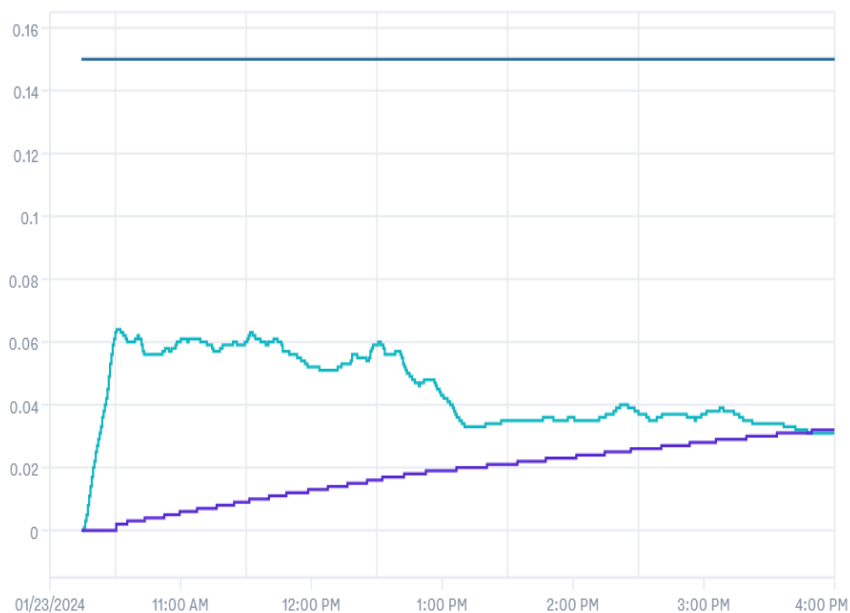

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm 5

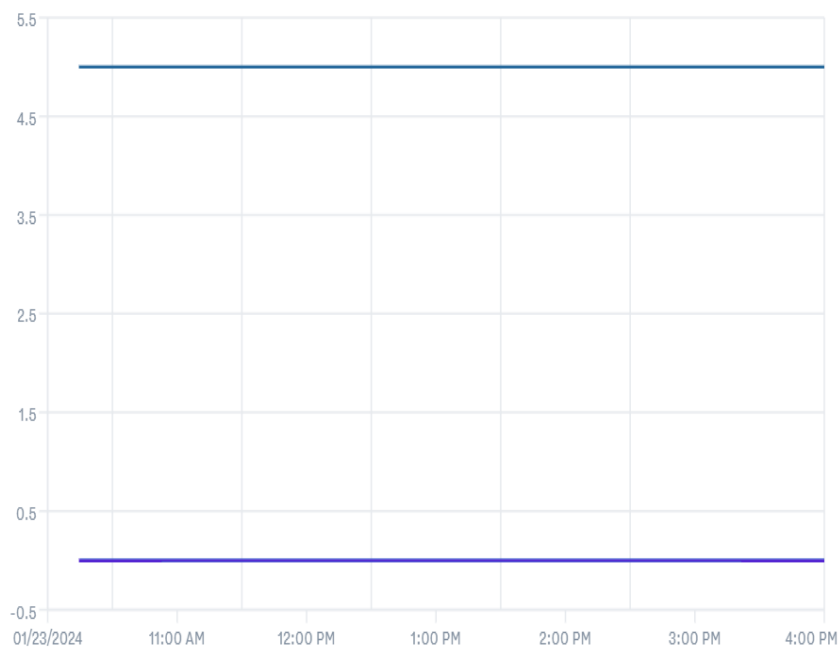

CAMP:
Upwind Particulates

Dust Levels


0.032 mg/m³ 0.034 mg/m³ 0.15

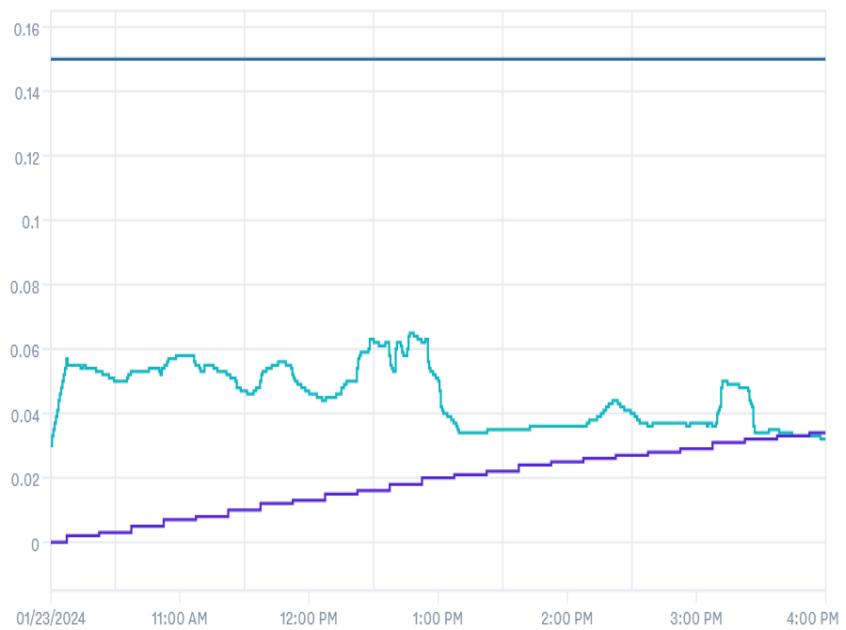

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0.005 ppm 5

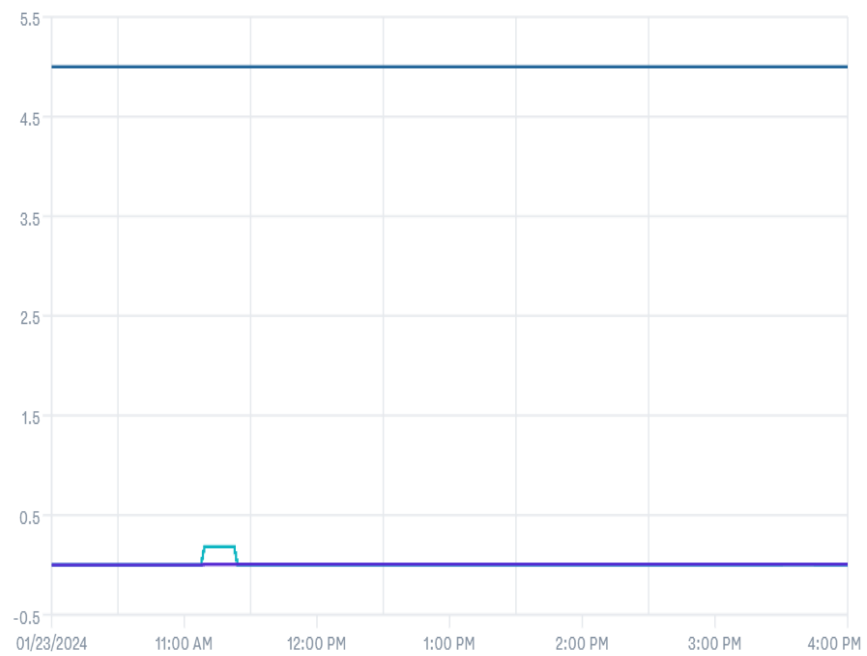

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/23/2024 10:00	1/23/2024 10:10	0.150	0.031	5	0
DW 47907	1/23/2024 10:10	1/23/2024 10:20	0.150	0	5	0
DW 47907	1/23/2024 10:20	1/23/2024 10:30	0.150	0	5	0
DW 47907	1/23/2024 10:30	1/23/2024 10:40	0.150	0.003	5	0
DW 47907	1/23/2024 10:40	1/23/2024 10:50	0.150	0.004	5	0
DW 47907	1/23/2024 10:50	1/23/2024 11:00	0.150	0.006	5	0
DW 47907	1/23/2024 11:00	1/23/2024 11:10	0.150	0.007	5	0
DW 47907	1/23/2024 11:10	1/23/2024 11:20	0.150	0.008	5	0
DW 47907	1/23/2024 11:20	1/23/2024 11:30	0.150	0.009	5	0
DW 47907	1/23/2024 11:30	1/23/2024 11:40	0.150	0.01	5	0
DW 47907	1/23/2024 11:40	1/23/2024 11:50	0.150	0.012	5	0
DW 47907	1/23/2024 11:50	1/23/2024 12:00	0.150	0.013	5	0
DW 47907	1/23/2024 12:00	1/23/2024 12:10	0.150	0.014	5	0
DW 47907	1/23/2024 12:10	1/23/2024 12:20	0.150	0.015	5	0
DW 47907	1/23/2024 12:20	1/23/2024 12:30	0.150	0.016	5	0
DW 47907	1/23/2024 12:30	1/23/2024 12:40	0.150	0.017	5	0
DW 47907	1/23/2024 12:40	1/23/2024 12:50	0.150	0.018	5	0
DW 47907	1/23/2024 12:50	1/23/2024 13:00	0.150	0.019	5	0
DW 47907	1/23/2024 13:00	1/23/2024 13:10	0.150	0.02	5	0
DW 47907	1/23/2024 13:10	1/23/2024 13:20	0.150	0.02	5	0
DW 47907	1/23/2024 13:20	1/23/2024 13:30	0.150	0.021	5	0
DW 47907	1/23/2024 13:30	1/23/2024 13:40	0.150	0.022	5	0
DW 47907	1/23/2024 13:40	1/23/2024 13:50	0.150	0.023	5	0
DW 47907	1/23/2024 13:50	1/23/2024 14:00	0.150	0.023	5	0
DW 47907	1/23/2024 14:00	1/23/2024 14:10	0.150	0.024	5	0
DW 47907	1/23/2024 14:10	1/23/2024 14:20	0.150	0.025	5	0
DW 47907	1/23/2024 14:20	1/23/2024 14:30	0.150	0.026	5	0
DW 47907	1/23/2024 14:30	1/23/2024 14:40	0.150	0.026	5	0
DW 47907	1/23/2024 14:40	1/23/2024 14:50	0.150	0.027	5	0
DW 47907	1/23/2024 14:50	1/23/2024 15:00	0.150	0.028	5	0
DW 47907	1/23/2024 15:00	1/23/2024 15:10	0.150	0.029	5	0
DW 47907	1/23/2024 15:10	1/23/2024 15:20	0.150	0.03	5	0
DW 47907	1/23/2024 15:20	1/23/2024 15:30	0.150	0.03	5	0
DW 47907	1/23/2024 15:30	1/23/2024 15:40	0.150	0.031	5	0
DW 47907	1/23/2024 15:40	1/23/2024 15:50	0.150	0.032	5	0
DW 47907	1/23/2024 15:50	1/23/2024 16:00	0.150	0.032	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/23/2024 10:00	1/23/2024 10:10	0.150	0.002	5	0
UW 212221	1/23/2024 10:10	1/23/2024 10:20	0.150	0.002	5	0
UW 212221	1/23/2024 10:20	1/23/2024 10:30	0.150	0.003	5	0
UW 212221	1/23/2024 10:30	1/23/2024 10:40	0.150	0.005	5	0
UW 212221	1/23/2024 10:40	1/23/2024 10:50	0.150	0.005	5	0
UW 212221	1/23/2024 10:50	1/23/2024 11:00	0.150	0.007	5	0
UW 212221	1/23/2024 11:00	1/23/2024 11:10	0.150	0.008	5	0.005
UW 212221	1/23/2024 11:10	1/23/2024 11:20	0.150	0.008	5	0.005
UW 212221	1/23/2024 11:20	1/23/2024 11:30	0.150	0.01	5	0.005
UW 212221	1/23/2024 11:30	1/23/2024 11:40	0.150	0.012	5	0.005
UW 212221	1/23/2024 11:40	1/23/2024 11:50	0.150	0.012	5	0.005
UW 212221	1/23/2024 11:50	1/23/2024 12:00	0.150	0.013	5	0.005
UW 212221	1/23/2024 12:00	1/23/2024 12:10	0.150	0.015	5	0.005
UW 212221	1/23/2024 12:10	1/23/2024 12:20	0.150	0.015	5	0.005
UW 212221	1/23/2024 12:20	1/23/2024 12:30	0.150	0.016	5	0.005
UW 212221	1/23/2024 12:30	1/23/2024 12:40	0.150	0.018	5	0.005
UW 212221	1/23/2024 12:40	1/23/2024 12:50	0.150	0.018	5	0.005
UW 212221	1/23/2024 12:50	1/23/2024 13:00	0.150	0.02	5	0.005
UW 212221	1/23/2024 13:00	1/23/2024 13:10	0.150	0.021	5	0.005
UW 212221	1/23/2024 13:10	1/23/2024 13:20	0.150	0.021	5	0.005
UW 212221	1/23/2024 13:20	1/23/2024 13:30	0.150	0.022	5	0.005
UW 212221	1/23/2024 13:30	1/23/2024 13:40	0.150	0.024	5	0.005
UW 212221	1/23/2024 13:40	1/23/2024 13:50	0.150	0.024	5	0.005
UW 212221	1/23/2024 13:50	1/23/2024 14:00	0.150	0.025	5	0.005
UW 212221	1/23/2024 14:00	1/23/2024 14:10	0.150	0.026	5	0.005
UW 212221	1/23/2024 14:10	1/23/2024 14:20	0.150	0.026	5	0.005
UW 212221	1/23/2024 14:20	1/23/2024 14:30	0.150	0.027	5	0.005
UW 212221	1/23/2024 14:30	1/23/2024 14:40	0.150	0.028	5	0.005
UW 212221	1/23/2024 14:40	1/23/2024 14:50	0.150	0.028	5	0.005
UW 212221	1/23/2024 14:50	1/23/2024 15:00	0.150	0.029	5	0.005
UW 212221	1/23/2024 15:00	1/23/2024 15:10	0.150	0.031	5	0.005
UW 212221	1/23/2024 15:10	1/23/2024 15:20	0.150	0.031	5	0.005
UW 212221	1/23/2024 15:20	1/23/2024 15:30	0.150	0.032	5	0.005
UW 212221	1/23/2024 15:30	1/23/2024 15:40	0.150	0.033	5	0.005
UW 212221	1/23/2024 15:40	1/23/2024 15:50	0.150	0.033	5	0.005
UW 212221	1/23/2024 15:50	1/23/2024 16:00	0.150	0.034	5	0.005

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/23/2024 10:00	1/23/2024 10:10	0.150	0	5	0
PER1 50057	1/23/2024 10:10	1/23/2024 10:20	0.150	0	5	0
PER1 50057	1/23/2024 10:20	1/23/2024 10:30	0.150	0	5	0
PER1 50057	1/23/2024 10:30	1/23/2024 10:40	0.150	0.003	5	0
PER1 50057	1/23/2024 10:40	1/23/2024 10:50	0.150	0.005	5	0
PER1 50057	1/23/2024 10:50	1/23/2024 11:00	0.150	0.006	5	0
PER1 50057	1/23/2024 11:00	1/23/2024 11:10	0.150	0.008	5	0
PER1 50057	1/23/2024 11:10	1/23/2024 11:20	0.150	0.009	5	0
PER1 50057	1/23/2024 11:20	1/23/2024 11:30	0.150	0.01	5	0
PER1 50057	1/23/2024 11:30	1/23/2024 11:40	0.150	0.012	5	0
PER1 50057	1/23/2024 11:40	1/23/2024 11:50	0.150	0.013	5	0
PER1 50057	1/23/2024 11:50	1/23/2024 12:00	0.150	0.014	5	0
PER1 50057	1/23/2024 12:00	1/23/2024 12:10	0.150	0.015	5	0
PER1 50057	1/23/2024 12:10	1/23/2024 12:20	0.150	0.016	5	0
PER1 50057	1/23/2024 12:20	1/23/2024 12:30	0.150	0.018	5	0
PER1 50057	1/23/2024 12:30	1/23/2024 12:40	0.150	0.019	5	0
PER1 50057	1/23/2024 12:40	1/23/2024 12:50	0.150	0.02	5	0
PER1 50057	1/23/2024 12:50	1/23/2024 13:00	0.150	0.021	5	0
PER1 50057	1/23/2024 13:00	1/23/2024 13:10	0.150	0.022	5	0
PER1 50057	1/23/2024 13:10	1/23/2024 13:20	0.150	0.022	5	0
PER1 50057	1/23/2024 13:20	1/23/2024 13:30	0.150	0.023	5	0
PER1 50057	1/23/2024 13:30	1/23/2024 13:40	0.150	0.024	5	0
PER1 50057	1/23/2024 13:40	1/23/2024 13:50	0.150	0.025	5	0
PER1 50057	1/23/2024 13:50	1/23/2024 14:00	0.150	0.026	5	0
PER1 50057	1/23/2024 14:00	1/23/2024 14:10	0.150	0.027	5	0
PER1 50057	1/23/2024 14:10	1/23/2024 14:20	0.150	0.028	5	0
PER1 50057	1/23/2024 14:20	1/23/2024 14:30	0.150	0.029	5	0
PER1 50057	1/23/2024 14:30	1/23/2024 14:40	0.150	0.029	5	0
PER1 50057	1/23/2024 14:40	1/23/2024 14:50	0.150	0.03	5	0
PER1 50057	1/23/2024 14:50	1/23/2024 15:00	0.150	0.031	5	0
PER1 50057	1/23/2024 15:00	1/23/2024 15:10	0.150	0.032	5	0
PER1 50057	1/23/2024 15:10	1/23/2024 15:20	0.150	0.033	5	0
PER1 50057	1/23/2024 15:20	1/23/2024 15:30	0.150	0.034	5	0
PER1 50057	1/23/2024 15:30	1/23/2024 15:40	0.150	0.034	5	0
PER1 50057	1/23/2024 15:40	1/23/2024 15:50	0.150	0.035	5	0
PER1 50057	1/23/2024 15:50	1/23/2024 16:00	0.150	0.036	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/23/2024 10:00	1/23/2024 10:10	0.150	0.028	5	0
PER2 46495	1/23/2024 10:10	1/23/2024 10:20	0.150	0	5	0
PER2 46495	1/23/2024 10:20	1/23/2024 10:30	0.150	0.002	5	0
PER2 46495	1/23/2024 10:30	1/23/2024 10:40	0.150	0.004	5	0
PER2 46495	1/23/2024 10:40	1/23/2024 10:50	0.150	0.005	5	0
PER2 46495	1/23/2024 10:50	1/23/2024 11:00	0.150	0.006	5	0
PER2 46495	1/23/2024 11:00	1/23/2024 11:10	0.150	0.008	5	0
PER2 46495	1/23/2024 11:10	1/23/2024 11:20	0.150	0.01	5	0
PER2 46495	1/23/2024 11:20	1/23/2024 11:30	0.150	0.011	5	0
PER2 46495	1/23/2024 11:30	1/23/2024 11:40	0.150	0.012	5	0
PER2 46495	1/23/2024 11:40	1/23/2024 11:50	0.150	0.014	5	0
PER2 46495	1/23/2024 11:50	1/23/2024 12:00	0.150	0.015	5	0
PER2 46495	1/23/2024 12:00	1/23/2024 12:10	0.150	0.016	5	0
PER2 46495	1/23/2024 12:10	1/23/2024 12:20	0.150	0.017	5	0
PER2 46495	1/23/2024 12:20	1/23/2024 12:30	0.150	0.018	5	0
PER2 46495	1/23/2024 12:30	1/23/2024 12:40	0.150	0.019	5	0
PER2 46495	1/23/2024 12:40	1/23/2024 12:50	0.150	0.021	5	0
PER2 46495	1/23/2024 12:50	1/23/2024 13:00	0.150	0.022	5	0
PER2 46495	1/23/2024 13:00	1/23/2024 13:10	0.150	0.022	5	0
PER2 46495	1/23/2024 13:10	1/23/2024 13:20	0.150	0.023	5	0
PER2 46495	1/23/2024 13:20	1/23/2024 13:30	0.150	0.024	5	0
PER2 46495	1/23/2024 13:30	1/23/2024 13:40	0.150	0.025	5	0
PER2 46495	1/23/2024 13:40	1/23/2024 13:50	0.150	0.025	5	0
PER2 46495	1/23/2024 13:50	1/23/2024 14:00	0.150	0.026	5	0
PER2 46495	1/23/2024 14:00	1/23/2024 14:10	0.150	0.027	5	0
PER2 46495	1/23/2024 14:10	1/23/2024 14:20	0.150	0.028	5	0
PER2 46495	1/23/2024 14:20	1/23/2024 14:30	0.150	0.029	5	0
PER2 46495	1/23/2024 14:30	1/23/2024 14:40	0.150	0.03	5	0
PER2 46495	1/23/2024 14:40	1/23/2024 14:50	0.150	0.03	5	0
PER2 46495	1/23/2024 14:50	1/23/2024 15:00	0.150	0.031	5	0
PER2 46495	1/23/2024 15:00	1/23/2024 15:10	0.150	0.032	5	0
PER2 46495	1/23/2024 15:10	1/23/2024 15:20	0.150	0.033	5	0
PER2 46495	1/23/2024 15:20	1/23/2024 15:30	0.150	0.034	5	0
PER2 46495	1/23/2024 15:30	1/23/2024 15:40	0.150	0.034	5	0
PER2 46495	1/23/2024 15:40	1/23/2024 15:50	0.150	0.035	5	0
PER2 46495	1/23/2024 15:50	1/23/2024 16:00	0.150	0.035	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/24/2024

Weather: 40 deg. F, Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, drilling piles and installing SOE in A3 building location.
- 2) Export of 15 loads (approximately 300 CY) of material from WC-22, 24, 26 & 28 for off-site disposal at the Earth Efficient MSM facility.

Is the dewatering system operating: YES NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA


Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to rain.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

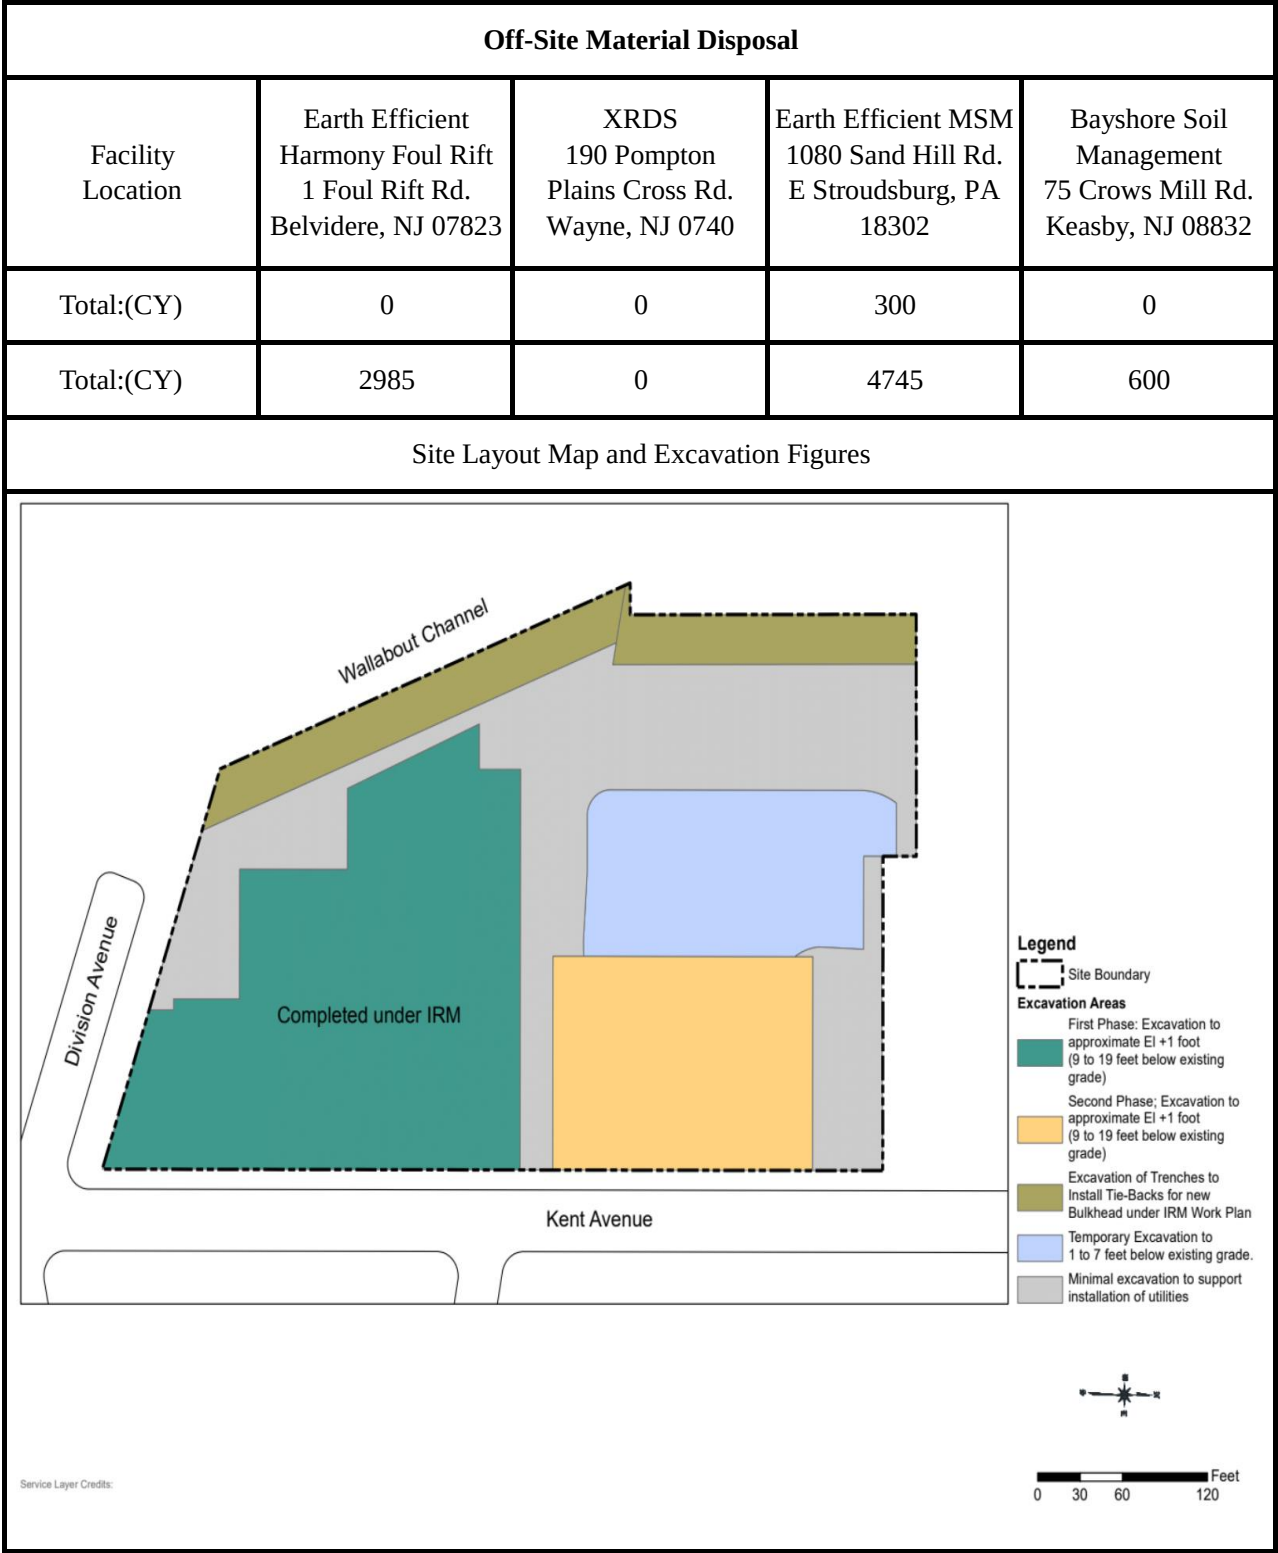

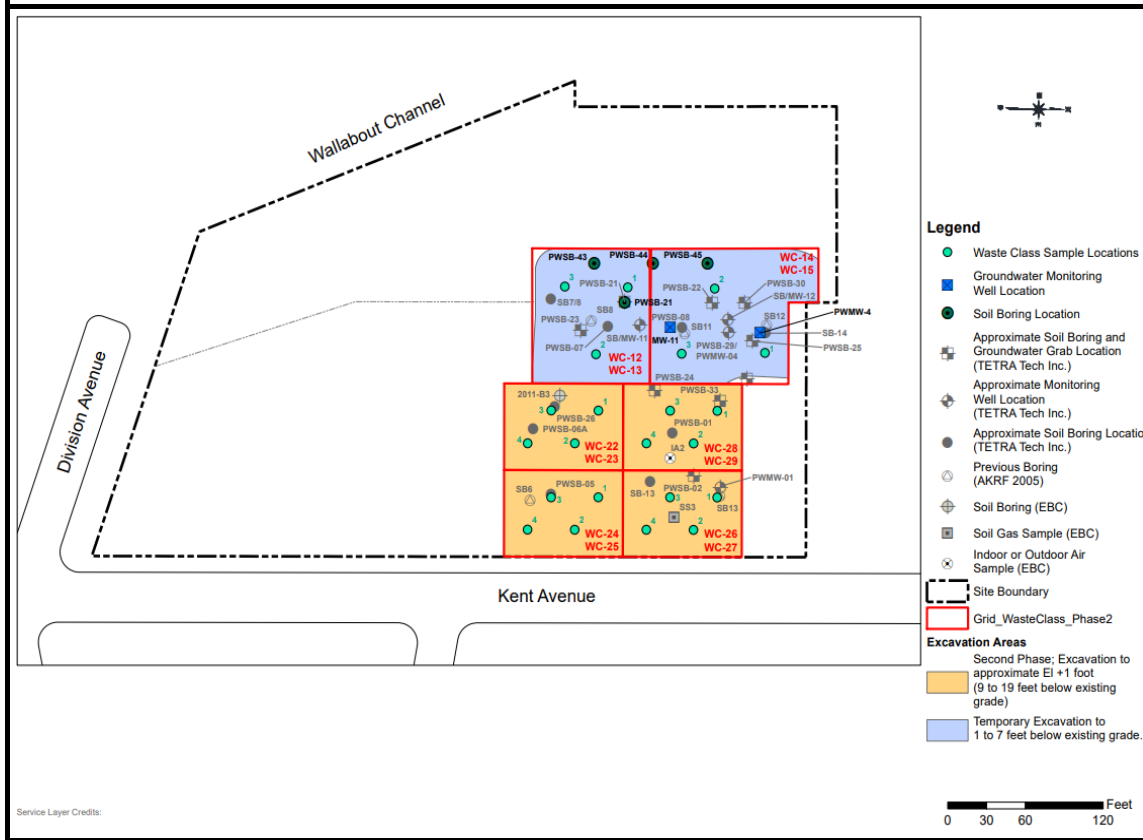
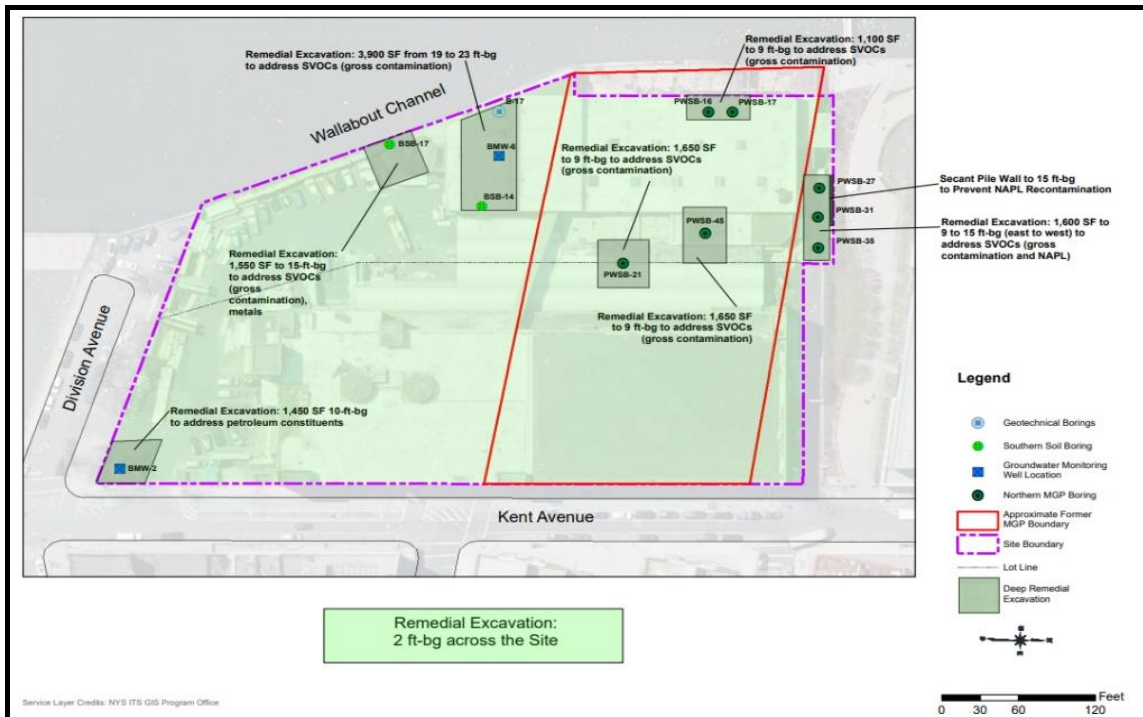


Photo 1:

View of pile installaton
and soil excavation
facing southwest.

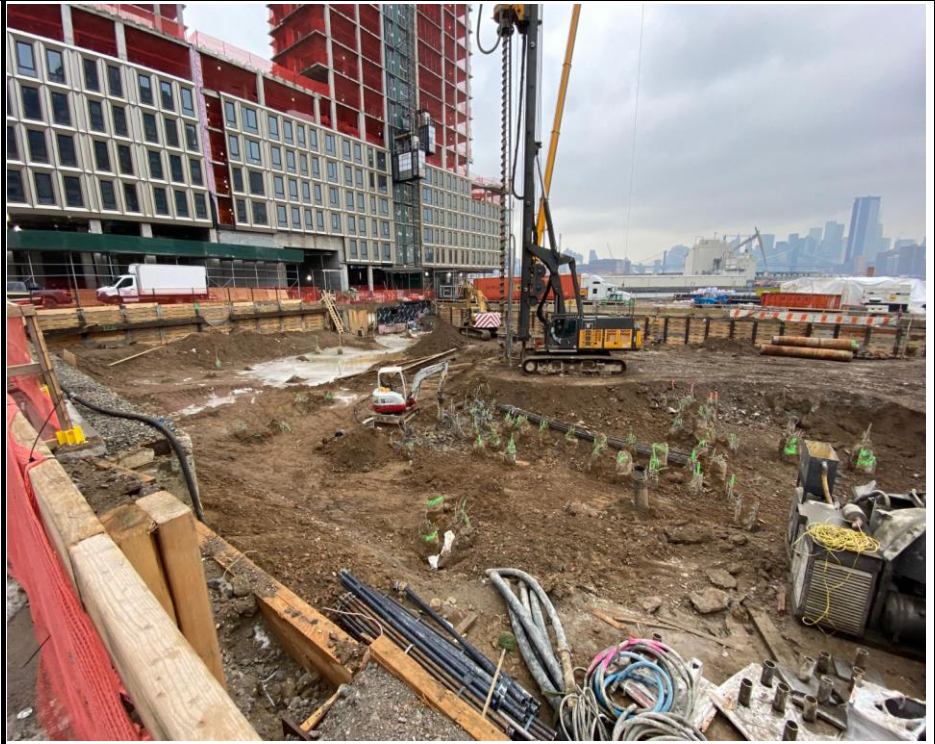


Photo 2:

View of pile installation
and site conditions facing
northeast.

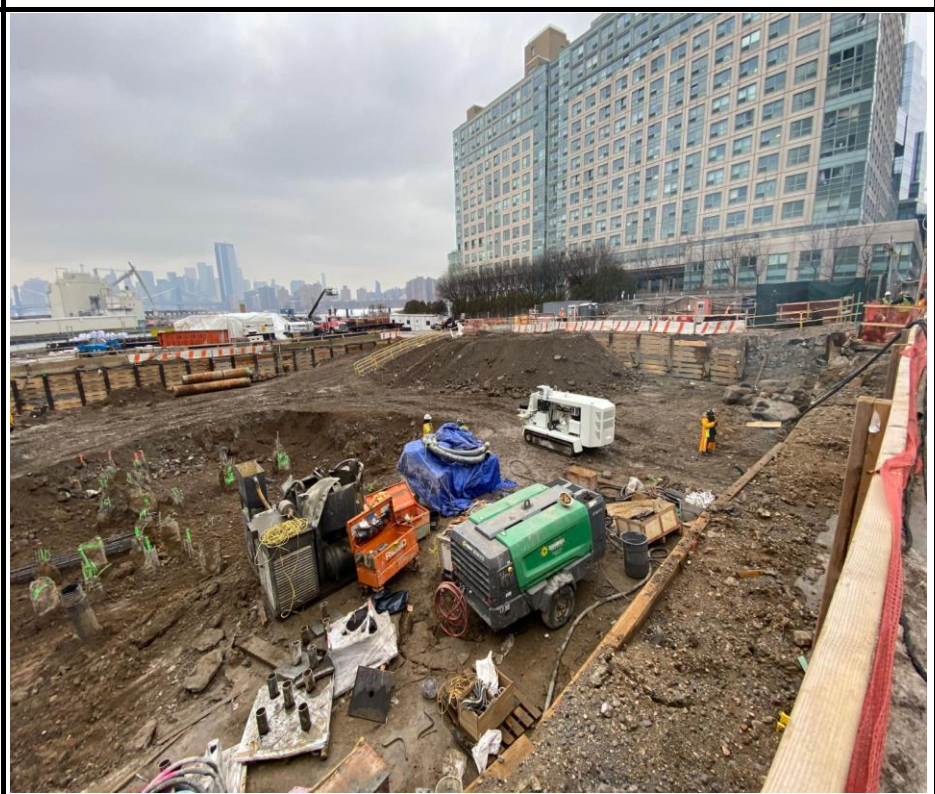


Photo 3:

View of soil excavation facing northwest.



Photo 4:

View of truck loading for off-site soil disposal.



CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/25/2024

Weather: 40 deg. F, Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

1) Alba continues excavation, drilling piles and installing SOE in A3 building location.

Is the dewatering system operating: **YES** NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA


Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to rain.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

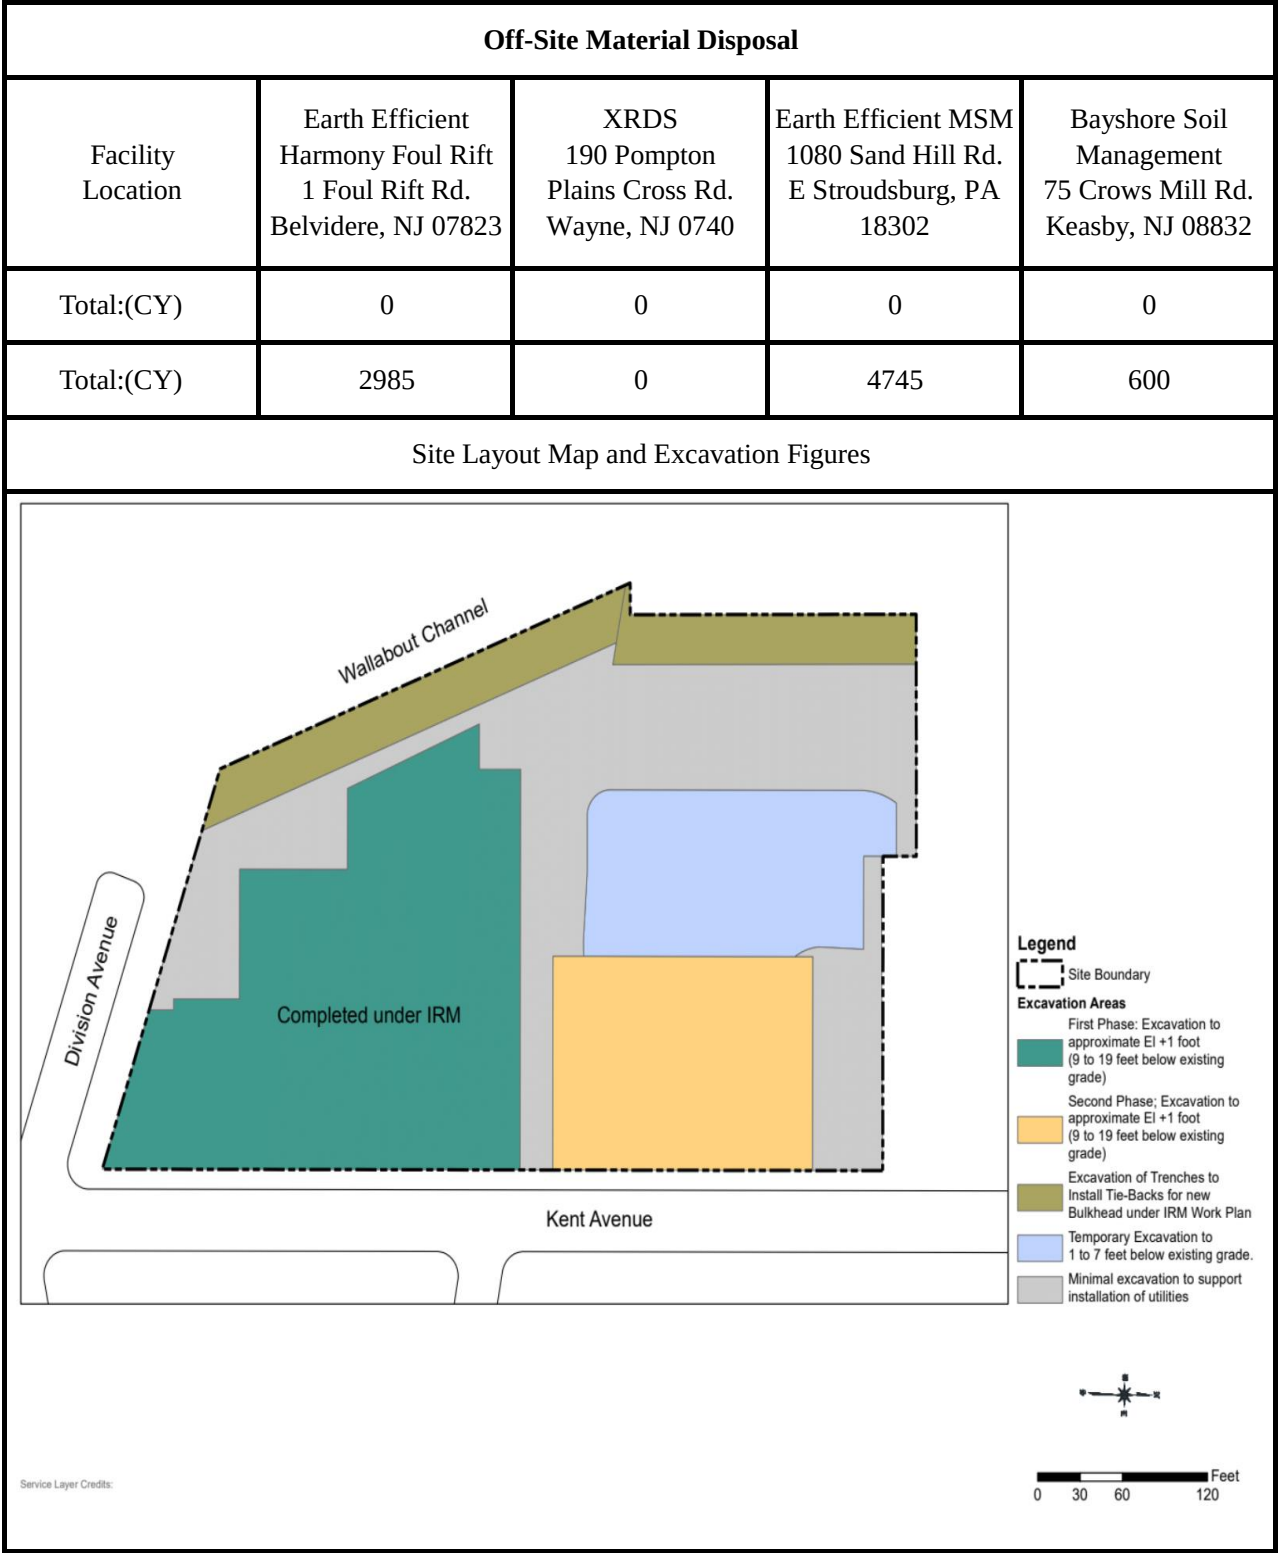

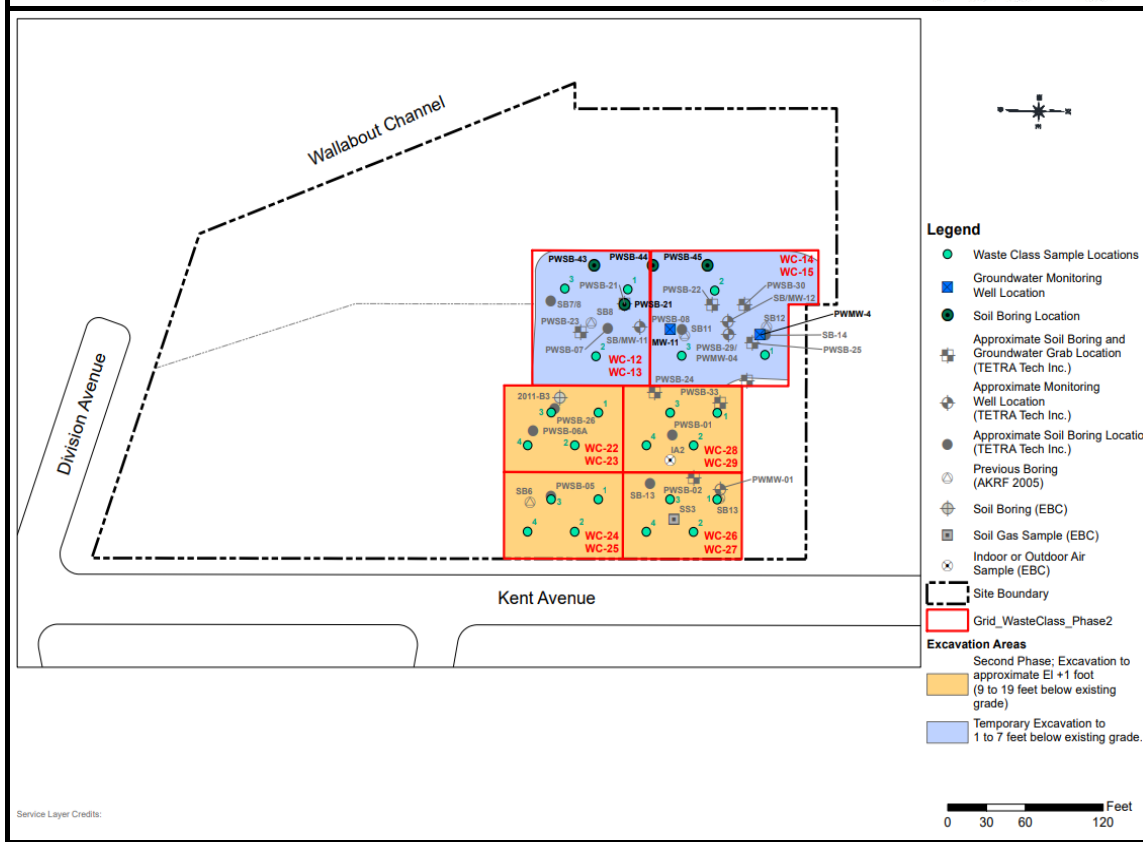
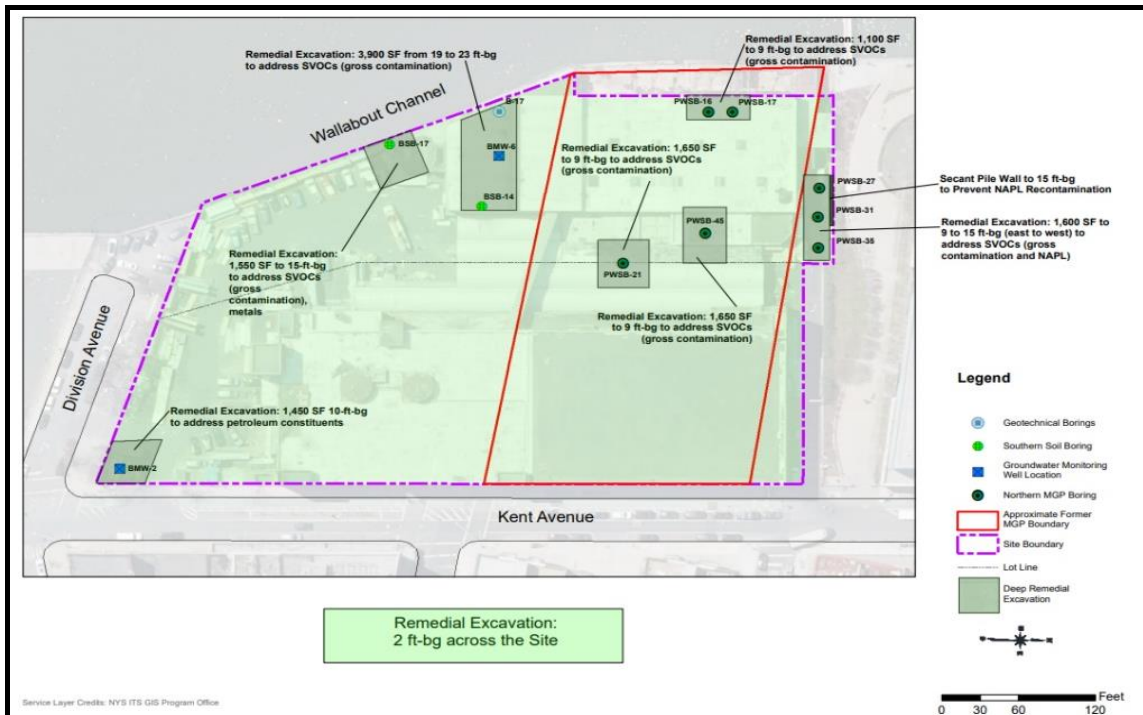


Photo 1:

View of pile installation and soil excavation facing northeast.



Photo 2:

View of pile installation and site conditions facing north.

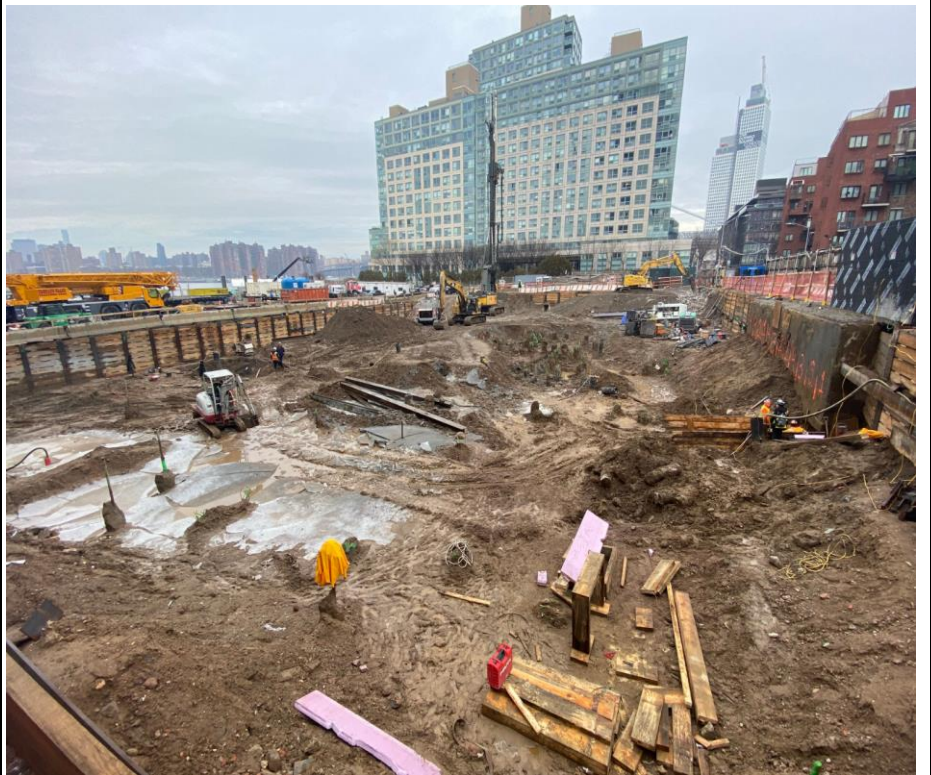



Photo 3:

View of Site
conditions facing
southeast.



Photo 4:

View of Site
conditions facing
east.

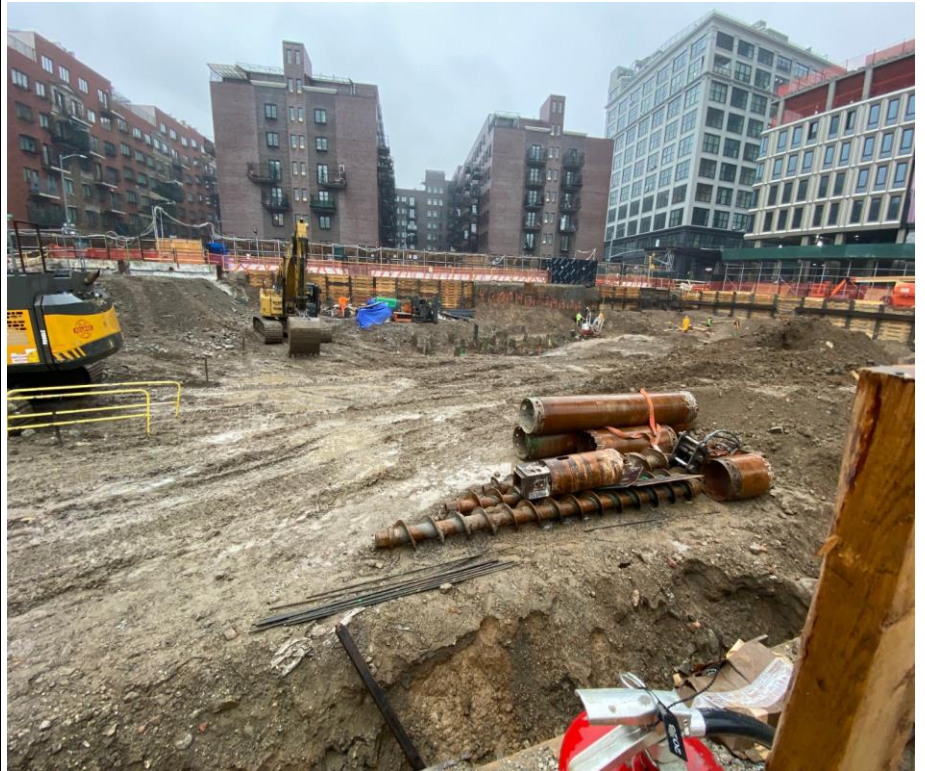

CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/26/2024

Weather: 40 deg. F, Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, exposing piles and installing SOE in A3 building location.
- 2) Import of one load of stone to refresh the trucking pad along Kent Avenue.

Is the dewatering system operating: **YES** NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA


Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to rain.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

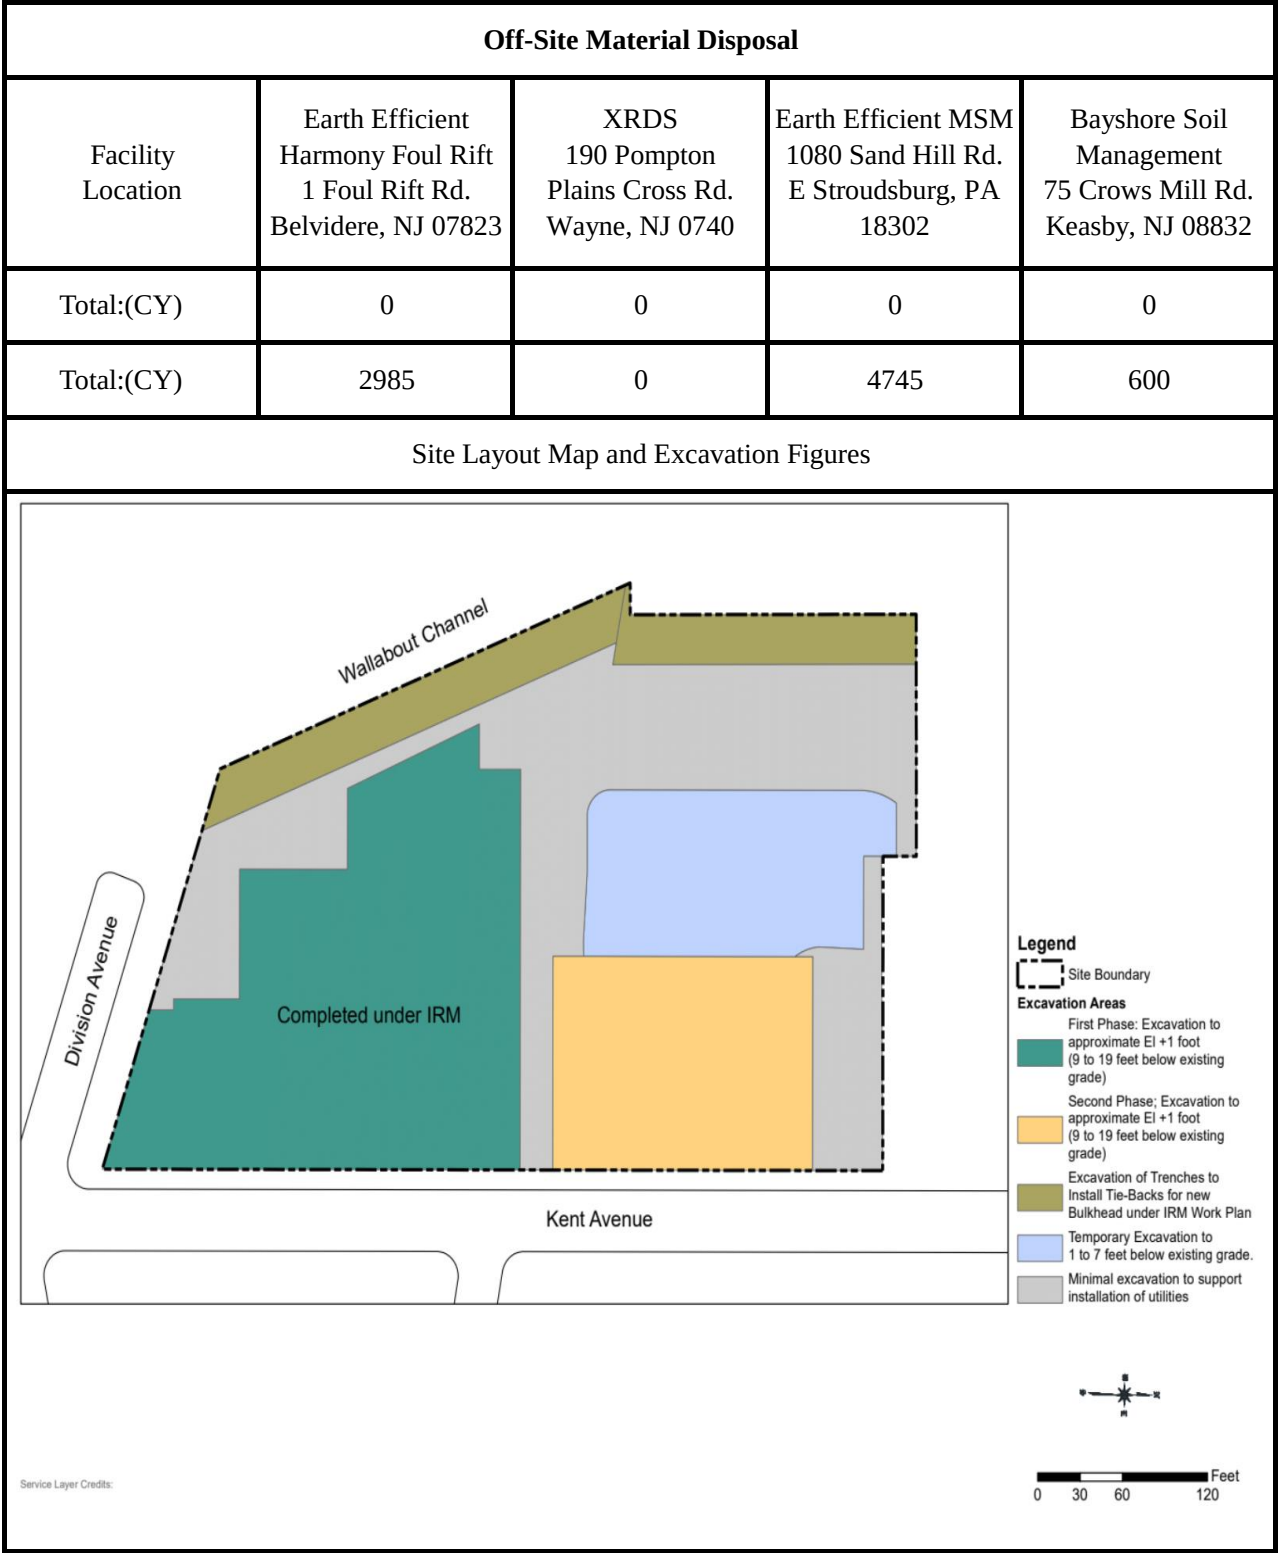

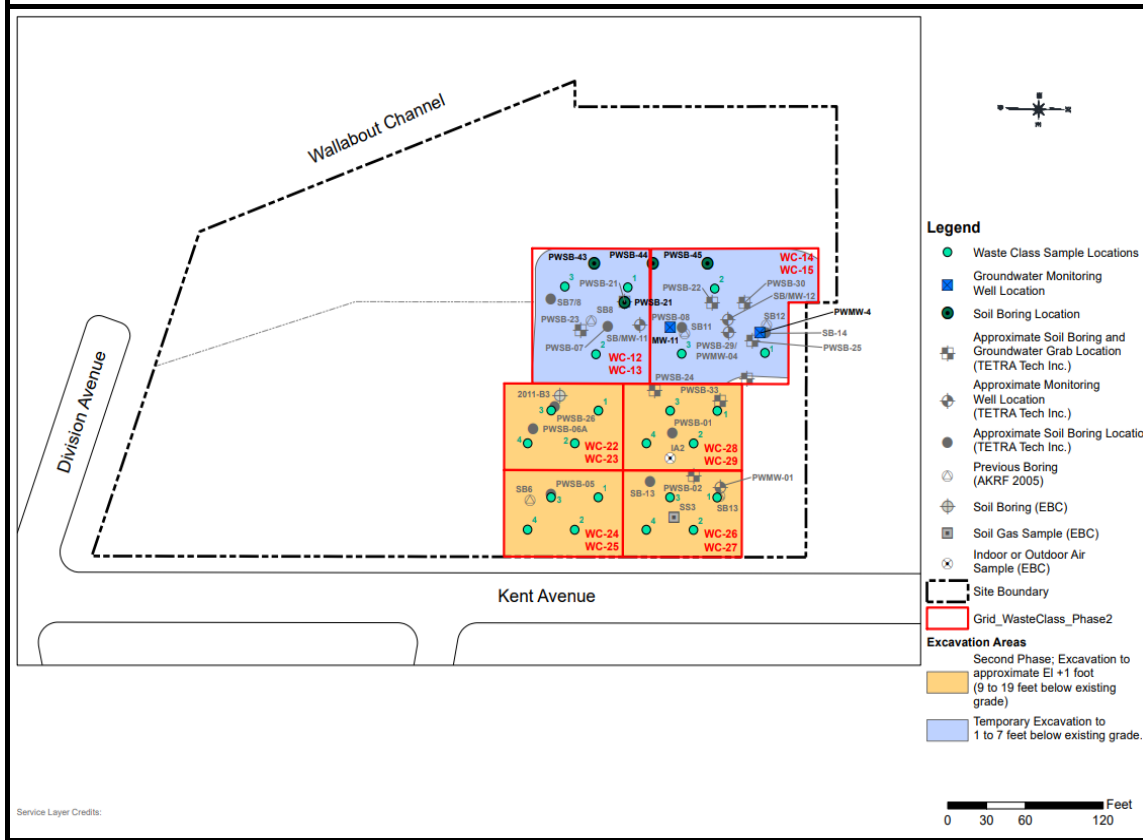
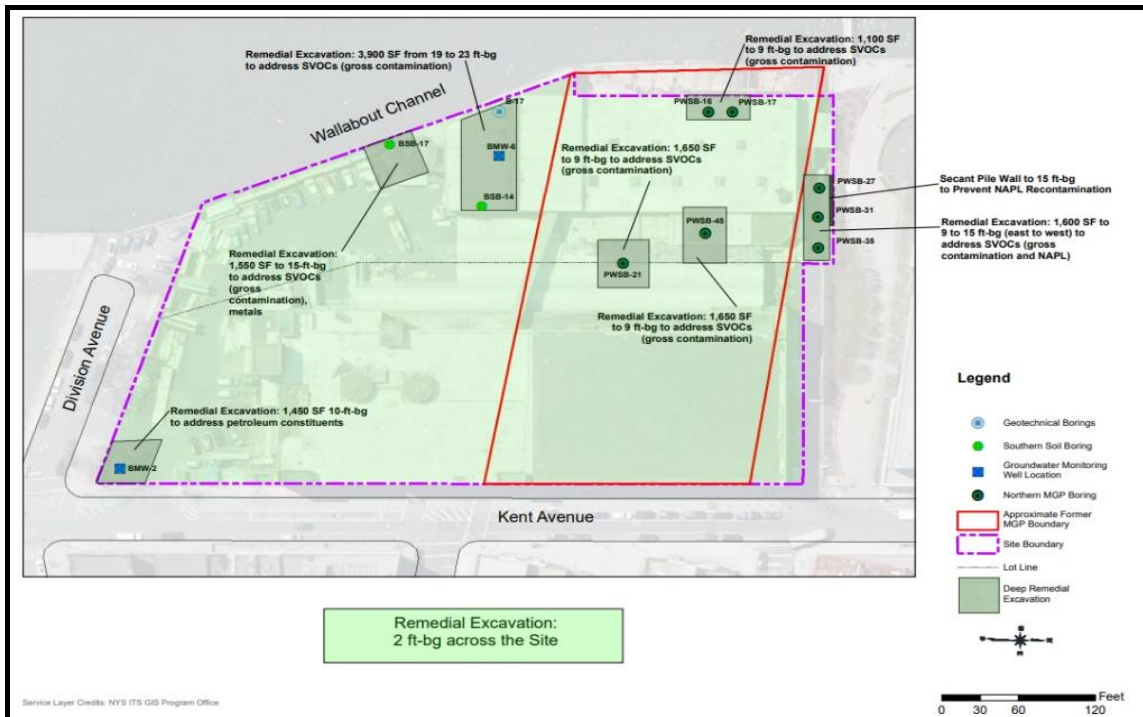


Photo 1:

View of soil excavation and Site conditions facing west.



Photo 2:

View of pile installation and site conditions facing northeast.

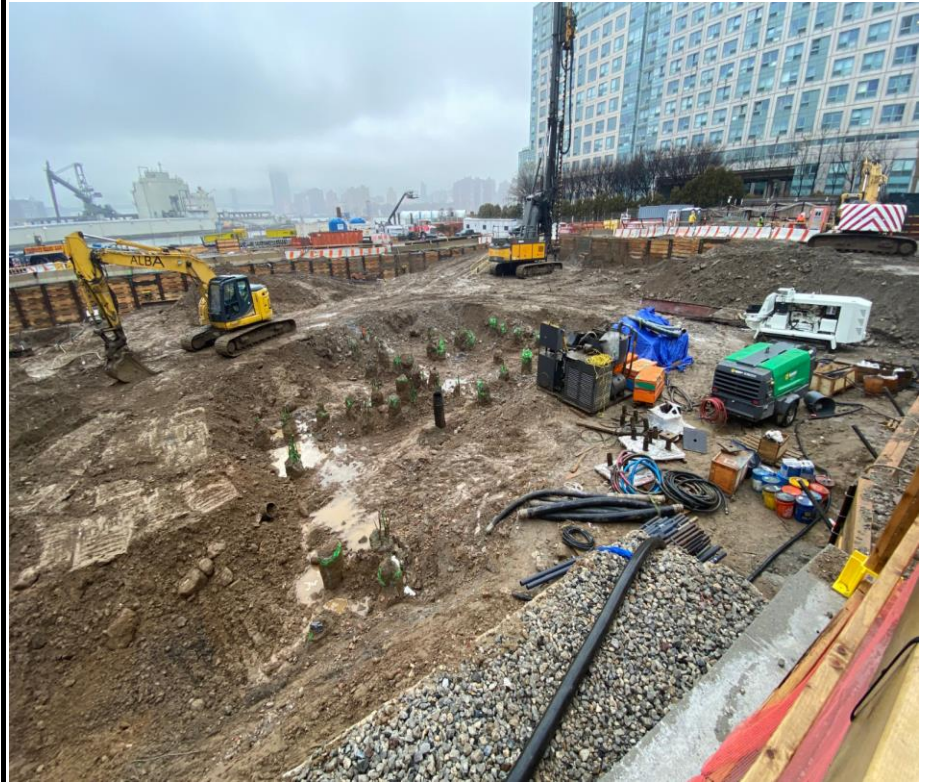


Photo 3:
View of Site
conditions facing
southeast.

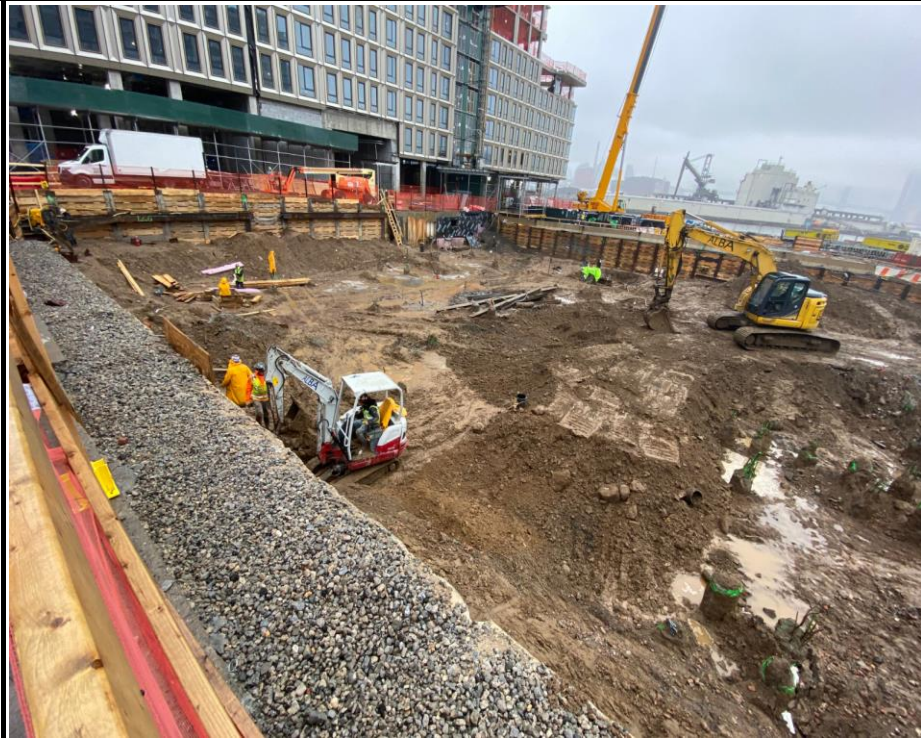


Photo 4:
View of forming of a
whaler in preparation
for development of
foundation elements.



CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA

Daily Status Report

Prepared by: C. Zaccheo

Date: 1/29/2024

Weather: 40 deg. F, Overcast/Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, exposing and drilling piles and installing SOE in A3 building location.
- 2) Import of two loads of stone to refresh the trucking pad along Division Avenue.

Is the dewatering system operating: **YES** NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA


Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.
CAMP stations were not turned on until 10AM due to rain.

Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

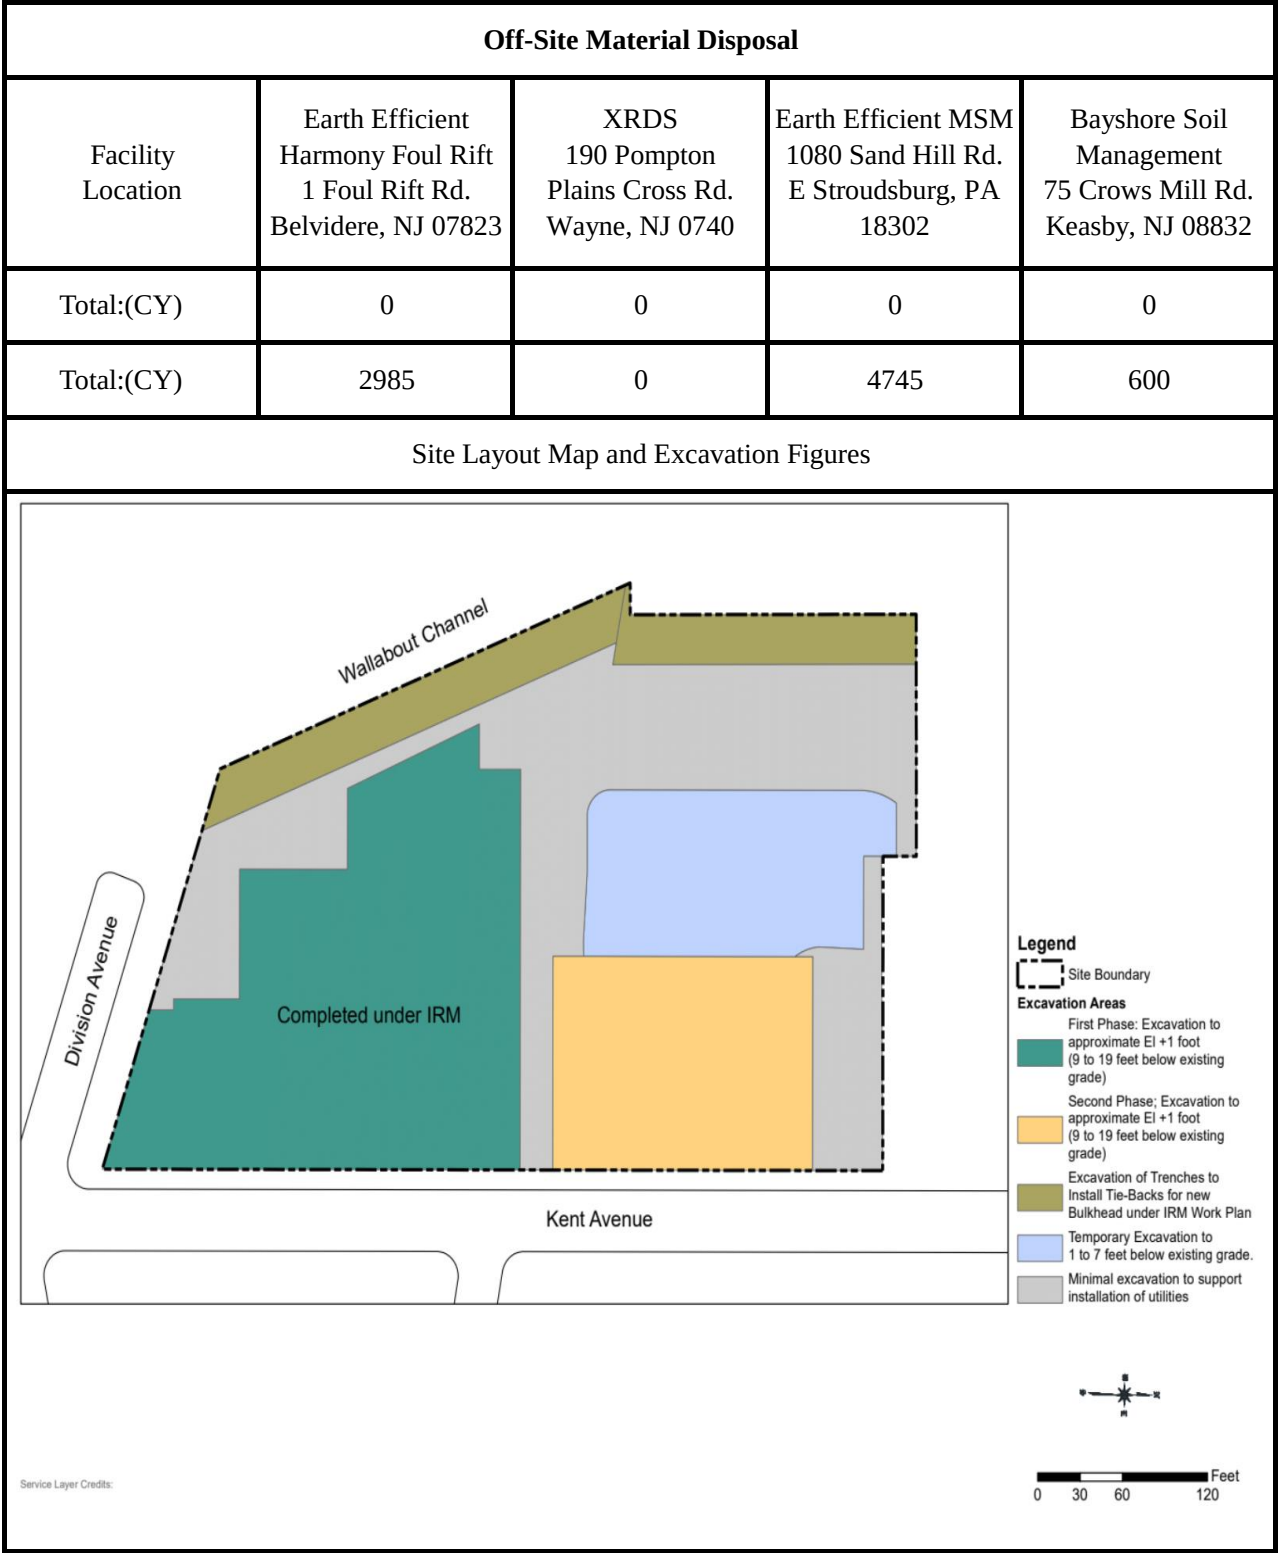

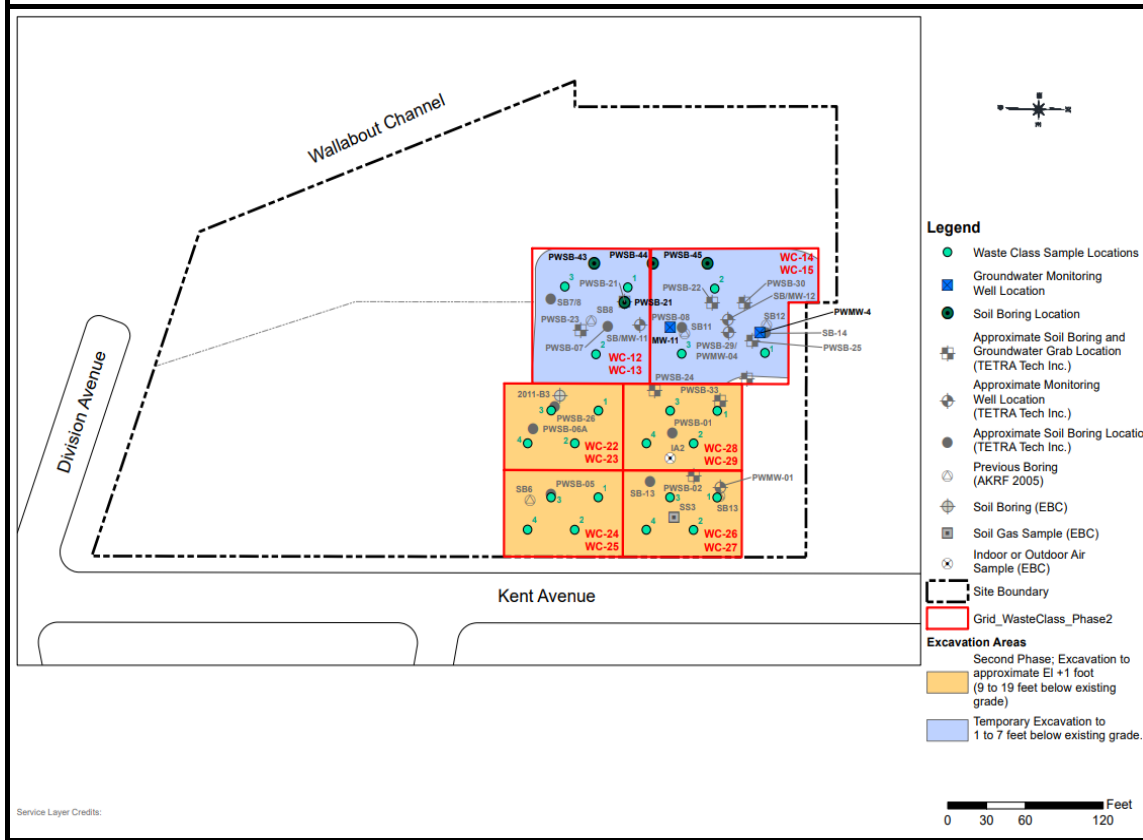
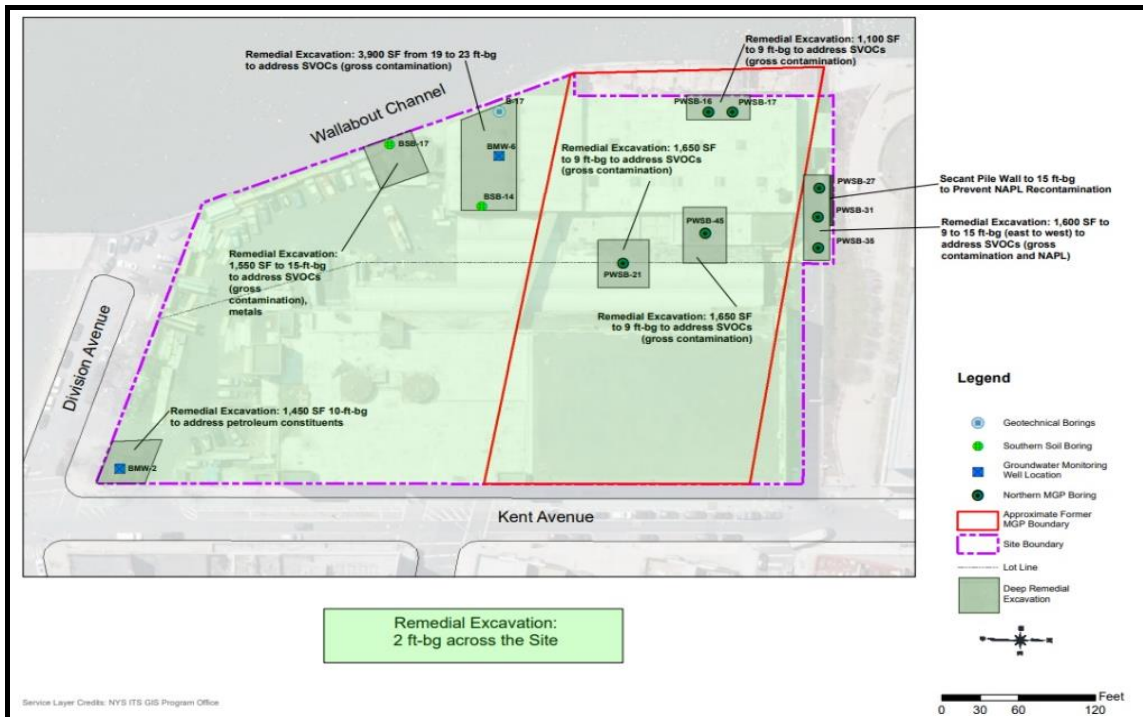


Photo 1:

View of soil excavation and Site conditions facing southeast.



Photo 2:

View of soil excavation.



Photo 3:

View of tone import
for trucking pad
along Kent Avenue.


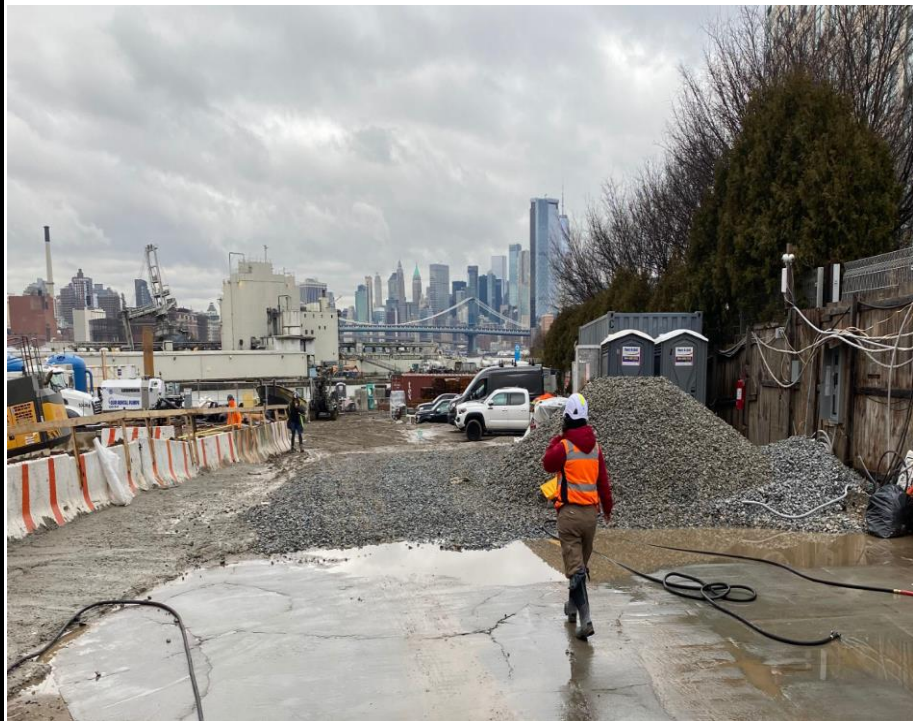



Photo 4:

View of stone import
in trucking pad along
Division Avenue.

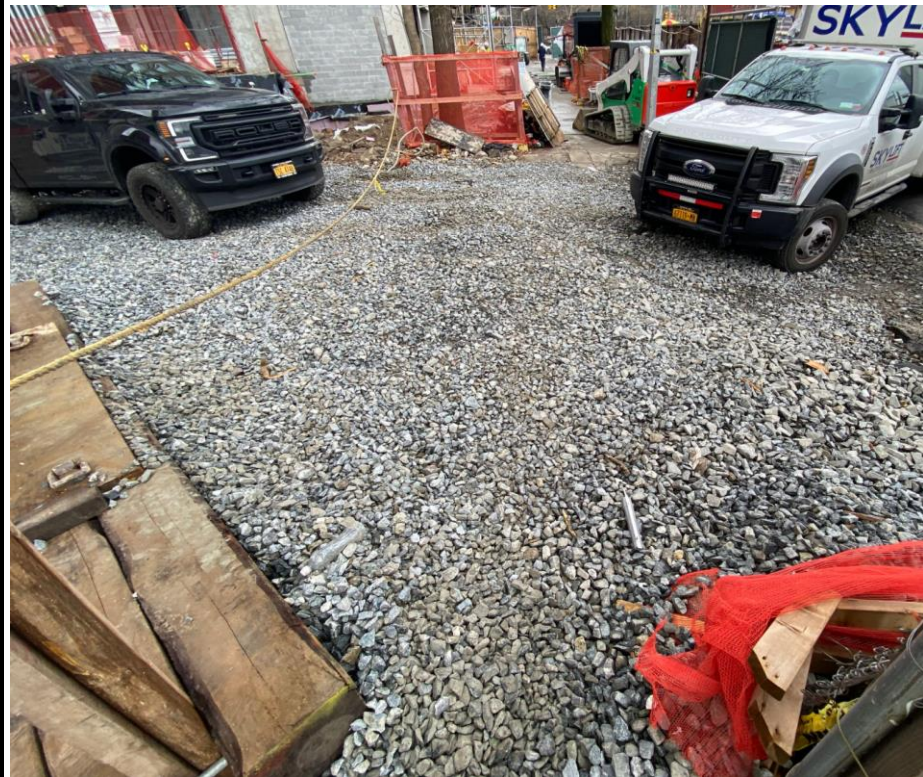


CAMP:
Downwind
Particulates

Dust Levels

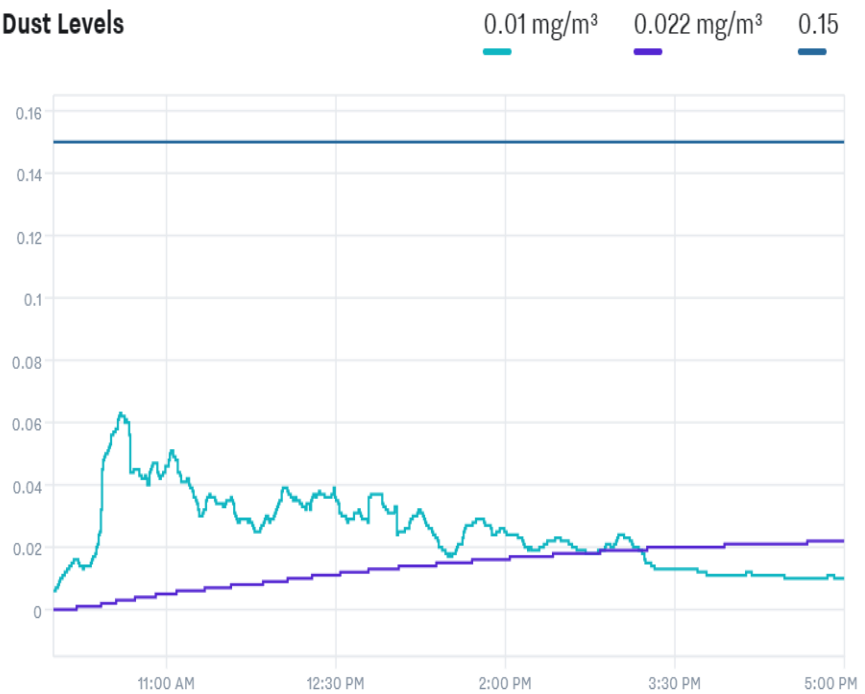

CAMP:
Downwind VOCs


VOC Levels

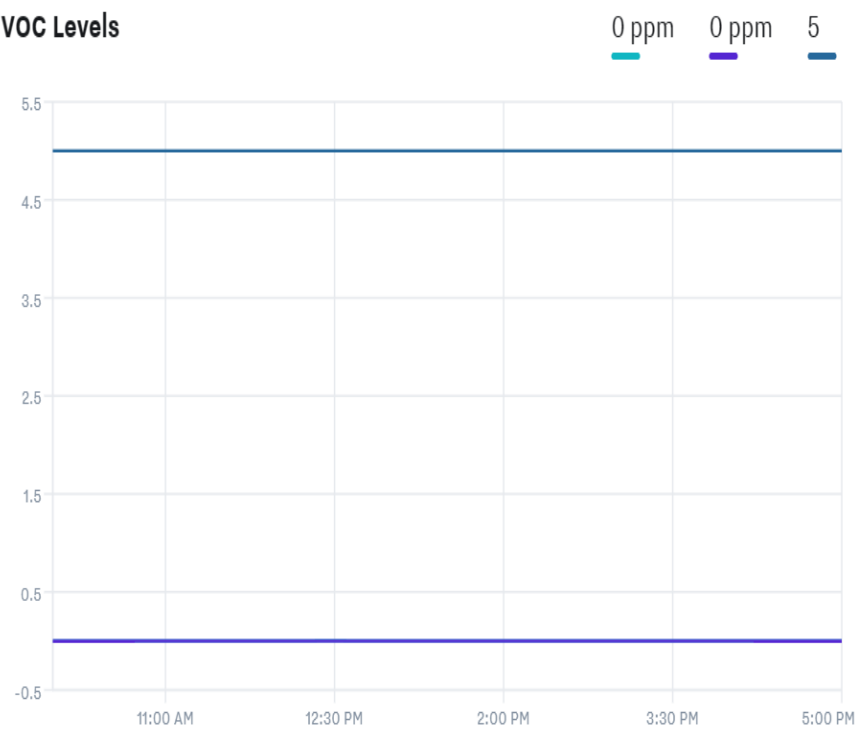

CAMP:
Upwind Particulates

Dust Levels


0.016 mg/m³ 0.021 mg/m³ 0.15

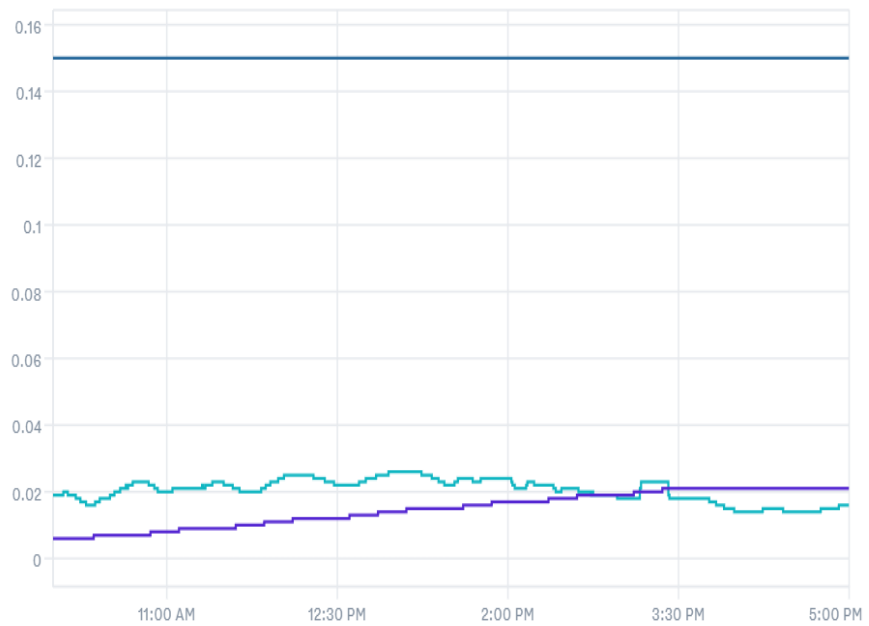

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

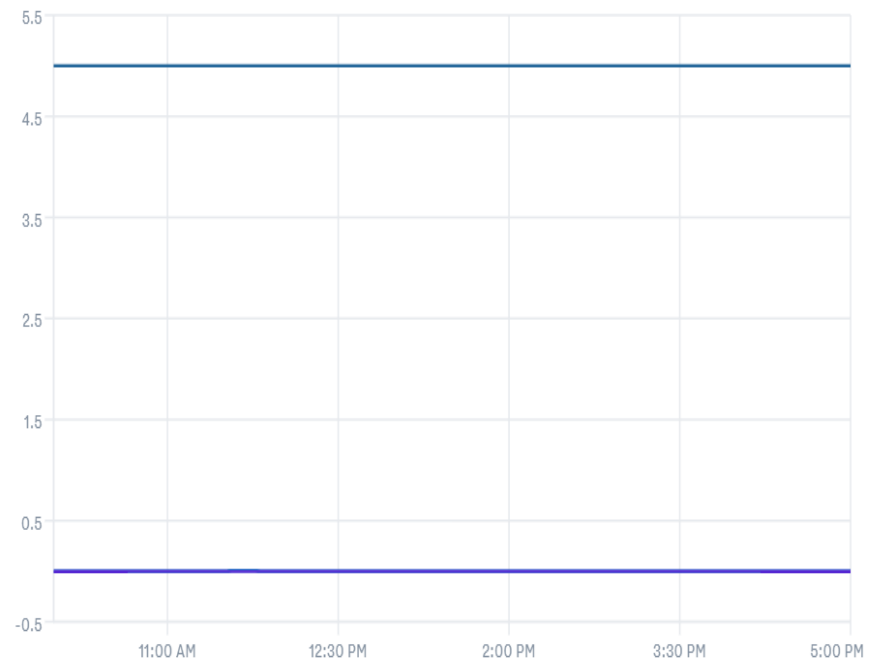

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/29/2024 10:00	1/29/2024 10:10	0.150	0	5	0
DW 47907	1/29/2024 10:10	1/29/2024 10:20	0.150	0.001	5	0
DW 47907	1/29/2024 10:20	1/29/2024 10:30	0.150	0.002	5	0
DW 47907	1/29/2024 10:30	1/29/2024 10:40	0.150	0.003	5	0
DW 47907	1/29/2024 10:40	1/29/2024 10:50	0.150	0.004	5	0
DW 47907	1/29/2024 10:50	1/29/2024 11:00	0.150	0.005	5	0
DW 47907	1/29/2024 11:00	1/29/2024 11:10	0.150	0.006	5	0
DW 47907	1/29/2024 11:10	1/29/2024 11:20	0.150	0.006	5	0
DW 47907	1/29/2024 11:20	1/29/2024 11:30	0.150	0.007	5	0
DW 47907	1/29/2024 11:30	1/29/2024 11:40	0.150	0.008	5	0
DW 47907	1/29/2024 11:40	1/29/2024 11:50	0.150	0.008	5	0
DW 47907	1/29/2024 11:50	1/29/2024 12:00	0.150	0.009	5	0
DW 47907	1/29/2024 12:00	1/29/2024 12:10	0.150	0.01	5	0
DW 47907	1/29/2024 12:10	1/29/2024 12:20	0.150	0.011	5	0
DW 47907	1/29/2024 12:20	1/29/2024 12:30	0.150	0.011	5	0
DW 47907	1/29/2024 12:30	1/29/2024 12:40	0.150	0.012	5	0
DW 47907	1/29/2024 12:40	1/29/2024 12:50	0.150	0.013	5	0
DW 47907	1/29/2024 12:50	1/29/2024 13:00	0.150	0.013	5	0
DW 47907	1/29/2024 13:00	1/29/2024 13:10	0.150	0.014	5	0
DW 47907	1/29/2024 13:10	1/29/2024 13:20	0.150	0.014	5	0
DW 47907	1/29/2024 13:20	1/29/2024 13:30	0.150	0.015	5	0
DW 47907	1/29/2024 13:30	1/29/2024 13:40	0.150	0.015	5	0
DW 47907	1/29/2024 13:40	1/29/2024 13:50	0.150	0.016	5	0
DW 47907	1/29/2024 13:50	1/29/2024 14:00	0.150	0.016	5	0
DW 47907	1/29/2024 14:00	1/29/2024 14:10	0.150	0.017	5	0
DW 47907	1/29/2024 14:10	1/29/2024 14:20	0.150	0.017	5	0
DW 47907	1/29/2024 14:20	1/29/2024 14:30	0.150	0.018	5	0
DW 47907	1/29/2024 14:30	1/29/2024 14:40	0.150	0.018	5	0
DW 47907	1/29/2024 14:40	1/29/2024 14:50	0.150	0.018	5	0
DW 47907	1/29/2024 14:50	1/29/2024 15:00	0.150	0.019	5	0
DW 47907	1/29/2024 15:00	1/29/2024 15:10	0.150	0.019	5	0
DW 47907	1/29/2024 15:10	1/29/2024 15:20	0.150	0.02	5	0
DW 47907	1/29/2024 15:20	1/29/2024 15:30	0.150	0.02	5	0
DW 47907	1/29/2024 15:30	1/29/2024 15:40	0.150	0.02	5	0
DW 47907	1/29/2024 15:40	1/29/2024 15:50	0.150	0.02	5	0
DW 47907	1/29/2024 15:50	1/29/2024 16:00	0.150	0.021	5	0
DW 47907	1/29/2024 16:00	1/29/2024 16:10	0.150	0.021	5	0
DW 47907	1/29/2024 16:10	1/29/2024 16:20	0.150	0.021	5	0
DW 47907	1/29/2024 16:20	1/29/2024 16:30	0.150	0.021	5	0
DW 47907	1/29/2024 16:30	1/29/2024 16:40	0.150	0.021	5	0
DW 47907	1/29/2024 16:40	1/29/2024 16:50	0.150	0.022	5	0
DW 47907	1/29/2024 16:50	1/29/2024 17:00	0.150	0.022	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/29/2024 10:00	1/29/2024 10:10	0.150	0	5	0
UW 212221	1/29/2024 10:10	1/29/2024 10:20	0.150	0	5	0
UW 212221	1/29/2024 10:20	1/29/2024 10:30	0.150	0	5	0
UW 212221	1/29/2024 10:30	1/29/2024 10:40	0.150	0	5	0
UW 212221	1/29/2024 10:40	1/29/2024 10:50	0.150	0.001	5	0
UW 212221	1/29/2024 10:50	1/29/2024 11:00	0.150	0.001	5	0
UW 212221	1/29/2024 11:00	1/29/2024 11:10	0.150	0.001	5	0
UW 212221	1/29/2024 11:10	1/29/2024 11:20	0.150	0.002	5	0
UW 212221	1/29/2024 11:20	1/29/2024 11:30	0.150	0.002	5	0
UW 212221	1/29/2024 11:30	1/29/2024 11:40	0.150	0.003	5	0
UW 212221	1/29/2024 11:40	1/29/2024 11:50	0.150	0.003	5	0
UW 212221	1/29/2024 11:50	1/29/2024 12:00	0.150	0.003	5	0
UW 212221	1/29/2024 12:00	1/29/2024 12:10	0.150	0.004	5	0
UW 212221	1/29/2024 12:10	1/29/2024 12:20	0.150	0.005	5	0
UW 212221	1/29/2024 12:20	1/29/2024 12:30	0.150	0.005	5	0
UW 212221	1/29/2024 12:30	1/29/2024 12:40	0.150	0.005	5	0
UW 212221	1/29/2024 12:40	1/29/2024 12:50	0.150	0.006	5	0
UW 212221	1/29/2024 12:50	1/29/2024 13:00	0.150	0.006	5	0
UW 212221	1/29/2024 13:00	1/29/2024 13:10	0.150	0.007	5	0
UW 212221	1/29/2024 13:10	1/29/2024 13:20	0.150	0.007	5	0
UW 212221	1/29/2024 13:20	1/29/2024 13:30	0.150	0.007	5	0
UW 212221	1/29/2024 13:30	1/29/2024 13:40	0.150	0.008	5	0
UW 212221	1/29/2024 13:40	1/29/2024 13:50	0.150	0.009	5	0
UW 212221	1/29/2024 13:50	1/29/2024 14:00	0.150	0.009	5	0
UW 212221	1/29/2024 14:00	1/29/2024 14:10	0.150	0.009	5	0
UW 212221	1/29/2024 14:10	1/29/2024 14:20	0.150	0.01	5	0
UW 212221	1/29/2024 14:20	1/29/2024 14:30	0.150	0.01	5	0
UW 212221	1/29/2024 14:30	1/29/2024 14:40	0.150	0.01	5	0
UW 212221	1/29/2024 14:40	1/29/2024 14:50	0.150	0.011	5	0
UW 212221	1/29/2024 14:50	1/29/2024 15:00	0.150	0.011	5	0
UW 212221	1/29/2024 15:00	1/29/2024 15:10	0.150	0.011	5	0
UW 212221	1/29/2024 15:10	1/29/2024 15:20	0.150	0.012	5	0
UW 212221	1/29/2024 15:20	1/29/2024 15:30	0.150	0.012	5	0
UW 212221	1/29/2024 15:30	1/29/2024 15:40	0.150	0.013	5	0
UW 212221	1/29/2024 15:40	1/29/2024 15:50	0.150	0.013	5	0
UW 212221	1/29/2024 15:50	1/29/2024 16:00	0.150	0.013	5	0.001
UW 212221	1/29/2024 16:00	1/29/2024 16:10	0.150	0.014	5	0.001
UW 212221	1/29/2024 16:10	1/29/2024 16:20	0.150	0.014	5	0.001
UW 212221	1/29/2024 16:20	1/29/2024 16:30	0.150	0.014	5	0.001
UW 212221	1/29/2024 16:30	1/29/2024 16:40	0.150	0.014	5	0.001
UW 212221	1/29/2024 16:40	1/29/2024 16:50	0.150	0.015	5	0.001
UW 212221	1/29/2024 16:50	1/29/2024 17:00	0.150	0.015	5	0.001

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/29/2024 10:00	1/29/2024 10:10	0.150	0	5	0
PER1 50057	1/29/2024 10:10	1/29/2024 10:20	0.150	0.001	5	0
PER1 50057	1/29/2024 10:20	1/29/2024 10:30	0.150	0.002	5	0
PER1 50057	1/29/2024 10:30	1/29/2024 10:40	0.150	0.002	5	0
PER1 50057	1/29/2024 10:40	1/29/2024 10:50	0.150	0.003	5	0
PER1 50057	1/29/2024 10:50	1/29/2024 11:00	0.150	0.004	5	0
PER1 50057	1/29/2024 11:00	1/29/2024 11:10	0.150	0.004	5	0
PER1 50057	1/29/2024 11:10	1/29/2024 11:20	0.150	0.005	5	0
PER1 50057	1/29/2024 11:20	1/29/2024 11:30	0.150	0.005	5	0
PER1 50057	1/29/2024 11:30	1/29/2024 11:40	0.150	0.006	5	0
PER1 50057	1/29/2024 11:40	1/29/2024 11:50	0.150	0.006	5	0
PER1 50057	1/29/2024 11:50	1/29/2024 12:00	0.150	0.007	5	0
PER1 50057	1/29/2024 12:00	1/29/2024 12:10	0.150	0.008	5	0
PER1 50057	1/29/2024 12:10	1/29/2024 12:20	0.150	0.008	5	0
PER1 50057	1/29/2024 12:20	1/29/2024 12:30	0.150	0.009	5	0
PER1 50057	1/29/2024 12:30	1/29/2024 12:40	0.150	0.01	5	0
PER1 50057	1/29/2024 12:40	1/29/2024 12:50	0.150	0.01	5	0
PER1 50057	1/29/2024 12:50	1/29/2024 13:00	0.150	0.011	5	0
PER1 50057	1/29/2024 13:00	1/29/2024 13:10	0.150	0.011	5	0
PER1 50057	1/29/2024 13:10	1/29/2024 13:20	0.150	0.012	5	0
PER1 50057	1/29/2024 13:20	1/29/2024 13:30	0.150	0.012	5	0
PER1 50057	1/29/2024 13:30	1/29/2024 13:40	0.150	0.013	5	0
PER1 50057	1/29/2024 13:40	1/29/2024 13:50	0.150	0.013	5	0
PER1 50057	1/29/2024 13:50	1/29/2024 14:00	0.150	0.014	5	0
PER1 50057	1/29/2024 14:00	1/29/2024 14:10	0.150	0.014	5	0
PER1 50057	1/29/2024 14:10	1/29/2024 14:20	0.150	0.014	5	0
PER1 50057	1/29/2024 14:20	1/29/2024 14:30	0.150	0.015	5	0
PER1 50057	1/29/2024 14:30	1/29/2024 14:40	0.150	0.015	5	0
PER1 50057	1/29/2024 14:40	1/29/2024 14:50	0.150	0.016	5	0
PER1 50057	1/29/2024 14:50	1/29/2024 15:00	0.150	0.016	5	0
PER1 50057	1/29/2024 15:00	1/29/2024 15:10	0.150	0.017	5	0
PER1 50057	1/29/2024 15:10	1/29/2024 15:20	0.150	0.017	5	0
PER1 50057	1/29/2024 15:20	1/29/2024 15:30	0.150	0.017	5	0
PER1 50057	1/29/2024 15:30	1/29/2024 15:40	0.150	0.018	5	0
PER1 50057	1/29/2024 15:40	1/29/2024 15:50	0.150	0.018	5	0
PER1 50057	1/29/2024 15:50	1/29/2024 16:00	0.150	0.019	5	0
PER1 50057	1/29/2024 16:00	1/29/2024 16:10	0.150	0.019	5	0
PER1 50057	1/29/2024 16:10	1/29/2024 16:20	0.150	0.019	5	0
PER1 50057	1/29/2024 16:20	1/29/2024 16:30	0.150	0.02	5	0
PER1 50057	1/29/2024 16:30	1/29/2024 16:40	0.150	0.02	5	0
PER1 50057	1/29/2024 16:40	1/29/2024 16:50	0.150	0.02	5	0
PER1 50057	1/29/2024 16:50	1/29/2024 17:00	0.150	0.021	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/29/2024 10:00	1/29/2024 10:10	0.150	0.001	5	0
PER2 46495	1/29/2024 10:10	1/29/2024 10:20	0.150	0.002	5	0
PER2 46495	1/29/2024 10:20	1/29/2024 10:30	0.150	0.002	5	0
PER2 46495	1/29/2024 10:30	1/29/2024 10:40	0.150	0.003	5	0
PER2 46495	1/29/2024 10:40	1/29/2024 10:50	0.150	0.003	5	0
PER2 46495	1/29/2024 10:50	1/29/2024 11:00	0.150	0.004	5	0
PER2 46495	1/29/2024 11:00	1/29/2024 11:10	0.150	0.004	5	0
PER2 46495	1/29/2024 11:10	1/29/2024 11:20	0.150	0.005	5	0
PER2 46495	1/29/2024 11:20	1/29/2024 11:30	0.150	0.005	5	0
PER2 46495	1/29/2024 11:30	1/29/2024 11:40	0.150	0.006	5	0
PER2 46495	1/29/2024 11:40	1/29/2024 11:50	0.150	0.006	5	0
PER2 46495	1/29/2024 11:50	1/29/2024 12:00	0.150	0.007	5	0
PER2 46495	1/29/2024 12:00	1/29/2024 12:10	0.150	0.007	5	0
PER2 46495	1/29/2024 12:10	1/29/2024 12:20	0.150	0.008	5	0
PER2 46495	1/29/2024 12:20	1/29/2024 12:30	0.150	0.008	5	0
PER2 46495	1/29/2024 12:30	1/29/2024 12:40	0.150	0.009	5	0
PER2 46495	1/29/2024 12:40	1/29/2024 12:50	0.150	0.009	5	0
PER2 46495	1/29/2024 12:50	1/29/2024 13:00	0.150	0.01	5	0
PER2 46495	1/29/2024 13:00	1/29/2024 13:10	0.150	0.01	5	0
PER2 46495	1/29/2024 13:10	1/29/2024 13:20	0.150	0.011	5	0
PER2 46495	1/29/2024 13:20	1/29/2024 13:30	0.150	0.011	5	0
PER2 46495	1/29/2024 13:30	1/29/2024 13:40	0.150	0.012	5	0
PER2 46495	1/29/2024 13:40	1/29/2024 13:50	0.150	0.012	5	0
PER2 46495	1/29/2024 13:50	1/29/2024 14:00	0.150	0.013	5	0
PER2 46495	1/29/2024 14:00	1/29/2024 14:10	0.150	0.013	5	0
PER2 46495	1/29/2024 14:10	1/29/2024 14:20	0.150	0.014	5	0
PER2 46495	1/29/2024 14:20	1/29/2024 14:30	0.150	0.014	5	0
PER2 46495	1/29/2024 14:30	1/29/2024 14:40	0.150	0.015	5	0
PER2 46495	1/29/2024 14:40	1/29/2024 14:50	0.150	0.015	5	0
PER2 46495	1/29/2024 14:50	1/29/2024 15:00	0.150	0.016	5	0
PER2 46495	1/29/2024 15:00	1/29/2024 15:10	0.150	0.016	5	0
PER2 46495	1/29/2024 15:10	1/29/2024 15:20	0.150	0.016	5	0
PER2 46495	1/29/2024 15:20	1/29/2024 15:30	0.150	0.017	5	0
PER2 46495	1/29/2024 15:30	1/29/2024 15:40	0.150	0.017	5	0
PER2 46495	1/29/2024 15:40	1/29/2024 15:50	0.150	0.018	5	0
PER2 46495	1/29/2024 15:50	1/29/2024 16:00	0.150	0.018	5	0
PER2 46495	1/29/2024 16:00	1/29/2024 16:10	0.150	0.018	5	0
PER2 46495	1/29/2024 16:10	1/29/2024 16:20	0.150	0.019	5	0
PER2 46495	1/29/2024 16:20	1/29/2024 16:30	0.150	0.019	5	0
PER2 46495	1/29/2024 16:30	1/29/2024 16:40	0.150	0.019	5	0
PER2 46495	1/29/2024 16:40	1/29/2024 16:50	0.150	0.02	5	0
PER2 46495	1/29/2024 16:50	1/29/2024 17:00	0.150	0.02	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 1/30/2024
	Weather: 40 deg. F, Overcast/Light rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA

Work Activities Performed: 1) Alba continues excavation, exposing and drilling piles and installing SOE in A3 building location. 2) Export of 30 loads (approximately 600 CY) of material from WC-25 and WC-27 to the Harmony Foul Rift disposal facility.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA
--

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	600	0	0	0	0
Total:(CY)	3585	0	4745	600	0

Site Layout Map and Excavation Figures

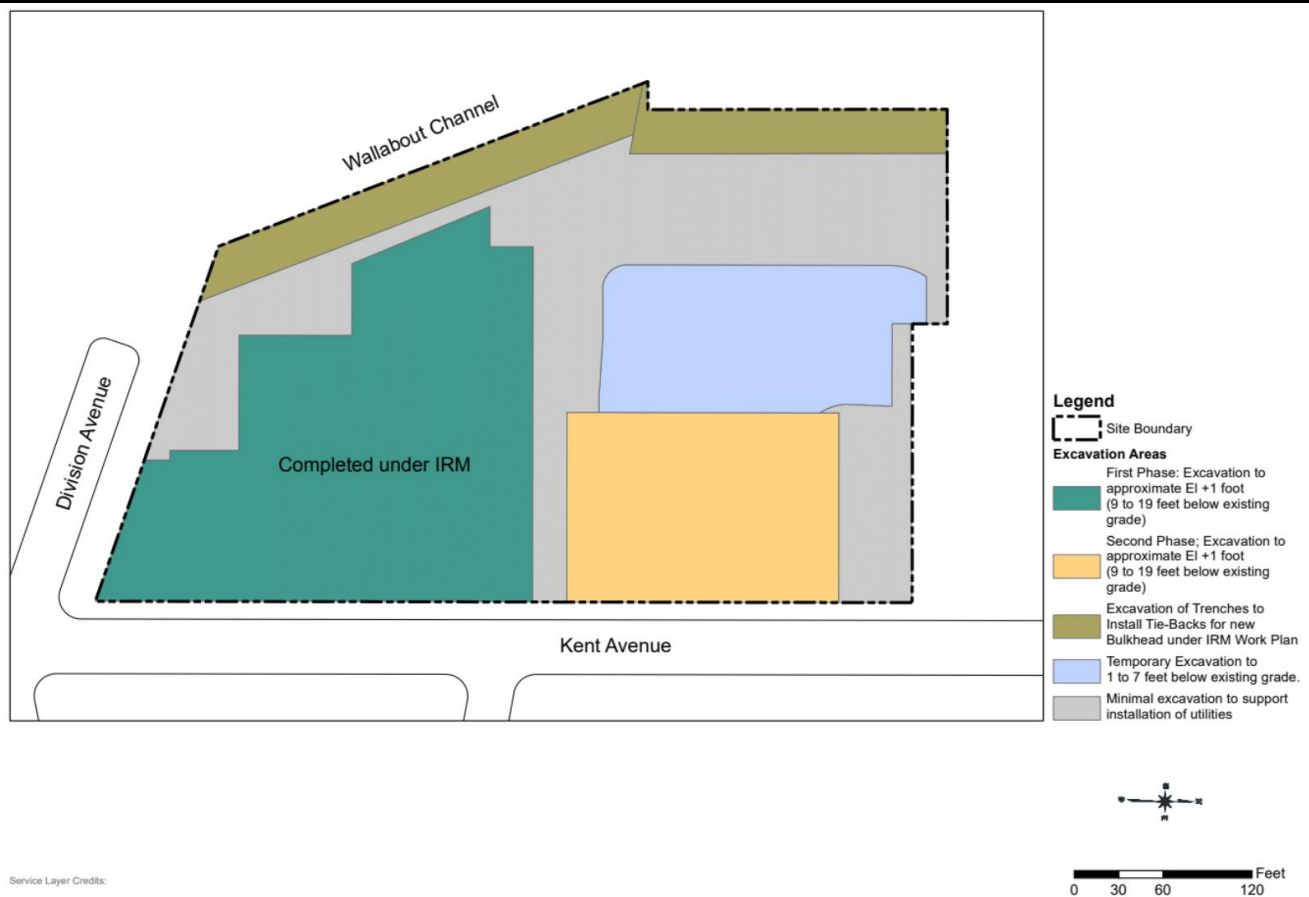

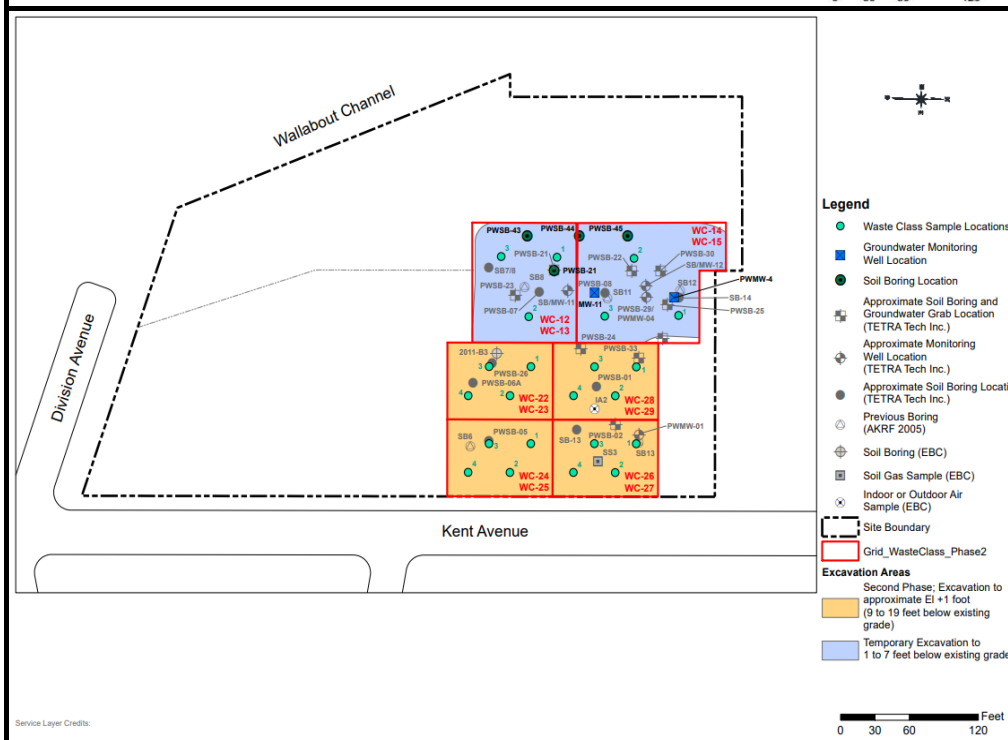
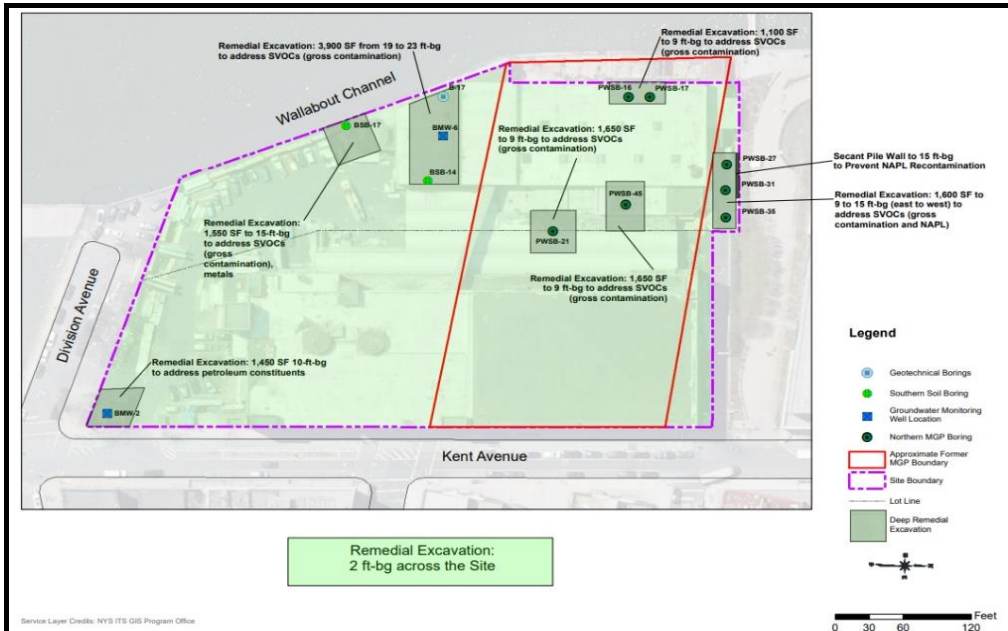


Photo 1:
View of truck loading for
off-site soil disposal.



Photo 2:
View of Site conditions
facing northwest.

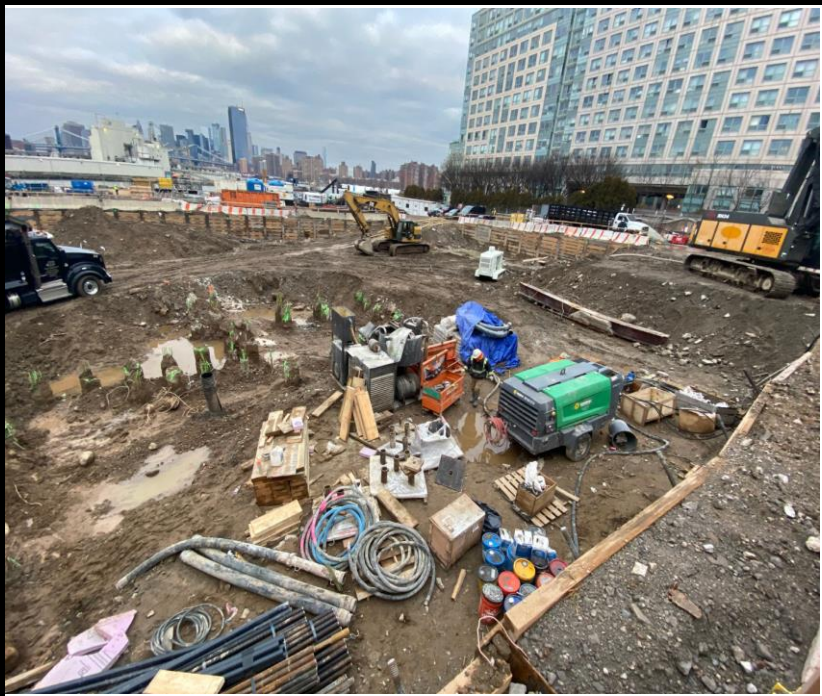



Photo 3:
View of Site
conditions facing
south.




Photo 4:
View of exposed
piles.




CAMP:
Downwind
Particulates

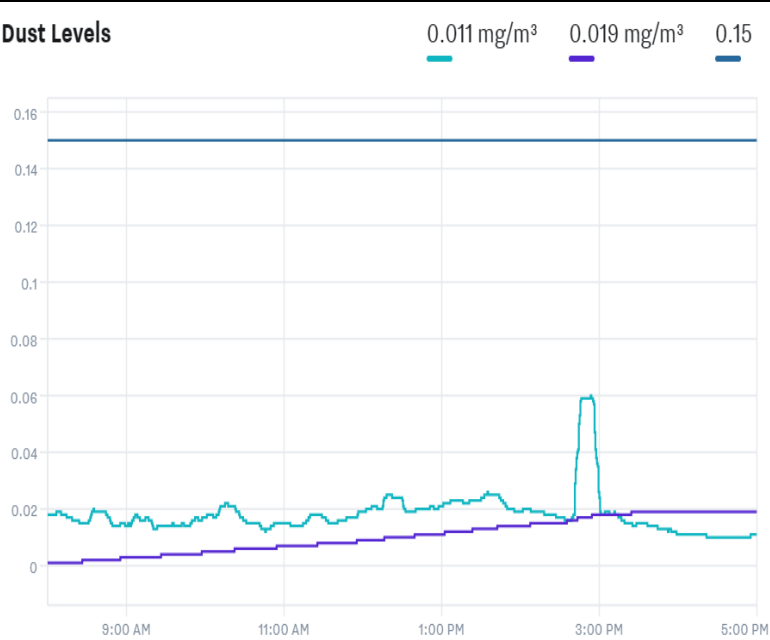


CAMP:
Downwind VOCs

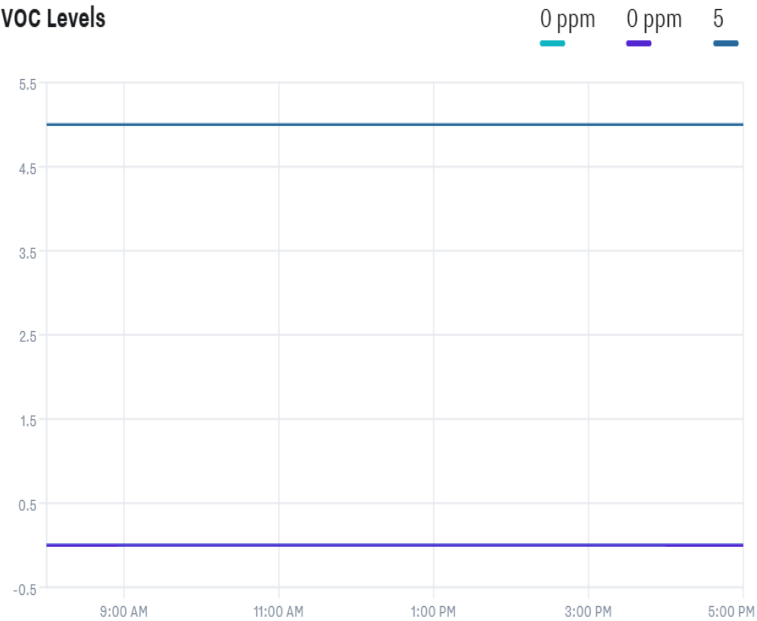

CAMP:
Upwind Particulates

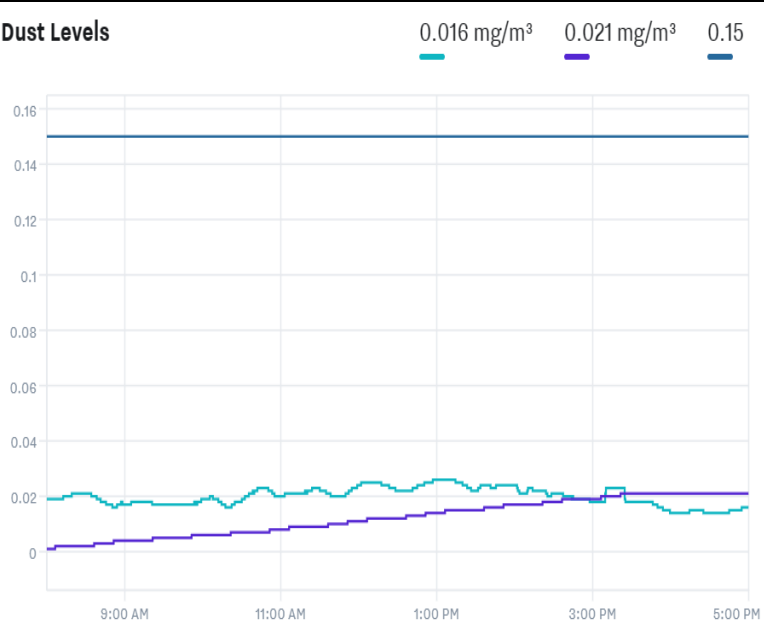

CAMP:
Upwind VOCs

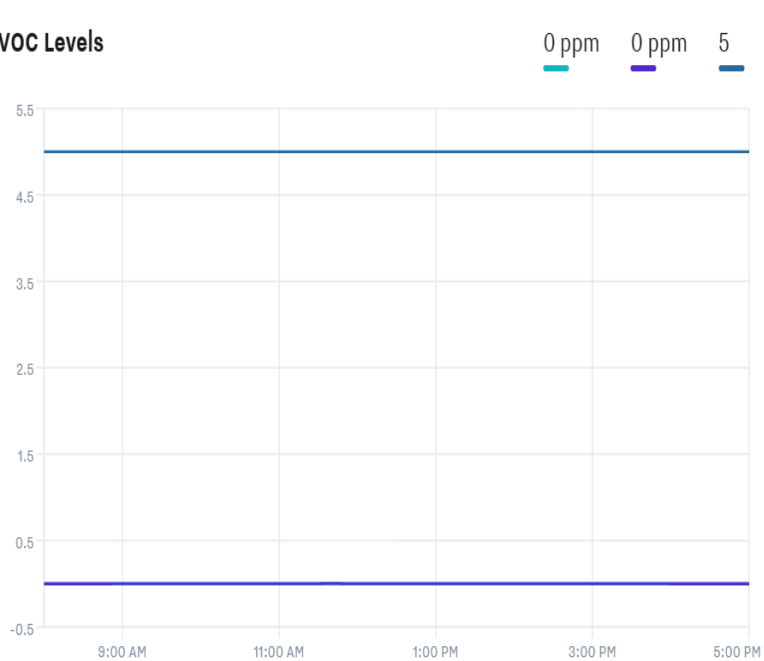

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/30/2024 8:00	1/30/2024 8:10	0.150	0.001	5	0
DW 47907	1/30/2024 8:10	1/30/2024 8:20	0.150	0.001	5	0
DW 47907	1/30/2024 8:20	1/30/2024 8:30	0.150	0.002	5	0
DW 47907	1/30/2024 8:30	1/30/2024 8:40	0.150	0.002	5	0
DW 47907	1/30/2024 8:40	1/30/2024 8:50	0.150	0.002	5	0
DW 47907	1/30/2024 8:50	1/30/2024 9:00	0.150	0.003	5	0
DW 47907	1/30/2024 9:00	1/30/2024 9:10	0.150	0.003	5	0
DW 47907	1/30/2024 9:10	1/30/2024 9:20	0.150	0.003	5	0
DW 47907	1/30/2024 9:20	1/30/2024 9:30	0.150	0.004	5	0
DW 47907	1/30/2024 9:30	1/30/2024 9:40	0.150	0.004	5	0
DW 47907	1/30/2024 9:40	1/30/2024 9:50	0.150	0.004	5	0
DW 47907	1/30/2024 9:50	1/30/2024 10:00	0.150	0.005	5	0
DW 47907	1/30/2024 10:00	1/30/2024 10:10	0.150	0.005	5	0
DW 47907	1/30/2024 10:10	1/30/2024 10:20	0.150	0.005	5	0
DW 47907	1/30/2024 10:20	1/30/2024 10:30	0.150	0.006	5	0
DW 47907	1/30/2024 10:30	1/30/2024 10:40	0.150	0.006	5	0
DW 47907	1/30/2024 10:40	1/30/2024 10:50	0.150	0.006	5	0
DW 47907	1/30/2024 10:50	1/30/2024 11:00	0.150	0.007	5	0
DW 47907	1/30/2024 11:00	1/30/2024 11:10	0.150	0.007	5	0
DW 47907	1/30/2024 11:10	1/30/2024 11:20	0.150	0.007	5	0
DW 47907	1/30/2024 11:20	1/30/2024 11:30	0.150	0.008	5	0
DW 47907	1/30/2024 11:30	1/30/2024 11:40	0.150	0.008	5	0
DW 47907	1/30/2024 11:40	1/30/2024 11:50	0.150	0.008	5	0
DW 47907	1/30/2024 11:50	1/30/2024 12:00	0.150	0.009	5	0
DW 47907	1/30/2024 12:00	1/30/2024 12:10	0.150	0.009	5	0
DW 47907	1/30/2024 12:10	1/30/2024 12:20	0.150	0.01	5	0
DW 47907	1/30/2024 12:20	1/30/2024 12:30	0.150	0.01	5	0
DW 47907	1/30/2024 12:30	1/30/2024 12:40	0.150	0.011	5	0
DW 47907	1/30/2024 12:40	1/30/2024 12:50	0.150	0.011	5	0
DW 47907	1/30/2024 12:50	1/30/2024 13:00	0.150	0.011	5	0
DW 47907	1/30/2024 13:00	1/30/2024 13:10	0.150	0.012	5	0
DW 47907	1/30/2024 13:10	1/30/2024 13:20	0.150	0.012	5	0
DW 47907	1/30/2024 13:20	1/30/2024 13:30	0.150	0.013	5	0
DW 47907	1/30/2024 13:30	1/30/2024 13:40	0.150	0.013	5	0
DW 47907	1/30/2024 13:40	1/30/2024 13:50	0.150	0.014	5	0
DW 47907	1/30/2024 13:50	1/30/2024 14:00	0.150	0.014	5	0
DW 47907	1/30/2024 14:00	1/30/2024 14:10	0.150	0.015	5	0
DW 47907	1/30/2024 14:10	1/30/2024 14:20	0.150	0.015	5	0
DW 47907	1/30/2024 14:20	1/30/2024 14:30	0.150	0.015	5	0
DW 47907	1/30/2024 14:30	1/30/2024 14:40	0.150	0.016	5	0
DW 47907	1/30/2024 14:40	1/30/2024 14:50	0.150	0.017	5	0
DW 47907	1/30/2024 14:50	1/30/2024 15:00	0.150	0.018	5	0
DW 47907	1/30/2024 15:00	1/30/2024 15:10	0.150	0.018	5	0
DW 47907	1/30/2024 15:10	1/30/2024 15:20	0.150	0.018	5	0
DW 47907	1/30/2024 15:20	1/30/2024 15:30	0.150	0.019	5	0
DW 47907	1/30/2024 15:30	1/30/2024 15:40	0.150	0.019	5	0
DW 47907	1/30/2024 15:40	1/30/2024 15:50	0.150	0.019	5	0
DW 47907	1/30/2024 15:50	1/30/2024 16:00	0.150	0.019	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/30/2024 8:00	1/30/2024 8:10	0.150	0.002	5	0
UW 212221	1/30/2024 8:10	1/30/2024 8:20	0.150	0.002	5	0
UW 212221	1/30/2024 8:20	1/30/2024 8:30	0.150	0.002	5	0
UW 212221	1/30/2024 8:30	1/30/2024 8:40	0.150	0.003	5	0
UW 212221	1/30/2024 8:40	1/30/2024 8:50	0.150	0.003	5	0
UW 212221	1/30/2024 8:50	1/30/2024 9:00	0.150	0.004	5	0
UW 212221	1/30/2024 9:00	1/30/2024 9:10	0.150	0.004	5	0
UW 212221	1/30/2024 9:10	1/30/2024 9:20	0.150	0.004	5	0
UW 212221	1/30/2024 9:20	1/30/2024 9:30	0.150	0.005	5	0
UW 212221	1/30/2024 9:30	1/30/2024 9:40	0.150	0.005	5	0
UW 212221	1/30/2024 9:40	1/30/2024 9:50	0.150	0.005	5	0
UW 212221	1/30/2024 9:50	1/30/2024 10:00	0.150	0.006	5	0
UW 212221	1/30/2024 10:00	1/30/2024 10:10	0.150	0.006	5	0
UW 212221	1/30/2024 10:10	1/30/2024 10:20	0.150	0.006	5	0
UW 212221	1/30/2024 10:20	1/30/2024 10:30	0.150	0.007	5	0
UW 212221	1/30/2024 10:30	1/30/2024 10:40	0.150	0.007	5	0
UW 212221	1/30/2024 10:40	1/30/2024 10:50	0.150	0.007	5	0
UW 212221	1/30/2024 10:50	1/30/2024 11:00	0.150	0.008	5	0
UW 212221	1/30/2024 11:00	1/30/2024 11:10	0.150	0.009	5	0
UW 212221	1/30/2024 11:10	1/30/2024 11:20	0.150	0.009	5	0
UW 212221	1/30/2024 11:20	1/30/2024 11:30	0.150	0.009	5	0
UW 212221	1/30/2024 11:30	1/30/2024 11:40	0.150	0.01	5	0
UW 212221	1/30/2024 11:40	1/30/2024 11:50	0.150	0.01	5	0
UW 212221	1/30/2024 11:50	1/30/2024 12:00	0.150	0.011	5	0
UW 212221	1/30/2024 12:00	1/30/2024 12:10	0.150	0.012	5	0
UW 212221	1/30/2024 12:10	1/30/2024 12:20	0.150	0.012	5	0
UW 212221	1/30/2024 12:20	1/30/2024 12:30	0.150	0.012	5	0
UW 212221	1/30/2024 12:30	1/30/2024 12:40	0.150	0.013	5	0
UW 212221	1/30/2024 12:40	1/30/2024 12:50	0.150	0.013	5	0
UW 212221	1/30/2024 12:50	1/30/2024 13:00	0.150	0.014	5	0
UW 212221	1/30/2024 13:00	1/30/2024 13:10	0.150	0.015	5	0
UW 212221	1/30/2024 13:10	1/30/2024 13:20	0.150	0.015	5	0
UW 212221	1/30/2024 13:20	1/30/2024 13:30	0.150	0.015	5	0
UW 212221	1/30/2024 13:30	1/30/2024 13:40	0.150	0.016	5	0
UW 212221	1/30/2024 13:40	1/30/2024 13:50	0.150	0.016	5	0
UW 212221	1/30/2024 13:50	1/30/2024 14:00	0.150	0.017	5	0
UW 212221	1/30/2024 14:00	1/30/2024 14:10	0.150	0.017	5	0
UW 212221	1/30/2024 14:10	1/30/2024 14:20	0.150	0.017	5	0
UW 212221	1/30/2024 14:20	1/30/2024 14:30	0.150	0.018	5	0
UW 212221	1/30/2024 14:30	1/30/2024 14:40	0.150	0.019	5	0
UW 212221	1/30/2024 14:40	1/30/2024 14:50	0.150	0.019	5	0
UW 212221	1/30/2024 14:50	1/30/2024 15:00	0.150	0.019	5	0
UW 212221	1/30/2024 15:00	1/30/2024 15:10	0.150	0.02	5	0
UW 212221	1/30/2024 15:10	1/30/2024 15:20	0.150	0.02	5	0
UW 212221	1/30/2024 15:20	1/30/2024 15:30	0.150	0.021	5	0
UW 212221	1/30/2024 15:30	1/30/2024 15:40	0.150	0.021	5	0
UW 212221	1/30/2024 15:40	1/30/2024 15:50	0.150	0.021	5	0
UW 212221	1/30/2024 15:50	1/30/2024 16:00	0.150	0.021	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/30/2024 8:00	1/30/2024 8:10	0.150	0.002	5	0
PER1 50057	1/30/2024 8:10	1/30/2024 8:20	0.150	0.002	5	0
PER1 50057	1/30/2024 8:20	1/30/2024 8:30	0.150	0.003	5	0
PER1 50057	1/30/2024 8:30	1/30/2024 8:40	0.150	0.003	5	0
PER1 50057	1/30/2024 8:40	1/30/2024 8:50	0.150	0.004	5	0
PER1 50057	1/30/2024 8:50	1/30/2024 9:00	0.150	0.004	5	0
PER1 50057	1/30/2024 9:00	1/30/2024 9:10	0.150	0.005	5	0
PER1 50057	1/30/2024 9:10	1/30/2024 9:20	0.150	0.005	5	0
PER1 50057	1/30/2024 9:20	1/30/2024 9:30	0.150	0.005	5	0
PER1 50057	1/30/2024 9:30	1/30/2024 9:40	0.150	0.006	5	0
PER1 50057	1/30/2024 9:40	1/30/2024 9:50	0.150	0.006	5	0
PER1 50057	1/30/2024 9:50	1/30/2024 10:00	0.150	0.006	5	0
PER1 50057	1/30/2024 10:00	1/30/2024 10:10	0.150	0.007	5	0
PER1 50057	1/30/2024 10:10	1/30/2024 10:20	0.150	0.007	5	0
PER1 50057	1/30/2024 10:20	1/30/2024 10:30	0.150	0.008	5	0
PER1 50057	1/30/2024 10:30	1/30/2024 10:40	0.150	0.008	5	0
PER1 50057	1/30/2024 10:40	1/30/2024 10:50	0.150	0.008	5	0
PER1 50057	1/30/2024 10:50	1/30/2024 11:00	0.150	0.009	5	0
PER1 50057	1/30/2024 11:00	1/30/2024 11:10	0.150	0.01	5	0
PER1 50057	1/30/2024 11:10	1/30/2024 11:20	0.150	0.01	5	0
PER1 50057	1/30/2024 11:20	1/30/2024 11:30	0.150	0.011	5	0
PER1 50057	1/30/2024 11:30	1/30/2024 11:40	0.150	0.011	5	0
PER1 50057	1/30/2024 11:40	1/30/2024 11:50	0.150	0.012	5	0
PER1 50057	1/30/2024 11:50	1/30/2024 12:00	0.150	0.012	5	0
PER1 50057	1/30/2024 12:00	1/30/2024 12:10	0.150	0.013	5	0
PER1 50057	1/30/2024 12:10	1/30/2024 12:20	0.150	0.013	5	0
PER1 50057	1/30/2024 12:20	1/30/2024 12:30	0.150	0.014	5	0
PER1 50057	1/30/2024 12:30	1/30/2024 12:40	0.150	0.014	5	0
PER1 50057	1/30/2024 12:40	1/30/2024 12:50	0.150	0.015	5	0
PER1 50057	1/30/2024 12:50	1/30/2024 13:00	0.150	0.016	5	0
PER1 50057	1/30/2024 13:00	1/30/2024 13:10	0.150	0.016	5	0
PER1 50057	1/30/2024 13:10	1/30/2024 13:20	0.150	0.017	5	0
PER1 50057	1/30/2024 13:20	1/30/2024 13:30	0.150	0.017	5	0
PER1 50057	1/30/2024 13:30	1/30/2024 13:40	0.150	0.018	5	0
PER1 50057	1/30/2024 13:40	1/30/2024 13:50	0.150	0.018	5	0
PER1 50057	1/30/2024 13:50	1/30/2024 14:00	0.150	0.019	5	0
PER1 50057	1/30/2024 14:00	1/30/2024 14:10	0.150	0.019	5	0
PER1 50057	1/30/2024 14:10	1/30/2024 14:20	0.150	0.02	5	0
PER1 50057	1/30/2024 14:20	1/30/2024 14:30	0.150	0.02	5	0
PER1 50057	1/30/2024 14:30	1/30/2024 14:40	0.150	0.021	5	0
PER1 50057	1/30/2024 14:40	1/30/2024 14:50	0.150	0.021	5	0
PER1 50057	1/30/2024 14:50	1/30/2024 15:00	0.150	0.022	5	0
PER1 50057	1/30/2024 15:00	1/30/2024 15:10	0.150	0.022	5	0
PER1 50057	1/30/2024 15:10	1/30/2024 15:20	0.150	0.023	5	0
PER1 50057	1/30/2024 15:20	1/30/2024 15:30	0.150	0.023	5	0
PER1 50057	1/30/2024 15:30	1/30/2024 15:40	0.150	0.023	5	0
PER1 50057	1/30/2024 15:40	1/30/2024 15:50	0.150	0.023	5	0
PER1 50057	1/30/2024 15:50	1/30/2024 16:00	0.150	0.023	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/30/2024 8:00	1/30/2024 8:10	0.150	0.001	5	0
PER2 46495	1/30/2024 8:10	1/30/2024 8:20	0.150	0.002	5	0
PER2 46495	1/30/2024 8:20	1/30/2024 8:30	0.150	0.002	5	0
PER2 46495	1/30/2024 8:30	1/30/2024 8:40	0.150	0.003	5	0
PER2 46495	1/30/2024 8:40	1/30/2024 8:50	0.150	0.003	5	0
PER2 46495	1/30/2024 8:50	1/30/2024 9:00	0.150	0.004	5	0
PER2 46495	1/30/2024 9:00	1/30/2024 9:10	0.150	0.004	5	0
PER2 46495	1/30/2024 9:10	1/30/2024 9:20	0.150	0.005	5	0
PER2 46495	1/30/2024 9:20	1/30/2024 9:30	0.150	0.005	5	0.002
PER2 46495	1/30/2024 9:30	1/30/2024 9:40	0.150	0.006	5	0.006
PER2 46495	1/30/2024 9:40	1/30/2024 9:50	0.150	0.006	5	0.006
PER2 46495	1/30/2024 9:50	1/30/2024 10:00	0.150	0.007	5	0.008
PER2 46495	1/30/2024 10:00	1/30/2024 10:10	0.150	0.007	5	0.009
PER2 46495	1/30/2024 10:10	1/30/2024 10:20	0.150	0.008	5	0.009
PER2 46495	1/30/2024 10:20	1/30/2024 10:30	0.150	0.009	5	0.009
PER2 46495	1/30/2024 10:30	1/30/2024 10:40	0.150	0.01	5	0.009
PER2 46495	1/30/2024 10:40	1/30/2024 10:50	0.150	0.01	5	0.009
PER2 46495	1/30/2024 10:50	1/30/2024 11:00	0.150	0.01	5	0.009
PER2 46495	1/30/2024 11:00	1/30/2024 11:10	0.150	0.011	5	0.009
PER2 46495	1/30/2024 11:10	1/30/2024 11:20	0.150	0.011	5	0.009
PER2 46495	1/30/2024 11:20	1/30/2024 11:30	0.150	0.012	5	0.009
PER2 46495	1/30/2024 11:30	1/30/2024 11:40	0.150	0.012	5	0.009
PER2 46495	1/30/2024 11:40	1/30/2024 11:50	0.150	0.013	5	0.009
PER2 46495	1/30/2024 11:50	1/30/2024 12:00	0.150	0.013	5	0.009
PER2 46495	1/30/2024 12:00	1/30/2024 12:10	0.150	0.014	5	0.009
PER2 46495	1/30/2024 12:10	1/30/2024 12:20	0.150	0.014	5	0.009
PER2 46495	1/30/2024 12:20	1/30/2024 12:30	0.150	0.015	5	0.009
PER2 46495	1/30/2024 12:30	1/30/2024 12:40	0.150	0.015	5	0.009
PER2 46495	1/30/2024 12:40	1/30/2024 12:50	0.150	0.016	5	0.009
PER2 46495	1/30/2024 12:50	1/30/2024 13:00	0.150	0.017	5	0.009
PER2 46495	1/30/2024 13:00	1/30/2024 13:10	0.150	0.017	5	0.009
PER2 46495	1/30/2024 13:10	1/30/2024 13:20	0.150	0.018	5	0.009
PER2 46495	1/30/2024 13:20	1/30/2024 13:30	0.150	0.018	5	0.009
PER2 46495	1/30/2024 13:30	1/30/2024 13:40	0.150	0.019	5	0.009
PER2 46495	1/30/2024 13:40	1/30/2024 13:50	0.150	0.023	5	0.009
PER2 46495	1/30/2024 13:50	1/30/2024 14:00	0.150	0.025	5	0.009
PER2 46495	1/30/2024 14:00	1/30/2024 14:10	0.150	0.025	5	0.009
PER2 46495	1/30/2024 14:10	1/30/2024 14:20	0.150	0.026	5	0.009
PER2 46495	1/30/2024 14:20	1/30/2024 14:30	0.150	0.026	5	0.009
PER2 46495	1/30/2024 14:30	1/30/2024 14:40	0.150	0.027	5	0.009
PER2 46495	1/30/2024 14:40	1/30/2024 14:50	0.150	0.027	5	0.009
PER2 46495	1/30/2024 14:50	1/30/2024 15:00	0.150	0.027	5	0.009
PER2 46495	1/30/2024 15:00	1/30/2024 15:10	0.150	0.028	5	0.009
PER2 46495	1/30/2024 15:10	1/30/2024 15:20	0.150	0.028	5	0.009
PER2 46495	1/30/2024 15:20	1/30/2024 15:30	0.150	0.029	5	0.009
PER2 46495	1/30/2024 15:30	1/30/2024 15:40	0.150	0.029	5	0.009
PER2 46495	1/30/2024 15:40	1/30/2024 15:50	0.150	0.029	5	0.009
PER2 46495	1/30/2024 15:50	1/30/2024 16:00	0.150	0.029	5	0.009

Daily Status Report	
Prepared by: C. Zaccheo	Date: 1/31/2024 Weather: 40 deg. F, Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA

Work Activities Performed: 1) Alba continues excavation, exposing and drilling piles and installing SOE in A3 building location. 2) Export of 6 loads (approximately 120 CY) of material from WC-25 and WC-27 for off-site disposal at the Harmony Foul Rift disposal facility. 3) Export of 13 loads (approximately 260 CY) of material from WC-23 for off-site disposal to the Middlesex County Utilities Authority facility. 4) Collect endpoint sample EP-60 in the southeast corner of WC-25.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA
--

Samples Collected (Since Last Report): EP-60

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	120	0	0	0	260
Total:(CY)	3705	0	4745	600	260

Site Layout Map and Excavation Figures

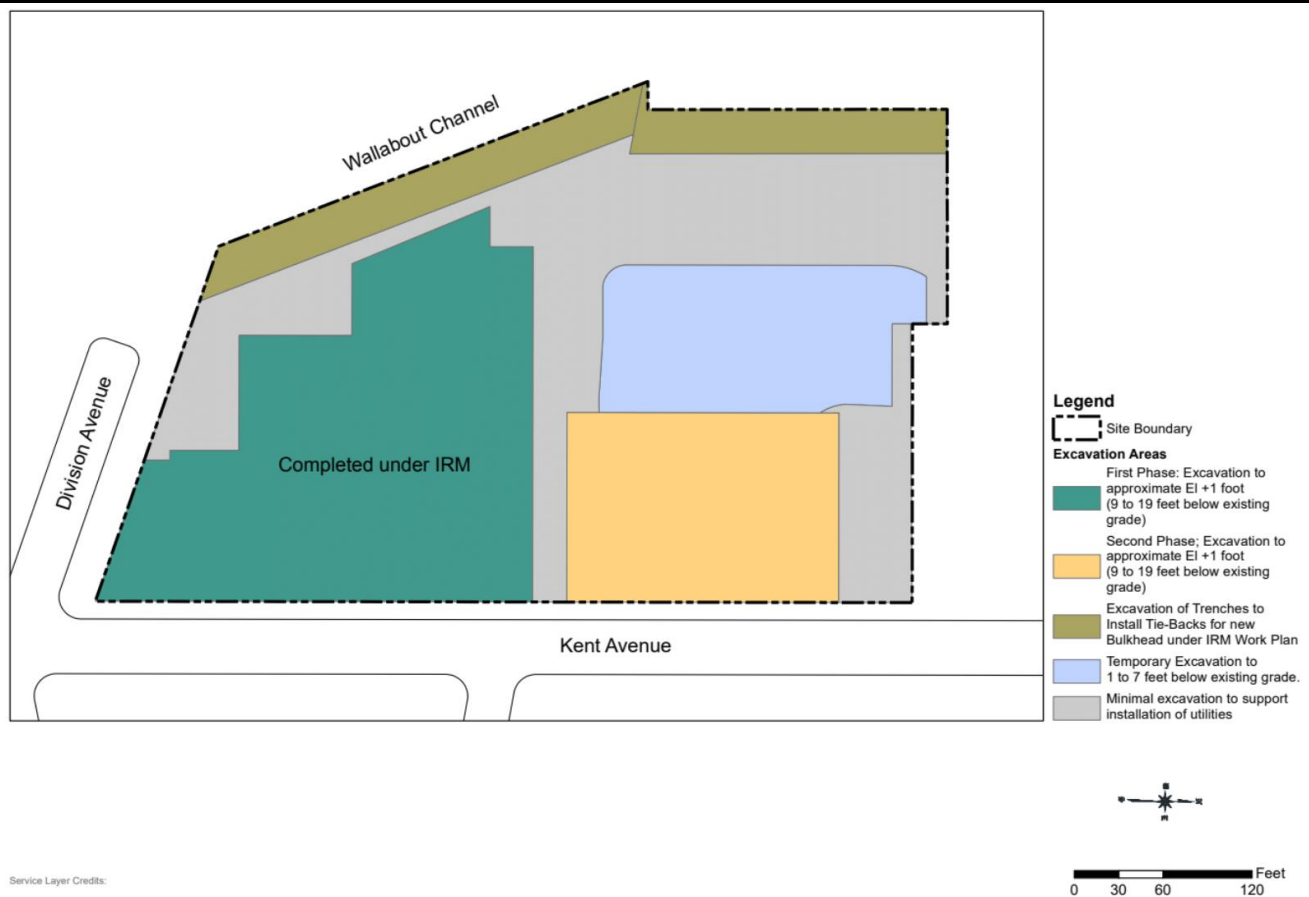

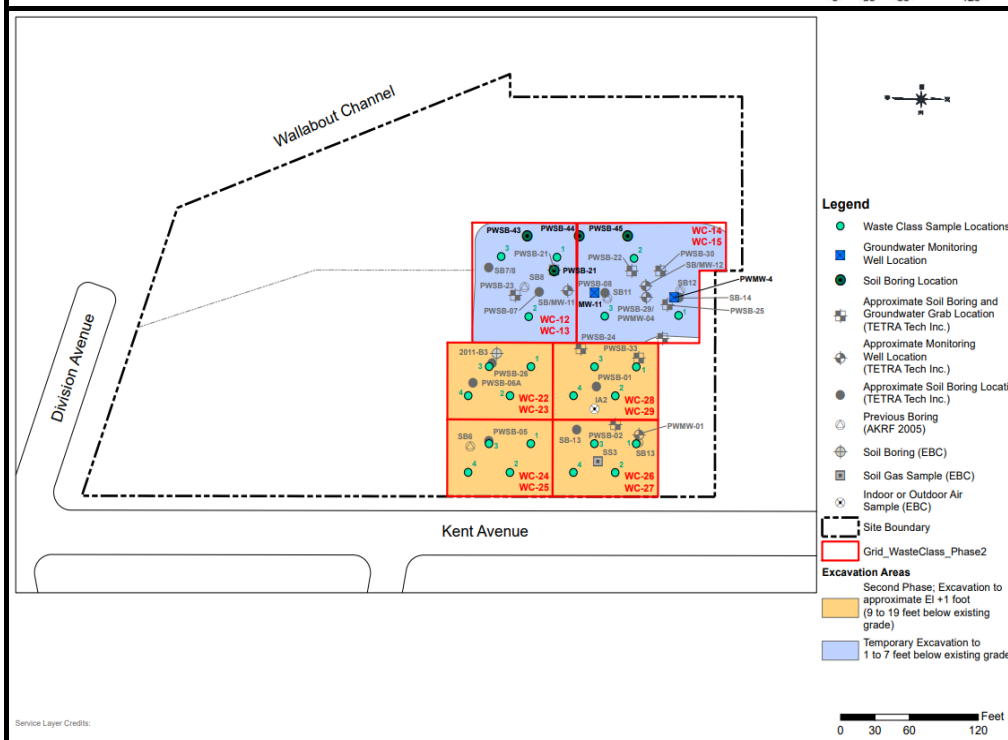
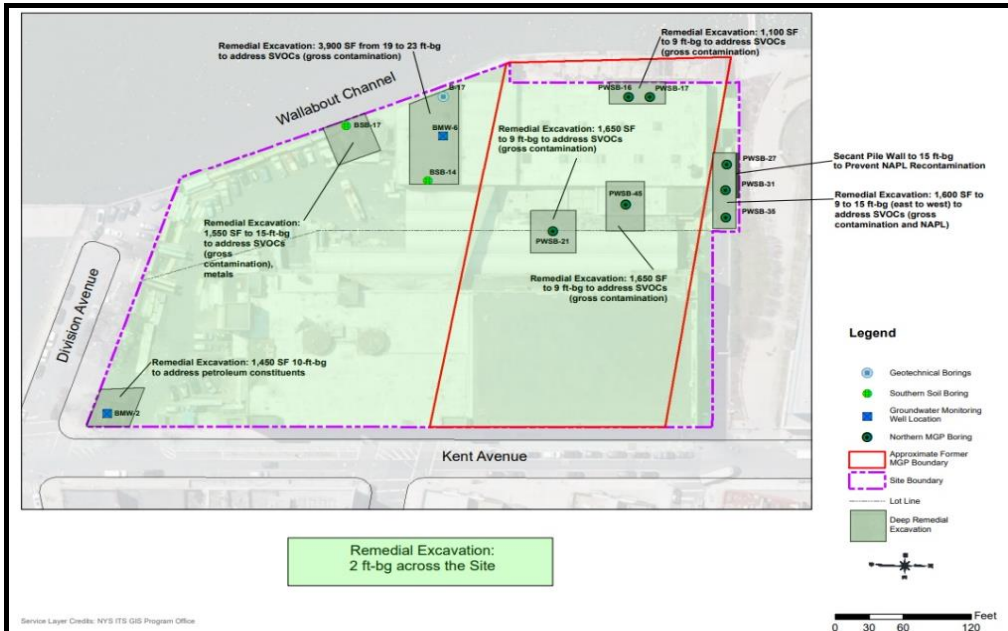


Photo 1:
View of Site conditions
facing north.

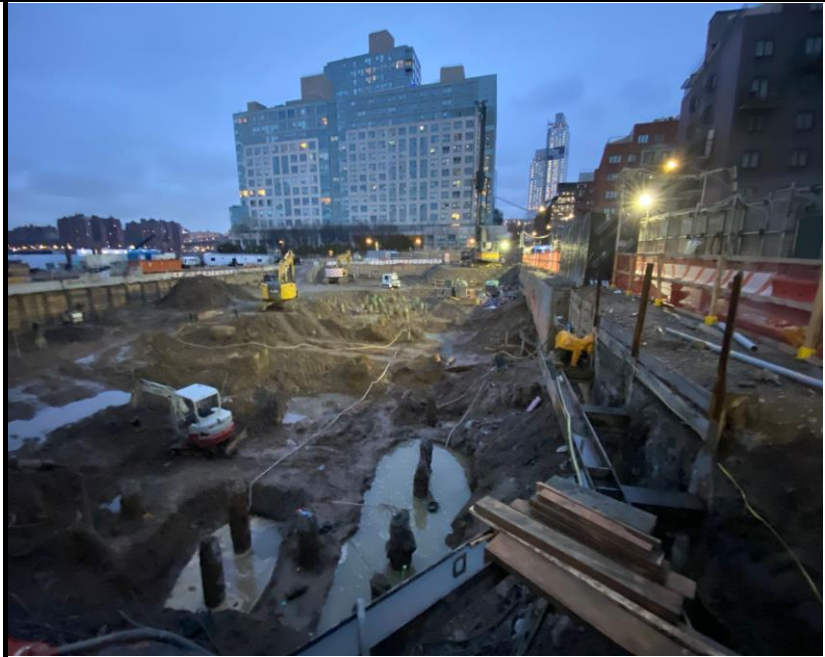


Photo 2:
View of truck loading for
off-site soil disposal.



Photo 3:
View of Site
conditions facing
east.




Photo 4:
View of Site
conditions facing
south.



CAMP:
Downwind
Particulates

Dust Levels


0.01 mg/m³ 0.011 mg/m³ 0.15

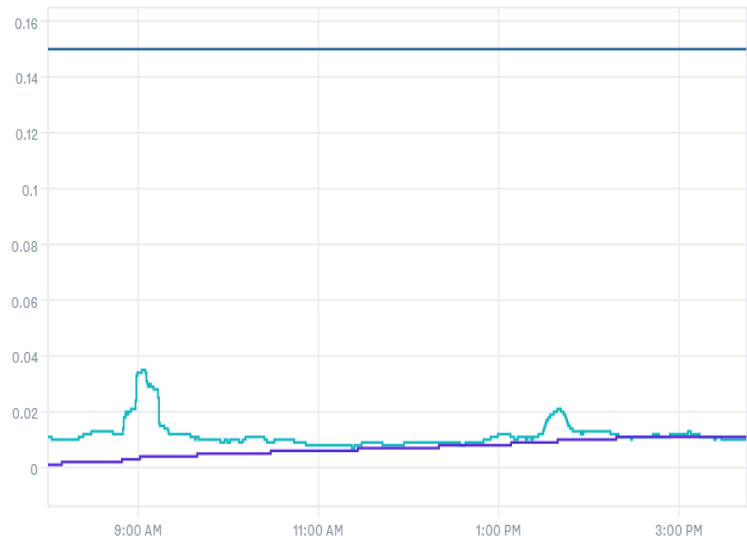

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm 5

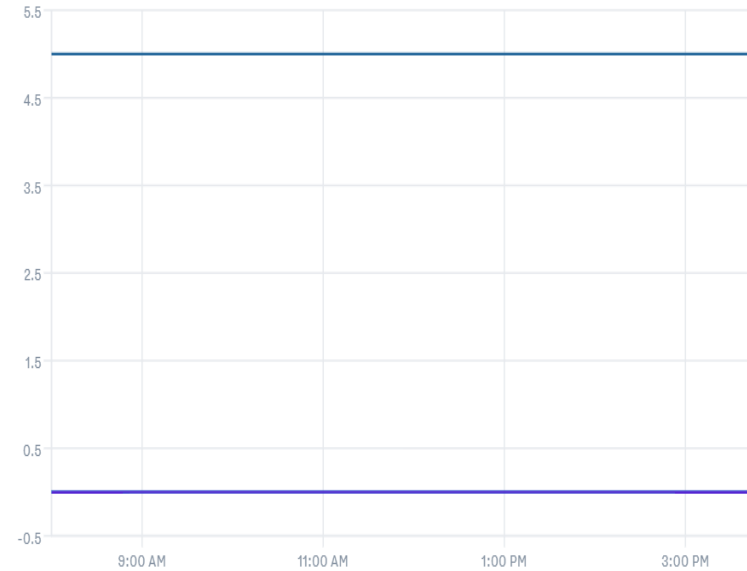

CAMP:
Upwind Particulates

Dust Levels


0.017 mg/m³ 0.016 mg/m³ 0.15

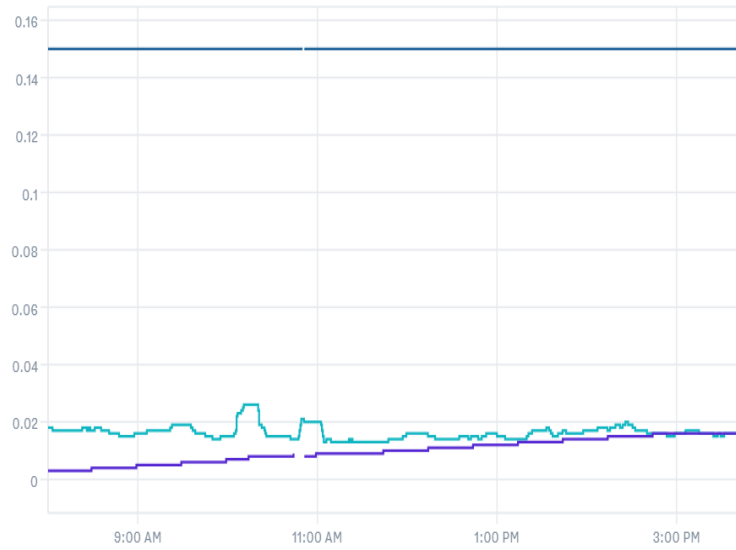

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0.004 ppm 5

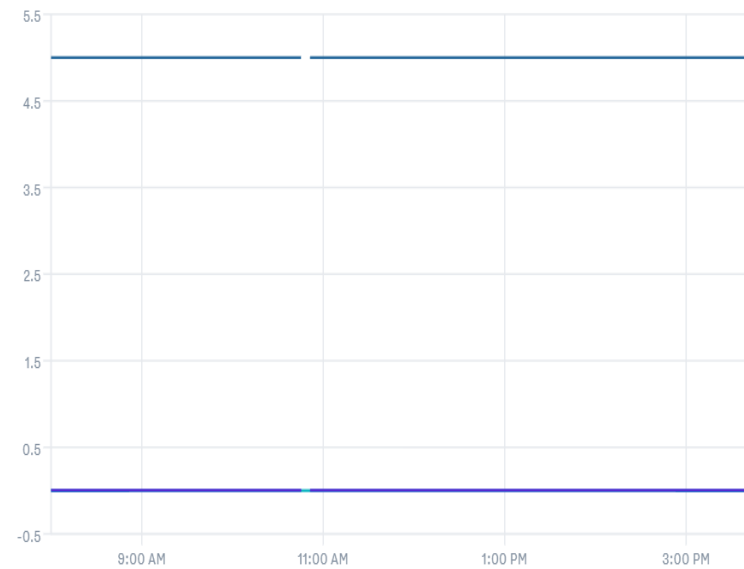

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 47907	1/31/2024 8:00	1/31/2024 8:10	0.150	0.002	5	0
DW 47907	1/31/2024 8:10	1/31/2024 8:20	0.150	0.002	5	0
DW 47907	1/31/2024 8:20	1/31/2024 8:30	0.150	0.002	5	0
DW 47907	1/31/2024 8:30	1/31/2024 8:40	0.150	0.002	5	0
DW 47907	1/31/2024 8:40	1/31/2024 8:50	0.150	0.003	5	0
DW 47907	1/31/2024 8:50	1/31/2024 9:00	0.150	0.003	5	0
DW 47907	1/31/2024 9:00	1/31/2024 9:10	0.150	0.004	5	0
DW 47907	1/31/2024 9:10	1/31/2024 9:20	0.150	0.004	5	0
DW 47907	1/31/2024 9:20	1/31/2024 9:30	0.150	0.004	5	0
DW 47907	1/31/2024 9:30	1/31/2024 9:40	0.150	0.005	5	0
DW 47907	1/31/2024 9:40	1/31/2024 9:50	0.150	0.005	5	0
DW 47907	1/31/2024 9:50	1/31/2024 10:00	0.150	0.005	5	0
DW 47907	1/31/2024 10:00	1/31/2024 10:10	0.150	0.005	5	0
DW 47907	1/31/2024 10:10	1/31/2024 10:20	0.150	0.005	5	0
DW 47907	1/31/2024 10:20	1/31/2024 10:30	0.150	0.006	5	0
DW 47907	1/31/2024 10:30	1/31/2024 10:40	0.150	0.006	5	0
DW 47907	1/31/2024 10:40	1/31/2024 10:50	0.150	0.006	5	0
DW 47907	1/31/2024 10:50	1/31/2024 11:00	0.150	0.006	5	0
DW 47907	1/31/2024 11:00	1/31/2024 11:10	0.150	0.006	5	0
DW 47907	1/31/2024 11:10	1/31/2024 11:20	0.150	0.006	5	0
DW 47907	1/31/2024 11:20	1/31/2024 11:30	0.150	0.007	5	0
DW 47907	1/31/2024 11:30	1/31/2024 11:40	0.150	0.007	5	0
DW 47907	1/31/2024 11:40	1/31/2024 11:50	0.150	0.007	5	0
DW 47907	1/31/2024 11:50	1/31/2024 12:00	0.150	0.007	5	0
DW 47907	1/31/2024 12:00	1/31/2024 12:10	0.150	0.007	5	0
DW 47907	1/31/2024 12:10	1/31/2024 12:20	0.150	0.007	5	0
DW 47907	1/31/2024 12:20	1/31/2024 12:30	0.150	0.008	5	0
DW 47907	1/31/2024 12:30	1/31/2024 12:40	0.150	0.008	5	0
DW 47907	1/31/2024 12:40	1/31/2024 12:50	0.150	0.008	5	0
DW 47907	1/31/2024 12:50	1/31/2024 13:00	0.150	0.008	5	0
DW 47907	1/31/2024 13:00	1/31/2024 13:10	0.150	0.009	5	0
DW 47907	1/31/2024 13:10	1/31/2024 13:20	0.150	0.009	5	0
DW 47907	1/31/2024 13:20	1/31/2024 13:30	0.150	0.009	5	0
DW 47907	1/31/2024 13:30	1/31/2024 13:40	0.150	0.01	5	0
DW 47907	1/31/2024 13:40	1/31/2024 13:50	0.150	0.01	5	0
DW 47907	1/31/2024 13:50	1/31/2024 14:00	0.150	0.01	5	0
DW 47907	1/31/2024 14:00	1/31/2024 14:10	0.150	0.01	5	0
DW 47907	1/31/2024 14:10	1/31/2024 14:20	0.150	0.011	5	0
DW 47907	1/31/2024 14:20	1/31/2024 14:30	0.150	0.011	5	0
DW 47907	1/31/2024 14:30	1/31/2024 14:40	0.150	0.011	5	0
DW 47907	1/31/2024 14:40	1/31/2024 14:50	0.150	0.011	5	0
DW 47907	1/31/2024 14:50	1/31/2024 15:00	0.150	0.011	5	0
DW 47907	1/31/2024 15:00	1/31/2024 15:10	0.150	0.011	5	0
DW 47907	1/31/2024 15:10	1/31/2024 15:20	0.150	0.011	5	0
DW 47907	1/31/2024 15:20	1/31/2024 15:30	0.150	0.011	5	0
DW 47907	1/31/2024 15:30	1/31/2024 15:40	0.150	0.011	5	0
DW 47907	1/31/2024 15:40	1/31/2024 15:50	0.150	0.011	5	0
DW 47907	1/31/2024 15:50	1/31/2024 16:00	0.150	0.011	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 212221	1/31/2024 8:00	1/31/2024 8:10	0.150	0.003	5	0.004
UW 212221	1/31/2024 8:10	1/31/2024 8:20	0.150	0.003	5	0.004
UW 212221	1/31/2024 8:20	1/31/2024 8:30	0.150	0.004	5	0.004
UW 212221	1/31/2024 8:30	1/31/2024 8:40	0.150	0.004	5	0.004
UW 212221	1/31/2024 8:40	1/31/2024 8:50	0.150	0.004	5	0.004
UW 212221	1/31/2024 8:50	1/31/2024 9:00	0.150	0.005	5	0.004
UW 212221	1/31/2024 9:00	1/31/2024 9:10	0.150	0.005	5	0.004
UW 212221	1/31/2024 9:10	1/31/2024 9:20	0.150	0.005	5	0.004
UW 212221	1/31/2024 9:20	1/31/2024 9:30	0.150	0.006	5	0.004
UW 212221	1/31/2024 9:30	1/31/2024 9:40	0.150	0.006	5	0.004
UW 212221	1/31/2024 9:40	1/31/2024 9:50	0.150	0.006	5	0.004
UW 212221	1/31/2024 9:50	1/31/2024 10:00	0.150	0.007	5	0.004
UW 212221	1/31/2024 10:00	1/31/2024 10:10	0.150	0.007	5	0.004
UW 212221	1/31/2024 10:10	1/31/2024 10:20	0.150	0.008	5	0.004
UW 212221	1/31/2024 10:20	1/31/2024 10:30	0.150	0.008	5	0.004
UW 212221	1/31/2024 10:30	1/31/2024 10:40	0.150	0.008	5	0.004
UW 212221	1/31/2024 10:40	1/31/2024 10:50	0.150	0.009	5	0.004
UW 212221	1/31/2024 10:50	1/31/2024 11:00	0.150	0.009	5	0.004
UW 212221	1/31/2024 11:00	1/31/2024 11:10	0.150	0.009	5	0.004
UW 212221	1/31/2024 11:10	1/31/2024 11:20	0.150	0.009	5	0.004
UW 212221	1/31/2024 11:20	1/31/2024 11:30	0.150	0.009	5	0.004
UW 212221	1/31/2024 11:30	1/31/2024 11:40	0.150	0.009	5	0.004
UW 212221	1/31/2024 11:40	1/31/2024 11:50	0.150	0.01	5	0.004
UW 212221	1/31/2024 11:50	1/31/2024 12:00	0.150	0.01	5	0.004
UW 212221	1/31/2024 12:00	1/31/2024 12:10	0.150	0.01	5	0.004
UW 212221	1/31/2024 12:10	1/31/2024 12:20	0.150	0.011	5	0.004
UW 212221	1/31/2024 12:20	1/31/2024 12:30	0.150	0.011	5	0.004
UW 212221	1/31/2024 12:30	1/31/2024 12:40	0.150	0.011	5	0.004
UW 212221	1/31/2024 12:40	1/31/2024 12:50	0.150	0.012	5	0.004
UW 212221	1/31/2024 12:50	1/31/2024 13:00	0.150	0.012	5	0.004
UW 212221	1/31/2024 13:00	1/31/2024 13:10	0.150	0.012	5	0.004
UW 212221	1/31/2024 13:10	1/31/2024 13:20	0.150	0.013	5	0.004
UW 212221	1/31/2024 13:20	1/31/2024 13:30	0.150	0.013	5	0.004
UW 212221	1/31/2024 13:30	1/31/2024 13:40	0.150	0.013	5	0.004
UW 212221	1/31/2024 13:40	1/31/2024 13:50	0.150	0.014	5	0.004
UW 212221	1/31/2024 13:50	1/31/2024 14:00	0.150	0.014	5	0.004
UW 212221	1/31/2024 14:00	1/31/2024 14:10	0.150	0.014	5	0.004
UW 212221	1/31/2024 14:10	1/31/2024 14:20	0.150	0.015	5	0.004
UW 212221	1/31/2024 14:20	1/31/2024 14:30	0.150	0.015	5	0.004
UW 212221	1/31/2024 14:30	1/31/2024 14:40	0.150	0.015	5	0.004
UW 212221	1/31/2024 14:40	1/31/2024 14:50	0.150	0.016	5	0.004
UW 212221	1/31/2024 14:50	1/31/2024 15:00	0.150	0.016	5	0.004
UW 212221	1/31/2024 15:00	1/31/2024 15:10	0.150	0.016	5	0.004
UW 212221	1/31/2024 15:10	1/31/2024 15:20	0.150	0.016	5	0.004
UW 212221	1/31/2024 15:20	1/31/2024 15:30	0.150	0.016	5	0.004
UW 212221	1/31/2024 15:30	1/31/2024 15:40	0.150	0.016	5	0.004
UW 212221	1/31/2024 15:40	1/31/2024 15:50	0.150	0.016	5	0.004
UW 212221	1/31/2024 15:50	1/31/2024 16:00	0.150	0.016	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 50057	1/31/2024 8:00	1/31/2024 8:10	0.150	0.003	5	0
PER1 50057	1/31/2024 8:10	1/31/2024 8:20	0.150	0.003	5	0
PER1 50057	1/31/2024 8:20	1/31/2024 8:30	0.150	0.004	5	0
PER1 50057	1/31/2024 8:30	1/31/2024 8:40	0.150	0.004	5	0
PER1 50057	1/31/2024 8:40	1/31/2024 8:50	0.150	0.005	5	0
PER1 50057	1/31/2024 8:50	1/31/2024 9:00	0.150	0.005	5	0
PER1 50057	1/31/2024 9:00	1/31/2024 9:10	0.150	0.006	5	0
PER1 50057	1/31/2024 9:10	1/31/2024 9:20	0.150	0.006	5	0
PER1 50057	1/31/2024 9:20	1/31/2024 9:30	0.150	0.006	5	0
PER1 50057	1/31/2024 9:30	1/31/2024 9:40	0.150	0.007	5	0
PER1 50057	1/31/2024 9:40	1/31/2024 9:50	0.150	0.007	5	0
PER1 50057	1/31/2024 9:50	1/31/2024 10:00	0.150	0.007	5	0
PER1 50057	1/31/2024 10:00	1/31/2024 10:10	0.150	0.008	5	0
PER1 50057	1/31/2024 10:10	1/31/2024 10:20	0.150	0.008	5	0
PER1 50057	1/31/2024 10:20	1/31/2024 10:30	0.150	0.009	5	0
PER1 50057	1/31/2024 10:30	1/31/2024 10:40	0.150	0.009	5	0
PER1 50057	1/31/2024 10:40	1/31/2024 10:50	0.150	0.009	5	0
PER1 50057	1/31/2024 10:50	1/31/2024 11:00	0.150	0.01	5	0
PER1 50057	1/31/2024 11:00	1/31/2024 11:10	0.150	0.01	5	0
PER1 50057	1/31/2024 11:10	1/31/2024 11:20	0.150	0.01	5	0
PER1 50057	1/31/2024 11:20	1/31/2024 11:30	0.150	0.011	5	0
PER1 50057	1/31/2024 11:30	1/31/2024 11:40	0.150	0.011	5	0
PER1 50057	1/31/2024 11:40	1/31/2024 11:50	0.150	0.012	5	0
PER1 50057	1/31/2024 11:50	1/31/2024 12:00	0.150	0.012	5	0
PER1 50057	1/31/2024 12:00	1/31/2024 12:10	0.150	0.012	5	0
PER1 50057	1/31/2024 12:10	1/31/2024 12:20	0.150	0.012	5	0
PER1 50057	1/31/2024 12:20	1/31/2024 12:30	0.150	0.013	5	0
PER1 50057	1/31/2024 12:30	1/31/2024 12:40	0.150	0.013	5	0
PER1 50057	1/31/2024 12:40	1/31/2024 12:50	0.150	0.013	5	0
PER1 50057	1/31/2024 12:50	1/31/2024 13:00	0.150	0.014	5	0
PER1 50057	1/31/2024 13:00	1/31/2024 13:10	0.150	0.014	5	0
PER1 50057	1/31/2024 13:10	1/31/2024 13:20	0.150	0.014	5	0
PER1 50057	1/31/2024 13:20	1/31/2024 13:30	0.150	0.015	5	0
PER1 50057	1/31/2024 13:30	1/31/2024 13:40	0.150	0.015	5	0
PER1 50057	1/31/2024 13:40	1/31/2024 13:50	0.150	0.016	5	0
PER1 50057	1/31/2024 13:50	1/31/2024 14:00	0.150	0.016	5	0
PER1 50057	1/31/2024 14:00	1/31/2024 14:10	0.150	0.016	5	0
PER1 50057	1/31/2024 14:10	1/31/2024 14:20	0.150	0.017	5	0
PER1 50057	1/31/2024 14:20	1/31/2024 14:30	0.150	0.017	5	0
PER1 50057	1/31/2024 14:30	1/31/2024 14:40	0.150	0.018	5	0
PER1 50057	1/31/2024 14:40	1/31/2024 14:50	0.150	0.018	5	0
PER1 50057	1/31/2024 14:50	1/31/2024 15:00	0.150	0.019	5	0
PER1 50057	1/31/2024 15:00	1/31/2024 15:10	0.150	0.019	5	0
PER1 50057	1/31/2024 15:10	1/31/2024 15:20	0.150	0.019	5	0
PER1 50057	1/31/2024 15:20	1/31/2024 15:30	0.150	0.019	5	0
PER1 50057	1/31/2024 15:30	1/31/2024 15:40	0.150	0.019	5	0
PER1 50057	1/31/2024 15:40	1/31/2024 15:50	0.150	0	5	0
PER1 50057	1/31/2024 15:50	1/31/2024 16:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 46495	1/31/2024 8:00	1/31/2024 8:10	0.150	0.003	5	0
PER2 46495	1/31/2024 8:10	1/31/2024 8:20	0.150	0.004	5	0
PER2 46495	1/31/2024 8:20	1/31/2024 8:30	0.150	0.004	5	0
PER2 46495	1/31/2024 8:30	1/31/2024 8:40	0.150	0.005	5	0
PER2 46495	1/31/2024 8:40	1/31/2024 8:50	0.150	0.005	5	0
PER2 46495	1/31/2024 8:50	1/31/2024 9:00	0.150	0.005	5	0
PER2 46495	1/31/2024 9:00	1/31/2024 9:10	0.150	0.006	5	0
PER2 46495	1/31/2024 9:10	1/31/2024 9:20	0.150	0.017	5	0
PER2 46495	1/31/2024 9:20	1/31/2024 9:30	0.150	0.018	5	0
PER2 46495	1/31/2024 9:30	1/31/2024 9:40	0.150	0.018	5	0
PER2 46495	1/31/2024 9:40	1/31/2024 9:50	0.150	0.019	5	0
PER2 46495	1/31/2024 9:50	1/31/2024 10:00	0.150	0.019	5	0
PER2 46495	1/31/2024 10:00	1/31/2024 10:10	0.150	0.019	5	0
PER2 46495	1/31/2024 10:10	1/31/2024 10:20	0.150	0.02	5	0
PER2 46495	1/31/2024 10:20	1/31/2024 10:30	0.150	0.02	5	0
PER2 46495	1/31/2024 10:30	1/31/2024 10:40	0.150	0.02	5	0
PER2 46495	1/31/2024 10:40	1/31/2024 10:50	0.150	0.021	5	0
PER2 46495	1/31/2024 10:50	1/31/2024 11:00	0.150	0.021	5	0
PER2 46495	1/31/2024 11:00	1/31/2024 11:10	0.150	0.022	5	0
PER2 46495	1/31/2024 11:10	1/31/2024 11:20	0.150	0.022	5	0
PER2 46495	1/31/2024 11:20	1/31/2024 11:30	0.150	0.022	5	0
PER2 46495	1/31/2024 11:30	1/31/2024 11:40	0.150	0.023	5	0
PER2 46495	1/31/2024 11:40	1/31/2024 11:50	0.150	0.023	5	0
PER2 46495	1/31/2024 11:50	1/31/2024 12:00	0.150	0.023	5	0
PER2 46495	1/31/2024 12:00	1/31/2024 12:10	0.150	0.024	5	0
PER2 46495	1/31/2024 12:10	1/31/2024 12:20	0.150	0.024	5	0
PER2 46495	1/31/2024 12:20	1/31/2024 12:30	0.150	0.024	5	0
PER2 46495	1/31/2024 12:30	1/31/2024 12:40	0.150	0.025	5	0
PER2 46495	1/31/2024 12:40	1/31/2024 12:50	0.150	0.025	5	0
PER2 46495	1/31/2024 12:50	1/31/2024 13:00	0.150	0.025	5	0
PER2 46495	1/31/2024 13:00	1/31/2024 13:10	0.150	0.026	5	0
PER2 46495	1/31/2024 13:10	1/31/2024 13:20	0.150	0.026	5	0
PER2 46495	1/31/2024 13:20	1/31/2024 13:30	0.150	0.027	5	0
PER2 46495	1/31/2024 13:30	1/31/2024 13:40	0.150	0.028	5	0
PER2 46495	1/31/2024 13:40	1/31/2024 13:50	0.150	0.028	5	0
PER2 46495	1/31/2024 13:50	1/31/2024 14:00	0.150	0.029	5	0
PER2 46495	1/31/2024 14:00	1/31/2024 14:10	0.150	0.029	5	0
PER2 46495	1/31/2024 14:10	1/31/2024 14:20	0.150	0.029	5	0
PER2 46495	1/31/2024 14:20	1/31/2024 14:30	0.150	0.03	5	0
PER2 46495	1/31/2024 14:30	1/31/2024 14:40	0.150	0.03	5	0
PER2 46495	1/31/2024 14:40	1/31/2024 14:50	0.150	0.03	5	0
PER2 46495	1/31/2024 14:50	1/31/2024 15:00	0.150	0.031	5	0
PER2 46495	1/31/2024 15:00	1/31/2024 15:10	0.150	0.031	5	0
PER2 46495	1/31/2024 15:10	1/31/2024 15:20	0.150	0.031	5	0
PER2 46495	1/31/2024 15:20	1/31/2024 15:30	0.150	0.031	5	0
PER2 46495	1/31/2024 15:30	1/31/2024 15:40	0.150	0.031	5	0
PER2 46495	1/31/2024 15:40	1/31/2024 15:50	0.150	0.031	5	0
PER2 46495	1/31/2024 15:50	1/31/2024 16:00	0.150	0.031	5	0
