

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/1/2024

Weather: 40 deg. F, Sunny


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continuing installing rebar, continuing with excavation, waterproofing installation, pile installation, concrete pouring and SOE installation. 2) ECD continues working on SOE in preparation for water front remedial excavation. 3) Alba exported 7 loads (approximately 140 CY) of material from WC-29 for off-site disposal at the MSM facility. 4) Alba exported 9 loads (approximately 180 CY) of material from WC-29 for off-site disposal at the Middlesex County Utilities Authority.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below. VOC spikes in the DW CAMP caused by welding activities in the vicinity the station.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	140	0	180
Total:(CY)	3765	0	6885	1520	2000

Site Layout Map and Excavation Figures

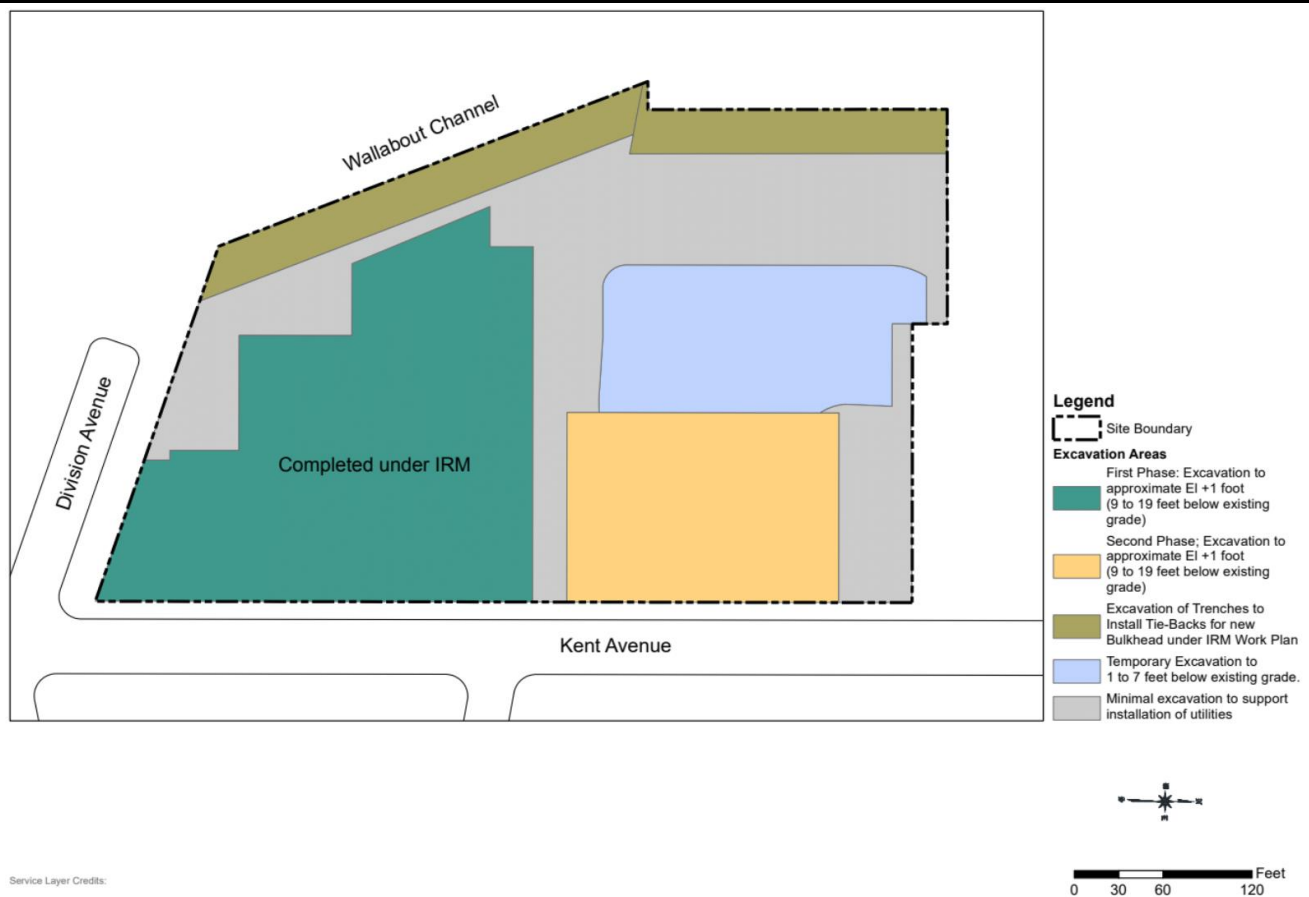

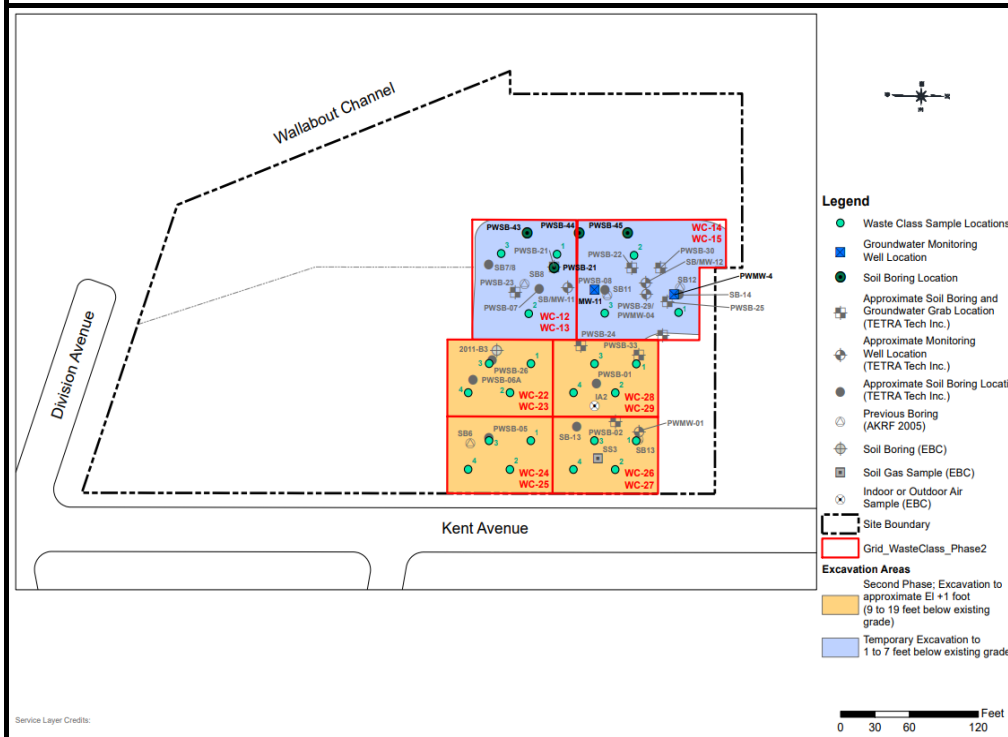
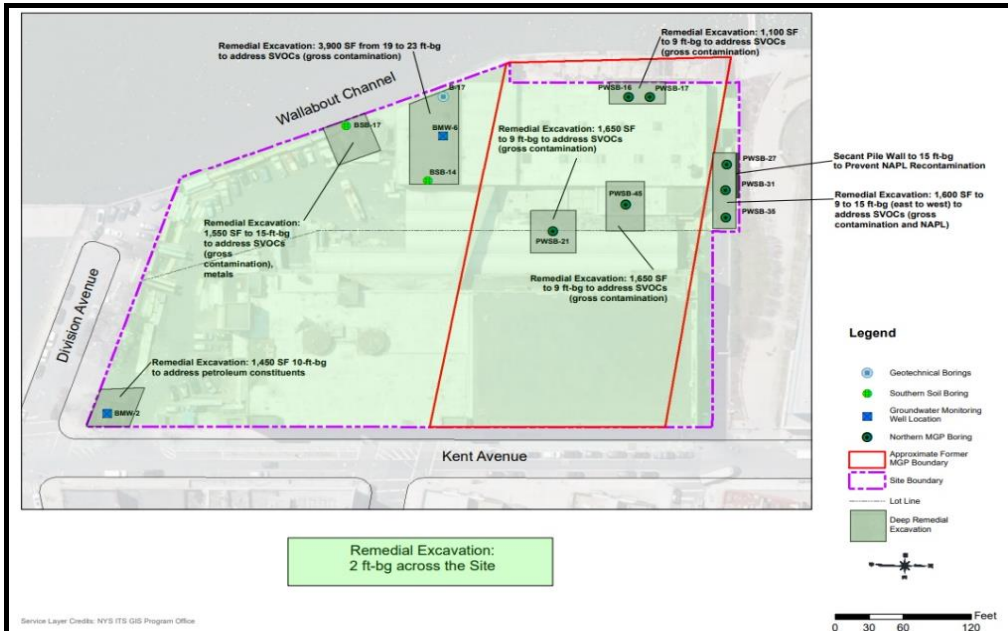


Photo 1:
View of Site conditions
facing southwest.

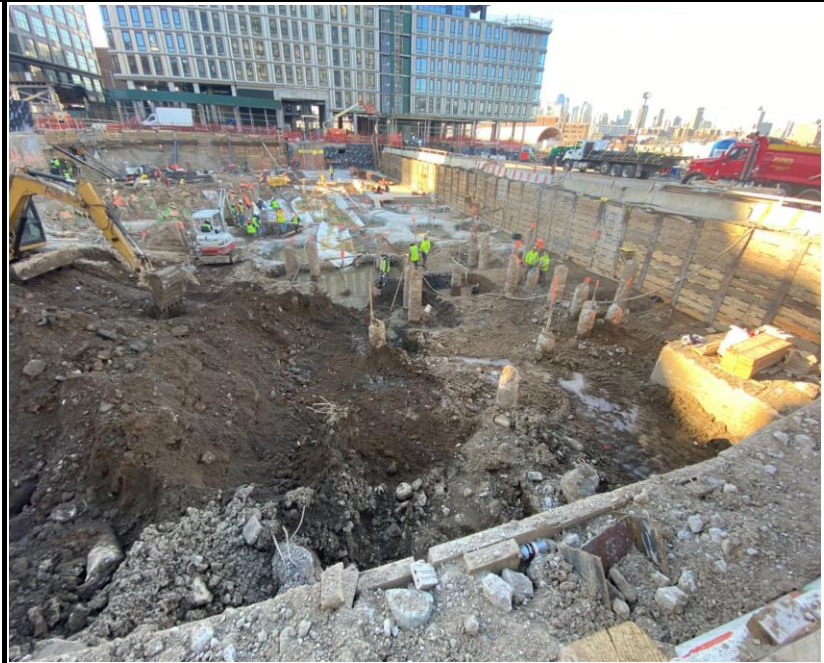


Photo 2:
View of soil excavation.




Photo 3:

View of concrete slab for building foundation development.



Photo 4:


View of continued SOE development for the waterfront remedial excavation.

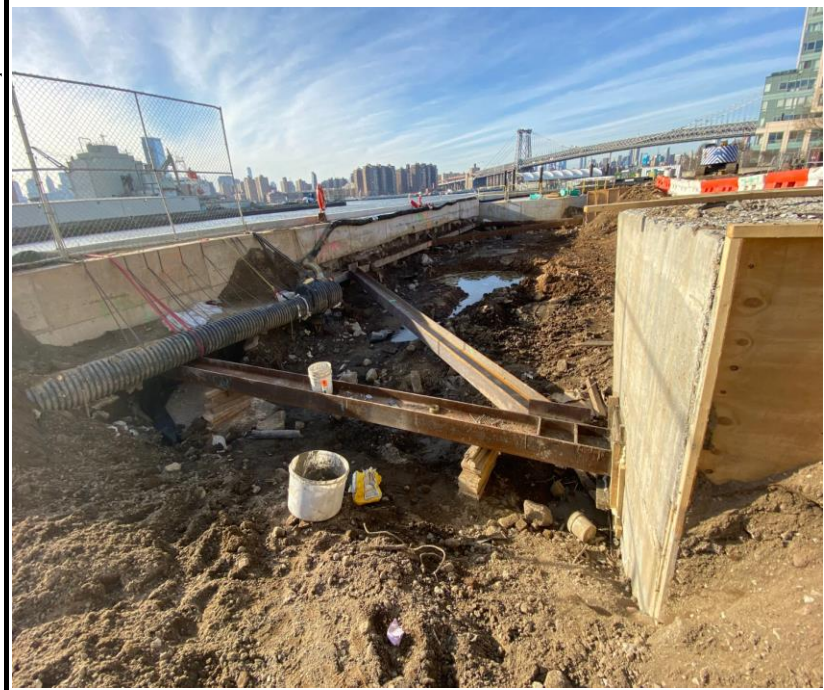

CAMP:
Downwind
Particulates

Dust Levels


0.023 mg/m³ 0.045 mg/m³

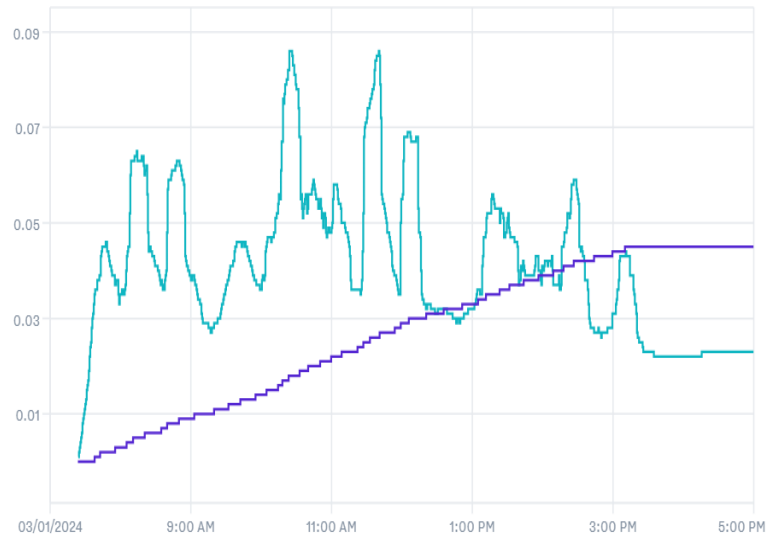

CAMP:
Downwind VOCs

VOC Levels


0.269 ppm 0.315 ppm

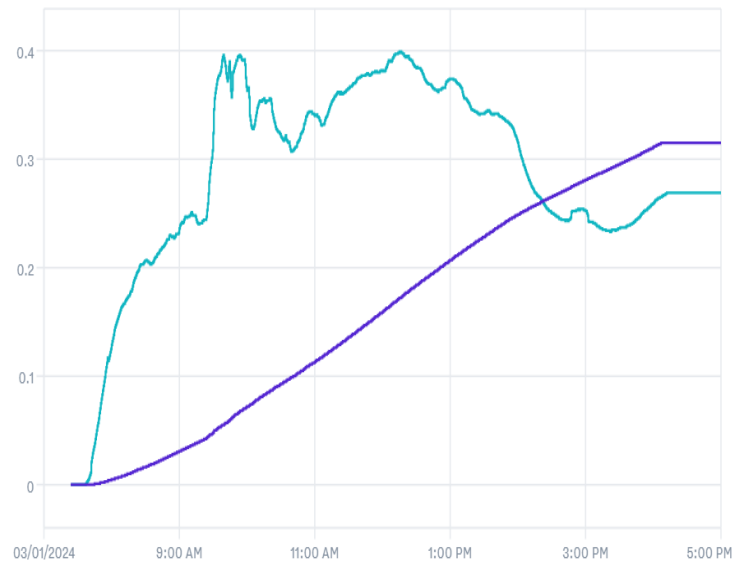

CAMP:
Upwind Particulates

Dust Levels


0.024 mg/m³ 0.026 mg/m³ 0.15

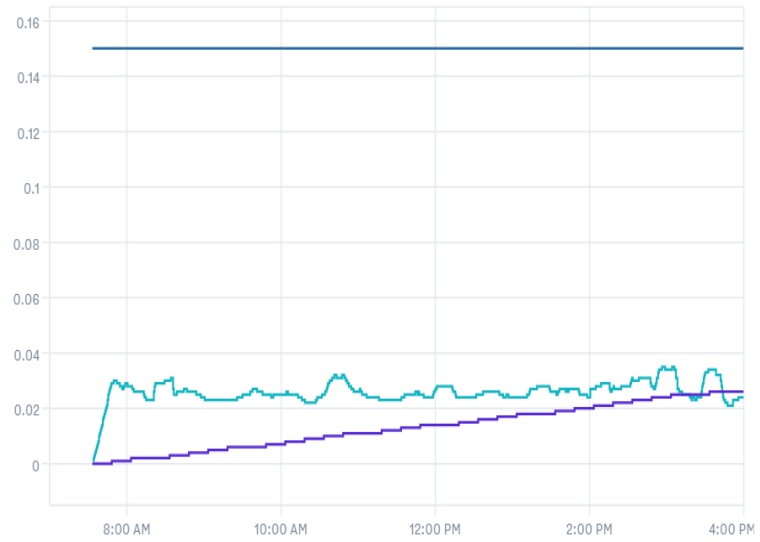

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0.008 ppm 5

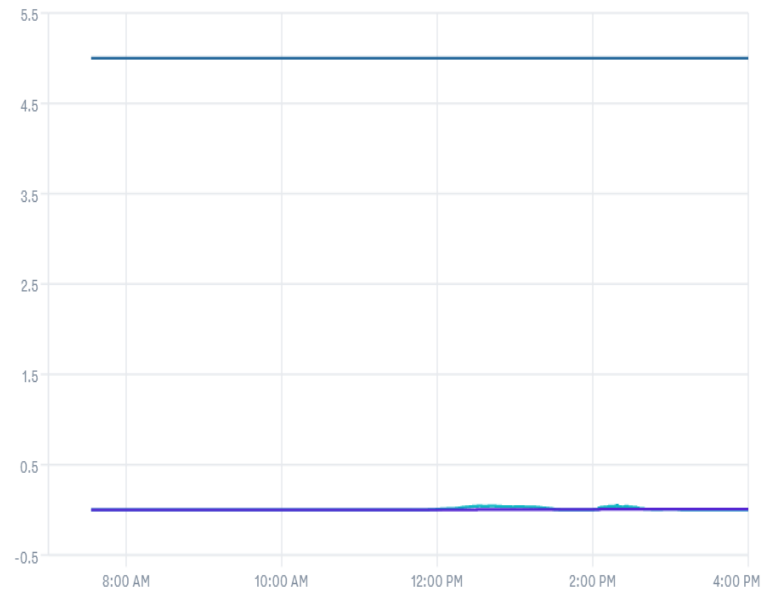

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/1/2024 7:30	3/1/2024 7:40	0.150	0.001	5	0
DW 2024	3/1/2024 7:40	3/1/2024 7:50	0.150	0.002	5	0.002
DW 2024	3/1/2024 7:50	3/1/2024 8:00	0.150	0.003	5	0.005
DW 2024	3/1/2024 8:00	3/1/2024 8:10	0.150	0.004	5	0.008
DW 2024	3/1/2024 8:10	3/1/2024 8:20	0.150	0.005	5	0.012
DW 2024	3/1/2024 8:20	3/1/2024 8:30	0.150	0.006	5	0.016
DW 2024	3/1/2024 8:30	3/1/2024 8:40	0.150	0.008	5	0.021
DW 2024	3/1/2024 8:40	3/1/2024 8:50	0.150	0.009	5	0.026
DW 2024	3/1/2024 8:50	3/1/2024 9:00	0.150	0.009	5	0.031
DW 2024	3/1/2024 9:00	3/1/2024 9:10	0.150	0.01	5	0.036
DW 2024	3/1/2024 9:10	3/1/2024 9:20	0.150	0.011	5	0.041
DW 2024	3/1/2024 9:20	3/1/2024 9:30	0.150	0.011	5	0.048
DW 2024	3/1/2024 9:30	3/1/2024 9:40	0.150	0.012	5	0.056
DW 2024	3/1/2024 9:40	3/1/2024 9:50	0.150	0.013	5	0.065
DW 2024	3/1/2024 9:50	3/1/2024 10:00	0.150	0.014	5	0.072
DW 2024	3/1/2024 10:00	3/1/2024 10:10	0.150	0.015	5	0.079
DW 2024	3/1/2024 10:10	3/1/2024 10:20	0.150	0.017	5	0.086
DW 2024	3/1/2024 10:20	3/1/2024 10:30	0.150	0.018	5	0.093
DW 2024	3/1/2024 10:30	3/1/2024 10:40	0.150	0.019	5	0.099
DW 2024	3/1/2024 10:40	3/1/2024 10:50	0.150	0.02	5	0.106
DW 2024	3/1/2024 10:50	3/1/2024 11:00	0.150	0.022	5	0.113
DW 2024	3/1/2024 11:00	3/1/2024 11:10	0.150	0.023	5	0.12
DW 2024	3/1/2024 11:10	3/1/2024 11:20	0.150	0.023	5	0.128
DW 2024	3/1/2024 11:20	3/1/2024 11:30	0.150	0.025	5	0.136
DW 2024	3/1/2024 11:30	3/1/2024 11:40	0.150	0.026	5	0.143
DW 2024	3/1/2024 11:40	3/1/2024 11:50	0.150	0.027	5	0.151
DW 2024	3/1/2024 11:50	3/1/2024 12:00	0.150	0.029	5	0.159
DW 2024	3/1/2024 12:00	3/1/2024 12:10	0.150	0.03	5	0.168
DW 2024	3/1/2024 12:10	3/1/2024 12:20	0.150	0.03	5	0.176
DW 2024	3/1/2024 12:20	3/1/2024 12:30	0.150	0.031	5	0.184
DW 2024	3/1/2024 12:30	3/1/2024 12:40	0.150	0.032	5	0.191
DW 2024	3/1/2024 12:40	3/1/2024 12:50	0.150	0.032	5	0.199
DW 2024	3/1/2024 12:50	3/1/2024 13:00	0.150	0.033	5	0.207
DW 2024	3/1/2024 13:00	3/1/2024 13:10	0.150	0.034	5	0.214
DW 2024	3/1/2024 13:10	3/1/2024 13:20	0.150	0.035	5	0.221
DW 2024	3/1/2024 13:20	3/1/2024 13:30	0.150	0.036	5	0.228
DW 2024	3/1/2024 13:30	3/1/2024 13:40	0.150	0.037	5	0.236
DW 2024	3/1/2024 13:40	3/1/2024 13:50	0.150	0.038	5	0.243
DW 2024	3/1/2024 13:50	3/1/2024 14:00	0.150	0.039	5	0.249
DW 2024	3/1/2024 14:00	3/1/2024 14:10	0.150	0.04	5	0.255
DW 2024	3/1/2024 14:10	3/1/2024 14:20	0.150	0.041	5	0.26
DW 2024	3/1/2024 14:20	3/1/2024 14:30	0.150	0.042	5	0.265
DW 2024	3/1/2024 14:30	3/1/2024 14:40	0.150	0.042	5	0.27
DW 2024	3/1/2024 14:40	3/1/2024 14:50	0.150	0.043	5	0.276
DW 2024	3/1/2024 14:50	3/1/2024 15:00	0.150	0.044	5	0.281
DW 2024	3/1/2024 15:00	3/1/2024 15:10	0.150	0.044	5	0.286
DW 2024	3/1/2024 15:10	3/1/2024 15:20	0.150	0.045	5	0.29
DW 2024	3/1/2024 15:20	3/1/2024 15:30	0.150	0.045	5	0.295
DW 2024	3/1/2024 15:30	3/1/2024 15:40	0.150	0.045	5	0.3
DW 2024	3/1/2024 15:40	3/1/2024 15:50	0.150	0.045	5	0.306
DW 2024	3/1/2024 15:50	3/1/2024 16:00	0.150	0.045	5	0.311
DW 2024	3/1/2024 16:00	3/1/2024 16:10	0.150	0.045	5	0.315
DW 2024	3/1/2024 16:10	3/1/2024 16:20	0.150	0.045	5	0.315
DW 2024	3/1/2024 16:20	3/1/2024 16:30	0.150	0.045	5	0.315
DW 2024	3/1/2024 16:30	3/1/2024 16:40	0.150	0.045	5	0.315
DW 2024	3/1/2024 16:40	3/1/2024 16:50	0.150	0.045	5	0.315
DW 2024	3/1/2024 16:50	3/1/2024 17:00	0.150	0.045	5	0.315

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/1/2024 7:30	3/1/2024 7:40	0.150	0	5	0
UW 2024	3/1/2024 7:40	3/1/2024 7:50	0.150	0.001	5	0
UW 2024	3/1/2024 7:50	3/1/2024 8:00	0.150	0.001	5	0
UW 2024	3/1/2024 8:00	3/1/2024 8:10	0.150	0.002	5	0
UW 2024	3/1/2024 8:10	3/1/2024 8:20	0.150	0.002	5	0
UW 2024	3/1/2024 8:20	3/1/2024 8:30	0.150	0.002	5	0
UW 2024	3/1/2024 8:30	3/1/2024 8:40	0.150	0.003	5	0
UW 2024	3/1/2024 8:40	3/1/2024 8:50	0.150	0.004	5	0
UW 2024	3/1/2024 8:50	3/1/2024 9:00	0.150	0.004	5	0
UW 2024	3/1/2024 9:00	3/1/2024 9:10	0.150	0.005	5	0
UW 2024	3/1/2024 9:10	3/1/2024 9:20	0.150	0.006	5	0
UW 2024	3/1/2024 9:20	3/1/2024 9:30	0.150	0.006	5	0
UW 2024	3/1/2024 9:30	3/1/2024 9:40	0.150	0.006	5	0
UW 2024	3/1/2024 9:40	3/1/2024 9:50	0.150	0.007	5	0
UW 2024	3/1/2024 9:50	3/1/2024 10:00	0.150	0.007	5	0
UW 2024	3/1/2024 10:00	3/1/2024 10:10	0.150	0.008	5	0
UW 2024	3/1/2024 10:10	3/1/2024 10:20	0.150	0.009	5	0
UW 2024	3/1/2024 10:20	3/1/2024 10:30	0.150	0.009	5	0
UW 2024	3/1/2024 10:30	3/1/2024 10:40	0.150	0.01	5	0
UW 2024	3/1/2024 10:40	3/1/2024 10:50	0.150	0.011	5	0
UW 2024	3/1/2024 10:50	3/1/2024 11:00	0.150	0.011	5	0
UW 2024	3/1/2024 11:00	3/1/2024 11:10	0.150	0.011	5	0
UW 2024	3/1/2024 11:10	3/1/2024 11:20	0.150	0.012	5	0
UW 2024	3/1/2024 11:20	3/1/2024 11:30	0.150	0.012	5	0
UW 2024	3/1/2024 11:30	3/1/2024 11:40	0.150	0.013	5	0
UW 2024	3/1/2024 11:40	3/1/2024 11:50	0.150	0.014	5	0
UW 2024	3/1/2024 11:50	3/1/2024 12:00	0.150	0.014	5	0
UW 2024	3/1/2024 12:00	3/1/2024 12:10	0.150	0.014	5	0
UW 2024	3/1/2024 12:10	3/1/2024 12:20	0.150	0.015	5	0.001
UW 2024	3/1/2024 12:20	3/1/2024 12:30	0.150	0.015	5	0.001
UW 2024	3/1/2024 12:30	3/1/2024 12:40	0.150	0.016	5	0.002
UW 2024	3/1/2024 12:40	3/1/2024 12:50	0.150	0.017	5	0.003
UW 2024	3/1/2024 12:50	3/1/2024 13:00	0.150	0.017	5	0.004
UW 2024	3/1/2024 13:00	3/1/2024 13:10	0.150	0.018	5	0.004
UW 2024	3/1/2024 13:10	3/1/2024 13:20	0.150	0.018	5	0.005
UW 2024	3/1/2024 13:20	3/1/2024 13:30	0.150	0.018	5	0.005
UW 2024	3/1/2024 13:30	3/1/2024 13:40	0.150	0.019	5	0.005
UW 2024	3/1/2024 13:40	3/1/2024 13:50	0.150	0.02	5	0.005
UW 2024	3/1/2024 13:50	3/1/2024 14:00	0.150	0.02	5	0.005
UW 2024	3/1/2024 14:00	3/1/2024 14:10	0.150	0.021	5	0.006
UW 2024	3/1/2024 14:10	3/1/2024 14:20	0.150	0.022	5	0.007
UW 2024	3/1/2024 14:20	3/1/2024 14:30	0.150	0.022	5	0.007
UW 2024	3/1/2024 14:30	3/1/2024 14:40	0.150	0.023	5	0.007
UW 2024	3/1/2024 14:40	3/1/2024 14:50	0.150	0.024	5	0.007
UW 2024	3/1/2024 14:50	3/1/2024 15:00	0.150	0.024	5	0.008
UW 2024	3/1/2024 15:00	3/1/2024 15:10	0.150	0.025	5	0.008
UW 2024	3/1/2024 15:10	3/1/2024 15:20	0.150	0.025	5	0.008
UW 2024	3/1/2024 15:20	3/1/2024 15:30	0.150	0.025	5	0.008
UW 2024	3/1/2024 15:30	3/1/2024 15:40	0.150	0.026	5	0.008
UW 2024	3/1/2024 15:40	3/1/2024 15:50	0.150	0.026	5	0.008
UW 2024	3/1/2024 15:50	3/1/2024 16:00	0.150	0.026	5	0.008
UW 2024	3/1/2024 16:00	3/1/2024 16:10	0.150	0.026	5	0.008
UW 2024	3/1/2024 16:10	3/1/2024 16:20	0.150	0.026	5	0
UW 2024	3/1/2024 16:20	3/1/2024 16:30	0.150	0	5	0
UW 2024	3/1/2024 16:30	3/1/2024 16:40	0.150	0	5	0
UW 2024	3/1/2024 16:40	3/1/2024 16:50	0.150	0	5	0
UW 2024	3/1/2024 16:50	3/1/2024 17:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/1/2024 7:30	3/1/2024 7:40	0.150	0	5	0
HS South	3/1/2024 7:40	3/1/2024 7:50	0.150	0.001	5	0
HS South	3/1/2024 7:50	3/1/2024 8:00	0.150	0.001	5	0
HS South	3/1/2024 8:00	3/1/2024 8:10	0.150	0.002	5	0
HS South	3/1/2024 8:10	3/1/2024 8:20	0.150	0.003	5	0
HS South	3/1/2024 8:20	3/1/2024 8:30	0.150	0.003	5	0
HS South	3/1/2024 8:30	3/1/2024 8:40	0.150	0.004	5	0
HS South	3/1/2024 8:40	3/1/2024 8:50	0.150	0.004	5	0
HS South	3/1/2024 8:50	3/1/2024 9:00	0.150	0.005	5	0
HS South	3/1/2024 9:00	3/1/2024 9:10	0.150	0.005	5	0
HS South	3/1/2024 9:10	3/1/2024 9:20	0.150	0.006	5	0
HS South	3/1/2024 9:20	3/1/2024 9:30	0.150	0.006	5	0
HS South	3/1/2024 9:30	3/1/2024 9:40	0.150	0.007	5	0
HS South	3/1/2024 9:40	3/1/2024 9:50	0.150	0.008	5	0
HS South	3/1/2024 9:50	3/1/2024 10:00	0.150	0.008	5	0
HS South	3/1/2024 10:00	3/1/2024 10:10	0.150	0.009	5	0
HS South	3/1/2024 10:10	3/1/2024 10:20	0.150	0.009	5	0
HS South	3/1/2024 10:20	3/1/2024 10:30	0.150	0.01	5	0
HS South	3/1/2024 10:30	3/1/2024 10:40	0.150	0.01	5	0
HS South	3/1/2024 10:40	3/1/2024 10:50	0.150	0.011	5	0
HS South	3/1/2024 10:50	3/1/2024 11:00	0.150	0.011	5	0
HS South	3/1/2024 11:00	3/1/2024 11:10	0.150	0.012	5	0
HS South	3/1/2024 11:10	3/1/2024 11:20	0.150	0.012	5	0
HS South	3/1/2024 11:20	3/1/2024 11:30	0.150	0.013	5	0
HS South	3/1/2024 11:30	3/1/2024 11:40	0.150	0.014	5	0
HS South	3/1/2024 11:40	3/1/2024 11:50	0.150	0.014	5	0
HS South	3/1/2024 11:50	3/1/2024 12:00	0.150	0.015	5	0
HS South	3/1/2024 12:00	3/1/2024 12:10	0.150	0.016	5	0
HS South	3/1/2024 12:10	3/1/2024 12:20	0.150	0.017	5	0
HS South	3/1/2024 12:20	3/1/2024 12:30	0.150	0.017	5	0
HS South	3/1/2024 12:30	3/1/2024 12:40	0.150	0.018	5	0
HS South	3/1/2024 12:40	3/1/2024 12:50	0.150	0.018	5	0
HS South	3/1/2024 12:50	3/1/2024 13:00	0.150	0.019	5	0
HS South	3/1/2024 13:00	3/1/2024 13:10	0.150	0.019	5	0
HS South	3/1/2024 13:10	3/1/2024 13:20	0.150	0.02	5	0
HS South	3/1/2024 13:20	3/1/2024 13:30	0.150	0.02	5	0
HS South	3/1/2024 13:30	3/1/2024 13:40	0.150	0.021	5	0
HS South	3/1/2024 13:40	3/1/2024 13:50	0.150	0.021	5	0
HS South	3/1/2024 13:50	3/1/2024 14:00	0.150	0.022	5	0
HS South	3/1/2024 14:00	3/1/2024 14:10	0.150	0.022	5	0
HS South	3/1/2024 14:10	3/1/2024 14:20	0.150	0.023	5	0
HS South	3/1/2024 14:20	3/1/2024 14:30	0.150	0.023	5	0
HS South	3/1/2024 14:30	3/1/2024 14:40	0.150	0.024	5	0
HS South	3/1/2024 14:40	3/1/2024 14:50	0.150	0.024	5	0
HS South	3/1/2024 14:50	3/1/2024 15:00	0.150	0.024	5	0
HS South	3/1/2024 15:00	3/1/2024 15:10	0.150	0.025	5	0
HS South	3/1/2024 15:10	3/1/2024 15:20	0.150	0.025	5	0
HS South	3/1/2024 15:20	3/1/2024 15:30	0.150	0.025	5	0
HS South	3/1/2024 15:30	3/1/2024 15:40	0.150	0.025	5	0
HS South	3/1/2024 15:40	3/1/2024 15:50	0.150	0.025	5	0
HS South	3/1/2024 15:50	3/1/2024 16:00	0.150	0.025	5	0
HS South	3/1/2024 16:00	3/1/2024 16:10	0.150	0.025	5	0
HS South	3/1/2024 16:10	3/1/2024 16:20	0.150	0.025	5	0
HS South	3/1/2024 16:20	3/1/2024 16:30	0.150	0.025	5	0
HS South	3/1/2024 16:30	3/1/2024 16:40	0.150	0.025	5	0
HS South	3/1/2024 16:40	3/1/2024 16:50	0.150	0.025	5	0
HS South	3/1/2024 16:50	3/1/2024 17:00	0.150	0.025	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/1/2024 7:30	3/1/2024 7:40	0.150	0	5	0
PER1 2024	3/1/2024 7:40	3/1/2024 7:50	0.150	0	5	0
PER1 2024	3/1/2024 7:50	3/1/2024 8:00	0.150	0.002	5	0
PER1 2024	3/1/2024 8:00	3/1/2024 8:10	0.150	0.002	5	0
PER1 2024	3/1/2024 8:10	3/1/2024 8:20	0.150	0.003	5	0
PER1 2024	3/1/2024 8:20	3/1/2024 8:30	0.150	0.004	5	0
PER1 2024	3/1/2024 8:30	3/1/2024 8:40	0.150	0.004	5	0
PER1 2024	3/1/2024 8:40	3/1/2024 8:50	0.150	0.005	5	0
PER1 2024	3/1/2024 8:50	3/1/2024 9:00	0.150	0.006	5	0
PER1 2024	3/1/2024 9:00	3/1/2024 9:10	0.150	0.006	5	0
PER1 2024	3/1/2024 9:10	3/1/2024 9:20	0.150	0.007	5	0
PER1 2024	3/1/2024 9:20	3/1/2024 9:30	0.150	0.008	5	0
PER1 2024	3/1/2024 9:30	3/1/2024 9:40	0.150	0.009	5	0
PER1 2024	3/1/2024 9:40	3/1/2024 9:50	0.150	0.01	5	0
PER1 2024	3/1/2024 9:50	3/1/2024 10:00	0.150	0.011	5	0
PER1 2024	3/1/2024 10:00	3/1/2024 10:10	0.150	0.012	5	0
PER1 2024	3/1/2024 10:10	3/1/2024 10:20	0.150	0.013	5	0
PER1 2024	3/1/2024 10:20	3/1/2024 10:30	0.150	0.013	5	0
PER1 2024	3/1/2024 10:30	3/1/2024 10:40	0.150	0.014	5	0
PER1 2024	3/1/2024 10:40	3/1/2024 10:50	0.150	0.015	5	0
PER1 2024	3/1/2024 10:50	3/1/2024 11:00	0.150	0.016	5	0
PER1 2024	3/1/2024 11:00	3/1/2024 11:10	0.150	0.017	5	0
PER1 2024	3/1/2024 11:10	3/1/2024 11:20	0.150	0.018	5	0
PER1 2024	3/1/2024 11:20	3/1/2024 11:30	0.150	0.019	5	0
PER1 2024	3/1/2024 11:30	3/1/2024 11:40	0.150	0.02	5	0
PER1 2024	3/1/2024 11:40	3/1/2024 11:50	0.150	0.02	5	0
PER1 2024	3/1/2024 11:50	3/1/2024 12:00	0.150	0.021	5	0
PER1 2024	3/1/2024 12:00	3/1/2024 12:10	0.150	0.022	5	0
PER1 2024	3/1/2024 12:10	3/1/2024 12:20	0.150	0.023	5	0
PER1 2024	3/1/2024 12:20	3/1/2024 12:30	0.150	0.024	5	0
PER1 2024	3/1/2024 12:30	3/1/2024 12:40	0.150	0.025	5	0
PER1 2024	3/1/2024 12:40	3/1/2024 12:50	0.150	0.026	5	0
PER1 2024	3/1/2024 12:50	3/1/2024 13:00	0.150	0.027	5	0
PER1 2024	3/1/2024 13:00	3/1/2024 13:10	0.150	0.028	5	0
PER1 2024	3/1/2024 13:10	3/1/2024 13:20	0.150	0.029	5	0
PER1 2024	3/1/2024 13:20	3/1/2024 13:30	0.150	0.03	5	0.001
PER1 2024	3/1/2024 13:30	3/1/2024 13:40	0.150	0.031	5	0.001
PER1 2024	3/1/2024 13:40	3/1/2024 13:50	0.150	0.032	5	0.001
PER1 2024	3/1/2024 13:50	3/1/2024 14:00	0.150	0.032	5	0.001
PER1 2024	3/1/2024 14:00	3/1/2024 14:10	0.150	0.033	5	0.001
PER1 2024	3/1/2024 14:10	3/1/2024 14:20	0.150	0.034	5	0.001
PER1 2024	3/1/2024 14:20	3/1/2024 14:30	0.150	0.035	5	0.001
PER1 2024	3/1/2024 14:30	3/1/2024 14:40	0.150	0.036	5	0.001
PER1 2024	3/1/2024 14:40	3/1/2024 14:50	0.150	0.036	5	0.001
PER1 2024	3/1/2024 14:50	3/1/2024 15:00	0.150	0.037	5	0.001
PER1 2024	3/1/2024 15:00	3/1/2024 15:10	0.150	0.038	5	0.001
PER1 2024	3/1/2024 15:10	3/1/2024 15:20	0.150	0.039	5	0.001
PER1 2024	3/1/2024 15:20	3/1/2024 15:30	0.150	0.04	5	0.001
PER1 2024	3/1/2024 15:30	3/1/2024 15:40	0.150	0.04	5	0.001
PER1 2024	3/1/2024 15:40	3/1/2024 15:50	0.150	0.04	5	0.001
PER1 2024	3/1/2024 15:50	3/1/2024 16:00	0.150	0.04	5	0
PER1 2024	3/1/2024 16:00	3/1/2024 16:10	0.150	0	5	0
PER1 2024	3/1/2024 16:10	3/1/2024 16:20	0.150	0	5	0
PER1 2024	3/1/2024 16:20	3/1/2024 16:30	0.150	0	5	0
PER1 2024	3/1/2024 16:30	3/1/2024 16:40	0.150	0	5	0
PER1 2024	3/1/2024 16:40	3/1/2024 16:50	0.150	0	5	0
PER1 2024	3/1/2024 16:50	3/1/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/1/2024 7:30	3/1/2024 7:40	0.150	0	5	0
PER2 2024	3/1/2024 7:40	3/1/2024 7:50	0.150	0	5	0
PER2 2024	3/1/2024 7:50	3/1/2024 8:00	0.150	0.001	5	0
PER2 2024	3/1/2024 8:00	3/1/2024 8:10	0.150	0.003	5	0
PER2 2024	3/1/2024 8:10	3/1/2024 8:20	0.150	0.005	5	0
PER2 2024	3/1/2024 8:20	3/1/2024 8:30	0.150	0.006	5	0.001
PER2 2024	3/1/2024 8:30	3/1/2024 8:40	0.150	0.007	5	0.002
PER2 2024	3/1/2024 8:40	3/1/2024 8:50	0.150	0.008	5	0.003
PER2 2024	3/1/2024 8:50	3/1/2024 9:00	0.150	0.009	5	0.004
PER2 2024	3/1/2024 9:00	3/1/2024 9:10	0.150	0.011	5	0.005
PER2 2024	3/1/2024 9:10	3/1/2024 9:20	0.150	0.011	5	0.006
PER2 2024	3/1/2024 9:20	3/1/2024 9:30	0.150	0.013	5	0.007
PER2 2024	3/1/2024 9:30	3/1/2024 9:40	0.150	0.015	5	0.009
PER2 2024	3/1/2024 9:40	3/1/2024 9:50	0.150	0.018	5	0.01
PER2 2024	3/1/2024 9:50	3/1/2024 10:00	0.150	0.02	5	0.012
PER2 2024	3/1/2024 10:00	3/1/2024 10:10	0.150	0.022	5	0.014
PER2 2024	3/1/2024 10:10	3/1/2024 10:20	0.150	0.023	5	0.016
PER2 2024	3/1/2024 10:20	3/1/2024 10:30	0.150	0.026	5	0.017
PER2 2024	3/1/2024 10:30	3/1/2024 10:40	0.150	0.026	5	0.018
PER2 2024	3/1/2024 10:40	3/1/2024 10:50	0.150	0.027	5	0.02
PER2 2024	3/1/2024 10:50	3/1/2024 11:00	0.150	0.028	5	0.021
PER2 2024	3/1/2024 11:00	3/1/2024 11:10	0.150	0.029	5	0.023
PER2 2024	3/1/2024 11:10	3/1/2024 11:20	0.150	0.03	5	0.025
PER2 2024	3/1/2024 11:20	3/1/2024 11:30	0.150	0.031	5	0.027
PER2 2024	3/1/2024 11:30	3/1/2024 11:40	0.150	0.032	5	0.028
PER2 2024	3/1/2024 11:40	3/1/2024 11:50	0.150	0.032	5	0.029
PER2 2024	3/1/2024 11:50	3/1/2024 12:00	0.150	0.033	5	0.031
PER2 2024	3/1/2024 12:00	3/1/2024 12:10	0.150	0.035	5	0.032
PER2 2024	3/1/2024 12:10	3/1/2024 12:20	0.150	0.036	5	0.033
PER2 2024	3/1/2024 12:20	3/1/2024 12:30	0.150	0.037	5	0.034
PER2 2024	3/1/2024 12:30	3/1/2024 12:40	0.150	0.037	5	0.035
PER2 2024	3/1/2024 12:40	3/1/2024 12:50	0.150	0.038	5	0.036
PER2 2024	3/1/2024 12:50	3/1/2024 13:00	0.150	0.039	5	0.037
PER2 2024	3/1/2024 13:00	3/1/2024 13:10	0.150	0.04	5	0.037
PER2 2024	3/1/2024 13:10	3/1/2024 13:20	0.150	0.041	5	0.038
PER2 2024	3/1/2024 13:20	3/1/2024 13:30	0.150	0.041	5	0.038
PER2 2024	3/1/2024 13:30	3/1/2024 13:40	0.150	0.042	5	0.039
PER2 2024	3/1/2024 13:40	3/1/2024 13:50	0.150	0.043	5	0.04
PER2 2024	3/1/2024 13:50	3/1/2024 14:00	0.150	0.043	5	0.04
PER2 2024	3/1/2024 14:00	3/1/2024 14:10	0.150	0.044	5	0.041
PER2 2024	3/1/2024 14:10	3/1/2024 14:20	0.150	0.045	5	0.042
PER2 2024	3/1/2024 14:20	3/1/2024 14:30	0.150	0.045	5	0.043
PER2 2024	3/1/2024 14:30	3/1/2024 14:40	0.150	0.046	5	0.044
PER2 2024	3/1/2024 14:40	3/1/2024 14:50	0.150	0.046	5	0.046
PER2 2024	3/1/2024 14:50	3/1/2024 15:00	0.150	0.047	5	0.047
PER2 2024	3/1/2024 15:00	3/1/2024 15:10	0.150	0.048	5	0.048
PER2 2024	3/1/2024 15:10	3/1/2024 15:20	0.150	0.048	5	0.049
PER2 2024	3/1/2024 15:20	3/1/2024 15:30	0.150	0.049	5	0.05
PER2 2024	3/1/2024 15:30	3/1/2024 15:40	0.150	0.049	5	0.051
PER2 2024	3/1/2024 15:40	3/1/2024 15:50	0.150	0.049	5	0.052
PER2 2024	3/1/2024 15:50	3/1/2024 16:00	0.150	0.049	5	0.053
PER2 2024	3/1/2024 16:00	3/1/2024 16:10	0.150	0.049	5	0.054
PER2 2024	3/1/2024 16:10	3/1/2024 16:20	0.150	0.049	5	0.054
PER2 2024	3/1/2024 16:20	3/1/2024 16:30	0.150	0.049	5	0.054
PER2 2024	3/1/2024 16:30	3/1/2024 16:40	0.150	0.049	5	0.054
PER2 2024	3/1/2024 16:40	3/1/2024 16:50	0.150	0.049	5	0.054
PER2 2024	3/1/2024 16:50	3/1/2024 17:00	0.150	0.049	5	0.054

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/4/2024

Weather: 50 deg. F, Overcast


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continuing installing rebar, continuing with excavation, waterproofing installation, pile installation, concrete pouring and SOE installation. 2) ECD continues working on SOE in preparation for water front remedial excavation. 3) Alba exported 4 loads (approximately 80 CY) of material from WC-29 for off-site disposal at the MSM facility. 4) Alba exported 6 loads (approximately 120 CY) of material from WC-29 for off-site disposal at the Middlesex County Utilities Authority. 5) Collect dewatering system influent and effluent samples.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): Influent_20240304 and Effluent_20240304	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below. The DW station experienced connectivity issues which were remedied around 10AM.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	80	0	120
Total:(CY)	3765	0	6965	1520	2120

Site Layout Map and Excavation Figures

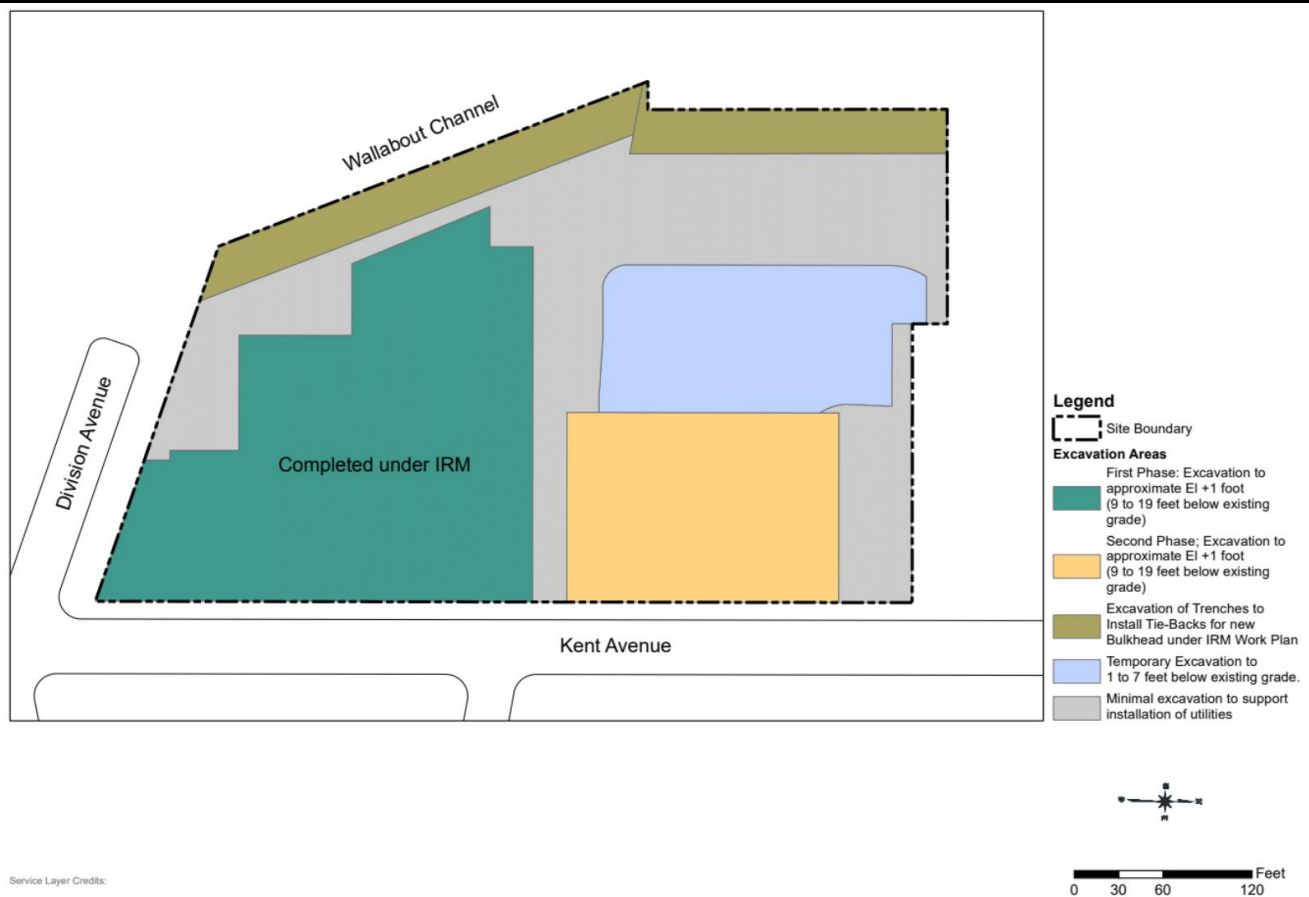

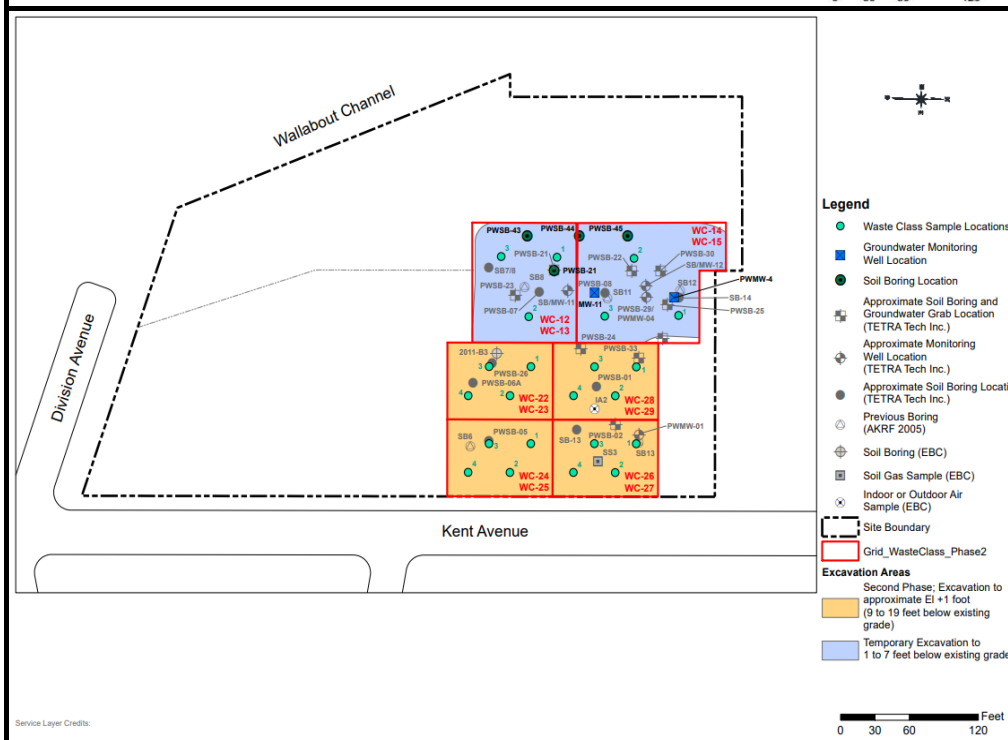
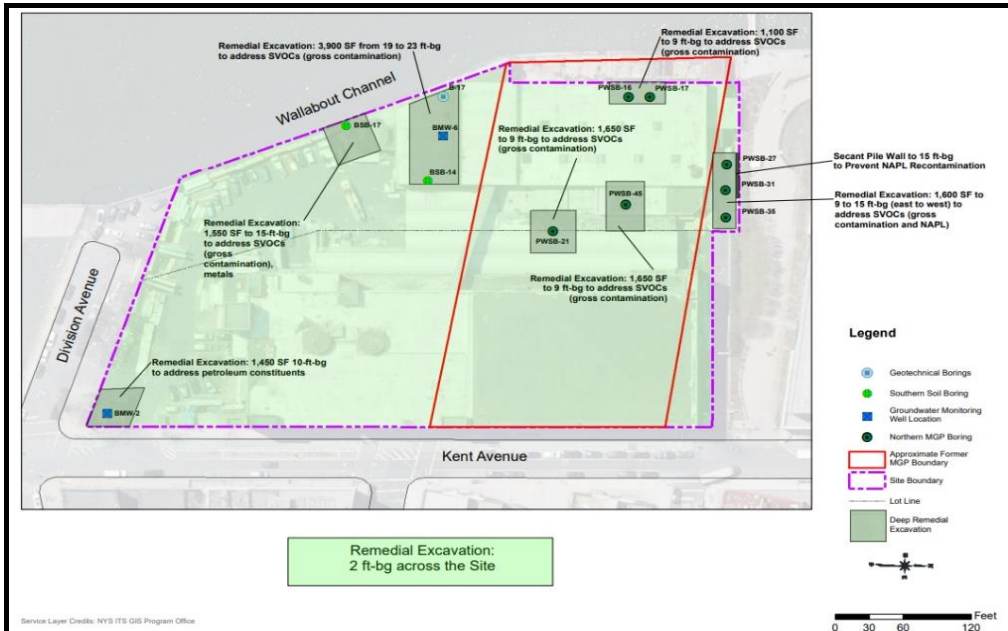


Photo 1:
View of Site conditions
facing southwest.



Photo 2:
View of truck loading for
off-site soil disposal.



Photo 3:
View of Site
conditions and
continued building
foundation
development facing
north.

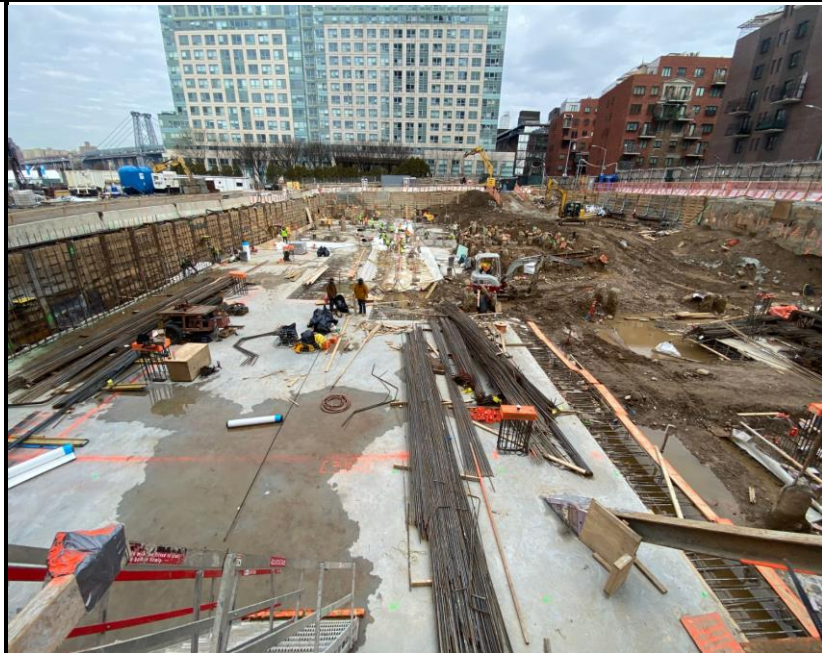



Photo 4:
View of continued
SOE development for
the waterfront
remedial excavation.



CAMP:
Downwind
Particulates

Dust Levels


0.018 mg/m³ 0.02 mg/m³

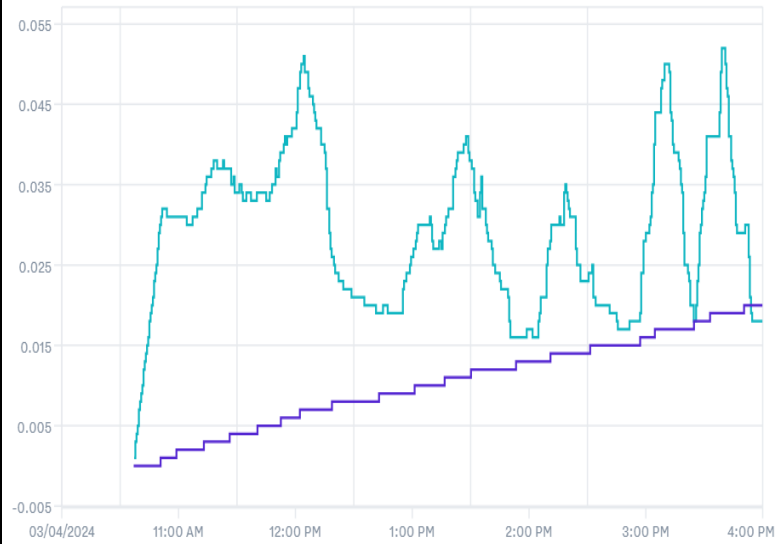

CAMP:
Downwind VOCs


VOC Levels

0.212 ppm 0.161 ppm

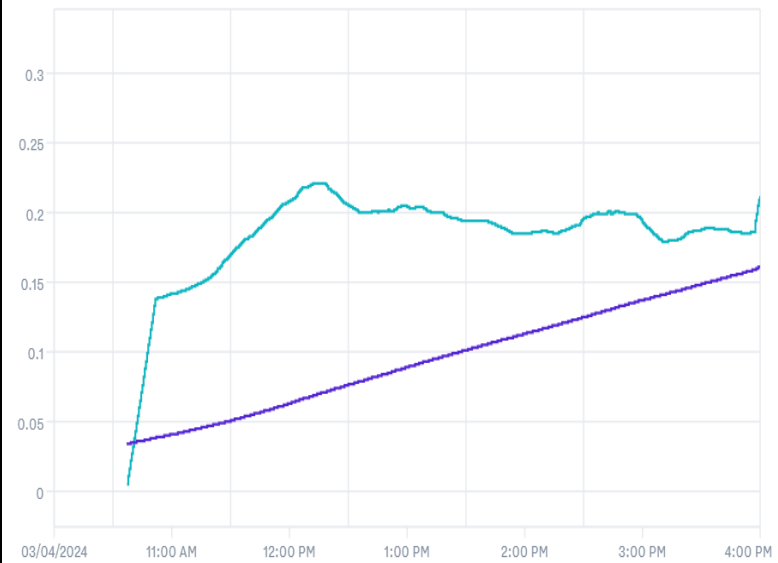


CAMP:
Upwind Particulates

Dust Levels

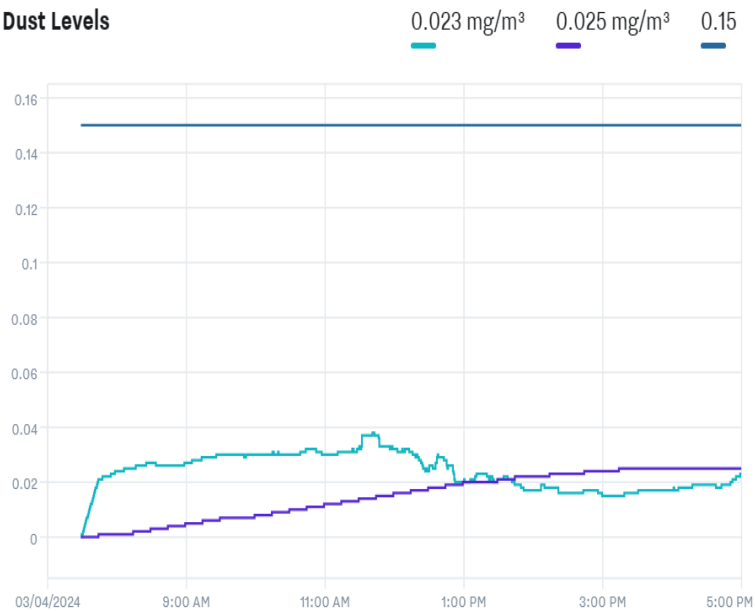

CAMP:
Upwind VOCs

VOC Levels

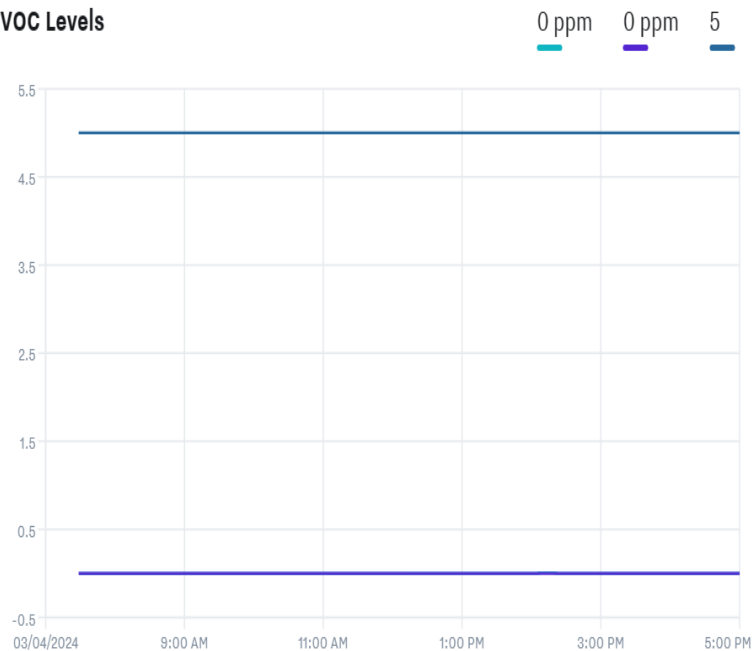

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/4/2024 10:00	3/4/2024 10:10	0.150	0	5	0
DW 2024	3/4/2024 10:10	3/4/2024 10:20	0.150	0	5	0
DW 2024	3/4/2024 10:20	3/4/2024 10:30	0.150	0	5	0
DW 2024	3/4/2024 10:30	3/4/2024 10:40	0.150	0	5	0.035
DW 2024	3/4/2024 10:40	3/4/2024 10:50	0.150	0	5	0.038
DW 2024	3/4/2024 10:50	3/4/2024 11:00	0.150	0.002	5	0.041
DW 2024	3/4/2024 11:00	3/4/2024 11:10	0.150	0.002	5	0.044
DW 2024	3/4/2024 11:10	3/4/2024 11:20	0.150	0.003	5	0.047
DW 2024	3/4/2024 11:20	3/4/2024 11:30	0.150	0.004	5	0.05
DW 2024	3/4/2024 11:30	3/4/2024 11:40	0.150	0.004	5	0.054
DW 2024	3/4/2024 11:40	3/4/2024 11:50	0.150	0.005	5	0.058
DW 2024	3/4/2024 11:50	3/4/2024 12:00	0.150	0.006	5	0.063
DW 2024	3/4/2024 12:00	3/4/2024 12:10	0.150	0.007	5	0.067
DW 2024	3/4/2024 12:10	3/4/2024 12:20	0.150	0.008	5	0.072
DW 2024	3/4/2024 12:20	3/4/2024 12:30	0.150	0.008	5	0.076
DW 2024	3/4/2024 12:30	3/4/2024 12:40	0.150	0.008	5	0.08
DW 2024	3/4/2024 12:40	3/4/2024 12:50	0.150	0.009	5	0.084
DW 2024	3/4/2024 12:50	3/4/2024 13:00	0.150	0.009	5	0.089
DW 2024	3/4/2024 13:00	3/4/2024 13:10	0.150	0.01	5	0.093
DW 2024	3/4/2024 13:10	3/4/2024 13:20	0.150	0.011	5	0.097
DW 2024	3/4/2024 13:20	3/4/2024 13:30	0.150	0.011	5	0.101
DW 2024	3/4/2024 13:30	3/4/2024 13:40	0.150	0.012	5	0.105
DW 2024	3/4/2024 13:40	3/4/2024 13:50	0.150	0.012	5	0.109
DW 2024	3/4/2024 13:50	3/4/2024 14:00	0.150	0.013	5	0.113
DW 2024	3/4/2024 14:00	3/4/2024 14:10	0.150	0.013	5	0.117
DW 2024	3/4/2024 14:10	3/4/2024 14:20	0.150	0.014	5	0.121
DW 2024	3/4/2024 14:20	3/4/2024 14:30	0.150	0.014	5	0.125
DW 2024	3/4/2024 14:30	3/4/2024 14:40	0.150	0.015	5	0.129
DW 2024	3/4/2024 14:40	3/4/2024 14:50	0.150	0.015	5	0.133
DW 2024	3/4/2024 14:50	3/4/2024 15:00	0.150	0.016	5	0.137
DW 2024	3/4/2024 15:00	3/4/2024 15:10	0.150	0.017	5	0.141
DW 2024	3/4/2024 15:10	3/4/2024 15:20	0.150	0.017	5	0.144
DW 2024	3/4/2024 15:20	3/4/2024 15:30	0.150	0.018	5	0.148
DW 2024	3/4/2024 15:30	3/4/2024 15:40	0.150	0.019	5	0.152
DW 2024	3/4/2024 15:40	3/4/2024 15:50	0.150	0.019	5	0.156
DW 2024	3/4/2024 15:50	3/4/2024 16:00	0.150	0.02	5	0.161
DW 2024	3/4/2024 16:00	3/4/2024 16:10	0.150	0.02	5	0.166
DW 2024	3/4/2024 16:10	3/4/2024 16:20	0.150	0.021	5	0.173
DW 2024	3/4/2024 16:20	3/4/2024 16:30	0.150	0.021	5	0.177
DW 2024	3/4/2024 16:30	3/4/2024 16:40	0.150	0.022	5	0.181
DW 2024	3/4/2024 16:40	3/4/2024 16:50	0.150	0.022	5	0.185
DW 2024	3/4/2024 16:50	3/4/2024 17:00	0.150	0.022	5	0.189

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/4/2024 7:30	3/4/2024 7:40	0.150	0	5	0
UW 2024	3/4/2024 7:40	3/4/2024 7:50	0.150	0.001	5	0
UW 2024	3/4/2024 7:50	3/4/2024 8:00	0.150	0.001	5	0
UW 2024	3/4/2024 8:00	3/4/2024 8:10	0.150	0.001	5	0
UW 2024	3/4/2024 8:10	3/4/2024 8:20	0.150	0.002	5	0
UW 2024	3/4/2024 8:20	3/4/2024 8:30	0.150	0.003	5	0
UW 2024	3/4/2024 8:30	3/4/2024 8:40	0.150	0.003	5	0
UW 2024	3/4/2024 8:40	3/4/2024 8:50	0.150	0.004	5	0
UW 2024	3/4/2024 8:50	3/4/2024 9:00	0.150	0.005	5	0
UW 2024	3/4/2024 9:00	3/4/2024 9:10	0.150	0.005	5	0
UW 2024	3/4/2024 9:10	3/4/2024 9:20	0.150	0.006	5	0
UW 2024	3/4/2024 9:20	3/4/2024 9:30	0.150	0.007	5	0
UW 2024	3/4/2024 9:30	3/4/2024 9:40	0.150	0.007	5	0
UW 2024	3/4/2024 9:40	3/4/2024 9:50	0.150	0.007	5	0
UW 2024	3/4/2024 9:50	3/4/2024 10:00	0.150	0.008	5	0
UW 2024	3/4/2024 10:00	3/4/2024 10:10	0.150	0.008	5	0
UW 2024	3/4/2024 10:10	3/4/2024 10:20	0.150	0.009	5	0
UW 2024	3/4/2024 10:20	3/4/2024 10:30	0.150	0.01	5	0
UW 2024	3/4/2024 10:30	3/4/2024 10:40	0.150	0.01	5	0
UW 2024	3/4/2024 10:40	3/4/2024 10:50	0.150	0.011	5	0
UW 2024	3/4/2024 10:50	3/4/2024 11:00	0.150	0.012	5	0
UW 2024	3/4/2024 11:00	3/4/2024 11:10	0.150	0.012	5	0
UW 2024	3/4/2024 11:10	3/4/2024 11:20	0.150	0.013	5	0
UW 2024	3/4/2024 11:20	3/4/2024 11:30	0.150	0.014	5	0
UW 2024	3/4/2024 11:30	3/4/2024 11:40	0.150	0.014	5	0
UW 2024	3/4/2024 11:40	3/4/2024 11:50	0.150	0.015	5	0
UW 2024	3/4/2024 11:50	3/4/2024 12:00	0.150	0.016	5	0
UW 2024	3/4/2024 12:00	3/4/2024 12:10	0.150	0.016	5	0
UW 2024	3/4/2024 12:10	3/4/2024 12:20	0.150	0.017	5	0
UW 2024	3/4/2024 12:20	3/4/2024 12:30	0.150	0.018	5	0
UW 2024	3/4/2024 12:30	3/4/2024 12:40	0.150	0.018	5	0
UW 2024	3/4/2024 12:40	3/4/2024 12:50	0.150	0.019	5	0
UW 2024	3/4/2024 12:50	3/4/2024 13:00	0.150	0.02	5	0
UW 2024	3/4/2024 13:00	3/4/2024 13:10	0.150	0.02	5	0
UW 2024	3/4/2024 13:10	3/4/2024 13:20	0.150	0.02	5	0
UW 2024	3/4/2024 13:20	3/4/2024 13:30	0.150	0.021	5	0
UW 2024	3/4/2024 13:30	3/4/2024 13:40	0.150	0.021	5	0
UW 2024	3/4/2024 13:40	3/4/2024 13:50	0.150	0.022	5	0
UW 2024	3/4/2024 13:50	3/4/2024 14:00	0.150	0.022	5	0
UW 2024	3/4/2024 14:00	3/4/2024 14:10	0.150	0.022	5	0
UW 2024	3/4/2024 14:10	3/4/2024 14:20	0.150	0.023	5	0
UW 2024	3/4/2024 14:20	3/4/2024 14:30	0.150	0.023	5	0
UW 2024	3/4/2024 14:30	3/4/2024 14:40	0.150	0.023	5	0
UW 2024	3/4/2024 14:40	3/4/2024 14:50	0.150	0.024	5	0
UW 2024	3/4/2024 14:50	3/4/2024 15:00	0.150	0.024	5	0
UW 2024	3/4/2024 15:00	3/4/2024 15:10	0.150	0.024	5	0
UW 2024	3/4/2024 15:10	3/4/2024 15:20	0.150	0.025	5	0
UW 2024	3/4/2024 15:20	3/4/2024 15:30	0.150	0.025	5	0
UW 2024	3/4/2024 15:30	3/4/2024 15:40	0.150	0.025	5	0
UW 2024	3/4/2024 15:40	3/4/2024 15:50	0.150	0.025	5	0
UW 2024	3/4/2024 15:50	3/4/2024 16:00	0.150	0.025	5	0
UW 2024	3/4/2024 16:00	3/4/2024 16:10	0.150	0.025	5	0
UW 2024	3/4/2024 16:10	3/4/2024 16:20	0.150	0.025	5	0
UW 2024	3/4/2024 16:20	3/4/2024 16:30	0.150	0.025	5	0
UW 2024	3/4/2024 16:30	3/4/2024 16:40	0.150	0.025	5	0
UW 2024	3/4/2024 16:40	3/4/2024 16:50	0.150	0.025	5	0
UW 2024	3/4/2024 16:50	3/4/2024 17:00	0.150	0.025	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/4/2024 7:30	3/4/2024 7:40	0.150	0	5	0
HS South	3/4/2024 7:40	3/4/2024 7:50	0.150	0	5	0
HS South	3/4/2024 7:50	3/4/2024 8:00	0.150	0.001	5	0
HS South	3/4/2024 8:00	3/4/2024 8:10	0.150	0.001	5	0
HS South	3/4/2024 8:10	3/4/2024 8:20	0.150	0.002	5	0
HS South	3/4/2024 8:20	3/4/2024 8:30	0.150	0.002	5	0
HS South	3/4/2024 8:30	3/4/2024 8:40	0.150	0.003	5	0
HS South	3/4/2024 8:40	3/4/2024 8:50	0.150	0.003	5	0
HS South	3/4/2024 8:50	3/4/2024 9:00	0.150	0.003	5	0
HS South	3/4/2024 9:00	3/4/2024 9:10	0.150	0.004	5	0
HS South	3/4/2024 9:10	3/4/2024 9:20	0.150	0.004	5	0
HS South	3/4/2024 9:20	3/4/2024 9:30	0.150	0.005	5	0
HS South	3/4/2024 9:30	3/4/2024 9:40	0.150	0.005	5	0
HS South	3/4/2024 9:40	3/4/2024 9:50	0.150	0.006	5	0
HS South	3/4/2024 9:50	3/4/2024 10:00	0.150	0.006	5	0
HS South	3/4/2024 10:00	3/4/2024 10:10	0.150	0.007	5	0
HS South	3/4/2024 10:10	3/4/2024 10:20	0.150	0.007	5	0
HS South	3/4/2024 10:20	3/4/2024 10:30	0.150	0.008	5	0
HS South	3/4/2024 10:30	3/4/2024 10:40	0.150	0.008	5	0
HS South	3/4/2024 10:40	3/4/2024 10:50	0.150	0.008	5	0
HS South	3/4/2024 10:50	3/4/2024 11:00	0.150	0.009	5	0
HS South	3/4/2024 11:00	3/4/2024 11:10	0.150	0.009	5	0
HS South	3/4/2024 11:10	3/4/2024 11:20	0.150	0.01	5	0
HS South	3/4/2024 11:20	3/4/2024 11:30	0.150	0.01	5	0
HS South	3/4/2024 11:30	3/4/2024 11:40	0.150	0.011	5	0
HS South	3/4/2024 11:40	3/4/2024 11:50	0.150	0.011	5	0
HS South	3/4/2024 11:50	3/4/2024 12:00	0.150	0.012	5	0
HS South	3/4/2024 12:00	3/4/2024 12:10	0.150	0.012	5	0
HS South	3/4/2024 12:10	3/4/2024 12:20	0.150	0.012	5	0
HS South	3/4/2024 12:20	3/4/2024 12:30	0.150	0.013	5	0
HS South	3/4/2024 12:30	3/4/2024 12:40	0.150	0.013	5	0
HS South	3/4/2024 12:40	3/4/2024 12:50	0.150	0.013	5	0
HS South	3/4/2024 12:50	3/4/2024 13:00	0.150	0.013	5	0
HS South	3/4/2024 13:00	3/4/2024 13:10	0.150	0.013	5	0
HS South	3/4/2024 13:10	3/4/2024 13:20	0.150	0.014	5	0
HS South	3/4/2024 13:20	3/4/2024 13:30	0.150	0.014	5	0
HS South	3/4/2024 13:30	3/4/2024 13:40	0.150	0.014	5	0
HS South	3/4/2024 13:40	3/4/2024 13:50	0.150	0.014	5	0
HS South	3/4/2024 13:50	3/4/2024 14:00	0.150	0.014	5	0
HS South	3/4/2024 14:00	3/4/2024 14:10	0.150	0.014	5	0
HS South	3/4/2024 14:10	3/4/2024 14:20	0.150	0.015	5	0
HS South	3/4/2024 14:20	3/4/2024 14:30	0.150	0.015	5	0
HS South	3/4/2024 14:30	3/4/2024 14:40	0.150	0.015	5	0
HS South	3/4/2024 14:40	3/4/2024 14:50	0.150	0.015	5	0
HS South	3/4/2024 14:50	3/4/2024 15:00	0.150	0.015	5	0
HS South	3/4/2024 15:00	3/4/2024 15:10	0.150	0.015	5	0
HS South	3/4/2024 15:10	3/4/2024 15:20	0.150	0.016	5	0
HS South	3/4/2024 15:20	3/4/2024 15:30	0.150	0.016	5	0
HS South	3/4/2024 15:30	3/4/2024 15:40	0.150	0.016	5	0
HS South	3/4/2024 15:40	3/4/2024 15:50	0.150	0.016	5	0
HS South	3/4/2024 15:50	3/4/2024 16:00	0.150	0.016	5	0
HS South	3/4/2024 16:00	3/4/2024 16:10	0.150	0.016	5	0
HS South	3/4/2024 16:10	3/4/2024 16:20	0.150	0.016	5	0
HS South	3/4/2024 16:20	3/4/2024 16:30	0.150	0.016	5	0
HS South	3/4/2024 16:30	3/4/2024 16:40	0.150	0.016	5	0
HS South	3/4/2024 16:40	3/4/2024 16:50	0.150	0.016	5	0
HS South	3/4/2024 16:50	3/4/2024 17:00	0.150	0.016	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/4/2024 7:30	3/4/2024 7:40	0.150	0.003	5	0
PER1 2024	3/4/2024 7:40	3/4/2024 7:50	0.150	0.004	5	0
PER1 2024	3/4/2024 7:50	3/4/2024 8:00	0.150	0.005	5	0
PER1 2024	3/4/2024 8:00	3/4/2024 8:10	0.150	0.005	5	0
PER1 2024	3/4/2024 8:10	3/4/2024 8:20	0.150	0.006	5	0
PER1 2024	3/4/2024 8:20	3/4/2024 8:30	0.150	0.008	5	0
PER1 2024	3/4/2024 8:30	3/4/2024 8:40	0.150	0.008	5	0.001
PER1 2024	3/4/2024 8:40	3/4/2024 8:50	0.150	0.009	5	0.001
PER1 2024	3/4/2024 8:50	3/4/2024 9:00	0.150	0.011	5	0.001
PER1 2024	3/4/2024 9:00	3/4/2024 9:10	0.150	0.012	5	0.001
PER1 2024	3/4/2024 9:10	3/4/2024 9:20	0.150	0.013	5	0.001
PER1 2024	3/4/2024 9:20	3/4/2024 9:30	0.150	0.014	5	0.001
PER1 2024	3/4/2024 9:30	3/4/2024 9:40	0.150	0.015	5	0.001
PER1 2024	3/4/2024 9:40	3/4/2024 9:50	0.150	0.016	5	0.001
PER1 2024	3/4/2024 9:50	3/4/2024 10:00	0.150	0.018	5	0.001
PER1 2024	3/4/2024 10:00	3/4/2024 10:10	0.150	0.019	5	0.001
PER1 2024	3/4/2024 10:10	3/4/2024 10:20	0.150	0.02	5	0.001
PER1 2024	3/4/2024 10:20	3/4/2024 10:30	0.150	0.021	5	0.002
PER1 2024	3/4/2024 10:30	3/4/2024 10:40	0.150	0.022	5	0.002
PER1 2024	3/4/2024 10:40	3/4/2024 10:50	0.150	0.023	5	0.002
PER1 2024	3/4/2024 10:50	3/4/2024 11:00	0.150	0.024	5	0.002
PER1 2024	3/4/2024 11:00	3/4/2024 11:10	0.150	0.025	5	0.002
PER1 2024	3/4/2024 11:10	3/4/2024 11:20	0.150	0.026	5	0.002
PER1 2024	3/4/2024 11:20	3/4/2024 11:30	0.150	0.027	5	0.002
PER1 2024	3/4/2024 11:30	3/4/2024 11:40	0.150	0.028	5	0.002
PER1 2024	3/4/2024 11:40	3/4/2024 11:50	0.150	0.029	5	0.002
PER1 2024	3/4/2024 11:50	3/4/2024 12:00	0.150	0.03	5	0.004
PER1 2024	3/4/2024 12:00	3/4/2024 12:10	0.150	0.031	5	0.004
PER1 2024	3/4/2024 12:10	3/4/2024 12:20	0.150	0.032	5	0.004
PER1 2024	3/4/2024 12:20	3/4/2024 12:30	0.150	0.032	5	0.004
PER1 2024	3/4/2024 12:30	3/4/2024 12:40	0.150	0.033	5	0.004
PER1 2024	3/4/2024 12:40	3/4/2024 12:50	0.150	0.033	5	0.004
PER1 2024	3/4/2024 12:50	3/4/2024 13:00	0.150	0.034	5	0.004
PER1 2024	3/4/2024 13:00	3/4/2024 13:10	0.150	0.035	5	0.004
PER1 2024	3/4/2024 13:10	3/4/2024 13:20	0.150	0.035	5	0.004
PER1 2024	3/4/2024 13:20	3/4/2024 13:30	0.150	0.036	5	0.004
PER1 2024	3/4/2024 13:30	3/4/2024 13:40	0.150	0.036	5	0.004
PER1 2024	3/4/2024 13:40	3/4/2024 13:50	0.150	0.037	5	0.004
PER1 2024	3/4/2024 13:50	3/4/2024 14:00	0.150	0.038	5	0.004
PER1 2024	3/4/2024 14:00	3/4/2024 14:10	0.150	0.038	5	0.004
PER1 2024	3/4/2024 14:10	3/4/2024 14:20	0.150	0.039	5	0.004
PER1 2024	3/4/2024 14:20	3/4/2024 14:30	0.150	0.039	5	0.004
PER1 2024	3/4/2024 14:30	3/4/2024 14:40	0.150	0.04	5	0.004
PER1 2024	3/4/2024 14:40	3/4/2024 14:50	0.150	0.041	5	0.004
PER1 2024	3/4/2024 14:50	3/4/2024 15:00	0.150	0.041	5	0.004
PER1 2024	3/4/2024 15:00	3/4/2024 15:10	0.150	0.042	5	0.004
PER1 2024	3/4/2024 15:10	3/4/2024 15:20	0.150	0.042	5	0.004
PER1 2024	3/4/2024 15:20	3/4/2024 15:30	0.150	0.042	5	0.004
PER1 2024	3/4/2024 15:30	3/4/2024 15:40	0.150	0.042	5	0.004
PER1 2024	3/4/2024 15:40	3/4/2024 15:50	0.150	0.042	5	0.004
PER1 2024	3/4/2024 15:50	3/4/2024 16:00	0.150	0.042	5	0.004
PER1 2024	3/4/2024 16:00	3/4/2024 16:10	0.150	0.042	5	0.004
PER1 2024	3/4/2024 16:10	3/4/2024 16:20	0.150	0.042	5	0.004
PER1 2024	3/4/2024 16:20	3/4/2024 16:30	0.150	0.042	5	0.004
PER1 2024	3/4/2024 16:30	3/4/2024 16:40	0.150	0.042	5	0.004
PER1 2024	3/4/2024 16:40	3/4/2024 16:50	0.150	0.042	5	0.004
PER1 2024	3/4/2024 16:50	3/4/2024 17:00	0.150	0.042	5	0.004

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/4/2024 7:30	3/4/2024 7:40	0.150	0	5	0
PER2 2024	3/4/2024 7:40	3/4/2024 7:50	0.150	0.001	5	0
PER2 2024	3/4/2024 7:50	3/4/2024 8:00	0.150	0.001	5	0
PER2 2024	3/4/2024 8:00	3/4/2024 8:10	0.150	0.002	5	0
PER2 2024	3/4/2024 8:10	3/4/2024 8:20	0.150	0.003	5	0
PER2 2024	3/4/2024 8:20	3/4/2024 8:30	0.150	0.003	5	0
PER2 2024	3/4/2024 8:30	3/4/2024 8:40	0.150	0.004	5	0
PER2 2024	3/4/2024 8:40	3/4/2024 8:50	0.150	0.004	5	0
PER2 2024	3/4/2024 8:50	3/4/2024 9:00	0.150	0.005	5	0
PER2 2024	3/4/2024 9:00	3/4/2024 9:10	0.150	0.006	5	0
PER2 2024	3/4/2024 9:10	3/4/2024 9:20	0.150	0.006	5	0
PER2 2024	3/4/2024 9:20	3/4/2024 9:30	0.150	0.007	5	0
PER2 2024	3/4/2024 9:30	3/4/2024 9:40	0.150	0.008	5	0
PER2 2024	3/4/2024 9:40	3/4/2024 9:50	0.150	0.008	5	0
PER2 2024	3/4/2024 9:50	3/4/2024 10:00	0.150	0.009	5	0
PER2 2024	3/4/2024 10:00	3/4/2024 10:10	0.150	0.01	5	0
PER2 2024	3/4/2024 10:10	3/4/2024 10:20	0.150	0.01	5	0
PER2 2024	3/4/2024 10:20	3/4/2024 10:30	0.150	0.011	5	0
PER2 2024	3/4/2024 10:30	3/4/2024 10:40	0.150	0.012	5	0
PER2 2024	3/4/2024 10:40	3/4/2024 10:50	0.150	0.013	5	0
PER2 2024	3/4/2024 10:50	3/4/2024 11:00	0.150	0.013	5	0
PER2 2024	3/4/2024 11:00	3/4/2024 11:10	0.150	0.014	5	0
PER2 2024	3/4/2024 11:10	3/4/2024 11:20	0.150	0.015	5	0
PER2 2024	3/4/2024 11:20	3/4/2024 11:30	0.150	0.015	5	0
PER2 2024	3/4/2024 11:30	3/4/2024 11:40	0.150	0.016	5	0
PER2 2024	3/4/2024 11:40	3/4/2024 11:50	0.150	0.017	5	0
PER2 2024	3/4/2024 11:50	3/4/2024 12:00	0.150	0.018	5	0
PER2 2024	3/4/2024 12:00	3/4/2024 12:10	0.150	0.019	5	0
PER2 2024	3/4/2024 12:10	3/4/2024 12:20	0.150	0.019	5	0
PER2 2024	3/4/2024 12:20	3/4/2024 12:30	0.150	0.02	5	0
PER2 2024	3/4/2024 12:30	3/4/2024 12:40	0.150	0.02	5	0
PER2 2024	3/4/2024 12:40	3/4/2024 12:50	0.150	0.021	5	0
PER2 2024	3/4/2024 12:50	3/4/2024 13:00	0.150	0.021	5	0
PER2 2024	3/4/2024 13:00	3/4/2024 13:10	0.150	0.022	5	0
PER2 2024	3/4/2024 13:10	3/4/2024 13:20	0.150	0.022	5	0
PER2 2024	3/4/2024 13:20	3/4/2024 13:30	0.150	0.023	5	0
PER2 2024	3/4/2024 13:30	3/4/2024 13:40	0.150	0.023	5	0
PER2 2024	3/4/2024 13:40	3/4/2024 13:50	0.150	0.023	5	0
PER2 2024	3/4/2024 13:50	3/4/2024 14:00	0.150	0.024	5	0
PER2 2024	3/4/2024 14:00	3/4/2024 14:10	0.150	0.024	5	0
PER2 2024	3/4/2024 14:10	3/4/2024 14:20	0.150	0.025	5	0
PER2 2024	3/4/2024 14:20	3/4/2024 14:30	0.150	0.025	5	0
PER2 2024	3/4/2024 14:30	3/4/2024 14:40	0.150	0.026	5	0
PER2 2024	3/4/2024 14:40	3/4/2024 14:50	0.150	0.026	5	0
PER2 2024	3/4/2024 14:50	3/4/2024 15:00	0.150	0.026	5	0
PER2 2024	3/4/2024 15:00	3/4/2024 15:10	0.150	0.027	5	0.001
PER2 2024	3/4/2024 15:10	3/4/2024 15:20	0.150	0.027	5	0.001
PER2 2024	3/4/2024 15:20	3/4/2024 15:30	0.150	0.028	5	0.001
PER2 2024	3/4/2024 15:30	3/4/2024 15:40	0.150	0.028	5	0.001
PER2 2024	3/4/2024 15:40	3/4/2024 15:50	0.150	0.028	5	0.001
PER2 2024	3/4/2024 15:50	3/4/2024 16:00	0.150	0.028	5	0.001
PER2 2024	3/4/2024 16:00	3/4/2024 16:10	0.150	0.028	5	0.001
PER2 2024	3/4/2024 16:10	3/4/2024 16:20	0.150	0.028	5	0.001
PER2 2024	3/4/2024 16:20	3/4/2024 16:30	0.150	0.028	5	0.001
PER2 2024	3/4/2024 16:30	3/4/2024 16:40	0.150	0.028	5	0.001
PER2 2024	3/4/2024 16:40	3/4/2024 16:50	0.150	0.028	5	0.001
PER2 2024	3/4/2024 16:50	3/4/2024 17:00	0.150	0.028	5	0.001

Daily Status Report	
Prepared by: C. Zaccheo	Date: 3/5/2024 Weather: 50 deg. F, Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA

Work Activities Performed: 1) Alba completed minor site maintenance and minor soil excavation. On-site work was limited due to the rain.
--

Is the dewatering system operating: YES NO

Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP stations were not set up due to heavy rain.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.
--

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3765	0	6965	1520	2120

Site Layout Map and Excavation Figures

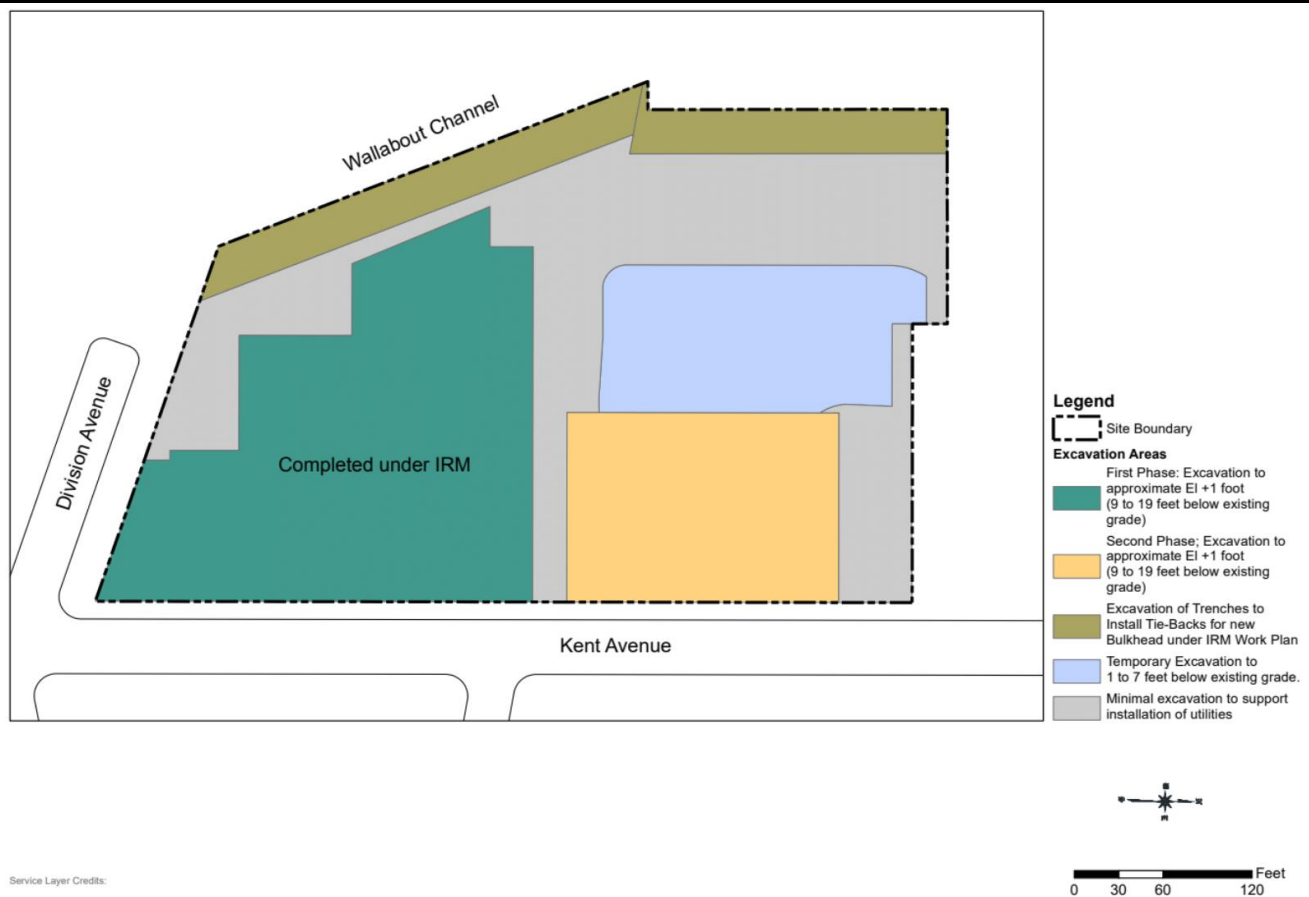

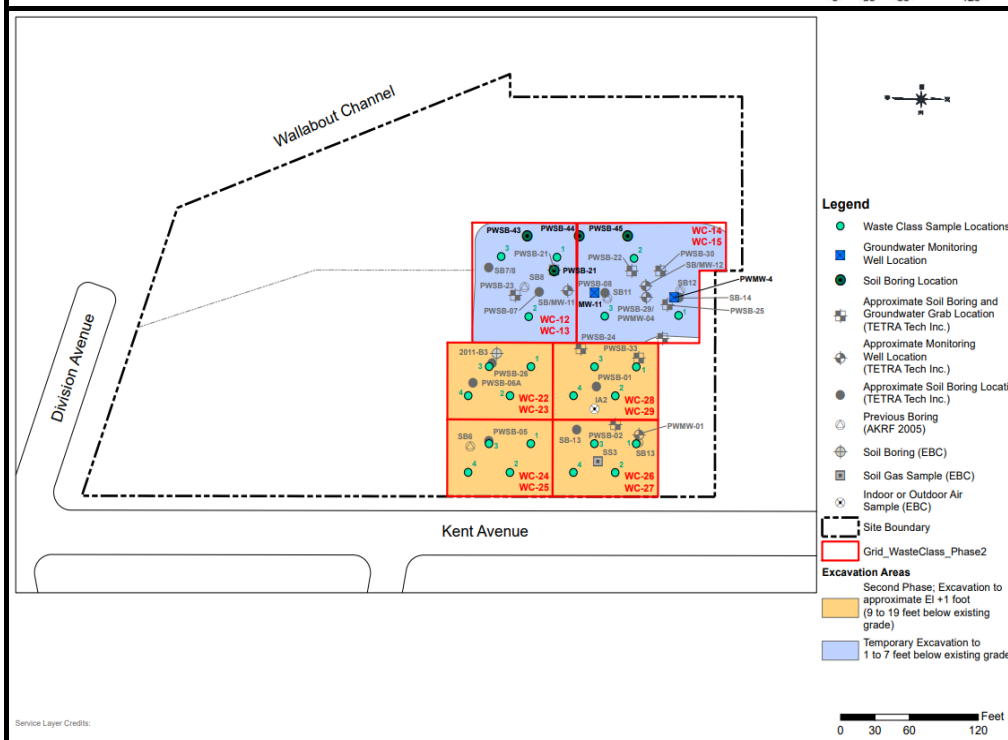
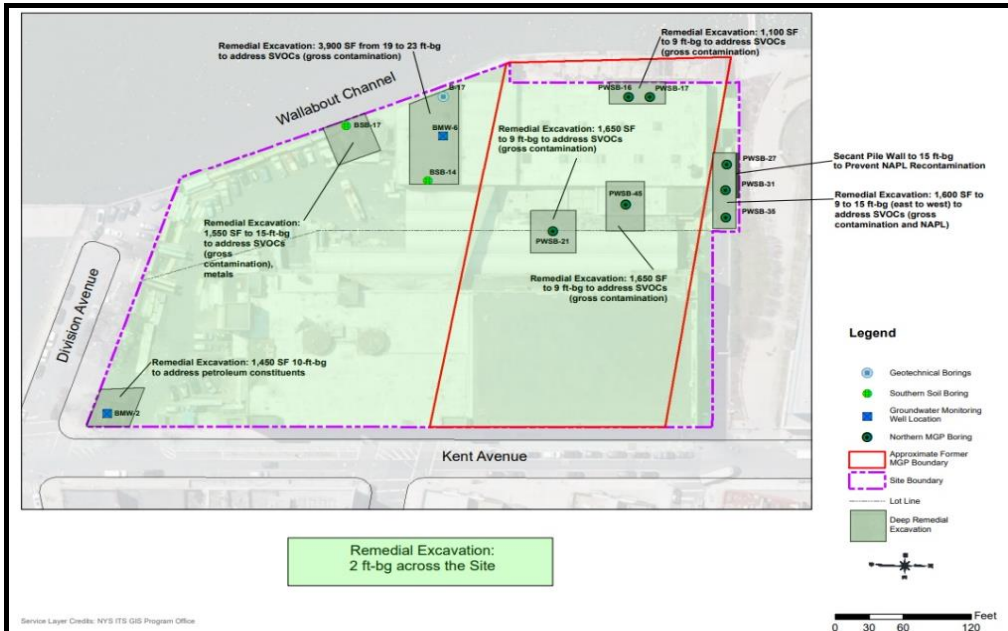


Photo 1:
View of Site conditions
facing south.



Photo 2:
Site conditions facing
southeast.

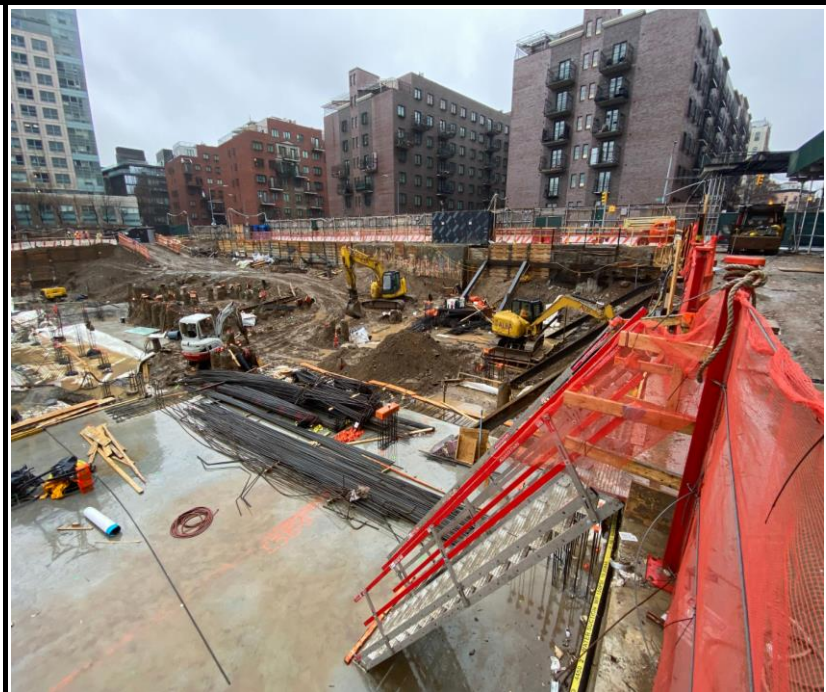


Photo 3:
View of Site
conditions facing
southwest.

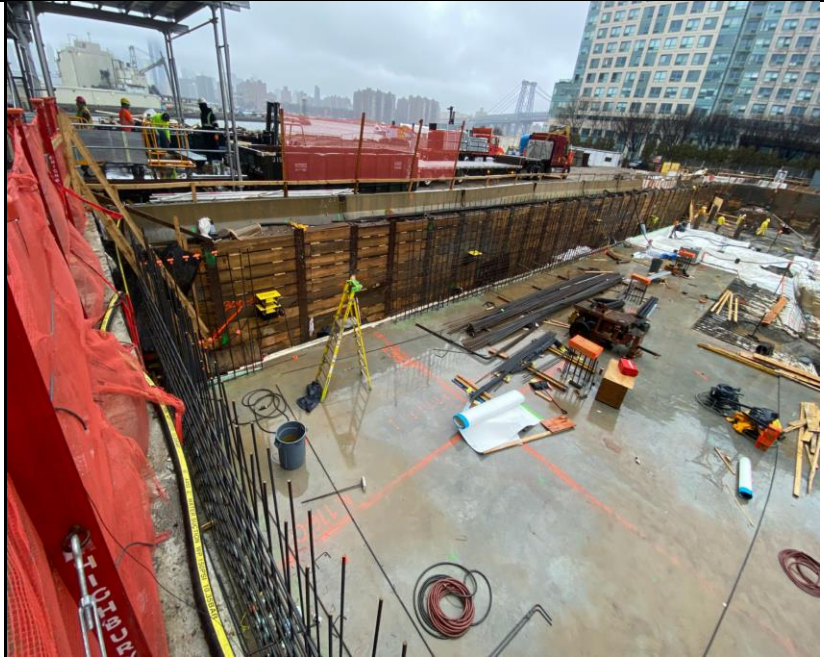


Photo 4:
View of Site
conditions facing
south.



CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/6/2024

Weather: 50 deg. F, Overcast/Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues SOE installation, soil excavation, foundation development, waterproofing installation and rebar installation.
- 2) Alba completed additional excavation and additional endpoint samples in the EP-86 sample location were collected.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): EP-86_20240306_N, EP-86_20240306_S, EP-86_20240306_E, EP-86_20240306_W and EP-86_20240306_C.

Air Monitoring (Since Last Report): CAMP tables and graphs are included below. CAMP stations were employed only between 930AM to 12PM due to heavy rain.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3765	0	6965	1520	2120

Site Layout Map and Excavation Figures

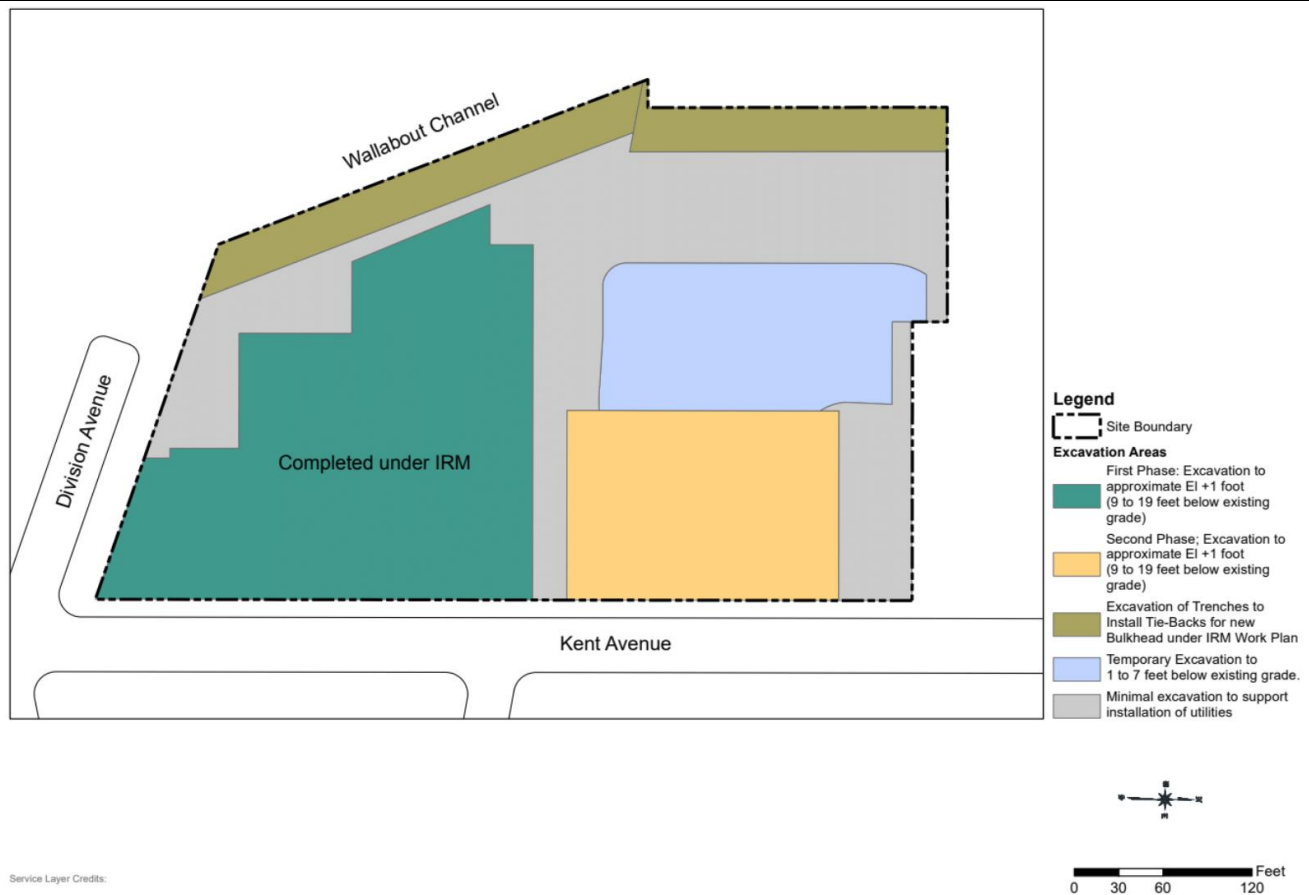

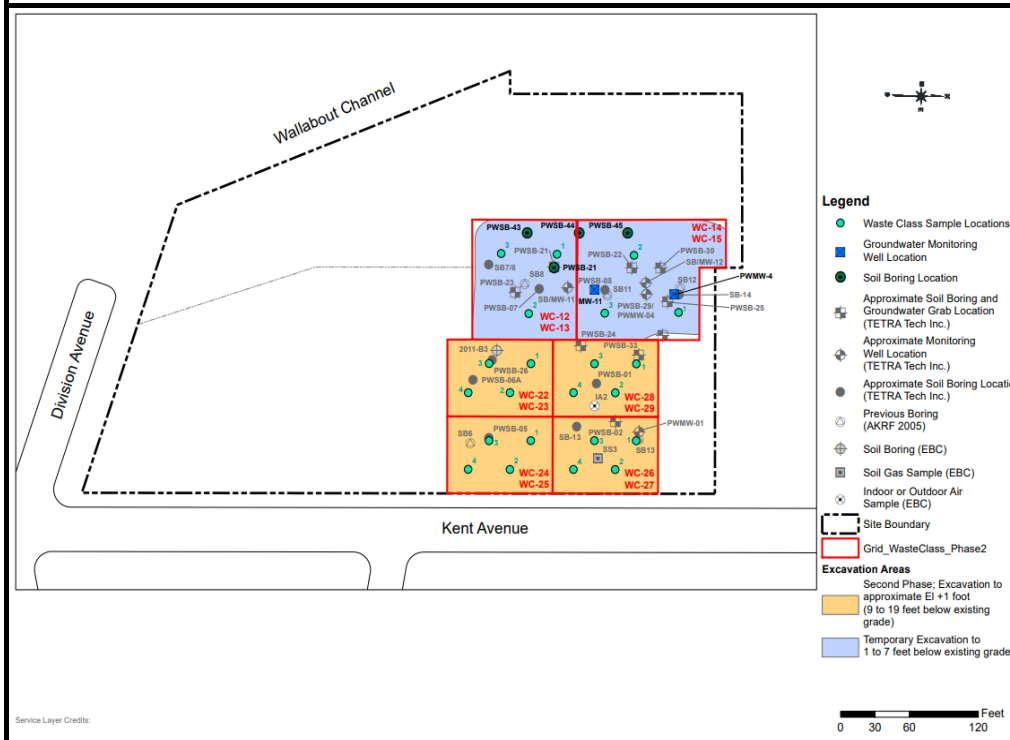
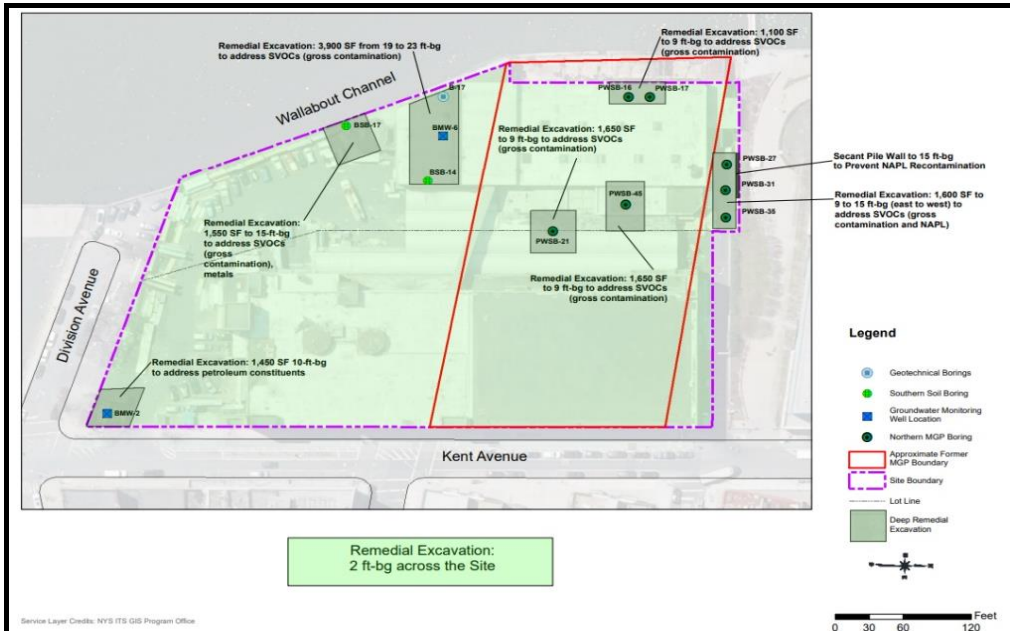


Photo 1:
View of Site conditions
and activities facing
northeast.



Photo 2:
Site conditions and SOE
installation and welding
facing east.



Photo 3:
View of Site
conditions, staged
rebar and soil
excavation facing
south.


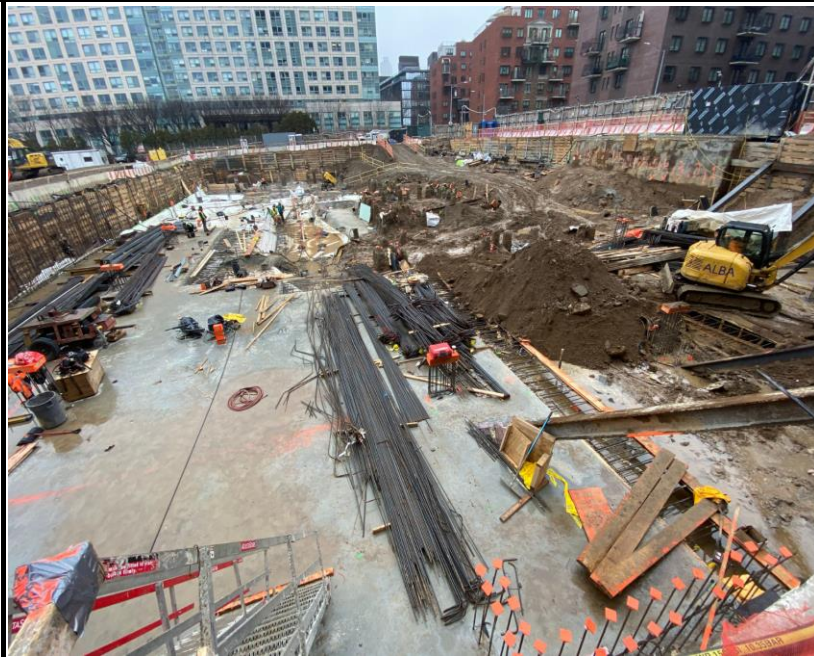



Photo 4:
View of Site
conditions and soil
excavation facing
northeast.

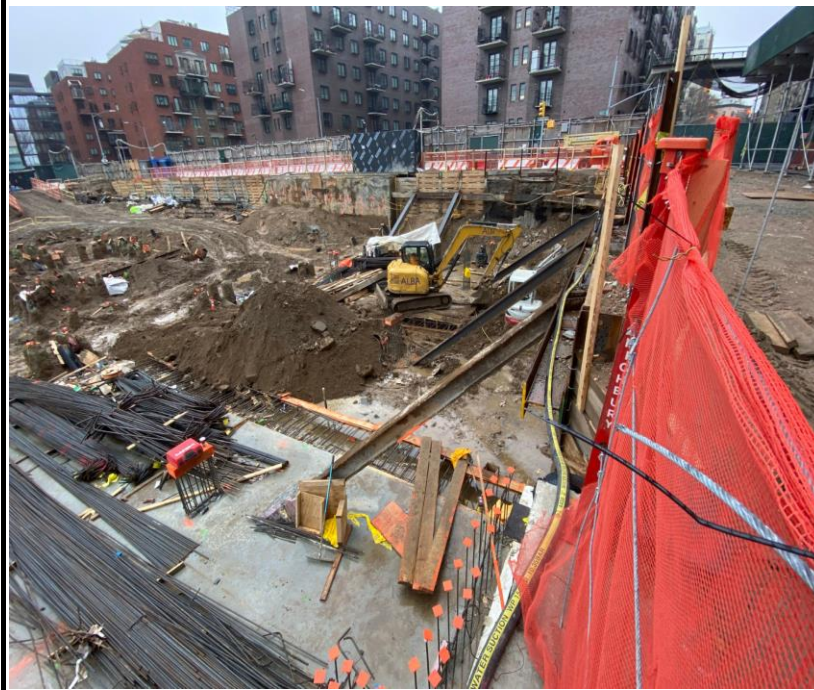

CAMP:
Downwind
Particulates

Dust Levels


0.06 mg/m³ 0.023 mg/m³

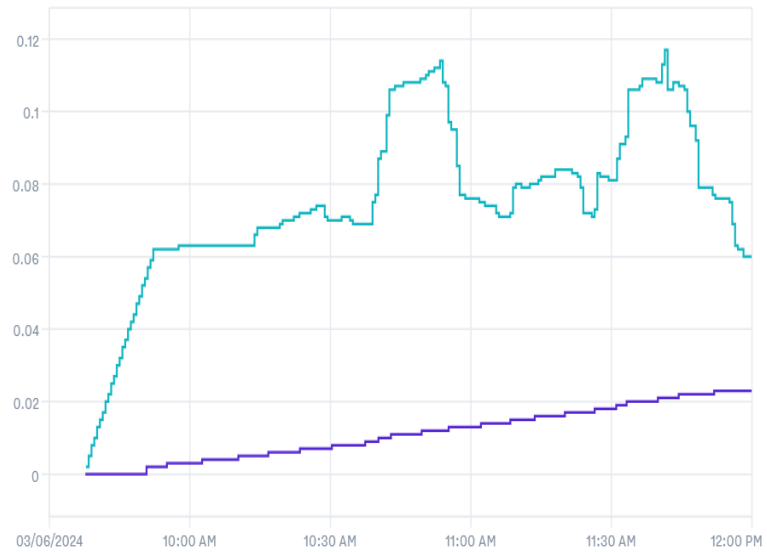


CAMP:
Downwind VOCs

VOC Levels


0.134 ppm 0.045 ppm

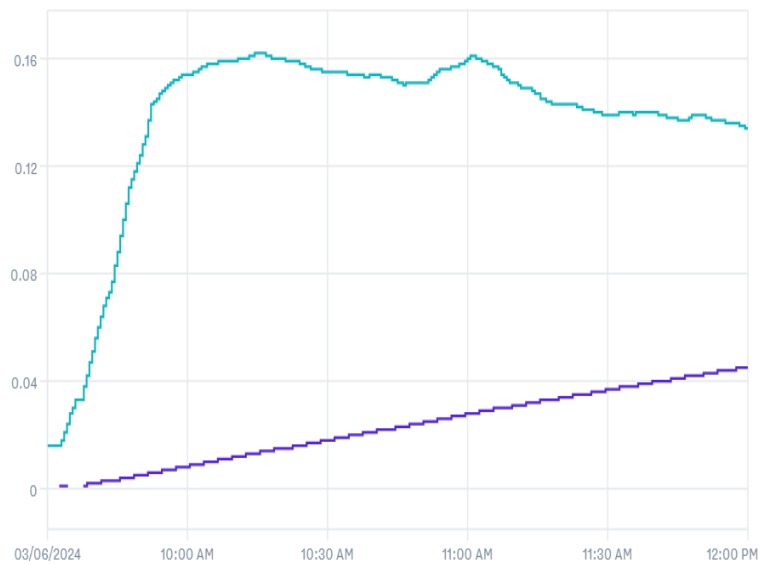

CAMP:
Upwind Particulates

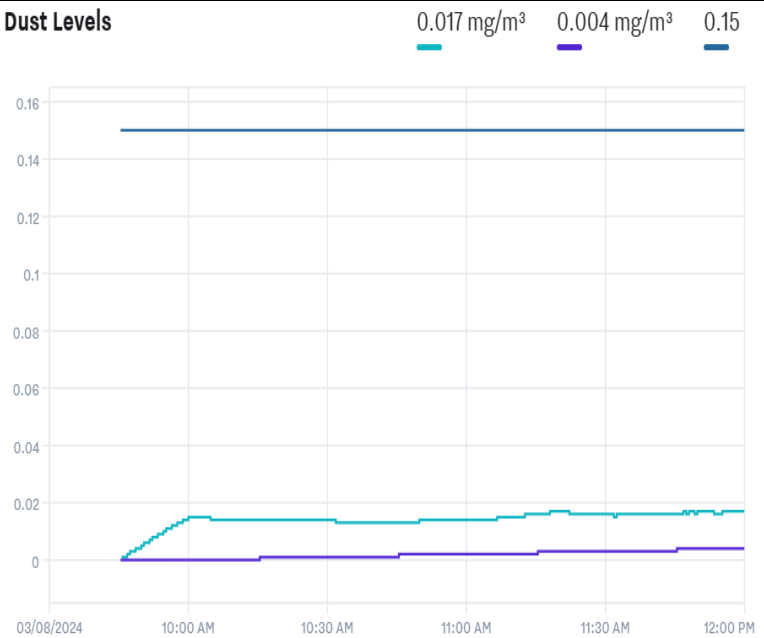

CAMP:
Upwind VOCs

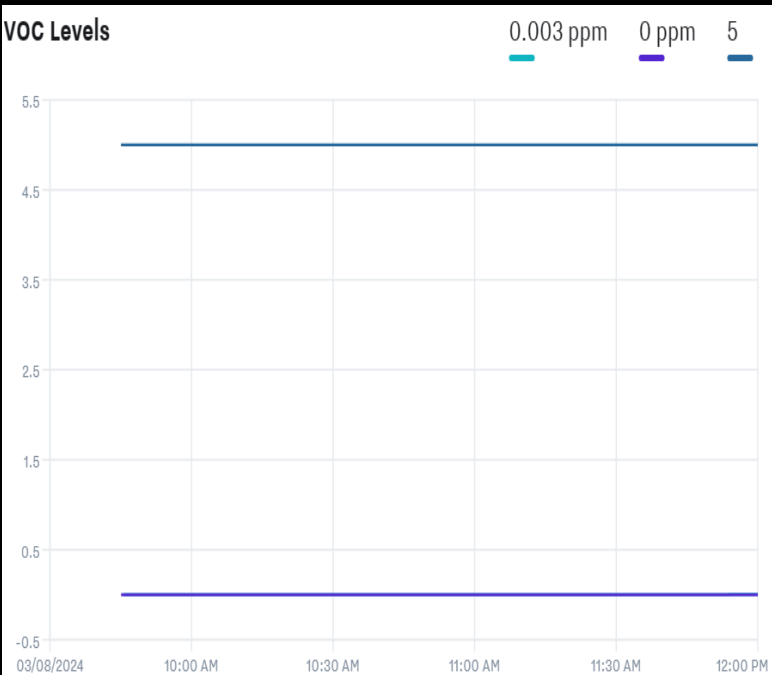

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/6/2024 9:30	3/6/2024 9:40	0.150	0	5	0.002
DW 2024	3/6/2024 9:40	3/6/2024 9:50	0.150	0	5	0.005
DW 2024	3/6/2024 9:50	3/6/2024 10:00	0.150	0.003	5	0.008
DW 2024	3/6/2024 10:00	3/6/2024 10:10	0.150	0.004	5	0.012
DW 2024	3/6/2024 10:10	3/6/2024 10:20	0.150	0.006	5	0.015
DW 2024	3/6/2024 10:20	3/6/2024 10:30	0.150	0.007	5	0.018
DW 2024	3/6/2024 10:30	3/6/2024 10:40	0.150	0.009	5	0.021
DW 2024	3/6/2024 10:40	3/6/2024 10:50	0.150	0.012	5	0.024
DW 2024	3/6/2024 10:50	3/6/2024 11:00	0.150	0.013	5	0.028
DW 2024	3/6/2024 11:00	3/6/2024 11:10	0.150	0.015	5	0.031
DW 2024	3/6/2024 11:10	3/6/2024 11:20	0.150	0.016	5	0.034
DW 2024	3/6/2024 11:20	3/6/2024 11:30	0.150	0.018	5	0.037
DW 2024	3/6/2024 11:30	3/6/2024 11:40	0.150	0.021	5	0.04
DW 2024	3/6/2024 11:40	3/6/2024 11:50	0.150	0.022	5	0.042
DW 2024	3/6/2024 11:50	3/6/2024 12:00	0.150	0.023	5	0.045

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/6/2024 9:30	3/6/2024 9:40	0.150	0.004	5	0
UW 2024	3/6/2024 9:40	3/6/2024 9:50	0.150	0.004	5	0
UW 2024	3/6/2024 9:50	3/6/2024 10:00	0.150	0.005	5	0
UW 2024	3/6/2024 10:00	3/6/2024 10:10	0.150	0.007	5	0
UW 2024	3/6/2024 10:10	3/6/2024 10:20	0.150	0.007	5	0
UW 2024	3/6/2024 10:20	3/6/2024 10:30	0.150	0.009	5	0
UW 2024	3/6/2024 10:30	3/6/2024 10:40	0.150	0.011	5	0
UW 2024	3/6/2024 10:40	3/6/2024 10:50	0.150	0.011	5	0
UW 2024	3/6/2024 10:50	3/6/2024 11:00	0.150	0.013	5	0
UW 2024	3/6/2024 11:00	3/6/2024 11:10	0.150	0.015	5	0
UW 2024	3/6/2024 11:10	3/6/2024 11:20	0.150	0.015	5	0
UW 2024	3/6/2024 11:20	3/6/2024 11:30	0.150	0.017	5	0.001
UW 2024	3/6/2024 11:30	3/6/2024 11:40	0.150	0.018	5	0.001
UW 2024	3/6/2024 11:40	3/6/2024 11:50	0.150	0.018	5	0.001
UW 2024	3/6/2024 11:50	3/6/2024 12:00	0.150	0.02	5	0.001

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/6/2024 9:30	3/6/2024 9:40	0.150	0.003	5	0
HS South	3/6/2024 9:40	3/6/2024 9:50	0.150	0.005	5	0
HS South	3/6/2024 9:50	3/6/2024 10:00	0.150	0.007	5	0
HS South	3/6/2024 10:00	3/6/2024 10:10	0.150	0.008	5	0
HS South	3/6/2024 10:10	3/6/2024 10:20	0.150	0.009	5	0
HS South	3/6/2024 10:20	3/6/2024 10:30	0.150	0.011	5	0
HS South	3/6/2024 10:30	3/6/2024 10:40	0.150	0.012	5	0
HS South	3/6/2024 10:40	3/6/2024 10:50	0.150	0.014	5	0
HS South	3/6/2024 10:50	3/6/2024 11:00	0.150	0.015	5	0
HS South	3/6/2024 11:00	3/6/2024 11:10	0.150	0.017	5	0
HS South	3/6/2024 11:10	3/6/2024 11:20	0.150	0.018	5	0
HS South	3/6/2024 11:20	3/6/2024 11:30	0.150	0.019	5	0
HS South	3/6/2024 11:30	3/6/2024 11:40	0.150	0.02	5	0
HS South	3/6/2024 11:40	3/6/2024 11:50	0.150	0.022	5	0
HS South	3/6/2024 11:50	3/6/2024 12:00	0.150	0.023	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/6/2024 9:30	3/6/2024 9:40	0.150	0	5	0
PER1 2024	3/6/2024 9:40	3/6/2024 9:50	0.150	0.004	5	0
PER1 2024	3/6/2024 9:50	3/6/2024 10:00	0.150	0.006	5	0
PER1 2024	3/6/2024 10:00	3/6/2024 10:10	0.150	0.007	5	0
PER1 2024	3/6/2024 10:10	3/6/2024 10:20	0.150	0.009	5	0
PER1 2024	3/6/2024 10:20	3/6/2024 10:30	0.150	0.01	5	0
PER1 2024	3/6/2024 10:30	3/6/2024 10:40	0.150	0.012	5	0
PER1 2024	3/6/2024 10:40	3/6/2024 10:50	0.150	0.014	5	0
PER1 2024	3/6/2024 10:50	3/6/2024 11:00	0.150	0.015	5	0
PER1 2024	3/6/2024 11:00	3/6/2024 11:10	0.150	0.017	5	0
PER1 2024	3/6/2024 11:10	3/6/2024 11:20	0.150	0.019	5	0
PER1 2024	3/6/2024 11:20	3/6/2024 11:30	0.150	0.02	5	0
PER1 2024	3/6/2024 11:30	3/6/2024 11:40	0.150	0.022	5	0
PER1 2024	3/6/2024 11:40	3/6/2024 11:50	0.150	0.023	5	0
PER1 2024	3/6/2024 11:50	3/6/2024 12:00	0.150	0.025	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/6/2024 9:30	3/6/2024 9:40	0.150	0.003	5	0
PER2 2024	3/6/2024 9:40	3/6/2024 9:50	0.150	0.005	5	0
PER2 2024	3/6/2024 9:50	3/6/2024 10:00	0.150	0.006	5	0
PER2 2024	3/6/2024 10:00	3/6/2024 10:10	0.150	0.008	5	0
PER2 2024	3/6/2024 10:10	3/6/2024 10:20	0.150	0.009	5	0
PER2 2024	3/6/2024 10:20	3/6/2024 10:30	0.150	0.011	5	0
PER2 2024	3/6/2024 10:30	3/6/2024 10:40	0.150	0.012	5	0
PER2 2024	3/6/2024 10:40	3/6/2024 10:50	0.150	0.014	5	0
PER2 2024	3/6/2024 10:50	3/6/2024 11:00	0.150	0.015	5	0
PER2 2024	3/6/2024 11:00	3/6/2024 11:10	0.150	0.017	5	0
PER2 2024	3/6/2024 11:10	3/6/2024 11:20	0.150	0.018	5	0
PER2 2024	3/6/2024 11:20	3/6/2024 11:30	0.150	0.02	5	0
PER2 2024	3/6/2024 11:30	3/6/2024 11:40	0.150	0.021	5	0
PER2 2024	3/6/2024 11:40	3/6/2024 11:50	0.150	0.022	5	0
PER2 2024	3/6/2024 11:50	3/6/2024 12:00	0.150	0.024	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/7/2024

Weather: 50 deg. F, Rain/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation.

Is the dewatering system operating: YES NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP tables and graphs are included below. CAMP stations were turned on around 9AM due to rain.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3765	0	6965	1520	2120

Site Layout Map and Excavation Figures

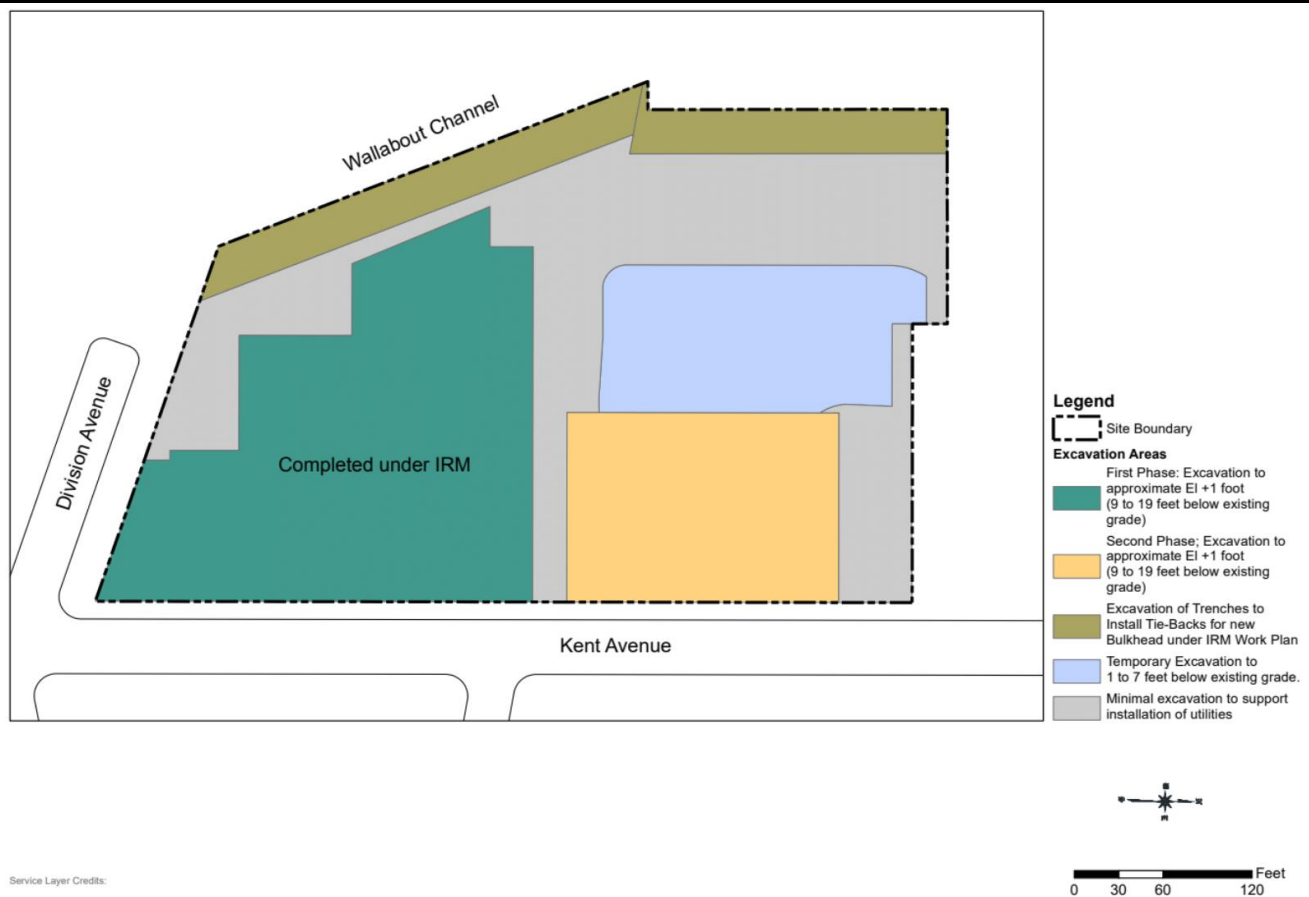

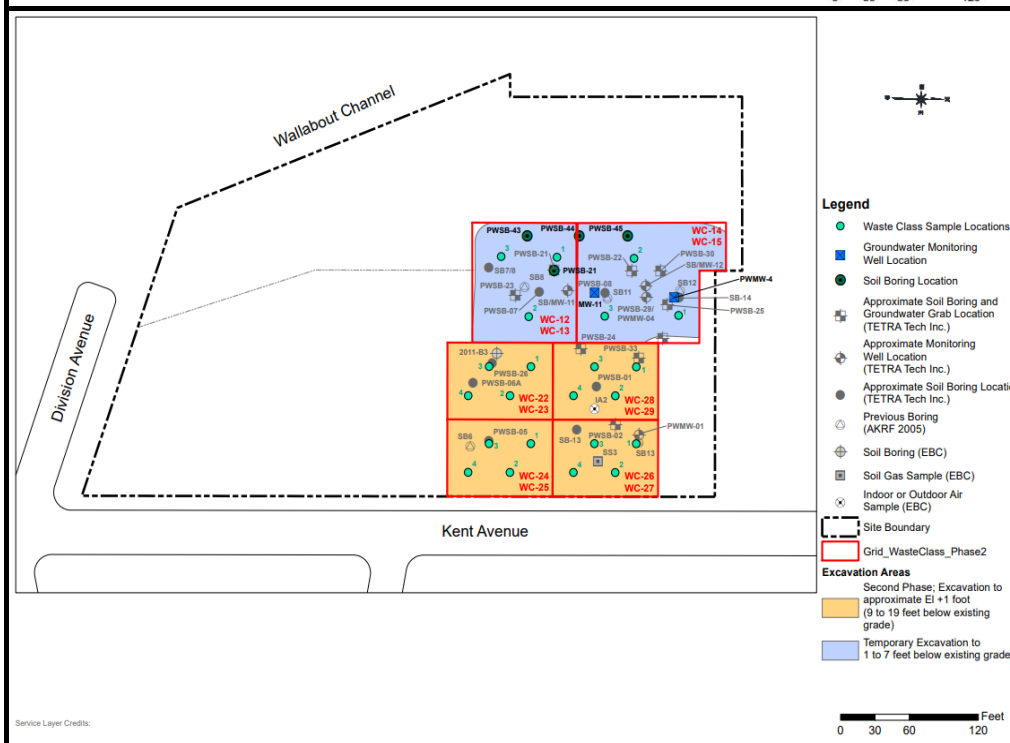
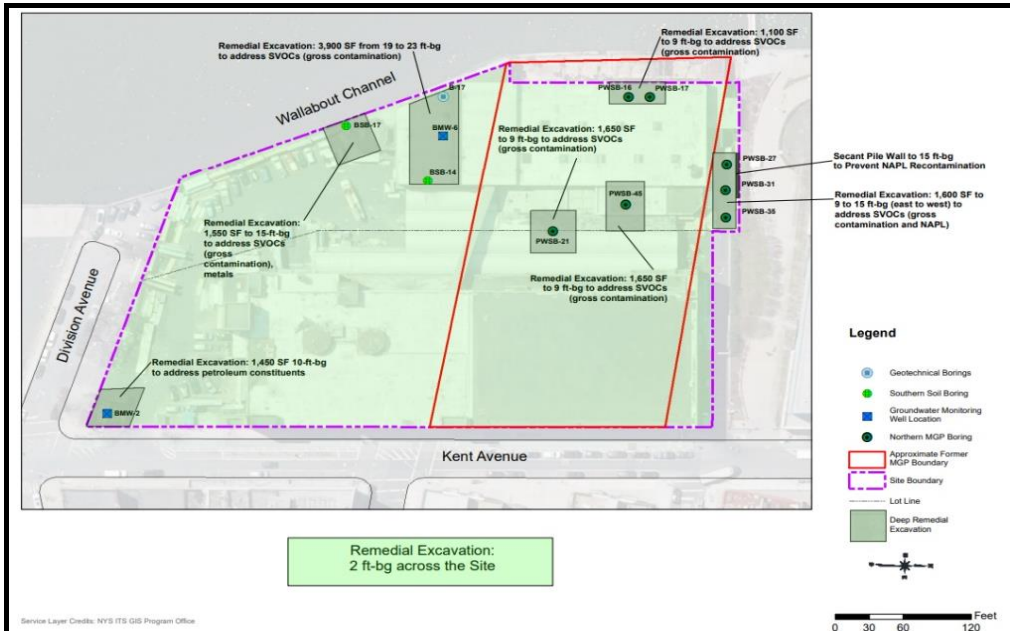


Photo 1:
View of Site conditions
and activities facing
northwest.




Photo 2:
Site conditions and SOE
installation facing
southwest.



Photo 3:
View of Site
conditions and
waterproofing and
rebar installation
facing southwest.




Photo 4:
View of Site
conditions and
waterproofing and
rebar installation
facing northwest.

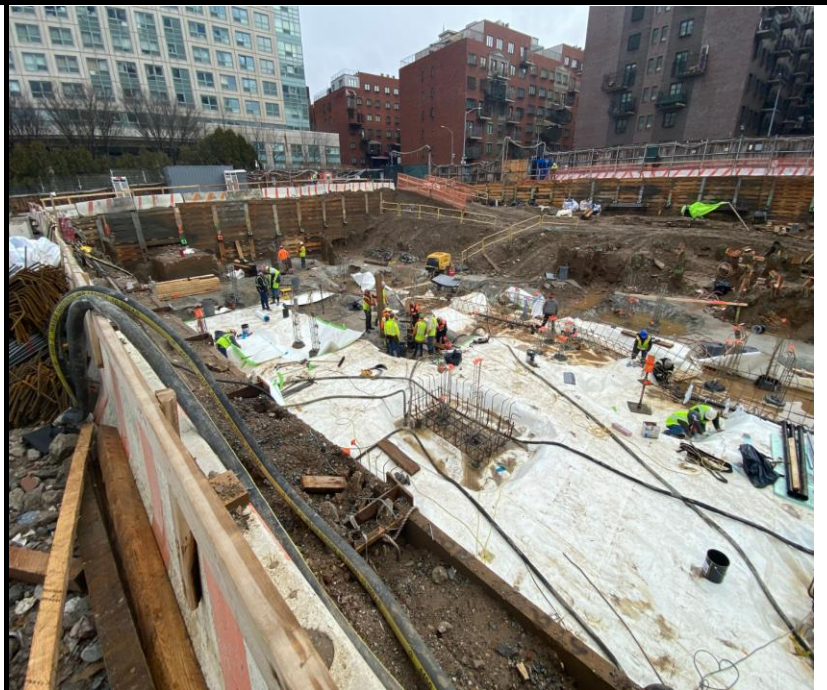

CAMP:
Downwind
Particulates

Dust Levels


0.013 mg/m³ 0.011 mg/m³

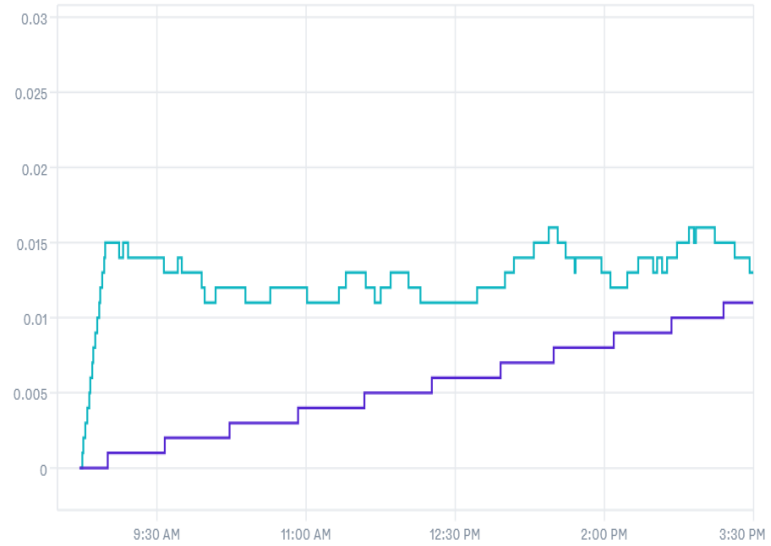

CAMP:
Downwind VOCs

VOC Levels


0.124 ppm 0.095 ppm

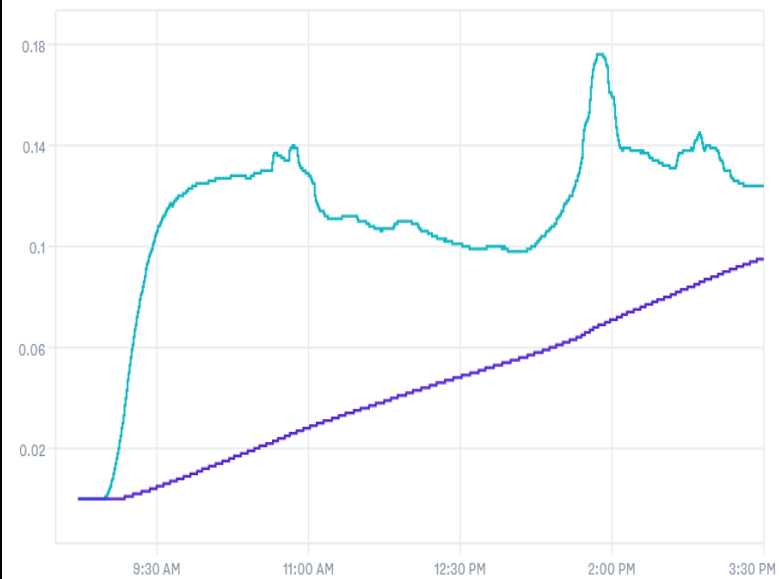

CAMP:
Upwind Particulates

Dust Levels


0.013 mg/m³ 0.011 mg/m³ 0.15

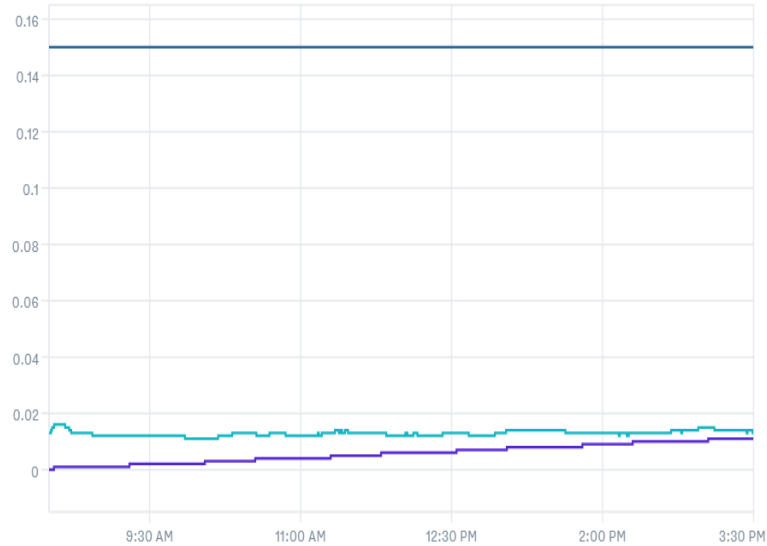

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

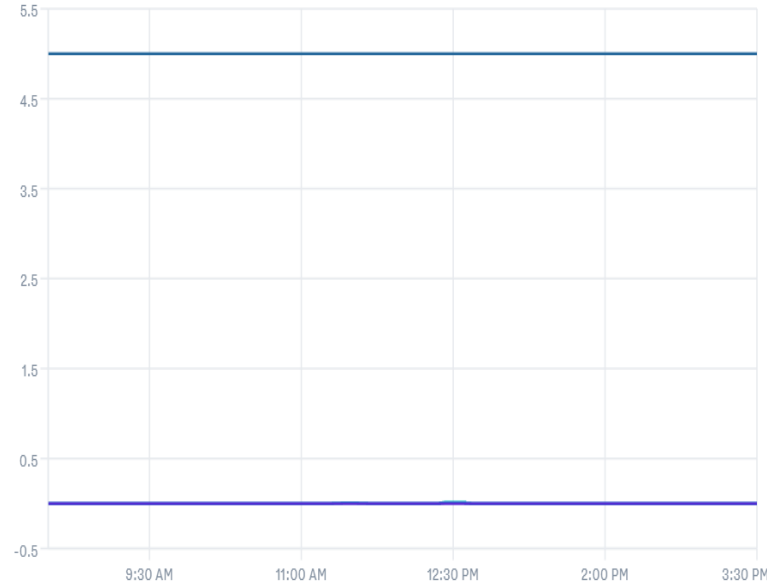

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/7/2024 9:00	3/7/2024 9:10	0.150	0.001	5	0
DW 2024	3/7/2024 9:10	3/7/2024 9:20	0.150	0.001	5	0.002
DW 2024	3/7/2024 9:20	3/7/2024 9:30	0.150	0.001	5	0.005
DW 2024	3/7/2024 9:30	3/7/2024 9:40	0.150	0.002	5	0.007
DW 2024	3/7/2024 9:40	3/7/2024 9:50	0.150	0.002	5	0.01
DW 2024	3/7/2024 9:50	3/7/2024 10:00	0.150	0.002	5	0.012
DW 2024	3/7/2024 10:00	3/7/2024 10:10	0.150	0.002	5	0.015
DW 2024	3/7/2024 10:10	3/7/2024 10:20	0.150	0.003	5	0.018
DW 2024	3/7/2024 10:20	3/7/2024 10:30	0.150	0.003	5	0.02
DW 2024	3/7/2024 10:30	3/7/2024 10:40	0.150	0.003	5	0.023
DW 2024	3/7/2024 10:40	3/7/2024 10:50	0.150	0.003	5	0.026
DW 2024	3/7/2024 10:50	3/7/2024 11:00	0.150	0.004	5	0.028
DW 2024	3/7/2024 11:00	3/7/2024 11:10	0.150	0.004	5	0.031
DW 2024	3/7/2024 11:10	3/7/2024 11:20	0.150	0.004	5	0.033
DW 2024	3/7/2024 11:20	3/7/2024 11:30	0.150	0.004	5	0.035
DW 2024	3/7/2024 11:30	3/7/2024 11:40	0.150	0.005	5	0.038
DW 2024	3/7/2024 11:40	3/7/2024 11:50	0.150	0.005	5	0.04
DW 2024	3/7/2024 11:50	3/7/2024 12:00	0.150	0.005	5	0.042
DW 2024	3/7/2024 12:00	3/7/2024 12:10	0.150	0.005	5	0.044
DW 2024	3/7/2024 12:10	3/7/2024 12:20	0.150	0.006	5	0.046
DW 2024	3/7/2024 12:20	3/7/2024 12:30	0.150	0.006	5	0.048
DW 2024	3/7/2024 12:30	3/7/2024 12:40	0.150	0.006	5	0.05
DW 2024	3/7/2024 12:40	3/7/2024 12:50	0.150	0.006	5	0.053
DW 2024	3/7/2024 12:50	3/7/2024 13:00	0.150	0.007	5	0.055
DW 2024	3/7/2024 13:00	3/7/2024 13:10	0.150	0.007	5	0.057
DW 2024	3/7/2024 13:10	3/7/2024 13:20	0.150	0.007	5	0.059
DW 2024	3/7/2024 13:20	3/7/2024 13:30	0.150	0.008	5	0.061
DW 2024	3/7/2024 13:30	3/7/2024 13:40	0.150	0.008	5	0.064
DW 2024	3/7/2024 13:40	3/7/2024 13:50	0.150	0.008	5	0.068
DW 2024	3/7/2024 13:50	3/7/2024 14:00	0.150	0.008	5	0.071
DW 2024	3/7/2024 14:00	3/7/2024 14:10	0.150	0.009	5	0.074
DW 2024	3/7/2024 14:10	3/7/2024 14:20	0.150	0.009	5	0.077
DW 2024	3/7/2024 14:20	3/7/2024 14:30	0.150	0.009	5	0.079
DW 2024	3/7/2024 14:30	3/7/2024 14:40	0.150	0.009	5	0.082
DW 2024	3/7/2024 14:40	3/7/2024 14:50	0.150	0.01	5	0.085
DW 2024	3/7/2024 14:50	3/7/2024 15:00	0.150	0.01	5	0.088
DW 2024	3/7/2024 15:00	3/7/2024 15:10	0.150	0.01	5	0.091
DW 2024	3/7/2024 15:10	3/7/2024 15:20	0.150	0.011	5	0.093
DW 2024	3/7/2024 15:20	3/7/2024 15:30	0.150	0.011	5	0.095

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/7/2024 9:00	3/7/2024 9:10	0.150	0.001	5	0
UW 2024	3/7/2024 9:10	3/7/2024 9:20	0.150	0.002	5	0
UW 2024	3/7/2024 9:20	3/7/2024 9:30	0.150	0.002	5	0
UW 2024	3/7/2024 9:30	3/7/2024 9:40	0.150	0.002	5	0
UW 2024	3/7/2024 9:40	3/7/2024 9:50	0.150	0.002	5	0
UW 2024	3/7/2024 9:50	3/7/2024 10:00	0.150	0.002	5	0
UW 2024	3/7/2024 10:00	3/7/2024 10:10	0.150	0.003	5	0
UW 2024	3/7/2024 10:10	3/7/2024 10:20	0.150	0.003	5	0
UW 2024	3/7/2024 10:20	3/7/2024 10:30	0.150	0.003	5	0
UW 2024	3/7/2024 10:30	3/7/2024 10:40	0.150	0.004	5	0
UW 2024	3/7/2024 10:40	3/7/2024 10:50	0.150	0.004	5	0
UW 2024	3/7/2024 10:50	3/7/2024 11:00	0.150	0.004	5	0
UW 2024	3/7/2024 11:00	3/7/2024 11:10	0.150	0.004	5	0
UW 2024	3/7/2024 11:10	3/7/2024 11:20	0.150	0.005	5	0
UW 2024	3/7/2024 11:20	3/7/2024 11:30	0.150	0.005	5	0
UW 2024	3/7/2024 11:30	3/7/2024 11:40	0.150	0.005	5	0
UW 2024	3/7/2024 11:40	3/7/2024 11:50	0.150	0.006	5	0
UW 2024	3/7/2024 11:50	3/7/2024 12:00	0.150	0.006	5	0
UW 2024	3/7/2024 12:00	3/7/2024 12:10	0.150	0.006	5	0
UW 2024	3/7/2024 12:10	3/7/2024 12:20	0.150	0.006	5	0
UW 2024	3/7/2024 12:20	3/7/2024 12:30	0.150	0.006	5	0
UW 2024	3/7/2024 12:30	3/7/2024 12:40	0.150	0.007	5	0
UW 2024	3/7/2024 12:40	3/7/2024 12:50	0.150	0.007	5	0
UW 2024	3/7/2024 12:50	3/7/2024 13:00	0.150	0.007	5	0
UW 2024	3/7/2024 13:00	3/7/2024 13:10	0.150	0.008	5	0
UW 2024	3/7/2024 13:10	3/7/2024 13:20	0.150	0.008	5	0
UW 2024	3/7/2024 13:20	3/7/2024 13:30	0.150	0.008	5	0
UW 2024	3/7/2024 13:30	3/7/2024 13:40	0.150	0.008	5	0
UW 2024	3/7/2024 13:40	3/7/2024 13:50	0.150	0.009	5	0
UW 2024	3/7/2024 13:50	3/7/2024 14:00	0.150	0.009	5	0
UW 2024	3/7/2024 14:00	3/7/2024 14:10	0.150	0.009	5	0
UW 2024	3/7/2024 14:10	3/7/2024 14:20	0.150	0.01	5	0
UW 2024	3/7/2024 14:20	3/7/2024 14:30	0.150	0.01	5	0
UW 2024	3/7/2024 14:30	3/7/2024 14:40	0.150	0.01	5	0
UW 2024	3/7/2024 14:40	3/7/2024 14:50	0.150	0.01	5	0
UW 2024	3/7/2024 14:50	3/7/2024 15:00	0.150	0.01	5	0
UW 2024	3/7/2024 15:00	3/7/2024 15:10	0.150	0.011	5	0
UW 2024	3/7/2024 15:10	3/7/2024 15:20	0.150	0.011	5	0
UW 2024	3/7/2024 15:20	3/7/2024 15:30	0.150	0.011	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/7/2024 9:00	3/7/2024 9:10	0.150	0	5	0
HS South	3/7/2024 9:10	3/7/2024 9:20	0.150	0	5	0
HS South	3/7/2024 9:20	3/7/2024 9:30	0.150	0	5	0
HS South	3/7/2024 9:30	3/7/2024 9:40	0.150	0.001	5	0
HS South	3/7/2024 9:40	3/7/2024 9:50	0.150	0.001	5	0
HS South	3/7/2024 9:50	3/7/2024 10:00	0.150	0.001	5	0
HS South	3/7/2024 10:00	3/7/2024 10:10	0.150	0.001	5	0
HS South	3/7/2024 10:10	3/7/2024 10:20	0.150	0.001	5	0
HS South	3/7/2024 10:20	3/7/2024 10:30	0.150	0.001	5	0
HS South	3/7/2024 10:30	3/7/2024 10:40	0.150	0.001	5	0
HS South	3/7/2024 10:40	3/7/2024 10:50	0.150	0.001	5	0
HS South	3/7/2024 10:50	3/7/2024 11:00	0.150	0.001	5	0
HS South	3/7/2024 11:00	3/7/2024 11:10	0.150	0.001	5	0
HS South	3/7/2024 11:10	3/7/2024 11:20	0.150	0.001	5	0
HS South	3/7/2024 11:20	3/7/2024 11:30	0.150	0.001	5	0
HS South	3/7/2024 11:30	3/7/2024 11:40	0.150	0.001	5	0
HS South	3/7/2024 11:40	3/7/2024 11:50	0.150	0.001	5	0
HS South	3/7/2024 11:50	3/7/2024 12:00	0.150	0.001	5	0
HS South	3/7/2024 12:00	3/7/2024 12:10	0.150	0.001	5	0
HS South	3/7/2024 12:10	3/7/2024 12:20	0.150	0.001	5	0
HS South	3/7/2024 12:20	3/7/2024 12:30	0.150	0.001	5	0
HS South	3/7/2024 12:30	3/7/2024 12:40	0.150	0.001	5	0
HS South	3/7/2024 12:40	3/7/2024 12:50	0.150	0.001	5	0
HS South	3/7/2024 12:50	3/7/2024 13:00	0.150	0.001	5	0
HS South	3/7/2024 13:00	3/7/2024 13:10	0.150	0.001	5	0
HS South	3/7/2024 13:10	3/7/2024 13:20	0.150	0.001	5	0
HS South	3/7/2024 13:20	3/7/2024 13:30	0.150	0.001	5	0
HS South	3/7/2024 13:30	3/7/2024 13:40	0.150	0.001	5	0
HS South	3/7/2024 13:40	3/7/2024 13:50	0.150	0.001	5	0
HS South	3/7/2024 13:50	3/7/2024 14:00	0.150	0.001	5	0
HS South	3/7/2024 14:00	3/7/2024 14:10	0.150	0.001	5	0
HS South	3/7/2024 14:10	3/7/2024 14:20	0.150	0.001	5	0
HS South	3/7/2024 14:20	3/7/2024 14:30	0.150	0.001	5	0
HS South	3/7/2024 14:30	3/7/2024 14:40	0.150	0.001	5	0
HS South	3/7/2024 14:40	3/7/2024 14:50	0.150	0.001	5	0
HS South	3/7/2024 14:50	3/7/2024 15:00	0.150	0.001	5	0
HS South	3/7/2024 15:00	3/7/2024 15:10	0.150	0.001	5	0
HS South	3/7/2024 15:10	3/7/2024 15:20	0.150	0.001	5	0
HS South	3/7/2024 15:20	3/7/2024 15:30	0.150	0.001	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/7/2024 9:00	3/7/2024 9:10	0.150	0.002	5	0
PER1 2024	3/7/2024 9:10	3/7/2024 9:20	0.150	0.002	5	0
PER1 2024	3/7/2024 9:20	3/7/2024 9:30	0.150	0.003	5	0
PER1 2024	3/7/2024 9:30	3/7/2024 9:40	0.150	0.004	5	0
PER1 2024	3/7/2024 9:40	3/7/2024 9:50	0.150	0.004	5	0
PER1 2024	3/7/2024 9:50	3/7/2024 10:00	0.150	0.005	5	0
PER1 2024	3/7/2024 10:00	3/7/2024 10:10	0.150	0.006	5	0
PER1 2024	3/7/2024 10:10	3/7/2024 10:20	0.150	0.006	5	0
PER1 2024	3/7/2024 10:20	3/7/2024 10:30	0.150	0.007	5	0
PER1 2024	3/7/2024 10:30	3/7/2024 10:40	0.150	0.007	5	0
PER1 2024	3/7/2024 10:40	3/7/2024 10:50	0.150	0.008	5	0
PER1 2024	3/7/2024 10:50	3/7/2024 11:00	0.150	0.009	5	0
PER1 2024	3/7/2024 11:00	3/7/2024 11:10	0.150	0.01	5	0
PER1 2024	3/7/2024 11:10	3/7/2024 11:20	0.150	0.01	5	0
PER1 2024	3/7/2024 11:20	3/7/2024 11:30	0.150	0.012	5	0
PER1 2024	3/7/2024 11:30	3/7/2024 11:40	0.150	0.013	5	0
PER1 2024	3/7/2024 11:40	3/7/2024 11:50	0.150	0.014	5	0
PER1 2024	3/7/2024 11:50	3/7/2024 12:00	0.150	0.014	5	0
PER1 2024	3/7/2024 12:00	3/7/2024 12:10	0.150	0.015	5	0
PER1 2024	3/7/2024 12:10	3/7/2024 12:20	0.150	0.015	5	0
PER1 2024	3/7/2024 12:20	3/7/2024 12:30	0.150	0.016	5	0
PER1 2024	3/7/2024 12:30	3/7/2024 12:40	0.150	0.016	5	0
PER1 2024	3/7/2024 12:40	3/7/2024 12:50	0.150	0.017	5	0
PER1 2024	3/7/2024 12:50	3/7/2024 13:00	0.150	0.018	5	0
PER1 2024	3/7/2024 13:00	3/7/2024 13:10	0.150	0.019	5	0
PER1 2024	3/7/2024 13:10	3/7/2024 13:20	0.150	0.02	5	0
PER1 2024	3/7/2024 13:20	3/7/2024 13:30	0.150	0.021	5	0
PER1 2024	3/7/2024 13:30	3/7/2024 13:40	0.150	0.022	5	0.01
PER1 2024	3/7/2024 13:40	3/7/2024 13:50	0.150	0.023	5	0.017
PER1 2024	3/7/2024 13:50	3/7/2024 14:00	0.150	0.024	5	0.021
PER1 2024	3/7/2024 14:00	3/7/2024 14:10	0.150	0.025	5	0.021
PER1 2024	3/7/2024 14:10	3/7/2024 14:20	0.150	0.026	5	0.022
PER1 2024	3/7/2024 14:20	3/7/2024 14:30	0.150	0.027	5	0.022
PER1 2024	3/7/2024 14:30	3/7/2024 14:40	0.150	0.028	5	0.022
PER1 2024	3/7/2024 14:40	3/7/2024 14:50	0.150	0.029	5	0.024
PER1 2024	3/7/2024 14:50	3/7/2024 15:00	0.150	0.031	5	0.024
PER1 2024	3/7/2024 15:00	3/7/2024 15:10	0.150	0.032	5	0.024
PER1 2024	3/7/2024 15:10	3/7/2024 15:20	0.150	0.033	5	0.024
PER1 2024	3/7/2024 15:20	3/7/2024 15:30	0.150	0.033	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/7/2024 9:00	3/7/2024 9:10	0.150	0.029	5	0
PER2 2024	3/7/2024 9:10	3/7/2024 9:20	0.150	0.029	5	0
PER2 2024	3/7/2024 9:20	3/7/2024 9:30	0.150	0.029	5	0
PER2 2024	3/7/2024 9:30	3/7/2024 9:40	0.150	0.029	5	0
PER2 2024	3/7/2024 9:40	3/7/2024 9:50	0.150	0.002	5	0
PER2 2024	3/7/2024 9:50	3/7/2024 10:00	0.150	0.002	5	0
PER2 2024	3/7/2024 10:00	3/7/2024 10:10	0.150	0.003	5	0
PER2 2024	3/7/2024 10:10	3/7/2024 10:20	0.150	0.003	5	0
PER2 2024	3/7/2024 10:20	3/7/2024 10:30	0.150	0.003	5	0
PER2 2024	3/7/2024 10:30	3/7/2024 10:40	0.150	0.004	5	0
PER2 2024	3/7/2024 10:40	3/7/2024 10:50	0.150	0.004	5	0
PER2 2024	3/7/2024 10:50	3/7/2024 11:00	0.150	0.004	5	0
PER2 2024	3/7/2024 11:00	3/7/2024 11:10	0.150	0.005	5	0
PER2 2024	3/7/2024 11:10	3/7/2024 11:20	0.150	0.005	5	0
PER2 2024	3/7/2024 11:20	3/7/2024 11:30	0.150	0.005	5	0
PER2 2024	3/7/2024 11:30	3/7/2024 11:40	0.150	0.006	5	0
PER2 2024	3/7/2024 11:40	3/7/2024 11:50	0.150	0.006	5	0
PER2 2024	3/7/2024 11:50	3/7/2024 12:00	0.150	0.006	5	0
PER2 2024	3/7/2024 12:00	3/7/2024 12:10	0.150	0.007	5	0
PER2 2024	3/7/2024 12:10	3/7/2024 12:20	0.150	0.007	5	0
PER2 2024	3/7/2024 12:20	3/7/2024 12:30	0.150	0.007	5	0
PER2 2024	3/7/2024 12:30	3/7/2024 12:40	0.150	0.008	5	0
PER2 2024	3/7/2024 12:40	3/7/2024 12:50	0.150	0.008	5	0
PER2 2024	3/7/2024 12:50	3/7/2024 13:00	0.150	0.008	5	0
PER2 2024	3/7/2024 13:00	3/7/2024 13:10	0.150	0.009	5	0
PER2 2024	3/7/2024 13:10	3/7/2024 13:20	0.150	0.009	5	0
PER2 2024	3/7/2024 13:20	3/7/2024 13:30	0.150	0.01	5	0
PER2 2024	3/7/2024 13:30	3/7/2024 13:40	0.150	0.01	5	0
PER2 2024	3/7/2024 13:40	3/7/2024 13:50	0.150	0.01	5	0
PER2 2024	3/7/2024 13:50	3/7/2024 14:00	0.150	0.011	5	0
PER2 2024	3/7/2024 14:00	3/7/2024 14:10	0.150	0.011	5	0
PER2 2024	3/7/2024 14:10	3/7/2024 14:20	0.150	0.011	5	0
PER2 2024	3/7/2024 14:20	3/7/2024 14:30	0.150	0.012	5	0
PER2 2024	3/7/2024 14:30	3/7/2024 14:40	0.150	0.012	5	0
PER2 2024	3/7/2024 14:40	3/7/2024 14:50	0.150	0.013	5	0
PER2 2024	3/7/2024 14:50	3/7/2024 15:00	0.150	0.013	5	0
PER2 2024	3/7/2024 15:00	3/7/2024 15:10	0.150	0.013	5	0
PER2 2024	3/7/2024 15:10	3/7/2024 15:20	0.150	0.014	5	0
PER2 2024	3/7/2024 15:20	3/7/2024 15:30	0.150	0.014	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/8/2024

Weather: 55 deg. F, Sunny

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation.
- 2) Alba completed additional excavation and Tenen collected additional endpoint samples in the EP-86 sample location. See below.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): EP-86_20240308_C and EP-86_20240308_W

Air Monitoring (Since Last Report): CAMP tables and graphs are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3765	0	6965	1520	2120

Site Layout Map and Excavation Figures

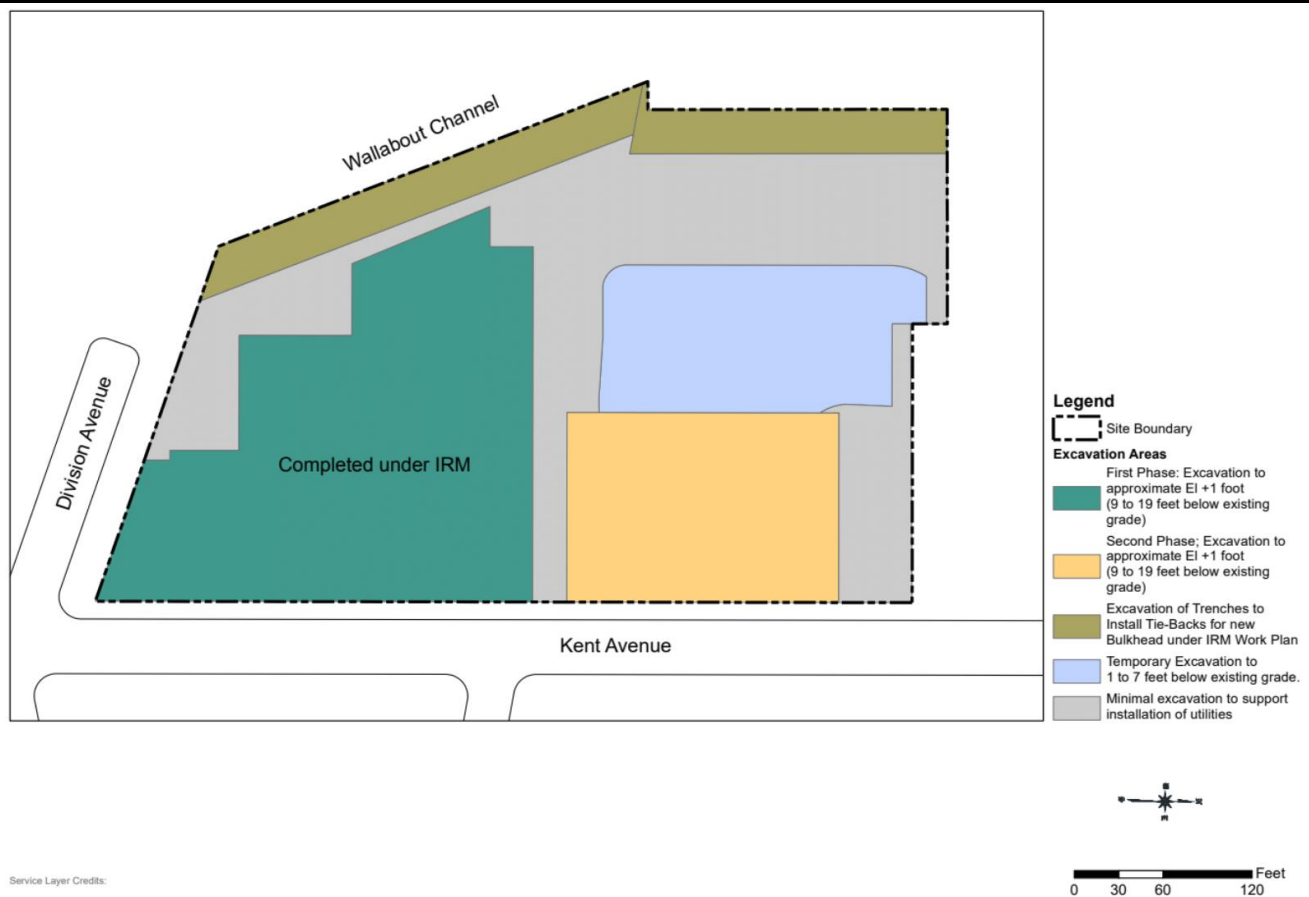

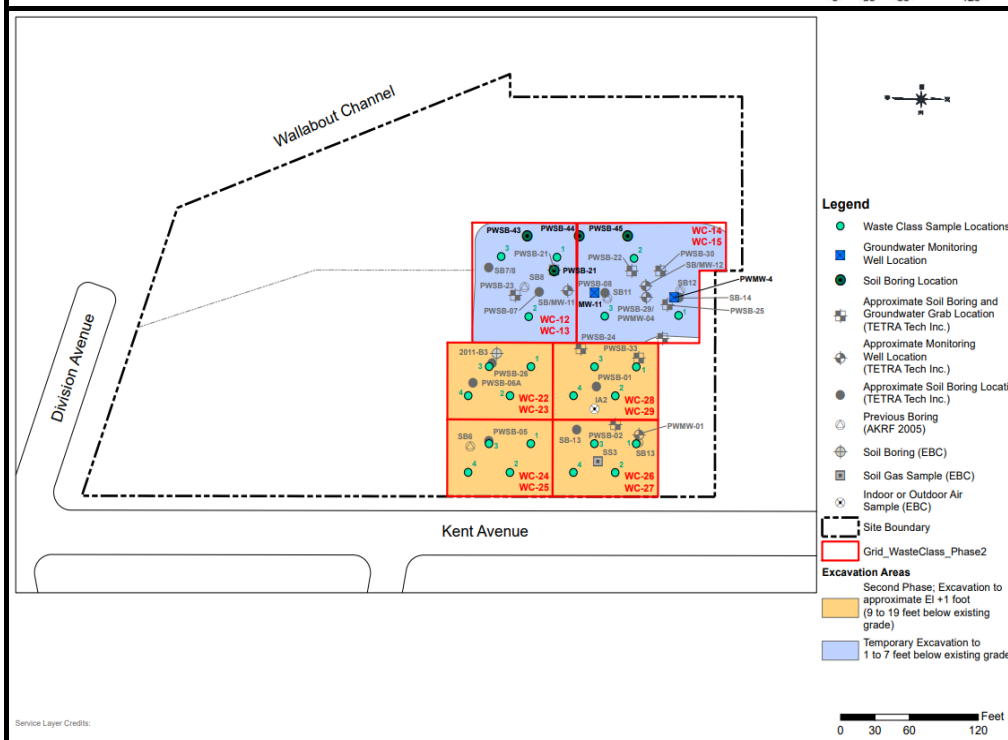
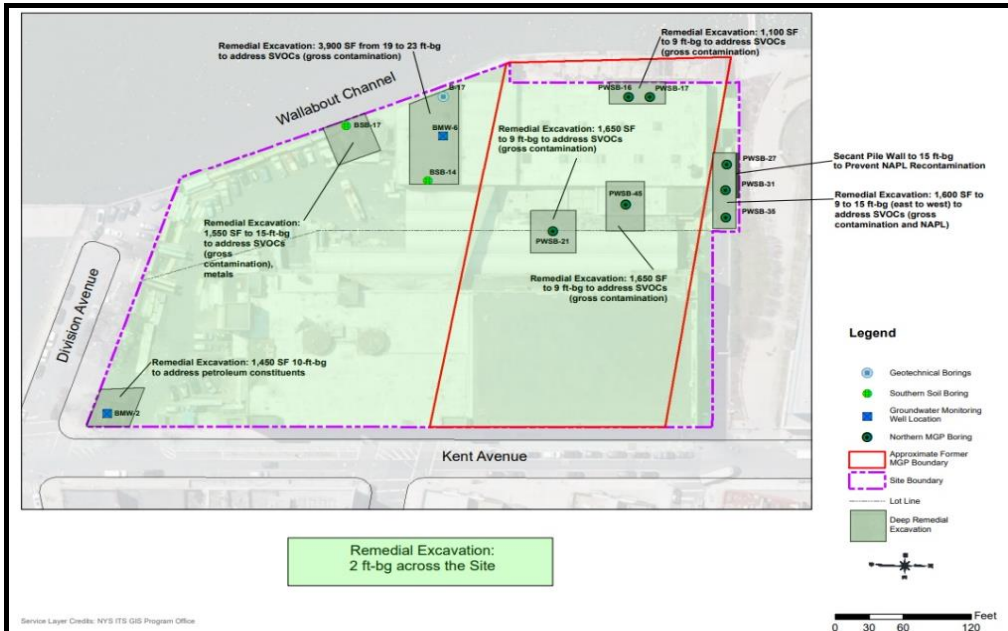


Photo 1:
View of Site conditions
and activities facing
south.




Photo 2:
Site conditions, framing
and rebar installation
facing west.



Photo 3:
View of Site
conditions and
waterproofing and
rebar installation
facing south.




Photo 4:
View of Site
conditions and
waterproofing and
rebar installation
facing southwest.

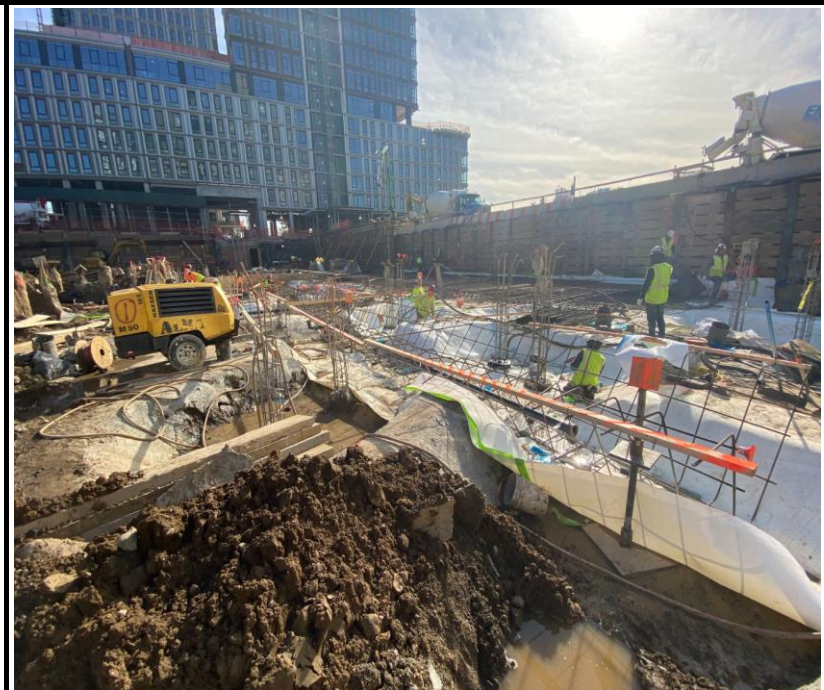

CAMP:
Downwind
Particulates

Dust Levels


0.012 mg/m³ 0.023 mg/m³

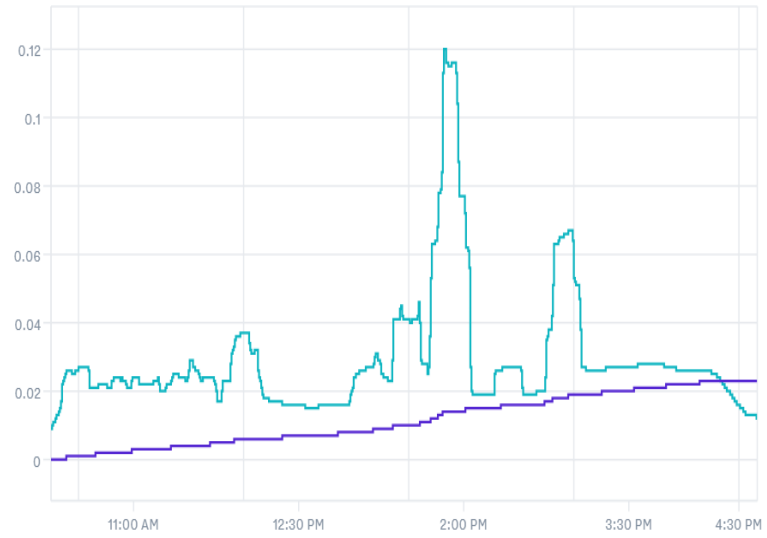


CAMP:
Downwind VOCs

VOC Levels


0.249 ppm 0.158 ppm

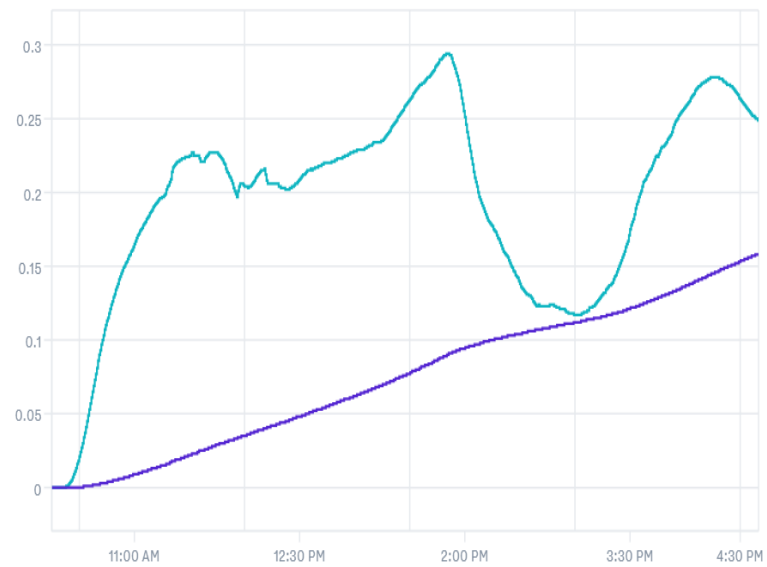

CAMP:
Upwind Particulates

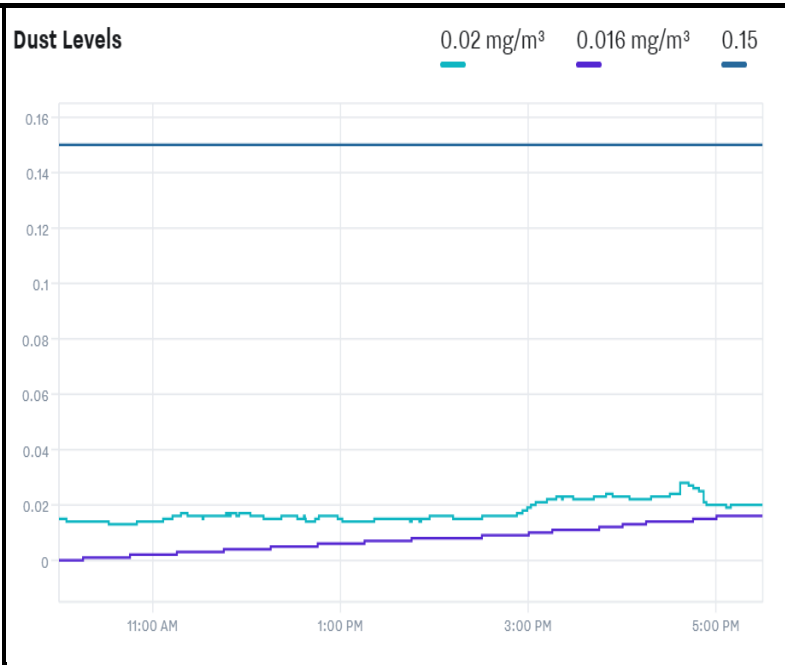

CAMP:
Upwind VOCs

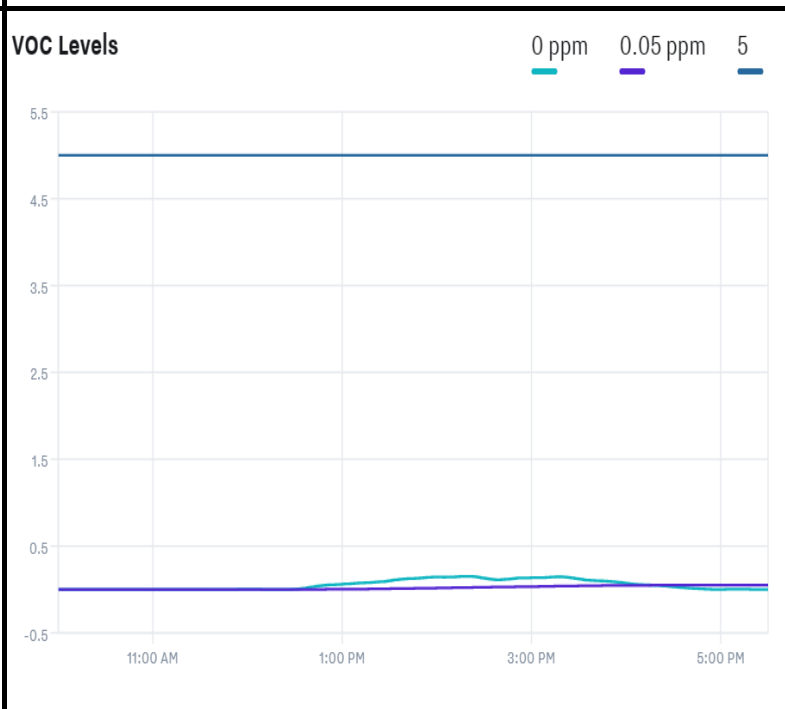

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/8/2024 10:00	3/8/2024 10:10	0.150	0	5	0
DW 2024	3/8/2024 10:10	3/8/2024 10:20	0.150	0	5	0
DW 2024	3/8/2024 10:20	3/8/2024 10:30	0.150	0.001	5	0
DW 2024	3/8/2024 10:30	3/8/2024 10:40	0.150	0.002	5	0.002
DW 2024	3/8/2024 10:40	3/8/2024 10:50	0.150	0.002	5	0.005
DW 2024	3/8/2024 10:50	3/8/2024 11:00	0.150	0.003	5	0.009
DW 2024	3/8/2024 11:00	3/8/2024 11:10	0.150	0.003	5	0.013
DW 2024	3/8/2024 11:10	3/8/2024 11:20	0.150	0.003	5	0.017
DW 2024	3/8/2024 11:20	3/8/2024 11:30	0.150	0.004	5	0.022
DW 2024	3/8/2024 11:30	3/8/2024 11:40	0.150	0.004	5	0.026
DW 2024	3/8/2024 11:40	3/8/2024 11:50	0.150	0.005	5	0.031
DW 2024	3/8/2024 11:50	3/8/2024 12:00	0.150	0.006	5	0.035
DW 2024	3/8/2024 12:00	3/8/2024 12:10	0.150	0.006	5	0.039
DW 2024	3/8/2024 12:10	3/8/2024 12:20	0.150	0.006	5	0.044
DW 2024	3/8/2024 12:20	3/8/2024 12:30	0.150	0.007	5	0.048
DW 2024	3/8/2024 12:30	3/8/2024 12:40	0.150	0.007	5	0.053
DW 2024	3/8/2024 12:40	3/8/2024 12:50	0.150	0.007	5	0.057
DW 2024	3/8/2024 12:50	3/8/2024 13:00	0.150	0.008	5	0.062
DW 2024	3/8/2024 13:00	3/8/2024 13:10	0.150	0.008	5	0.067
DW 2024	3/8/2024 13:10	3/8/2024 13:20	0.150	0.009	5	0.072
DW 2024	3/8/2024 13:20	3/8/2024 13:30	0.150	0.01	5	0.077
DW 2024	3/8/2024 13:30	3/8/2024 13:40	0.150	0.011	5	0.083
DW 2024	3/8/2024 13:40	3/8/2024 13:50	0.150	0.014	5	0.089
DW 2024	3/8/2024 13:50	3/8/2024 14:00	0.150	0.014	5	0.094
DW 2024	3/8/2024 14:00	3/8/2024 14:10	0.150	0.015	5	0.098
DW 2024	3/8/2024 14:10	3/8/2024 14:20	0.150	0.015	5	0.101
DW 2024	3/8/2024 14:20	3/8/2024 14:30	0.150	0.016	5	0.104
DW 2024	3/8/2024 14:30	3/8/2024 14:40	0.150	0.016	5	0.107
DW 2024	3/8/2024 14:40	3/8/2024 14:50	0.150	0.018	5	0.109
DW 2024	3/8/2024 14:50	3/8/2024 15:00	0.150	0.019	5	0.112
DW 2024	3/8/2024 15:00	3/8/2024 15:10	0.150	0.019	5	0.114
DW 2024	3/8/2024 15:10	3/8/2024 15:20	0.150	0.02	5	0.117
DW 2024	3/8/2024 15:20	3/8/2024 15:30	0.150	0.02	5	0.121
DW 2024	3/8/2024 15:30	3/8/2024 15:40	0.150	0.021	5	0.126
DW 2024	3/8/2024 15:40	3/8/2024 15:50	0.150	0.021	5	0.131
DW 2024	3/8/2024 15:50	3/8/2024 16:00	0.150	0.022	5	0.136
DW 2024	3/8/2024 16:00	3/8/2024 16:10	0.150	0.023	5	0.142
DW 2024	3/8/2024 16:10	3/8/2024 16:20	0.150	0.023	5	0.148
DW 2024	3/8/2024 16:20	3/8/2024 16:30	0.150	0.023	5	0.153
DW 2024	3/8/2024 16:30	3/8/2024 16:40	0.150	0.023	5	0.158
DW 2024	3/8/2024 16:40	3/8/2024 16:50	0.150	0.023	5	0
DW 2024	3/8/2024 16:50	3/8/2024 17:00	0.150	0	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/8/2024 10:00	3/8/2024 10:10	0.150	0	5	0
UW 2024	3/8/2024 10:10	3/8/2024 10:20	0.150	0.001	5	0
UW 2024	3/8/2024 10:20	3/8/2024 10:30	0.150	0.001	5	0
UW 2024	3/8/2024 10:30	3/8/2024 10:40	0.150	0.001	5	0
UW 2024	3/8/2024 10:40	3/8/2024 10:50	0.150	0.002	5	0
UW 2024	3/8/2024 10:50	3/8/2024 11:00	0.150	0.002	5	0
UW 2024	3/8/2024 11:00	3/8/2024 11:10	0.150	0.002	5	0
UW 2024	3/8/2024 11:10	3/8/2024 11:20	0.150	0.003	5	0
UW 2024	3/8/2024 11:20	3/8/2024 11:30	0.150	0.003	5	0
UW 2024	3/8/2024 11:30	3/8/2024 11:40	0.150	0.003	5	0
UW 2024	3/8/2024 11:40	3/8/2024 11:50	0.150	0.004	5	0
UW 2024	3/8/2024 11:50	3/8/2024 12:00	0.150	0.004	5	0
UW 2024	3/8/2024 12:00	3/8/2024 12:10	0.150	0.004	5	0
UW 2024	3/8/2024 12:10	3/8/2024 12:20	0.150	0.005	5	0
UW 2024	3/8/2024 12:20	3/8/2024 12:30	0.150	0.005	5	0
UW 2024	3/8/2024 12:30	3/8/2024 12:40	0.150	0.005	5	0
UW 2024	3/8/2024 12:40	3/8/2024 12:50	0.150	0.006	5	0.002
UW 2024	3/8/2024 12:50	3/8/2024 13:00	0.150	0.006	5	0.003
UW 2024	3/8/2024 13:00	3/8/2024 13:10	0.150	0.006	5	0.004
UW 2024	3/8/2024 13:10	3/8/2024 13:20	0.150	0.007	5	0.006
UW 2024	3/8/2024 13:20	3/8/2024 13:30	0.150	0.007	5	0.008
UW 2024	3/8/2024 13:30	3/8/2024 13:40	0.150	0.007	5	0.011
UW 2024	3/8/2024 13:40	3/8/2024 13:50	0.150	0.008	5	0.014
UW 2024	3/8/2024 13:50	3/8/2024 14:00	0.150	0.008	5	0.017
UW 2024	3/8/2024 14:00	3/8/2024 14:10	0.150	0.008	5	0.02
UW 2024	3/8/2024 14:10	3/8/2024 14:20	0.150	0.008	5	0.023
UW 2024	3/8/2024 14:20	3/8/2024 14:30	0.150	0.008	5	0.025
UW 2024	3/8/2024 14:30	3/8/2024 14:40	0.150	0.009	5	0.028
UW 2024	3/8/2024 14:40	3/8/2024 14:50	0.150	0.009	5	0.031
UW 2024	3/8/2024 14:50	3/8/2024 15:00	0.150	0.009	5	0.033
UW 2024	3/8/2024 15:00	3/8/2024 15:10	0.150	0.01	5	0.036
UW 2024	3/8/2024 15:10	3/8/2024 15:20	0.150	0.011	5	0.039
UW 2024	3/8/2024 15:20	3/8/2024 15:30	0.150	0.011	5	0.042
UW 2024	3/8/2024 15:30	3/8/2024 15:40	0.150	0.011	5	0.044
UW 2024	3/8/2024 15:40	3/8/2024 15:50	0.150	0.012	5	0.046
UW 2024	3/8/2024 15:50	3/8/2024 16:00	0.150	0.012	5	0.047
UW 2024	3/8/2024 16:00	3/8/2024 16:10	0.150	0.013	5	0.048
UW 2024	3/8/2024 16:10	3/8/2024 16:20	0.150	0.014	5	0.049
UW 2024	3/8/2024 16:20	3/8/2024 16:30	0.150	0.014	5	0.049
UW 2024	3/8/2024 16:30	3/8/2024 16:40	0.150	0.014	5	0.05
UW 2024	3/8/2024 16:40	3/8/2024 16:50	0.150	0.015	5	0.05
UW 2024	3/8/2024 16:50	3/8/2024 17:00	0.150	0.015	5	0.05

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/8/2024 10:00	3/8/2024 10:10	0.150	0.001	5	0
HS South	3/8/2024 10:10	3/8/2024 10:20	0.150	0	5	0
HS South	3/8/2024 10:20	3/8/2024 10:30	0.150	0	5	0
HS South	3/8/2024 10:30	3/8/2024 10:40	0.150	0	5	0
HS South	3/8/2024 10:40	3/8/2024 10:50	0.150	0.001	5	0
HS South	3/8/2024 10:50	3/8/2024 11:00	0.150	0.001	5	0
HS South	3/8/2024 11:00	3/8/2024 11:10	0.150	0.001	5	0
HS South	3/8/2024 11:10	3/8/2024 11:20	0.150	0.001	5	0
HS South	3/8/2024 11:20	3/8/2024 11:30	0.150	0.001	5	0
HS South	3/8/2024 11:30	3/8/2024 11:40	0.150	0.001	5	0
HS South	3/8/2024 11:40	3/8/2024 11:50	0.150	0.002	5	0
HS South	3/8/2024 11:50	3/8/2024 12:00	0.150	0.002	5	0
HS South	3/8/2024 12:00	3/8/2024 12:10	0.150	0.002	5	0
HS South	3/8/2024 12:10	3/8/2024 12:20	0.150	0.002	5	0
HS South	3/8/2024 12:20	3/8/2024 12:30	0.150	0.002	5	0
HS South	3/8/2024 12:30	3/8/2024 12:40	0.150	0.002	5	0
HS South	3/8/2024 12:40	3/8/2024 12:50	0.150	0.002	5	0
HS South	3/8/2024 12:50	3/8/2024 13:00	0.150	0.002	5	0
HS South	3/8/2024 13:00	3/8/2024 13:10	0.150	0.002	5	0
HS South	3/8/2024 13:10	3/8/2024 13:20	0.150	0.002	5	0
HS South	3/8/2024 13:20	3/8/2024 13:30	0.150	0.002	5	0
HS South	3/8/2024 13:30	3/8/2024 13:40	0.150	0.002	5	0
HS South	3/8/2024 13:40	3/8/2024 13:50	0.150	0.002	5	0
HS South	3/8/2024 13:50	3/8/2024 14:00	0.150	0.002	5	0
HS South	3/8/2024 14:00	3/8/2024 14:10	0.150	0.002	5	0
HS South	3/8/2024 14:10	3/8/2024 14:20	0.150	0.002	5	0
HS South	3/8/2024 14:20	3/8/2024 14:30	0.150	0.002	5	0
HS South	3/8/2024 14:30	3/8/2024 14:40	0.150	0.002	5	0
HS South	3/8/2024 14:40	3/8/2024 14:50	0.150	0.002	5	0
HS South	3/8/2024 14:50	3/8/2024 15:00	0.150	0.002	5	0
HS South	3/8/2024 15:00	3/8/2024 15:10	0.150	0.003	5	0
HS South	3/8/2024 15:10	3/8/2024 15:20	0.150	0.003	5	0
HS South	3/8/2024 15:20	3/8/2024 15:30	0.150	0.003	5	0
HS South	3/8/2024 15:30	3/8/2024 15:40	0.150	0.003	5	0
HS South	3/8/2024 15:40	3/8/2024 15:50	0.150	0.003	5	0
HS South	3/8/2024 15:50	3/8/2024 16:00	0.150	0.004	5	0
HS South	3/8/2024 16:00	3/8/2024 16:10	0.150	0.004	5	0
HS South	3/8/2024 16:10	3/8/2024 16:20	0.150	0.004	5	0
HS South	3/8/2024 16:20	3/8/2024 16:30	0.150	0.004	5	0
HS South	3/8/2024 16:30	3/8/2024 16:40	0.150	0.004	5	0
HS South	3/8/2024 16:40	3/8/2024 16:50	0.150	0.004	5	0
HS South	3/8/2024 16:50	3/8/2024 17:00	0.150	0.004	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/8/2024 10:00	3/8/2024 10:10	0.150	0	5	0
PER1 2024	3/8/2024 10:10	3/8/2024 10:20	0.150	0	5	0
PER1 2024	3/8/2024 10:20	3/8/2024 10:30	0.150	0.001	5	0
PER1 2024	3/8/2024 10:30	3/8/2024 10:40	0.150	0.002	5	0
PER1 2024	3/8/2024 10:40	3/8/2024 10:50	0.150	0.003	5	0
PER1 2024	3/8/2024 10:50	3/8/2024 11:00	0.150	0.004	5	0
PER1 2024	3/8/2024 11:00	3/8/2024 11:10	0.150	0.005	5	0
PER1 2024	3/8/2024 11:10	3/8/2024 11:20	0.150	0.005	5	0
PER1 2024	3/8/2024 11:20	3/8/2024 11:30	0.150	0.006	5	0
PER1 2024	3/8/2024 11:30	3/8/2024 11:40	0.150	0.006	5	0
PER1 2024	3/8/2024 11:40	3/8/2024 11:50	0.150	0.007	5	0
PER1 2024	3/8/2024 11:50	3/8/2024 12:00	0.150	0.008	5	0
PER1 2024	3/8/2024 12:00	3/8/2024 12:10	0.150	0.009	5	0
PER1 2024	3/8/2024 12:10	3/8/2024 12:20	0.150	0.009	5	0
PER1 2024	3/8/2024 12:20	3/8/2024 12:30	0.150	0.01	5	0
PER1 2024	3/8/2024 12:30	3/8/2024 12:40	0.150	0.01	5	0
PER1 2024	3/8/2024 12:40	3/8/2024 12:50	0.150	0.011	5	0
PER1 2024	3/8/2024 12:50	3/8/2024 13:00	0.150	0.011	5	0
PER1 2024	3/8/2024 13:00	3/8/2024 13:10	0.150	0.013	5	0.01
PER1 2024	3/8/2024 13:10	3/8/2024 13:20	0.150	0.014	5	0.01
PER1 2024	3/8/2024 13:20	3/8/2024 13:30	0.150	0.014	5	0.01
PER1 2024	3/8/2024 13:30	3/8/2024 13:40	0.150	0.015	5	0.012
PER1 2024	3/8/2024 13:40	3/8/2024 13:50	0.150	0.016	5	0.02
PER1 2024	3/8/2024 13:50	3/8/2024 14:00	0.150	0.017	5	0.025
PER1 2024	3/8/2024 14:00	3/8/2024 14:10	0.150	0.017	5	0.028
PER1 2024	3/8/2024 14:10	3/8/2024 14:20	0.150	0.018	5	0.028
PER1 2024	3/8/2024 14:20	3/8/2024 14:30	0.150	0.019	5	0.028
PER1 2024	3/8/2024 14:30	3/8/2024 14:40	0.150	0.02	5	0.028
PER1 2024	3/8/2024 14:40	3/8/2024 14:50	0.150	0.021	5	0.028
PER1 2024	3/8/2024 14:50	3/8/2024 15:00	0.150	0.022	5	0.028
PER1 2024	3/8/2024 15:00	3/8/2024 15:10	0.150	0.022	5	0.028
PER1 2024	3/8/2024 15:10	3/8/2024 15:20	0.150	0.023	5	0.028
PER1 2024	3/8/2024 15:20	3/8/2024 15:30	0.150	0.024	5	4.076
PER1 2024	3/8/2024 15:30	3/8/2024 15:40	0.150	0.025	5	4.382
PER1 2024	3/8/2024 15:40	3/8/2024 15:50	0.150	0.026	5	4.399
PER1 2024	3/8/2024 15:50	3/8/2024 16:00	0.150	0.026	5	4.399
PER1 2024	3/8/2024 16:00	3/8/2024 16:10	0.150	0.027	5	4.399
PER1 2024	3/8/2024 16:10	3/8/2024 16:20	0.150	0.028	5	4.399
PER1 2024	3/8/2024 16:20	3/8/2024 16:30	0.150	0.028	5	0
PER1 2024	3/8/2024 16:30	3/8/2024 16:40	0.150	0	5	0
PER1 2024	3/8/2024 16:40	3/8/2024 16:50	0.150	0	5	0
PER1 2024	3/8/2024 16:50	3/8/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/8/2024 10:00	3/8/2024 10:10	0.150	0	5	0
PER2 2024	3/8/2024 10:10	3/8/2024 10:20	0.150	0	5	0
PER2 2024	3/8/2024 10:20	3/8/2024 10:30	0.150	0.001	5	0
PER2 2024	3/8/2024 10:30	3/8/2024 10:40	0.150	0.001	5	0
PER2 2024	3/8/2024 10:40	3/8/2024 10:50	0.150	0.001	5	0
PER2 2024	3/8/2024 10:50	3/8/2024 11:00	0.150	0.002	5	0
PER2 2024	3/8/2024 11:00	3/8/2024 11:10	0.150	0.002	5	0
PER2 2024	3/8/2024 11:10	3/8/2024 11:20	0.150	0.003	5	0
PER2 2024	3/8/2024 11:20	3/8/2024 11:30	0.150	0.003	5	0
PER2 2024	3/8/2024 11:30	3/8/2024 11:40	0.150	0.003	5	0
PER2 2024	3/8/2024 11:40	3/8/2024 11:50	0.150	0.004	5	0
PER2 2024	3/8/2024 11:50	3/8/2024 12:00	0.150	0.004	5	0.004
PER2 2024	3/8/2024 12:00	3/8/2024 12:10	0.150	0.005	5	0.005
PER2 2024	3/8/2024 12:10	3/8/2024 12:20	0.150	0.005	5	0.005
PER2 2024	3/8/2024 12:20	3/8/2024 12:30	0.150	0.006	5	0.005
PER2 2024	3/8/2024 12:30	3/8/2024 12:40	0.150	0.006	5	0.005
PER2 2024	3/8/2024 12:40	3/8/2024 12:50	0.150	0.006	5	0.005
PER2 2024	3/8/2024 12:50	3/8/2024 13:00	0.150	0.007	5	0.005
PER2 2024	3/8/2024 13:00	3/8/2024 13:10	0.150	0.007	5	0.005
PER2 2024	3/8/2024 13:10	3/8/2024 13:20	0.150	0.008	5	0.005
PER2 2024	3/8/2024 13:20	3/8/2024 13:30	0.150	0.009	5	0.005
PER2 2024	3/8/2024 13:30	3/8/2024 13:40	0.150	0.009	5	0.005
PER2 2024	3/8/2024 13:40	3/8/2024 13:50	0.150	0.009	5	0.005
PER2 2024	3/8/2024 13:50	3/8/2024 14:00	0.150	0.01	5	0.005
PER2 2024	3/8/2024 14:00	3/8/2024 14:10	0.150	0.01	5	0.005
PER2 2024	3/8/2024 14:10	3/8/2024 14:20	0.150	0.011	5	0.005
PER2 2024	3/8/2024 14:20	3/8/2024 14:30	0.150	0.011	5	0.005
PER2 2024	3/8/2024 14:30	3/8/2024 14:40	0.150	0.012	5	0.005
PER2 2024	3/8/2024 14:40	3/8/2024 14:50	0.150	0.012	5	0.005
PER2 2024	3/8/2024 14:50	3/8/2024 15:00	0.150	0.013	5	0.005
PER2 2024	3/8/2024 15:00	3/8/2024 15:10	0.150	0.014	5	0.005
PER2 2024	3/8/2024 15:10	3/8/2024 15:20	0.150	0.014	5	0.005
PER2 2024	3/8/2024 15:20	3/8/2024 15:30	0.150	0.015	5	0.005
PER2 2024	3/8/2024 15:30	3/8/2024 15:40	0.150	0.016	5	0.005
PER2 2024	3/8/2024 15:40	3/8/2024 15:50	0.150	0.016	5	0.005
PER2 2024	3/8/2024 15:50	3/8/2024 16:00	0.150	0.017	5	0.005
PER2 2024	3/8/2024 16:00	3/8/2024 16:10	0.150	0.018	5	0.005
PER2 2024	3/8/2024 16:10	3/8/2024 16:20	0.150	0.018	5	0.005
PER2 2024	3/8/2024 16:20	3/8/2024 16:30	0.150	0.019	5	0.005
PER2 2024	3/8/2024 16:30	3/8/2024 16:40	0.150	0.02	5	0.005
PER2 2024	3/8/2024 16:40	3/8/2024 16:50	0.150	0.02	5	0.005
PER2 2024	3/8/2024 16:50	3/8/2024 17:00	0.150	0.02	5	0.005

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/11/2024

Weather: 55 deg. F, Sunny

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation.
- 2) ECD was not on-site and no work was completed in the waterfront remedial excavation.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP tables and graphs are included below. The DW station experienced battery issues. The field personnel completed troubleshooting and the station was brought back online around 1145AM.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3765	0	6965	1520	2120

Site Layout Map and Excavation Figures

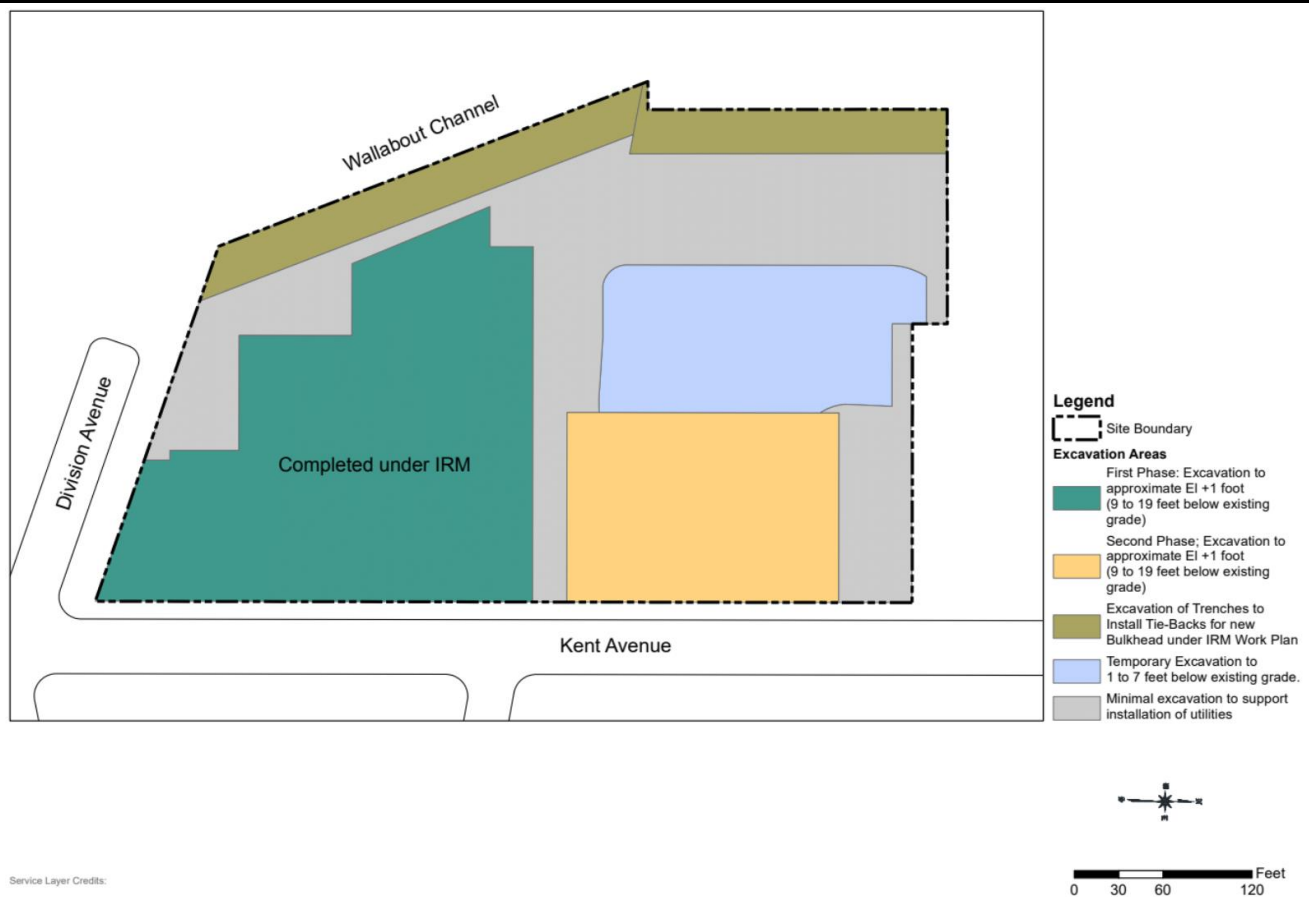

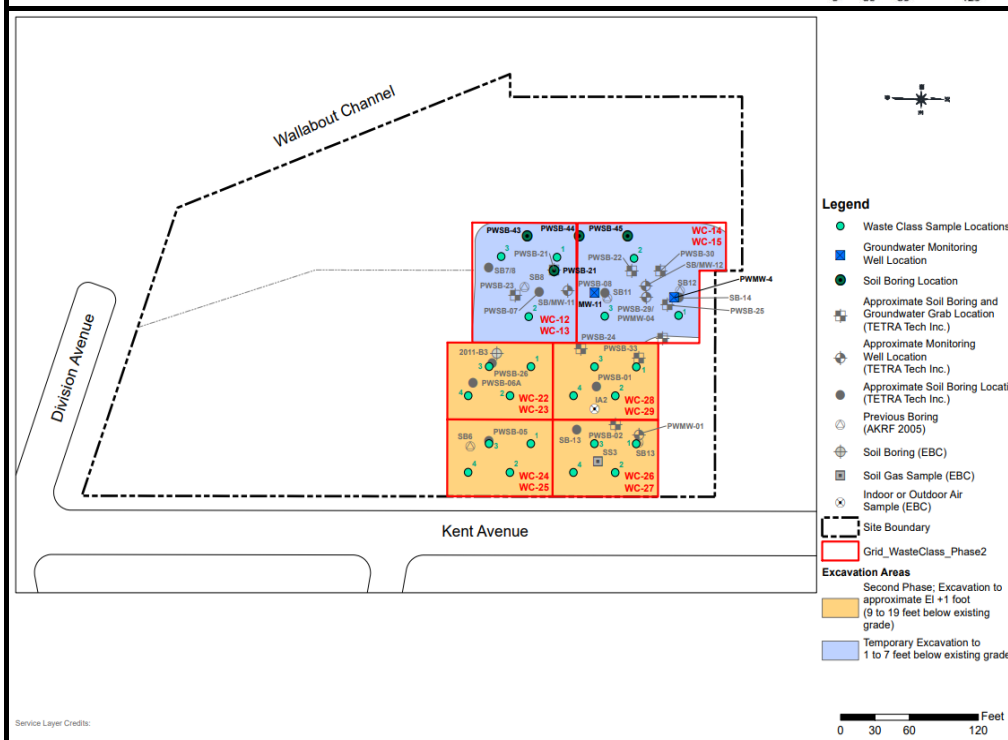
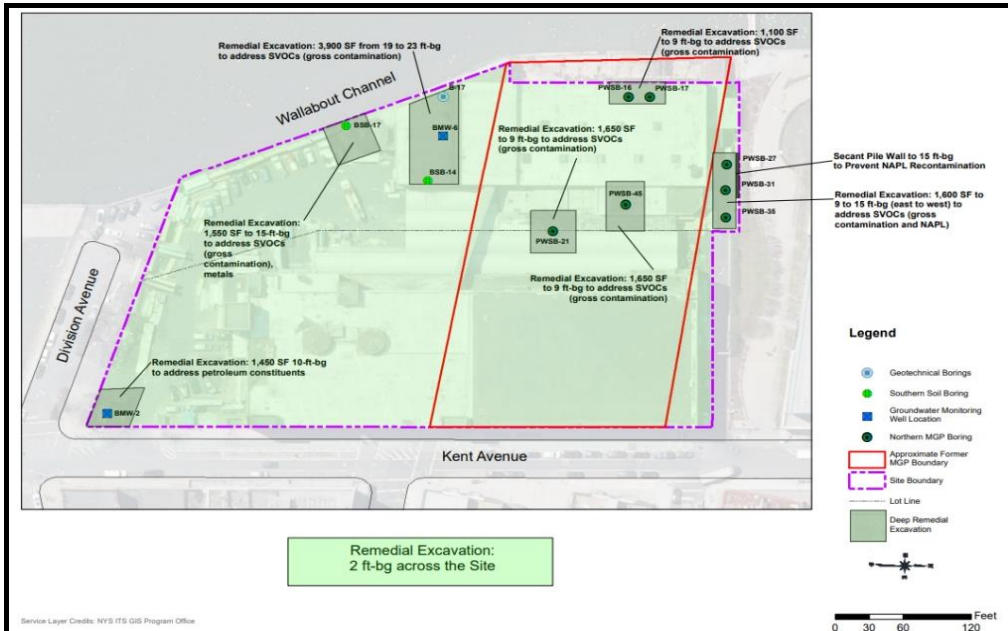


Photo 1:
View of Site conditions
and activities facing
southeast.



Photo 2:
View of Site conditions,
framing and rebar
installation.



Photo 3:
View of Site
conditions and
waterproofing and
rebar installation
facing southwest.




Photo 4:
View of concrete
pouring and
waterproofing
installation.



CAMP:
Downwind
Particulates

Dust Levels


0.006 mg/m³ 0.003 mg/m³

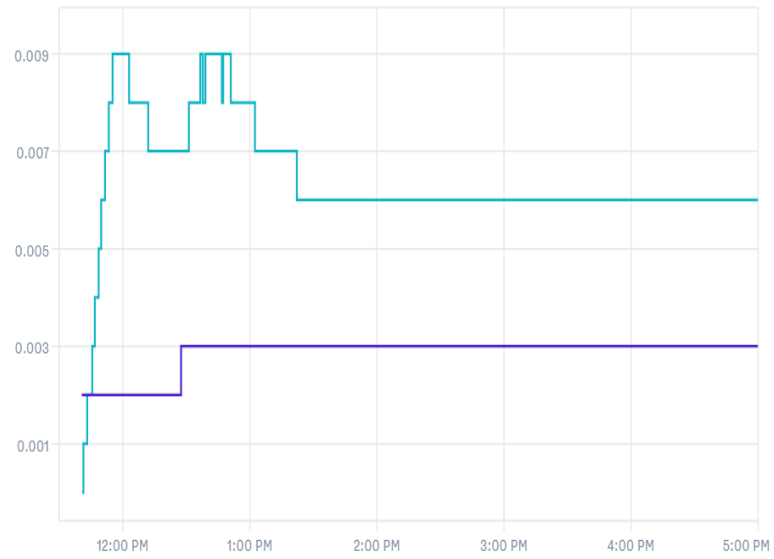

CAMP:
Downwind VOCs

VOC Levels


0.175 ppm 0.057 ppm

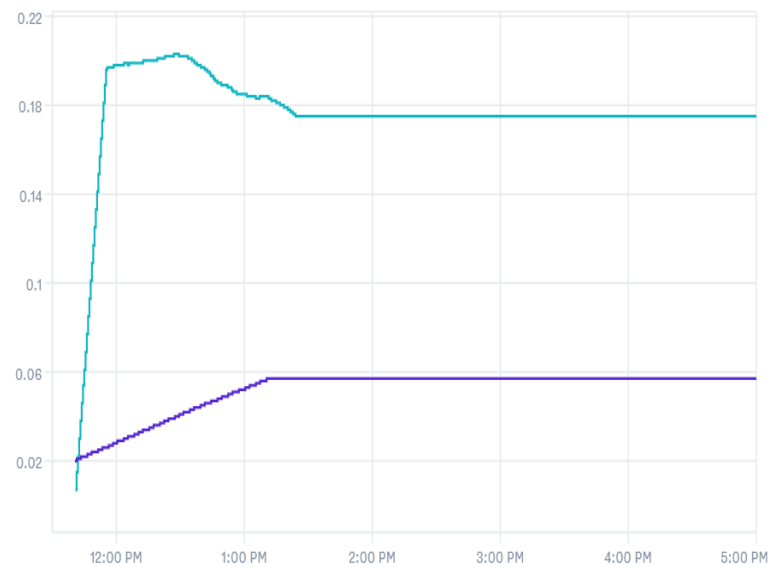

CAMP:
Upwind Particulates

Dust Levels


0.02 mg/m³ 0.02 mg/m³ 0.15

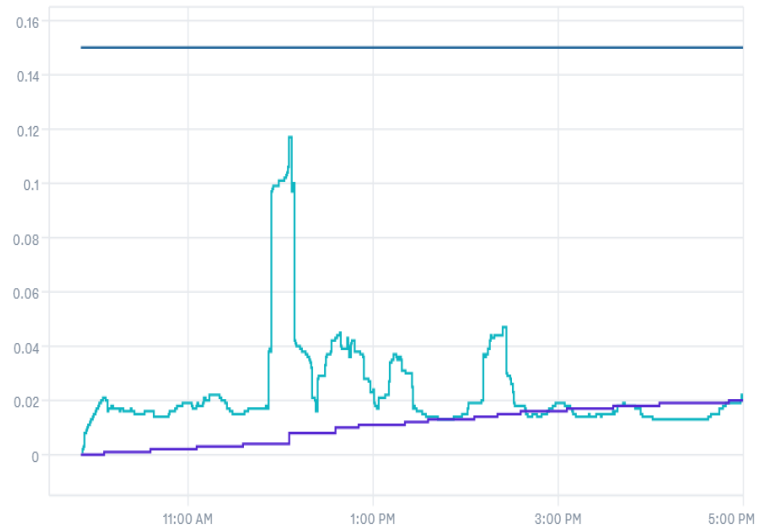

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

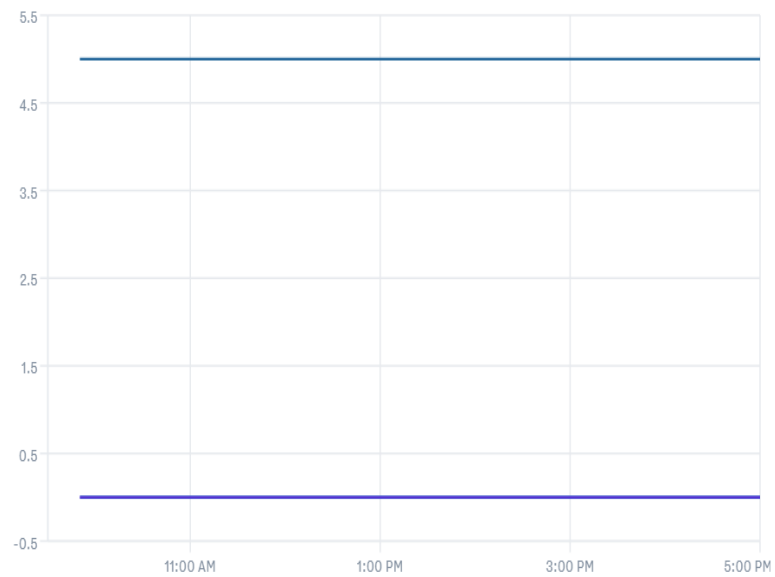

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/11/2024 11:40	3/11/2024 11:50	0.150	0.002	5	0.024
DW 2024	3/11/2024 11:50	3/11/2024 12:00	0.150	0.002	5	0.028
DW 2024	3/11/2024 12:00	3/11/2024 12:10	0.150	0.002	5	0.032
DW 2024	3/11/2024 12:10	3/11/2024 12:20	0.150	0.002	5	0.036
DW 2024	3/11/2024 12:20	3/11/2024 12:30	0.150	0.003	5	0.041
DW 2024	3/11/2024 12:30	3/11/2024 12:40	0.150	0.003	5	0.045
DW 2024	3/11/2024 12:40	3/11/2024 12:50	0.150	0.003	5	0.049
DW 2024	3/11/2024 12:50	3/11/2024 13:00	0.150	0.003	5	0.052
DW 2024	3/11/2024 13:00	3/11/2024 13:10	0.150	0.003	5	0.056
DW 2024	3/11/2024 13:10	3/11/2024 13:20	0.150	0.003	5	0.057
DW 2024	3/11/2024 13:20	3/11/2024 13:30	0.150	0.003	5	0.057
DW 2024	3/11/2024 13:30	3/11/2024 13:40	0.150	0.003	5	0.057
DW 2024	3/11/2024 13:40	3/11/2024 13:50	0.150	0.003	5	0.057
DW 2024	3/11/2024 13:50	3/11/2024 14:00	0.150	0.003	5	0.057
DW 2024	3/11/2024 14:00	3/11/2024 14:10	0.150	0.003	5	0.057
DW 2024	3/11/2024 14:10	3/11/2024 14:20	0.150	0.003	5	0.057
DW 2024	3/11/2024 14:20	3/11/2024 14:30	0.150	0.003	5	0.057
DW 2024	3/11/2024 14:30	3/11/2024 14:40	0.150	0.003	5	0.057
DW 2024	3/11/2024 14:40	3/11/2024 14:50	0.150	0.003	5	0.057
DW 2024	3/11/2024 14:50	3/11/2024 15:00	0.150	0.003	5	0.057
DW 2024	3/11/2024 15:00	3/11/2024 15:10	0.150	0.003	5	0.057
DW 2024	3/11/2024 15:10	3/11/2024 15:20	0.150	0.003	5	0.057
DW 2024	3/11/2024 15:20	3/11/2024 15:30	0.150	0.003	5	0.057
DW 2024	3/11/2024 15:30	3/11/2024 15:40	0.150	0.003	5	0.057
DW 2024	3/11/2024 15:40	3/11/2024 15:50	0.150	0.003	5	0.057
DW 2024	3/11/2024 15:50	3/11/2024 16:00	0.150	0.003	5	0.057
DW 2024	3/11/2024 16:00	3/11/2024 16:10	0.150	0.003	5	0.057
DW 2024	3/11/2024 16:10	3/11/2024 16:20	0.150	0.003	5	0.057
DW 2024	3/11/2024 16:20	3/11/2024 16:30	0.150	0.003	5	0.057
DW 2024	3/11/2024 16:30	3/11/2024 16:40	0.150	0.003	5	0.057
DW 2024	3/11/2024 16:40	3/11/2024 16:50	0.150	0.003	5	0.057
DW 2024	3/11/2024 16:50	3/11/2024 17:00	0.150	0.003	5	0.057

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/11/2024 9:00	3/11/2024 9:10	0.150	0	5	0
UW 2024	3/11/2024 9:10	3/11/2024 9:20	0.150	0	5	0
UW 2024	3/11/2024 9:20	3/11/2024 9:30	0.150	0	5	0
UW 2024	3/11/2024 9:30	3/11/2024 9:40	0.150	0	5	0
UW 2024	3/11/2024 9:40	3/11/2024 9:50	0.150	0	5	0
UW 2024	3/11/2024 9:50	3/11/2024 10:00	0.150	0	5	0
UW 2024	3/11/2024 10:00	3/11/2024 10:10	0.150	0.001	5	0
UW 2024	3/11/2024 10:10	3/11/2024 10:20	0.150	0.001	5	0
UW 2024	3/11/2024 10:20	3/11/2024 10:30	0.150	0.001	5	0
UW 2024	3/11/2024 10:30	3/11/2024 10:40	0.150	0.002	5	0
UW 2024	3/11/2024 10:40	3/11/2024 10:50	0.150	0.002	5	0
UW 2024	3/11/2024 10:50	3/11/2024 11:00	0.150	0.002	5	0
UW 2024	3/11/2024 11:00	3/11/2024 11:10	0.150	0.003	5	0
UW 2024	3/11/2024 11:10	3/11/2024 11:20	0.150	0.003	5	0
UW 2024	3/11/2024 11:20	3/11/2024 11:30	0.150	0.003	5	0
UW 2024	3/11/2024 11:30	3/11/2024 11:40	0.150	0.004	5	0
UW 2024	3/11/2024 11:40	3/11/2024 11:50	0.150	0.004	5	0
UW 2024	3/11/2024 11:50	3/11/2024 12:00	0.150	0.004	5	0
UW 2024	3/11/2024 12:00	3/11/2024 12:10	0.150	0.008	5	0
UW 2024	3/11/2024 12:10	3/11/2024 12:20	0.150	0.008	5	0
UW 2024	3/11/2024 12:20	3/11/2024 12:30	0.150	0.008	5	0
UW 2024	3/11/2024 12:30	3/11/2024 12:40	0.150	0.01	5	0
UW 2024	3/11/2024 12:40	3/11/2024 12:50	0.150	0.01	5	0
UW 2024	3/11/2024 12:50	3/11/2024 13:00	0.150	0.011	5	0
UW 2024	3/11/2024 13:00	3/11/2024 13:10	0.150	0.011	5	0
UW 2024	3/11/2024 13:10	3/11/2024 13:20	0.150	0.011	5	0
UW 2024	3/11/2024 13:20	3/11/2024 13:30	0.150	0.012	5	0
UW 2024	3/11/2024 13:30	3/11/2024 13:40	0.150	0.013	5	0
UW 2024	3/11/2024 13:40	3/11/2024 13:50	0.150	0.013	5	0
UW 2024	3/11/2024 13:50	3/11/2024 14:00	0.150	0.013	5	0
UW 2024	3/11/2024 14:00	3/11/2024 14:10	0.150	0.014	5	0
UW 2024	3/11/2024 14:10	3/11/2024 14:20	0.150	0.014	5	0
UW 2024	3/11/2024 14:20	3/11/2024 14:30	0.150	0.015	5	0
UW 2024	3/11/2024 14:30	3/11/2024 14:40	0.150	0.016	5	0
UW 2024	3/11/2024 14:40	3/11/2024 14:50	0.150	0.016	5	0
UW 2024	3/11/2024 14:50	3/11/2024 15:00	0.150	0.016	5	0
UW 2024	3/11/2024 15:00	3/11/2024 15:10	0.150	0.017	5	0
UW 2024	3/11/2024 15:10	3/11/2024 15:20	0.150	0.017	5	0
UW 2024	3/11/2024 15:20	3/11/2024 15:30	0.150	0.017	5	0
UW 2024	3/11/2024 15:30	3/11/2024 15:40	0.150	0.018	5	0
UW 2024	3/11/2024 15:40	3/11/2024 15:50	0.150	0.018	5	0
UW 2024	3/11/2024 15:50	3/11/2024 16:00	0.150	0.018	5	0
UW 2024	3/11/2024 16:00	3/11/2024 16:10	0.150	0.019	5	0
UW 2024	3/11/2024 16:10	3/11/2024 16:20	0.150	0.019	5	0
UW 2024	3/11/2024 16:20	3/11/2024 16:30	0.150	0.019	5	0
UW 2024	3/11/2024 16:30	3/11/2024 16:40	0.150	0.019	5	0
UW 2024	3/11/2024 16:40	3/11/2024 16:50	0.150	0.019	5	0
UW 2024	3/11/2024 16:50	3/11/2024 17:00	0.150	0.02	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/11/2024 9:00	3/11/2024 9:10	0.150	0	5	0
HS South	3/11/2024 9:10	3/11/2024 9:20	0.150	0	5	0
HS South	3/11/2024 9:20	3/11/2024 9:30	0.150	0	5	0
HS South	3/11/2024 9:30	3/11/2024 9:40	0.150	0	5	0
HS South	3/11/2024 9:40	3/11/2024 9:50	0.150	0	5	0
HS South	3/11/2024 9:50	3/11/2024 10:00	0.150	0	5	0
HS South	3/11/2024 10:00	3/11/2024 10:10	0.150	0	5	0
HS South	3/11/2024 10:10	3/11/2024 10:20	0.150	0	5	0
HS South	3/11/2024 10:20	3/11/2024 10:30	0.150	0	5	0
HS South	3/11/2024 10:30	3/11/2024 10:40	0.150	0.001	5	0
HS South	3/11/2024 10:40	3/11/2024 10:50	0.150	0.001	5	0
HS South	3/11/2024 10:50	3/11/2024 11:00	0.150	0.001	5	0
HS South	3/11/2024 11:00	3/11/2024 11:10	0.150	0.001	5	0
HS South	3/11/2024 11:10	3/11/2024 11:20	0.150	0.001	5	0
HS South	3/11/2024 11:20	3/11/2024 11:30	0.150	0.001	5	0
HS South	3/11/2024 11:30	3/11/2024 11:40	0.150	0.001	5	0
HS South	3/11/2024 11:40	3/11/2024 11:50	0.150	0.001	5	0
HS South	3/11/2024 11:50	3/11/2024 12:00	0.150	0.002	5	0
HS South	3/11/2024 12:00	3/11/2024 12:10	0.150	0.002	5	0
HS South	3/11/2024 12:10	3/11/2024 12:20	0.150	0.002	5	0
HS South	3/11/2024 12:20	3/11/2024 12:30	0.150	0.002	5	0
HS South	3/11/2024 12:30	3/11/2024 12:40	0.150	0.002	5	0
HS South	3/11/2024 12:40	3/11/2024 12:50	0.150	0.002	5	0
HS South	3/11/2024 12:50	3/11/2024 13:00	0.150	0.002	5	0
HS South	3/11/2024 13:00	3/11/2024 13:10	0.150	0.002	5	0
HS South	3/11/2024 13:10	3/11/2024 13:20	0.150	0.002	5	0
HS South	3/11/2024 13:20	3/11/2024 13:30	0.150	0.002	5	0
HS South	3/11/2024 13:30	3/11/2024 13:40	0.150	0.002	5	0
HS South	3/11/2024 13:40	3/11/2024 13:50	0.150	0.002	5	0
HS South	3/11/2024 13:50	3/11/2024 14:00	0.150	0.002	5	0
HS South	3/11/2024 14:00	3/11/2024 14:10	0.150	0.002	5	0
HS South	3/11/2024 14:10	3/11/2024 14:20	0.150	0.002	5	0
HS South	3/11/2024 14:20	3/11/2024 14:30	0.150	0.002	5	0
HS South	3/11/2024 14:30	3/11/2024 14:40	0.150	0.002	5	0
HS South	3/11/2024 14:40	3/11/2024 14:50	0.150	0.002	5	0
HS South	3/11/2024 14:50	3/11/2024 15:00	0.150	0.002	5	0
HS South	3/11/2024 15:00	3/11/2024 15:10	0.150	0.003	5	0
HS South	3/11/2024 15:10	3/11/2024 15:20	0.150	0.003	5	0
HS South	3/11/2024 15:20	3/11/2024 15:30	0.150	0.003	5	0
HS South	3/11/2024 15:30	3/11/2024 15:40	0.150	0.003	5	0
HS South	3/11/2024 15:40	3/11/2024 15:50	0.150	0.003	5	0
HS South	3/11/2024 15:50	3/11/2024 16:00	0.150	0.003	5	0
HS South	3/11/2024 16:00	3/11/2024 16:10	0.150	0.003	5	0
HS South	3/11/2024 16:10	3/11/2024 16:20	0.150	0.003	5	0
HS South	3/11/2024 16:20	3/11/2024 16:30	0.150	0.003	5	0
HS South	3/11/2024 16:30	3/11/2024 16:40	0.150	0.003	5	0
HS South	3/11/2024 16:40	3/11/2024 16:50	0.150	0.003	5	0
HS South	3/11/2024 16:50	3/11/2024 17:00	0.150	0.003	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/11/2024 9:00	3/11/2024 9:10	0.150	0	5	0
PER1 2024	3/11/2024 9:10	3/11/2024 9:20	0.150	0	5	0
PER1 2024	3/11/2024 9:20	3/11/2024 9:30	0.150	0	5	0
PER1 2024	3/11/2024 9:30	3/11/2024 9:40	0.150	0	5	0
PER1 2024	3/11/2024 9:40	3/11/2024 9:50	0.150	0	5	0
PER1 2024	3/11/2024 9:50	3/11/2024 10:00	0.150	0	5	0
PER1 2024	3/11/2024 10:00	3/11/2024 10:10	0.150	0	5	0
PER1 2024	3/11/2024 10:10	3/11/2024 10:20	0.150	0.007	5	0
PER1 2024	3/11/2024 10:20	3/11/2024 10:30	0.150	0.008	5	0
PER1 2024	3/11/2024 10:30	3/11/2024 10:40	0.150	0.009	5	0
PER1 2024	3/11/2024 10:40	3/11/2024 10:50	0.150	0.01	5	0
PER1 2024	3/11/2024 10:50	3/11/2024 11:00	0.150	0.011	5	0
PER1 2024	3/11/2024 11:00	3/11/2024 11:10	0.150	0.012	5	0
PER1 2024	3/11/2024 11:10	3/11/2024 11:20	0.150	0.013	5	0
PER1 2024	3/11/2024 11:20	3/11/2024 11:30	0.150	0.014	5	0
PER1 2024	3/11/2024 11:30	3/11/2024 11:40	0.150	0.014	5	0.003
PER1 2024	3/11/2024 11:40	3/11/2024 11:50	0.150	0.015	5	0.003
PER1 2024	3/11/2024 11:50	3/11/2024 12:00	0.150	0.018	5	0.003
PER1 2024	3/11/2024 12:00	3/11/2024 12:10	0.150	0.02	5	0.003
PER1 2024	3/11/2024 12:10	3/11/2024 12:20	0.150	0.021	5	0.003
PER1 2024	3/11/2024 12:20	3/11/2024 12:30	0.150	0.023	5	0.003
PER1 2024	3/11/2024 12:30	3/11/2024 12:40	0.150	0.026	5	0.003
PER1 2024	3/11/2024 12:40	3/11/2024 12:50	0.150	0.03	5	0.003
PER1 2024	3/11/2024 12:50	3/11/2024 13:00	0.150	0.035	5	0.003
PER1 2024	3/11/2024 13:00	3/11/2024 13:10	0.150	0.04	5	0.003
PER1 2024	3/11/2024 13:10	3/11/2024 13:20	0.150	0.043	5	0.003
PER1 2024	3/11/2024 13:20	3/11/2024 13:30	0.150	0.043	5	0.003
PER1 2024	3/11/2024 13:30	3/11/2024 13:40	0.150	0.044	5	0.003
PER1 2024	3/11/2024 13:40	3/11/2024 13:50	0.150	0.045	5	0.003
PER1 2024	3/11/2024 13:50	3/11/2024 14:00	0.150	0.045	5	0.003
PER1 2024	3/11/2024 14:00	3/11/2024 14:10	0.150	0.046	5	0.01
PER1 2024	3/11/2024 14:10	3/11/2024 14:20	0.150	0.047	5	0.01
PER1 2024	3/11/2024 14:20	3/11/2024 14:30	0.150	0.048	5	0.01
PER1 2024	3/11/2024 14:30	3/11/2024 14:40	0.150	0.048	5	0.01
PER1 2024	3/11/2024 14:40	3/11/2024 14:50	0.150	0.049	5	0.011
PER1 2024	3/11/2024 14:50	3/11/2024 15:00	0.150	0.05	5	0.011
PER1 2024	3/11/2024 15:00	3/11/2024 15:10	0.150	0.051	5	0.011
PER1 2024	3/11/2024 15:10	3/11/2024 15:20	0.150	0.054	5	0.011
PER1 2024	3/11/2024 15:20	3/11/2024 15:30	0.150	0.056	5	0.011
PER1 2024	3/11/2024 15:30	3/11/2024 15:40	0.150	0.057	5	0.011
PER1 2024	3/11/2024 15:40	3/11/2024 15:50	0.150	0.058	5	0.011
PER1 2024	3/11/2024 15:50	3/11/2024 16:00	0.150	0.058	5	0.011
PER1 2024	3/11/2024 16:00	3/11/2024 16:10	0.150	0.059	5	0.011
PER1 2024	3/11/2024 16:10	3/11/2024 16:20	0.150	0.059	5	0.011
PER1 2024	3/11/2024 16:20	3/11/2024 16:30	0.150	0.06	5	0.011
PER1 2024	3/11/2024 16:30	3/11/2024 16:40	0.150	0.061	5	0.011
PER1 2024	3/11/2024 16:40	3/11/2024 16:50	0.150	0.062	5	0.011
PER1 2024	3/11/2024 16:50	3/11/2024 17:00	0.150	0.063	5	0.011

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/11/2024 9:00	3/11/2024 9:10	0.150	0.02	5	0
PER2 2024	3/11/2024 9:10	3/11/2024 9:20	0.150	0.02	5	0
PER2 2024	3/11/2024 9:20	3/11/2024 9:30	0.150	0.02	5	0
PER2 2024	3/11/2024 9:30	3/11/2024 9:40	0.150	0.02	5	0
PER2 2024	3/11/2024 9:40	3/11/2024 9:50	0.150	0.02	5	0
PER2 2024	3/11/2024 9:50	3/11/2024 10:00	0.150	0.02	5	0
PER2 2024	3/11/2024 10:00	3/11/2024 10:10	0.150	0.02	5	0
PER2 2024	3/11/2024 10:10	3/11/2024 10:20	0.150	0	5	0
PER2 2024	3/11/2024 10:20	3/11/2024 10:30	0.150	0.001	5	0
PER2 2024	3/11/2024 10:30	3/11/2024 10:40	0.150	0.001	5	0
PER2 2024	3/11/2024 10:40	3/11/2024 10:50	0.150	0.002	5	0
PER2 2024	3/11/2024 10:50	3/11/2024 11:00	0.150	0.002	5	0
PER2 2024	3/11/2024 11:00	3/11/2024 11:10	0.150	0.002	5	0
PER2 2024	3/11/2024 11:10	3/11/2024 11:20	0.150	0.003	5	0
PER2 2024	3/11/2024 11:20	3/11/2024 11:30	0.150	0.003	5	0
PER2 2024	3/11/2024 11:30	3/11/2024 11:40	0.150	0.004	5	0
PER2 2024	3/11/2024 11:40	3/11/2024 11:50	0.150	0.004	5	0
PER2 2024	3/11/2024 11:50	3/11/2024 12:00	0.150	0.004	5	0
PER2 2024	3/11/2024 12:00	3/11/2024 12:10	0.150	0.005	5	0
PER2 2024	3/11/2024 12:10	3/11/2024 12:20	0.150	0.005	5	0
PER2 2024	3/11/2024 12:20	3/11/2024 12:30	0.150	0.005	5	0
PER2 2024	3/11/2024 12:30	3/11/2024 12:40	0.150	0.006	5	0
PER2 2024	3/11/2024 12:40	3/11/2024 12:50	0.150	0.006	5	0
PER2 2024	3/11/2024 12:50	3/11/2024 13:00	0.150	0.007	5	0
PER2 2024	3/11/2024 13:00	3/11/2024 13:10	0.150	0.007	5	0
PER2 2024	3/11/2024 13:10	3/11/2024 13:20	0.150	0.008	5	0
PER2 2024	3/11/2024 13:20	3/11/2024 13:30	0.150	0.008	5	0
PER2 2024	3/11/2024 13:30	3/11/2024 13:40	0.150	0.008	5	0
PER2 2024	3/11/2024 13:40	3/11/2024 13:50	0.150	0.009	5	0
PER2 2024	3/11/2024 13:50	3/11/2024 14:00	0.150	0.009	5	0
PER2 2024	3/11/2024 14:00	3/11/2024 14:10	0.150	0.01	5	0
PER2 2024	3/11/2024 14:10	3/11/2024 14:20	0.150	0.01	5	0
PER2 2024	3/11/2024 14:20	3/11/2024 14:30	0.150	0.011	5	0
PER2 2024	3/11/2024 14:30	3/11/2024 14:40	0.150	0.011	5	0
PER2 2024	3/11/2024 14:40	3/11/2024 14:50	0.150	0.012	5	0
PER2 2024	3/11/2024 14:50	3/11/2024 15:00	0.150	0.012	5	0
PER2 2024	3/11/2024 15:00	3/11/2024 15:10	0.150	0.013	5	0
PER2 2024	3/11/2024 15:10	3/11/2024 15:20	0.150	0.013	5	0
PER2 2024	3/11/2024 15:20	3/11/2024 15:30	0.150	0.014	5	0
PER2 2024	3/11/2024 15:30	3/11/2024 15:40	0.150	0.014	5	0
PER2 2024	3/11/2024 15:40	3/11/2024 15:50	0.150	0.014	5	0
PER2 2024	3/11/2024 15:50	3/11/2024 16:00	0.150	0.015	5	0
PER2 2024	3/11/2024 16:00	3/11/2024 16:10	0.150	0.015	5	0
PER2 2024	3/11/2024 16:10	3/11/2024 16:20	0.150	0.015	5	0
PER2 2024	3/11/2024 16:20	3/11/2024 16:30	0.150	0.016	5	0
PER2 2024	3/11/2024 16:30	3/11/2024 16:40	0.150	0.016	5	0
PER2 2024	3/11/2024 16:40	3/11/2024 16:50	0.150	0.017	5	0
PER2 2024	3/11/2024 16:50	3/11/2024 17:00	0.150	0.017	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/12/2024

Weather: 55 deg. F, Sunny

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation.
- 2) ECD completed soil excavation in the waterfront remedial excavation.
- 3) Collect endpoint samples EP-74 and EP-77.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): EP-74 and EP-77

Air Monitoring (Since Last Report): CAMP tables and graphs are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3765	0	6965	1520	2120

Site Layout Map and Excavation Figures

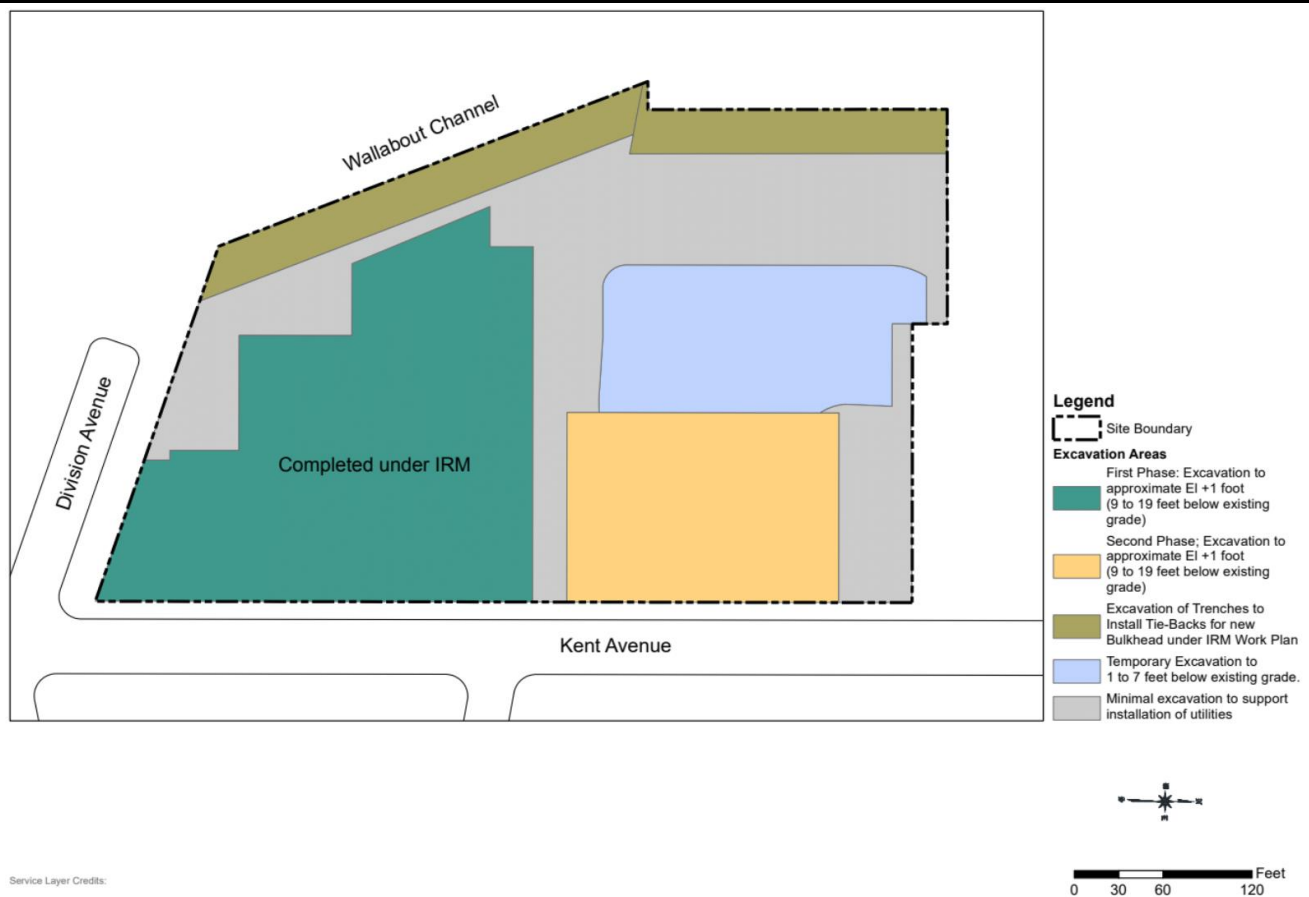

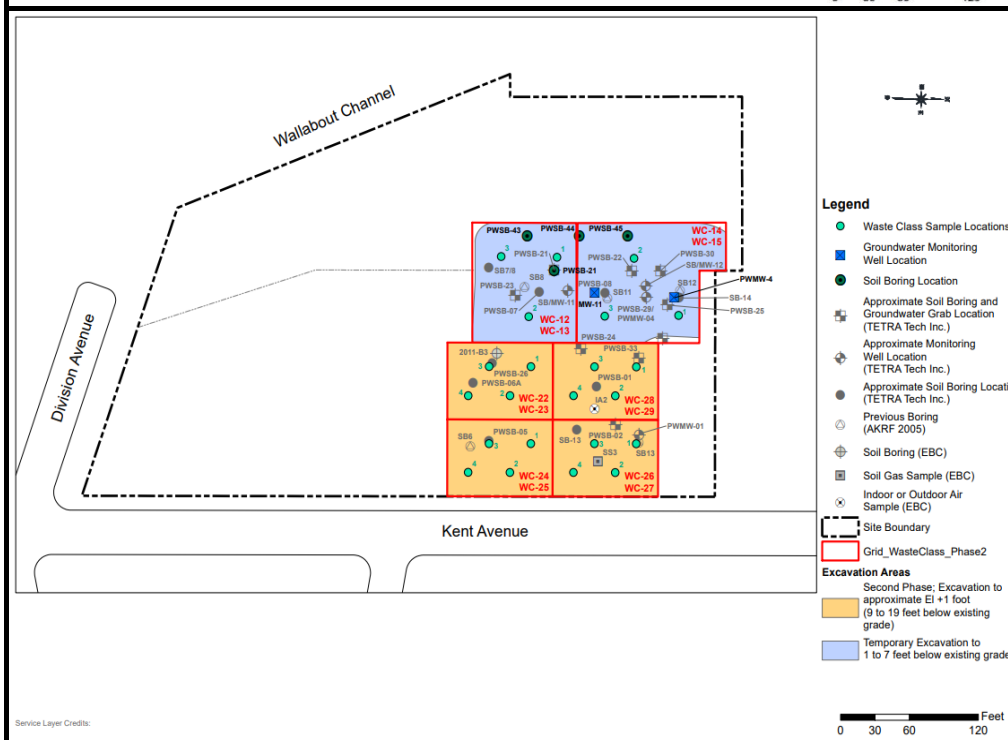
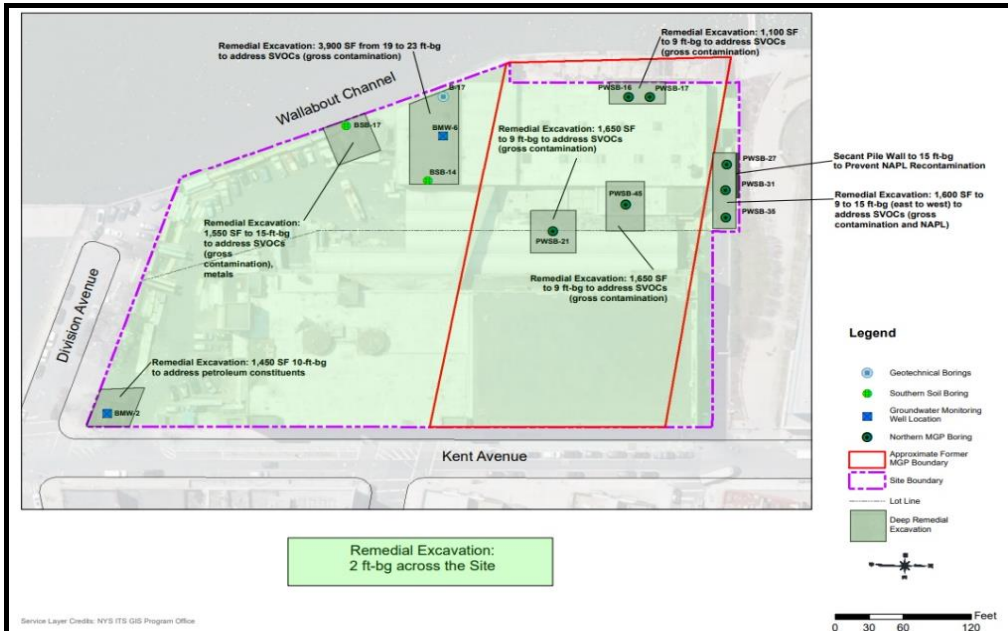


Photo 1:
View of Site conditions
and activities facing
northwest.



Photo 2:
View of Site conditions,
framing and rebar
installation.

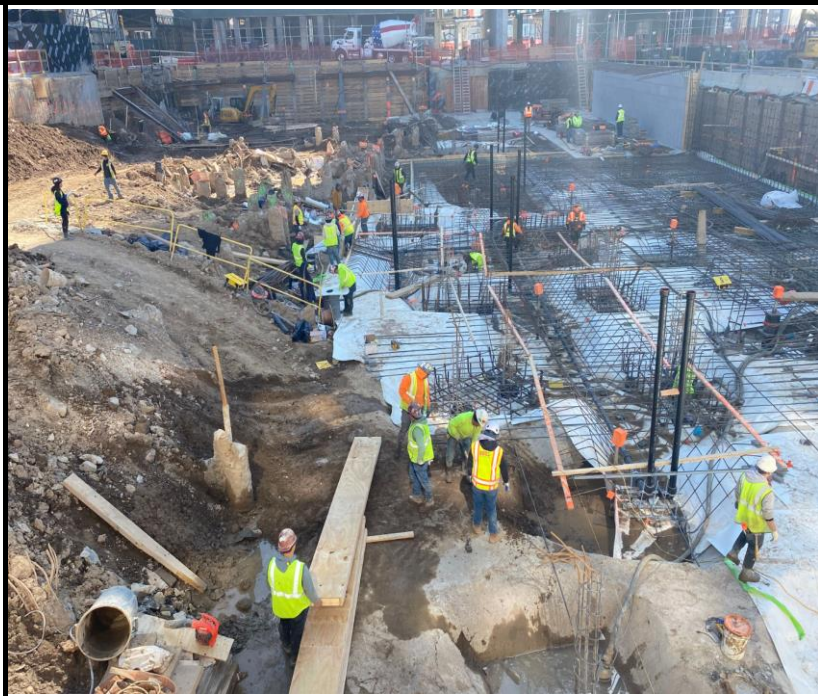
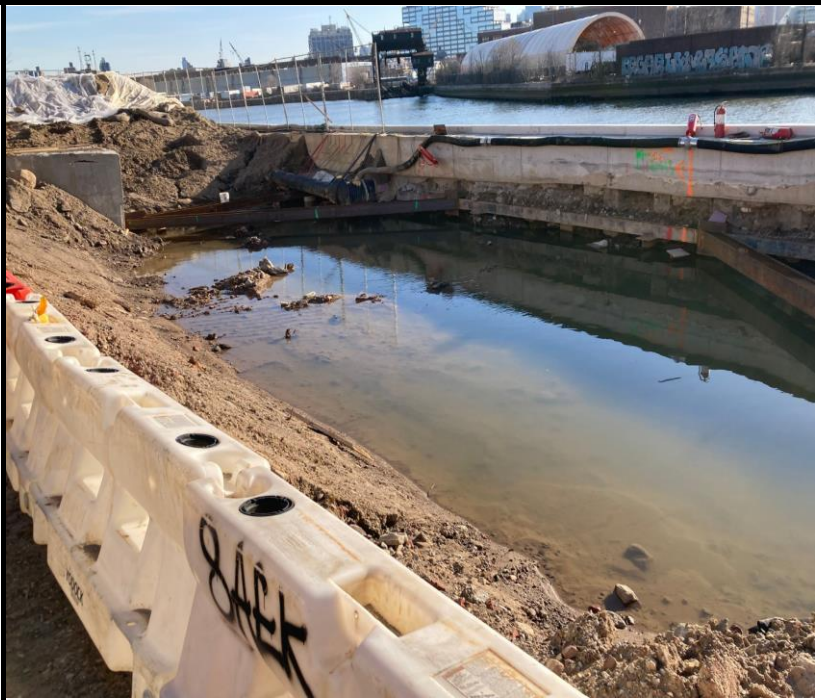


Photo 3:
View of haybales
surrounding the
remedial excavation
soil stockpile.

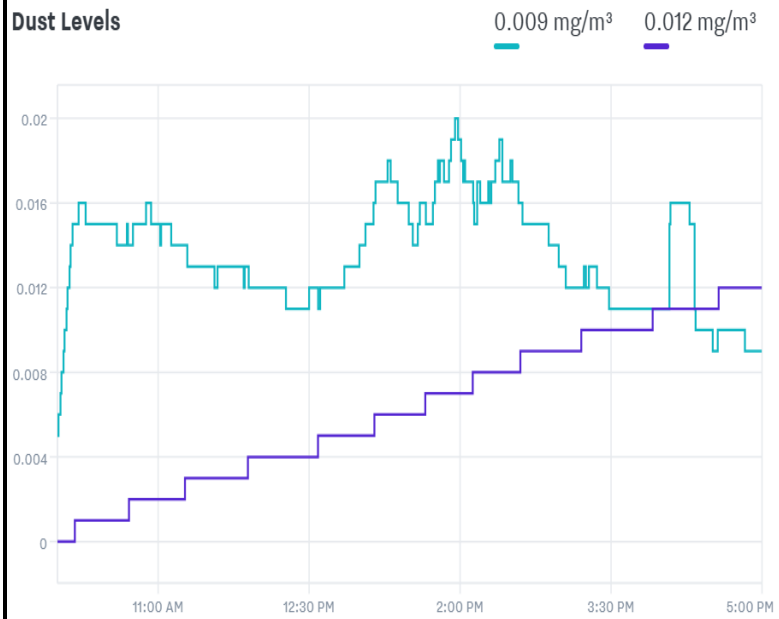


Photo 4:
View of the remedial
excavation.




CAMP:
Downwind
Particulates

Dust Levels




CAMP:
Downwind VOCs

VOC Levels

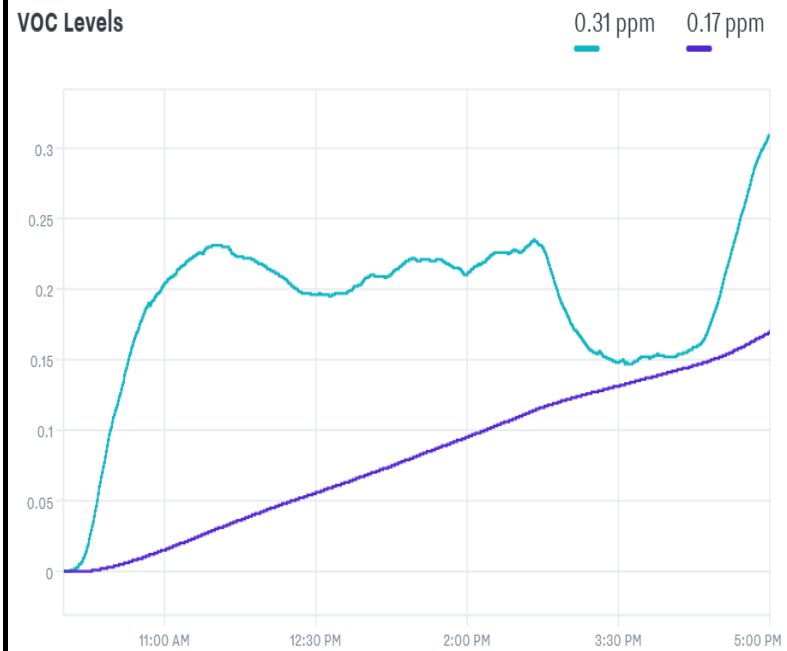


CAMP:
Upwind Particulates

Dust Levels

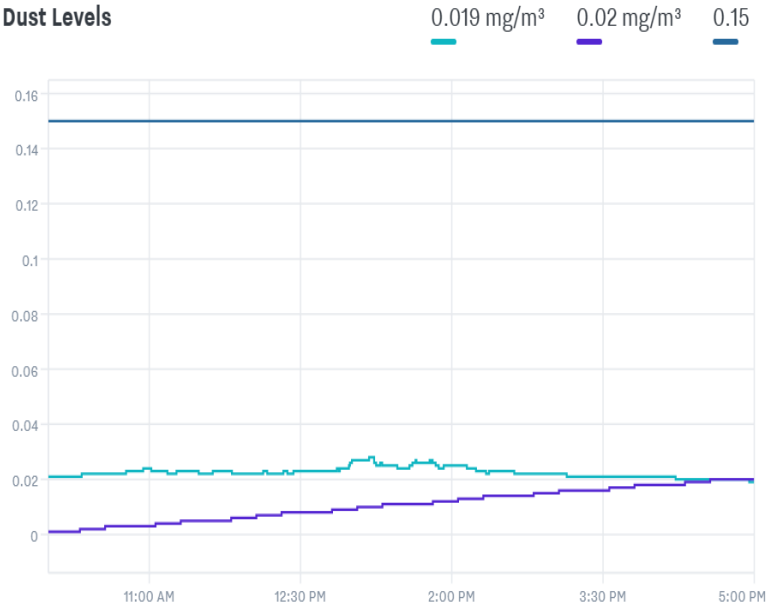

CAMP:
Upwind VOCs

VOC Levels

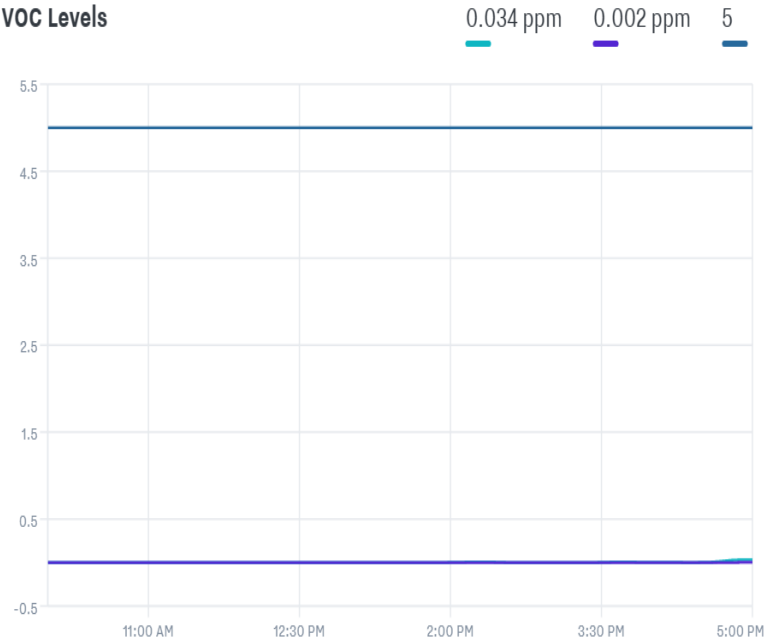

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/12/2024 10:00	3/12/2024 10:10	0.150	0	5	0
DW 2024	3/12/2024 10:10	3/12/2024 10:20	0.150	0.001	5	0.001
DW 2024	3/12/2024 10:20	3/12/2024 10:30	0.150	0.001	5	0.004
DW 2024	3/12/2024 10:30	3/12/2024 10:40	0.150	0.001	5	0.007
DW 2024	3/12/2024 10:40	3/12/2024 10:50	0.150	0.002	5	0.011
DW 2024	3/12/2024 10:50	3/12/2024 11:00	0.150	0.002	5	0.015
DW 2024	3/12/2024 11:00	3/12/2024 11:10	0.150	0.002	5	0.02
DW 2024	3/12/2024 11:10	3/12/2024 11:20	0.150	0.003	5	0.025
DW 2024	3/12/2024 11:20	3/12/2024 11:30	0.150	0.003	5	0.03
DW 2024	3/12/2024 11:30	3/12/2024 11:40	0.150	0.003	5	0.034
DW 2024	3/12/2024 11:40	3/12/2024 11:50	0.150	0.003	5	0.039
DW 2024	3/12/2024 11:50	3/12/2024 12:00	0.150	0.004	5	0.043
DW 2024	3/12/2024 12:00	3/12/2024 12:10	0.150	0.004	5	0.048
DW 2024	3/12/2024 12:10	3/12/2024 12:20	0.150	0.004	5	0.052
DW 2024	3/12/2024 12:20	3/12/2024 12:30	0.150	0.004	5	0.056
DW 2024	3/12/2024 12:30	3/12/2024 12:40	0.150	0.005	5	0.06
DW 2024	3/12/2024 12:40	3/12/2024 12:50	0.150	0.005	5	0.064
DW 2024	3/12/2024 12:50	3/12/2024 13:00	0.150	0.005	5	0.068
DW 2024	3/12/2024 13:00	3/12/2024 13:10	0.150	0.006	5	0.073
DW 2024	3/12/2024 13:10	3/12/2024 13:20	0.150	0.006	5	0.077
DW 2024	3/12/2024 13:20	3/12/2024 13:30	0.150	0.006	5	0.082
DW 2024	3/12/2024 13:30	3/12/2024 13:40	0.150	0.007	5	0.086
DW 2024	3/12/2024 13:40	3/12/2024 13:50	0.150	0.007	5	0.091
DW 2024	3/12/2024 13:50	3/12/2024 14:00	0.150	0.007	5	0.095
DW 2024	3/12/2024 14:00	3/12/2024 14:10	0.150	0.008	5	0.1
DW 2024	3/12/2024 14:10	3/12/2024 14:20	0.150	0.008	5	0.105
DW 2024	3/12/2024 14:20	3/12/2024 14:30	0.150	0.008	5	0.109
DW 2024	3/12/2024 14:30	3/12/2024 14:40	0.150	0.009	5	0.114
DW 2024	3/12/2024 14:40	3/12/2024 14:50	0.150	0.009	5	0.118
DW 2024	3/12/2024 14:50	3/12/2024 15:00	0.150	0.009	5	0.122
DW 2024	3/12/2024 15:00	3/12/2024 15:10	0.150	0.009	5	0.125
DW 2024	3/12/2024 15:10	3/12/2024 15:20	0.150	0.01	5	0.128
DW 2024	3/12/2024 15:20	3/12/2024 15:30	0.150	0.01	5	0.131
DW 2024	3/12/2024 15:30	3/12/2024 15:40	0.150	0.01	5	0.135
DW 2024	3/12/2024 15:40	3/12/2024 15:50	0.150	0.01	5	0.138
DW 2024	3/12/2024 15:50	3/12/2024 16:00	0.150	0.011	5	0.141
DW 2024	3/12/2024 16:00	3/12/2024 16:10	0.150	0.011	5	0.144
DW 2024	3/12/2024 16:10	3/12/2024 16:20	0.150	0.011	5	0.148
DW 2024	3/12/2024 16:20	3/12/2024 16:30	0.150	0.011	5	0.152
DW 2024	3/12/2024 16:30	3/12/2024 16:40	0.150	0.012	5	0.157
DW 2024	3/12/2024 16:40	3/12/2024 16:50	0.150	0.012	5	0.163
DW 2024	3/12/2024 16:50	3/12/2024 17:00	0.150	0.012	5	0.17

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/12/2024 10:00	3/12/2024 10:10	0.150	0.001	5	0
UW 2024	3/12/2024 10:10	3/12/2024 10:20	0.150	0.002	5	0
UW 2024	3/12/2024 10:20	3/12/2024 10:30	0.150	0.002	5	0
UW 2024	3/12/2024 10:30	3/12/2024 10:40	0.150	0.003	5	0
UW 2024	3/12/2024 10:40	3/12/2024 10:50	0.150	0.003	5	0
UW 2024	3/12/2024 10:50	3/12/2024 11:00	0.150	0.003	5	0
UW 2024	3/12/2024 11:00	3/12/2024 11:10	0.150	0.004	5	0
UW 2024	3/12/2024 11:10	3/12/2024 11:20	0.150	0.005	5	0
UW 2024	3/12/2024 11:20	3/12/2024 11:30	0.150	0.005	5	0
UW 2024	3/12/2024 11:30	3/12/2024 11:40	0.150	0.005	5	0
UW 2024	3/12/2024 11:40	3/12/2024 11:50	0.150	0.006	5	0
UW 2024	3/12/2024 11:50	3/12/2024 12:00	0.150	0.006	5	0
UW 2024	3/12/2024 12:00	3/12/2024 12:10	0.150	0.007	5	0
UW 2024	3/12/2024 12:10	3/12/2024 12:20	0.150	0.008	5	0
UW 2024	3/12/2024 12:20	3/12/2024 12:30	0.150	0.008	5	0
UW 2024	3/12/2024 12:30	3/12/2024 12:40	0.150	0.008	5	0
UW 2024	3/12/2024 12:40	3/12/2024 12:50	0.150	0.009	5	0
UW 2024	3/12/2024 12:50	3/12/2024 13:00	0.150	0.009	5	0
UW 2024	3/12/2024 13:00	3/12/2024 13:10	0.150	0.01	5	0
UW 2024	3/12/2024 13:10	3/12/2024 13:20	0.150	0.011	5	0
UW 2024	3/12/2024 13:20	3/12/2024 13:30	0.150	0.011	5	0
UW 2024	3/12/2024 13:30	3/12/2024 13:40	0.150	0.011	5	0
UW 2024	3/12/2024 13:40	3/12/2024 13:50	0.150	0.012	5	0
UW 2024	3/12/2024 13:50	3/12/2024 14:00	0.150	0.012	5	0
UW 2024	3/12/2024 14:00	3/12/2024 14:10	0.150	0.013	5	0
UW 2024	3/12/2024 14:10	3/12/2024 14:20	0.150	0.014	5	0
UW 2024	3/12/2024 14:20	3/12/2024 14:30	0.150	0.014	5	0
UW 2024	3/12/2024 14:30	3/12/2024 14:40	0.150	0.014	5	0
UW 2024	3/12/2024 14:40	3/12/2024 14:50	0.150	0.015	5	0
UW 2024	3/12/2024 14:50	3/12/2024 15:00	0.150	0.015	5	0
UW 2024	3/12/2024 15:00	3/12/2024 15:10	0.150	0.016	5	0
UW 2024	3/12/2024 15:10	3/12/2024 15:20	0.150	0.016	5	0
UW 2024	3/12/2024 15:20	3/12/2024 15:30	0.150	0.016	5	0
UW 2024	3/12/2024 15:30	3/12/2024 15:40	0.150	0.017	5	0
UW 2024	3/12/2024 15:40	3/12/2024 15:50	0.150	0.018	5	0
UW 2024	3/12/2024 15:50	3/12/2024 16:00	0.150	0.018	5	0
UW 2024	3/12/2024 16:00	3/12/2024 16:10	0.150	0.018	5	0
UW 2024	3/12/2024 16:10	3/12/2024 16:20	0.150	0.019	5	0
UW 2024	3/12/2024 16:20	3/12/2024 16:30	0.150	0.019	5	0
UW 2024	3/12/2024 16:30	3/12/2024 16:40	0.150	0.02	5	0.001
UW 2024	3/12/2024 16:40	3/12/2024 16:50	0.150	0.02	5	0.001
UW 2024	3/12/2024 16:50	3/12/2024 17:00	0.150	0.02	5	0.002

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/12/2024 10:00	3/12/2024 10:10	0.150	0.001	5	0
HS South	3/12/2024 10:10	3/12/2024 10:20	0.150	0.001	5	0
HS South	3/12/2024 10:20	3/12/2024 10:30	0.150	0.001	5	0
HS South	3/12/2024 10:30	3/12/2024 10:40	0.150	0.001	5	0
HS South	3/12/2024 10:40	3/12/2024 10:50	0.150	0.002	5	0
HS South	3/12/2024 10:50	3/12/2024 11:00	0.150	0.003	5	0
HS South	3/12/2024 11:00	3/12/2024 11:10	0.150	0.003	5	0
HS South	3/12/2024 11:10	3/12/2024 11:20	0.150	0.004	5	0
HS South	3/12/2024 11:20	3/12/2024 11:30	0.150	0.004	5	0
HS South	3/12/2024 11:30	3/12/2024 11:40	0.150	0.004	5	0
HS South	3/12/2024 11:40	3/12/2024 11:50	0.150	0.004	5	0
HS South	3/12/2024 11:50	3/12/2024 12:00	0.150	0.005	5	0
HS South	3/12/2024 12:00	3/12/2024 12:10	0.150	0.005	5	0
HS South	3/12/2024 12:10	3/12/2024 12:20	0.150	0.005	5	0
HS South	3/12/2024 12:20	3/12/2024 12:30	0.150	0.005	5	0
HS South	3/12/2024 12:30	3/12/2024 12:40	0.150	0.006	5	0
HS South	3/12/2024 12:40	3/12/2024 12:50	0.150	0.006	5	0
HS South	3/12/2024 12:50	3/12/2024 13:00	0.150	0.006	5	0
HS South	3/12/2024 13:00	3/12/2024 13:10	0.150	0.006	5	0
HS South	3/12/2024 13:10	3/12/2024 13:20	0.150	0.007	5	0
HS South	3/12/2024 13:20	3/12/2024 13:30	0.150	0.007	5	0
HS South	3/12/2024 13:30	3/12/2024 13:40	0.150	0.007	5	0.001
HS South	3/12/2024 13:40	3/12/2024 13:50	0.150	0.007	5	0.001
HS South	3/12/2024 13:50	3/12/2024 14:00	0.150	0.008	5	0.001
HS South	3/12/2024 14:00	3/12/2024 14:10	0.150	0.008	5	0.001
HS South	3/12/2024 14:10	3/12/2024 14:20	0.150	0.008	5	0.001
HS South	3/12/2024 14:20	3/12/2024 14:30	0.150	0.008	5	0.001
HS South	3/12/2024 14:30	3/12/2024 14:40	0.150	0.008	5	0.001
HS South	3/12/2024 14:40	3/12/2024 14:50	0.150	0.008	5	0.001
HS South	3/12/2024 14:50	3/12/2024 15:00	0.150	0.009	5	0.001
HS South	3/12/2024 15:00	3/12/2024 15:10	0.150	0.009	5	0.001
HS South	3/12/2024 15:10	3/12/2024 15:20	0.150	0.009	5	0.001
HS South	3/12/2024 15:20	3/12/2024 15:30	0.150	0.009	5	0.001
HS South	3/12/2024 15:30	3/12/2024 15:40	0.150	0.009	5	0.001
HS South	3/12/2024 15:40	3/12/2024 15:50	0.150	0.009	5	0.001
HS South	3/12/2024 15:50	3/12/2024 16:00	0.150	0.009	5	0.001
HS South	3/12/2024 16:00	3/12/2024 16:10	0.150	0.009	5	0.001
HS South	3/12/2024 16:10	3/12/2024 16:20	0.150	0.009	5	0.001
HS South	3/12/2024 16:20	3/12/2024 16:30	0.150	0.009	5	0.001
HS South	3/12/2024 16:30	3/12/2024 16:40	0.150	0.01	5	0.001
HS South	3/12/2024 16:40	3/12/2024 16:50	0.150	0.01	5	0.001
HS South	3/12/2024 16:50	3/12/2024 17:00	0.150	0.01	5	0.001

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/12/2024 10:00	3/12/2024 10:10	0.150	0.002	5	0
PER1 2024	3/12/2024 10:10	3/12/2024 10:20	0.150	0.002	5	0
PER1 2024	3/12/2024 10:20	3/12/2024 10:30	0.150	0.003	5	0
PER1 2024	3/12/2024 10:30	3/12/2024 10:40	0.150	0.004	5	0
PER1 2024	3/12/2024 10:40	3/12/2024 10:50	0.150	0.004	5	0
PER1 2024	3/12/2024 10:50	3/12/2024 11:00	0.150	0.005	5	0
PER1 2024	3/12/2024 11:00	3/12/2024 11:10	0.150	0.006	5	0
PER1 2024	3/12/2024 11:10	3/12/2024 11:20	0.150	0.007	5	0
PER1 2024	3/12/2024 11:20	3/12/2024 11:30	0.150	0.008	5	0
PER1 2024	3/12/2024 11:30	3/12/2024 11:40	0.150	0.008	5	0
PER1 2024	3/12/2024 11:40	3/12/2024 11:50	0.150	0.013	5	0
PER1 2024	3/12/2024 11:50	3/12/2024 12:00	0.150	0.016	5	0
PER1 2024	3/12/2024 12:00	3/12/2024 12:10	0.150	0.018	5	0
PER1 2024	3/12/2024 12:10	3/12/2024 12:20	0.150	0.019	5	0
PER1 2024	3/12/2024 12:20	3/12/2024 12:30	0.150	0.02	5	0
PER1 2024	3/12/2024 12:30	3/12/2024 12:40	0.150	0.021	5	0
PER1 2024	3/12/2024 12:40	3/12/2024 12:50	0.150	0.022	5	0
PER1 2024	3/12/2024 12:50	3/12/2024 13:00	0.150	0.024	5	0
PER1 2024	3/12/2024 13:00	3/12/2024 13:10	0.150	0.025	5	0
PER1 2024	3/12/2024 13:10	3/12/2024 13:20	0.150	0.026	5	0
PER1 2024	3/12/2024 13:20	3/12/2024 13:30	0.150	0.026	5	0
PER1 2024	3/12/2024 13:30	3/12/2024 13:40	0.150	0.028	5	0
PER1 2024	3/12/2024 13:40	3/12/2024 13:50	0.150	0.029	5	0
PER1 2024	3/12/2024 13:50	3/12/2024 14:00	0.150	0.03	5	0
PER1 2024	3/12/2024 14:00	3/12/2024 14:10	0.150	0.031	5	0
PER1 2024	3/12/2024 14:10	3/12/2024 14:20	0.150	0.033	5	0
PER1 2024	3/12/2024 14:20	3/12/2024 14:30	0.150	0.036	5	0
PER1 2024	3/12/2024 14:30	3/12/2024 14:40	0.150	0.041	5	0
PER1 2024	3/12/2024 14:40	3/12/2024 14:50	0.150	0.042	5	0
PER1 2024	3/12/2024 14:50	3/12/2024 15:00	0.150	0.045	5	0
PER1 2024	3/12/2024 15:00	3/12/2024 15:10	0.150	0.046	5	0
PER1 2024	3/12/2024 15:10	3/12/2024 15:20	0.150	0.048	5	0
PER1 2024	3/12/2024 15:20	3/12/2024 15:30	0.150	0.049	5	0
PER1 2024	3/12/2024 15:30	3/12/2024 15:40	0.150	0.051	5	0
PER1 2024	3/12/2024 15:40	3/12/2024 15:50	0.150	0.053	5	0
PER1 2024	3/12/2024 15:50	3/12/2024 16:00	0.150	0.054	5	0
PER1 2024	3/12/2024 16:00	3/12/2024 16:10	0.150	0.06	5	0
PER1 2024	3/12/2024 16:10	3/12/2024 16:20	0.150	0.061	5	0
PER1 2024	3/12/2024 16:20	3/12/2024 16:30	0.150	0.061	5	0
PER1 2024	3/12/2024 16:30	3/12/2024 16:40	0.150	0.062	5	0
PER1 2024	3/12/2024 16:40	3/12/2024 16:50	0.150	0.063	5	0
PER1 2024	3/12/2024 16:50	3/12/2024 17:00	0.150	0.064	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/12/2024 10:00	3/12/2024 10:10	0.150	0	5	0
PER2 2024	3/12/2024 10:10	3/12/2024 10:20	0.150	0.001	5	0
PER2 2024	3/12/2024 10:20	3/12/2024 10:30	0.150	0.001	5	0
PER2 2024	3/12/2024 10:30	3/12/2024 10:40	0.150	0.002	5	0
PER2 2024	3/12/2024 10:40	3/12/2024 10:50	0.150	0.002	5	0
PER2 2024	3/12/2024 10:50	3/12/2024 11:00	0.150	0.003	5	0
PER2 2024	3/12/2024 11:00	3/12/2024 11:10	0.150	0.003	5	0
PER2 2024	3/12/2024 11:10	3/12/2024 11:20	0.150	0.004	5	0
PER2 2024	3/12/2024 11:20	3/12/2024 11:30	0.150	0.004	5	0
PER2 2024	3/12/2024 11:30	3/12/2024 11:40	0.150	0.005	5	0
PER2 2024	3/12/2024 11:40	3/12/2024 11:50	0.150	0.005	5	0
PER2 2024	3/12/2024 11:50	3/12/2024 12:00	0.150	0.005	5	0
PER2 2024	3/12/2024 12:00	3/12/2024 12:10	0.150	0.006	5	0
PER2 2024	3/12/2024 12:10	3/12/2024 12:20	0.150	0.006	5	0
PER2 2024	3/12/2024 12:20	3/12/2024 12:30	0.150	0.006	5	0
PER2 2024	3/12/2024 12:30	3/12/2024 12:40	0.150	0.007	5	0
PER2 2024	3/12/2024 12:40	3/12/2024 12:50	0.150	0.008	5	0
PER2 2024	3/12/2024 12:50	3/12/2024 13:00	0.150	0.008	5	0
PER2 2024	3/12/2024 13:00	3/12/2024 13:10	0.150	0.009	5	0
PER2 2024	3/12/2024 13:10	3/12/2024 13:20	0.150	0.009	5	0
PER2 2024	3/12/2024 13:20	3/12/2024 13:30	0.150	0.01	5	0
PER2 2024	3/12/2024 13:30	3/12/2024 13:40	0.150	0.01	5	0
PER2 2024	3/12/2024 13:40	3/12/2024 13:50	0.150	0.011	5	0
PER2 2024	3/12/2024 13:50	3/12/2024 14:00	0.150	0.012	5	0
PER2 2024	3/12/2024 14:00	3/12/2024 14:10	0.150	0.012	5	0
PER2 2024	3/12/2024 14:10	3/12/2024 14:20	0.150	0.013	5	0
PER2 2024	3/12/2024 14:20	3/12/2024 14:30	0.150	0.013	5	0
PER2 2024	3/12/2024 14:30	3/12/2024 14:40	0.150	0.014	5	0
PER2 2024	3/12/2024 14:40	3/12/2024 14:50	0.150	0.014	5	0
PER2 2024	3/12/2024 14:50	3/12/2024 15:00	0.150	0.015	5	0
PER2 2024	3/12/2024 15:00	3/12/2024 15:10	0.150	0.015	5	0
PER2 2024	3/12/2024 15:10	3/12/2024 15:20	0.150	0.016	5	0
PER2 2024	3/12/2024 15:20	3/12/2024 15:30	0.150	0.016	5	0
PER2 2024	3/12/2024 15:30	3/12/2024 15:40	0.150	0.016	5	0
PER2 2024	3/12/2024 15:40	3/12/2024 15:50	0.150	0.017	5	0
PER2 2024	3/12/2024 15:50	3/12/2024 16:00	0.150	0.017	5	0
PER2 2024	3/12/2024 16:00	3/12/2024 16:10	0.150	0.017	5	0
PER2 2024	3/12/2024 16:10	3/12/2024 16:20	0.150	0.018	5	0
PER2 2024	3/12/2024 16:20	3/12/2024 16:30	0.150	0.018	5	0
PER2 2024	3/12/2024 16:30	3/12/2024 16:40	0.150	0.018	5	0
PER2 2024	3/12/2024 16:40	3/12/2024 16:50	0.150	0.019	5	0
PER2 2024	3/12/2024 16:50	3/12/2024 17:00	0.150	0.019	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/13/2024

Weather: 55 deg. F, Sunny

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation.
- 2) ECD prepared the dewatering system connection in preparation for soil excavation in the waterfront remedial excavation; Collect hotspot influent and effluent dewatering samples.
- 4) Export 5 loads (approximately 100 CY) of material from WC-29 for off-site disposal at MCUA.
- 5) Export of 10 loads (approximately 200 CY) of material from WC-29 for off-site disposal at Harmony Foul Rift.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): HS_Influent_20240313 and Effluent_20240313

Air Monitoring (Since Last Report): CAMP tables and graphs are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	200	0	0	0	100
Total:(CY)	3965	0	6965	1520	2220

Site Layout Map and Excavation Figures

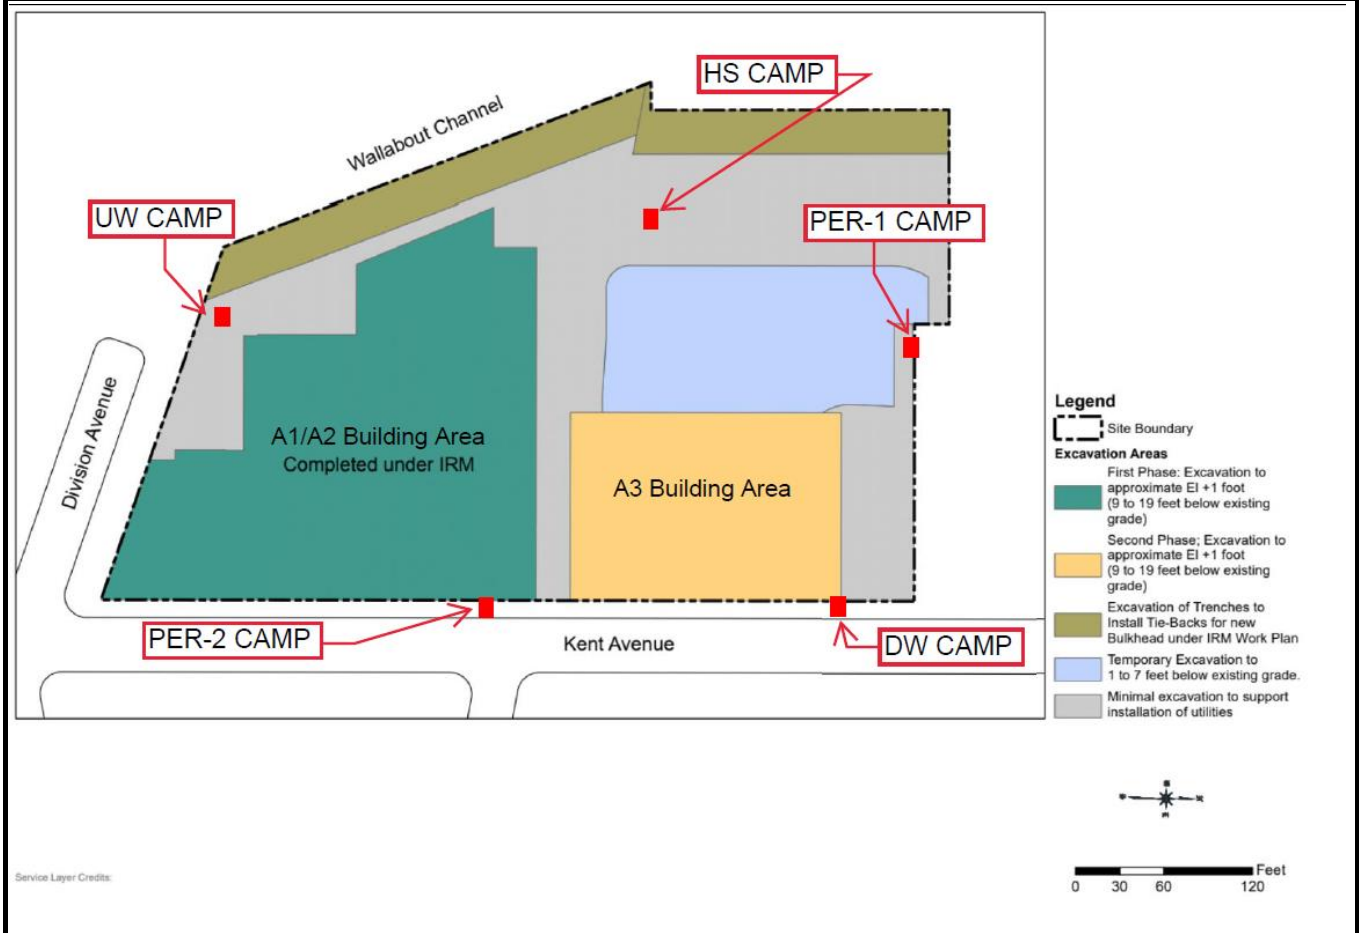

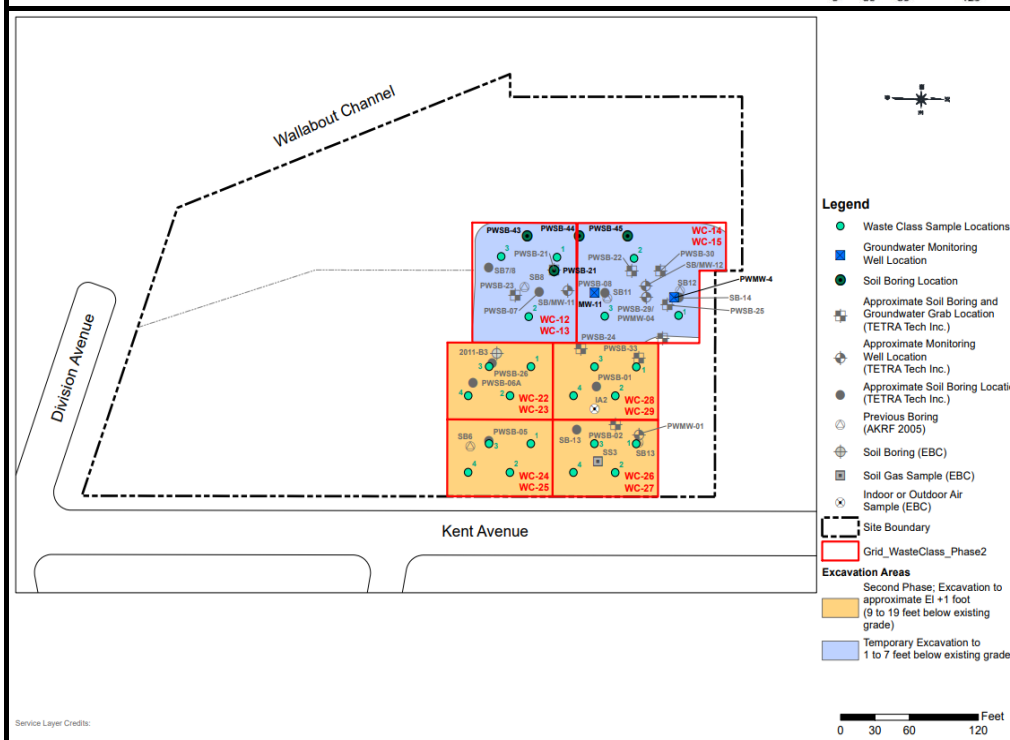
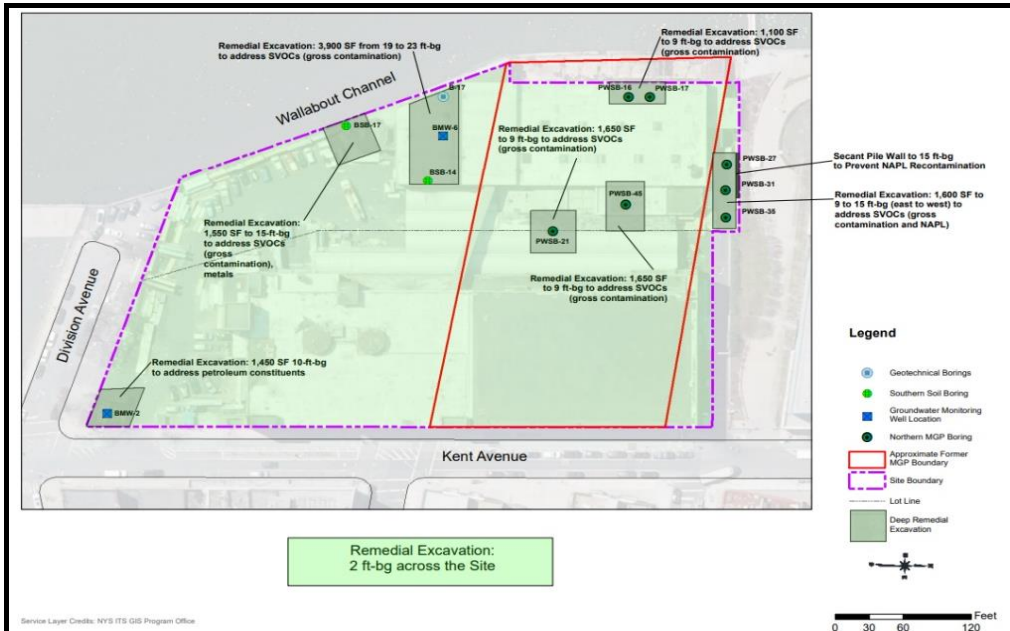


Photo 1:
View of Site conditions
and activities facing
southeast.

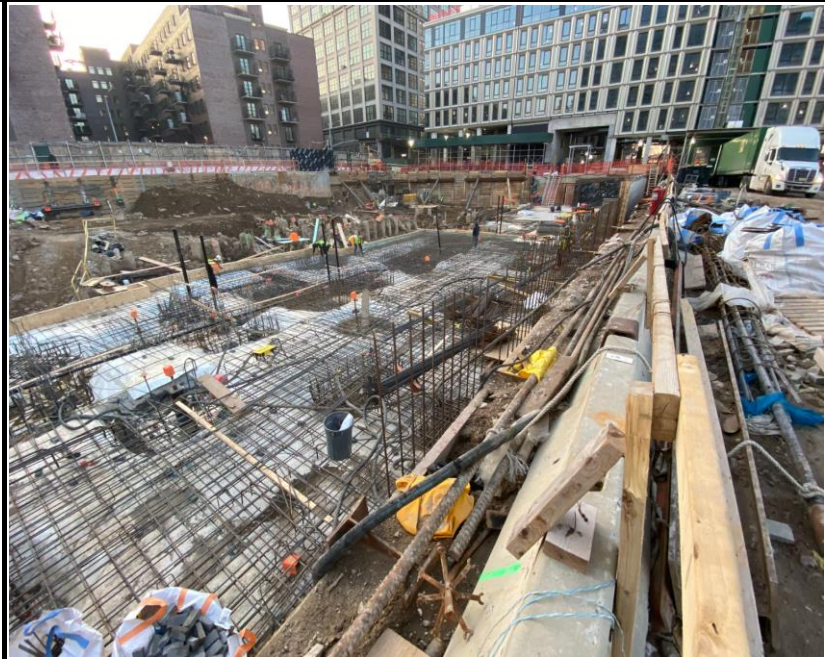


Photo 2:
View of Site conditions,
framing and rebar
installation.



Photo 3:
View of Site
conditions and
activities facing
northeast.




Photo 4:
View of the remedial
excavation.



CAMP:
Downwind
Particulates

Dust Levels


0.019 mg/m³ 0.028 mg/m³

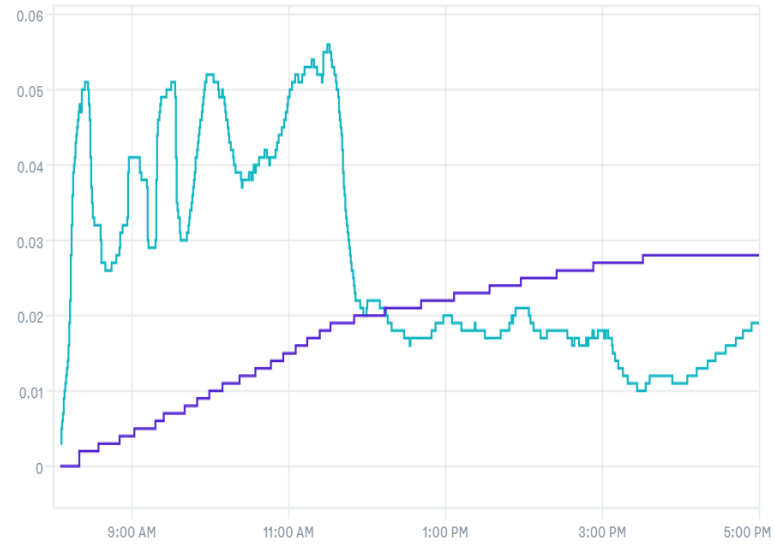

CAMP:
Downwind VOCs

VOC Levels

0.244 ppm 0.279 ppm

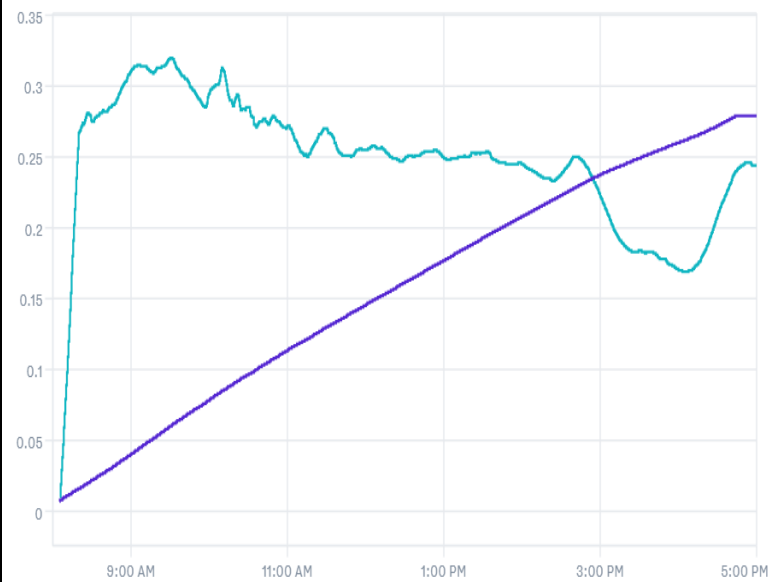


CAMP:
Upwind Particulates

Dust Levels

0.028 mg/m³

0.033 mg/m³

0.15

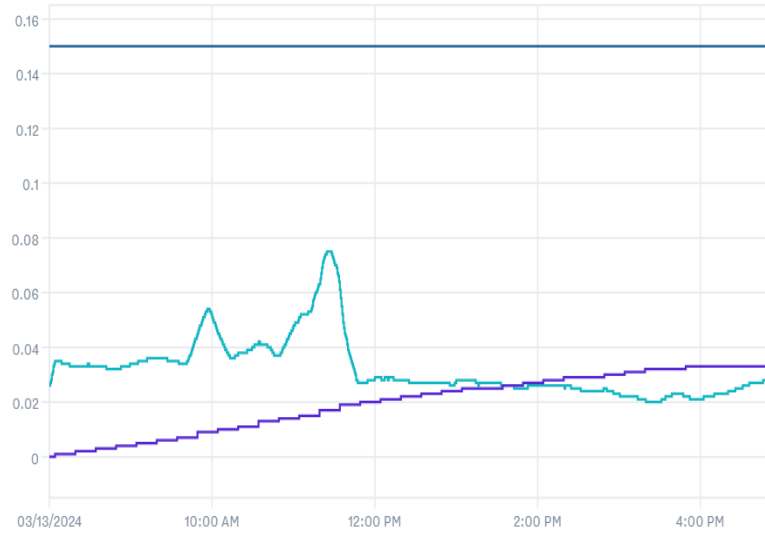


CAMP:
Upwind VOCs

VOC Levels

0.102 ppm

0.014 ppm

5

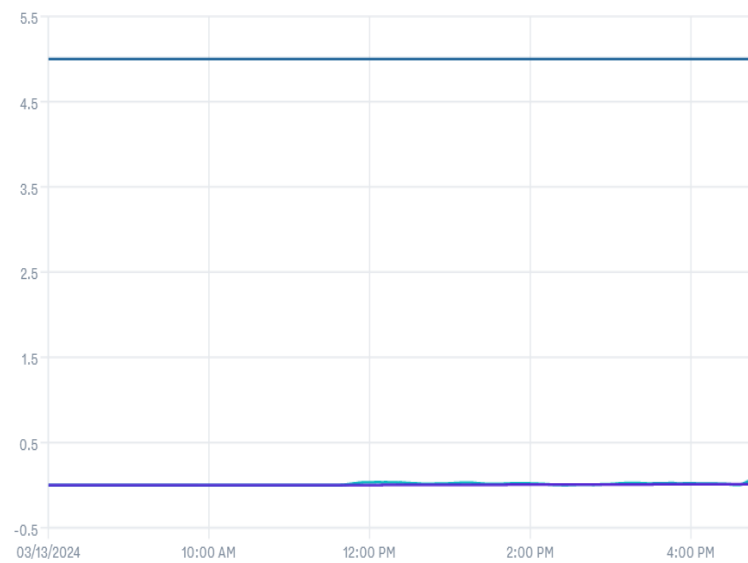

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/13/2024 9:00	3/13/2024 9:10	0.150	0.005	5	0.047
DW 2024	3/13/2024 9:10	3/13/2024 9:20	0.150	0.006	5	0.053
DW 2024	3/13/2024 9:20	3/13/2024 9:30	0.150	0.007	5	0.06
DW 2024	3/13/2024 9:30	3/13/2024 9:40	0.150	0.007	5	0.066
DW 2024	3/13/2024 9:40	3/13/2024 9:50	0.150	0.009	5	0.072
DW 2024	3/13/2024 9:50	3/13/2024 10:00	0.150	0.01	5	0.078
DW 2024	3/13/2024 10:00	3/13/2024 10:10	0.150	0.011	5	0.085
DW 2024	3/13/2024 10:10	3/13/2024 10:20	0.150	0.011	5	0.091
DW 2024	3/13/2024 10:20	3/13/2024 10:30	0.150	0.012	5	0.096
DW 2024	3/13/2024 10:30	3/13/2024 10:40	0.150	0.013	5	0.102
DW 2024	3/13/2024 10:40	3/13/2024 10:50	0.150	0.014	5	0.108
DW 2024	3/13/2024 10:50	3/13/2024 11:00	0.150	0.015	5	0.113
DW 2024	3/13/2024 11:00	3/13/2024 11:10	0.150	0.016	5	0.119
DW 2024	3/13/2024 11:10	3/13/2024 11:20	0.150	0.017	5	0.124
DW 2024	3/13/2024 11:20	3/13/2024 11:30	0.150	0.018	5	0.13
DW 2024	3/13/2024 11:30	3/13/2024 11:40	0.150	0.019	5	0.135
DW 2024	3/13/2024 11:40	3/13/2024 11:50	0.150	0.02	5	0.14
DW 2024	3/13/2024 11:50	3/13/2024 12:00	0.150	0.02	5	0.145
DW 2024	3/13/2024 12:00	3/13/2024 12:10	0.150	0.02	5	0.151
DW 2024	3/13/2024 12:10	3/13/2024 12:20	0.150	0.021	5	0.156
DW 2024	3/13/2024 12:20	3/13/2024 12:30	0.150	0.021	5	0.161
DW 2024	3/13/2024 12:30	3/13/2024 12:40	0.150	0.021	5	0.166
DW 2024	3/13/2024 12:40	3/13/2024 12:50	0.150	0.022	5	0.172
DW 2024	3/13/2024 12:50	3/13/2024 13:00	0.150	0.022	5	0.177
DW 2024	3/13/2024 13:00	3/13/2024 13:10	0.150	0.023	5	0.182
DW 2024	3/13/2024 13:10	3/13/2024 13:20	0.150	0.023	5	0.187
DW 2024	3/13/2024 13:20	3/13/2024 13:30	0.150	0.023	5	0.193
DW 2024	3/13/2024 13:30	3/13/2024 13:40	0.150	0.024	5	0.198
DW 2024	3/13/2024 13:40	3/13/2024 13:50	0.150	0.024	5	0.203
DW 2024	3/13/2024 13:50	3/13/2024 14:00	0.150	0.025	5	0.208
DW 2024	3/13/2024 14:00	3/13/2024 14:10	0.150	0.025	5	0.213
DW 2024	3/13/2024 14:10	3/13/2024 14:20	0.150	0.025	5	0.218
DW 2024	3/13/2024 14:20	3/13/2024 14:30	0.150	0.026	5	0.223
DW 2024	3/13/2024 14:30	3/13/2024 14:40	0.150	0.026	5	0.228
DW 2024	3/13/2024 14:40	3/13/2024 14:50	0.150	0.026	5	0.233
DW 2024	3/13/2024 14:50	3/13/2024 15:00	0.150	0.027	5	0.237
DW 2024	3/13/2024 15:00	3/13/2024 15:10	0.150	0.027	5	0.241
DW 2024	3/13/2024 15:10	3/13/2024 15:20	0.150	0.027	5	0.245
DW 2024	3/13/2024 15:20	3/13/2024 15:30	0.150	0.027	5	0.249
DW 2024	3/13/2024 15:30	3/13/2024 15:40	0.150	0.028	5	0.253
DW 2024	3/13/2024 15:40	3/13/2024 15:50	0.150	0.028	5	0.256
DW 2024	3/13/2024 15:50	3/13/2024 16:00	0.150	0.028	5	0.26
DW 2024	3/13/2024 16:00	3/13/2024 16:10	0.150	0.028	5	0.264
DW 2024	3/13/2024 16:10	3/13/2024 16:20	0.150	0.028	5	0.267
DW 2024	3/13/2024 16:20	3/13/2024 16:30	0.150	0.028	5	0.272
DW 2024	3/13/2024 16:30	3/13/2024 16:40	0.150	0.028	5	0.277
DW 2024	3/13/2024 16:40	3/13/2024 16:50	0.150	0.028	5	0.279
DW 2024	3/13/2024 16:50	3/13/2024 17:00	0.150	0.028	5	0.279

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/13/2024 9:10	3/13/2024 9:20	0.150	0.006	5	0
UW 2024	3/13/2024 9:20	3/13/2024 9:30	0.150	0.006	5	0
UW 2024	3/13/2024 9:30	3/13/2024 9:40	0.150	0.007	5	0
UW 2024	3/13/2024 9:40	3/13/2024 9:50	0.150	0.009	5	0
UW 2024	3/13/2024 9:50	3/13/2024 10:00	0.150	0.009	5	0
UW 2024	3/13/2024 10:00	3/13/2024 10:10	0.150	0.01	5	0
UW 2024	3/13/2024 10:10	3/13/2024 10:20	0.150	0.011	5	0
UW 2024	3/13/2024 10:20	3/13/2024 10:30	0.150	0.011	5	0
UW 2024	3/13/2024 10:30	3/13/2024 10:40	0.150	0.013	5	0
UW 2024	3/13/2024 10:40	3/13/2024 10:50	0.150	0.014	5	0
UW 2024	3/13/2024 10:50	3/13/2024 11:00	0.150	0.014	5	0
UW 2024	3/13/2024 11:00	3/13/2024 11:10	0.150	0.015	5	0
UW 2024	3/13/2024 11:10	3/13/2024 11:20	0.150	0.017	5	0
UW 2024	3/13/2024 11:20	3/13/2024 11:30	0.150	0.017	5	0
UW 2024	3/13/2024 11:30	3/13/2024 11:40	0.150	0.019	5	0
UW 2024	3/13/2024 11:40	3/13/2024 11:50	0.150	0.02	5	0
UW 2024	3/13/2024 11:50	3/13/2024 12:00	0.150	0.02	5	0.001
UW 2024	3/13/2024 12:00	3/13/2024 12:10	0.150	0.021	5	0.002
UW 2024	3/13/2024 12:10	3/13/2024 12:20	0.150	0.022	5	0.002
UW 2024	3/13/2024 12:20	3/13/2024 12:30	0.150	0.022	5	0.003
UW 2024	3/13/2024 12:30	3/13/2024 12:40	0.150	0.023	5	0.003
UW 2024	3/13/2024 12:40	3/13/2024 12:50	0.150	0.024	5	0.003
UW 2024	3/13/2024 12:50	3/13/2024 13:00	0.150	0.024	5	0.004
UW 2024	3/13/2024 13:00	3/13/2024 13:10	0.150	0.025	5	0.004
UW 2024	3/13/2024 13:10	3/13/2024 13:20	0.150	0.025	5	0.005
UW 2024	3/13/2024 13:20	3/13/2024 13:30	0.150	0.025	5	0.005
UW 2024	3/13/2024 13:30	3/13/2024 13:40	0.150	0.026	5	0.005
UW 2024	3/13/2024 13:40	3/13/2024 13:50	0.150	0.027	5	0.006
UW 2024	3/13/2024 13:50	3/13/2024 14:00	0.150	0.027	5	0.006
UW 2024	3/13/2024 14:00	3/13/2024 14:10	0.150	0.028	5	0.006
UW 2024	3/13/2024 14:10	3/13/2024 14:20	0.150	0.029	5	0.006
UW 2024	3/13/2024 14:20	3/13/2024 14:30	0.150	0.029	5	0.007
UW 2024	3/13/2024 14:30	3/13/2024 14:40	0.150	0.029	5	0.007
UW 2024	3/13/2024 14:40	3/13/2024 14:50	0.150	0.03	5	0.007
UW 2024	3/13/2024 14:50	3/13/2024 15:00	0.150	0.03	5	0.007
UW 2024	3/13/2024 15:00	3/13/2024 15:10	0.150	0.031	5	0.008
UW 2024	3/13/2024 15:10	3/13/2024 15:20	0.150	0.032	5	0.008
UW 2024	3/13/2024 15:20	3/13/2024 15:30	0.150	0.032	5	0.008
UW 2024	3/13/2024 15:30	3/13/2024 15:40	0.150	0.032	5	0.009
UW 2024	3/13/2024 15:40	3/13/2024 15:50	0.150	0.033	5	0.009
UW 2024	3/13/2024 15:50	3/13/2024 16:00	0.150	0.033	5	0.01
UW 2024	3/13/2024 16:00	3/13/2024 16:10	0.150	0.033	5	0.01
UW 2024	3/13/2024 16:10	3/13/2024 16:20	0.150	0.033	5	0.01
UW 2024	3/13/2024 16:20	3/13/2024 16:30	0.150	0.033	5	0.011
UW 2024	3/13/2024 16:30	3/13/2024 16:40	0.150	0.033	5	0.011
UW 2024	3/13/2024 16:40	3/13/2024 16:50	0.150	0.033	5	0.014
UW 2024	3/13/2024 16:50	3/13/2024 17:00	0.150	0.033	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/13/2024 9:00	3/13/2024 9:10	0.150	0.007	5	0
HS South	3/13/2024 9:10	3/13/2024 9:20	0.150	0.008	5	0
HS South	3/13/2024 9:20	3/13/2024 9:30	0.150	0.009	5	0
HS South	3/13/2024 9:30	3/13/2024 9:40	0.150	0.01	5	0
HS South	3/13/2024 9:40	3/13/2024 9:50	0.150	0.011	5	0
HS South	3/13/2024 9:50	3/13/2024 10:00	0.150	0.012	5	0
HS South	3/13/2024 10:00	3/13/2024 10:10	0.150	0.013	5	0
HS South	3/13/2024 10:10	3/13/2024 10:20	0.150	0.013	5	0
HS South	3/13/2024 10:20	3/13/2024 10:30	0.150	0.014	5	0
HS South	3/13/2024 10:30	3/13/2024 10:40	0.150	0.015	5	0
HS South	3/13/2024 10:40	3/13/2024 10:50	0.150	0.016	5	0
HS South	3/13/2024 10:50	3/13/2024 11:00	0.150	0.017	5	0
HS South	3/13/2024 11:00	3/13/2024 11:10	0.150	0.018	5	0
HS South	3/13/2024 11:10	3/13/2024 11:20	0.150	0.019	5	0
HS South	3/13/2024 11:20	3/13/2024 11:30	0.150	0.02	5	0
HS South	3/13/2024 11:30	3/13/2024 11:40	0.150	0.021	5	0
HS South	3/13/2024 11:40	3/13/2024 11:50	0.150	0.021	5	0
HS South	3/13/2024 11:50	3/13/2024 12:00	0.150	0.022	5	0
HS South	3/13/2024 12:00	3/13/2024 12:10	0.150	0.022	5	0
HS South	3/13/2024 12:10	3/13/2024 12:20	0.150	0.023	5	0
HS South	3/13/2024 12:20	3/13/2024 12:30	0.150	0.023	5	0
HS South	3/13/2024 12:30	3/13/2024 12:40	0.150	0.023	5	0
HS South	3/13/2024 12:40	3/13/2024 12:50	0.150	0.024	5	0
HS South	3/13/2024 12:50	3/13/2024 13:00	0.150	0.024	5	0
HS South	3/13/2024 13:00	3/13/2024 13:10	0.150	0.025	5	0
HS South	3/13/2024 13:10	3/13/2024 13:20	0.150	0.025	5	0
HS South	3/13/2024 13:20	3/13/2024 13:30	0.150	0.025	5	0
HS South	3/13/2024 13:30	3/13/2024 13:40	0.150	0.026	5	0
HS South	3/13/2024 13:40	3/13/2024 13:50	0.150	0.026	5	0
HS South	3/13/2024 13:50	3/13/2024 14:00	0.150	0.027	5	0
HS South	3/13/2024 14:00	3/13/2024 14:10	0.150	0.027	5	0
HS South	3/13/2024 14:10	3/13/2024 14:20	0.150	0.027	5	0
HS South	3/13/2024 14:20	3/13/2024 14:30	0.150	0.028	5	0
HS South	3/13/2024 14:30	3/13/2024 14:40	0.150	0.028	5	0
HS South	3/13/2024 14:40	3/13/2024 14:50	0.150	0.028	5	0
HS South	3/13/2024 14:50	3/13/2024 15:00	0.150	0.029	5	0
HS South	3/13/2024 15:00	3/13/2024 15:10	0.150	0.029	5	0
HS South	3/13/2024 15:10	3/13/2024 15:20	0.150	0.029	5	0
HS South	3/13/2024 15:20	3/13/2024 15:30	0.150	0.029	5	0
HS South	3/13/2024 15:30	3/13/2024 15:40	0.150	0.03	5	0
HS South	3/13/2024 15:40	3/13/2024 15:50	0.150	0.03	5	0
HS South	3/13/2024 15:50	3/13/2024 16:00	0.150	0.03	5	0
HS South	3/13/2024 16:00	3/13/2024 16:10	0.150	0.03	5	0
HS South	3/13/2024 16:10	3/13/2024 16:20	0.150	0.03	5	0
HS South	3/13/2024 16:20	3/13/2024 16:30	0.150	0.03	5	0
HS South	3/13/2024 16:30	3/13/2024 16:40	0.150	0.03	5	0
HS South	3/13/2024 16:40	3/13/2024 16:50	0.150	0.03	5	0
HS South	3/13/2024 16:50	3/13/2024 17:00	0.150	0.03	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/13/2024 9:00	3/13/2024 9:10	0.150	0.014	5	0.041
PER1 2024	3/13/2024 9:10	3/13/2024 9:20	0.150	0.015	5	0.041
PER1 2024	3/13/2024 9:20	3/13/2024 9:30	0.150	0.016	5	0.041
PER1 2024	3/13/2024 9:30	3/13/2024 9:40	0.150	0.017	5	0.041
PER1 2024	3/13/2024 9:40	3/13/2024 9:50	0.150	0.018	5	0.042
PER1 2024	3/13/2024 9:50	3/13/2024 10:00	0.150	0.02	5	0.042
PER1 2024	3/13/2024 10:00	3/13/2024 10:10	0.150	0.021	5	0.042
PER1 2024	3/13/2024 10:10	3/13/2024 10:20	0.150	0.022	5	0.042
PER1 2024	3/13/2024 10:20	3/13/2024 10:30	0.150	0.023	5	0.042
PER1 2024	3/13/2024 10:30	3/13/2024 10:40	0.150	0.024	5	0.042
PER1 2024	3/13/2024 10:40	3/13/2024 10:50	0.150	0.026	5	0.042
PER1 2024	3/13/2024 10:50	3/13/2024 11:00	0.150	0.027	5	0.042
PER1 2024	3/13/2024 11:00	3/13/2024 11:10	0.150	0.028	5	0.042
PER1 2024	3/13/2024 11:10	3/13/2024 11:20	0.150	0.03	5	0.042
PER1 2024	3/13/2024 11:20	3/13/2024 11:30	0.150	0.031	5	0.042
PER1 2024	3/13/2024 11:30	3/13/2024 11:40	0.150	0.033	5	0.042
PER1 2024	3/13/2024 11:40	3/13/2024 11:50	0.150	0.034	5	0.042
PER1 2024	3/13/2024 11:50	3/13/2024 12:00	0.150	0.035	5	0.042
PER1 2024	3/13/2024 12:00	3/13/2024 12:10	0.150	0.035	5	0.042
PER1 2024	3/13/2024 12:10	3/13/2024 12:20	0.150	0.036	5	0.042
PER1 2024	3/13/2024 12:20	3/13/2024 12:30	0.150	0.037	5	0.042
PER1 2024	3/13/2024 12:30	3/13/2024 12:40	0.150	0.038	5	0.042
PER1 2024	3/13/2024 12:40	3/13/2024 12:50	0.150	0.039	5	0.042
PER1 2024	3/13/2024 12:50	3/13/2024 13:00	0.150	0.04	5	0.042
PER1 2024	3/13/2024 13:00	3/13/2024 13:10	0.150	0.041	5	0.042
PER1 2024	3/13/2024 13:10	3/13/2024 13:20	0.150	0.042	5	0.042
PER1 2024	3/13/2024 13:20	3/13/2024 13:30	0.150	0.043	5	0.042
PER1 2024	3/13/2024 13:30	3/13/2024 13:40	0.150	0.044	5	0.042
PER1 2024	3/13/2024 13:40	3/13/2024 13:50	0.150	0.045	5	0.042
PER1 2024	3/13/2024 13:50	3/13/2024 14:00	0.150	0.046	5	0.042
PER1 2024	3/13/2024 14:00	3/13/2024 14:10	0.150	0.047	5	0.042
PER1 2024	3/13/2024 14:10	3/13/2024 14:20	0.150	0.048	5	0.042
PER1 2024	3/13/2024 14:20	3/13/2024 14:30	0.150	0.049	5	0.042
PER1 2024	3/13/2024 14:30	3/13/2024 14:40	0.150	0.05	5	0.042
PER1 2024	3/13/2024 14:40	3/13/2024 14:50	0.150	0.051	5	0.042
PER1 2024	3/13/2024 14:50	3/13/2024 15:00	0.150	0.051	5	0.042
PER1 2024	3/13/2024 15:00	3/13/2024 15:10	0.150	0.052	5	0.042
PER1 2024	3/13/2024 15:10	3/13/2024 15:20	0.150	0.053	5	0.042
PER1 2024	3/13/2024 15:20	3/13/2024 15:30	0.150	0.053	5	0.042
PER1 2024	3/13/2024 15:30	3/13/2024 15:40	0.150	0.053	5	0.042
PER1 2024	3/13/2024 15:40	3/13/2024 15:50	0.150	0.053	5	0.042
PER1 2024	3/13/2024 15:50	3/13/2024 16:00	0.150	0.053	5	0.042
PER1 2024	3/13/2024 16:00	3/13/2024 16:10	0.150	0.053	5	0.042
PER1 2024	3/13/2024 16:10	3/13/2024 16:20	0.150	0.053	5	0.042
PER1 2024	3/13/2024 16:20	3/13/2024 16:30	0.150	0.053	5	0.042
PER1 2024	3/13/2024 16:30	3/13/2024 16:40	0.150	0.053	5	0
PER1 2024	3/13/2024 16:40	3/13/2024 16:50	0.150	0	5	0
PER1 2024	3/13/2024 16:50	3/13/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/13/2024 9:00	3/13/2024 9:10	0.150	0.006	5	0.017
PER2 2024	3/13/2024 9:10	3/13/2024 9:20	0.150	0.007	5	0.02
PER2 2024	3/13/2024 9:20	3/13/2024 9:30	0.150	0.008	5	0.023
PER2 2024	3/13/2024 9:30	3/13/2024 9:40	0.150	0.009	5	0.025
PER2 2024	3/13/2024 9:40	3/13/2024 9:50	0.150	0.01	5	0.027
PER2 2024	3/13/2024 9:50	3/13/2024 10:00	0.150	0.012	5	0.03
PER2 2024	3/13/2024 10:00	3/13/2024 10:10	0.150	0.013	5	0.032
PER2 2024	3/13/2024 10:10	3/13/2024 10:20	0.150	0.014	5	0.035
PER2 2024	3/13/2024 10:20	3/13/2024 10:30	0.150	0.015	5	0.036
PER2 2024	3/13/2024 10:30	3/13/2024 10:40	0.150	0.016	5	0.037
PER2 2024	3/13/2024 10:40	3/13/2024 10:50	0.150	0.017	5	0.038
PER2 2024	3/13/2024 10:50	3/13/2024 11:00	0.150	0.019	5	0.04
PER2 2024	3/13/2024 11:00	3/13/2024 11:10	0.150	0.02	5	0.041
PER2 2024	3/13/2024 11:10	3/13/2024 11:20	0.150	0.022	5	0.043
PER2 2024	3/13/2024 11:20	3/13/2024 11:30	0.150	0.024	5	0.045
PER2 2024	3/13/2024 11:30	3/13/2024 11:40	0.150	0.025	5	0.046
PER2 2024	3/13/2024 11:40	3/13/2024 11:50	0.150	0.026	5	0.046
PER2 2024	3/13/2024 11:50	3/13/2024 12:00	0.150	0.026	5	0.046
PER2 2024	3/13/2024 12:00	3/13/2024 12:10	0.150	0.027	5	0.046
PER2 2024	3/13/2024 12:10	3/13/2024 12:20	0.150	0.027	5	0.046
PER2 2024	3/13/2024 12:20	3/13/2024 12:30	0.150	0.028	5	0.046
PER2 2024	3/13/2024 12:30	3/13/2024 12:40	0.150	0.029	5	0.046
PER2 2024	3/13/2024 12:40	3/13/2024 12:50	0.150	0.029	5	0.046
PER2 2024	3/13/2024 12:50	3/13/2024 13:00	0.150	0.03	5	0.046
PER2 2024	3/13/2024 13:00	3/13/2024 13:10	0.150	0.03	5	0.046
PER2 2024	3/13/2024 13:10	3/13/2024 13:20	0.150	0.031	5	0.046
PER2 2024	3/13/2024 13:20	3/13/2024 13:30	0.150	0.031	5	0.046
PER2 2024	3/13/2024 13:30	3/13/2024 13:40	0.150	0.032	5	0.046
PER2 2024	3/13/2024 13:40	3/13/2024 13:50	0.150	0.032	5	0.046
PER2 2024	3/13/2024 13:50	3/13/2024 14:00	0.150	0.033	5	0.046
PER2 2024	3/13/2024 14:00	3/13/2024 14:10	0.150	0.034	5	0.046
PER2 2024	3/13/2024 14:10	3/13/2024 14:20	0.150	0.034	5	0.046
PER2 2024	3/13/2024 14:20	3/13/2024 14:30	0.150	0.035	5	0.046
PER2 2024	3/13/2024 14:30	3/13/2024 14:40	0.150	0.035	5	0.046
PER2 2024	3/13/2024 14:40	3/13/2024 14:50	0.150	0.035	5	0.046
PER2 2024	3/13/2024 14:50	3/13/2024 15:00	0.150	0.036	5	0.046
PER2 2024	3/13/2024 15:00	3/13/2024 15:10	0.150	0.036	5	0.046
PER2 2024	3/13/2024 15:10	3/13/2024 15:20	0.150	0.037	5	0.046
PER2 2024	3/13/2024 15:20	3/13/2024 15:30	0.150	0.037	5	0.046
PER2 2024	3/13/2024 15:30	3/13/2024 15:40	0.150	0.037	5	0.046
PER2 2024	3/13/2024 15:40	3/13/2024 15:50	0.150	0.038	5	0.046
PER2 2024	3/13/2024 15:50	3/13/2024 16:00	0.150	0.038	5	0.046
PER2 2024	3/13/2024 16:00	3/13/2024 16:10	0.150	0.038	5	0.046
PER2 2024	3/13/2024 16:10	3/13/2024 16:20	0.150	0.038	5	0.046
PER2 2024	3/13/2024 16:20	3/13/2024 16:30	0.150	0.038	5	0.046
PER2 2024	3/13/2024 16:30	3/13/2024 16:40	0.150	0.038	5	0.046
PER2 2024	3/13/2024 16:40	3/13/2024 16:50	0.150	0.038	5	0.046
PER2 2024	3/13/2024 16:50	3/13/2024 17:00	0.150	0.038	5	0.046
UW 2024	3/13/2024 9:00	3/13/2024 9:10	0.150	0.005	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/14/2024

Weather: 50 deg. F, Sunny

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation.
- 2) ECD was not on-Site and no work was completed on the waterfront remedial excavation. The HS CAMP station was not set up, see details below.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP tables and graphs are included below. The HS dustrak experienced operational issues and was maintained by the field personnel.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and pile installation. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3965	0	6965	1520	2220

Site Layout Map and Excavation Figures

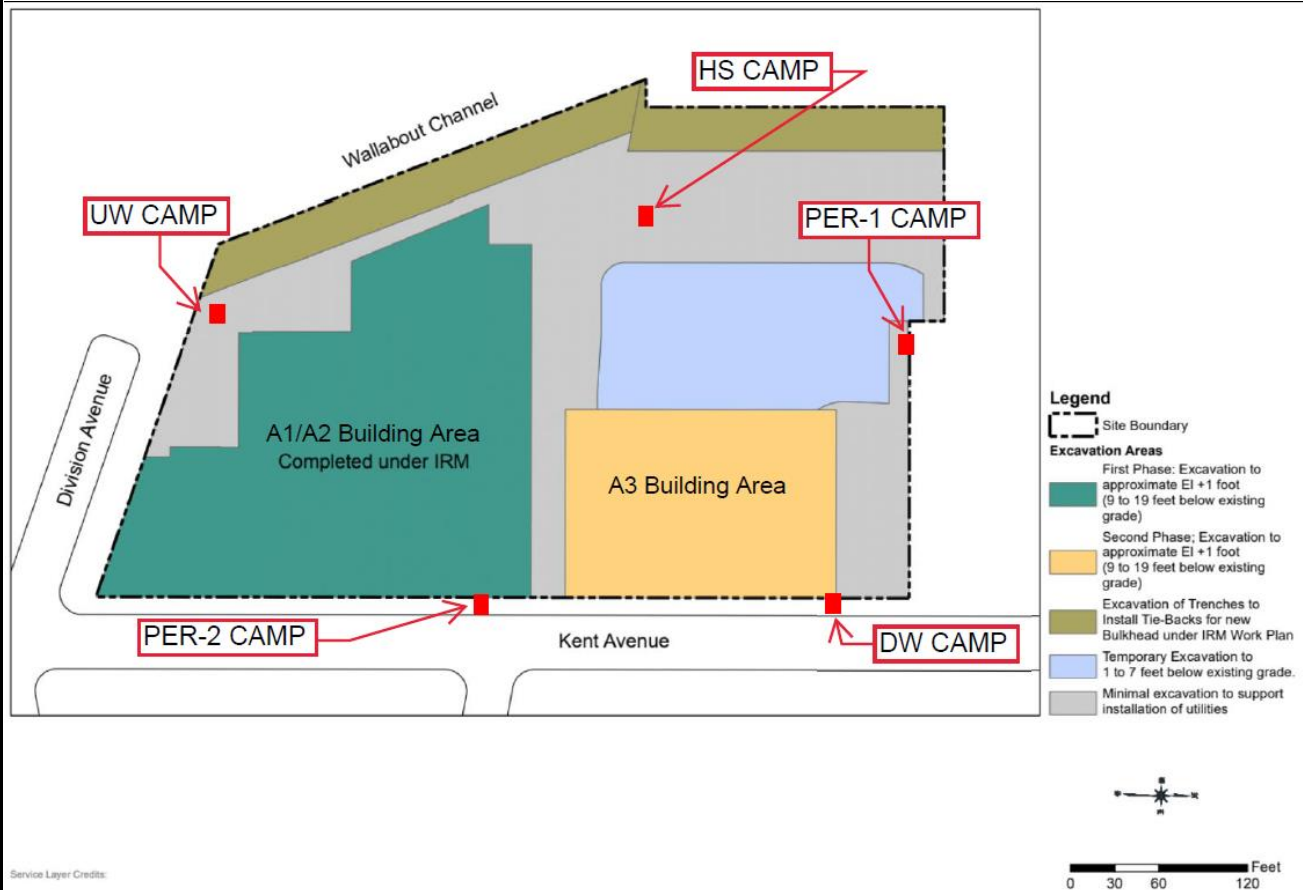

Service Layer Credits:

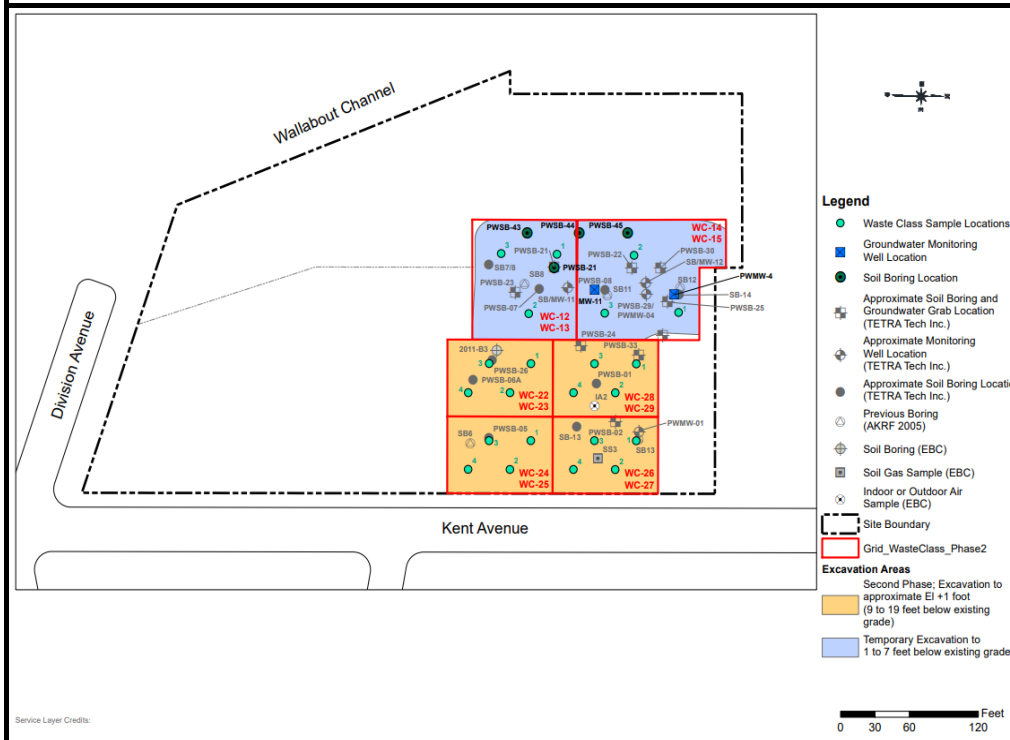
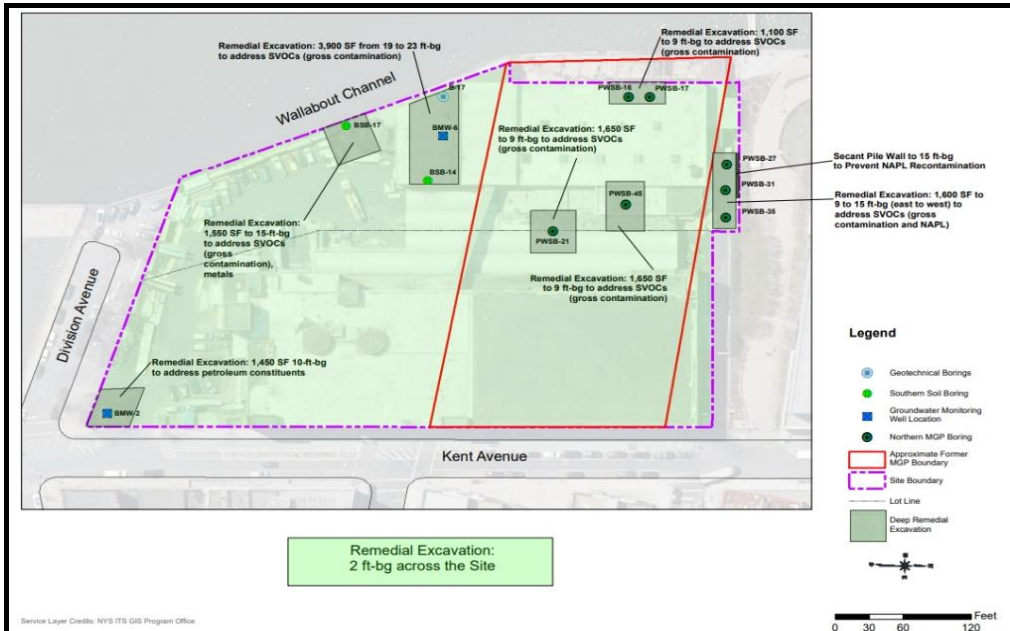


Photo 1:
View of Site conditions
and activities facing
south.



Photo 2:
View of Site conditions
facing north.

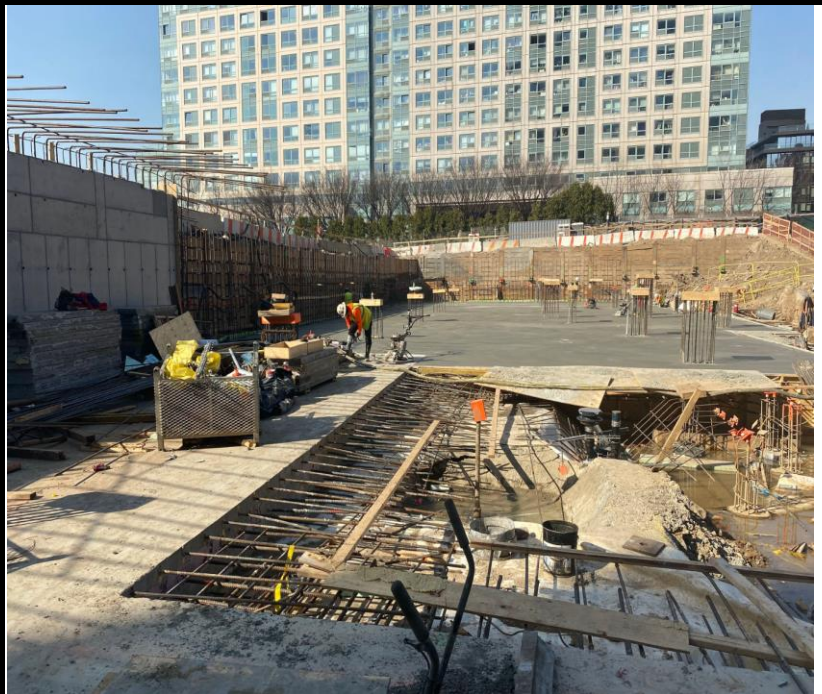


Photo 3:
View of concrete
pouring for building
foundation
development, facing
south.




Photo 4:
View of soil
excavation and SOE
installation facing
east.



CAMP:
Downwind
Particulates

Dust Levels


0.056 mg/m³ 0.074 mg/m³

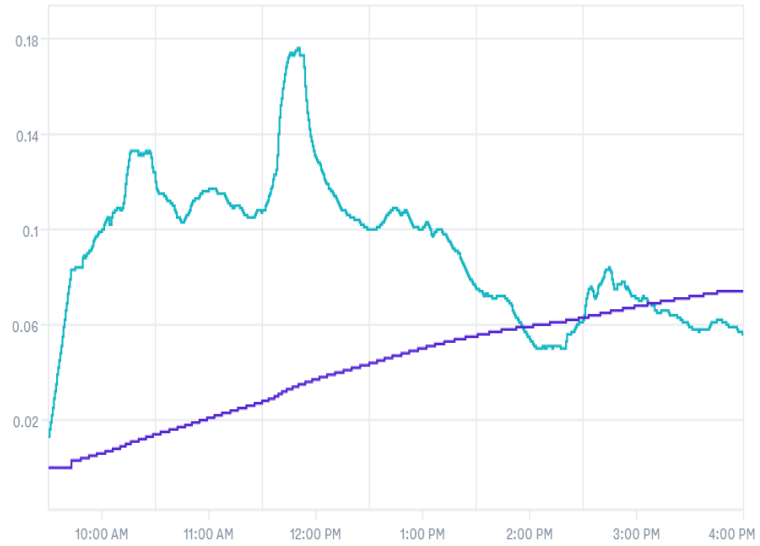

CAMP:
Downwind VOCs

VOC Levels


0.278 ppm 0.193 ppm

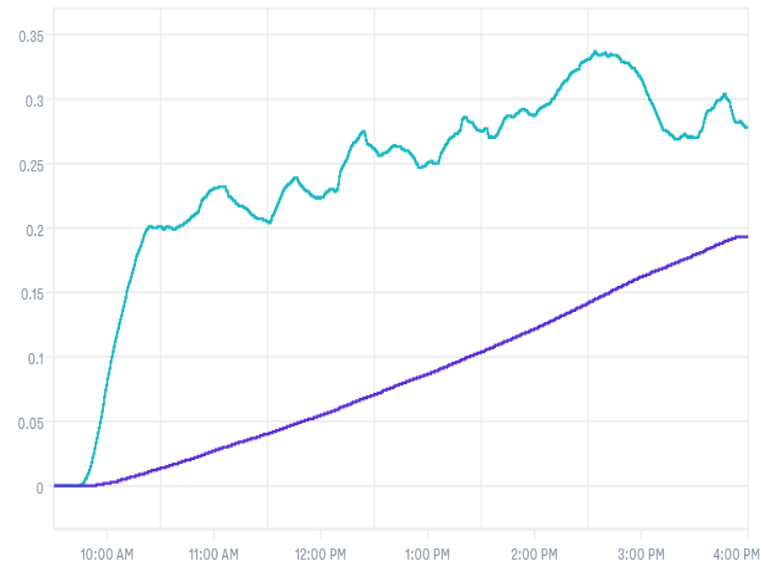

CAMP:
Upwind Particulates

Dust Levels


0.055 mg/m³ 0.057 mg/m³ 0.15

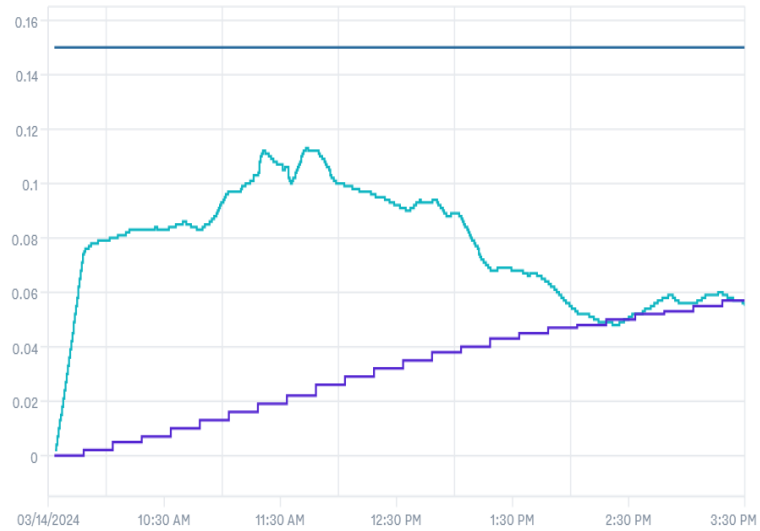

CAMP:
Upwind VOCs

VOC Levels

0.171 ppm 0.08 ppm 5

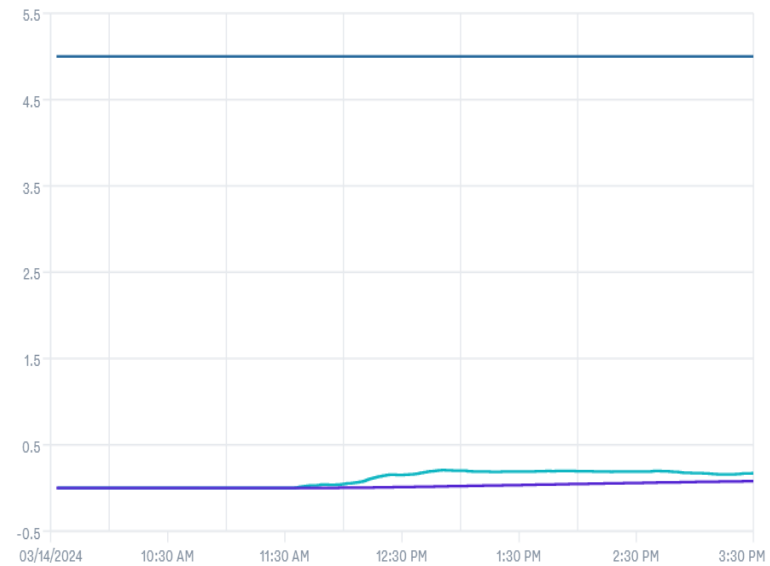

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/14/2024 9:40	3/14/2024 9:50	0.150	0.004	5	0
DW 2024	3/14/2024 9:50	3/14/2024 10:00	0.150	0.006	5	0.002
DW 2024	3/14/2024 10:00	3/14/2024 10:10	0.150	0.008	5	0.005
DW 2024	3/14/2024 10:10	3/14/2024 10:20	0.150	0.011	5	0.009
DW 2024	3/14/2024 10:20	3/14/2024 10:30	0.150	0.014	5	0.014
DW 2024	3/14/2024 10:30	3/14/2024 10:40	0.150	0.016	5	0.018
DW 2024	3/14/2024 10:40	3/14/2024 10:50	0.150	0.018	5	0.022
DW 2024	3/14/2024 10:50	3/14/2024 11:00	0.150	0.021	5	0.027
DW 2024	3/14/2024 11:00	3/14/2024 11:10	0.150	0.023	5	0.032
DW 2024	3/14/2024 11:10	3/14/2024 11:20	0.150	0.025	5	0.036
DW 2024	3/14/2024 11:20	3/14/2024 11:30	0.150	0.028	5	0.04
DW 2024	3/14/2024 11:30	3/14/2024 11:40	0.150	0.031	5	0.045
DW 2024	3/14/2024 11:40	3/14/2024 11:50	0.150	0.034	5	0.05
DW 2024	3/14/2024 11:50	3/14/2024 12:00	0.150	0.037	5	0.055
DW 2024	3/14/2024 12:00	3/14/2024 12:10	0.150	0.039	5	0.06
DW 2024	3/14/2024 12:10	3/14/2024 12:20	0.150	0.041	5	0.066
DW 2024	3/14/2024 12:20	3/14/2024 12:30	0.150	0.044	5	0.071
DW 2024	3/14/2024 12:30	3/14/2024 12:40	0.150	0.046	5	0.076
DW 2024	3/14/2024 12:40	3/14/2024 12:50	0.150	0.048	5	0.082
DW 2024	3/14/2024 12:50	3/14/2024 13:00	0.150	0.05	5	0.087
DW 2024	3/14/2024 13:00	3/14/2024 13:10	0.150	0.052	5	0.092
DW 2024	3/14/2024 13:10	3/14/2024 13:20	0.150	0.054	5	0.098
DW 2024	3/14/2024 13:20	3/14/2024 13:30	0.150	0.055	5	0.104
DW 2024	3/14/2024 13:30	3/14/2024 13:40	0.150	0.057	5	0.11
DW 2024	3/14/2024 13:40	3/14/2024 13:50	0.150	0.058	5	0.116
DW 2024	3/14/2024 13:50	3/14/2024 14:00	0.150	0.059	5	0.122
DW 2024	3/14/2024 14:00	3/14/2024 14:10	0.150	0.06	5	0.128
DW 2024	3/14/2024 14:10	3/14/2024 14:20	0.150	0.061	5	0.135
DW 2024	3/14/2024 14:20	3/14/2024 14:30	0.150	0.063	5	0.142
DW 2024	3/14/2024 14:30	3/14/2024 14:40	0.150	0.065	5	0.149
DW 2024	3/14/2024 14:40	3/14/2024 14:50	0.150	0.066	5	0.156
DW 2024	3/14/2024 14:50	3/14/2024 15:00	0.150	0.068	5	0.162
DW 2024	3/14/2024 15:00	3/14/2024 15:10	0.150	0.069	5	0.168
DW 2024	3/14/2024 15:10	3/14/2024 15:20	0.150	0.07	5	0.173
DW 2024	3/14/2024 15:20	3/14/2024 15:30	0.150	0.072	5	0.179
DW 2024	3/14/2024 15:30	3/14/2024 15:40	0.150	0.073	5	0.185
DW 2024	3/14/2024 15:40	3/14/2024 15:50	0.150	0.074	5	0.191
DW 2024	3/14/2024 15:50	3/14/2024 16:00	0.150	0.074	5	0.193

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/14/2024 9:40	3/14/2024 9:50	0.150	0.002	5	0
UW 2024	3/14/2024 9:50	3/14/2024 10:00	0.150	0.002	5	0
UW 2024	3/14/2024 10:00	3/14/2024 10:10	0.150	0.005	5	0
UW 2024	3/14/2024 10:10	3/14/2024 10:20	0.150	0.007	5	0
UW 2024	3/14/2024 10:20	3/14/2024 10:30	0.150	0.007	5	0
UW 2024	3/14/2024 10:30	3/14/2024 10:40	0.150	0.01	5	0
UW 2024	3/14/2024 10:40	3/14/2024 10:50	0.150	0.013	5	0
UW 2024	3/14/2024 10:50	3/14/2024 11:00	0.150	0.013	5	0
UW 2024	3/14/2024 11:00	3/14/2024 11:10	0.150	0.016	5	0
UW 2024	3/14/2024 11:10	3/14/2024 11:20	0.150	0.019	5	0
UW 2024	3/14/2024 11:20	3/14/2024 11:30	0.150	0.019	5	0
UW 2024	3/14/2024 11:30	3/14/2024 11:40	0.150	0.022	5	0
UW 2024	3/14/2024 11:40	3/14/2024 11:50	0.150	0.026	5	0.001
UW 2024	3/14/2024 11:50	3/14/2024 12:00	0.150	0.026	5	0.002
UW 2024	3/14/2024 12:00	3/14/2024 12:10	0.150	0.029	5	0.004
UW 2024	3/14/2024 12:10	3/14/2024 12:20	0.150	0.032	5	0.007
UW 2024	3/14/2024 12:20	3/14/2024 12:30	0.150	0.032	5	0.01
UW 2024	3/14/2024 12:30	3/14/2024 12:40	0.150	0.035	5	0.014
UW 2024	3/14/2024 12:40	3/14/2024 12:50	0.150	0.038	5	0.018
UW 2024	3/14/2024 12:50	3/14/2024 13:00	0.150	0.038	5	0.022
UW 2024	3/14/2024 13:00	3/14/2024 13:10	0.150	0.04	5	0.026
UW 2024	3/14/2024 13:10	3/14/2024 13:20	0.150	0.043	5	0.03
UW 2024	3/14/2024 13:20	3/14/2024 13:30	0.150	0.043	5	0.034
UW 2024	3/14/2024 13:30	3/14/2024 13:40	0.150	0.045	5	0.038
UW 2024	3/14/2024 13:40	3/14/2024 13:50	0.150	0.047	5	0.042
UW 2024	3/14/2024 13:50	3/14/2024 14:00	0.150	0.047	5	0.046
UW 2024	3/14/2024 14:00	3/14/2024 14:10	0.150	0.048	5	0.05
UW 2024	3/14/2024 14:10	3/14/2024 14:20	0.150	0.05	5	0.054
UW 2024	3/14/2024 14:20	3/14/2024 14:30	0.150	0.05	5	0.058
UW 2024	3/14/2024 14:30	3/14/2024 14:40	0.150	0.052	5	0.062
UW 2024	3/14/2024 14:40	3/14/2024 14:50	0.150	0.053	5	0.066
UW 2024	3/14/2024 14:50	3/14/2024 15:00	0.150	0.053	5	0.069
UW 2024	3/14/2024 15:00	3/14/2024 15:10	0.150	0.055	5	0.073
UW 2024	3/14/2024 15:10	3/14/2024 15:20	0.150	0.057	5	0.076
UW 2024	3/14/2024 15:20	3/14/2024 15:30	0.150	0.057	5	0.08
UW 2024	3/14/2024 15:30	3/14/2024 15:40	0.150	0.059	5	0.083
UW 2024	3/14/2024 15:40	3/14/2024 15:50	0.150	0.059	5	0
UW 2024	3/14/2024 15:50	3/14/2024 16:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/14/2024 9:50	3/14/2024 10:00	0.150	0.005	5	0
PER1 2024	3/14/2024 10:00	3/14/2024 10:10	0.150	0.007	5	0
PER1 2024	3/14/2024 10:10	3/14/2024 10:20	0.150	0.009	5	0
PER1 2024	3/14/2024 10:20	3/14/2024 10:30	0.150	0.011	5	0
PER1 2024	3/14/2024 10:30	3/14/2024 10:40	0.150	0.013	5	0
PER1 2024	3/14/2024 10:40	3/14/2024 10:50	0.150	0.015	5	0
PER1 2024	3/14/2024 10:50	3/14/2024 11:00	0.150	0.017	5	0
PER1 2024	3/14/2024 11:00	3/14/2024 11:10	0.150	0.02	5	0
PER1 2024	3/14/2024 11:10	3/14/2024 11:20	0.150	0.022	5	0
PER1 2024	3/14/2024 11:20	3/14/2024 11:30	0.150	0.024	5	0
PER1 2024	3/14/2024 11:30	3/14/2024 11:40	0.150	0.027	5	0
PER1 2024	3/14/2024 11:40	3/14/2024 11:50	0.150	0.029	5	0
PER1 2024	3/14/2024 11:50	3/14/2024 12:00	0.150	0.032	5	0
PER1 2024	3/14/2024 12:00	3/14/2024 12:10	0.150	0.035	5	0
PER1 2024	3/14/2024 12:10	3/14/2024 12:20	0.150	0.037	5	0
PER1 2024	3/14/2024 12:20	3/14/2024 12:30	0.150	0.039	5	0.001
PER1 2024	3/14/2024 12:30	3/14/2024 12:40	0.150	0.042	5	0.001
PER1 2024	3/14/2024 12:40	3/14/2024 12:50	0.150	0.045	5	0.001
PER1 2024	3/14/2024 12:50	3/14/2024 13:00	0.150	0.047	5	0.001
PER1 2024	3/14/2024 13:00	3/14/2024 13:10	0.150	0.049	5	0.001
PER1 2024	3/14/2024 13:10	3/14/2024 13:20	0.150	0.051	5	0.001
PER1 2024	3/14/2024 13:20	3/14/2024 13:30	0.150	0.053	5	0.001
PER1 2024	3/14/2024 13:30	3/14/2024 13:40	0.150	0.055	5	0.001
PER1 2024	3/14/2024 13:40	3/14/2024 13:50	0.150	0.057	5	0.001
PER1 2024	3/14/2024 13:50	3/14/2024 14:00	0.150	0.058	5	0.001
PER1 2024	3/14/2024 14:00	3/14/2024 14:10	0.150	0.06	5	0.001
PER1 2024	3/14/2024 14:10	3/14/2024 14:20	0.150	0.061	5	0.001
PER1 2024	3/14/2024 14:20	3/14/2024 14:30	0.150	0.063	5	0.001
PER1 2024	3/14/2024 14:30	3/14/2024 14:40	0.150	0.065	5	0.001
PER1 2024	3/14/2024 14:40	3/14/2024 14:50	0.150	0.066	5	0.001
PER1 2024	3/14/2024 14:50	3/14/2024 15:00	0.150	0.068	5	0.001
PER1 2024	3/14/2024 15:00	3/14/2024 15:10	0.150	0.07	5	0.001
PER1 2024	3/14/2024 15:10	3/14/2024 15:20	0.150	0.071	5	0.001
PER1 2024	3/14/2024 15:20	3/14/2024 15:30	0.150	0.073	5	0.001
PER1 2024	3/14/2024 15:30	3/14/2024 15:40	0.150	0.075	5	0.001
PER1 2024	3/14/2024 15:40	3/14/2024 15:50	0.150	0.076	5	0
PER1 2024	3/14/2024 15:50	3/14/2024 16:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/14/2024 9:40	3/14/2024 9:50	0.150	0.004	5	0
PER2 2024	3/14/2024 9:50	3/14/2024 10:00	0.150	0.006	5	0
PER2 2024	3/14/2024 10:00	3/14/2024 10:10	0.150	0.009	5	0
PER2 2024	3/14/2024 10:10	3/14/2024 10:20	0.150	0.012	5	0
PER2 2024	3/14/2024 10:20	3/14/2024 10:30	0.150	0.014	5	0
PER2 2024	3/14/2024 10:30	3/14/2024 10:40	0.150	0.017	5	0
PER2 2024	3/14/2024 10:40	3/14/2024 10:50	0.150	0.02	5	0
PER2 2024	3/14/2024 10:50	3/14/2024 11:00	0.150	0.022	5	0
PER2 2024	3/14/2024 11:00	3/14/2024 11:10	0.150	0.025	5	0
PER2 2024	3/14/2024 11:10	3/14/2024 11:20	0.150	0.027	5	0
PER2 2024	3/14/2024 11:20	3/14/2024 11:30	0.150	0.03	5	0
PER2 2024	3/14/2024 11:30	3/14/2024 11:40	0.150	0.035	5	0.001
PER2 2024	3/14/2024 11:40	3/14/2024 11:50	0.150	0.04	5	0.001
PER2 2024	3/14/2024 11:50	3/14/2024 12:00	0.150	0.043	5	0.001
PER2 2024	3/14/2024 12:00	3/14/2024 12:10	0.150	0.046	5	0.001
PER2 2024	3/14/2024 12:10	3/14/2024 12:20	0.150	0.049	5	0.004
PER2 2024	3/14/2024 12:20	3/14/2024 12:30	0.150	0.052	5	0.007
PER2 2024	3/14/2024 12:30	3/14/2024 12:40	0.150	0.055	5	0.01
PER2 2024	3/14/2024 12:40	3/14/2024 12:50	0.150	0.057	5	0.013
PER2 2024	3/14/2024 12:50	3/14/2024 13:00	0.150	0.06	5	0.019
PER2 2024	3/14/2024 13:00	3/14/2024 13:10	0.150	0.062	5	0.024
PER2 2024	3/14/2024 13:10	3/14/2024 13:20	0.150	0.065	5	0.03
PER2 2024	3/14/2024 13:20	3/14/2024 13:30	0.150	0.067	5	0.039
PER2 2024	3/14/2024 13:30	3/14/2024 13:40	0.150	0.07	5	0.045
PER2 2024	3/14/2024 13:40	3/14/2024 13:50	0.150	0.072	5	0.047
PER2 2024	3/14/2024 13:50	3/14/2024 14:00	0.150	0.074	5	0.049
PER2 2024	3/14/2024 14:00	3/14/2024 14:10	0.150	0.077	5	0.053
PER2 2024	3/14/2024 14:10	3/14/2024 14:20	0.150	0.08	5	0.061
PER2 2024	3/14/2024 14:20	3/14/2024 14:30	0.150	0.082	5	0.067
PER2 2024	3/14/2024 14:30	3/14/2024 14:40	0.150	0.084	5	0.071
PER2 2024	3/14/2024 14:40	3/14/2024 14:50	0.150	0.087	5	0.079
PER2 2024	3/14/2024 14:50	3/14/2024 15:00	0.150	0.089	5	0.084
PER2 2024	3/14/2024 15:00	3/14/2024 15:10	0.150	0.091	5	0.089
PER2 2024	3/14/2024 15:10	3/14/2024 15:20	0.150	0.093	5	0.093
PER2 2024	3/14/2024 15:20	3/14/2024 15:30	0.150	0.095	5	0.095
PER2 2024	3/14/2024 15:30	3/14/2024 15:40	0.150	0.096	5	0.097
PER2 2024	3/14/2024 15:40	3/14/2024 15:50	0.150	0.098	5	0.098
PER2 2024	3/14/2024 15:50	3/14/2024 16:00	0.150	0.098	5	0.098

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/15/2024

Weather: 50 deg. F, Overcast/Rain


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation. 2) Import of 2 loads of 2.5" stone 3) ECD was not on-Site and no work was completed on the waterfront remedial excavation. Excavation is planned to resume on Monday, 3/18.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP tables and graphs are included below. CAMP stations were turned on at approximately 945AM following rain.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3965	0	6965	1520	2220

Site Layout Map and Excavation Figures

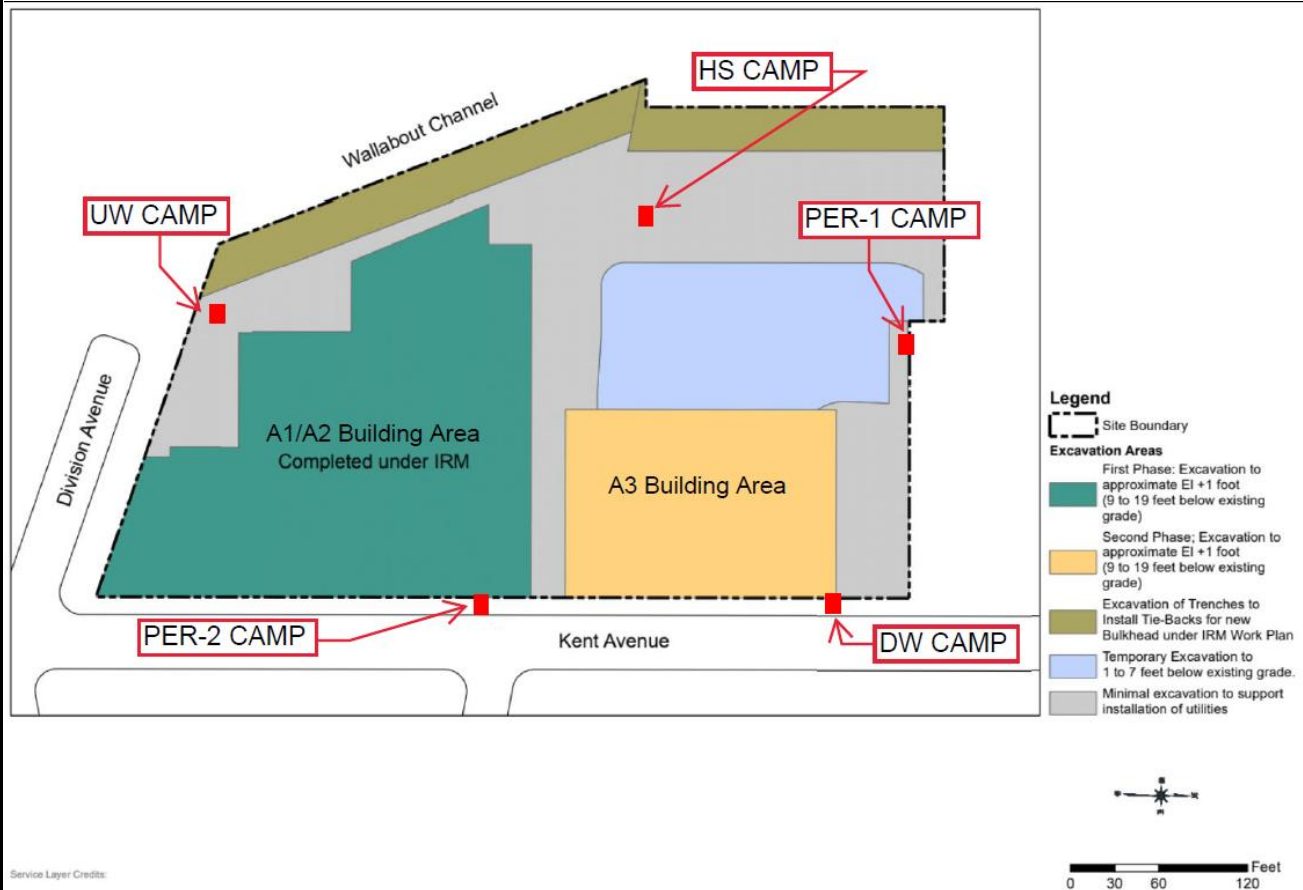

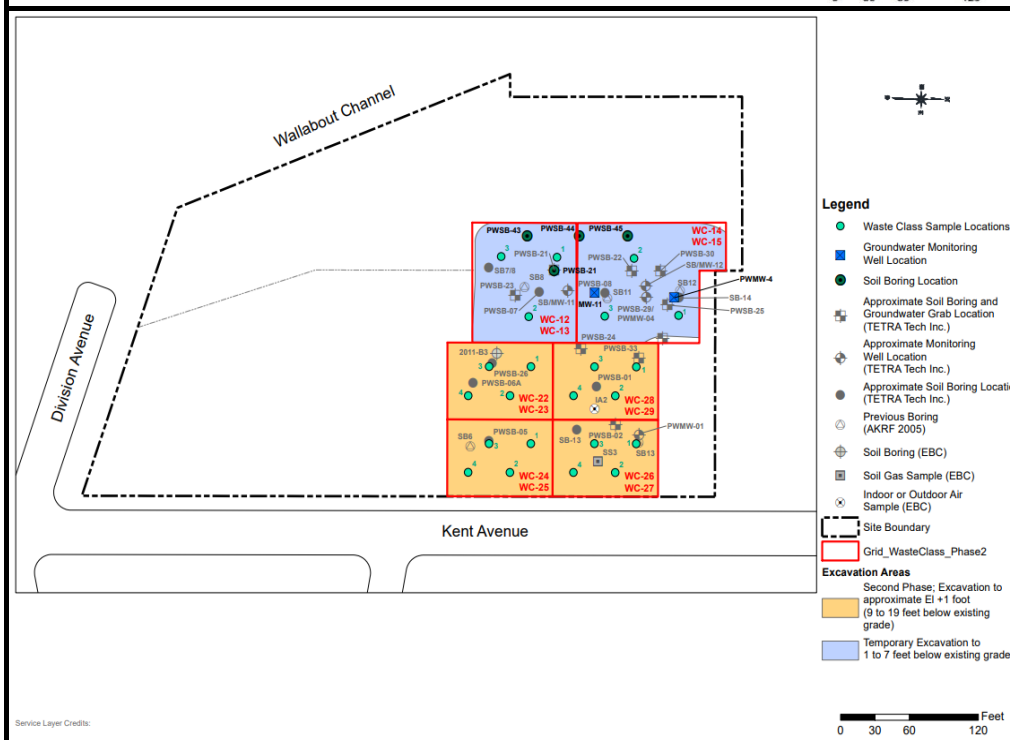
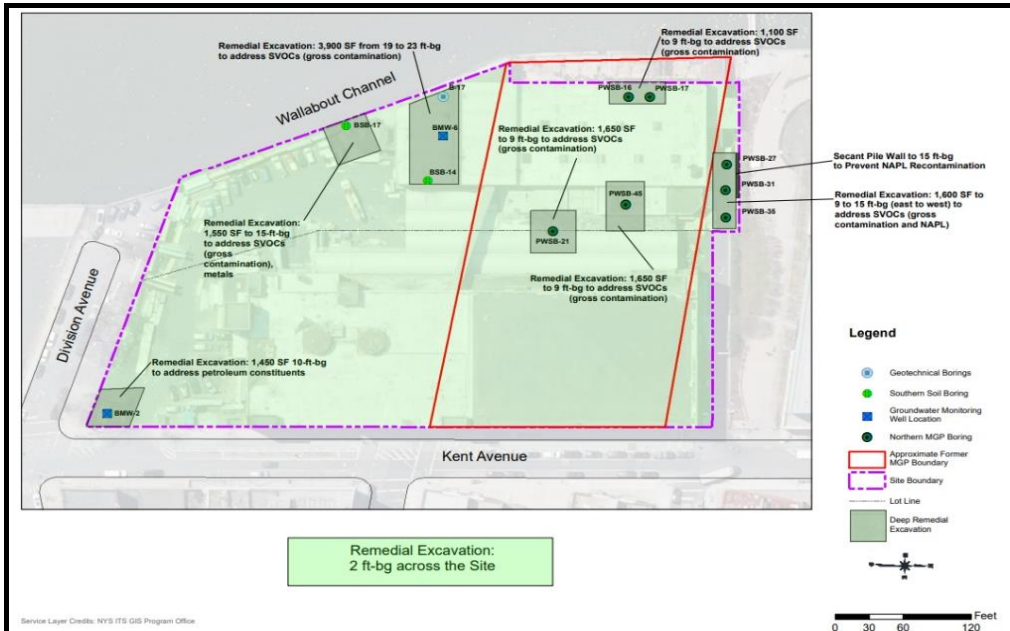


Photo 1:
View of Site conditions
and activities facing
south.



Photo 2:
View of Site conditions
and activities facing
west.

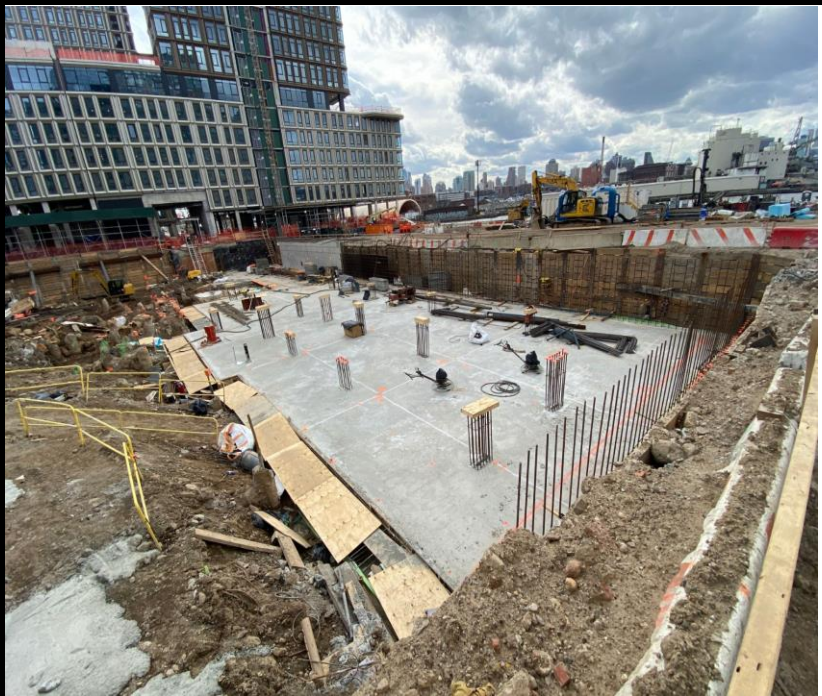



Photo 3:
View of 2.5" stone
import.




Photo 4:
View of soil
excavation and SOE
installation facing
east.




CAMP:
Downwind
Particulates

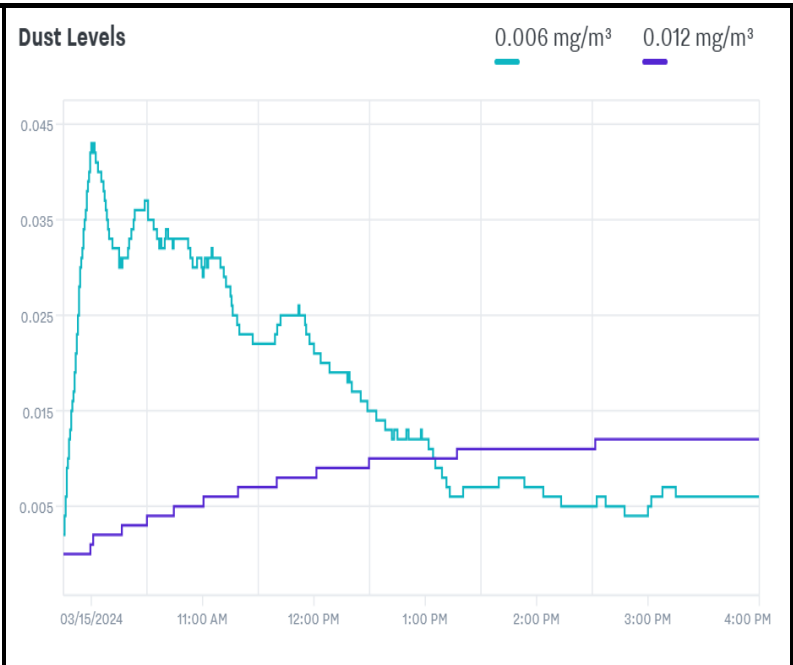


CAMP:
Downwind VOCs

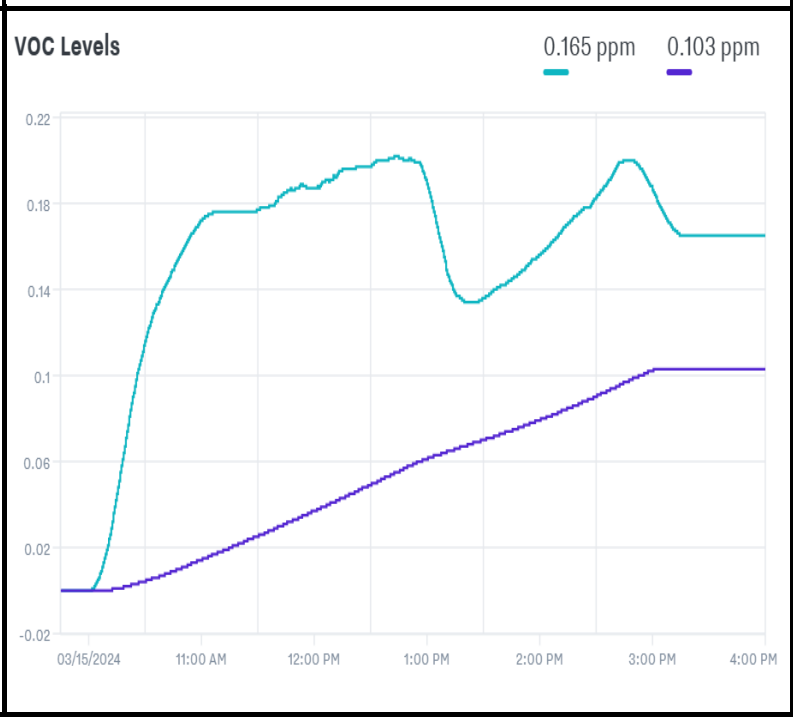

CAMP:
Upwind Particulates

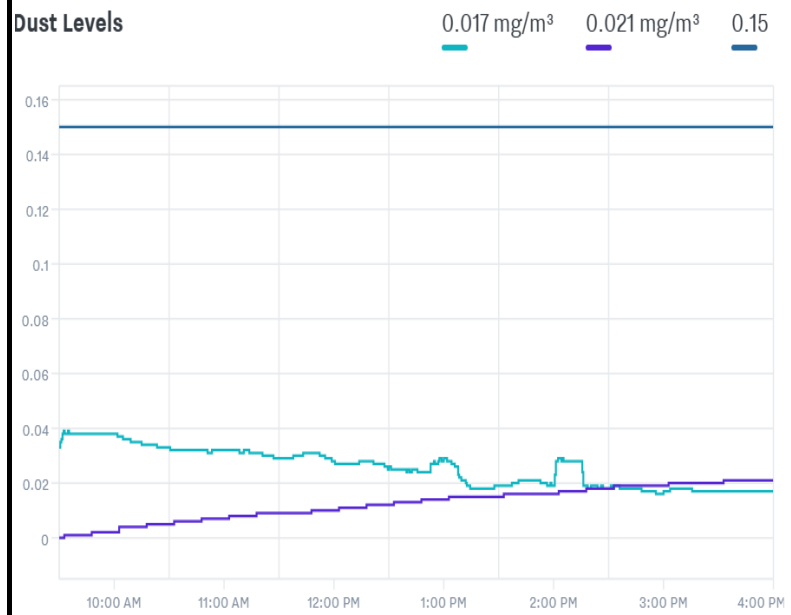

CAMP:
Upwind VOCs

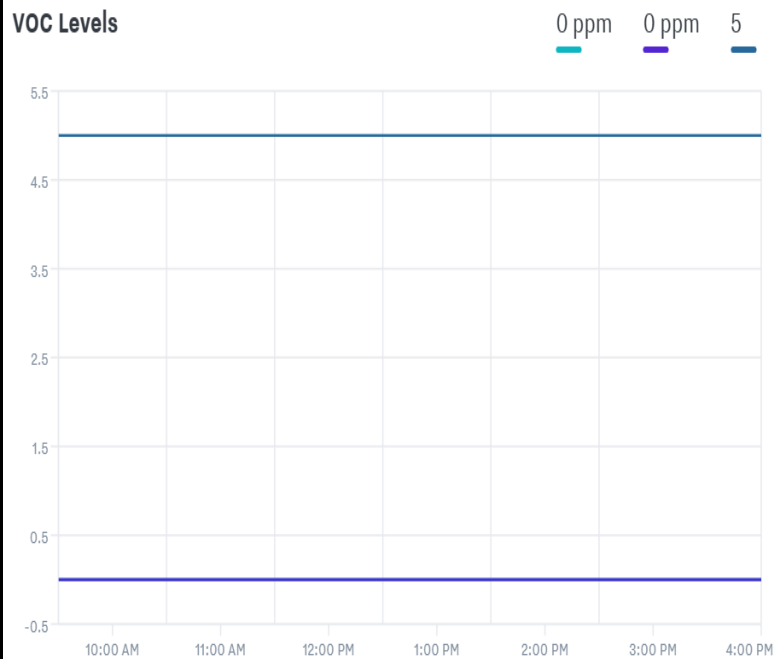

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/15/2024 9:45	3/15/2024 9:55	0.150	0	5	0
DW 2024	3/15/2024 9:55	3/15/2024 10:05	0.150	0.002	5	0
DW 2024	3/15/2024 10:05	3/15/2024 10:15	0.150	0.002	5	0.001
DW 2024	3/15/2024 10:15	3/15/2024 10:25	0.150	0.003	5	0.003
DW 2024	3/15/2024 10:25	3/15/2024 10:35	0.150	0.004	5	0.006
DW 2024	3/15/2024 10:35	3/15/2024 10:45	0.150	0.005	5	0.009
DW 2024	3/15/2024 10:45	3/15/2024 10:55	0.150	0.005	5	0.013
DW 2024	3/15/2024 10:55	3/15/2024 11:05	0.150	0.006	5	0.016
DW 2024	3/15/2024 11:05	3/15/2024 11:15	0.150	0.006	5	0.02
DW 2024	3/15/2024 11:15	3/15/2024 11:25	0.150	0.007	5	0.024
DW 2024	3/15/2024 11:25	3/15/2024 11:35	0.150	0.007	5	0.027
DW 2024	3/15/2024 11:35	3/15/2024 11:45	0.150	0.008	5	0.031
DW 2024	3/15/2024 11:45	3/15/2024 11:55	0.150	0.008	5	0.035
DW 2024	3/15/2024 11:55	3/15/2024 12:05	0.150	0.009	5	0.039
DW 2024	3/15/2024 12:05	3/15/2024 12:15	0.150	0.009	5	0.043
DW 2024	3/15/2024 12:15	3/15/2024 12:25	0.150	0.009	5	0.047
DW 2024	3/15/2024 12:25	3/15/2024 12:35	0.150	0.01	5	0.051
DW 2024	3/15/2024 12:35	3/15/2024 12:45	0.150	0.01	5	0.055
DW 2024	3/15/2024 12:45	3/15/2024 12:55	0.150	0.01	5	0.06
DW 2024	3/15/2024 12:55	3/15/2024 13:05	0.150	0.01	5	0.063
DW 2024	3/15/2024 13:05	3/15/2024 13:15	0.150	0.01	5	0.066
DW 2024	3/15/2024 13:15	3/15/2024 13:25	0.150	0.011	5	0.069
DW 2024	3/15/2024 13:25	3/15/2024 13:35	0.150	0.011	5	0.071
DW 2024	3/15/2024 13:35	3/15/2024 13:45	0.150	0.011	5	0.074
DW 2024	3/15/2024 13:45	3/15/2024 13:55	0.150	0.011	5	0.078
DW 2024	3/15/2024 13:55	3/15/2024 14:05	0.150	0.011	5	0.081
DW 2024	3/15/2024 14:05	3/15/2024 14:15	0.150	0.011	5	0.085
DW 2024	3/15/2024 14:15	3/15/2024 14:25	0.150	0.011	5	0.088
DW 2024	3/15/2024 14:25	3/15/2024 14:35	0.150	0.012	5	0.092
DW 2024	3/15/2024 14:35	3/15/2024 14:45	0.150	0.012	5	0.097
DW 2024	3/15/2024 14:45	3/15/2024 14:55	0.150	0.012	5	0.1
DW 2024	3/15/2024 14:55	3/15/2024 15:05	0.150	0.012	5	0.103
DW 2024	3/15/2024 15:05	3/15/2024 15:15	0.150	0.012	5	0.103
DW 2024	3/15/2024 15:15	3/15/2024 15:25	0.150	0.012	5	0.103
DW 2024	3/15/2024 15:25	3/15/2024 15:35	0.150	0.012	5	0.103
DW 2024	3/15/2024 15:35	3/15/2024 15:45	0.150	0.012	5	0.103
DW 2024	3/15/2024 15:45	3/15/2024 15:55	0.150	0.012	5	0.103
DW 2024	3/15/2024 15:55	3/15/2024 16:00	0.150	0.012	5	0.103

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/15/2024 9:45	3/15/2024 9:55	0.150	0.002	5	0
UW 2024	3/15/2024 9:55	3/15/2024 10:05	0.150	0.004	5	0
UW 2024	3/15/2024 10:05	3/15/2024 10:15	0.150	0.004	5	0
UW 2024	3/15/2024 10:15	3/15/2024 10:25	0.150	0.005	5	0
UW 2024	3/15/2024 10:25	3/15/2024 10:35	0.150	0.006	5	0
UW 2024	3/15/2024 10:35	3/15/2024 10:45	0.150	0.006	5	0
UW 2024	3/15/2024 10:45	3/15/2024 10:55	0.150	0.007	5	0
UW 2024	3/15/2024 10:55	3/15/2024 11:05	0.150	0.008	5	0
UW 2024	3/15/2024 11:05	3/15/2024 11:15	0.150	0.008	5	0
UW 2024	3/15/2024 11:15	3/15/2024 11:25	0.150	0.009	5	0
UW 2024	3/15/2024 11:25	3/15/2024 11:35	0.150	0.009	5	0
UW 2024	3/15/2024 11:35	3/15/2024 11:45	0.150	0.009	5	0
UW 2024	3/15/2024 11:45	3/15/2024 11:55	0.150	0.01	5	0
UW 2024	3/15/2024 11:55	3/15/2024 12:05	0.150	0.011	5	0
UW 2024	3/15/2024 12:05	3/15/2024 12:15	0.150	0.011	5	0
UW 2024	3/15/2024 12:15	3/15/2024 12:25	0.150	0.012	5	0
UW 2024	3/15/2024 12:25	3/15/2024 12:35	0.150	0.013	5	0
UW 2024	3/15/2024 12:35	3/15/2024 12:45	0.150	0.013	5	0
UW 2024	3/15/2024 12:45	3/15/2024 12:55	0.150	0.014	5	0
UW 2024	3/15/2024 12:55	3/15/2024 13:05	0.150	0.015	5	0
UW 2024	3/15/2024 13:05	3/15/2024 13:15	0.150	0.015	5	0
UW 2024	3/15/2024 13:15	3/15/2024 13:25	0.150	0.015	5	0
UW 2024	3/15/2024 13:25	3/15/2024 13:35	0.150	0.016	5	0
UW 2024	3/15/2024 13:35	3/15/2024 13:45	0.150	0.016	5	0
UW 2024	3/15/2024 13:45	3/15/2024 13:55	0.150	0.016	5	0
UW 2024	3/15/2024 13:55	3/15/2024 14:05	0.150	0.017	5	0
UW 2024	3/15/2024 14:05	3/15/2024 14:15	0.150	0.017	5	0
UW 2024	3/15/2024 14:15	3/15/2024 14:25	0.150	0.018	5	0
UW 2024	3/15/2024 14:25	3/15/2024 14:35	0.150	0.019	5	0
UW 2024	3/15/2024 14:35	3/15/2024 14:45	0.150	0.019	5	0
UW 2024	3/15/2024 14:45	3/15/2024 14:55	0.150	0.019	5	0
UW 2024	3/15/2024 14:55	3/15/2024 15:05	0.150	0.02	5	0
UW 2024	3/15/2024 15:05	3/15/2024 15:15	0.150	0.02	5	0
UW 2024	3/15/2024 15:15	3/15/2024 15:25	0.150	0.02	5	0
UW 2024	3/15/2024 15:25	3/15/2024 15:35	0.150	0.021	5	0
UW 2024	3/15/2024 15:35	3/15/2024 15:45	0.150	0.021	5	0
UW 2024	3/15/2024 15:45	3/15/2024 15:55	0.150	0.021	5	0
UW 2024	3/15/2024 15:55	3/15/2024 16:00	0.150	0.021	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/15/2024 9:45	3/15/2024 9:55	0.150	0	5	0
HS South	3/15/2024 9:55	3/15/2024 10:05	0.150	0	5	0
HS South	3/15/2024 10:05	3/15/2024 10:15	0.150	0.001	5	0
HS South	3/15/2024 10:15	3/15/2024 10:25	0.150	0.001	5	0
HS South	3/15/2024 10:25	3/15/2024 10:35	0.150	0.002	5	0
HS South	3/15/2024 10:35	3/15/2024 10:45	0.150	0.002	5	0
HS South	3/15/2024 10:45	3/15/2024 10:55	0.150	0.002	5	0
HS South	3/15/2024 10:55	3/15/2024 11:05	0.150	0.003	5	0
HS South	3/15/2024 11:05	3/15/2024 11:15	0.150	0.003	5	0
HS South	3/15/2024 11:15	3/15/2024 11:25	0.150	0.004	5	0
HS South	3/15/2024 11:25	3/15/2024 11:35	0.150	0.004	5	0
HS South	3/15/2024 11:35	3/15/2024 11:45	0.150	0.004	5	0
HS South	3/15/2024 11:45	3/15/2024 11:55	0.150	0.005	5	0
HS South	3/15/2024 11:55	3/15/2024 12:05	0.150	0.005	5	0
HS South	3/15/2024 12:05	3/15/2024 12:15	0.150	0.005	5	0
HS South	3/15/2024 12:15	3/15/2024 12:25	0.150	0.005	5	0
HS South	3/15/2024 12:25	3/15/2024 12:35	0.150	0.006	5	0
HS South	3/15/2024 12:35	3/15/2024 12:45	0.150	0.006	5	0
HS South	3/15/2024 12:45	3/15/2024 12:55	0.150	0.006	5	0
HS South	3/15/2024 12:55	3/15/2024 13:05	0.150	0.006	5	0
HS South	3/15/2024 13:05	3/15/2024 13:15	0.150	0.006	5	0
HS South	3/15/2024 13:15	3/15/2024 13:25	0.150	0.006	5	0
HS South	3/15/2024 13:25	3/15/2024 13:35	0.150	0.006	5	0
HS South	3/15/2024 13:35	3/15/2024 13:45	0.150	0.006	5	0
HS South	3/15/2024 13:45	3/15/2024 13:55	0.150	0.006	5	0
HS South	3/15/2024 13:55	3/15/2024 14:05	0.150	0.006	5	0
HS South	3/15/2024 14:05	3/15/2024 14:15	0.150	0.006	5	0
HS South	3/15/2024 14:15	3/15/2024 14:25	0.150	0.006	5	0
HS South	3/15/2024 14:25	3/15/2024 14:35	0.150	0.006	5	0
HS South	3/15/2024 14:35	3/15/2024 14:45	0.150	0.006	5	0
HS South	3/15/2024 14:45	3/15/2024 14:55	0.150	0.006	5	0
HS South	3/15/2024 14:55	3/15/2024 15:05	0.150	0.006	5	0
HS South	3/15/2024 15:05	3/15/2024 15:15	0.150	0.006	5	0
HS South	3/15/2024 15:15	3/15/2024 15:25	0.150	0.006	5	0
HS South	3/15/2024 15:25	3/15/2024 15:35	0.150	0.006	5	0
HS South	3/15/2024 15:35	3/15/2024 15:45	0.150	0.006	5	0
HS South	3/15/2024 15:45	3/15/2024 15:55	0.150	0.006	5	0
HS South	3/15/2024 15:55	3/15/2024 16:00	0.150	0.006	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/15/2024 9:45	3/15/2024 9:55	0.150	0	5	0
PER1 2024	3/15/2024 9:55	3/15/2024 10:05	0.150	0	5	0
PER1 2024	3/15/2024 10:05	3/15/2024 10:15	0.150	0.002	5	0
PER1 2024	3/15/2024 10:15	3/15/2024 10:25	0.150	0.003	5	0
PER1 2024	3/15/2024 10:25	3/15/2024 10:35	0.150	0.004	5	0
PER1 2024	3/15/2024 10:35	3/15/2024 10:45	0.150	0.005	5	0
PER1 2024	3/15/2024 10:45	3/15/2024 10:55	0.150	0.006	5	0
PER1 2024	3/15/2024 10:55	3/15/2024 11:05	0.150	0.007	5	0
PER1 2024	3/15/2024 11:05	3/15/2024 11:15	0.150	0.007	5	0
PER1 2024	3/15/2024 11:15	3/15/2024 11:25	0.150	0.008	5	0
PER1 2024	3/15/2024 11:25	3/15/2024 11:35	0.150	0.009	5	0
PER1 2024	3/15/2024 11:35	3/15/2024 11:45	0.150	0.01	5	0
PER1 2024	3/15/2024 11:45	3/15/2024 11:55	0.150	0.011	5	0
PER1 2024	3/15/2024 11:55	3/15/2024 12:05	0.150	0.011	5	0
PER1 2024	3/15/2024 12:05	3/15/2024 12:15	0.150	0.012	5	0
PER1 2024	3/15/2024 12:15	3/15/2024 12:25	0.150	0.013	5	0
PER1 2024	3/15/2024 12:25	3/15/2024 12:35	0.150	0.014	5	0
PER1 2024	3/15/2024 12:35	3/15/2024 12:45	0.150	0.014	5	0
PER1 2024	3/15/2024 12:45	3/15/2024 12:55	0.150	0.017	5	0
PER1 2024	3/15/2024 12:55	3/15/2024 13:05	0.150	0.017	5	0
PER1 2024	3/15/2024 13:05	3/15/2024 13:15	0.150	0.018	5	0
PER1 2024	3/15/2024 13:15	3/15/2024 13:25	0.150	0.018	5	0
PER1 2024	3/15/2024 13:25	3/15/2024 13:35	0.150	0.019	5	0
PER1 2024	3/15/2024 13:35	3/15/2024 13:45	0.150	0.019	5	0
PER1 2024	3/15/2024 13:45	3/15/2024 13:55	0.150	0.02	5	0
PER1 2024	3/15/2024 13:55	3/15/2024 14:05	0.150	0.02	5	0
PER1 2024	3/15/2024 14:05	3/15/2024 14:15	0.150	0.021	5	0
PER1 2024	3/15/2024 14:15	3/15/2024 14:25	0.150	0.022	5	0
PER1 2024	3/15/2024 14:25	3/15/2024 14:35	0.150	0.023	5	0
PER1 2024	3/15/2024 14:35	3/15/2024 14:45	0.150	0.023	5	0
PER1 2024	3/15/2024 14:45	3/15/2024 14:55	0.150	0.024	5	0
PER1 2024	3/15/2024 14:55	3/15/2024 15:05	0.150	0	5	0
PER1 2024	3/15/2024 15:05	3/15/2024 15:15	0.150	0	5	0
PER1 2024	3/15/2024 15:15	3/15/2024 15:25	0.150	0	5	0
PER1 2024	3/15/2024 15:25	3/15/2024 15:35	0.150	0	5	0
PER1 2024	3/15/2024 15:35	3/15/2024 15:45	0.150	0	5	0
PER1 2024	3/15/2024 15:45	3/15/2024 15:55	0.150	0	5	0
PER1 2024	3/15/2024 15:55	3/15/2024 16:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/15/2024 9:45	3/15/2024 9:55	0.150	0.003	5	0
PER2 2024	3/15/2024 9:55	3/15/2024 10:05	0.150	0.003	5	0
PER2 2024	3/15/2024 10:05	3/15/2024 10:15	0.150	0.004	5	0
PER2 2024	3/15/2024 10:15	3/15/2024 10:25	0.150	0.005	5	0
PER2 2024	3/15/2024 10:25	3/15/2024 10:35	0.150	0.006	5	0
PER2 2024	3/15/2024 10:35	3/15/2024 10:45	0.150	0.007	5	0
PER2 2024	3/15/2024 10:45	3/15/2024 10:55	0.150	0.008	5	0
PER2 2024	3/15/2024 10:55	3/15/2024 11:05	0.150	0.008	5	0
PER2 2024	3/15/2024 11:05	3/15/2024 11:15	0.150	0.009	5	0
PER2 2024	3/15/2024 11:15	3/15/2024 11:25	0.150	0.01	5	0
PER2 2024	3/15/2024 11:25	3/15/2024 11:35	0.150	0.011	5	0
PER2 2024	3/15/2024 11:35	3/15/2024 11:45	0.150	0.013	5	0
PER2 2024	3/15/2024 11:45	3/15/2024 11:55	0.150	0.014	5	0
PER2 2024	3/15/2024 11:55	3/15/2024 12:05	0.150	0.014	5	0
PER2 2024	3/15/2024 12:05	3/15/2024 12:15	0.150	0.015	5	0
PER2 2024	3/15/2024 12:15	3/15/2024 12:25	0.150	0.015	5	0
PER2 2024	3/15/2024 12:25	3/15/2024 12:35	0.150	0.016	5	0
PER2 2024	3/15/2024 12:35	3/15/2024 12:45	0.150	0.016	5	0
PER2 2024	3/15/2024 12:45	3/15/2024 12:55	0.150	0.017	5	0
PER2 2024	3/15/2024 12:55	3/15/2024 13:05	0.150	0.017	5	0
PER2 2024	3/15/2024 13:05	3/15/2024 13:15	0.150	0.017	5	0
PER2 2024	3/15/2024 13:15	3/15/2024 13:25	0.150	0.018	5	0
PER2 2024	3/15/2024 13:25	3/15/2024 13:35	0.150	0.018	5	0
PER2 2024	3/15/2024 13:35	3/15/2024 13:45	0.150	0.018	5	0
PER2 2024	3/15/2024 13:45	3/15/2024 13:55	0.150	0.018	5	0
PER2 2024	3/15/2024 13:55	3/15/2024 14:05	0.150	0.019	5	0
PER2 2024	3/15/2024 14:05	3/15/2024 14:15	0.150	0.019	5	0
PER2 2024	3/15/2024 14:15	3/15/2024 14:25	0.150	0.019	5	0
PER2 2024	3/15/2024 14:25	3/15/2024 14:35	0.150	0.019	5	0
PER2 2024	3/15/2024 14:35	3/15/2024 14:45	0.150	0.02	5	0
PER2 2024	3/15/2024 14:45	3/15/2024 14:55	0.150	0.02	5	0
PER2 2024	3/15/2024 14:55	3/15/2024 15:05	0.150	0.02	5	0
PER2 2024	3/15/2024 15:05	3/15/2024 15:15	0.150	0.02	5	0
PER2 2024	3/15/2024 15:15	3/15/2024 15:25	0.150	0.02	5	0
PER2 2024	3/15/2024 15:25	3/15/2024 15:35	0.150	0.02	5	0
PER2 2024	3/15/2024 15:35	3/15/2024 15:45	0.150	0.02	5	0
PER2 2024	3/15/2024 15:45	3/15/2024 15:55	0.150	0.02	5	0
PER2 2024	3/15/2024 15:55	3/15/2024 16:00	0.150	0.02	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/18/2024

Weather: 45 deg. F, Sunny

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation.
- 2) ECD continued marine waterfront remedial excavation.

Is the dewatering system operating: YES NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP tables and graphs are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	3965	0	6965	1520	2220

Site Layout Map and Excavation Figures

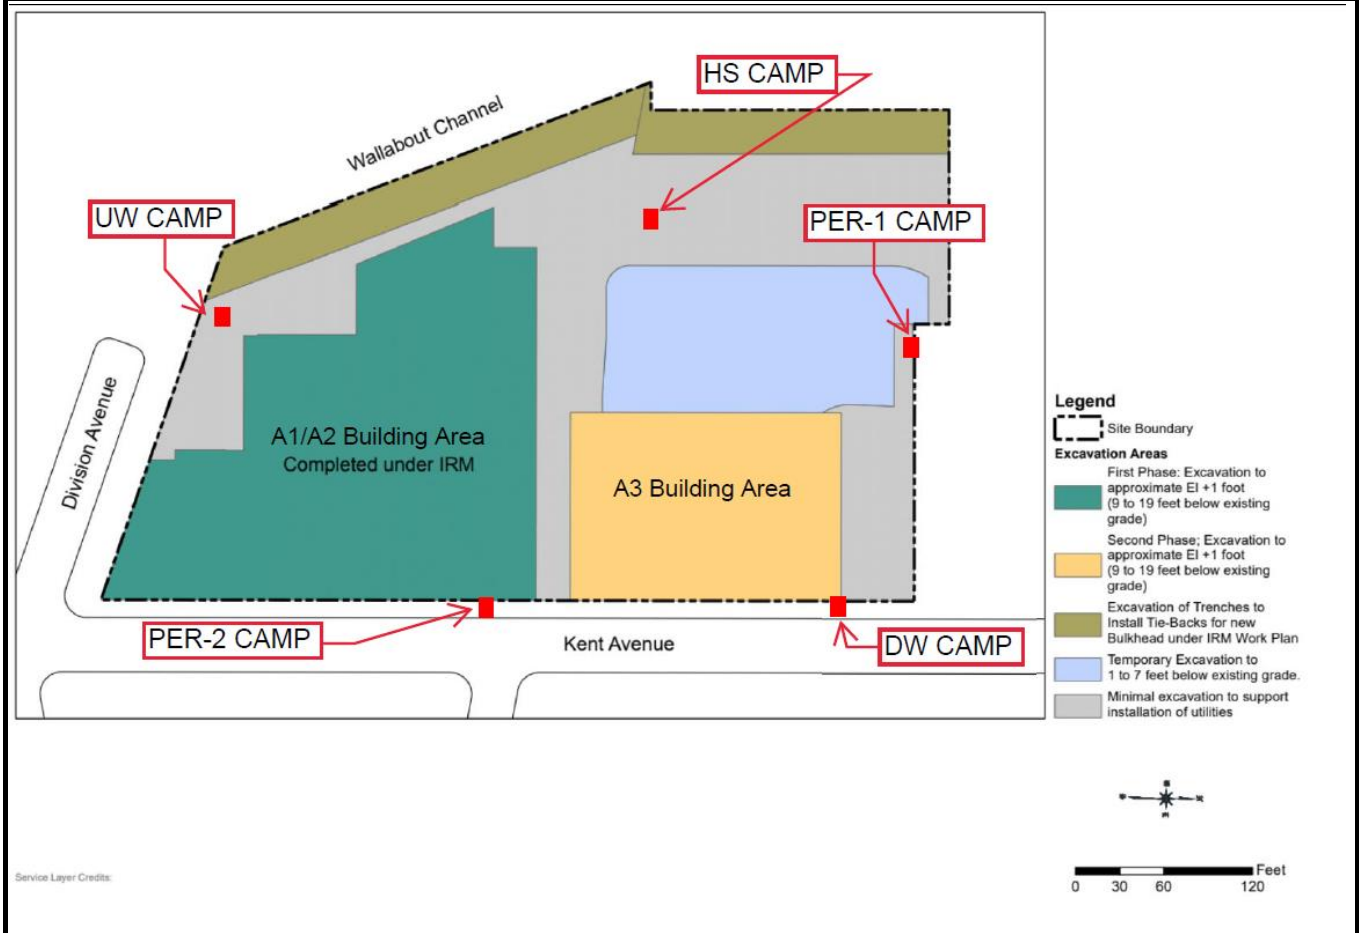

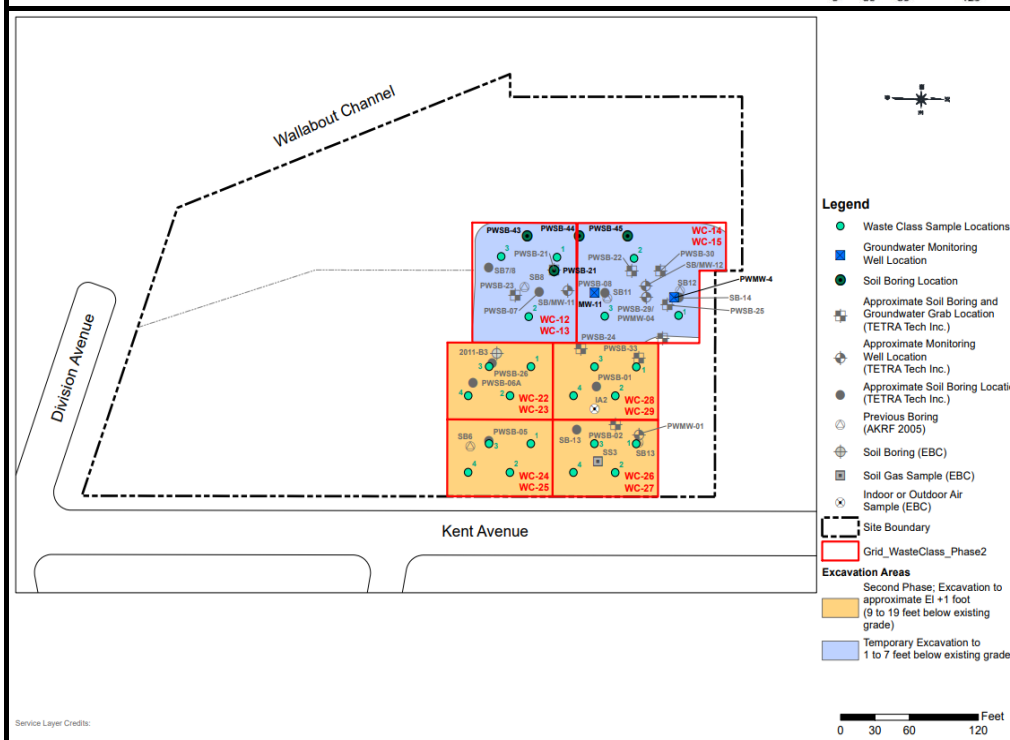
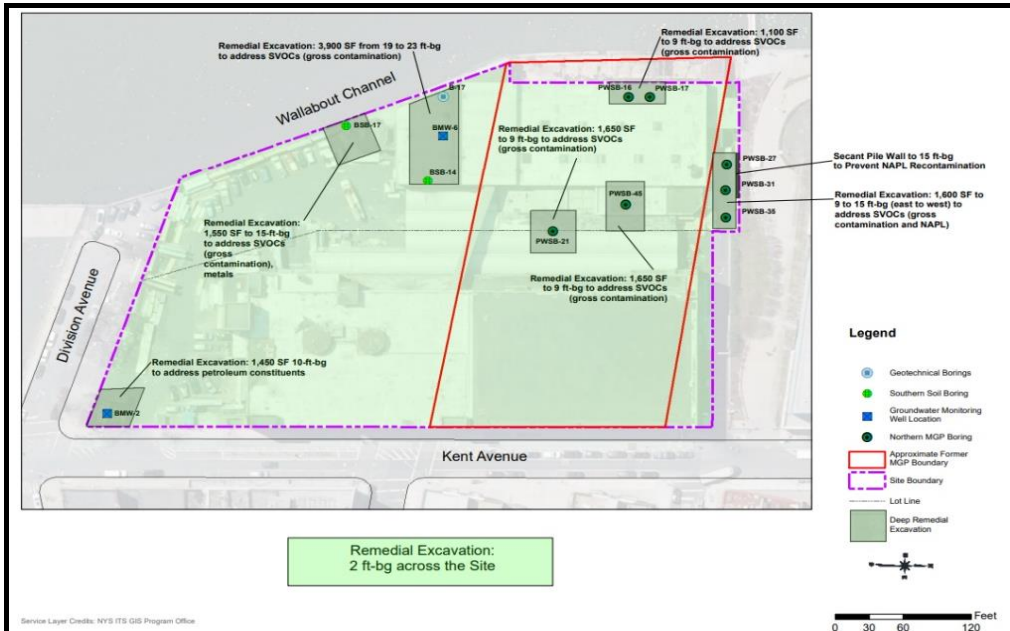


Photo 1:
View of Site conditions
and activities facing
south.



Photo 2:
View of soil excavation
and lagging installation
for SOE.



Photo 3:
View of Site
conditions facing
north.




Photo 4:
View of the
waterfront remedial
excavation.



CAMP:
Downwind
Particulates

Dust Levels


0.006 mg/m³ 0.009 mg/m³

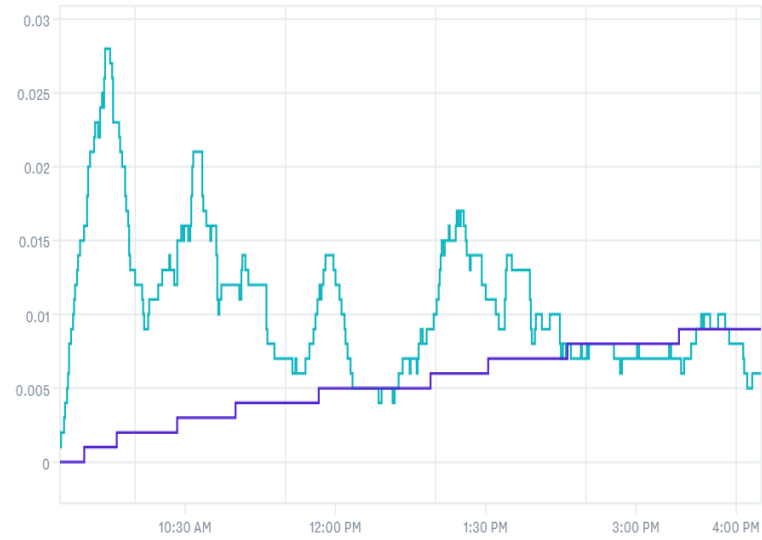

CAMP:
Downwind VOCs

VOC Levels


0.175 ppm 0.167 ppm

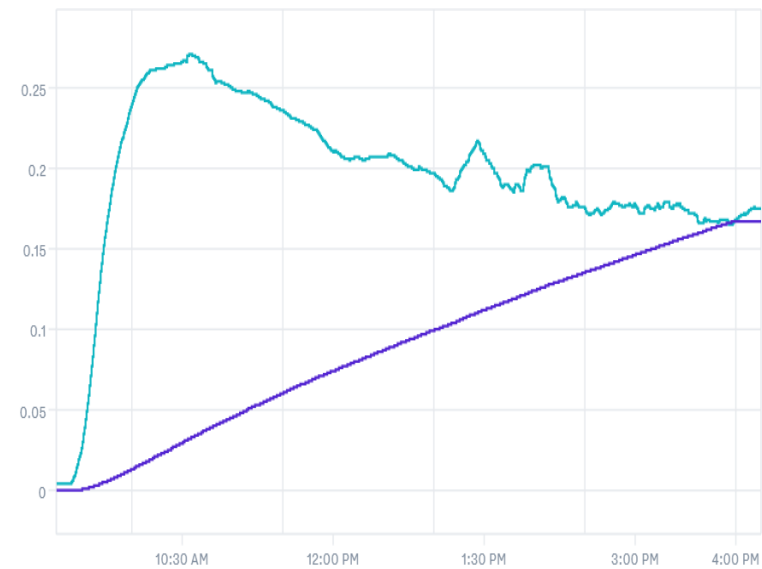

CAMP:
Upwind Particulates

Dust Levels


0.015 mg/m³ 0.015 mg/m³ 0.15

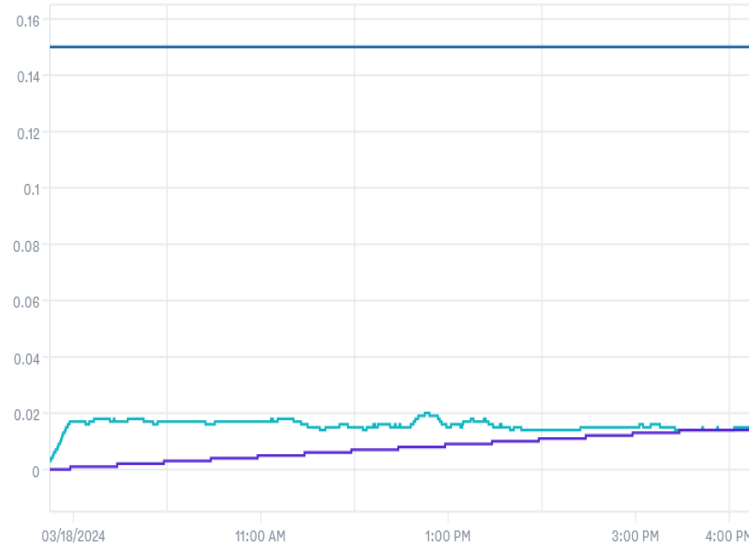

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

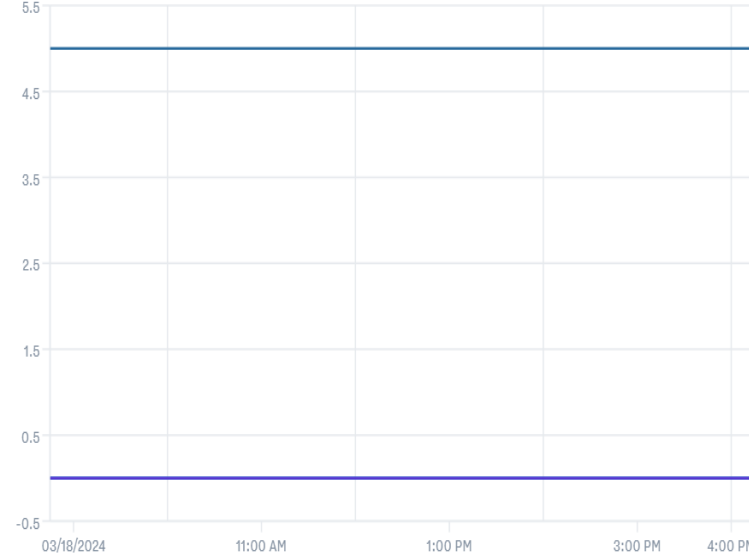

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/18/2024 9:10	3/18/2024 9:20	0.150	0	5	0
DW 2024	3/18/2024 9:20	3/18/2024 9:30	0.150	0.001	5	0
DW 2024	3/18/2024 9:30	3/18/2024 9:40	0.150	0.001	5	0.003
DW 2024	3/18/2024 9:40	3/18/2024 9:50	0.150	0.002	5	0.008
DW 2024	3/18/2024 9:50	3/18/2024 10:00	0.150	0.002	5	0.013
DW 2024	3/18/2024 10:00	3/18/2024 10:10	0.150	0.002	5	0.018
DW 2024	3/18/2024 10:10	3/18/2024 10:20	0.150	0.002	5	0.024
DW 2024	3/18/2024 10:20	3/18/2024 10:30	0.150	0.003	5	0.029
DW 2024	3/18/2024 10:30	3/18/2024 10:40	0.150	0.003	5	0.035
DW 2024	3/18/2024 10:40	3/18/2024 10:50	0.150	0.003	5	0.04
DW 2024	3/18/2024 10:50	3/18/2024 11:00	0.150	0.003	5	0.045
DW 2024	3/18/2024 11:00	3/18/2024 11:10	0.150	0.004	5	0.051
DW 2024	3/18/2024 11:10	3/18/2024 11:20	0.150	0.004	5	0.055
DW 2024	3/18/2024 11:20	3/18/2024 11:30	0.150	0.004	5	0.06
DW 2024	3/18/2024 11:30	3/18/2024 11:40	0.150	0.004	5	0.065
DW 2024	3/18/2024 11:40	3/18/2024 11:50	0.150	0.005	5	0.07
DW 2024	3/18/2024 11:50	3/18/2024 12:00	0.150	0.005	5	0.074
DW 2024	3/18/2024 12:00	3/18/2024 12:10	0.150	0.005	5	0.078
DW 2024	3/18/2024 12:10	3/18/2024 12:20	0.150	0.005	5	0.083
DW 2024	3/18/2024 12:20	3/18/2024 12:30	0.150	0.005	5	0.087
DW 2024	3/18/2024 12:30	3/18/2024 12:40	0.150	0.005	5	0.091
DW 2024	3/18/2024 12:40	3/18/2024 12:50	0.150	0.005	5	0.095
DW 2024	3/18/2024 12:50	3/18/2024 13:00	0.150	0.006	5	0.099
DW 2024	3/18/2024 13:00	3/18/2024 13:10	0.150	0.006	5	0.103
DW 2024	3/18/2024 13:10	3/18/2024 13:20	0.150	0.006	5	0.108
DW 2024	3/18/2024 13:20	3/18/2024 13:30	0.150	0.006	5	0.112
DW 2024	3/18/2024 13:30	3/18/2024 13:40	0.150	0.007	5	0.116
DW 2024	3/18/2024 13:40	3/18/2024 13:50	0.150	0.007	5	0.12
DW 2024	3/18/2024 13:50	3/18/2024 14:00	0.150	0.007	5	0.124
DW 2024	3/18/2024 14:00	3/18/2024 14:10	0.150	0.007	5	0.128
DW 2024	3/18/2024 14:10	3/18/2024 14:20	0.150	0.008	5	0.132
DW 2024	3/18/2024 14:20	3/18/2024 14:30	0.150	0.008	5	0.135
DW 2024	3/18/2024 14:30	3/18/2024 14:40	0.150	0.008	5	0.139
DW 2024	3/18/2024 14:40	3/18/2024 14:50	0.150	0.008	5	0.142
DW 2024	3/18/2024 14:50	3/18/2024 15:00	0.150	0.008	5	0.146
DW 2024	3/18/2024 15:00	3/18/2024 15:10	0.150	0.008	5	0.15
DW 2024	3/18/2024 15:10	3/18/2024 15:20	0.150	0.008	5	0.153
DW 2024	3/18/2024 15:20	3/18/2024 15:30	0.150	0.009	5	0.157
DW 2024	3/18/2024 15:30	3/18/2024 15:40	0.150	0.009	5	0.16
DW 2024	3/18/2024 15:40	3/18/2024 15:50	0.150	0.009	5	0.164
DW 2024	3/18/2024 15:50	3/18/2024 16:00	0.150	0.009	5	0.167
DW 2024	3/18/2024 16:00	3/18/2024 16:10	0.150	0.009	5	0.167
DW 2024	3/18/2024 16:10	3/18/2024 16:20	0.150	0.009	5	0.167
DW 2024	3/18/2024 16:20	3/18/2024 16:30	0.150	0.009	5	0.167
DW 2024	3/18/2024 16:30	3/18/2024 16:40	0.150	0.009	5	0.167
DW 2024	3/18/2024 16:40	3/18/2024 16:50	0.150	0.009	5	0.167
DW 2024	3/18/2024 16:50	3/18/2024 17:00	0.150	0.009	5	0.167

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/18/2024 8:50	3/18/2024 9:00	0.150	0.001	5	0
UW 2024	3/18/2024 9:00	3/18/2024 9:10	0.150	0.001	5	0
UW 2024	3/18/2024 9:10	3/18/2024 9:20	0.150	0.001	5	0
UW 2024	3/18/2024 9:20	3/18/2024 9:30	0.150	0.002	5	0
UW 2024	3/18/2024 9:30	3/18/2024 9:40	0.150	0.002	5	0
UW 2024	3/18/2024 9:40	3/18/2024 9:50	0.150	0.002	5	0
UW 2024	3/18/2024 9:50	3/18/2024 10:00	0.150	0.003	5	0
UW 2024	3/18/2024 10:00	3/18/2024 10:10	0.150	0.003	5	0
UW 2024	3/18/2024 10:10	3/18/2024 10:20	0.150	0.003	5	0
UW 2024	3/18/2024 10:20	3/18/2024 10:30	0.150	0.004	5	0
UW 2024	3/18/2024 10:30	3/18/2024 10:40	0.150	0.004	5	0
UW 2024	3/18/2024 10:40	3/18/2024 10:50	0.150	0.004	5	0
UW 2024	3/18/2024 10:50	3/18/2024 11:00	0.150	0.005	5	0
UW 2024	3/18/2024 11:00	3/18/2024 11:10	0.150	0.005	5	0
UW 2024	3/18/2024 11:10	3/18/2024 11:20	0.150	0.005	5	0
UW 2024	3/18/2024 11:20	3/18/2024 11:30	0.150	0.006	5	0
UW 2024	3/18/2024 11:30	3/18/2024 11:40	0.150	0.006	5	0
UW 2024	3/18/2024 11:40	3/18/2024 11:50	0.150	0.006	5	0
UW 2024	3/18/2024 11:50	3/18/2024 12:00	0.150	0.007	5	0
UW 2024	3/18/2024 12:00	3/18/2024 12:10	0.150	0.007	5	0
UW 2024	3/18/2024 12:10	3/18/2024 12:20	0.150	0.007	5	0
UW 2024	3/18/2024 12:20	3/18/2024 12:30	0.150	0.008	5	0
UW 2024	3/18/2024 12:30	3/18/2024 12:40	0.150	0.008	5	0
UW 2024	3/18/2024 12:40	3/18/2024 12:50	0.150	0.008	5	0
UW 2024	3/18/2024 12:50	3/18/2024 13:00	0.150	0.009	5	0
UW 2024	3/18/2024 13:00	3/18/2024 13:10	0.150	0.009	5	0
UW 2024	3/18/2024 13:10	3/18/2024 13:20	0.150	0.009	5	0
UW 2024	3/18/2024 13:20	3/18/2024 13:30	0.150	0.01	5	0
UW 2024	3/18/2024 13:30	3/18/2024 13:40	0.150	0.01	5	0
UW 2024	3/18/2024 13:40	3/18/2024 13:50	0.150	0.01	5	0
UW 2024	3/18/2024 13:50	3/18/2024 14:00	0.150	0.011	5	0
UW 2024	3/18/2024 14:00	3/18/2024 14:10	0.150	0.011	5	0
UW 2024	3/18/2024 14:10	3/18/2024 14:20	0.150	0.011	5	0
UW 2024	3/18/2024 14:20	3/18/2024 14:30	0.150	0.012	5	0
UW 2024	3/18/2024 14:30	3/18/2024 14:40	0.150	0.012	5	0
UW 2024	3/18/2024 14:40	3/18/2024 14:50	0.150	0.012	5	0
UW 2024	3/18/2024 14:50	3/18/2024 15:00	0.150	0.013	5	0
UW 2024	3/18/2024 15:00	3/18/2024 15:10	0.150	0.013	5	0
UW 2024	3/18/2024 15:10	3/18/2024 15:20	0.150	0.013	5	0
UW 2024	3/18/2024 15:20	3/18/2024 15:30	0.150	0.014	5	0
UW 2024	3/18/2024 15:30	3/18/2024 15:40	0.150	0.014	5	0
UW 2024	3/18/2024 15:40	3/18/2024 15:50	0.150	0.014	5	0
UW 2024	3/18/2024 15:50	3/18/2024 16:00	0.150	0.014	5	0
UW 2024	3/18/2024 16:00	3/18/2024 16:10	0.150	0.014	5	0
UW 2024	3/18/2024 16:10	3/18/2024 16:20	0.150	0.015	5	0
UW 2024	3/18/2024 16:20	3/18/2024 16:30	0.150	0.015	5	0
UW 2024	3/18/2024 16:30	3/18/2024 16:40	0.150	0	5	0
UW 2024	3/18/2024 16:40	3/18/2024 16:50	0.150	0	5	0
UW 2024	3/18/2024 16:50	3/18/2024 17:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/18/2024 8:50	3/18/2024 9:00	0.150	0	5	0
HS South	3/18/2024 9:00	3/18/2024 9:10	0.150	0	5	0
HS South	3/18/2024 9:10	3/18/2024 9:20	0.150	0	5	0
HS South	3/18/2024 9:20	3/18/2024 9:30	0.150	0	5	0
HS South	3/18/2024 9:30	3/18/2024 9:40	0.150	0.001	5	0
HS South	3/18/2024 9:40	3/18/2024 9:50	0.150	0.001	5	0
HS South	3/18/2024 9:50	3/18/2024 10:00	0.150	0.001	5	0
HS South	3/18/2024 10:00	3/18/2024 10:10	0.150	0.001	5	0
HS South	3/18/2024 10:10	3/18/2024 10:20	0.150	0.001	5	0
HS South	3/18/2024 10:20	3/18/2024 10:30	0.150	0.001	5	0
HS South	3/18/2024 10:30	3/18/2024 10:40	0.150	0.001	5	0
HS South	3/18/2024 10:40	3/18/2024 10:50	0.150	0.001	5	0
HS South	3/18/2024 10:50	3/18/2024 11:00	0.150	0.001	5	0
HS South	3/18/2024 11:00	3/18/2024 11:10	0.150	0.002	5	0
HS South	3/18/2024 11:10	3/18/2024 11:20	0.150	0.002	5	0
HS South	3/18/2024 11:20	3/18/2024 11:30	0.150	0.002	5	0
HS South	3/18/2024 11:30	3/18/2024 11:40	0.150	0.002	5	0
HS South	3/18/2024 11:40	3/18/2024 11:50	0.150	0.002	5	0
HS South	3/18/2024 11:50	3/18/2024 12:00	0.150	0.002	5	0
HS South	3/18/2024 12:00	3/18/2024 12:10	0.150	0.002	5	0
HS South	3/18/2024 12:10	3/18/2024 12:20	0.150	0.002	5	0
HS South	3/18/2024 12:20	3/18/2024 12:30	0.150	0.002	5	0
HS South	3/18/2024 12:30	3/18/2024 12:40	0.150	0.002	5	0
HS South	3/18/2024 12:40	3/18/2024 12:50	0.150	0.002	5	0
HS South	3/18/2024 12:50	3/18/2024 13:00	0.150	0.002	5	0
HS South	3/18/2024 13:00	3/18/2024 13:10	0.150	0.002	5	0
HS South	3/18/2024 13:10	3/18/2024 13:20	0.150	0.002	5	0
HS South	3/18/2024 13:20	3/18/2024 13:30	0.150	0.002	5	0
HS South	3/18/2024 13:30	3/18/2024 13:40	0.150	0.002	5	0
HS South	3/18/2024 13:40	3/18/2024 13:50	0.150	0.002	5	0
HS South	3/18/2024 13:50	3/18/2024 14:00	0.150	0.002	5	0
HS South	3/18/2024 14:00	3/18/2024 14:10	0.150	0.002	5	0
HS South	3/18/2024 14:10	3/18/2024 14:20	0.150	0.002	5	0
HS South	3/18/2024 14:20	3/18/2024 14:30	0.150	0.002	5	0
HS South	3/18/2024 14:30	3/18/2024 14:40	0.150	0.003	5	0
HS South	3/18/2024 14:40	3/18/2024 14:50	0.150	0.003	5	0
HS South	3/18/2024 14:50	3/18/2024 15:00	0.150	0.003	5	0
HS South	3/18/2024 15:00	3/18/2024 15:10	0.150	0.003	5	0
HS South	3/18/2024 15:10	3/18/2024 15:20	0.150	0.003	5	0
HS South	3/18/2024 15:20	3/18/2024 15:30	0.150	0.003	5	0
HS South	3/18/2024 15:30	3/18/2024 15:40	0.150	0.003	5	0
HS South	3/18/2024 15:40	3/18/2024 15:50	0.150	0.003	5	0
HS South	3/18/2024 15:50	3/18/2024 16:00	0.150	0.003	5	0
HS South	3/18/2024 16:00	3/18/2024 16:10	0.150	0.003	5	0
HS South	3/18/2024 16:10	3/18/2024 16:20	0.150	0.003	5	0
HS South	3/18/2024 16:20	3/18/2024 16:30	0.150	0.003	5	0
HS South	3/18/2024 16:30	3/18/2024 16:40	0.150	0.003	5	0
HS South	3/18/2024 16:40	3/18/2024 16:50	0.150	0.003	5	0
HS South	3/18/2024 16:50	3/18/2024 17:00	0.150	0.003	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/18/2024 9:00	3/18/2024 9:10	0.150	0	5	0.005
PER1 2024	3/18/2024 9:10	3/18/2024 9:20	0.150	0.002	5	0.005
PER1 2024	3/18/2024 9:20	3/18/2024 9:30	0.150	0.003	5	0.005
PER1 2024	3/18/2024 9:30	3/18/2024 9:40	0.150	0.004	5	0.005
PER1 2024	3/18/2024 9:40	3/18/2024 9:50	0.150	0.004	5	0.005
PER1 2024	3/18/2024 9:50	3/18/2024 10:00	0.150	0.005	5	0.005
PER1 2024	3/18/2024 10:00	3/18/2024 10:10	0.150	0.006	5	0.005
PER1 2024	3/18/2024 10:10	3/18/2024 10:20	0.150	0.006	5	0.005
PER1 2024	3/18/2024 10:20	3/18/2024 10:30	0.150	0.006	5	0.005
PER1 2024	3/18/2024 10:30	3/18/2024 10:40	0.150	0.007	5	0.005
PER1 2024	3/18/2024 10:40	3/18/2024 10:50	0.150	0.007	5	0.005
PER1 2024	3/18/2024 10:50	3/18/2024 11:00	0.150	0.008	5	0.005
PER1 2024	3/18/2024 11:00	3/18/2024 11:10	0.150	0.008	5	0.005
PER1 2024	3/18/2024 11:10	3/18/2024 11:20	0.150	0.009	5	0.006
PER1 2024	3/18/2024 11:20	3/18/2024 11:30	0.150	0.01	5	0.006
PER1 2024	3/18/2024 11:30	3/18/2024 11:40	0.150	0.01	5	0.006
PER1 2024	3/18/2024 11:40	3/18/2024 11:50	0.150	0.011	5	0.006
PER1 2024	3/18/2024 11:50	3/18/2024 12:00	0.150	0.012	5	0.006
PER1 2024	3/18/2024 12:00	3/18/2024 12:10	0.150	0.012	5	0.006
PER1 2024	3/18/2024 12:10	3/18/2024 12:20	0.150	0.014	5	0.006
PER1 2024	3/18/2024 12:20	3/18/2024 12:30	0.150	0.014	5	0.006
PER1 2024	3/18/2024 12:30	3/18/2024 12:40	0.150	0.015	5	0.006
PER1 2024	3/18/2024 12:40	3/18/2024 12:50	0.150	0.016	5	0.006
PER1 2024	3/18/2024 12:50	3/18/2024 13:00	0.150	0.018	5	0.006
PER1 2024	3/18/2024 13:00	3/18/2024 13:10	0.150	0.018	5	0.006
PER1 2024	3/18/2024 13:10	3/18/2024 13:20	0.150	0.019	5	0.006
PER1 2024	3/18/2024 13:20	3/18/2024 13:30	0.150	0.019	5	0.006
PER1 2024	3/18/2024 13:30	3/18/2024 13:40	0.150	0.02	5	0.006
PER1 2024	3/18/2024 13:40	3/18/2024 13:50	0.150	0.02	5	0.006
PER1 2024	3/18/2024 13:50	3/18/2024 14:00	0.150	0.021	5	0.006
PER1 2024	3/18/2024 14:00	3/18/2024 14:10	0.150	0.021	5	0.006
PER1 2024	3/18/2024 14:10	3/18/2024 14:20	0.150	0.022	5	0.006
PER1 2024	3/18/2024 14:20	3/18/2024 14:30	0.150	0.022	5	0.03
PER1 2024	3/18/2024 14:30	3/18/2024 14:40	0.150	0.023	5	0.03
PER1 2024	3/18/2024 14:40	3/18/2024 14:50	0.150	0.023	5	0.03
PER1 2024	3/18/2024 14:50	3/18/2024 15:00	0.150	0.023	5	0.03
PER1 2024	3/18/2024 15:00	3/18/2024 15:10	0.150	0.024	5	0.03
PER1 2024	3/18/2024 15:10	3/18/2024 15:20	0.150	0.024	5	0.03
PER1 2024	3/18/2024 15:20	3/18/2024 15:30	0.150	0.025	5	0.03
PER1 2024	3/18/2024 15:30	3/18/2024 15:40	0.150	0.026	5	0.03
PER1 2024	3/18/2024 15:40	3/18/2024 15:50	0.150	0.027	5	0.03
PER1 2024	3/18/2024 15:50	3/18/2024 16:00	0.150	0.029	5	0
PER1 2024	3/18/2024 16:00	3/18/2024 16:10	0.150	0	5	0
PER1 2024	3/18/2024 16:10	3/18/2024 16:20	0.150	0	5	0
PER1 2024	3/18/2024 16:20	3/18/2024 16:30	0.150	0	5	0
PER1 2024	3/18/2024 16:30	3/18/2024 16:40	0.150	0	5	0
PER1 2024	3/18/2024 16:40	3/18/2024 16:50	0.150	0	5	0
PER1 2024	3/18/2024 16:50	3/18/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/18/2024 8:50	3/18/2024 9:00	0.150	0.02	5	0
PER2 2024	3/18/2024 9:00	3/18/2024 9:10	0.150	0.02	5	0
PER2 2024	3/18/2024 9:10	3/18/2024 9:20	0.150	0	5	0
PER2 2024	3/18/2024 9:20	3/18/2024 9:30	0.150	0	5	0
PER2 2024	3/18/2024 9:30	3/18/2024 9:40	0.150	0.001	5	0
PER2 2024	3/18/2024 9:40	3/18/2024 9:50	0.150	0.001	5	0
PER2 2024	3/18/2024 9:50	3/18/2024 10:00	0.150	0.001	5	0
PER2 2024	3/18/2024 10:00	3/18/2024 10:10	0.150	0.001	5	0.001
PER2 2024	3/18/2024 10:10	3/18/2024 10:20	0.150	0.002	5	0.001
PER2 2024	3/18/2024 10:20	3/18/2024 10:30	0.150	0.002	5	0.001
PER2 2024	3/18/2024 10:30	3/18/2024 10:40	0.150	0.002	5	0.001
PER2 2024	3/18/2024 10:40	3/18/2024 10:50	0.150	0.002	5	0.001
PER2 2024	3/18/2024 10:50	3/18/2024 11:00	0.150	0.003	5	0.001
PER2 2024	3/18/2024 11:00	3/18/2024 11:10	0.150	0.003	5	0.001
PER2 2024	3/18/2024 11:10	3/18/2024 11:20	0.150	0.003	5	0.001
PER2 2024	3/18/2024 11:20	3/18/2024 11:30	0.150	0.003	5	0.001
PER2 2024	3/18/2024 11:30	3/18/2024 11:40	0.150	0.004	5	0.002
PER2 2024	3/18/2024 11:40	3/18/2024 11:50	0.150	0.004	5	0.002
PER2 2024	3/18/2024 11:50	3/18/2024 12:00	0.150	0.004	5	0.007
PER2 2024	3/18/2024 12:00	3/18/2024 12:10	0.150	0.005	5	0.013
PER2 2024	3/18/2024 12:10	3/18/2024 12:20	0.150	0.005	5	0.015
PER2 2024	3/18/2024 12:20	3/18/2024 12:30	0.150	0.005	5	0.016
PER2 2024	3/18/2024 12:30	3/18/2024 12:40	0.150	0.005	5	0.016
PER2 2024	3/18/2024 12:40	3/18/2024 12:50	0.150	0.005	5	0.016
PER2 2024	3/18/2024 12:50	3/18/2024 13:00	0.150	0.006	5	0.016
PER2 2024	3/18/2024 13:00	3/18/2024 13:10	0.150	0.006	5	0.016
PER2 2024	3/18/2024 13:10	3/18/2024 13:20	0.150	0.006	5	0.016
PER2 2024	3/18/2024 13:20	3/18/2024 13:30	0.150	0.007	5	0.016
PER2 2024	3/18/2024 13:30	3/18/2024 13:40	0.150	0.007	5	0.016
PER2 2024	3/18/2024 13:40	3/18/2024 13:50	0.150	0.007	5	0.016
PER2 2024	3/18/2024 13:50	3/18/2024 14:00	0.150	0.007	5	0.016
PER2 2024	3/18/2024 14:00	3/18/2024 14:10	0.150	0.007	5	0.016
PER2 2024	3/18/2024 14:10	3/18/2024 14:20	0.150	0.008	5	0.016
PER2 2024	3/18/2024 14:20	3/18/2024 14:30	0.150	0.008	5	0.016
PER2 2024	3/18/2024 14:30	3/18/2024 14:40	0.150	0.009	5	0.016
PER2 2024	3/18/2024 14:40	3/18/2024 14:50	0.150	0.009	5	0.016
PER2 2024	3/18/2024 14:50	3/18/2024 15:00	0.150	0.009	5	0.016
PER2 2024	3/18/2024 15:00	3/18/2024 15:10	0.150	0.01	5	0.016
PER2 2024	3/18/2024 15:10	3/18/2024 15:20	0.150	0.01	5	0.016
PER2 2024	3/18/2024 15:20	3/18/2024 15:30	0.150	0.01	5	0.016
PER2 2024	3/18/2024 15:30	3/18/2024 15:40	0.150	0.011	5	0.016
PER2 2024	3/18/2024 15:40	3/18/2024 15:50	0.150	0.011	5	0.016
PER2 2024	3/18/2024 15:50	3/18/2024 16:00	0.150	0.011	5	0.016
PER2 2024	3/18/2024 16:00	3/18/2024 16:10	0.150	0.011	5	0.016
PER2 2024	3/18/2024 16:10	3/18/2024 16:20	0.150	0.011	5	0.016
PER2 2024	3/18/2024 16:20	3/18/2024 16:30	0.150	0.011	5	0.016
PER2 2024	3/18/2024 16:30	3/18/2024 16:40	0.150	0.011	5	0.016
PER2 2024	3/18/2024 16:40	3/18/2024 16:50	0.150	0.011	5	0.016
PER2 2024	3/18/2024 16:50	3/18/2024 17:00	0.150	0.011	5	0.016

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/19/2024

Weather: 35 deg. F, Sunny


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues SOE installation, soil excavation and stockpiling, foundation development, waterproofing installation and rebar installation. 2) Alba exports 10 loads (approximately 200 CY) of material from WC-25 for off-site disposal at the Harmony Foul Rift facility. 3) ECD continued marine waterfront remedial excavation.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP tables and graphs are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	200	0	0	0	0
Total:(CY)	4165	0	6965	1520	2220

Site Layout Map and Excavation Figures

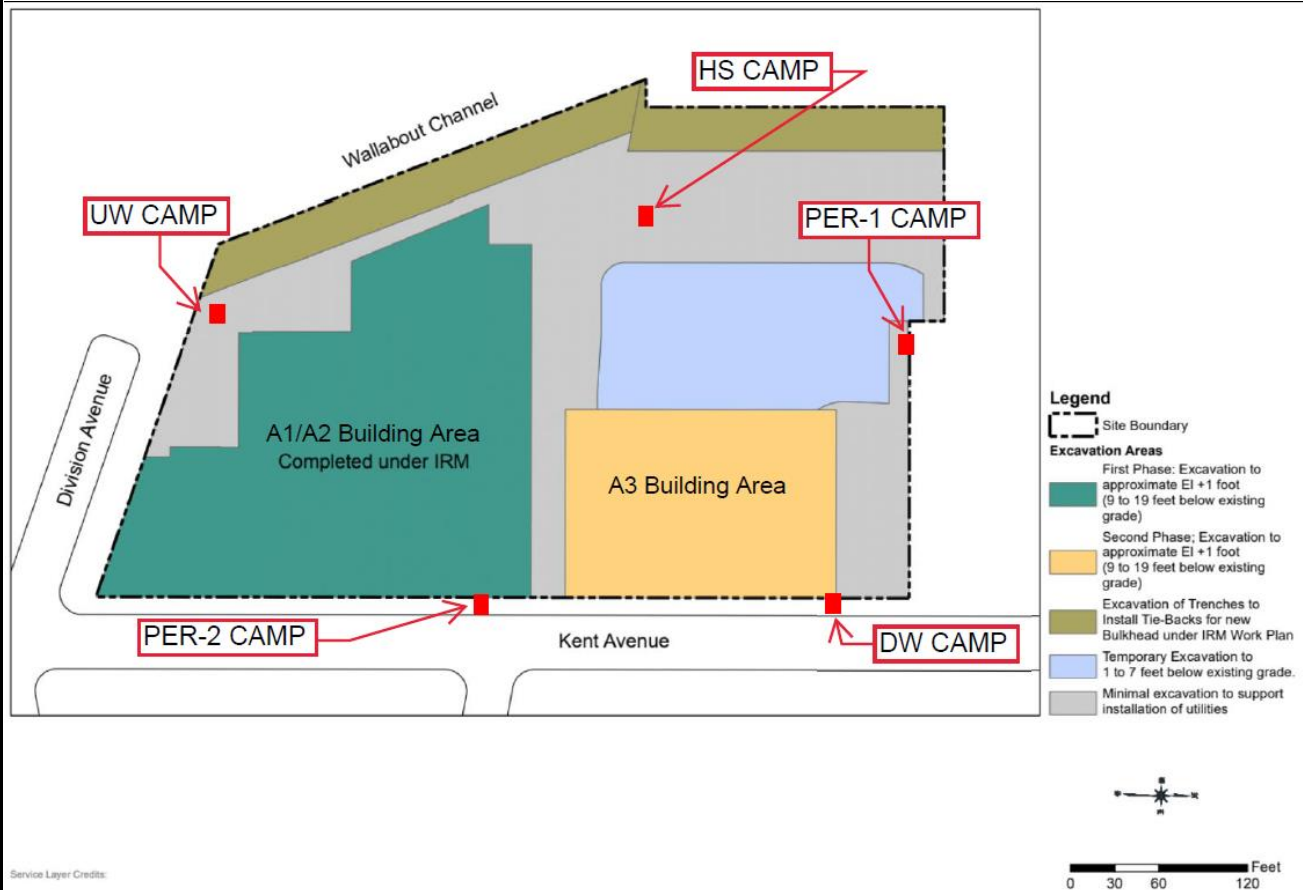

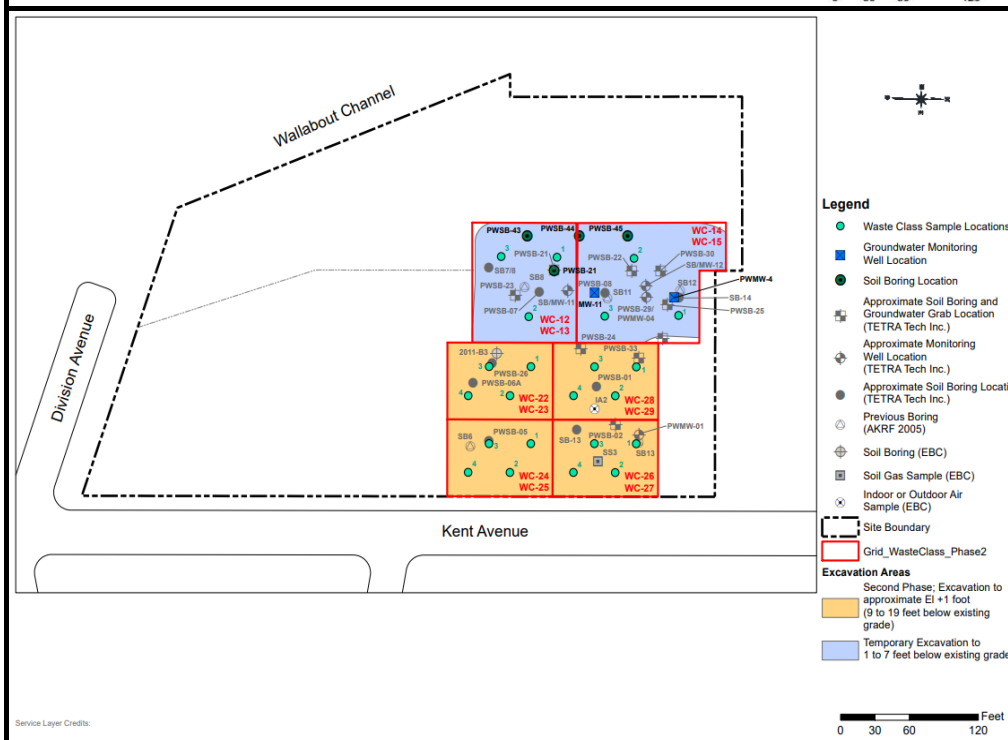
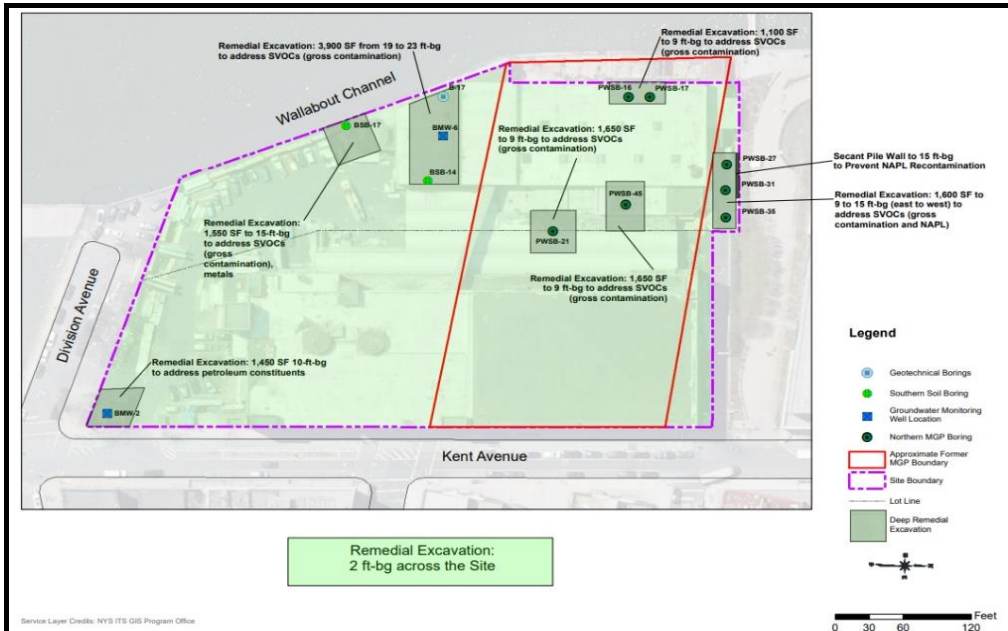


Photo 1:

View of Site conditions, soil excavation and truck loading facing south.



Photo 2:

View of soil excavation and truck loading facing east.

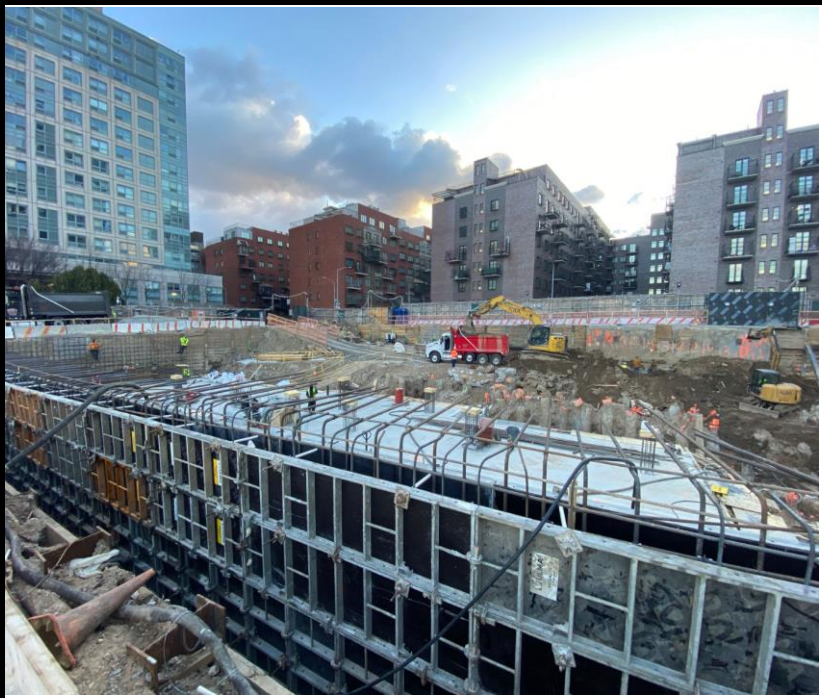


Photo 3:
View of remedial
excavation.

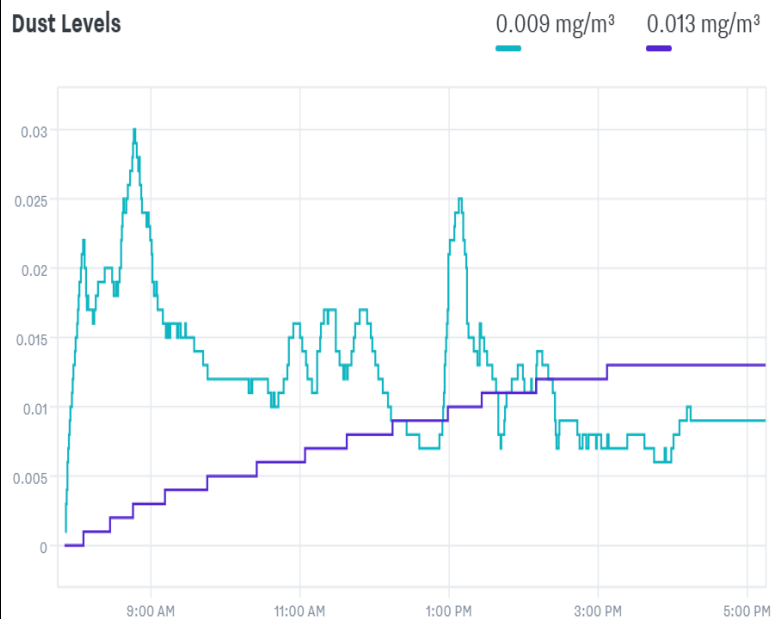


Photo 4:
View of the
waterfront remedial
excavation.




CAMP:
Downwind
Particulates

Dust Levels



CAMP:
Downwind VOCs

VOC Levels

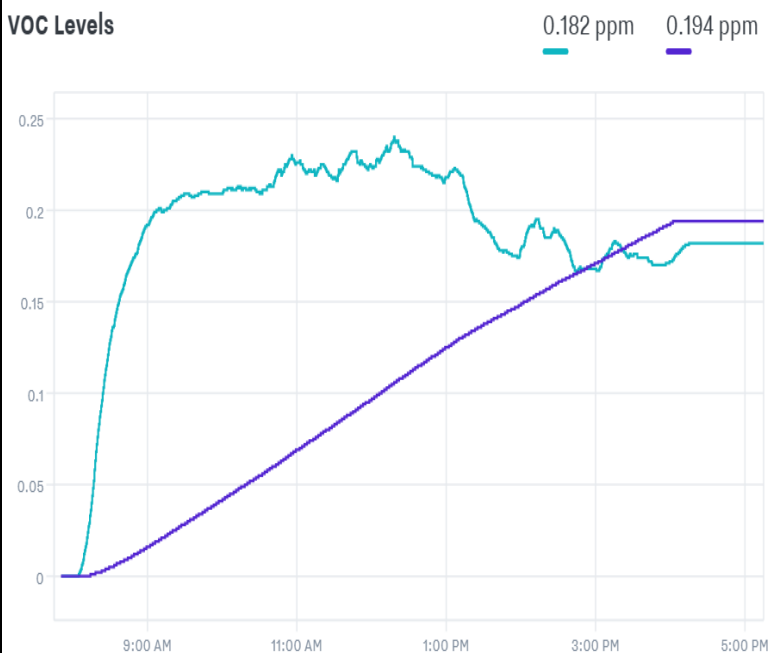


CAMP:
Upwind Particulates

Dust Levels

0.018 mg/m³

0.018 mg/m³

0.15

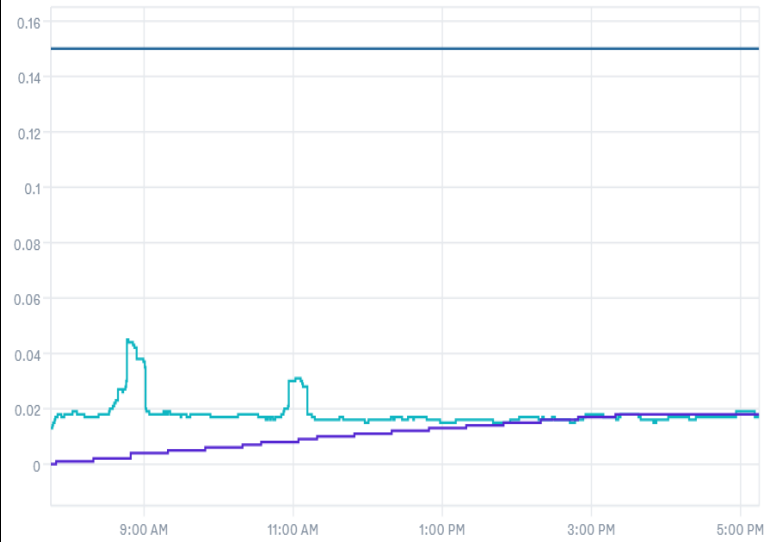


CAMP:
Upwind VOCs

VOC Levels

0 ppm

0 ppm

5

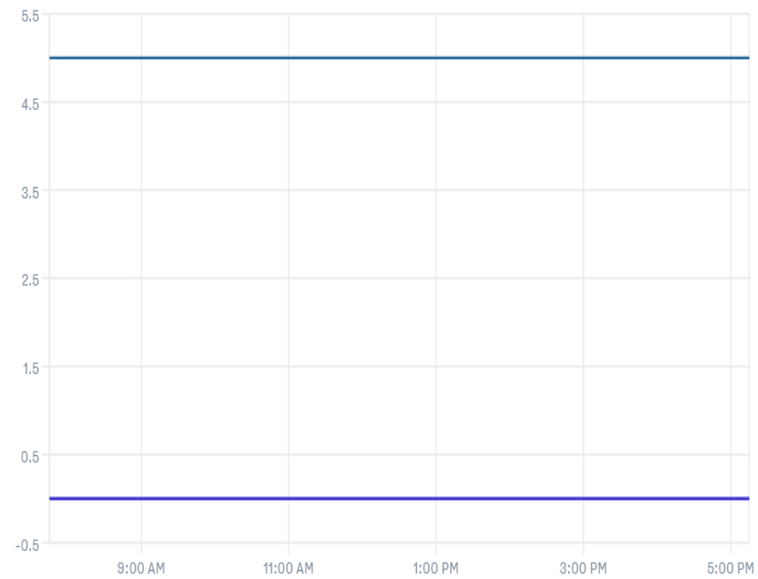

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/19/2024 8:00	3/19/2024 8:10	0.150	0.001	5	0
DW 2024	3/19/2024 8:10	3/19/2024 8:20	0.150	0.001	5	0.002
DW 2024	3/19/2024 8:20	3/19/2024 8:30	0.150	0.002	5	0.005
DW 2024	3/19/2024 8:30	3/19/2024 8:40	0.150	0.002	5	0.008
DW 2024	3/19/2024 8:40	3/19/2024 8:50	0.150	0.003	5	0.012
DW 2024	3/19/2024 8:50	3/19/2024 9:00	0.150	0.003	5	0.016
DW 2024	3/19/2024 9:00	3/19/2024 9:10	0.150	0.003	5	0.02
DW 2024	3/19/2024 9:10	3/19/2024 9:20	0.150	0.004	5	0.024
DW 2024	3/19/2024 9:20	3/19/2024 9:30	0.150	0.004	5	0.028
DW 2024	3/19/2024 9:30	3/19/2024 9:40	0.150	0.004	5	0.033
DW 2024	3/19/2024 9:40	3/19/2024 9:50	0.150	0.005	5	0.037
DW 2024	3/19/2024 9:50	3/19/2024 10:00	0.150	0.005	5	0.041
DW 2024	3/19/2024 10:00	3/19/2024 10:10	0.150	0.005	5	0.046
DW 2024	3/19/2024 10:10	3/19/2024 10:20	0.150	0.005	5	0.05
DW 2024	3/19/2024 10:20	3/19/2024 10:30	0.150	0.006	5	0.055
DW 2024	3/19/2024 10:30	3/19/2024 10:40	0.150	0.006	5	0.059
DW 2024	3/19/2024 10:40	3/19/2024 10:50	0.150	0.006	5	0.064
DW 2024	3/19/2024 10:50	3/19/2024 11:00	0.150	0.006	5	0.069
DW 2024	3/19/2024 11:00	3/19/2024 11:10	0.150	0.007	5	0.073
DW 2024	3/19/2024 11:10	3/19/2024 11:20	0.150	0.007	5	0.078
DW 2024	3/19/2024 11:20	3/19/2024 11:30	0.150	0.007	5	0.082
DW 2024	3/19/2024 11:30	3/19/2024 11:40	0.150	0.008	5	0.087
DW 2024	3/19/2024 11:40	3/19/2024 11:50	0.150	0.008	5	0.092
DW 2024	3/19/2024 11:50	3/19/2024 12:00	0.150	0.008	5	0.096
DW 2024	3/19/2024 12:00	3/19/2024 12:10	0.150	0.008	5	0.101
DW 2024	3/19/2024 12:10	3/19/2024 12:20	0.150	0.009	5	0.106
DW 2024	3/19/2024 12:20	3/19/2024 12:30	0.150	0.009	5	0.111
DW 2024	3/19/2024 12:30	3/19/2024 12:40	0.150	0.009	5	0.115
DW 2024	3/19/2024 12:40	3/19/2024 12:50	0.150	0.009	5	0.12
DW 2024	3/19/2024 12:50	3/19/2024 13:00	0.150	0.01	5	0.125
DW 2024	3/19/2024 13:00	3/19/2024 13:10	0.150	0.01	5	0.129
DW 2024	3/19/2024 13:10	3/19/2024 13:20	0.150	0.01	5	0.133
DW 2024	3/19/2024 13:20	3/19/2024 13:30	0.150	0.011	5	0.137
DW 2024	3/19/2024 13:30	3/19/2024 13:40	0.150	0.011	5	0.141
DW 2024	3/19/2024 13:40	3/19/2024 13:50	0.150	0.011	5	0.145
DW 2024	3/19/2024 13:50	3/19/2024 14:00	0.150	0.011	5	0.148
DW 2024	3/19/2024 14:00	3/19/2024 14:10	0.150	0.012	5	0.152
DW 2024	3/19/2024 14:10	3/19/2024 14:20	0.150	0.012	5	0.156
DW 2024	3/19/2024 14:20	3/19/2024 14:30	0.150	0.012	5	0.16
DW 2024	3/19/2024 14:30	3/19/2024 14:40	0.150	0.012	5	0.164
DW 2024	3/19/2024 14:40	3/19/2024 14:50	0.150	0.012	5	0.167
DW 2024	3/19/2024 14:50	3/19/2024 15:00	0.150	0.012	5	0.171
DW 2024	3/19/2024 15:00	3/19/2024 15:10	0.150	0.013	5	0.174
DW 2024	3/19/2024 15:10	3/19/2024 15:20	0.150	0.013	5	0.178
DW 2024	3/19/2024 15:20	3/19/2024 15:30	0.150	0.013	5	0.182
DW 2024	3/19/2024 15:30	3/19/2024 15:40	0.150	0.013	5	0.185
DW 2024	3/19/2024 15:40	3/19/2024 15:50	0.150	0.013	5	0.189
DW 2024	3/19/2024 15:50	3/19/2024 16:00	0.150	0.013	5	0.192
DW 2024	3/19/2024 16:00	3/19/2024 16:10	0.150	0.013	5	0.194
DW 2024	3/19/2024 16:10	3/19/2024 16:20	0.150	0.013	5	0.194
DW 2024	3/19/2024 16:20	3/19/2024 16:30	0.150	0.013	5	0.194
DW 2024	3/19/2024 16:30	3/19/2024 16:40	0.150	0.013	5	0.194
DW 2024	3/19/2024 16:40	3/19/2024 16:50	0.150	0.013	5	0.194
DW 2024	3/19/2024 16:50	3/19/2024 17:00	0.150	0.013	5	0.194

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/19/2024 8:00	3/19/2024 8:10	0.150	0.001	5	0
UW 2024	3/19/2024 8:10	3/19/2024 8:20	0.150	0.002	5	0
UW 2024	3/19/2024 8:20	3/19/2024 8:30	0.150	0.002	5	0
UW 2024	3/19/2024 8:30	3/19/2024 8:40	0.150	0.002	5	0
UW 2024	3/19/2024 8:40	3/19/2024 8:50	0.150	0.004	5	0
UW 2024	3/19/2024 8:50	3/19/2024 9:00	0.150	0.004	5	0
UW 2024	3/19/2024 9:00	3/19/2024 9:10	0.150	0.004	5	0
UW 2024	3/19/2024 9:10	3/19/2024 9:20	0.150	0.005	5	0
UW 2024	3/19/2024 9:20	3/19/2024 9:30	0.150	0.005	5	0
UW 2024	3/19/2024 9:30	3/19/2024 9:40	0.150	0.005	5	0
UW 2024	3/19/2024 9:40	3/19/2024 9:50	0.150	0.006	5	0
UW 2024	3/19/2024 9:50	3/19/2024 10:00	0.150	0.006	5	0
UW 2024	3/19/2024 10:00	3/19/2024 10:10	0.150	0.006	5	0
UW 2024	3/19/2024 10:10	3/19/2024 10:20	0.150	0.007	5	0
UW 2024	3/19/2024 10:20	3/19/2024 10:30	0.150	0.007	5	0
UW 2024	3/19/2024 10:30	3/19/2024 10:40	0.150	0.008	5	0
UW 2024	3/19/2024 10:40	3/19/2024 10:50	0.150	0.008	5	0
UW 2024	3/19/2024 10:50	3/19/2024 11:00	0.150	0.008	5	0
UW 2024	3/19/2024 11:00	3/19/2024 11:10	0.150	0.009	5	0
UW 2024	3/19/2024 11:10	3/19/2024 11:20	0.150	0.01	5	0
UW 2024	3/19/2024 11:20	3/19/2024 11:30	0.150	0.01	5	0
UW 2024	3/19/2024 11:30	3/19/2024 11:40	0.150	0.01	5	0
UW 2024	3/19/2024 11:40	3/19/2024 11:50	0.150	0.011	5	0
UW 2024	3/19/2024 11:50	3/19/2024 12:00	0.150	0.011	5	0
UW 2024	3/19/2024 12:00	3/19/2024 12:10	0.150	0.011	5	0
UW 2024	3/19/2024 12:10	3/19/2024 12:20	0.150	0.012	5	0
UW 2024	3/19/2024 12:20	3/19/2024 12:30	0.150	0.012	5	0
UW 2024	3/19/2024 12:30	3/19/2024 12:40	0.150	0.012	5	0
UW 2024	3/19/2024 12:40	3/19/2024 12:50	0.150	0.013	5	0
UW 2024	3/19/2024 12:50	3/19/2024 13:00	0.150	0.013	5	0
UW 2024	3/19/2024 13:00	3/19/2024 13:10	0.150	0.013	5	0
UW 2024	3/19/2024 13:10	3/19/2024 13:20	0.150	0.014	5	0
UW 2024	3/19/2024 13:20	3/19/2024 13:30	0.150	0.014	5	0
UW 2024	3/19/2024 13:30	3/19/2024 13:40	0.150	0.014	5	0
UW 2024	3/19/2024 13:40	3/19/2024 13:50	0.150	0.015	5	0
UW 2024	3/19/2024 13:50	3/19/2024 14:00	0.150	0.015	5	0
UW 2024	3/19/2024 14:00	3/19/2024 14:10	0.150	0.015	5	0
UW 2024	3/19/2024 14:10	3/19/2024 14:20	0.150	0.016	5	0
UW 2024	3/19/2024 14:20	3/19/2024 14:30	0.150	0.016	5	0
UW 2024	3/19/2024 14:30	3/19/2024 14:40	0.150	0.016	5	0
UW 2024	3/19/2024 14:40	3/19/2024 14:50	0.150	0.017	5	0
UW 2024	3/19/2024 14:50	3/19/2024 15:00	0.150	0.017	5	0
UW 2024	3/19/2024 15:00	3/19/2024 15:10	0.150	0.017	5	0
UW 2024	3/19/2024 15:10	3/19/2024 15:20	0.150	0.018	5	0
UW 2024	3/19/2024 15:20	3/19/2024 15:30	0.150	0.018	5	0
UW 2024	3/19/2024 15:30	3/19/2024 15:40	0.150	0.018	5	0
UW 2024	3/19/2024 15:40	3/19/2024 15:50	0.150	0.018	5	0
UW 2024	3/19/2024 15:50	3/19/2024 16:00	0.150	0.018	5	0
UW 2024	3/19/2024 16:00	3/19/2024 16:10	0.150	0.018	5	0
UW 2024	3/19/2024 16:10	3/19/2024 16:20	0.150	0.018	5	0
UW 2024	3/19/2024 16:20	3/19/2024 16:30	0.150	0.018	5	0
UW 2024	3/19/2024 16:30	3/19/2024 16:40	0.150	0.018	5	0
UW 2024	3/19/2024 16:40	3/19/2024 16:50	0.150	0.018	5	0
UW 2024	3/19/2024 16:50	3/19/2024 17:00	0.150	0.018	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/19/2024 8:00	3/19/2024 8:10	0.150	0.001	5	0
HS South	3/19/2024 8:10	3/19/2024 8:20	0.150	0.001	5	0
HS South	3/19/2024 8:20	3/19/2024 8:30	0.150	0.002	5	0
HS South	3/19/2024 8:30	3/19/2024 8:40	0.150	0.003	5	0
HS South	3/19/2024 8:40	3/19/2024 8:50	0.150	0.003	5	0
HS South	3/19/2024 8:50	3/19/2024 9:00	0.150	0.003	5	0
HS South	3/19/2024 9:00	3/19/2024 9:10	0.150	0.004	5	0
HS South	3/19/2024 9:10	3/19/2024 9:20	0.150	0.004	5	0
HS South	3/19/2024 9:20	3/19/2024 9:30	0.150	0.004	5	0
HS South	3/19/2024 9:30	3/19/2024 9:40	0.150	0.004	5	0
HS South	3/19/2024 9:40	3/19/2024 9:50	0.150	0.004	5	0
HS South	3/19/2024 9:50	3/19/2024 10:00	0.150	0.004	5	0
HS South	3/19/2024 10:00	3/19/2024 10:10	0.150	0.004	5	0
HS South	3/19/2024 10:10	3/19/2024 10:20	0.150	0.005	5	0
HS South	3/19/2024 10:20	3/19/2024 10:30	0.150	0.005	5	0
HS South	3/19/2024 10:30	3/19/2024 10:40	0.150	0.005	5	0
HS South	3/19/2024 10:40	3/19/2024 10:50	0.150	0.005	5	0
HS South	3/19/2024 10:50	3/19/2024 11:00	0.150	0.006	5	0
HS South	3/19/2024 11:00	3/19/2024 11:10	0.150	0.006	5	0
HS South	3/19/2024 11:10	3/19/2024 11:20	0.150	0.006	5	0
HS South	3/19/2024 11:20	3/19/2024 11:30	0.150	0.006	5	0
HS South	3/19/2024 11:30	3/19/2024 11:40	0.150	0.006	5	0
HS South	3/19/2024 11:40	3/19/2024 11:50	0.150	0.007	5	0
HS South	3/19/2024 11:50	3/19/2024 12:00	0.150	0.007	5	0
HS South	3/19/2024 12:00	3/19/2024 12:10	0.150	0.007	5	0
HS South	3/19/2024 12:10	3/19/2024 12:20	0.150	0.007	5	0
HS South	3/19/2024 12:20	3/19/2024 12:30	0.150	0.008	5	0
HS South	3/19/2024 12:30	3/19/2024 12:40	0.150	0.008	5	0
HS South	3/19/2024 12:40	3/19/2024 12:50	0.150	0.008	5	0
HS South	3/19/2024 12:50	3/19/2024 13:00	0.150	0.008	5	0
HS South	3/19/2024 13:00	3/19/2024 13:10	0.150	0.009	5	0
HS South	3/19/2024 13:10	3/19/2024 13:20	0.150	0.009	5	0
HS South	3/19/2024 13:20	3/19/2024 13:30	0.150	0.009	5	0
HS South	3/19/2024 13:30	3/19/2024 13:40	0.150	0.009	5	0
HS South	3/19/2024 13:40	3/19/2024 13:50	0.150	0.01	5	0
HS South	3/19/2024 13:50	3/19/2024 14:00	0.150	0.01	5	0
HS South	3/19/2024 14:00	3/19/2024 14:10	0.150	0.01	5	0
HS South	3/19/2024 14:10	3/19/2024 14:20	0.150	0.01	5	0
HS South	3/19/2024 14:20	3/19/2024 14:30	0.150	0.01	5	0
HS South	3/19/2024 14:30	3/19/2024 14:40	0.150	0.01	5	0
HS South	3/19/2024 14:40	3/19/2024 14:50	0.150	0.011	5	0
HS South	3/19/2024 14:50	3/19/2024 15:00	0.150	0.011	5	0
HS South	3/19/2024 15:00	3/19/2024 15:10	0.150	0.011	5	0
HS South	3/19/2024 15:10	3/19/2024 15:20	0.150	0.012	5	0
HS South	3/19/2024 15:20	3/19/2024 15:30	0.150	0.012	5	0
HS South	3/19/2024 15:30	3/19/2024 15:40	0.150	0.012	5	0
HS South	3/19/2024 15:40	3/19/2024 15:50	0.150	0.012	5	0
HS South	3/19/2024 15:50	3/19/2024 16:00	0.150	0.012	5	0
HS South	3/19/2024 16:00	3/19/2024 16:10	0.150	0.012	5	0
HS South	3/19/2024 16:10	3/19/2024 16:20	0.150	0.012	5	0
HS South	3/19/2024 16:20	3/19/2024 16:30	0.150	0.012	5	0
HS South	3/19/2024 16:30	3/19/2024 16:40	0.150	0.012	5	0
HS South	3/19/2024 16:40	3/19/2024 16:50	0.150	0.012	5	0
HS South	3/19/2024 16:50	3/19/2024 17:00	0.150	0.012	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/19/2024 8:00	3/19/2024 8:10	0.150	0.006	5	0
PER1 2024	3/19/2024 8:10	3/19/2024 8:20	0.150	0.007	5	0
PER1 2024	3/19/2024 8:20	3/19/2024 8:30	0.150	0.009	5	0
PER1 2024	3/19/2024 8:30	3/19/2024 8:40	0.150	0.033	5	0
PER1 2024	3/19/2024 8:40	3/19/2024 8:50	0.150	0.035	5	0
PER1 2024	3/19/2024 8:50	3/19/2024 9:00	0.150	0.035	5	0
PER1 2024	3/19/2024 9:00	3/19/2024 9:10	0.150	0.036	5	0
PER1 2024	3/19/2024 9:10	3/19/2024 9:20	0.150	0.036	5	0
PER1 2024	3/19/2024 9:20	3/19/2024 9:30	0.150	0.037	5	0
PER1 2024	3/19/2024 9:30	3/19/2024 9:40	0.150	0.038	5	0
PER1 2024	3/19/2024 9:40	3/19/2024 9:50	0.150	0.039	5	0
PER1 2024	3/19/2024 9:50	3/19/2024 10:00	0.150	0.039	5	0
PER1 2024	3/19/2024 10:00	3/19/2024 10:10	0.150	0.04	5	0
PER1 2024	3/19/2024 10:10	3/19/2024 10:20	0.150	0.04	5	0
PER1 2024	3/19/2024 10:20	3/19/2024 10:30	0.150	0.04	5	0
PER1 2024	3/19/2024 10:30	3/19/2024 10:40	0.150	0.041	5	0
PER1 2024	3/19/2024 10:40	3/19/2024 10:50	0.150	0.041	5	0
PER1 2024	3/19/2024 10:50	3/19/2024 11:00	0.150	0.042	5	0
PER1 2024	3/19/2024 11:00	3/19/2024 11:10	0.150	0.042	5	0
PER1 2024	3/19/2024 11:10	3/19/2024 11:20	0.150	0.043	5	0
PER1 2024	3/19/2024 11:20	3/19/2024 11:30	0.150	0.043	5	0
PER1 2024	3/19/2024 11:30	3/19/2024 11:40	0.150	0.044	5	0
PER1 2024	3/19/2024 11:40	3/19/2024 11:50	0.150	0.045	5	0
PER1 2024	3/19/2024 11:50	3/19/2024 12:00	0.150	0.045	5	0
PER1 2024	3/19/2024 12:00	3/19/2024 12:10	0.150	0.045	5	0
PER1 2024	3/19/2024 12:10	3/19/2024 12:20	0.150	0.046	5	0
PER1 2024	3/19/2024 12:20	3/19/2024 12:30	0.150	0.046	5	0
PER1 2024	3/19/2024 12:30	3/19/2024 12:40	0.150	0.047	5	0
PER1 2024	3/19/2024 12:40	3/19/2024 12:50	0.150	0.047	5	0
PER1 2024	3/19/2024 12:50	3/19/2024 13:00	0.150	0.048	5	0
PER1 2024	3/19/2024 13:00	3/19/2024 13:10	0.150	0.048	5	0.001
PER1 2024	3/19/2024 13:10	3/19/2024 13:20	0.150	0.049	5	0.001
PER1 2024	3/19/2024 13:20	3/19/2024 13:30	0.150	0.05	5	0.001
PER1 2024	3/19/2024 13:30	3/19/2024 13:40	0.150	0.051	5	0.001
PER1 2024	3/19/2024 13:40	3/19/2024 13:50	0.150	0.054	5	0.001
PER1 2024	3/19/2024 13:50	3/19/2024 14:00	0.150	0.055	5	0.001
PER1 2024	3/19/2024 14:00	3/19/2024 14:10	0.150	0.055	5	0.001
PER1 2024	3/19/2024 14:10	3/19/2024 14:20	0.150	0.056	5	0.001
PER1 2024	3/19/2024 14:20	3/19/2024 14:30	0.150	0.057	5	0.001
PER1 2024	3/19/2024 14:30	3/19/2024 14:40	0.150	0.057	5	0.001
PER1 2024	3/19/2024 14:40	3/19/2024 14:50	0.150	0.057	5	0.001
PER1 2024	3/19/2024 14:50	3/19/2024 15:00	0.150	0.058	5	0.003
PER1 2024	3/19/2024 15:00	3/19/2024 15:10	0.150	0.058	5	0.003
PER1 2024	3/19/2024 15:10	3/19/2024 15:20	0.150	0.059	5	0.003
PER1 2024	3/19/2024 15:20	3/19/2024 15:30	0.150	0.059	5	0.003
PER1 2024	3/19/2024 15:30	3/19/2024 15:40	0.150	0.059	5	0.003
PER1 2024	3/19/2024 15:40	3/19/2024 15:50	0.150	0.059	5	0.003
PER1 2024	3/19/2024 15:50	3/19/2024 16:00	0.150	0.059	5	0.003
PER1 2024	3/19/2024 16:00	3/19/2024 16:10	0.150	0.059	5	0
PER1 2024	3/19/2024 16:10	3/19/2024 16:20	0.150	0	5	0
PER1 2024	3/19/2024 16:20	3/19/2024 16:30	0.150	0	5	0
PER1 2024	3/19/2024 16:30	3/19/2024 16:40	0.150	0	5	0
PER1 2024	3/19/2024 16:40	3/19/2024 16:50	0.150	0	5	0
PER1 2024	3/19/2024 16:50	3/19/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/19/2024 8:00	3/19/2024 8:10	0.150	0.001	5	0
PER2 2024	3/19/2024 8:10	3/19/2024 8:20	0.150	0.001	5	0
PER2 2024	3/19/2024 8:20	3/19/2024 8:30	0.150	0.001	5	0
PER2 2024	3/19/2024 8:30	3/19/2024 8:40	0.150	0.002	5	0
PER2 2024	3/19/2024 8:40	3/19/2024 8:50	0.150	0.002	5	0
PER2 2024	3/19/2024 8:50	3/19/2024 9:00	0.150	0.003	5	0
PER2 2024	3/19/2024 9:00	3/19/2024 9:10	0.150	0.003	5	0
PER2 2024	3/19/2024 9:10	3/19/2024 9:20	0.150	0.003	5	0
PER2 2024	3/19/2024 9:20	3/19/2024 9:30	0.150	0.003	5	0
PER2 2024	3/19/2024 9:30	3/19/2024 9:40	0.150	0.004	5	0
PER2 2024	3/19/2024 9:40	3/19/2024 9:50	0.150	0.004	5	0
PER2 2024	3/19/2024 9:50	3/19/2024 10:00	0.150	0.004	5	0
PER2 2024	3/19/2024 10:00	3/19/2024 10:10	0.150	0.004	5	0
PER2 2024	3/19/2024 10:10	3/19/2024 10:20	0.150	0.004	5	0
PER2 2024	3/19/2024 10:20	3/19/2024 10:30	0.150	0.005	5	0
PER2 2024	3/19/2024 10:30	3/19/2024 10:40	0.150	0.005	5	0
PER2 2024	3/19/2024 10:40	3/19/2024 10:50	0.150	0.005	5	0
PER2 2024	3/19/2024 10:50	3/19/2024 11:00	0.150	0.006	5	0
PER2 2024	3/19/2024 11:00	3/19/2024 11:10	0.150	0.006	5	0
PER2 2024	3/19/2024 11:10	3/19/2024 11:20	0.150	0.006	5	0
PER2 2024	3/19/2024 11:20	3/19/2024 11:30	0.150	0.006	5	0
PER2 2024	3/19/2024 11:30	3/19/2024 11:40	0.150	0.006	5	0
PER2 2024	3/19/2024 11:40	3/19/2024 11:50	0.150	0.007	5	0
PER2 2024	3/19/2024 11:50	3/19/2024 12:00	0.150	0.007	5	0
PER2 2024	3/19/2024 12:00	3/19/2024 12:10	0.150	0.007	5	0
PER2 2024	3/19/2024 12:10	3/19/2024 12:20	0.150	0.007	5	0
PER2 2024	3/19/2024 12:20	3/19/2024 12:30	0.150	0.007	5	0
PER2 2024	3/19/2024 12:30	3/19/2024 12:40	0.150	0.007	5	0
PER2 2024	3/19/2024 12:40	3/19/2024 12:50	0.150	0.008	5	0
PER2 2024	3/19/2024 12:50	3/19/2024 13:00	0.150	0.008	5	0
PER2 2024	3/19/2024 13:00	3/19/2024 13:10	0.150	0.008	5	0
PER2 2024	3/19/2024 13:10	3/19/2024 13:20	0.150	0.008	5	0
PER2 2024	3/19/2024 13:20	3/19/2024 13:30	0.150	0.009	5	0
PER2 2024	3/19/2024 13:30	3/19/2024 13:40	0.150	0.009	5	0
PER2 2024	3/19/2024 13:40	3/19/2024 13:50	0.150	0.009	5	0
PER2 2024	3/19/2024 13:50	3/19/2024 14:00	0.150	0.009	5	0
PER2 2024	3/19/2024 14:00	3/19/2024 14:10	0.150	0.01	5	0
PER2 2024	3/19/2024 14:10	3/19/2024 14:20	0.150	0.01	5	0
PER2 2024	3/19/2024 14:20	3/19/2024 14:30	0.150	0.011	5	0
PER2 2024	3/19/2024 14:30	3/19/2024 14:40	0.150	0.011	5	0
PER2 2024	3/19/2024 14:40	3/19/2024 14:50	0.150	0.011	5	0
PER2 2024	3/19/2024 14:50	3/19/2024 15:00	0.150	0.012	5	0
PER2 2024	3/19/2024 15:00	3/19/2024 15:10	0.150	0.012	5	0
PER2 2024	3/19/2024 15:10	3/19/2024 15:20	0.150	0.012	5	0
PER2 2024	3/19/2024 15:20	3/19/2024 15:30	0.150	0.012	5	0
PER2 2024	3/19/2024 15:30	3/19/2024 15:40	0.150	0.012	5	0
PER2 2024	3/19/2024 15:40	3/19/2024 15:50	0.150	0.013	5	0
PER2 2024	3/19/2024 15:50	3/19/2024 16:00	0.150	0.013	5	0
PER2 2024	3/19/2024 16:00	3/19/2024 16:10	0.150	0.013	5	0
PER2 2024	3/19/2024 16:10	3/19/2024 16:20	0.150	0.013	5	0
PER2 2024	3/19/2024 16:20	3/19/2024 16:30	0.150	0.013	5	0
PER2 2024	3/19/2024 16:30	3/19/2024 16:40	0.150	0.013	5	0
PER2 2024	3/19/2024 16:40	3/19/2024 16:50	0.150	0.013	5	0
PER2 2024	3/19/2024 16:50	3/19/2024 17:00	0.150	0.013	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/20/2024

Weather: 35 deg. F, Sunny

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation and foundation development.
- 2) Alba exports 6 loads (~120 CY) of material from WC-25 for off-site disposal at the HFR facility.
- 3) Alba exports 3 loads (~ 60 CY) of material from WC-25 for off-site disposal at the MSM facility.
- 4) Alba exports 14 loads (~ 280 CY) of material from WC-25 for off-site disposal at the MCUA facility.
- 5) ECD continued marine waterfront remedial excavation.

Is the dewatering system operating: YES NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP tables and graphs are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	120	0	60	0	280
Total:(CY)	4285	0	7025	1520	2500

Site Layout Map and Excavation Figures

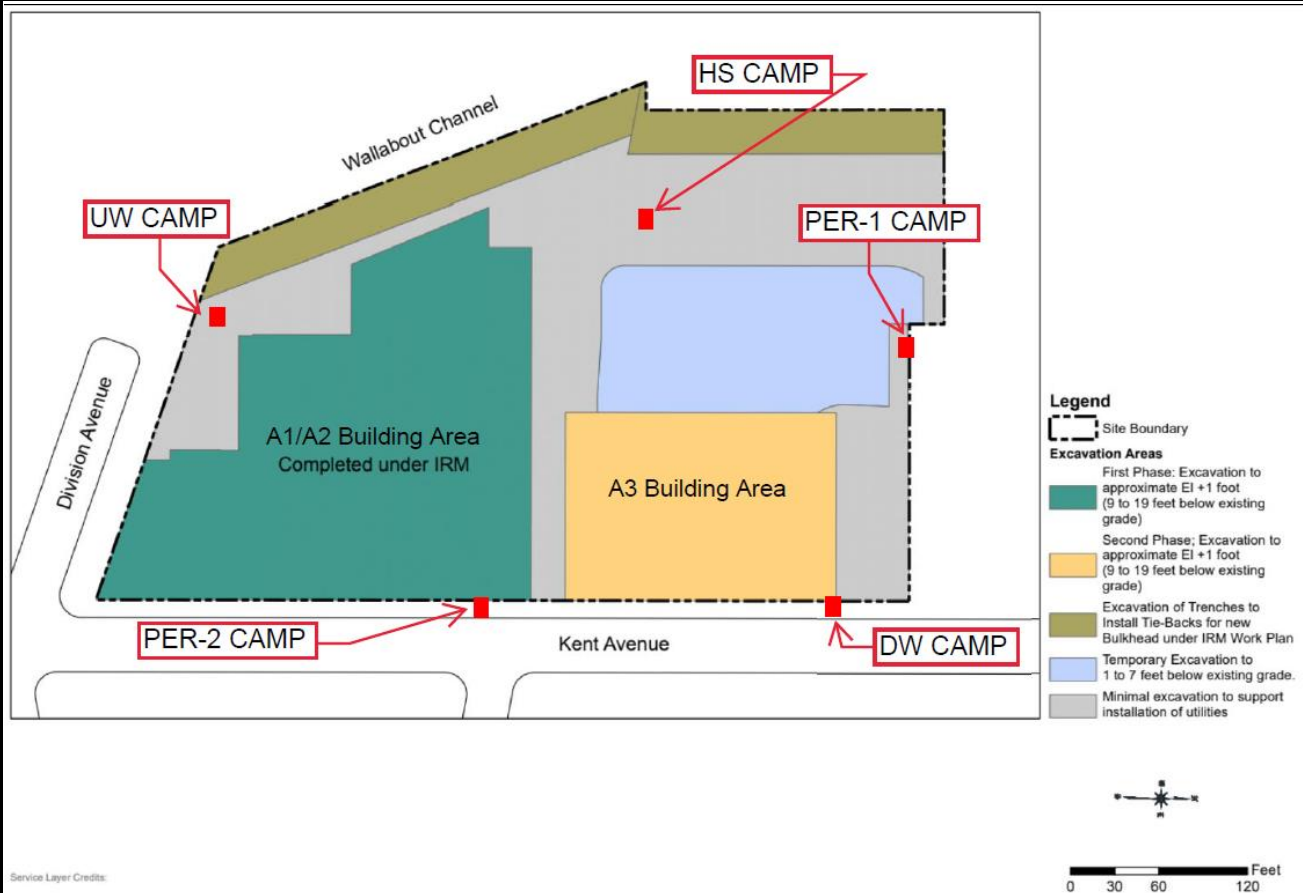

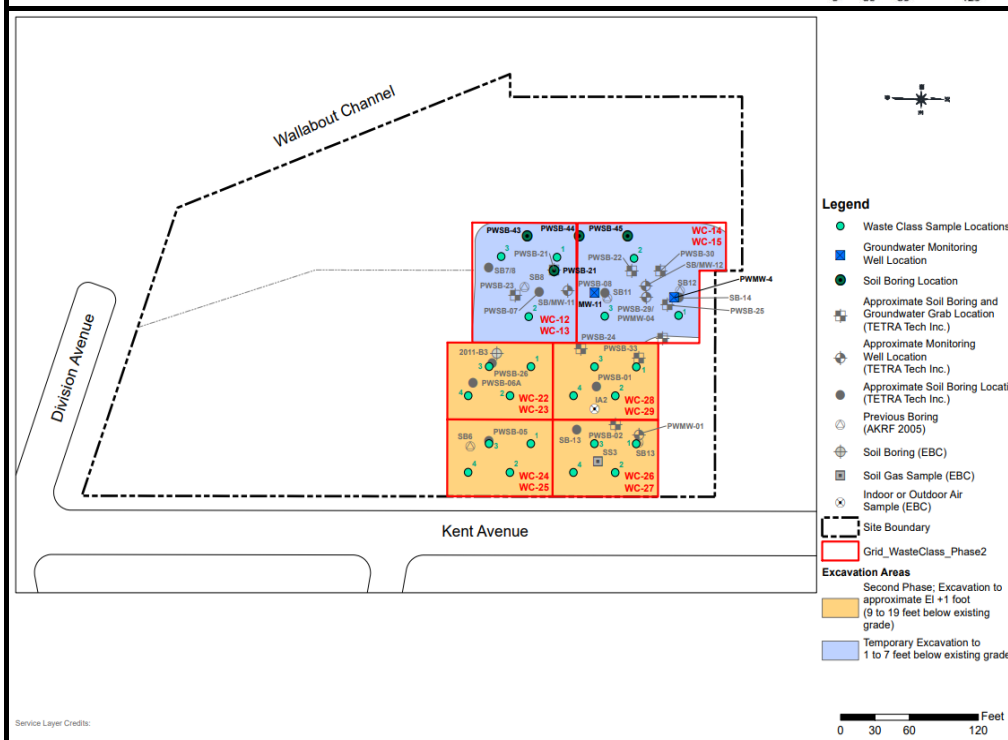
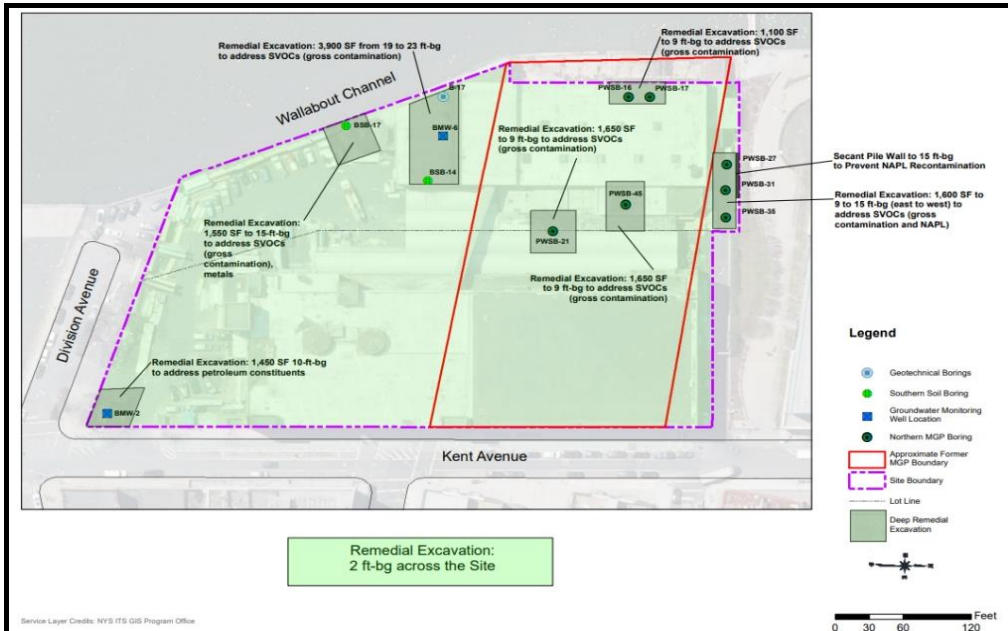


Photo 1:

View of Site conditions,
soil excavation and
truck loading facing east.



Photo 2:

View of Site conditions
and activities facing
west.

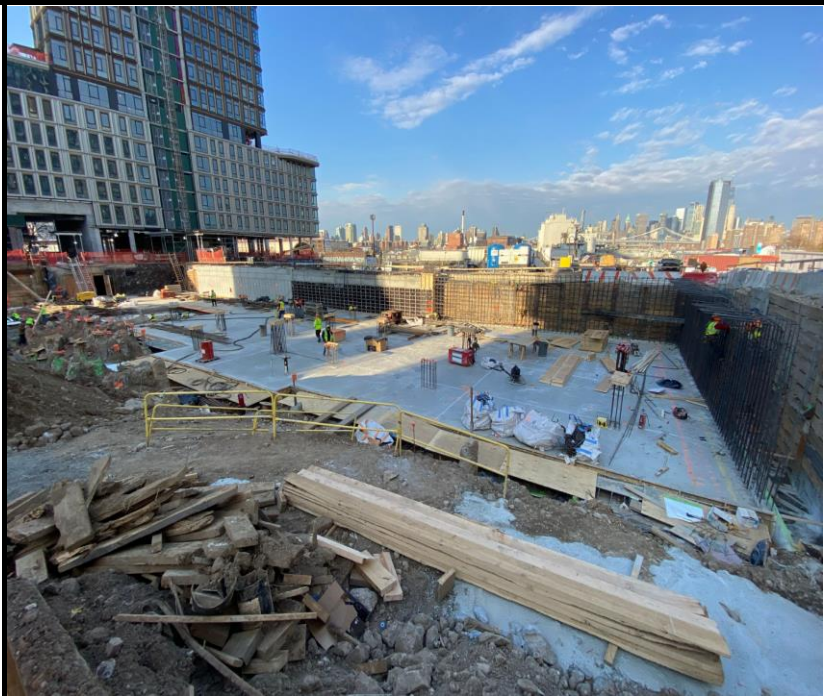


Photo 3:
View of truck
loading for off-site
soil disposal.




Photo 4:
View of the
waterfront remedial
excavation.



CAMP:
Downwind
Particulates

Dust Levels


0.03 mg/m³ 0.031 mg/m³

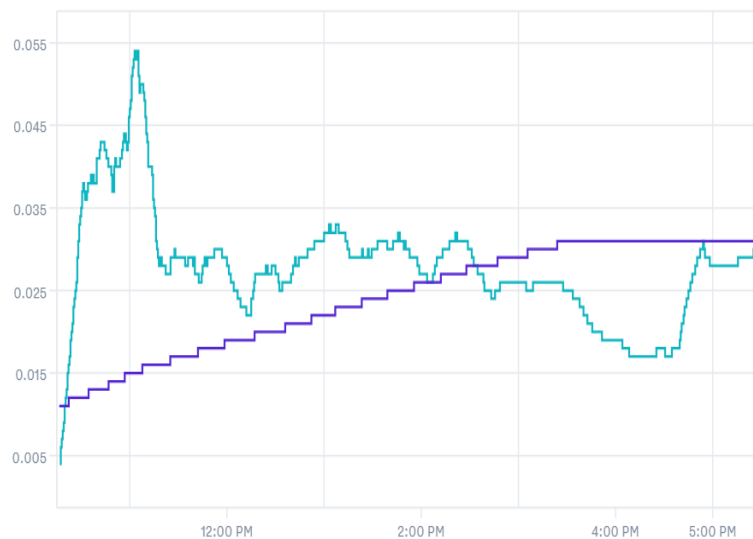

CAMP:
Downwind VOCs

VOC Levels


0.156 ppm 0.279 ppm

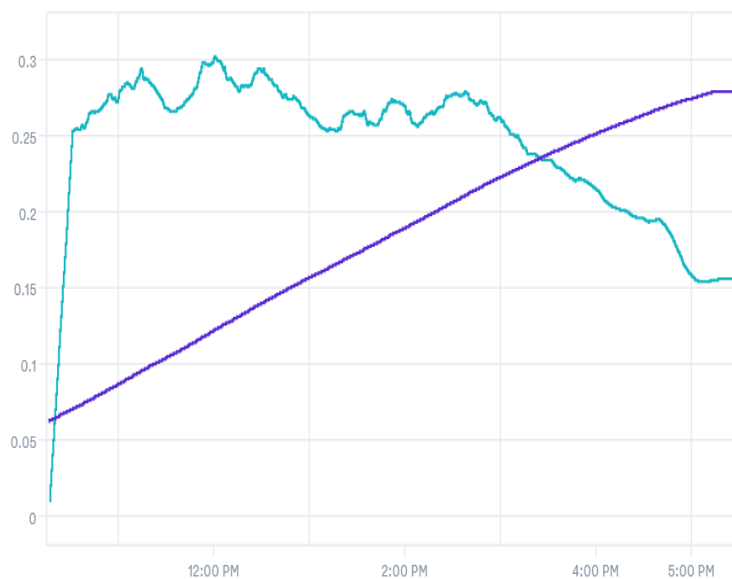

CAMP:
Upwind Particulates

Dust Levels


0.035 mg/m³ 0.032 mg/m³ 0.15

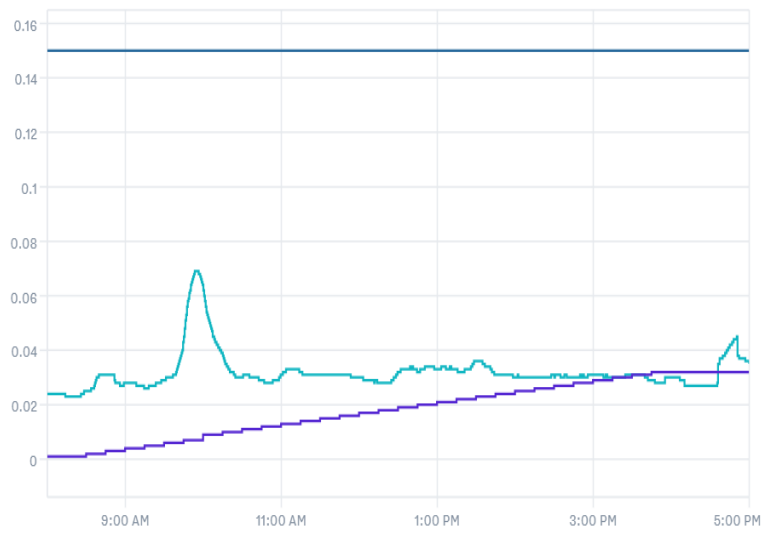

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

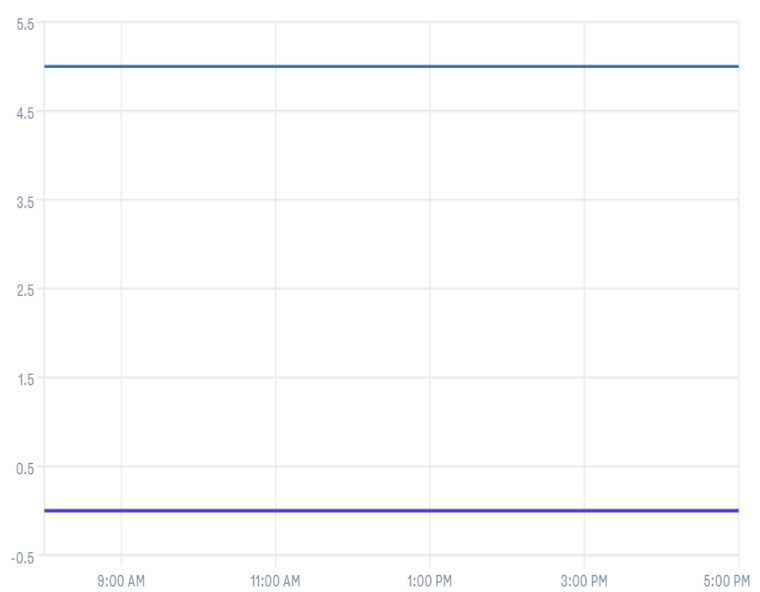

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/20/2024 8:00	3/20/2024 8:10	0.150	0.013	5	0.194
DW 2024	3/20/2024 8:10	3/20/2024 8:20	0.150	0.013	5	0.194
DW 2024	3/20/2024 8:20	3/20/2024 8:30	0.150	0.013	5	0.194
DW 2024	3/20/2024 8:30	3/20/2024 8:40	0.150	0.013	5	0.194
DW 2024	3/20/2024 8:40	3/20/2024 8:50	0.150	0.013	5	0.194
DW 2024	3/20/2024 8:50	3/20/2024 9:00	0.150	0.013	5	0.194
DW 2024	3/20/2024 9:00	3/20/2024 9:10	0.150	0.013	5	0.194
DW 2024	3/20/2024 9:10	3/20/2024 9:20	0.150	0.013	5	0.194
DW 2024	3/20/2024 9:20	3/20/2024 9:30	0.150	0.013	5	0.194
DW 2024	3/20/2024 9:30	3/20/2024 9:40	0.150	0.013	5	0.194
DW 2024	3/20/2024 9:40	3/20/2024 9:50	0.150	0.013	5	0.194
DW 2024	3/20/2024 9:50	3/20/2024 10:00	0.150	0.013	5	0.194
DW 2024	3/20/2024 10:00	3/20/2024 10:10	0.150	0.013	5	0.194
DW 2024	3/20/2024 10:10	3/20/2024 10:20	0.150	0.011	5	0.064
DW 2024	3/20/2024 10:20	3/20/2024 10:30	0.150	0.012	5	0.07
DW 2024	3/20/2024 10:30	3/20/2024 10:40	0.150	0.013	5	0.075
DW 2024	3/20/2024 10:40	3/20/2024 10:50	0.150	0.014	5	0.081
DW 2024	3/20/2024 10:50	3/20/2024 11:00	0.150	0.015	5	0.087
DW 2024	3/20/2024 11:00	3/20/2024 11:10	0.150	0.016	5	0.093
DW 2024	3/20/2024 11:10	3/20/2024 11:20	0.150	0.016	5	0.099
DW 2024	3/20/2024 11:20	3/20/2024 11:30	0.150	0.017	5	0.104
DW 2024	3/20/2024 11:30	3/20/2024 11:40	0.150	0.017	5	0.11
DW 2024	3/20/2024 11:40	3/20/2024 11:50	0.150	0.018	5	0.116
DW 2024	3/20/2024 11:50	3/20/2024 12:00	0.150	0.019	5	0.122
DW 2024	3/20/2024 12:00	3/20/2024 12:10	0.150	0.019	5	0.128
DW 2024	3/20/2024 12:10	3/20/2024 12:20	0.150	0.02	5	0.134
DW 2024	3/20/2024 12:20	3/20/2024 12:30	0.150	0.02	5	0.14
DW 2024	3/20/2024 12:30	3/20/2024 12:40	0.150	0.021	5	0.146
DW 2024	3/20/2024 12:40	3/20/2024 12:50	0.150	0.021	5	0.151
DW 2024	3/20/2024 12:50	3/20/2024 13:00	0.150	0.022	5	0.157
DW 2024	3/20/2024 13:00	3/20/2024 13:10	0.150	0.023	5	0.162
DW 2024	3/20/2024 13:10	3/20/2024 13:20	0.150	0.023	5	0.167
DW 2024	3/20/2024 13:20	3/20/2024 13:30	0.150	0.024	5	0.173
DW 2024	3/20/2024 13:30	3/20/2024 13:40	0.150	0.025	5	0.178
DW 2024	3/20/2024 13:40	3/20/2024 13:50	0.150	0.025	5	0.184
DW 2024	3/20/2024 13:50	3/20/2024 14:00	0.150	0.026	5	0.189
DW 2024	3/20/2024 14:00	3/20/2024 14:10	0.150	0.026	5	0.195
DW 2024	3/20/2024 14:10	3/20/2024 14:20	0.150	0.027	5	0.2
DW 2024	3/20/2024 14:20	3/20/2024 14:30	0.150	0.028	5	0.206
DW 2024	3/20/2024 14:30	3/20/2024 14:40	0.150	0.028	5	0.212
DW 2024	3/20/2024 14:40	3/20/2024 14:50	0.150	0.029	5	0.218
DW 2024	3/20/2024 14:50	3/20/2024 15:00	0.150	0.029	5	0.223
DW 2024	3/20/2024 15:00	3/20/2024 15:10	0.150	0.03	5	0.228
DW 2024	3/20/2024 15:10	3/20/2024 15:20	0.150	0.03	5	0.233
DW 2024	3/20/2024 15:20	3/20/2024 15:30	0.150	0.031	5	0.238
DW 2024	3/20/2024 15:30	3/20/2024 15:40	0.150	0.031	5	0.242
DW 2024	3/20/2024 15:40	3/20/2024 15:50	0.150	0.031	5	0.247
DW 2024	3/20/2024 15:50	3/20/2024 16:00	0.150	0.031	5	0.251
DW 2024	3/20/2024 16:00	3/20/2024 16:10	0.150	0.031	5	0.256
DW 2024	3/20/2024 16:10	3/20/2024 16:20	0.150	0.031	5	0.26
DW 2024	3/20/2024 16:20	3/20/2024 16:30	0.150	0.031	5	0.264
DW 2024	3/20/2024 16:30	3/20/2024 16:40	0.150	0.031	5	0.268
DW 2024	3/20/2024 16:40	3/20/2024 16:50	0.150	0.031	5	0.271
DW 2024	3/20/2024 16:50	3/20/2024 17:00	0.150	0.031	5	0.274

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/20/2024 8:00	3/20/2024 8:10	0.150	0.001	5	0
UW 2024	3/20/2024 8:10	3/20/2024 8:20	0.150	0.001	5	0
UW 2024	3/20/2024 8:20	3/20/2024 8:30	0.150	0.002	5	0
UW 2024	3/20/2024 8:30	3/20/2024 8:40	0.150	0.002	5	0
UW 2024	3/20/2024 8:40	3/20/2024 8:50	0.150	0.003	5	0
UW 2024	3/20/2024 8:50	3/20/2024 9:00	0.150	0.004	5	0
UW 2024	3/20/2024 9:00	3/20/2024 9:10	0.150	0.004	5	0
UW 2024	3/20/2024 9:10	3/20/2024 9:20	0.150	0.005	5	0
UW 2024	3/20/2024 9:20	3/20/2024 9:30	0.150	0.006	5	0
UW 2024	3/20/2024 9:30	3/20/2024 9:40	0.150	0.006	5	0
UW 2024	3/20/2024 9:40	3/20/2024 9:50	0.150	0.007	5	0
UW 2024	3/20/2024 9:50	3/20/2024 10:00	0.150	0.009	5	0
UW 2024	3/20/2024 10:00	3/20/2024 10:10	0.150	0.009	5	0
UW 2024	3/20/2024 10:10	3/20/2024 10:20	0.150	0.01	5	0
UW 2024	3/20/2024 10:20	3/20/2024 10:30	0.150	0.011	5	0
UW 2024	3/20/2024 10:30	3/20/2024 10:40	0.150	0.011	5	0
UW 2024	3/20/2024 10:40	3/20/2024 10:50	0.150	0.012	5	0
UW 2024	3/20/2024 10:50	3/20/2024 11:00	0.150	0.013	5	0
UW 2024	3/20/2024 11:00	3/20/2024 11:10	0.150	0.013	5	0
UW 2024	3/20/2024 11:10	3/20/2024 11:20	0.150	0.014	5	0
UW 2024	3/20/2024 11:20	3/20/2024 11:30	0.150	0.015	5	0
UW 2024	3/20/2024 11:30	3/20/2024 11:40	0.150	0.015	5	0
UW 2024	3/20/2024 11:40	3/20/2024 11:50	0.150	0.016	5	0
UW 2024	3/20/2024 11:50	3/20/2024 12:00	0.150	0.017	5	0
UW 2024	3/20/2024 12:00	3/20/2024 12:10	0.150	0.017	5	0
UW 2024	3/20/2024 12:10	3/20/2024 12:20	0.150	0.018	5	0
UW 2024	3/20/2024 12:20	3/20/2024 12:30	0.150	0.019	5	0
UW 2024	3/20/2024 12:30	3/20/2024 12:40	0.150	0.019	5	0
UW 2024	3/20/2024 12:40	3/20/2024 12:50	0.150	0.02	5	0
UW 2024	3/20/2024 12:50	3/20/2024 13:00	0.150	0.021	5	0
UW 2024	3/20/2024 13:00	3/20/2024 13:10	0.150	0.021	5	0
UW 2024	3/20/2024 13:10	3/20/2024 13:20	0.150	0.022	5	0
UW 2024	3/20/2024 13:20	3/20/2024 13:30	0.150	0.023	5	0
UW 2024	3/20/2024 13:30	3/20/2024 13:40	0.150	0.023	5	0
UW 2024	3/20/2024 13:40	3/20/2024 13:50	0.150	0.024	5	0
UW 2024	3/20/2024 13:50	3/20/2024 14:00	0.150	0.025	5	0
UW 2024	3/20/2024 14:00	3/20/2024 14:10	0.150	0.025	5	0
UW 2024	3/20/2024 14:10	3/20/2024 14:20	0.150	0.026	5	0
UW 2024	3/20/2024 14:20	3/20/2024 14:30	0.150	0.027	5	0
UW 2024	3/20/2024 14:30	3/20/2024 14:40	0.150	0.027	5	0
UW 2024	3/20/2024 14:40	3/20/2024 14:50	0.150	0.028	5	0
UW 2024	3/20/2024 14:50	3/20/2024 15:00	0.150	0.029	5	0
UW 2024	3/20/2024 15:00	3/20/2024 15:10	0.150	0.029	5	0
UW 2024	3/20/2024 15:10	3/20/2024 15:20	0.150	0.03	5	0
UW 2024	3/20/2024 15:20	3/20/2024 15:30	0.150	0.031	5	0
UW 2024	3/20/2024 15:30	3/20/2024 15:40	0.150	0.031	5	0
UW 2024	3/20/2024 15:40	3/20/2024 15:50	0.150	0.032	5	0
UW 2024	3/20/2024 15:50	3/20/2024 16:00	0.150	0.032	5	0
UW 2024	3/20/2024 16:00	3/20/2024 16:10	0.150	0.032	5	0
UW 2024	3/20/2024 16:10	3/20/2024 16:20	0.150	0.032	5	0
UW 2024	3/20/2024 16:20	3/20/2024 16:30	0.150	0.032	5	0
UW 2024	3/20/2024 16:30	3/20/2024 16:40	0.150	0.032	5	0
UW 2024	3/20/2024 16:40	3/20/2024 16:50	0.150	0.032	5	0
UW 2024	3/20/2024 16:50	3/20/2024 17:00	0.150	0.032	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/20/2024 8:00	3/20/2024 8:10	0.150	0.002	5	0
HS South	3/20/2024 8:10	3/20/2024 8:20	0.150	0.002	5	0
HS South	3/20/2024 8:20	3/20/2024 8:30	0.150	0.003	5	0
HS South	3/20/2024 8:30	3/20/2024 8:40	0.150	0.003	5	0
HS South	3/20/2024 8:40	3/20/2024 8:50	0.150	0.004	5	0
HS South	3/20/2024 8:50	3/20/2024 9:00	0.150	0.005	5	0
HS South	3/20/2024 9:00	3/20/2024 9:10	0.150	0.005	5	0
HS South	3/20/2024 9:10	3/20/2024 9:20	0.150	0.006	5	0
HS South	3/20/2024 9:20	3/20/2024 9:30	0.150	0.007	5	0
HS South	3/20/2024 9:30	3/20/2024 9:40	0.150	0.008	5	0
HS South	3/20/2024 9:40	3/20/2024 9:50	0.150	0.01	5	0
HS South	3/20/2024 9:50	3/20/2024 10:00	0.150	0.011	5	0
HS South	3/20/2024 10:00	3/20/2024 10:10	0.150	0.012	5	0
HS South	3/20/2024 10:10	3/20/2024 10:20	0.150	0.012	5	0
HS South	3/20/2024 10:20	3/20/2024 10:30	0.150	0.012	5	0
HS South	3/20/2024 10:30	3/20/2024 10:40	0.150	0.013	5	0
HS South	3/20/2024 10:40	3/20/2024 10:50	0.150	0.014	5	0
HS South	3/20/2024 10:50	3/20/2024 11:00	0.150	0.014	5	0
HS South	3/20/2024 11:00	3/20/2024 11:10	0.150	0.014	5	0
HS South	3/20/2024 11:10	3/20/2024 11:20	0.150	0.015	5	0
HS South	3/20/2024 11:20	3/20/2024 11:30	0.150	0.016	5	0
HS South	3/20/2024 11:30	3/20/2024 11:40	0.150	0.016	5	0
HS South	3/20/2024 11:40	3/20/2024 11:50	0.150	0.017	5	0
HS South	3/20/2024 11:50	3/20/2024 12:00	0.150	0.018	5	0
HS South	3/20/2024 12:00	3/20/2024 12:10	0.150	0.018	5	0
HS South	3/20/2024 12:10	3/20/2024 12:20	0.150	0.019	5	0
HS South	3/20/2024 12:20	3/20/2024 12:30	0.150	0.019	5	0
HS South	3/20/2024 12:30	3/20/2024 12:40	0.150	0.02	5	0
HS South	3/20/2024 12:40	3/20/2024 12:50	0.150	0.02	5	0
HS South	3/20/2024 12:50	3/20/2024 13:00	0.150	0.021	5	0
HS South	3/20/2024 13:00	3/20/2024 13:10	0.150	0.021	5	0
HS South	3/20/2024 13:10	3/20/2024 13:20	0.150	0.022	5	0
HS South	3/20/2024 13:20	3/20/2024 13:30	0.150	0.022	5	0
HS South	3/20/2024 13:30	3/20/2024 13:40	0.150	0.023	5	0
HS South	3/20/2024 13:40	3/20/2024 13:50	0.150	0.023	5	0
HS South	3/20/2024 13:50	3/20/2024 14:00	0.150	0.023	5	0
HS South	3/20/2024 14:00	3/20/2024 14:10	0.150	0.023	5	0
HS South	3/20/2024 14:10	3/20/2024 14:20	0.150	0.023	5	0
HS South	3/20/2024 14:20	3/20/2024 14:30	0.150	0.023	5	0
HS South	3/20/2024 14:30	3/20/2024 14:40	0.150	0.023	5	0
HS South	3/20/2024 14:40	3/20/2024 14:50	0.150	0.023	5	0
HS South	3/20/2024 14:50	3/20/2024 15:00	0.150	0.023	5	0
HS South	3/20/2024 15:00	3/20/2024 15:10	0.150	0.023	5	0
HS South	3/20/2024 15:10	3/20/2024 15:20	0.150	0.023	5	0
HS South	3/20/2024 15:20	3/20/2024 15:30	0.150	0.023	5	0
HS South	3/20/2024 15:30	3/20/2024 15:40	0.150	0.023	5	0
HS South	3/20/2024 15:40	3/20/2024 15:50	0.150	0.023	5	0
HS South	3/20/2024 15:50	3/20/2024 16:00	0.150	0.023	5	0
HS South	3/20/2024 16:00	3/20/2024 16:10	0.150	0.023	5	0
HS South	3/20/2024 16:10	3/20/2024 16:20	0.150	0.023	5	0
HS South	3/20/2024 16:20	3/20/2024 16:30	0.150	0.023	5	0
HS South	3/20/2024 16:30	3/20/2024 16:40	0.150	0.023	5	0
HS South	3/20/2024 16:40	3/20/2024 16:50	0.150	0.023	5	0
HS South	3/20/2024 16:50	3/20/2024 17:00	0.150	0.023	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/20/2024 8:00	3/20/2024 8:10	0.150	0.002	5	0
PER1 2024	3/20/2024 8:10	3/20/2024 8:20	0.150	0.002	5	0
PER1 2024	3/20/2024 8:20	3/20/2024 8:30	0.150	0.003	5	0
PER1 2024	3/20/2024 8:30	3/20/2024 8:40	0.150	0.004	5	0
PER1 2024	3/20/2024 8:40	3/20/2024 8:50	0.150	0.004	5	0
PER1 2024	3/20/2024 8:50	3/20/2024 9:00	0.150	0.005	5	0
PER1 2024	3/20/2024 9:00	3/20/2024 9:10	0.150	0.005	5	0
PER1 2024	3/20/2024 9:10	3/20/2024 9:20	0.150	0.006	5	0
PER1 2024	3/20/2024 9:20	3/20/2024 9:30	0.150	0.007	5	0
PER1 2024	3/20/2024 9:30	3/20/2024 9:40	0.150	0.008	5	0
PER1 2024	3/20/2024 9:40	3/20/2024 9:50	0.150	0.009	5	0
PER1 2024	3/20/2024 9:50	3/20/2024 10:00	0.150	0.01	5	0
PER1 2024	3/20/2024 10:00	3/20/2024 10:10	0.150	0.011	5	0
PER1 2024	3/20/2024 10:10	3/20/2024 10:20	0.150	0.012	5	0
PER1 2024	3/20/2024 10:20	3/20/2024 10:30	0.150	0.013	5	0
PER1 2024	3/20/2024 10:30	3/20/2024 10:40	0.150	0.013	5	0
PER1 2024	3/20/2024 10:40	3/20/2024 10:50	0.150	0.014	5	0
PER1 2024	3/20/2024 10:50	3/20/2024 11:00	0.150	0.015	5	0
PER1 2024	3/20/2024 11:00	3/20/2024 11:10	0.150	0.015	5	0
PER1 2024	3/20/2024 11:10	3/20/2024 11:20	0.150	0.016	5	0
PER1 2024	3/20/2024 11:20	3/20/2024 11:30	0.150	0.017	5	0
PER1 2024	3/20/2024 11:30	3/20/2024 11:40	0.150	0.017	5	0
PER1 2024	3/20/2024 11:40	3/20/2024 11:50	0.150	0.018	5	0
PER1 2024	3/20/2024 11:50	3/20/2024 12:00	0.150	0.019	5	0
PER1 2024	3/20/2024 12:00	3/20/2024 12:10	0.150	0.019	5	0
PER1 2024	3/20/2024 12:10	3/20/2024 12:20	0.150	0.02	5	0
PER1 2024	3/20/2024 12:20	3/20/2024 12:30	0.150	0.021	5	0
PER1 2024	3/20/2024 12:30	3/20/2024 12:40	0.150	0.021	5	0
PER1 2024	3/20/2024 12:40	3/20/2024 12:50	0.150	0.022	5	0
PER1 2024	3/20/2024 12:50	3/20/2024 13:00	0.150	0.023	5	0
PER1 2024	3/20/2024 13:00	3/20/2024 13:10	0.150	0.024	5	0
PER1 2024	3/20/2024 13:10	3/20/2024 13:20	0.150	0.025	5	0
PER1 2024	3/20/2024 13:20	3/20/2024 13:30	0.150	0.025	5	0
PER1 2024	3/20/2024 13:30	3/20/2024 13:40	0.150	0.026	5	0
PER1 2024	3/20/2024 13:40	3/20/2024 13:50	0.150	0.027	5	0
PER1 2024	3/20/2024 13:50	3/20/2024 14:00	0.150	0.028	5	0
PER1 2024	3/20/2024 14:00	3/20/2024 14:10	0.150	0.028	5	0
PER1 2024	3/20/2024 14:10	3/20/2024 14:20	0.150	0.029	5	0
PER1 2024	3/20/2024 14:20	3/20/2024 14:30	0.150	0.03	5	0
PER1 2024	3/20/2024 14:30	3/20/2024 14:40	0.150	0.03	5	0
PER1 2024	3/20/2024 14:40	3/20/2024 14:50	0.150	0.031	5	0
PER1 2024	3/20/2024 14:50	3/20/2024 15:00	0.150	0.032	5	0
PER1 2024	3/20/2024 15:00	3/20/2024 15:10	0.150	0.033	5	0
PER1 2024	3/20/2024 15:10	3/20/2024 15:20	0.150	0.033	5	0
PER1 2024	3/20/2024 15:20	3/20/2024 15:30	0.150	0.034	5	0
PER1 2024	3/20/2024 15:30	3/20/2024 15:40	0.150	0.034	5	0
PER1 2024	3/20/2024 15:40	3/20/2024 15:50	0.150	0.034	5	0
PER1 2024	3/20/2024 15:50	3/20/2024 16:00	0.150	0.034	5	0
PER1 2024	3/20/2024 16:00	3/20/2024 16:10	0.150	0.034	5	0
PER1 2024	3/20/2024 16:10	3/20/2024 16:20	0.150	0.034	5	0
PER1 2024	3/20/2024 16:20	3/20/2024 16:30	0.150	0.034	5	0
PER1 2024	3/20/2024 16:30	3/20/2024 16:40	0.150	0.034	5	0
PER1 2024	3/20/2024 16:40	3/20/2024 16:50	0.150	0.034	5	0
PER1 2024	3/20/2024 16:50	3/20/2024 17:00	0.150	0.034	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/20/2024 8:00	3/20/2024 8:10	0.150	0.001	5	0
PER2 2024	3/20/2024 8:10	3/20/2024 8:20	0.150	0.002	5	0
PER2 2024	3/20/2024 8:20	3/20/2024 8:30	0.150	0.002	5	0
PER2 2024	3/20/2024 8:30	3/20/2024 8:40	0.150	0.003	5	0
PER2 2024	3/20/2024 8:40	3/20/2024 8:50	0.150	0.004	5	0
PER2 2024	3/20/2024 8:50	3/20/2024 9:00	0.150	0.004	5	0
PER2 2024	3/20/2024 9:00	3/20/2024 9:10	0.150	0.004	5	0
PER2 2024	3/20/2024 9:10	3/20/2024 9:20	0.150	0.004	5	0
PER2 2024	3/20/2024 9:20	3/20/2024 9:30	0.150	0.004	5	0
PER2 2024	3/20/2024 9:30	3/20/2024 9:40	0.150	0.004	5	0
PER2 2024	3/20/2024 9:40	3/20/2024 9:50	0.150	0.004	5	0
PER2 2024	3/20/2024 9:50	3/20/2024 10:00	0.150	0.004	5	0
PER2 2024	3/20/2024 10:00	3/20/2024 10:10	0.150	0.004	5	0
PER2 2024	3/20/2024 10:10	3/20/2024 10:20	0.150	0.004	5	0
PER2 2024	3/20/2024 10:20	3/20/2024 10:30	0.150	0.001	5	0
PER2 2024	3/20/2024 10:30	3/20/2024 10:40	0.150	0.002	5	0
PER2 2024	3/20/2024 10:40	3/20/2024 10:50	0.150	0.003	5	0
PER2 2024	3/20/2024 10:50	3/20/2024 11:00	0.150	0.004	5	0
PER2 2024	3/20/2024 11:00	3/20/2024 11:10	0.150	0.004	5	0
PER2 2024	3/20/2024 11:10	3/20/2024 11:20	0.150	0.005	5	0
PER2 2024	3/20/2024 11:20	3/20/2024 11:30	0.150	0.006	5	0
PER2 2024	3/20/2024 11:30	3/20/2024 11:40	0.150	0.006	5	0
PER2 2024	3/20/2024 11:40	3/20/2024 11:50	0.150	0.007	5	0
PER2 2024	3/20/2024 11:50	3/20/2024 12:00	0.150	0.008	5	0
PER2 2024	3/20/2024 12:00	3/20/2024 12:10	0.150	0.008	5	0
PER2 2024	3/20/2024 12:10	3/20/2024 12:20	0.150	0.009	5	0
PER2 2024	3/20/2024 12:20	3/20/2024 12:30	0.150	0.009	5	0
PER2 2024	3/20/2024 12:30	3/20/2024 12:40	0.150	0.01	5	0
PER2 2024	3/20/2024 12:40	3/20/2024 12:50	0.150	0.011	5	0
PER2 2024	3/20/2024 12:50	3/20/2024 13:00	0.150	0.011	5	0
PER2 2024	3/20/2024 13:00	3/20/2024 13:10	0.150	0.012	5	0
PER2 2024	3/20/2024 13:10	3/20/2024 13:20	0.150	0.013	5	0
PER2 2024	3/20/2024 13:20	3/20/2024 13:30	0.150	0.014	5	0
PER2 2024	3/20/2024 13:30	3/20/2024 13:40	0.150	0.014	5	0
PER2 2024	3/20/2024 13:40	3/20/2024 13:50	0.150	0.015	5	0
PER2 2024	3/20/2024 13:50	3/20/2024 14:00	0.150	0.016	5	0.001
PER2 2024	3/20/2024 14:00	3/20/2024 14:10	0.150	0.016	5	0.001
PER2 2024	3/20/2024 14:10	3/20/2024 14:20	0.150	0.017	5	0.002
PER2 2024	3/20/2024 14:20	3/20/2024 14:30	0.150	0.018	5	0.002
PER2 2024	3/20/2024 14:30	3/20/2024 14:40	0.150	0.019	5	0.002
PER2 2024	3/20/2024 14:40	3/20/2024 14:50	0.150	0.02	5	0.002
PER2 2024	3/20/2024 14:50	3/20/2024 15:00	0.150	0.02	5	0.002
PER2 2024	3/20/2024 15:00	3/20/2024 15:10	0.150	0.021	5	0.002
PER2 2024	3/20/2024 15:10	3/20/2024 15:20	0.150	0.022	5	0.002
PER2 2024	3/20/2024 15:20	3/20/2024 15:30	0.150	0.022	5	0.002
PER2 2024	3/20/2024 15:30	3/20/2024 15:40	0.150	0.023	5	0.002
PER2 2024	3/20/2024 15:40	3/20/2024 15:50	0.150	0.023	5	0.002
PER2 2024	3/20/2024 15:50	3/20/2024 16:00	0.150	0.024	5	0.002
PER2 2024	3/20/2024 16:00	3/20/2024 16:10	0.150	0.024	5	0.002
PER2 2024	3/20/2024 16:10	3/20/2024 16:20	0.150	0.025	5	0.002
PER2 2024	3/20/2024 16:20	3/20/2024 16:30	0.150	0.025	5	0.002
PER2 2024	3/20/2024 16:30	3/20/2024 16:40	0.150	0.026	5	0.002
PER2 2024	3/20/2024 16:40	3/20/2024 16:50	0.150	0.027	5	0.002
PER2 2024	3/20/2024 16:50	3/20/2024 17:00	0.150	0.028	5	0.002

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/21/2024

Weather: 30 deg. F, Sunny


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation and foundation development. 2) ECD continued marine waterfront remedial excavation and exports 5 loads (~100 CY) of material off-site to the Bayshore Soil Management facility. 3) Temporarily turn off the dewatering system to clear out sediment in the bottom of the settling tank.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP tables and graphs are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4285	0	7025	1520	2500

Site Layout Map and Excavation Figures

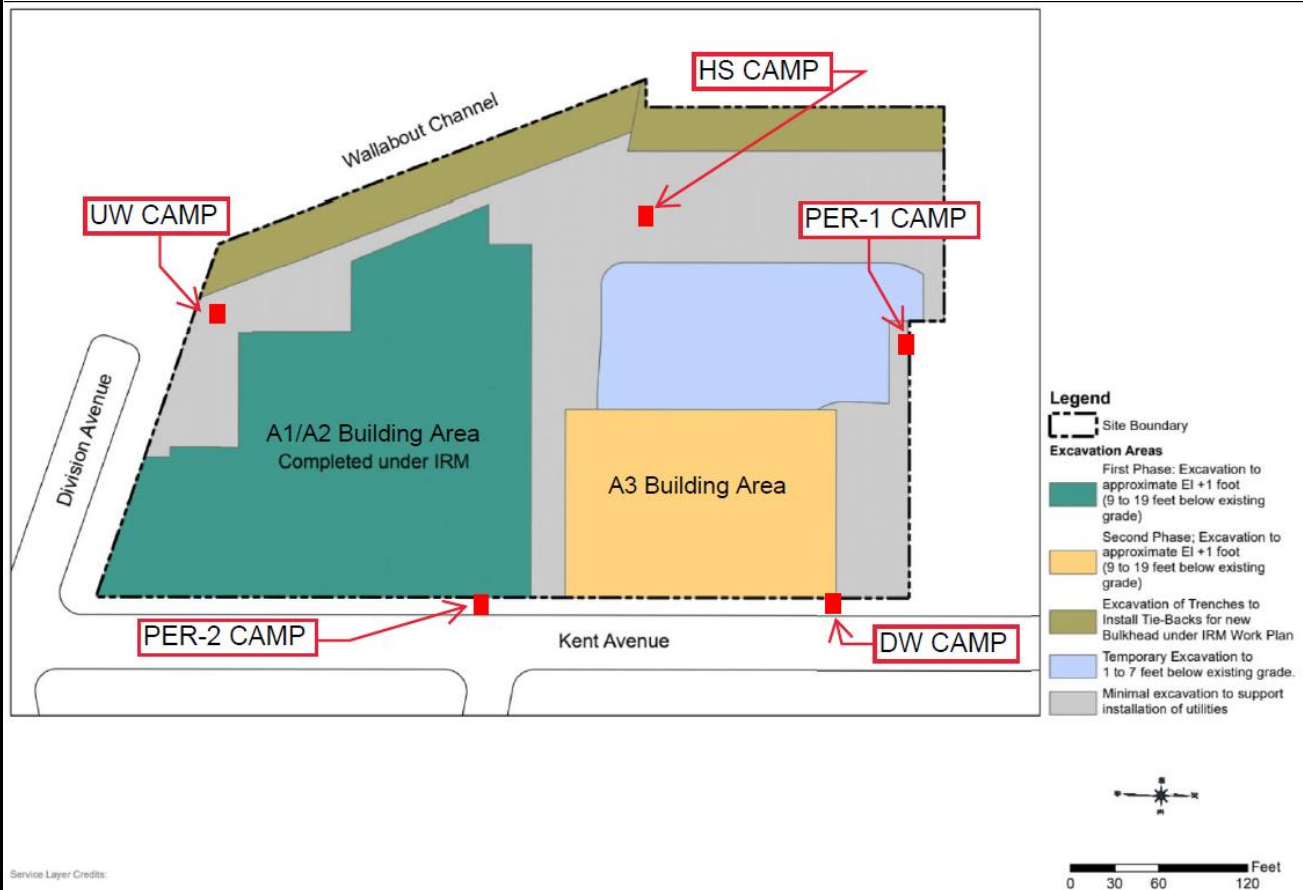

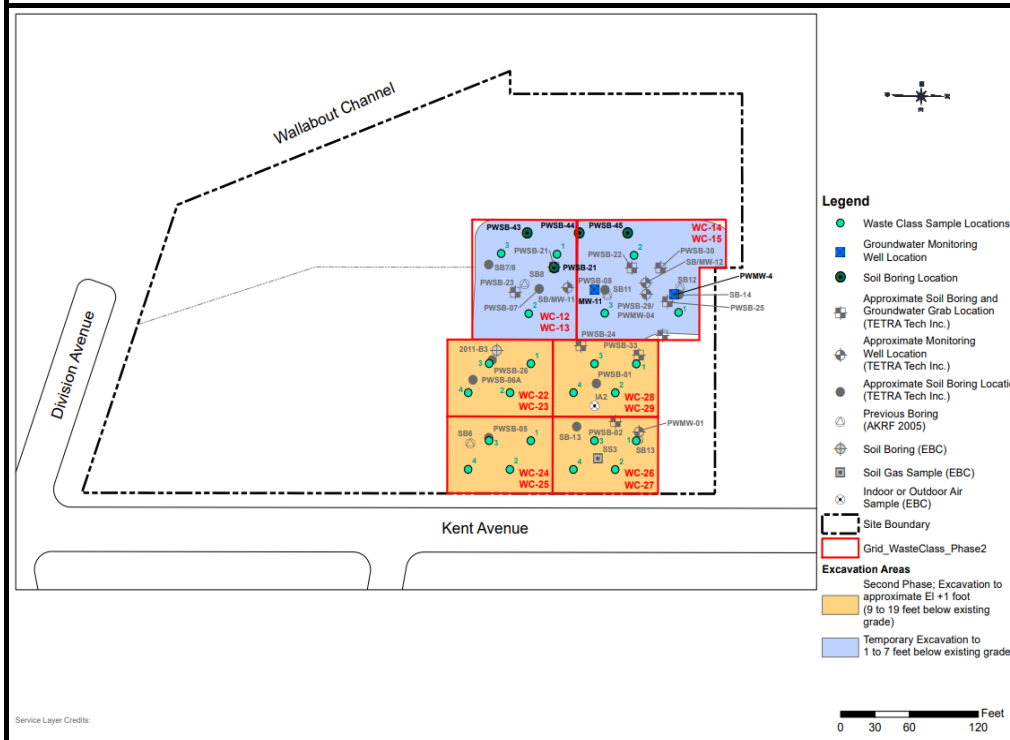
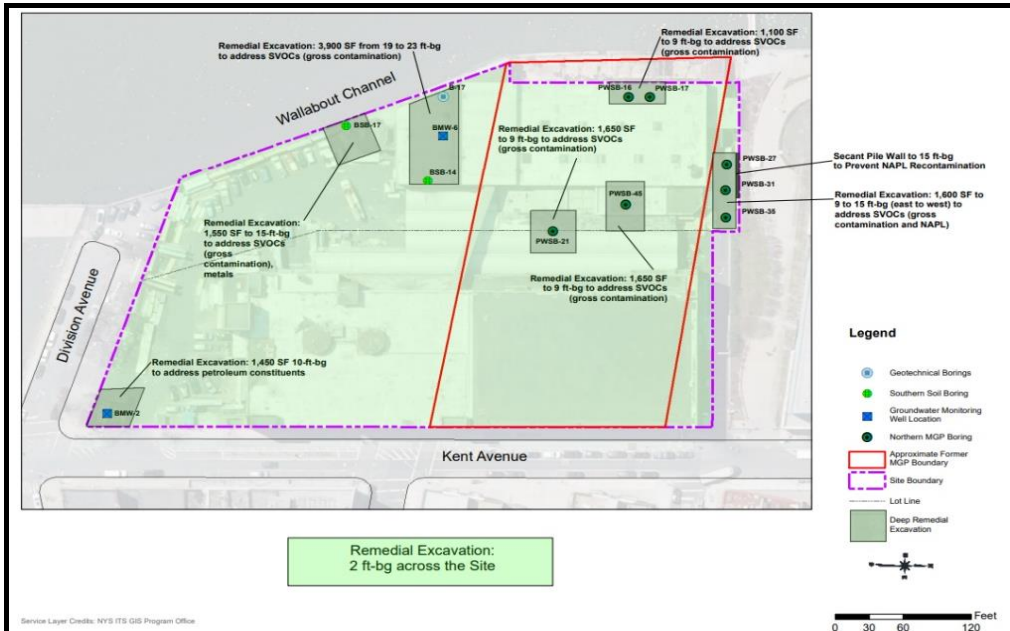


Photo 1:
View of Site conditions,
and activities facing
northwest.

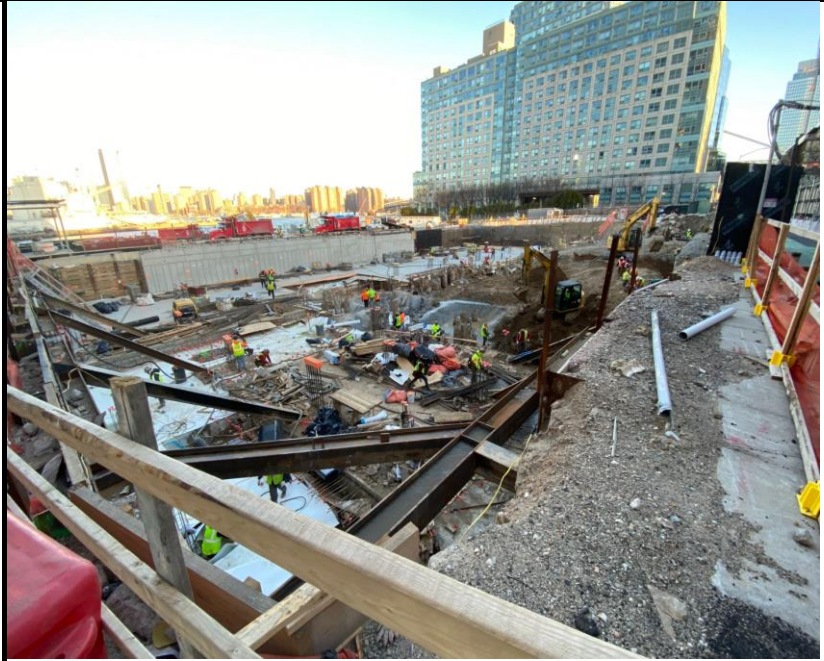


Photo 2:
View of Site conditions
and activities facing
south.



Photo 3:
View of Site
conditions and
activities facing
northeast.

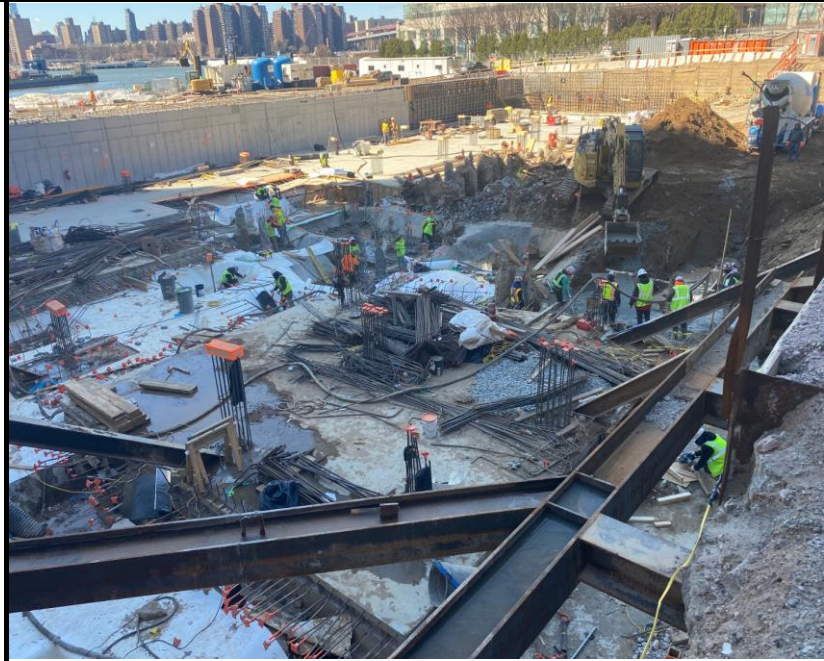



Photo 4:
View of rebar
installation and
foundation framing.



CAMP:
Downwind
Particulates

Dust Levels


0.017 mg/m³ 0.014 mg/m³

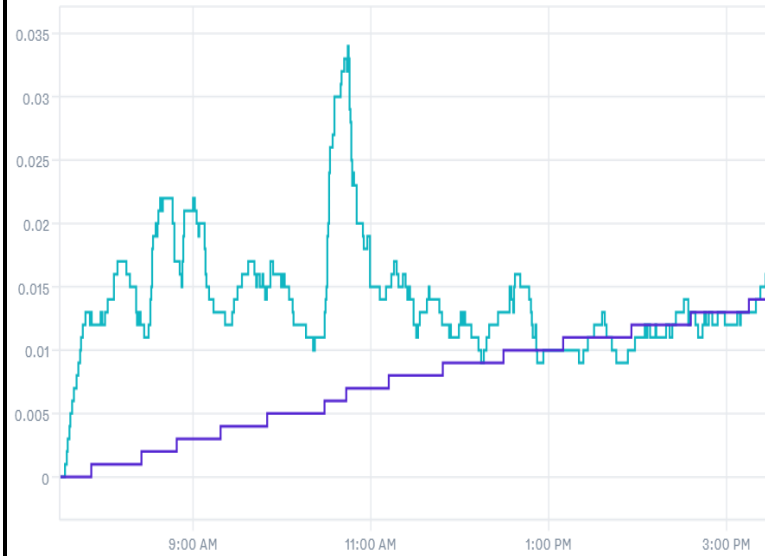

CAMP:
Downwind VOCs

VOC Levels


0.131 ppm 0.176 ppm

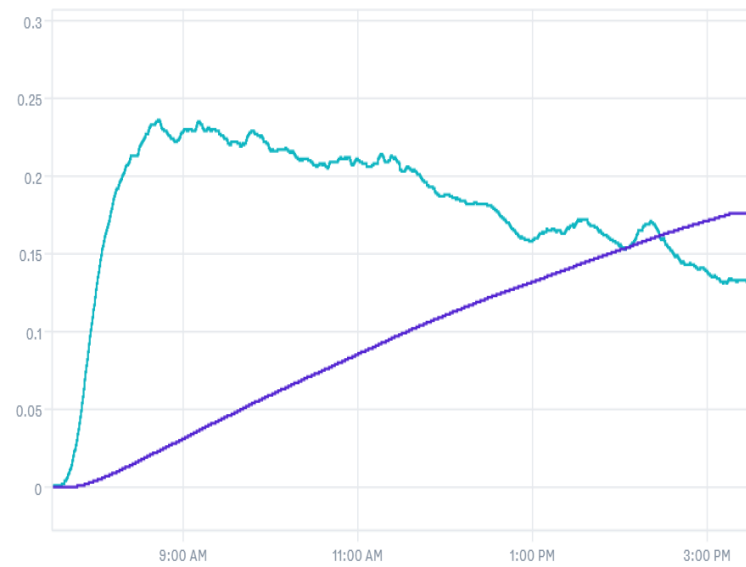

CAMP:
Upwind Particulates

Dust Levels


0.016 mg/m³ 0.017 mg/m³ 0.15

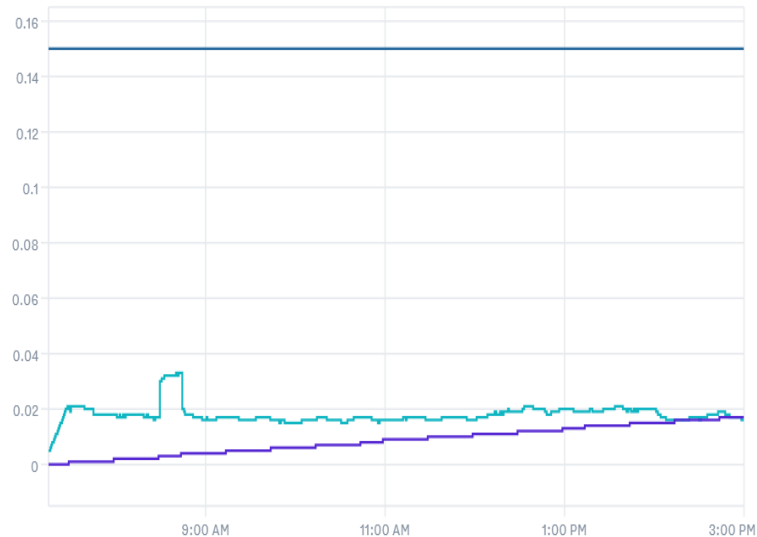

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

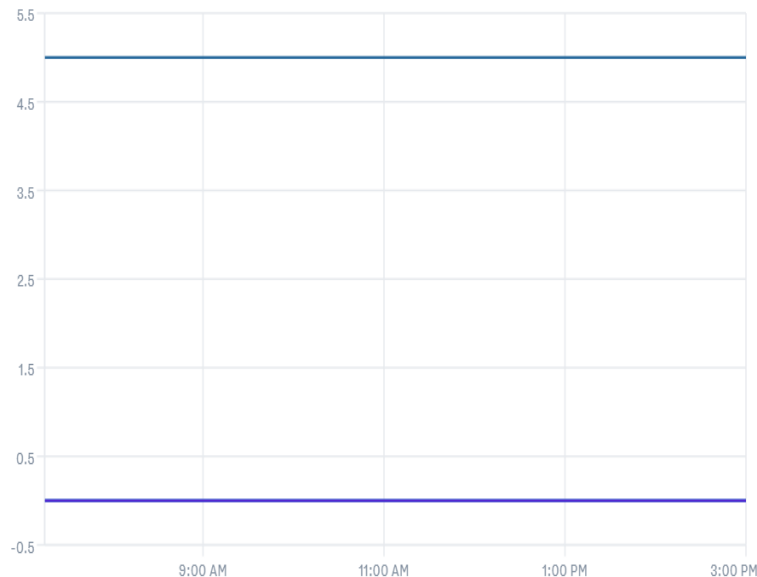

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/21/2024 8:00	3/21/2024 8:10	0.150	0.001	5	0.008
DW 2024	3/21/2024 8:10	3/21/2024 8:20	0.150	0.001	5	0.012
DW 2024	3/21/2024 8:20	3/21/2024 8:30	0.150	0.002	5	0.017
DW 2024	3/21/2024 8:30	3/21/2024 8:40	0.150	0.002	5	0.022
DW 2024	3/21/2024 8:40	3/21/2024 8:50	0.150	0.003	5	0.026
DW 2024	3/21/2024 8:50	3/21/2024 9:00	0.150	0.003	5	0.031
DW 2024	3/21/2024 9:00	3/21/2024 9:10	0.150	0.003	5	0.036
DW 2024	3/21/2024 9:10	3/21/2024 9:20	0.150	0.004	5	0.041
DW 2024	3/21/2024 9:20	3/21/2024 9:30	0.150	0.004	5	0.045
DW 2024	3/21/2024 9:30	3/21/2024 9:40	0.150	0.004	5	0.05
DW 2024	3/21/2024 9:40	3/21/2024 9:50	0.150	0.004	5	0.055
DW 2024	3/21/2024 9:50	3/21/2024 10:00	0.150	0.005	5	0.059
DW 2024	3/21/2024 10:00	3/21/2024 10:10	0.150	0.005	5	0.063
DW 2024	3/21/2024 10:10	3/21/2024 10:20	0.150	0.005	5	0.068
DW 2024	3/21/2024 10:20	3/21/2024 10:30	0.150	0.006	5	0.072
DW 2024	3/21/2024 10:30	3/21/2024 10:40	0.150	0.006	5	0.076
DW 2024	3/21/2024 10:40	3/21/2024 10:50	0.150	0.007	5	0.081
DW 2024	3/21/2024 10:50	3/21/2024 11:00	0.150	0.007	5	0.085
DW 2024	3/21/2024 11:00	3/21/2024 11:10	0.150	0.007	5	0.089
DW 2024	3/21/2024 11:10	3/21/2024 11:20	0.150	0.008	5	0.094
DW 2024	3/21/2024 11:20	3/21/2024 11:30	0.150	0.008	5	0.098
DW 2024	3/21/2024 11:30	3/21/2024 11:40	0.150	0.008	5	0.102
DW 2024	3/21/2024 11:40	3/21/2024 11:50	0.150	0.009	5	0.106
DW 2024	3/21/2024 11:50	3/21/2024 12:00	0.150	0.009	5	0.11
DW 2024	3/21/2024 12:00	3/21/2024 12:10	0.150	0.009	5	0.114
DW 2024	3/21/2024 12:10	3/21/2024 12:20	0.150	0.009	5	0.118
DW 2024	3/21/2024 12:20	3/21/2024 12:30	0.150	0.01	5	0.122
DW 2024	3/21/2024 12:30	3/21/2024 12:40	0.150	0.01	5	0.125
DW 2024	3/21/2024 12:40	3/21/2024 12:50	0.150	0.01	5	0.128
DW 2024	3/21/2024 12:50	3/21/2024 13:00	0.150	0.01	5	0.132
DW 2024	3/21/2024 13:00	3/21/2024 13:10	0.150	0.011	5	0.135
DW 2024	3/21/2024 13:10	3/21/2024 13:20	0.150	0.011	5	0.139
DW 2024	3/21/2024 13:20	3/21/2024 13:30	0.150	0.011	5	0.142
DW 2024	3/21/2024 13:30	3/21/2024 13:40	0.150	0.011	5	0.146
DW 2024	3/21/2024 13:40	3/21/2024 13:50	0.150	0.011	5	0.149
DW 2024	3/21/2024 13:50	3/21/2024 14:00	0.150	0.012	5	0.152
DW 2024	3/21/2024 14:00	3/21/2024 14:10	0.150	0.012	5	0.156
DW 2024	3/21/2024 14:10	3/21/2024 14:20	0.150	0.012	5	0.159
DW 2024	3/21/2024 14:20	3/21/2024 14:30	0.150	0.012	5	0.162
DW 2024	3/21/2024 14:30	3/21/2024 14:40	0.150	0.013	5	0.165
DW 2024	3/21/2024 14:40	3/21/2024 14:50	0.150	0.013	5	0.168
DW 2024	3/21/2024 14:50	3/21/2024 15:00	0.150	0.013	5	0.171
DW 2024	3/21/2024 15:00	3/21/2024 15:10	0.150	0.013	5	0.174
DW 2024	3/21/2024 15:10	3/21/2024 15:20	0.150	0.014	5	0.176
DW 2024	3/21/2024 15:20	3/21/2024 15:30	0.150	0.014	5	0.176
DW 2024	3/21/2024 15:30	3/21/2024 15:40	0.150	0.014	5	0.176
DW 2024	3/21/2024 15:40	3/21/2024 15:50	0.150	0.014	5	0.176
DW 2024	3/21/2024 15:50	3/21/2024 16:00	0.150	0.014	5	0.176
DW 2024	3/21/2024 16:00	3/21/2024 16:10	0.150	0.014	5	0.176
DW 2024	3/21/2024 16:10	3/21/2024 16:20	0.150	0.014	5	0.176
DW 2024	3/21/2024 16:20	3/21/2024 16:30	0.150	0.014	5	0.176
DW 2024	3/21/2024 16:30	3/21/2024 16:40	0.150	0.014	5	0.176
DW 2024	3/21/2024 16:40	3/21/2024 16:50	0.150	0.014	5	0.176
DW 2024	3/21/2024 16:50	3/21/2024 17:00	0.150	0.014	5	0.176

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/21/2024 8:00	3/21/2024 8:10	0.150	0.002	5	0
UW 2024	3/21/2024 8:10	3/21/2024 8:20	0.150	0.002	5	0
UW 2024	3/21/2024 8:20	3/21/2024 8:30	0.150	0.003	5	0
UW 2024	3/21/2024 8:30	3/21/2024 8:40	0.150	0.003	5	0
UW 2024	3/21/2024 8:40	3/21/2024 8:50	0.150	0.004	5	0
UW 2024	3/21/2024 8:50	3/21/2024 9:00	0.150	0.004	5	0
UW 2024	3/21/2024 9:00	3/21/2024 9:10	0.150	0.004	5	0
UW 2024	3/21/2024 9:10	3/21/2024 9:20	0.150	0.005	5	0
UW 2024	3/21/2024 9:20	3/21/2024 9:30	0.150	0.005	5	0
UW 2024	3/21/2024 9:30	3/21/2024 9:40	0.150	0.005	5	0
UW 2024	3/21/2024 9:40	3/21/2024 9:50	0.150	0.006	5	0
UW 2024	3/21/2024 9:50	3/21/2024 10:00	0.150	0.006	5	0
UW 2024	3/21/2024 10:00	3/21/2024 10:10	0.150	0.006	5	0
UW 2024	3/21/2024 10:10	3/21/2024 10:20	0.150	0.007	5	0
UW 2024	3/21/2024 10:20	3/21/2024 10:30	0.150	0.007	5	0
UW 2024	3/21/2024 10:30	3/21/2024 10:40	0.150	0.007	5	0
UW 2024	3/21/2024 10:40	3/21/2024 10:50	0.150	0.008	5	0
UW 2024	3/21/2024 10:50	3/21/2024 11:00	0.150	0.009	5	0
UW 2024	3/21/2024 11:00	3/21/2024 11:10	0.150	0.009	5	0
UW 2024	3/21/2024 11:10	3/21/2024 11:20	0.150	0.009	5	0
UW 2024	3/21/2024 11:20	3/21/2024 11:30	0.150	0.01	5	0
UW 2024	3/21/2024 11:30	3/21/2024 11:40	0.150	0.01	5	0
UW 2024	3/21/2024 11:40	3/21/2024 11:50	0.150	0.01	5	0
UW 2024	3/21/2024 11:50	3/21/2024 12:00	0.150	0.011	5	0
UW 2024	3/21/2024 12:00	3/21/2024 12:10	0.150	0.011	5	0
UW 2024	3/21/2024 12:10	3/21/2024 12:20	0.150	0.011	5	0
UW 2024	3/21/2024 12:20	3/21/2024 12:30	0.150	0.012	5	0
UW 2024	3/21/2024 12:30	3/21/2024 12:40	0.150	0.012	5	0
UW 2024	3/21/2024 12:40	3/21/2024 12:50	0.150	0.012	5	0
UW 2024	3/21/2024 12:50	3/21/2024 13:00	0.150	0.013	5	0
UW 2024	3/21/2024 13:00	3/21/2024 13:10	0.150	0.013	5	0
UW 2024	3/21/2024 13:10	3/21/2024 13:20	0.150	0.014	5	0
UW 2024	3/21/2024 13:20	3/21/2024 13:30	0.150	0.014	5	0
UW 2024	3/21/2024 13:30	3/21/2024 13:40	0.150	0.014	5	0
UW 2024	3/21/2024 13:40	3/21/2024 13:50	0.150	0.015	5	0
UW 2024	3/21/2024 13:50	3/21/2024 14:00	0.150	0.015	5	0
UW 2024	3/21/2024 14:00	3/21/2024 14:10	0.150	0.015	5	0
UW 2024	3/21/2024 14:10	3/21/2024 14:20	0.150	0.016	5	0
UW 2024	3/21/2024 14:20	3/21/2024 14:30	0.150	0.016	5	0
UW 2024	3/21/2024 14:30	3/21/2024 14:40	0.150	0.016	5	0
UW 2024	3/21/2024 14:40	3/21/2024 14:50	0.150	0.017	5	0
UW 2024	3/21/2024 14:50	3/21/2024 15:00	0.150	0.017	5	0
UW 2024	3/21/2024 15:00	3/21/2024 15:10	0.150	0.017	5	0
UW 2024	3/21/2024 15:10	3/21/2024 15:20	0.150	0.018	5	0
UW 2024	3/21/2024 15:20	3/21/2024 15:30	0.150	0	5	0
UW 2024	3/21/2024 15:30	3/21/2024 15:40	0.150	0	5	0
UW 2024	3/21/2024 15:40	3/21/2024 15:50	0.150	0	5	0
UW 2024	3/21/2024 15:50	3/21/2024 16:00	0.150	0	5	0
UW 2024	3/21/2024 16:00	3/21/2024 16:10	0.150	0	5	0
UW 2024	3/21/2024 16:10	3/21/2024 16:20	0.150	0	5	0
UW 2024	3/21/2024 16:20	3/21/2024 16:30	0.150	0	5	0
UW 2024	3/21/2024 16:30	3/21/2024 16:40	0.150	0	5	0
UW 2024	3/21/2024 16:40	3/21/2024 16:50	0.150	0	5	0
UW 2024	3/21/2024 16:50	3/21/2024 17:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/21/2024 8:00	3/21/2024 8:10	0.150	0.002	5	0
HS South	3/21/2024 8:10	3/21/2024 8:20	0.150	0.003	5	0
HS South	3/21/2024 8:20	3/21/2024 8:30	0.150	0.004	5	0
HS South	3/21/2024 8:30	3/21/2024 8:40	0.150	0.004	5	0
HS South	3/21/2024 8:40	3/21/2024 8:50	0.150	0.004	5	0
HS South	3/21/2024 8:50	3/21/2024 9:00	0.150	0.005	5	0
HS South	3/21/2024 9:00	3/21/2024 9:10	0.150	0.005	5	0
HS South	3/21/2024 9:10	3/21/2024 9:20	0.150	0.005	5	0
HS South	3/21/2024 9:20	3/21/2024 9:30	0.150	0.006	5	0
HS South	3/21/2024 9:30	3/21/2024 9:40	0.150	0.006	5	0
HS South	3/21/2024 9:40	3/21/2024 9:50	0.150	0.006	5	0
HS South	3/21/2024 9:50	3/21/2024 10:00	0.150	0.006	5	0
HS South	3/21/2024 10:00	3/21/2024 10:10	0.150	0.006	5	0
HS South	3/21/2024 10:10	3/21/2024 10:20	0.150	0.006	5	0
HS South	3/21/2024 10:20	3/21/2024 10:30	0.150	0.006	5	0
HS South	3/21/2024 10:30	3/21/2024 10:40	0.150	0.007	5	0
HS South	3/21/2024 10:40	3/21/2024 10:50	0.150	0.007	5	0
HS South	3/21/2024 10:50	3/21/2024 11:00	0.150	0.007	5	0
HS South	3/21/2024 11:00	3/21/2024 11:10	0.150	0.007	5	0
HS South	3/21/2024 11:10	3/21/2024 11:20	0.150	0.007	5	0
HS South	3/21/2024 11:20	3/21/2024 11:30	0.150	0.007	5	0
HS South	3/21/2024 11:30	3/21/2024 11:40	0.150	0.007	5	0
HS South	3/21/2024 11:40	3/21/2024 11:50	0.150	0.008	5	0
HS South	3/21/2024 11:50	3/21/2024 12:00	0.150	0.008	5	0
HS South	3/21/2024 12:00	3/21/2024 12:10	0.150	0.008	5	0
HS South	3/21/2024 12:10	3/21/2024 12:20	0.150	0.01	5	0
HS South	3/21/2024 12:20	3/21/2024 12:30	0.150	0.011	5	0
HS South	3/21/2024 12:30	3/21/2024 12:40	0.150	0.011	5	0
HS South	3/21/2024 12:40	3/21/2024 12:50	0.150	0.012	5	0
HS South	3/21/2024 12:50	3/21/2024 13:00	0.150	0.012	5	0
HS South	3/21/2024 13:00	3/21/2024 13:10	0.150	0.013	5	0
HS South	3/21/2024 13:10	3/21/2024 13:20	0.150	0.013	5	0
HS South	3/21/2024 13:20	3/21/2024 13:30	0.150	0.013	5	0
HS South	3/21/2024 13:30	3/21/2024 13:40	0.150	0.014	5	0
HS South	3/21/2024 13:40	3/21/2024 13:50	0.150	0.015	5	0
HS South	3/21/2024 13:50	3/21/2024 14:00	0.150	0.015	5	0
HS South	3/21/2024 14:00	3/21/2024 14:10	0.150	0.016	5	0
HS South	3/21/2024 14:10	3/21/2024 14:20	0.150	0.016	5	0
HS South	3/21/2024 14:20	3/21/2024 14:30	0.150	0.016	5	0
HS South	3/21/2024 14:30	3/21/2024 14:40	0.150	0.016	5	0
HS South	3/21/2024 14:40	3/21/2024 14:50	0.150	0.016	5	0
HS South	3/21/2024 14:50	3/21/2024 15:00	0.150	0.016	5	0
HS South	3/21/2024 15:00	3/21/2024 15:10	0.150	0.016	5	0
HS South	3/21/2024 15:10	3/21/2024 15:20	0.150	0.016	5	0
HS South	3/21/2024 15:20	3/21/2024 15:30	0.150	0.016	5	0
HS South	3/21/2024 15:30	3/21/2024 15:40	0.150	0.016	5	0
HS South	3/21/2024 15:40	3/21/2024 15:50	0.150	0.016	5	0
HS South	3/21/2024 15:50	3/21/2024 16:00	0.150	0.016	5	0
HS South	3/21/2024 16:00	3/21/2024 16:10	0.150	0.016	5	0
HS South	3/21/2024 16:10	3/21/2024 16:20	0.150	0.016	5	0
HS South	3/21/2024 16:20	3/21/2024 16:30	0.150	0.016	5	0
HS South	3/21/2024 16:30	3/21/2024 16:40	0.150	0.016	5	0
HS South	3/21/2024 16:40	3/21/2024 16:50	0.150	0.016	5	0
HS South	3/21/2024 16:50	3/21/2024 17:00	0.150	0.016	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/21/2024 8:00	3/21/2024 8:10	0.150	0.007	5	0
PER1 2024	3/21/2024 8:10	3/21/2024 8:20	0.150	0.009	5	0
PER1 2024	3/21/2024 8:20	3/21/2024 8:30	0.150	0.011	5	0
PER1 2024	3/21/2024 8:30	3/21/2024 8:40	0.150	0.012	5	0
PER1 2024	3/21/2024 8:40	3/21/2024 8:50	0.150	0.014	5	0
PER1 2024	3/21/2024 8:50	3/21/2024 9:00	0.150	0.014	5	0
PER1 2024	3/21/2024 9:00	3/21/2024 9:10	0.150	0.015	5	0
PER1 2024	3/21/2024 9:10	3/21/2024 9:20	0.150	0.015	5	0
PER1 2024	3/21/2024 9:20	3/21/2024 9:30	0.150	0.016	5	0
PER1 2024	3/21/2024 9:30	3/21/2024 9:40	0.150	0.016	5	0
PER1 2024	3/21/2024 9:40	3/21/2024 9:50	0.150	0.017	5	0
PER1 2024	3/21/2024 9:50	3/21/2024 10:00	0.150	0.017	5	0
PER1 2024	3/21/2024 10:00	3/21/2024 10:10	0.150	0.017	5	0
PER1 2024	3/21/2024 10:10	3/21/2024 10:20	0.150	0.018	5	0
PER1 2024	3/21/2024 10:20	3/21/2024 10:30	0.150	0.018	5	0
PER1 2024	3/21/2024 10:30	3/21/2024 10:40	0.150	0.018	5	0
PER1 2024	3/21/2024 10:40	3/21/2024 10:50	0.150	0.019	5	0
PER1 2024	3/21/2024 10:50	3/21/2024 11:00	0.150	0.019	5	0.002
PER1 2024	3/21/2024 11:00	3/21/2024 11:10	0.150	0.02	5	0.002
PER1 2024	3/21/2024 11:10	3/21/2024 11:20	0.150	0.02	5	0.002
PER1 2024	3/21/2024 11:20	3/21/2024 11:30	0.150	0.02	5	0.002
PER1 2024	3/21/2024 11:30	3/21/2024 11:40	0.150	0.021	5	0.002
PER1 2024	3/21/2024 11:40	3/21/2024 11:50	0.150	0.021	5	0.002
PER1 2024	3/21/2024 11:50	3/21/2024 12:00	0.150	0.021	5	0.002
PER1 2024	3/21/2024 12:00	3/21/2024 12:10	0.150	0.022	5	0.002
PER1 2024	3/21/2024 12:10	3/21/2024 12:20	0.150	0.023	5	0.002
PER1 2024	3/21/2024 12:20	3/21/2024 12:30	0.150	0.023	5	0.002
PER1 2024	3/21/2024 12:30	3/21/2024 12:40	0.150	0.024	5	0.002
PER1 2024	3/21/2024 12:40	3/21/2024 12:50	0.150	0.024	5	0.002
PER1 2024	3/21/2024 12:50	3/21/2024 13:00	0.150	0.024	5	0.002
PER1 2024	3/21/2024 13:00	3/21/2024 13:10	0.150	0.025	5	0.002
PER1 2024	3/21/2024 13:10	3/21/2024 13:20	0.150	0.026	5	0.002
PER1 2024	3/21/2024 13:20	3/21/2024 13:30	0.150	0.026	5	0.002
PER1 2024	3/21/2024 13:30	3/21/2024 13:40	0.150	0.027	5	0.002
PER1 2024	3/21/2024 13:40	3/21/2024 13:50	0.150	0.027	5	0.002
PER1 2024	3/21/2024 13:50	3/21/2024 14:00	0.150	0.027	5	0.002
PER1 2024	3/21/2024 14:00	3/21/2024 14:10	0.150	0.028	5	0.002
PER1 2024	3/21/2024 14:10	3/21/2024 14:20	0.150	0.028	5	0.002
PER1 2024	3/21/2024 14:20	3/21/2024 14:30	0.150	0.029	5	0.002
PER1 2024	3/21/2024 14:30	3/21/2024 14:40	0.150	0.03	5	0.002
PER1 2024	3/21/2024 14:40	3/21/2024 14:50	0.150	0.031	5	0.002
PER1 2024	3/21/2024 14:50	3/21/2024 15:00	0.150	0.031	5	0.002
PER1 2024	3/21/2024 15:00	3/21/2024 15:10	0.150	0.031	5	0.002
PER1 2024	3/21/2024 15:10	3/21/2024 15:20	0.150	0.031	5	0.003
PER1 2024	3/21/2024 15:20	3/21/2024 15:30	0.150	0.031	5	0
PER1 2024	3/21/2024 15:30	3/21/2024 15:40	0.150	0	5	0
PER1 2024	3/21/2024 15:40	3/21/2024 15:50	0.150	0	5	0
PER1 2024	3/21/2024 15:50	3/21/2024 16:00	0.150	0	5	0
PER1 2024	3/21/2024 16:00	3/21/2024 16:10	0.150	0	5	0
PER1 2024	3/21/2024 16:10	3/21/2024 16:20	0.150	0	5	0
PER1 2024	3/21/2024 16:20	3/21/2024 16:30	0.150	0	5	0
PER1 2024	3/21/2024 16:30	3/21/2024 16:40	0.150	0	5	0
PER1 2024	3/21/2024 16:40	3/21/2024 16:50	0.150	0	5	0
PER1 2024	3/21/2024 16:50	3/21/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/21/2024 8:00	3/21/2024 8:10	0.150	0.001	5	0
PER2 2024	3/21/2024 8:10	3/21/2024 8:20	0.150	0.001	5	0
PER2 2024	3/21/2024 8:20	3/21/2024 8:30	0.150	0.001	5	0
PER2 2024	3/21/2024 8:30	3/21/2024 8:40	0.150	0.001	5	0
PER2 2024	3/21/2024 8:40	3/21/2024 8:50	0.150	0.001	5	0
PER2 2024	3/21/2024 8:50	3/21/2024 9:00	0.150	0.001	5	0
PER2 2024	3/21/2024 9:00	3/21/2024 9:10	0.150	0.002	5	0
PER2 2024	3/21/2024 9:10	3/21/2024 9:20	0.150	0.002	5	0
PER2 2024	3/21/2024 9:20	3/21/2024 9:30	0.150	0.002	5	0
PER2 2024	3/21/2024 9:30	3/21/2024 9:40	0.150	0.002	5	0
PER2 2024	3/21/2024 9:40	3/21/2024 9:50	0.150	0.002	5	0
PER2 2024	3/21/2024 9:50	3/21/2024 10:00	0.150	0.002	5	0
PER2 2024	3/21/2024 10:00	3/21/2024 10:10	0.150	0.002	5	0
PER2 2024	3/21/2024 10:10	3/21/2024 10:20	0.150	0.003	5	0
PER2 2024	3/21/2024 10:20	3/21/2024 10:30	0.150	0.003	5	0
PER2 2024	3/21/2024 10:30	3/21/2024 10:40	0.150	0.003	5	0
PER2 2024	3/21/2024 10:40	3/21/2024 10:50	0.150	0.003	5	0
PER2 2024	3/21/2024 10:50	3/21/2024 11:00	0.150	0.003	5	0
PER2 2024	3/21/2024 11:00	3/21/2024 11:10	0.150	0.003	5	0
PER2 2024	3/21/2024 11:10	3/21/2024 11:20	0.150	0.003	5	0
PER2 2024	3/21/2024 11:20	3/21/2024 11:30	0.150	0.004	5	0
PER2 2024	3/21/2024 11:30	3/21/2024 11:40	0.150	0.004	5	0
PER2 2024	3/21/2024 11:40	3/21/2024 11:50	0.150	0.004	5	0
PER2 2024	3/21/2024 11:50	3/21/2024 12:00	0.150	0.004	5	0
PER2 2024	3/21/2024 12:00	3/21/2024 12:10	0.150	0.004	5	0
PER2 2024	3/21/2024 12:10	3/21/2024 12:20	0.150	0.005	5	0
PER2 2024	3/21/2024 12:20	3/21/2024 12:30	0.150	0.005	5	0
PER2 2024	3/21/2024 12:30	3/21/2024 12:40	0.150	0.005	5	0
PER2 2024	3/21/2024 12:40	3/21/2024 12:50	0.150	0.005	5	0
PER2 2024	3/21/2024 12:50	3/21/2024 13:00	0.150	0.006	5	0
PER2 2024	3/21/2024 13:00	3/21/2024 13:10	0.150	0.006	5	0
PER2 2024	3/21/2024 13:10	3/21/2024 13:20	0.150	0.006	5	0
PER2 2024	3/21/2024 13:20	3/21/2024 13:30	0.150	0.006	5	0
PER2 2024	3/21/2024 13:30	3/21/2024 13:40	0.150	0.007	5	0
PER2 2024	3/21/2024 13:40	3/21/2024 13:50	0.150	0.007	5	0
PER2 2024	3/21/2024 13:50	3/21/2024 14:00	0.150	0.007	5	0
PER2 2024	3/21/2024 14:00	3/21/2024 14:10	0.150	0.007	5	0
PER2 2024	3/21/2024 14:10	3/21/2024 14:20	0.150	0.008	5	0
PER2 2024	3/21/2024 14:20	3/21/2024 14:30	0.150	0.008	5	0
PER2 2024	3/21/2024 14:30	3/21/2024 14:40	0.150	0.008	5	0
PER2 2024	3/21/2024 14:40	3/21/2024 14:50	0.150	0.008	5	0
PER2 2024	3/21/2024 14:50	3/21/2024 15:00	0.150	0.008	5	0
PER2 2024	3/21/2024 15:00	3/21/2024 15:10	0.150	0.009	5	0
PER2 2024	3/21/2024 15:10	3/21/2024 15:20	0.150	0.009	5	0
PER2 2024	3/21/2024 15:20	3/21/2024 15:30	0.150	0.009	5	0
PER2 2024	3/21/2024 15:30	3/21/2024 15:40	0.150	0.009	5	0
PER2 2024	3/21/2024 15:40	3/21/2024 15:50	0.150	0.009	5	0
PER2 2024	3/21/2024 15:50	3/21/2024 16:00	0.150	0.009	5	0
PER2 2024	3/21/2024 16:00	3/21/2024 16:10	0.150	0.009	5	0
PER2 2024	3/21/2024 16:10	3/21/2024 16:20	0.150	0.009	5	0
PER2 2024	3/21/2024 16:20	3/21/2024 16:30	0.150	0.009	5	0
PER2 2024	3/21/2024 16:30	3/21/2024 16:40	0.150	0.009	5	0
PER2 2024	3/21/2024 16:40	3/21/2024 16:50	0.150	0.009	5	0
PER2 2024	3/21/2024 16:50	3/21/2024 17:00	0.150	0.009	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/22/2024

Weather: 30 deg. F, Cloudy

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation and foundation development.
- 2) ECD continued marine waterfront remedial excavation.
- 3) Alba performs additional excavation for recollection of EP-77, see below for details.
- 4) Collect one bottom and one sidewall sample from BMW-6/B-17/BSB-14 remedial excavation, see below for details.
- 5) Alba exported 6 loads (~120 CY) of material from WC-25 for offsite disposal at MCUA.
- 6) Alba exports 3 loads (~60 CY) of material from WC-25 for off-site disposal at the MSM facility.

Is the dewatering system operating: YES NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): EP-77_20240322_C, EP-77_20240322_E, EP-77_20240322_W, EP-77_20240322_N, EP-77_20240322_S, REBMW-6_BOT1_20240322 and REBMW-6_SW1_20240322

Air Monitoring (Since Last Report): CAMP tables and graphs are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	60	0	120
Total:(CY)	4285	0	7085	1520	2620

Site Layout Map and Excavation Figures

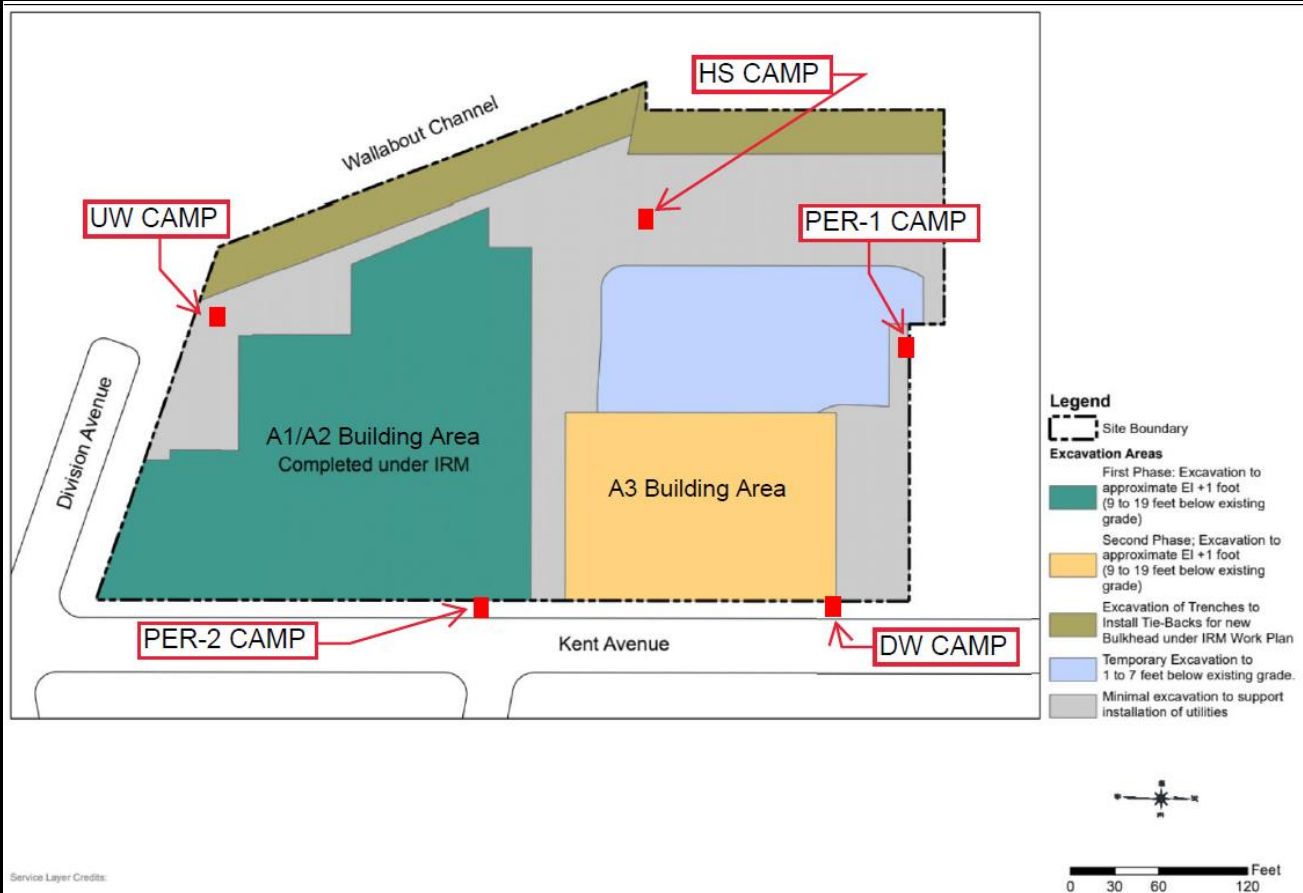

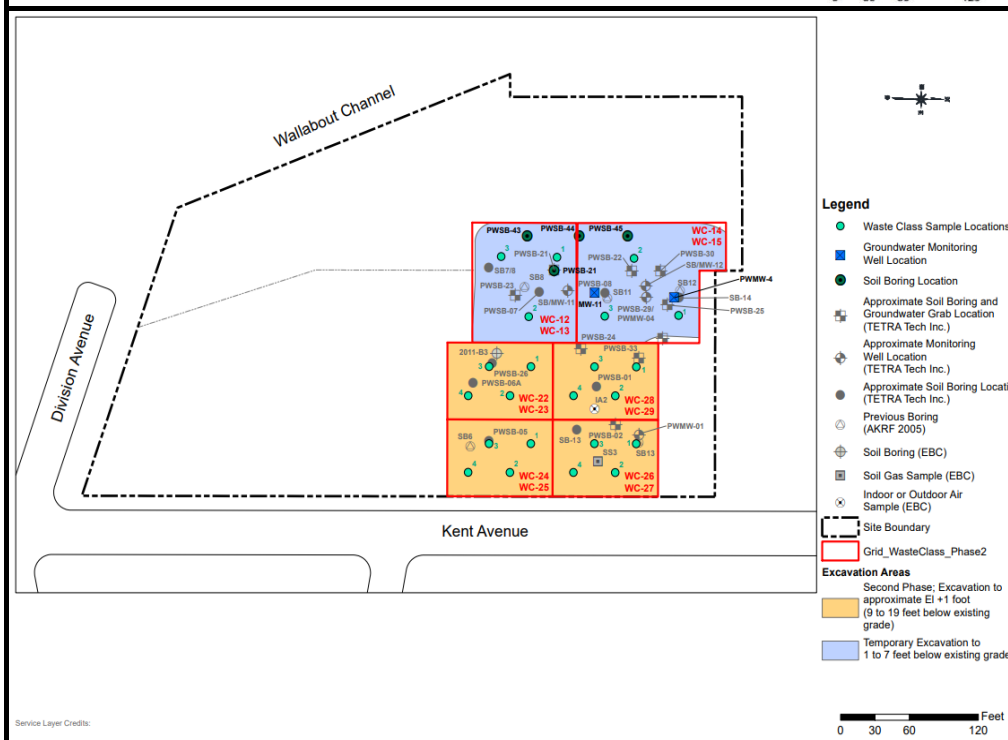
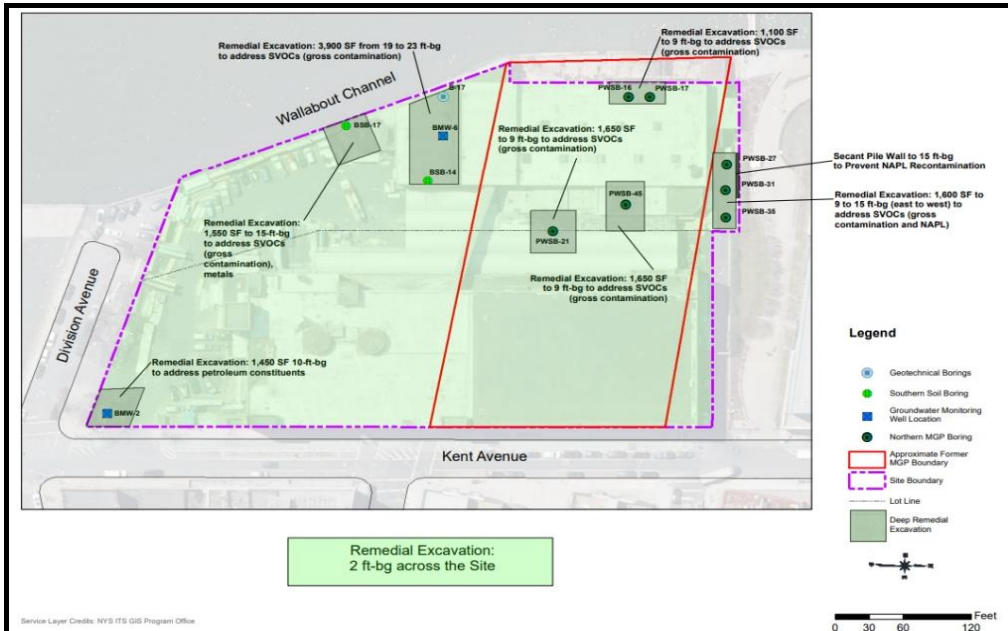


Photo 1:
View of truck loading for
off-site soil disposal.



Photo 2:
View of Site conditions
and activities facing
north.

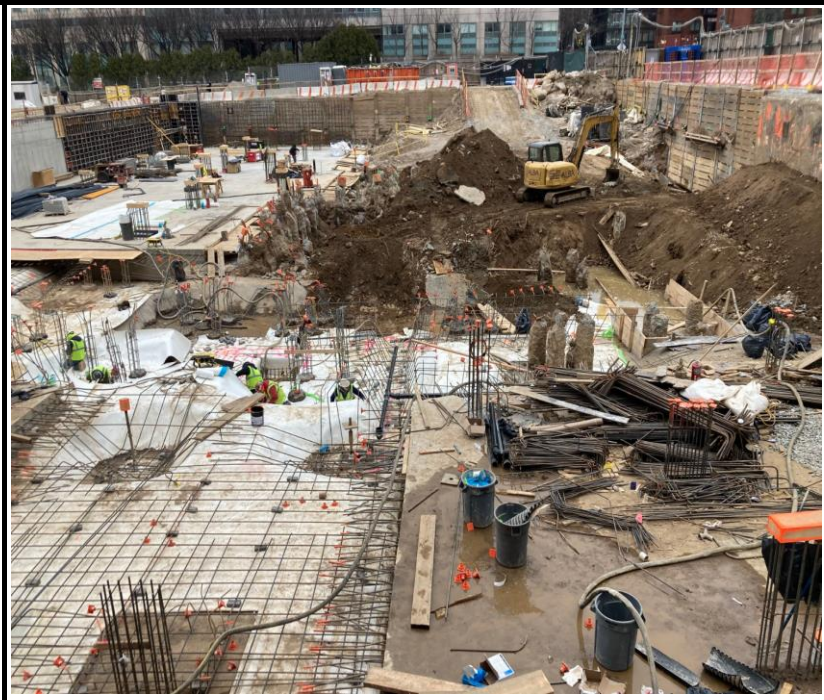


Photo 3:
View of covered
remedial excavation
soil stockpile.




Photo 4:
View of the remedial
excavation facing
west.



CAMP:
Downwind
Particulates

Dust Levels


0.018 mg/m³ 0.024 mg/m³

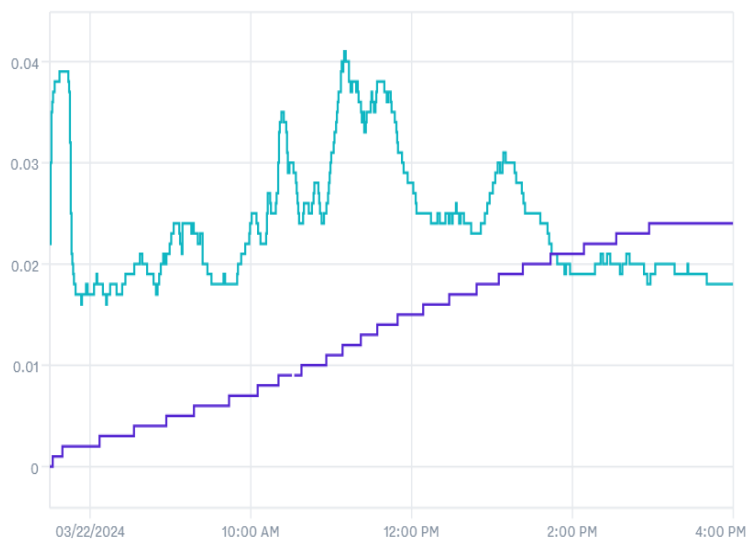

CAMP:
Downwind VOCs


VOC Levels

0.191 ppm 0.216 ppm

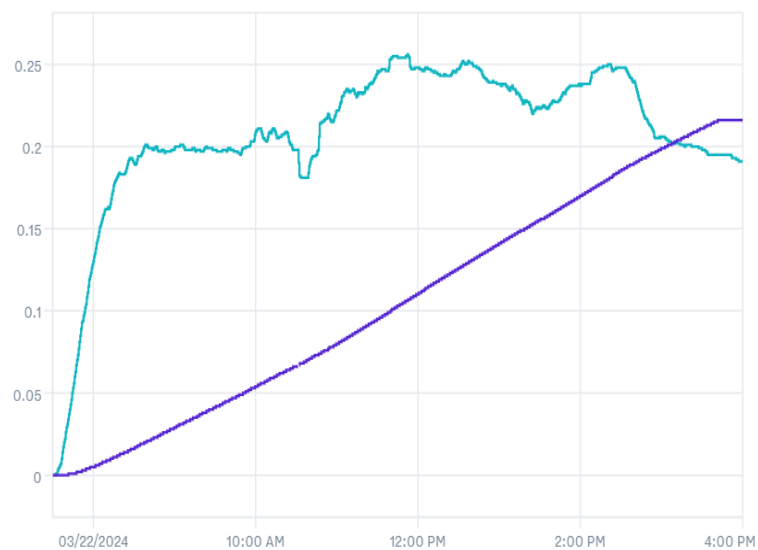


CAMP:
Upwind Particulates

Dust Levels

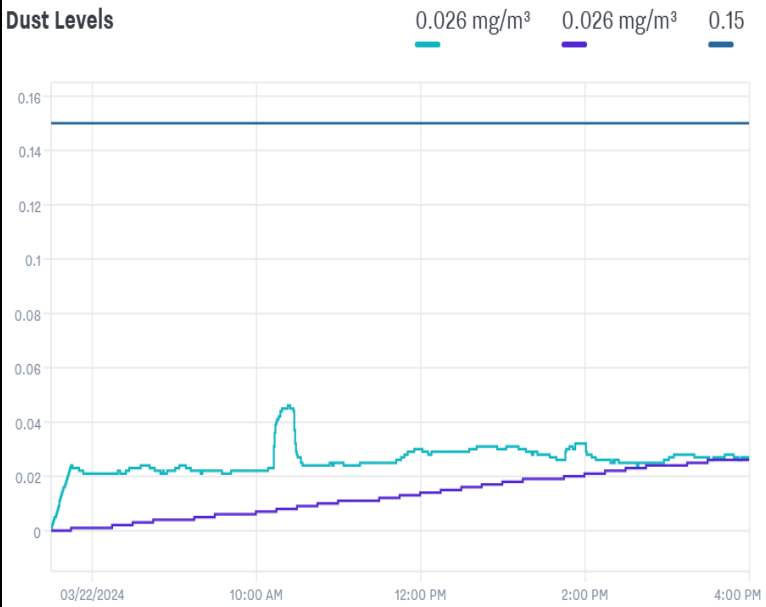

CAMP:
Upwind VOCs

VOC Levels

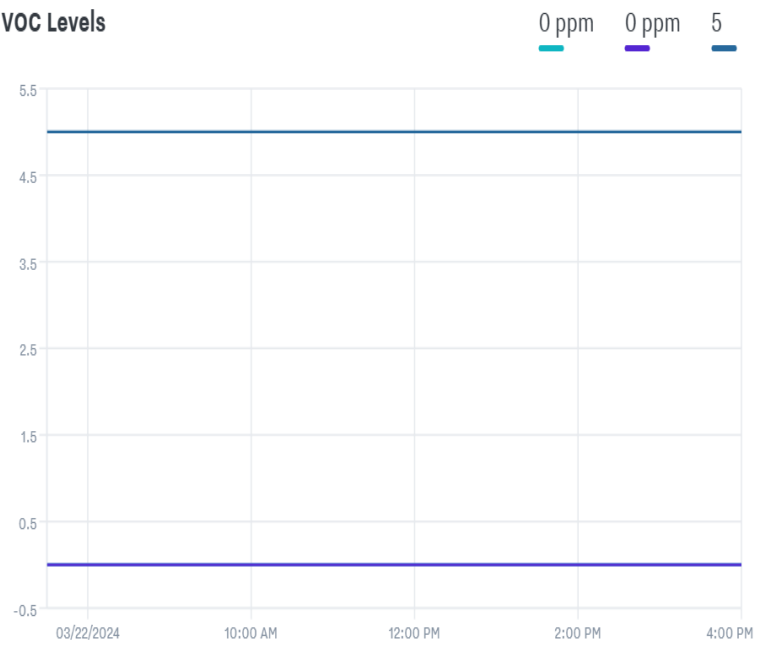

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/22/2024 7:30	3/22/2024 7:40	0.150	0.002	5	0
DW 2024	3/22/2024 7:40	3/22/2024 7:50	0.150	0.002	5	0.002
DW 2024	3/22/2024 7:50	3/22/2024 8:00	0.150	0.002	5	0.005
DW 2024	3/22/2024 8:00	3/22/2024 8:10	0.150	0.003	5	0.009
DW 2024	3/22/2024 8:10	3/22/2024 8:20	0.150	0.003	5	0.013
DW 2024	3/22/2024 8:20	3/22/2024 8:30	0.150	0.003	5	0.016
DW 2024	3/22/2024 8:30	3/22/2024 8:40	0.150	0.004	5	0.021
DW 2024	3/22/2024 8:40	3/22/2024 8:50	0.150	0.004	5	0.025
DW 2024	3/22/2024 8:50	3/22/2024 9:00	0.150	0.005	5	0.029
DW 2024	3/22/2024 9:00	3/22/2024 9:10	0.150	0.005	5	0.033
DW 2024	3/22/2024 9:10	3/22/2024 9:20	0.150	0.006	5	0.037
DW 2024	3/22/2024 9:20	3/22/2024 9:30	0.150	0.006	5	0.041
DW 2024	3/22/2024 9:30	3/22/2024 9:40	0.150	0.006	5	0.045
DW 2024	3/22/2024 9:40	3/22/2024 9:50	0.150	0.007	5	0.049
DW 2024	3/22/2024 9:50	3/22/2024 10:00	0.150	0.007	5	0.054
DW 2024	3/22/2024 10:00	3/22/2024 10:10	0.150	0.008	5	0.058
DW 2024	3/22/2024 10:10	3/22/2024 10:20	0.150	0.008	5	0.062
DW 2024	3/22/2024 10:20	3/22/2024 10:30	0.150	0.009	5	0.066
DW 2024	3/22/2024 10:30	3/22/2024 10:40	0.150	0.01	5	0.071
DW 2024	3/22/2024 10:40	3/22/2024 10:50	0.150	0.01	5	0.075
DW 2024	3/22/2024 10:50	3/22/2024 11:00	0.150	0.011	5	0.08
DW 2024	3/22/2024 11:00	3/22/2024 11:10	0.150	0.012	5	0.085
DW 2024	3/22/2024 11:10	3/22/2024 11:20	0.150	0.012	5	0.09
DW 2024	3/22/2024 11:20	3/22/2024 11:30	0.150	0.013	5	0.095
DW 2024	3/22/2024 11:30	3/22/2024 11:40	0.150	0.014	5	0.1
DW 2024	3/22/2024 11:40	3/22/2024 11:50	0.150	0.015	5	0.105
DW 2024	3/22/2024 11:50	3/22/2024 12:00	0.150	0.015	5	0.11
DW 2024	3/22/2024 12:00	3/22/2024 12:10	0.150	0.016	5	0.116
DW 2024	3/22/2024 12:10	3/22/2024 12:20	0.150	0.016	5	0.121
DW 2024	3/22/2024 12:20	3/22/2024 12:30	0.150	0.017	5	0.126
DW 2024	3/22/2024 12:30	3/22/2024 12:40	0.150	0.017	5	0.131
DW 2024	3/22/2024 12:40	3/22/2024 12:50	0.150	0.018	5	0.136
DW 2024	3/22/2024 12:50	3/22/2024 13:00	0.150	0.018	5	0.141
DW 2024	3/22/2024 13:00	3/22/2024 13:10	0.150	0.019	5	0.146
DW 2024	3/22/2024 13:10	3/22/2024 13:20	0.150	0.019	5	0.15
DW 2024	3/22/2024 13:20	3/22/2024 13:30	0.150	0.02	5	0.155
DW 2024	3/22/2024 13:30	3/22/2024 13:40	0.150	0.02	5	0.16
DW 2024	3/22/2024 13:40	3/22/2024 13:50	0.150	0.021	5	0.165
DW 2024	3/22/2024 13:50	3/22/2024 14:00	0.150	0.021	5	0.17
DW 2024	3/22/2024 14:00	3/22/2024 14:10	0.150	0.022	5	0.175
DW 2024	3/22/2024 14:10	3/22/2024 14:20	0.150	0.022	5	0.18
DW 2024	3/22/2024 14:20	3/22/2024 14:30	0.150	0.022	5	0.185
DW 2024	3/22/2024 14:30	3/22/2024 14:40	0.150	0.023	5	0.19
DW 2024	3/22/2024 14:40	3/22/2024 14:50	0.150	0.023	5	0.194
DW 2024	3/22/2024 14:50	3/22/2024 15:00	0.150	0.024	5	0.199
DW 2024	3/22/2024 15:00	3/22/2024 15:10	0.150	0.024	5	0.203
DW 2024	3/22/2024 15:10	3/22/2024 15:20	0.150	0.024	5	0.207
DW 2024	3/22/2024 15:20	3/22/2024 15:30	0.150	0.024	5	0.211
DW 2024	3/22/2024 15:30	3/22/2024 15:40	0.150	0.024	5	0.215
DW 2024	3/22/2024 15:40	3/22/2024 15:50	0.150	0.024	5	0.216
DW 2024	3/22/2024 15:50	3/22/2024 16:00	0.150	0.024	5	0.216
DW 2024	3/22/2024 16:00	3/22/2024 16:10	0.150	0.024	5	0.216
DW 2024	3/22/2024 16:10	3/22/2024 16:20	0.150	0.024	5	0.216
DW 2024	3/22/2024 16:20	3/22/2024 16:30	0.150	0.024	5	0.216

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/22/2024 7:30	3/22/2024 7:40	0.150	0	5	0
UW 2024	3/22/2024 7:40	3/22/2024 7:50	0.150	0.001	5	0
UW 2024	3/22/2024 7:50	3/22/2024 8:00	0.150	0.001	5	0
UW 2024	3/22/2024 8:00	3/22/2024 8:10	0.150	0.001	5	0
UW 2024	3/22/2024 8:10	3/22/2024 8:20	0.150	0.002	5	0
UW 2024	3/22/2024 8:20	3/22/2024 8:30	0.150	0.003	5	0
UW 2024	3/22/2024 8:30	3/22/2024 8:40	0.150	0.003	5	0
UW 2024	3/22/2024 8:40	3/22/2024 8:50	0.150	0.004	5	0
UW 2024	3/22/2024 8:50	3/22/2024 9:00	0.150	0.004	5	0
UW 2024	3/22/2024 9:00	3/22/2024 9:10	0.150	0.004	5	0
UW 2024	3/22/2024 9:10	3/22/2024 9:20	0.150	0.005	5	0
UW 2024	3/22/2024 9:20	3/22/2024 9:30	0.150	0.006	5	0
UW 2024	3/22/2024 9:30	3/22/2024 9:40	0.150	0.006	5	0
UW 2024	3/22/2024 9:40	3/22/2024 9:50	0.150	0.006	5	0
UW 2024	3/22/2024 9:50	3/22/2024 10:00	0.150	0.007	5	0
UW 2024	3/22/2024 10:00	3/22/2024 10:10	0.150	0.007	5	0
UW 2024	3/22/2024 10:10	3/22/2024 10:20	0.150	0.008	5	0
UW 2024	3/22/2024 10:20	3/22/2024 10:30	0.150	0.009	5	0
UW 2024	3/22/2024 10:30	3/22/2024 10:40	0.150	0.009	5	0
UW 2024	3/22/2024 10:40	3/22/2024 10:50	0.150	0.01	5	0
UW 2024	3/22/2024 10:50	3/22/2024 11:00	0.150	0.011	5	0
UW 2024	3/22/2024 11:00	3/22/2024 11:10	0.150	0.011	5	0
UW 2024	3/22/2024 11:10	3/22/2024 11:20	0.150	0.011	5	0
UW 2024	3/22/2024 11:20	3/22/2024 11:30	0.150	0.012	5	0
UW 2024	3/22/2024 11:30	3/22/2024 11:40	0.150	0.012	5	0
UW 2024	3/22/2024 11:40	3/22/2024 11:50	0.150	0.013	5	0
UW 2024	3/22/2024 11:50	3/22/2024 12:00	0.150	0.014	5	0
UW 2024	3/22/2024 12:00	3/22/2024 12:10	0.150	0.014	5	0
UW 2024	3/22/2024 12:10	3/22/2024 12:20	0.150	0.015	5	0
UW 2024	3/22/2024 12:20	3/22/2024 12:30	0.150	0.016	5	0
UW 2024	3/22/2024 12:30	3/22/2024 12:40	0.150	0.016	5	0
UW 2024	3/22/2024 12:40	3/22/2024 12:50	0.150	0.017	5	0
UW 2024	3/22/2024 12:50	3/22/2024 13:00	0.150	0.018	5	0
UW 2024	3/22/2024 13:00	3/22/2024 13:10	0.150	0.018	5	0
UW 2024	3/22/2024 13:10	3/22/2024 13:20	0.150	0.019	5	0
UW 2024	3/22/2024 13:20	3/22/2024 13:30	0.150	0.019	5	0
UW 2024	3/22/2024 13:30	3/22/2024 13:40	0.150	0.019	5	0
UW 2024	3/22/2024 13:40	3/22/2024 13:50	0.150	0.02	5	0
UW 2024	3/22/2024 13:50	3/22/2024 14:00	0.150	0.021	5	0
UW 2024	3/22/2024 14:00	3/22/2024 14:10	0.150	0.021	5	0
UW 2024	3/22/2024 14:10	3/22/2024 14:20	0.150	0.022	5	0
UW 2024	3/22/2024 14:20	3/22/2024 14:30	0.150	0.023	5	0
UW 2024	3/22/2024 14:30	3/22/2024 14:40	0.150	0.023	5	0
UW 2024	3/22/2024 14:40	3/22/2024 14:50	0.150	0.024	5	0
UW 2024	3/22/2024 14:50	3/22/2024 15:00	0.150	0.024	5	0
UW 2024	3/22/2024 15:00	3/22/2024 15:10	0.150	0.024	5	0
UW 2024	3/22/2024 15:10	3/22/2024 15:20	0.150	0.025	5	0
UW 2024	3/22/2024 15:20	3/22/2024 15:30	0.150	0.026	5	0
UW 2024	3/22/2024 15:30	3/22/2024 15:40	0.150	0.026	5	0
UW 2024	3/22/2024 15:40	3/22/2024 15:50	0.150	0.026	5	0
UW 2024	3/22/2024 15:50	3/22/2024 16:00	0.150	0.026	5	0
UW 2024	3/22/2024 16:00	3/22/2024 16:10	0.150	0.026	5	0
UW 2024	3/22/2024 16:10	3/22/2024 16:20	0.150	0.026	5	0
UW 2024	3/22/2024 16:20	3/22/2024 16:30	0.150	0.026	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/22/2024 7:30	3/22/2024 7:40	0.150	0	5	0
HS South	3/22/2024 7:40	3/22/2024 7:50	0.150	0	5	0
HS South	3/22/2024 7:50	3/22/2024 8:00	0.150	0.001	5	0
HS South	3/22/2024 8:00	3/22/2024 8:10	0.150	0.001	5	0
HS South	3/22/2024 8:10	3/22/2024 8:20	0.150	0.001	5	0
HS South	3/22/2024 8:20	3/22/2024 8:30	0.150	0.002	5	0
HS South	3/22/2024 8:30	3/22/2024 8:40	0.150	0.002	5	0
HS South	3/22/2024 8:40	3/22/2024 8:50	0.150	0.002	5	0
HS South	3/22/2024 8:50	3/22/2024 9:00	0.150	0.003	5	0
HS South	3/22/2024 9:00	3/22/2024 9:10	0.150	0.003	5	0
HS South	3/22/2024 9:10	3/22/2024 9:20	0.150	0.003	5	0
HS South	3/22/2024 9:20	3/22/2024 9:30	0.150	0.004	5	0
HS South	3/22/2024 9:30	3/22/2024 9:40	0.150	0.004	5	0
HS South	3/22/2024 9:40	3/22/2024 9:50	0.150	0.004	5	0
HS South	3/22/2024 9:50	3/22/2024 10:00	0.150	0.004	5	0
HS South	3/22/2024 10:00	3/22/2024 10:10	0.150	0.004	5	0
HS South	3/22/2024 10:10	3/22/2024 10:20	0.150	0.005	5	0
HS South	3/22/2024 10:20	3/22/2024 10:30	0.150	0.005	5	0
HS South	3/22/2024 10:30	3/22/2024 10:40	0.150	0.005	5	0
HS South	3/22/2024 10:40	3/22/2024 10:50	0.150	0.005	5	0
HS South	3/22/2024 10:50	3/22/2024 11:00	0.150	0.006	5	0
HS South	3/22/2024 11:00	3/22/2024 11:10	0.150	0.006	5	0
HS South	3/22/2024 11:10	3/22/2024 11:20	0.150	0.006	5	0
HS South	3/22/2024 11:20	3/22/2024 11:30	0.150	0.006	5	0
HS South	3/22/2024 11:30	3/22/2024 11:40	0.150	0.007	5	0
HS South	3/22/2024 11:40	3/22/2024 11:50	0.150	0.007	5	0
HS South	3/22/2024 11:50	3/22/2024 12:00	0.150	0.008	5	0
HS South	3/22/2024 12:00	3/22/2024 12:10	0.150	0.008	5	0
HS South	3/22/2024 12:10	3/22/2024 12:20	0.150	0.008	5	0
HS South	3/22/2024 12:20	3/22/2024 12:30	0.150	0.009	5	0
HS South	3/22/2024 12:30	3/22/2024 12:40	0.150	0.009	5	0
HS South	3/22/2024 12:40	3/22/2024 12:50	0.150	0.01	5	0
HS South	3/22/2024 12:50	3/22/2024 13:00	0.150	0.01	5	0
HS South	3/22/2024 13:00	3/22/2024 13:10	0.150	0.01	5	0
HS South	3/22/2024 13:10	3/22/2024 13:20	0.150	0.011	5	0
HS South	3/22/2024 13:20	3/22/2024 13:30	0.150	0.012	5	0
HS South	3/22/2024 13:30	3/22/2024 13:40	0.150	0.012	5	0
HS South	3/22/2024 13:40	3/22/2024 13:50	0.150	0.013	5	0
HS South	3/22/2024 13:50	3/22/2024 14:00	0.150	0.013	5	0
HS South	3/22/2024 14:00	3/22/2024 14:10	0.150	0.013	5	0
HS South	3/22/2024 14:10	3/22/2024 14:20	0.150	0.014	5	0
HS South	3/22/2024 14:20	3/22/2024 14:30	0.150	0.015	5	0
HS South	3/22/2024 14:30	3/22/2024 14:40	0.150	0.015	5	0
HS South	3/22/2024 14:40	3/22/2024 14:50	0.150	0.015	5	0
HS South	3/22/2024 14:50	3/22/2024 15:00	0.150	0.015	5	0
HS South	3/22/2024 15:00	3/22/2024 15:10	0.150	0.016	5	0
HS South	3/22/2024 15:10	3/22/2024 15:20	0.150	0.016	5	0
HS South	3/22/2024 15:20	3/22/2024 15:30	0.150	0.016	5	0
HS South	3/22/2024 15:30	3/22/2024 15:40	0.150	0.017	5	0
HS South	3/22/2024 15:40	3/22/2024 15:50	0.150	0.017	5	0
HS South	3/22/2024 15:50	3/22/2024 16:00	0.150	0.017	5	0
HS South	3/22/2024 16:00	3/22/2024 16:10	0.150	0.017	5	0
HS South	3/22/2024 16:10	3/22/2024 16:20	0.150	0.017	5	0
HS South	3/22/2024 16:20	3/22/2024 16:30	0.150	0.017	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/22/2024 7:30	3/22/2024 7:40	0.150	0.001	5	0
PER1 2024	3/22/2024 7:40	3/22/2024 7:50	0.150	0.002	5	0
PER1 2024	3/22/2024 7:50	3/22/2024 8:00	0.150	0.002	5	0
PER1 2024	3/22/2024 8:00	3/22/2024 8:10	0.150	0.003	5	0
PER1 2024	3/22/2024 8:10	3/22/2024 8:20	0.150	0.003	5	0
PER1 2024	3/22/2024 8:20	3/22/2024 8:30	0.150	0.004	5	0
PER1 2024	3/22/2024 8:30	3/22/2024 8:40	0.150	0.004	5	0
PER1 2024	3/22/2024 8:40	3/22/2024 8:50	0.150	0.005	5	0
PER1 2024	3/22/2024 8:50	3/22/2024 9:00	0.150	0.005	5	0
PER1 2024	3/22/2024 9:00	3/22/2024 9:10	0.150	0.006	5	0
PER1 2024	3/22/2024 9:10	3/22/2024 9:20	0.150	0.006	5	0
PER1 2024	3/22/2024 9:20	3/22/2024 9:30	0.150	0.006	5	0
PER1 2024	3/22/2024 9:30	3/22/2024 9:40	0.150	0.007	5	0
PER1 2024	3/22/2024 9:40	3/22/2024 9:50	0.150	0.007	5	0
PER1 2024	3/22/2024 9:50	3/22/2024 10:00	0.150	0.008	5	0
PER1 2024	3/22/2024 10:00	3/22/2024 10:10	0.150	0.008	5	0
PER1 2024	3/22/2024 10:10	3/22/2024 10:20	0.150	0.009	5	0
PER1 2024	3/22/2024 10:20	3/22/2024 10:30	0.150	0.009	5	0
PER1 2024	3/22/2024 10:30	3/22/2024 10:40	0.150	0.01	5	0
PER1 2024	3/22/2024 10:40	3/22/2024 10:50	0.150	0.01	5	0
PER1 2024	3/22/2024 10:50	3/22/2024 11:00	0.150	0.011	5	0
PER1 2024	3/22/2024 11:00	3/22/2024 11:10	0.150	0.012	5	0
PER1 2024	3/22/2024 11:10	3/22/2024 11:20	0.150	0.013	5	0
PER1 2024	3/22/2024 11:20	3/22/2024 11:30	0.150	0.013	5	0
PER1 2024	3/22/2024 11:30	3/22/2024 11:40	0.150	0.014	5	0
PER1 2024	3/22/2024 11:40	3/22/2024 11:50	0.150	0.014	5	0.105
PER1 2024	3/22/2024 11:50	3/22/2024 12:00	0.150	0.015	5	0.108
PER1 2024	3/22/2024 12:00	3/22/2024 12:10	0.150	0.015	5	0.108
PER1 2024	3/22/2024 12:10	3/22/2024 12:20	0.150	0.016	5	0.108
PER1 2024	3/22/2024 12:20	3/22/2024 12:30	0.150	0.017	5	0.108
PER1 2024	3/22/2024 12:30	3/22/2024 12:40	0.150	0.017	5	0.108
PER1 2024	3/22/2024 12:40	3/22/2024 12:50	0.150	0.018	5	0.108
PER1 2024	3/22/2024 12:50	3/22/2024 13:00	0.150	0.019	5	0.108
PER1 2024	3/22/2024 13:00	3/22/2024 13:10	0.150	0.019	5	0.108
PER1 2024	3/22/2024 13:10	3/22/2024 13:20	0.150	0.02	5	0.108
PER1 2024	3/22/2024 13:20	3/22/2024 13:30	0.150	0.021	5	0.108
PER1 2024	3/22/2024 13:30	3/22/2024 13:40	0.150	0.021	5	0.108
PER1 2024	3/22/2024 13:40	3/22/2024 13:50	0.150	0.022	5	0.108
PER1 2024	3/22/2024 13:50	3/22/2024 14:00	0.150	0.023	5	0.108
PER1 2024	3/22/2024 14:00	3/22/2024 14:10	0.150	0.023	5	0.108
PER1 2024	3/22/2024 14:10	3/22/2024 14:20	0.150	0.024	5	0.108
PER1 2024	3/22/2024 14:20	3/22/2024 14:30	0.150	0.025	5	0.108
PER1 2024	3/22/2024 14:30	3/22/2024 14:40	0.150	0.026	5	0.108
PER1 2024	3/22/2024 14:40	3/22/2024 14:50	0.150	0.026	5	0.108
PER1 2024	3/22/2024 14:50	3/22/2024 15:00	0.150	0.027	5	0.108
PER1 2024	3/22/2024 15:00	3/22/2024 15:10	0.150	0.028	5	0.108
PER1 2024	3/22/2024 15:10	3/22/2024 15:20	0.150	0.028	5	0.108
PER1 2024	3/22/2024 15:20	3/22/2024 15:30	0.150	0.028	5	0.108
PER1 2024	3/22/2024 15:30	3/22/2024 15:40	0.150	0.028	5	0
PER1 2024	3/22/2024 15:40	3/22/2024 15:50	0.150	0	5	0
PER1 2024	3/22/2024 15:50	3/22/2024 16:00	0.150	0	5	0
PER1 2024	3/22/2024 16:00	3/22/2024 16:10	0.150	0	5	0
PER1 2024	3/22/2024 16:10	3/22/2024 16:20	0.150	0	5	0
PER1 2024	3/22/2024 16:20	3/22/2024 16:30	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/22/2024 7:30	3/22/2024 7:40	0.150	0.001	5	0
PER2 2024	3/22/2024 7:40	3/22/2024 7:50	0.150	0.001	5	0
PER2 2024	3/22/2024 7:50	3/22/2024 8:00	0.150	0.001	5	0
PER2 2024	3/22/2024 8:00	3/22/2024 8:10	0.150	0.001	5	0
PER2 2024	3/22/2024 8:10	3/22/2024 8:20	0.150	0.002	5	0
PER2 2024	3/22/2024 8:20	3/22/2024 8:30	0.150	0.002	5	0
PER2 2024	3/22/2024 8:30	3/22/2024 8:40	0.150	0.002	5	0
PER2 2024	3/22/2024 8:40	3/22/2024 8:50	0.150	0.003	5	0
PER2 2024	3/22/2024 8:50	3/22/2024 9:00	0.150	0.003	5	0
PER2 2024	3/22/2024 9:00	3/22/2024 9:10	0.150	0.004	5	0
PER2 2024	3/22/2024 9:10	3/22/2024 9:20	0.150	0.004	5	0
PER2 2024	3/22/2024 9:20	3/22/2024 9:30	0.150	0.004	5	0
PER2 2024	3/22/2024 9:30	3/22/2024 9:40	0.150	0.005	5	0
PER2 2024	3/22/2024 9:40	3/22/2024 9:50	0.150	0.005	5	0
PER2 2024	3/22/2024 9:50	3/22/2024 10:00	0.150	0.005	5	0
PER2 2024	3/22/2024 10:00	3/22/2024 10:10	0.150	0.006	5	0
PER2 2024	3/22/2024 10:10	3/22/2024 10:20	0.150	0.006	5	0
PER2 2024	3/22/2024 10:20	3/22/2024 10:30	0.150	0.006	5	0
PER2 2024	3/22/2024 10:30	3/22/2024 10:40	0.150	0.008	5	0
PER2 2024	3/22/2024 10:40	3/22/2024 10:50	0.150	0.008	5	0
PER2 2024	3/22/2024 10:50	3/22/2024 11:00	0.150	0.009	5	0
PER2 2024	3/22/2024 11:00	3/22/2024 11:10	0.150	0.009	5	0
PER2 2024	3/22/2024 11:10	3/22/2024 11:20	0.150	0.01	5	0
PER2 2024	3/22/2024 11:20	3/22/2024 11:30	0.150	0.01	5	0
PER2 2024	3/22/2024 11:30	3/22/2024 11:40	0.150	0.011	5	0
PER2 2024	3/22/2024 11:40	3/22/2024 11:50	0.150	0.011	5	0
PER2 2024	3/22/2024 11:50	3/22/2024 12:00	0.150	0.012	5	0
PER2 2024	3/22/2024 12:00	3/22/2024 12:10	0.150	0.012	5	0
PER2 2024	3/22/2024 12:10	3/22/2024 12:20	0.150	0.013	5	0
PER2 2024	3/22/2024 12:20	3/22/2024 12:30	0.150	0.013	5	0
PER2 2024	3/22/2024 12:30	3/22/2024 12:40	0.150	0.014	5	0
PER2 2024	3/22/2024 12:40	3/22/2024 12:50	0.150	0.015	5	0
PER2 2024	3/22/2024 12:50	3/22/2024 13:00	0.150	0.015	5	0
PER2 2024	3/22/2024 13:00	3/22/2024 13:10	0.150	0.016	5	0
PER2 2024	3/22/2024 13:10	3/22/2024 13:20	0.150	0.016	5	0
PER2 2024	3/22/2024 13:20	3/22/2024 13:30	0.150	0.017	5	0
PER2 2024	3/22/2024 13:30	3/22/2024 13:40	0.150	0.017	5	0
PER2 2024	3/22/2024 13:40	3/22/2024 13:50	0.150	0.018	5	0
PER2 2024	3/22/2024 13:50	3/22/2024 14:00	0.150	0.018	5	0
PER2 2024	3/22/2024 14:00	3/22/2024 14:10	0.150	0.019	5	0
PER2 2024	3/22/2024 14:10	3/22/2024 14:20	0.150	0.019	5	0
PER2 2024	3/22/2024 14:20	3/22/2024 14:30	0.150	0.02	5	0
PER2 2024	3/22/2024 14:30	3/22/2024 14:40	0.150	0.02	5	0
PER2 2024	3/22/2024 14:40	3/22/2024 14:50	0.150	0.021	5	0
PER2 2024	3/22/2024 14:50	3/22/2024 15:00	0.150	0.021	5	0
PER2 2024	3/22/2024 15:00	3/22/2024 15:10	0.150	0.022	5	0
PER2 2024	3/22/2024 15:10	3/22/2024 15:20	0.150	0.022	5	0
PER2 2024	3/22/2024 15:20	3/22/2024 15:30	0.150	0.022	5	0
PER2 2024	3/22/2024 15:30	3/22/2024 15:40	0.150	0.022	5	0
PER2 2024	3/22/2024 15:40	3/22/2024 15:50	0.150	0.022	5	0
PER2 2024	3/22/2024 15:50	3/22/2024 16:00	0.150	0.022	5	0
PER2 2024	3/22/2024 16:00	3/22/2024 16:10	0.150	0.022	5	0
PER2 2024	3/22/2024 16:10	3/22/2024 16:20	0.150	0.022	5	0
PER2 2024	3/22/2024 16:20	3/22/2024 16:30	0.150	0.022	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/25/2024

Weather: 40 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation and foundation development.
- 2) ECD continued marine waterfront remedial excavation and received two loads of clean stone.
- 3) Alba exported 10 loads (~200 CY) of material from WC-25 for offsite disposal at the MSM facility.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP tables and graphs are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	200	0	0
Total:(CY)	4285	0	7285	1520	2620

Site Layout Map and Excavation Figures

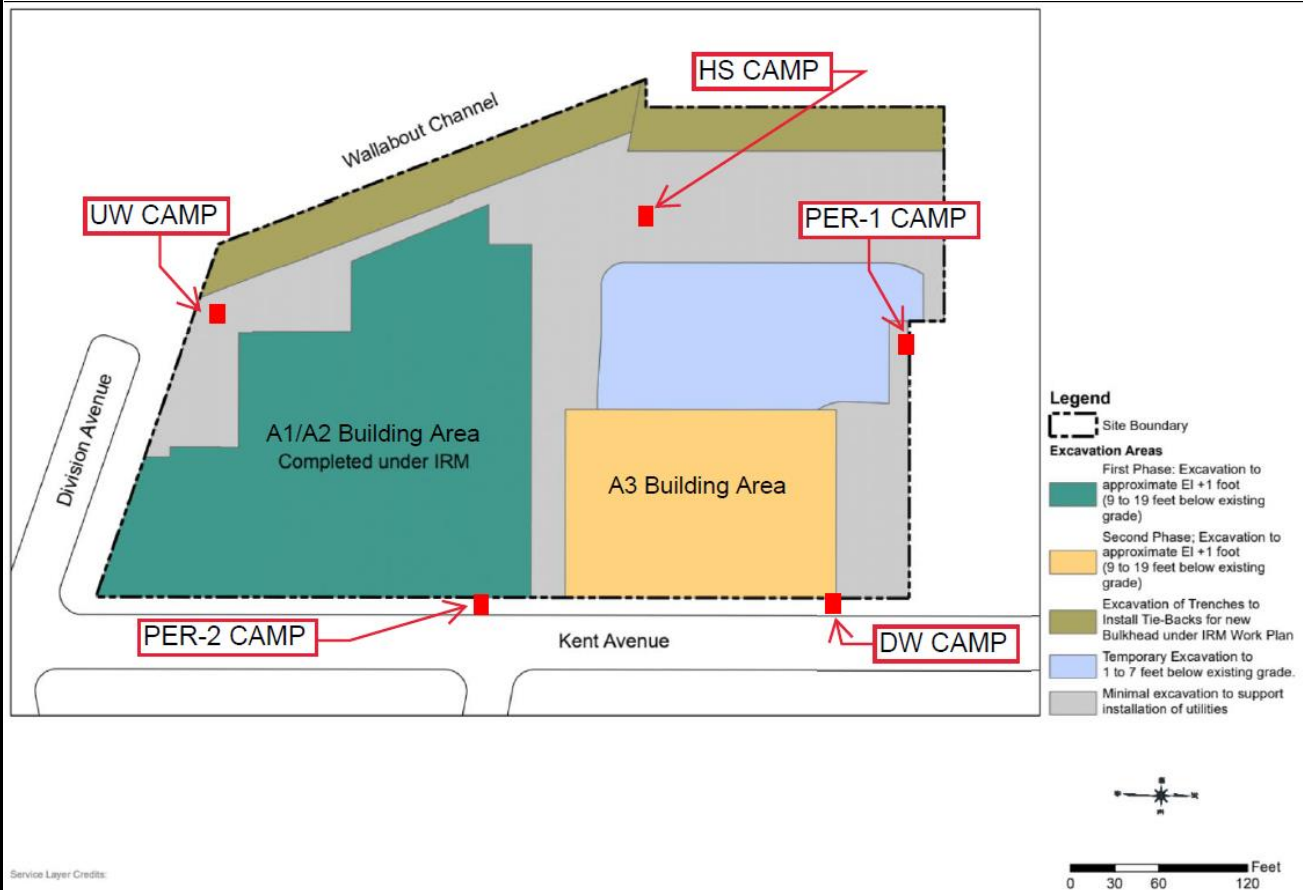

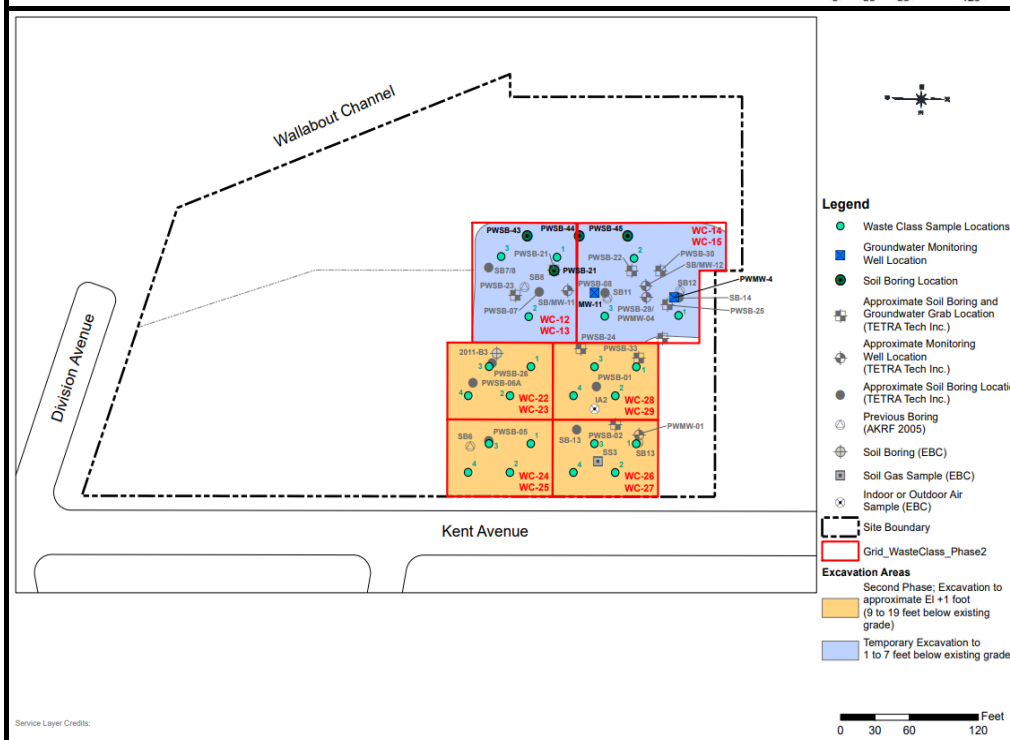
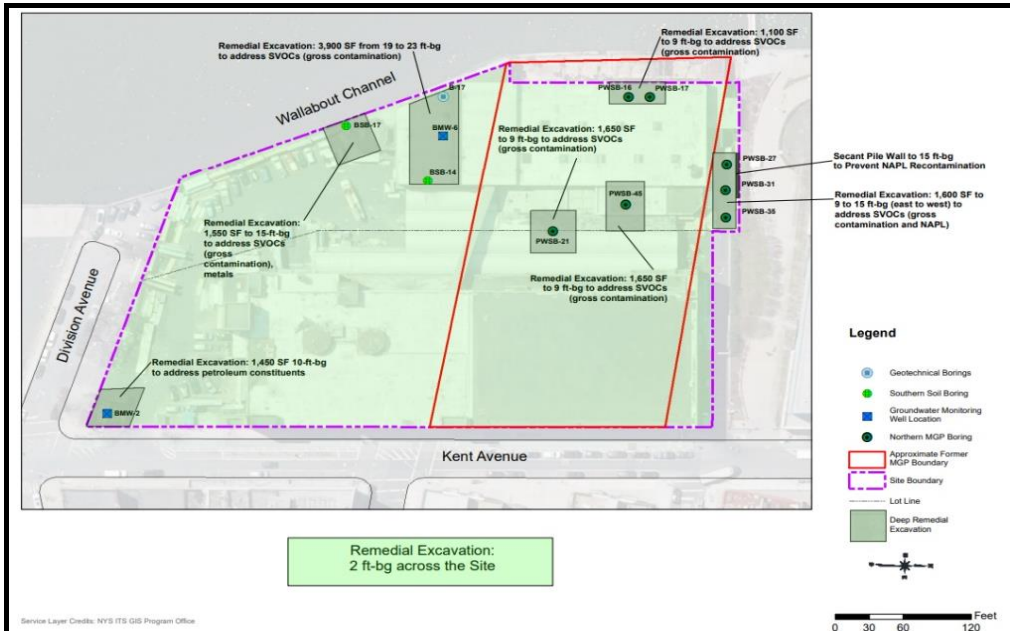


Photo 1:
View of Site conditions
and activities facing
northwest.

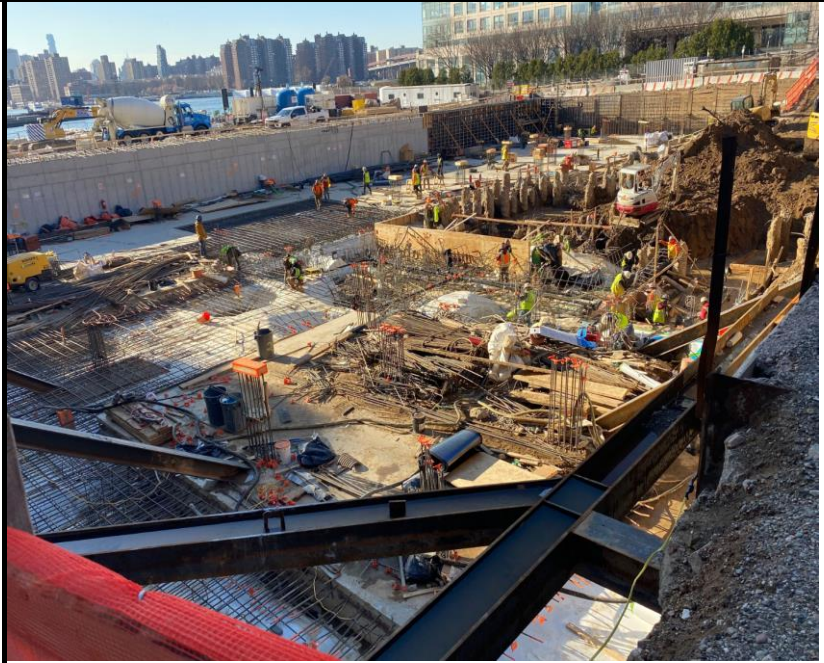


Photo 2:
View of soil excavation.



Photo 3:
View of soil
excavation and Site
conditions facing
north.


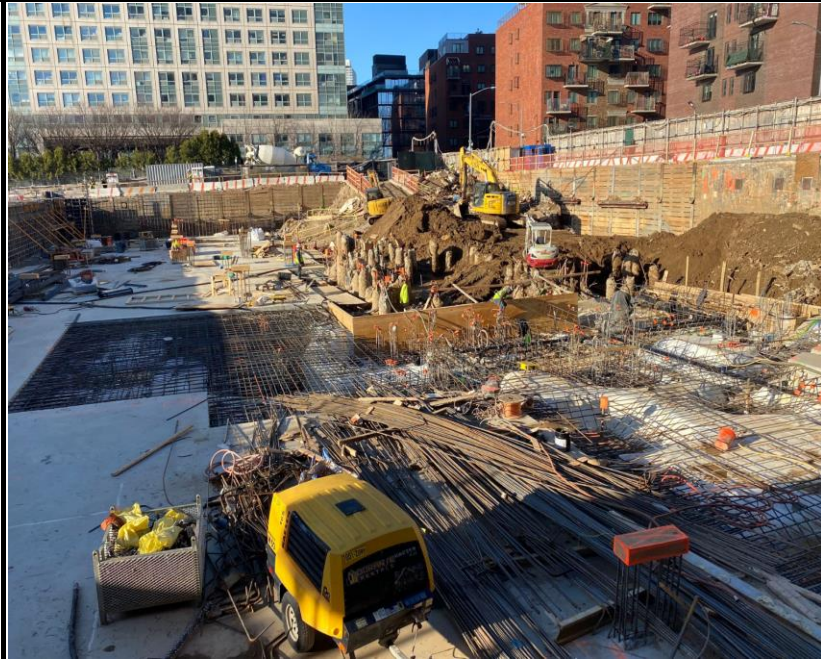


Photo 4:
View of the remedial
excavation stockpile.




CAMP:
Downwind
Particulates

Dust Levels

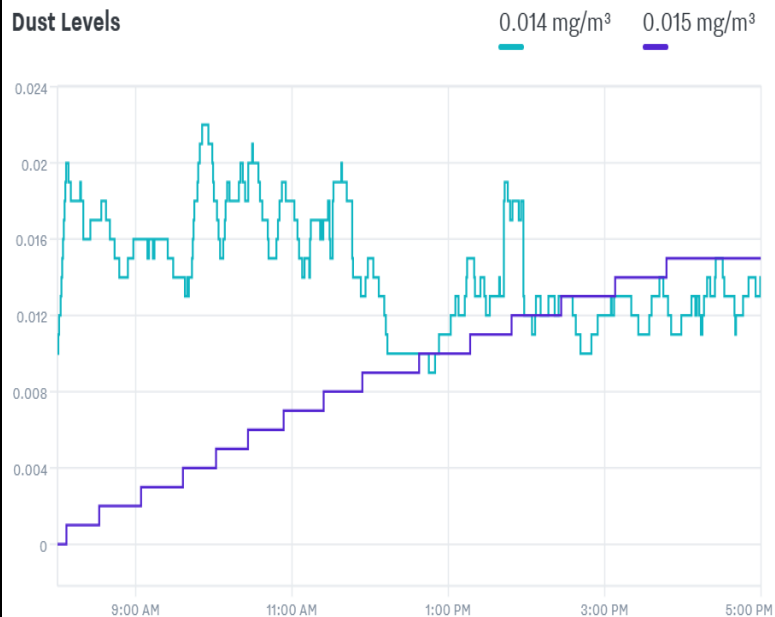


CAMP:
Downwind VOCs


VOC Levels

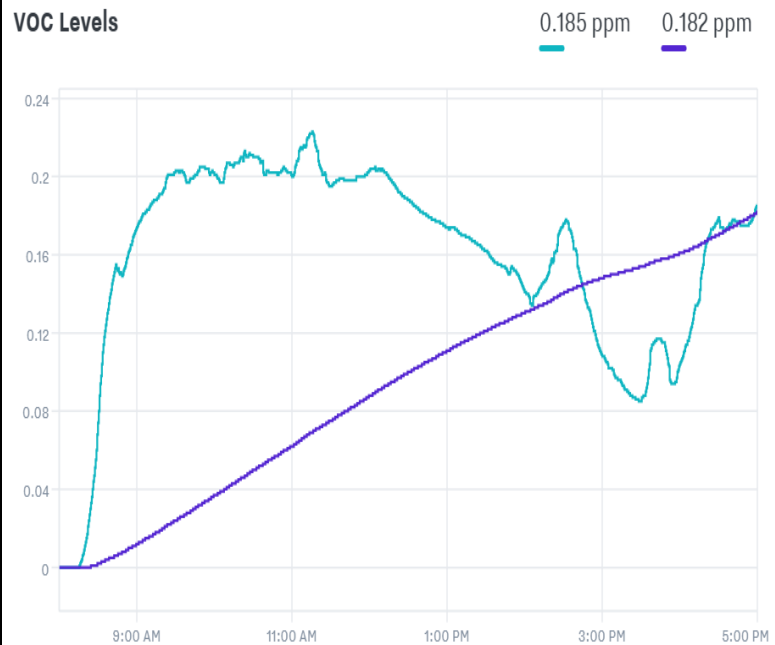

CAMP:
Upwind Particulates

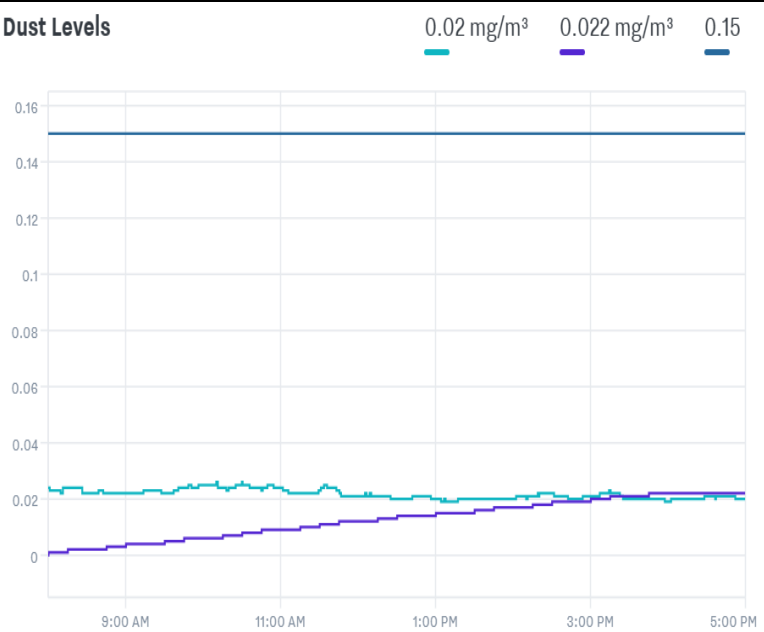

CAMP:
Upwind VOCs

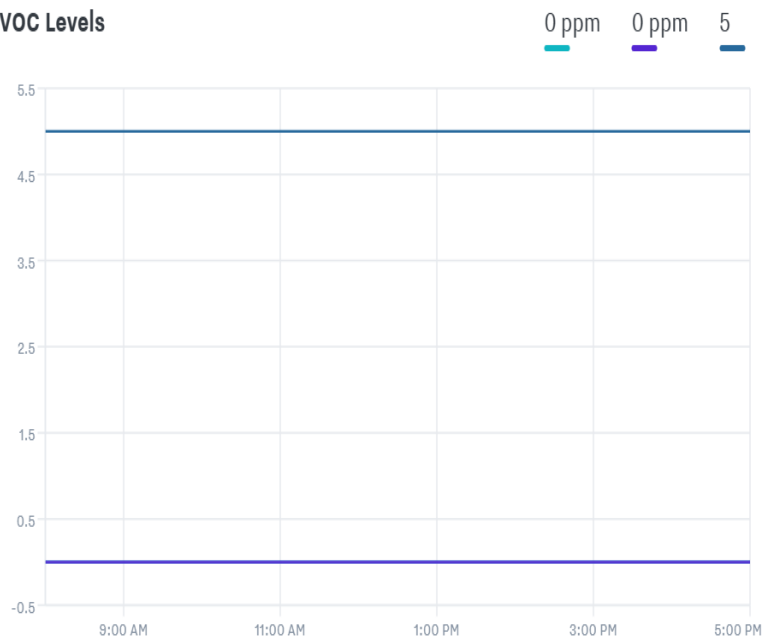

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/25/2024 8:00	3/25/2024 8:10	0.150	0.001	5	0
DW 2024	3/25/2024 8:10	3/25/2024 8:20	0.150	0.001	5	0
DW 2024	3/25/2024 8:20	3/25/2024 8:30	0.150	0.001	5	0.002
DW 2024	3/25/2024 8:30	3/25/2024 8:40	0.150	0.002	5	0.005
DW 2024	3/25/2024 8:40	3/25/2024 8:50	0.150	0.002	5	0.008
DW 2024	3/25/2024 8:50	3/25/2024 9:00	0.150	0.002	5	0.012
DW 2024	3/25/2024 9:00	3/25/2024 9:10	0.150	0.003	5	0.016
DW 2024	3/25/2024 9:10	3/25/2024 9:20	0.150	0.003	5	0.02
DW 2024	3/25/2024 9:20	3/25/2024 9:30	0.150	0.003	5	0.024
DW 2024	3/25/2024 9:30	3/25/2024 9:40	0.150	0.004	5	0.028
DW 2024	3/25/2024 9:40	3/25/2024 9:50	0.150	0.004	5	0.032
DW 2024	3/25/2024 9:50	3/25/2024 10:00	0.150	0.004	5	0.037
DW 2024	3/25/2024 10:00	3/25/2024 10:10	0.150	0.005	5	0.041
DW 2024	3/25/2024 10:10	3/25/2024 10:20	0.150	0.005	5	0.045
DW 2024	3/25/2024 10:20	3/25/2024 10:30	0.150	0.006	5	0.05
DW 2024	3/25/2024 10:30	3/25/2024 10:40	0.150	0.006	5	0.054
DW 2024	3/25/2024 10:40	3/25/2024 10:50	0.150	0.006	5	0.058
DW 2024	3/25/2024 10:50	3/25/2024 11:00	0.150	0.007	5	0.062
DW 2024	3/25/2024 11:00	3/25/2024 11:10	0.150	0.007	5	0.067
DW 2024	3/25/2024 11:10	3/25/2024 11:20	0.150	0.007	5	0.071
DW 2024	3/25/2024 11:20	3/25/2024 11:30	0.150	0.008	5	0.075
DW 2024	3/25/2024 11:30	3/25/2024 11:40	0.150	0.008	5	0.079
DW 2024	3/25/2024 11:40	3/25/2024 11:50	0.150	0.008	5	0.083
DW 2024	3/25/2024 11:50	3/25/2024 12:00	0.150	0.009	5	0.088
DW 2024	3/25/2024 12:00	3/25/2024 12:10	0.150	0.009	5	0.092
DW 2024	3/25/2024 12:10	3/25/2024 12:20	0.150	0.009	5	0.096
DW 2024	3/25/2024 12:20	3/25/2024 12:30	0.150	0.009	5	0.1
DW 2024	3/25/2024 12:30	3/25/2024 12:40	0.150	0.01	5	0.103
DW 2024	3/25/2024 12:40	3/25/2024 12:50	0.150	0.01	5	0.107
DW 2024	3/25/2024 12:50	3/25/2024 13:00	0.150	0.01	5	0.111
DW 2024	3/25/2024 13:00	3/25/2024 13:10	0.150	0.01	5	0.114
DW 2024	3/25/2024 13:10	3/25/2024 13:20	0.150	0.011	5	0.118
DW 2024	3/25/2024 13:20	3/25/2024 13:30	0.150	0.011	5	0.121
DW 2024	3/25/2024 13:30	3/25/2024 13:40	0.150	0.011	5	0.124
DW 2024	3/25/2024 13:40	3/25/2024 13:50	0.150	0.012	5	0.127
DW 2024	3/25/2024 13:50	3/25/2024 14:00	0.150	0.012	5	0.13
DW 2024	3/25/2024 14:00	3/25/2024 14:10	0.150	0.012	5	0.133
DW 2024	3/25/2024 14:10	3/25/2024 14:20	0.150	0.012	5	0.136
DW 2024	3/25/2024 14:20	3/25/2024 14:30	0.150	0.013	5	0.14
DW 2024	3/25/2024 14:30	3/25/2024 14:40	0.150	0.013	5	0.143
DW 2024	3/25/2024 14:40	3/25/2024 14:50	0.150	0.013	5	0.146
DW 2024	3/25/2024 14:50	3/25/2024 15:00	0.150	0.013	5	0.148
DW 2024	3/25/2024 15:00	3/25/2024 15:10	0.150	0.014	5	0.15
DW 2024	3/25/2024 15:10	3/25/2024 15:20	0.150	0.014	5	0.152
DW 2024	3/25/2024 15:20	3/25/2024 15:30	0.150	0.014	5	0.154
DW 2024	3/25/2024 15:30	3/25/2024 15:40	0.150	0.014	5	0.156
DW 2024	3/25/2024 15:40	3/25/2024 15:50	0.150	0.015	5	0.158
DW 2024	3/25/2024 15:50	3/25/2024 16:00	0.150	0.015	5	0.161
DW 2024	3/25/2024 16:00	3/25/2024 16:10	0.150	0.015	5	0.163
DW 2024	3/25/2024 16:10	3/25/2024 16:20	0.150	0.015	5	0.167
DW 2024	3/25/2024 16:20	3/25/2024 16:30	0.150	0.015	5	0.17
DW 2024	3/25/2024 16:30	3/25/2024 16:40	0.150	0.015	5	0.174
DW 2024	3/25/2024 16:40	3/25/2024 16:50	0.150	0.015	5	0.178
DW 2024	3/25/2024 16:50	3/25/2024 17:00	0.150	0.015	5	0.182
DW 2024	3/25/2024 17:00	3/25/2024 17:10	0.150	0.015	5	0.186
DW 2024	3/25/2024 17:10	3/25/2024 17:20	0.150	0.015	5	0.189
DW 2024	3/25/2024 17:20	3/25/2024 17:30	0.150	0.015	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/25/2024 8:00	3/25/2024 8:10	0.150	0.001	5	0
UW 2024	3/25/2024 8:10	3/25/2024 8:20	0.150	0.002	5	0
UW 2024	3/25/2024 8:20	3/25/2024 8:30	0.150	0.002	5	0
UW 2024	3/25/2024 8:30	3/25/2024 8:40	0.150	0.002	5	0
UW 2024	3/25/2024 8:40	3/25/2024 8:50	0.150	0.003	5	0
UW 2024	3/25/2024 8:50	3/25/2024 9:00	0.150	0.003	5	0
UW 2024	3/25/2024 9:00	3/25/2024 9:10	0.150	0.004	5	0
UW 2024	3/25/2024 9:10	3/25/2024 9:20	0.150	0.004	5	0
UW 2024	3/25/2024 9:20	3/25/2024 9:30	0.150	0.004	5	0
UW 2024	3/25/2024 9:30	3/25/2024 9:40	0.150	0.005	5	0
UW 2024	3/25/2024 9:40	3/25/2024 9:50	0.150	0.006	5	0
UW 2024	3/25/2024 9:50	3/25/2024 10:00	0.150	0.006	5	0
UW 2024	3/25/2024 10:00	3/25/2024 10:10	0.150	0.006	5	0
UW 2024	3/25/2024 10:10	3/25/2024 10:20	0.150	0.007	5	0
UW 2024	3/25/2024 10:20	3/25/2024 10:30	0.150	0.007	5	0
UW 2024	3/25/2024 10:30	3/25/2024 10:40	0.150	0.008	5	0
UW 2024	3/25/2024 10:40	3/25/2024 10:50	0.150	0.009	5	0
UW 2024	3/25/2024 10:50	3/25/2024 11:00	0.150	0.009	5	0
UW 2024	3/25/2024 11:00	3/25/2024 11:10	0.150	0.009	5	0
UW 2024	3/25/2024 11:10	3/25/2024 11:20	0.150	0.01	5	0
UW 2024	3/25/2024 11:20	3/25/2024 11:30	0.150	0.01	5	0
UW 2024	3/25/2024 11:30	3/25/2024 11:40	0.150	0.011	5	0
UW 2024	3/25/2024 11:40	3/25/2024 11:50	0.150	0.012	5	0
UW 2024	3/25/2024 11:50	3/25/2024 12:00	0.150	0.012	5	0
UW 2024	3/25/2024 12:00	3/25/2024 12:10	0.150	0.012	5	0
UW 2024	3/25/2024 12:10	3/25/2024 12:20	0.150	0.013	5	0
UW 2024	3/25/2024 12:20	3/25/2024 12:30	0.150	0.013	5	0
UW 2024	3/25/2024 12:30	3/25/2024 12:40	0.150	0.014	5	0
UW 2024	3/25/2024 12:40	3/25/2024 12:50	0.150	0.014	5	0
UW 2024	3/25/2024 12:50	3/25/2024 13:00	0.150	0.014	5	0
UW 2024	3/25/2024 13:00	3/25/2024 13:10	0.150	0.015	5	0
UW 2024	3/25/2024 13:10	3/25/2024 13:20	0.150	0.015	5	0
UW 2024	3/25/2024 13:20	3/25/2024 13:30	0.150	0.015	5	0
UW 2024	3/25/2024 13:30	3/25/2024 13:40	0.150	0.016	5	0
UW 2024	3/25/2024 13:40	3/25/2024 13:50	0.150	0.017	5	0
UW 2024	3/25/2024 13:50	3/25/2024 14:00	0.150	0.017	5	0
UW 2024	3/25/2024 14:00	3/25/2024 14:10	0.150	0.017	5	0
UW 2024	3/25/2024 14:10	3/25/2024 14:20	0.150	0.018	5	0
UW 2024	3/25/2024 14:20	3/25/2024 14:30	0.150	0.018	5	0
UW 2024	3/25/2024 14:30	3/25/2024 14:40	0.150	0.019	5	0
UW 2024	3/25/2024 14:40	3/25/2024 14:50	0.150	0.019	5	0
UW 2024	3/25/2024 14:50	3/25/2024 15:00	0.150	0.019	5	0
UW 2024	3/25/2024 15:00	3/25/2024 15:10	0.150	0.02	5	0
UW 2024	3/25/2024 15:10	3/25/2024 15:20	0.150	0.021	5	0
UW 2024	3/25/2024 15:20	3/25/2024 15:30	0.150	0.021	5	0
UW 2024	3/25/2024 15:30	3/25/2024 15:40	0.150	0.021	5	0
UW 2024	3/25/2024 15:40	3/25/2024 15:50	0.150	0.022	5	0
UW 2024	3/25/2024 15:50	3/25/2024 16:00	0.150	0.022	5	0
UW 2024	3/25/2024 16:00	3/25/2024 16:10	0.150	0.022	5	0
UW 2024	3/25/2024 16:10	3/25/2024 16:20	0.150	0.022	5	0
UW 2024	3/25/2024 16:20	3/25/2024 16:30	0.150	0.022	5	0
UW 2024	3/25/2024 16:30	3/25/2024 16:40	0.150	0.022	5	0
UW 2024	3/25/2024 16:40	3/25/2024 16:50	0.150	0.022	5	0
UW 2024	3/25/2024 16:50	3/25/2024 17:00	0.150	0.022	5	0
UW 2024	3/25/2024 17:00	3/25/2024 17:10	0.150	0.022	5	0
UW 2024	3/25/2024 17:10	3/25/2024 17:20	0.150	0.022	5	0
UW 2024	3/25/2024 17:20	3/25/2024 17:30	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/25/2024 8:00	3/25/2024 8:10	0.150	0	5	0
HS South	3/25/2024 8:10	3/25/2024 8:20	0.150	0.001	5	0
HS South	3/25/2024 8:20	3/25/2024 8:30	0.150	0.001	5	0
HS South	3/25/2024 8:30	3/25/2024 8:40	0.150	0.001	5	0
HS South	3/25/2024 8:40	3/25/2024 8:50	0.150	0.002	5	0
HS South	3/25/2024 8:50	3/25/2024 9:00	0.150	0.002	5	0
HS South	3/25/2024 9:00	3/25/2024 9:10	0.150	0.002	5	0
HS South	3/25/2024 9:10	3/25/2024 9:20	0.150	0.002	5	0
HS South	3/25/2024 9:20	3/25/2024 9:30	0.150	0.002	5	0
HS South	3/25/2024 9:30	3/25/2024 9:40	0.150	0.003	5	0
HS South	3/25/2024 9:40	3/25/2024 9:50	0.150	0.003	5	0
HS South	3/25/2024 9:50	3/25/2024 10:00	0.150	0.003	5	0
HS South	3/25/2024 10:00	3/25/2024 10:10	0.150	0.003	5	0
HS South	3/25/2024 10:10	3/25/2024 10:20	0.150	0.004	5	0
HS South	3/25/2024 10:20	3/25/2024 10:30	0.150	0.004	5	0
HS South	3/25/2024 10:30	3/25/2024 10:40	0.150	0.004	5	0
HS South	3/25/2024 10:40	3/25/2024 10:50	0.150	0.004	5	0
HS South	3/25/2024 10:50	3/25/2024 11:00	0.150	0.004	5	0
HS South	3/25/2024 11:00	3/25/2024 11:10	0.150	0.004	5	0
HS South	3/25/2024 11:10	3/25/2024 11:20	0.150	0.005	5	0
HS South	3/25/2024 11:20	3/25/2024 11:30	0.150	0.005	5	0
HS South	3/25/2024 11:30	3/25/2024 11:40	0.150	0.005	5	0
HS South	3/25/2024 11:40	3/25/2024 11:50	0.150	0.005	5	0
HS South	3/25/2024 11:50	3/25/2024 12:00	0.150	0.005	5	0
HS South	3/25/2024 12:00	3/25/2024 12:10	0.150	0.005	5	0
HS South	3/25/2024 12:10	3/25/2024 12:20	0.150	0.006	5	0
HS South	3/25/2024 12:20	3/25/2024 12:30	0.150	0.006	5	0
HS South	3/25/2024 12:30	3/25/2024 12:40	0.150	0.006	5	0
HS South	3/25/2024 12:40	3/25/2024 12:50	0.150	0.006	5	0
HS South	3/25/2024 12:50	3/25/2024 13:00	0.150	0.006	5	0
HS South	3/25/2024 13:00	3/25/2024 13:10	0.150	0.006	5	0
HS South	3/25/2024 13:10	3/25/2024 13:20	0.150	0.006	5	0
HS South	3/25/2024 13:20	3/25/2024 13:30	0.150	0.006	5	0
HS South	3/25/2024 13:30	3/25/2024 13:40	0.150	0.007	5	0
HS South	3/25/2024 13:40	3/25/2024 13:50	0.150	0.007	5	0
HS South	3/25/2024 13:50	3/25/2024 14:00	0.150	0.007	5	0
HS South	3/25/2024 14:00	3/25/2024 14:10	0.150	0.007	5	0
HS South	3/25/2024 14:10	3/25/2024 14:20	0.150	0.007	5	0
HS South	3/25/2024 14:20	3/25/2024 14:30	0.150	0.007	5	0
HS South	3/25/2024 14:30	3/25/2024 14:40	0.150	0.007	5	0
HS South	3/25/2024 14:40	3/25/2024 14:50	0.150	0.007	5	0
HS South	3/25/2024 14:50	3/25/2024 15:00	0.150	0.007	5	0
HS South	3/25/2024 15:00	3/25/2024 15:10	0.150	0.007	5	0
HS South	3/25/2024 15:10	3/25/2024 15:20	0.150	0.007	5	0
HS South	3/25/2024 15:20	3/25/2024 15:30	0.150	0.007	5	0
HS South	3/25/2024 15:30	3/25/2024 15:40	0.150	0.008	5	0
HS South	3/25/2024 15:40	3/25/2024 15:50	0.150	0.008	5	0
HS South	3/25/2024 15:50	3/25/2024 16:00	0.150	0.008	5	0
HS South	3/25/2024 16:00	3/25/2024 16:10	0.150	0.008	5	0
HS South	3/25/2024 16:10	3/25/2024 16:20	0.150	0.008	5	0
HS South	3/25/2024 16:20	3/25/2024 16:30	0.150	0.008	5	0
HS South	3/25/2024 16:30	3/25/2024 16:40	0.150	0.008	5	0
HS South	3/25/2024 16:40	3/25/2024 16:50	0.150	0.008	5	0
HS South	3/25/2024 16:50	3/25/2024 17:00	0.150	0.008	5	0
HS South	3/25/2024 17:00	3/25/2024 17:10	0.150	0.008	5	0
HS South	3/25/2024 17:10	3/25/2024 17:20	0.150	0.008	5	0
HS South	3/25/2024 17:20	3/25/2024 17:30	0.150	0.008	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/25/2024 8:00	3/25/2024 8:10	0.150	0	5	0
PER1 2024	3/25/2024 8:10	3/25/2024 8:20	0.150	0.002	5	0
PER1 2024	3/25/2024 8:20	3/25/2024 8:30	0.150	0.003	5	0
PER1 2024	3/25/2024 8:30	3/25/2024 8:40	0.150	0.003	5	0
PER1 2024	3/25/2024 8:40	3/25/2024 8:50	0.150	0.004	5	0
PER1 2024	3/25/2024 8:50	3/25/2024 9:00	0.150	0.004	5	0
PER1 2024	3/25/2024 9:00	3/25/2024 9:10	0.150	0.005	5	0
PER1 2024	3/25/2024 9:10	3/25/2024 9:20	0.150	0.006	5	0
PER1 2024	3/25/2024 9:20	3/25/2024 9:30	0.150	0.006	5	0
PER1 2024	3/25/2024 9:30	3/25/2024 9:40	0.150	0.007	5	0
PER1 2024	3/25/2024 9:40	3/25/2024 9:50	0.150	0.009	5	0
PER1 2024	3/25/2024 9:50	3/25/2024 10:00	0.150	0.01	5	0
PER1 2024	3/25/2024 10:00	3/25/2024 10:10	0.150	0.011	5	0
PER1 2024	3/25/2024 10:10	3/25/2024 10:20	0.150	0.012	5	0
PER1 2024	3/25/2024 10:20	3/25/2024 10:30	0.150	0.013	5	0
PER1 2024	3/25/2024 10:30	3/25/2024 10:40	0.150	0.014	5	0
PER1 2024	3/25/2024 10:40	3/25/2024 10:50	0.150	0.014	5	0
PER1 2024	3/25/2024 10:50	3/25/2024 11:00	0.150	0.015	5	0
PER1 2024	3/25/2024 11:00	3/25/2024 11:10	0.150	0.016	5	0
PER1 2024	3/25/2024 11:10	3/25/2024 11:20	0.150	0.017	5	0
PER1 2024	3/25/2024 11:20	3/25/2024 11:30	0.150	0.017	5	0
PER1 2024	3/25/2024 11:30	3/25/2024 11:40	0.150	0.018	5	0
PER1 2024	3/25/2024 11:40	3/25/2024 11:50	0.150	0.019	5	0
PER1 2024	3/25/2024 11:50	3/25/2024 12:00	0.150	0.019	5	0
PER1 2024	3/25/2024 12:00	3/25/2024 12:10	0.150	0.021	5	0
PER1 2024	3/25/2024 12:10	3/25/2024 12:20	0.150	0.022	5	0
PER1 2024	3/25/2024 12:20	3/25/2024 12:30	0.150	0.023	5	0
PER1 2024	3/25/2024 12:30	3/25/2024 12:40	0.150	0.024	5	0
PER1 2024	3/25/2024 12:40	3/25/2024 12:50	0.150	0.024	5	0
PER1 2024	3/25/2024 12:50	3/25/2024 13:00	0.150	0.024	5	0
PER1 2024	3/25/2024 13:00	3/25/2024 13:10	0.150	0.026	5	0
PER1 2024	3/25/2024 13:10	3/25/2024 13:20	0.150	0.026	5	0
PER1 2024	3/25/2024 13:20	3/25/2024 13:30	0.150	0.026	5	0
PER1 2024	3/25/2024 13:30	3/25/2024 13:40	0.150	0.027	5	0
PER1 2024	3/25/2024 13:40	3/25/2024 13:50	0.150	0.027	5	0
PER1 2024	3/25/2024 13:50	3/25/2024 14:00	0.150	0.028	5	0
PER1 2024	3/25/2024 14:00	3/25/2024 14:10	0.150	0.029	5	0
PER1 2024	3/25/2024 14:10	3/25/2024 14:20	0.150	0.03	5	0
PER1 2024	3/25/2024 14:20	3/25/2024 14:30	0.150	0.031	5	0
PER1 2024	3/25/2024 14:30	3/25/2024 14:40	0.150	0.031	5	0
PER1 2024	3/25/2024 14:40	3/25/2024 14:50	0.150	0.034	5	0
PER1 2024	3/25/2024 14:50	3/25/2024 15:00	0.150	0.035	5	0
PER1 2024	3/25/2024 15:00	3/25/2024 15:10	0.150	0.036	5	0
PER1 2024	3/25/2024 15:10	3/25/2024 15:20	0.150	0.037	5	0
PER1 2024	3/25/2024 15:20	3/25/2024 15:30	0.150	0.038	5	0
PER1 2024	3/25/2024 15:30	3/25/2024 15:40	0.150	0.039	5	0
PER1 2024	3/25/2024 15:40	3/25/2024 15:50	0.150	0.039	5	0
PER1 2024	3/25/2024 15:50	3/25/2024 16:00	0.150	0.04	5	0
PER1 2024	3/25/2024 16:00	3/25/2024 16:10	0.150	0.04	5	0
PER1 2024	3/25/2024 16:10	3/25/2024 16:20	0.150	0.04	5	0
PER1 2024	3/25/2024 16:20	3/25/2024 16:30	0.150	0.04	5	0
PER1 2024	3/25/2024 16:30	3/25/2024 16:40	0.150	0.04	5	0
PER1 2024	3/25/2024 16:40	3/25/2024 16:50	0.150	0.04	5	0
PER1 2024	3/25/2024 16:50	3/25/2024 17:00	0.150	0.04	5	0
PER1 2024	3/25/2024 17:00	3/25/2024 17:10	0.150	0.04	5	0
PER1 2024	3/25/2024 17:10	3/25/2024 17:20	0.150	0.04	5	0
PER1 2024	3/25/2024 17:20	3/25/2024 17:30	0.150	0.04	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/25/2024 8:10	3/25/2024 8:20	0.150	0.001	5	0
PER2 2024	3/25/2024 8:20	3/25/2024 8:30	0.150	0.001	5	0
PER2 2024	3/25/2024 8:30	3/25/2024 8:40	0.150	0.001	5	0
PER2 2024	3/25/2024 8:40	3/25/2024 8:50	0.150	0.001	5	0
PER2 2024	3/25/2024 8:50	3/25/2024 9:00	0.150	0.001	5	0
PER2 2024	3/25/2024 9:00	3/25/2024 9:10	0.150	0.002	5	0
PER2 2024	3/25/2024 9:10	3/25/2024 9:20	0.150	0.002	5	0
PER2 2024	3/25/2024 9:20	3/25/2024 9:30	0.150	0.002	5	0
PER2 2024	3/25/2024 9:30	3/25/2024 9:40	0.150	0.002	5	0
PER2 2024	3/25/2024 9:40	3/25/2024 9:50	0.150	0.003	5	0
PER2 2024	3/25/2024 9:50	3/25/2024 10:00	0.150	0.003	5	0
PER2 2024	3/25/2024 10:00	3/25/2024 10:10	0.150	0.003	5	0
PER2 2024	3/25/2024 10:10	3/25/2024 10:20	0.150	0.003	5	0
PER2 2024	3/25/2024 10:20	3/25/2024 10:30	0.150	0.004	5	0
PER2 2024	3/25/2024 10:30	3/25/2024 10:40	0.150	0.004	5	0
PER2 2024	3/25/2024 10:40	3/25/2024 10:50	0.150	0.004	5	0
PER2 2024	3/25/2024 10:50	3/25/2024 11:00	0.150	0.004	5	0
PER2 2024	3/25/2024 11:00	3/25/2024 11:10	0.150	0.005	5	0
PER2 2024	3/25/2024 11:10	3/25/2024 11:20	0.150	0.005	5	0
PER2 2024	3/25/2024 11:20	3/25/2024 11:30	0.150	0.005	5	0
PER2 2024	3/25/2024 11:30	3/25/2024 11:40	0.150	0.005	5	0
PER2 2024	3/25/2024 11:40	3/25/2024 11:50	0.150	0.005	5	0
PER2 2024	3/25/2024 11:50	3/25/2024 12:00	0.150	0.006	5	0
PER2 2024	3/25/2024 12:00	3/25/2024 12:10	0.150	0.006	5	0
PER2 2024	3/25/2024 12:10	3/25/2024 12:20	0.150	0.006	5	0
PER2 2024	3/25/2024 12:20	3/25/2024 12:30	0.150	0.006	5	0
PER2 2024	3/25/2024 12:30	3/25/2024 12:40	0.150	0.006	5	0
PER2 2024	3/25/2024 12:40	3/25/2024 12:50	0.150	0.007	5	0
PER2 2024	3/25/2024 12:50	3/25/2024 13:00	0.150	0.007	5	0
PER2 2024	3/25/2024 13:00	3/25/2024 13:10	0.150	0.007	5	0
PER2 2024	3/25/2024 13:10	3/25/2024 13:20	0.150	0.007	5	0
PER2 2024	3/25/2024 13:20	3/25/2024 13:30	0.150	0.007	5	0
PER2 2024	3/25/2024 13:30	3/25/2024 13:40	0.150	0.008	5	0
PER2 2024	3/25/2024 13:40	3/25/2024 13:50	0.150	0.008	5	0
PER2 2024	3/25/2024 13:50	3/25/2024 14:00	0.150	0.008	5	0
PER2 2024	3/25/2024 14:00	3/25/2024 14:10	0.150	0.008	5	0
PER2 2024	3/25/2024 14:10	3/25/2024 14:20	0.150	0.008	5	0
PER2 2024	3/25/2024 14:20	3/25/2024 14:30	0.150	0.009	5	0
PER2 2024	3/25/2024 14:30	3/25/2024 14:40	0.150	0.009	5	0
PER2 2024	3/25/2024 14:40	3/25/2024 14:50	0.150	0.009	5	0
PER2 2024	3/25/2024 14:50	3/25/2024 15:00	0.150	0.009	5	0
PER2 2024	3/25/2024 15:00	3/25/2024 15:10	0.150	0.01	5	0
PER2 2024	3/25/2024 15:10	3/25/2024 15:20	0.150	0.01	5	0
PER2 2024	3/25/2024 15:20	3/25/2024 15:30	0.150	0.01	5	0
PER2 2024	3/25/2024 15:30	3/25/2024 15:40	0.150	0.01	5	0
PER2 2024	3/25/2024 15:40	3/25/2024 15:50	0.150	0.01	5	0
PER2 2024	3/25/2024 15:50	3/25/2024 16:00	0.150	0.01	5	0
PER2 2024	3/25/2024 16:00	3/25/2024 16:10	0.150	0.01	5	0
PER2 2024	3/25/2024 16:10	3/25/2024 16:20	0.150	0.01	5	0
PER2 2024	3/25/2024 16:20	3/25/2024 16:30	0.150	0.01	5	0
PER2 2024	3/25/2024 16:30	3/25/2024 16:40	0.150	0.01	5	0
PER2 2024	3/25/2024 16:40	3/25/2024 16:50	0.150	0.01	5	0
PER2 2024	3/25/2024 16:50	3/25/2024 17:00	0.150	0.01	5	0
PER2 2024	3/25/2024 17:00	3/25/2024 17:10	0.150	0.01	5	0
PER2 2024	3/25/2024 17:10	3/25/2024 17:20	0.150	0.01	5	0
PER2 2024	3/25/2024 17:20	3/25/2024 17:30	0.150	0.01	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/26/2024

Weather: 40 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation and foundation development. 2) ECD was not on-Site and no remedial excavation work was completed. 3) Alba exported 10 loads (~200 CY) of material from WC-25 for offsite disposal at the Harmony Foul Rift facility. 4) Around 430PM, the dewatering effluent was observed to be highly turbid. The system was temporarily shut down while maintenance was completed to remedy the issue. The DEC PM was notified via voicemail. See below for more information.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP tables and graphs are included below.	
Problems Encountered: High turbidity in the dewatering effluent was caused by an influx of turbid water from a portion of the building footprint excavation. While the system was turned off, the bag filters were changed and the system was flushed. Additional filtration was installed in the dewatering well where the water was highly turbid in the excavation.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	200	0	0	0	0
Total:(CY)	4485	0	7285	1520	2620

Site Layout Map and Excavation Figures

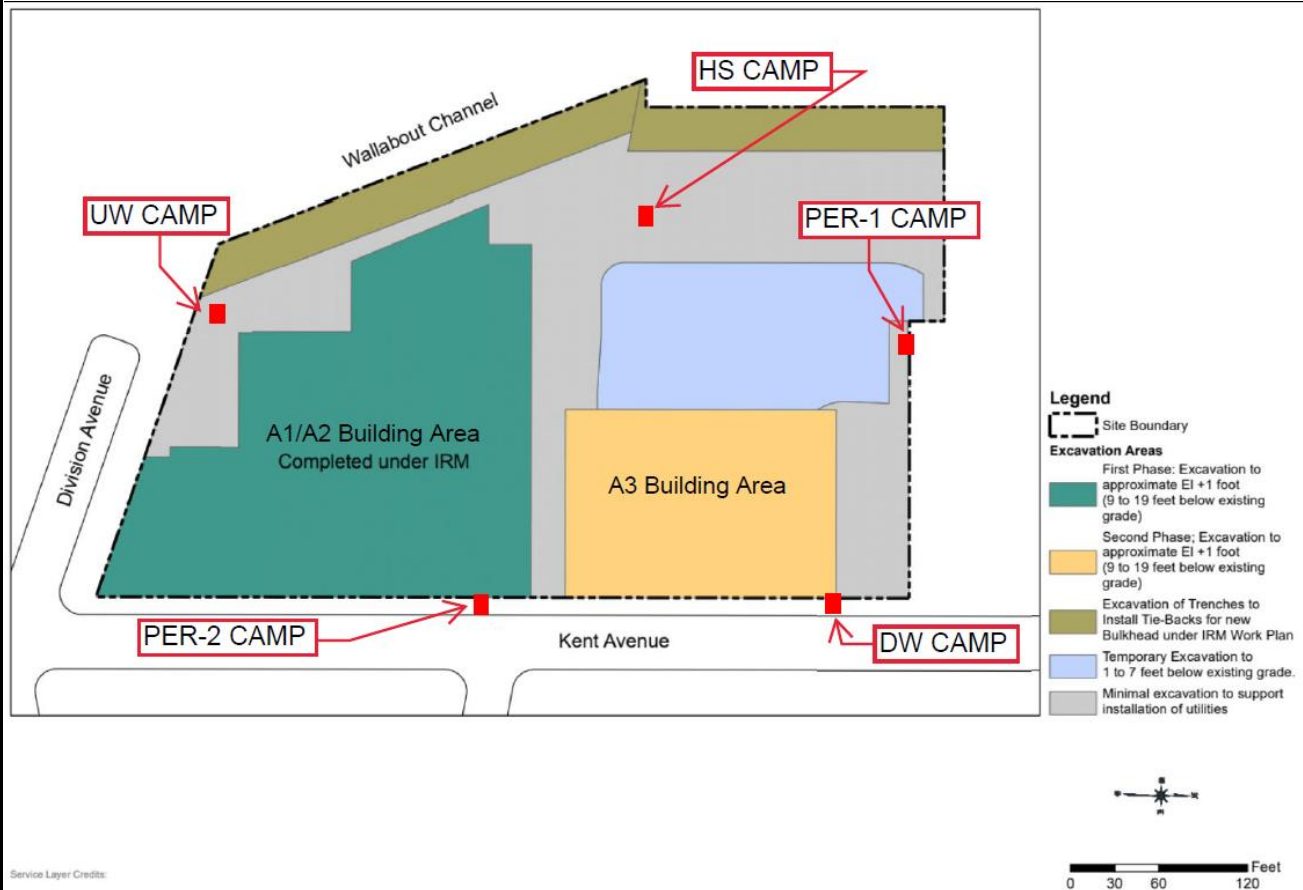

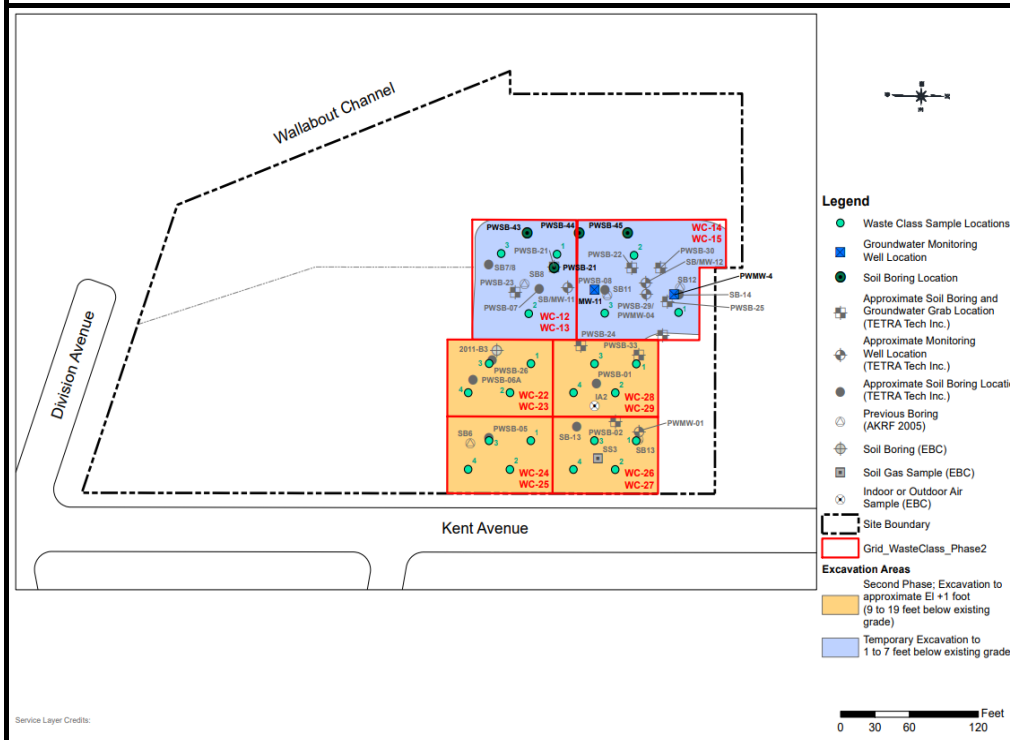
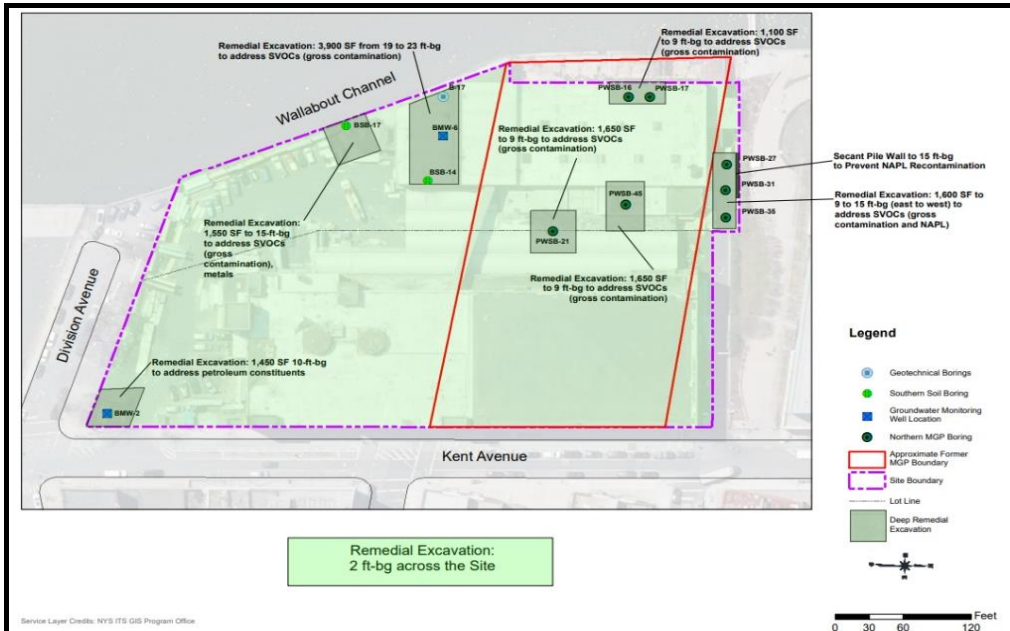


Photo 1:
View of Site conditions
and activities facing
north.



Photo 2:
View of soil excavation,
Site activities ..

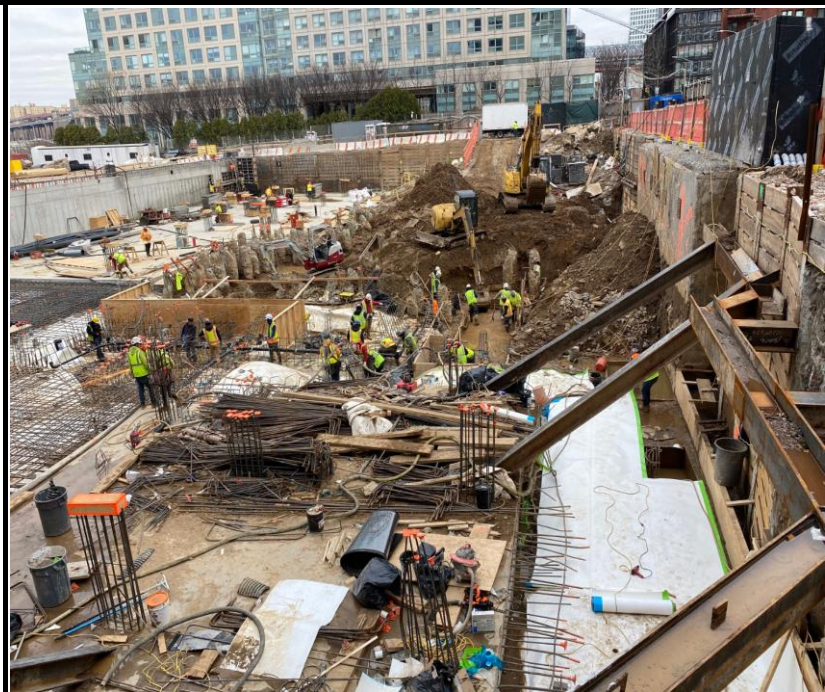
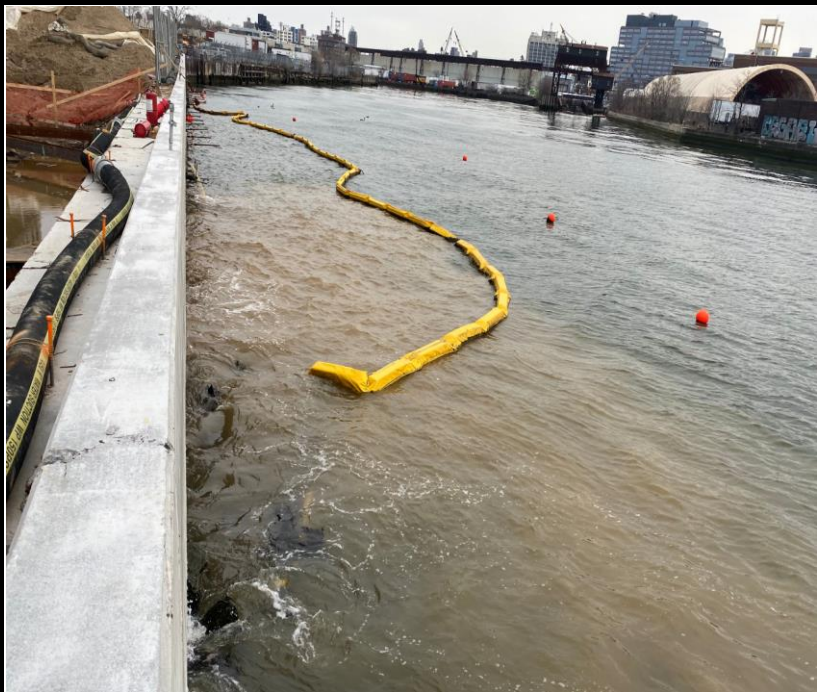


Photo 3:
View of soil
excavation and truck
loading for off-site
soil disposal.

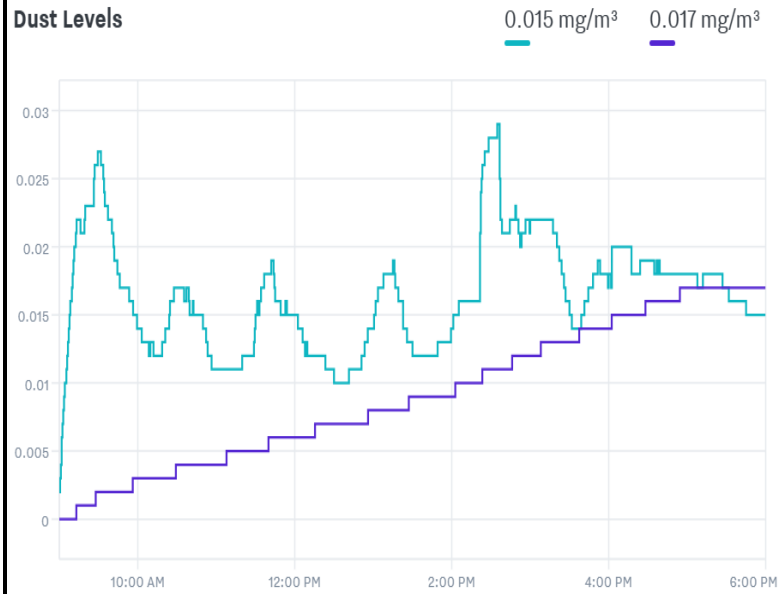


Photo 4:
View of the turbid
effluent immediately
prior to turning off
the system for
maintenance.




CAMP:
Downwind
Particulates

Dust Levels



CAMP:
Downwind VOCs


VOC Levels

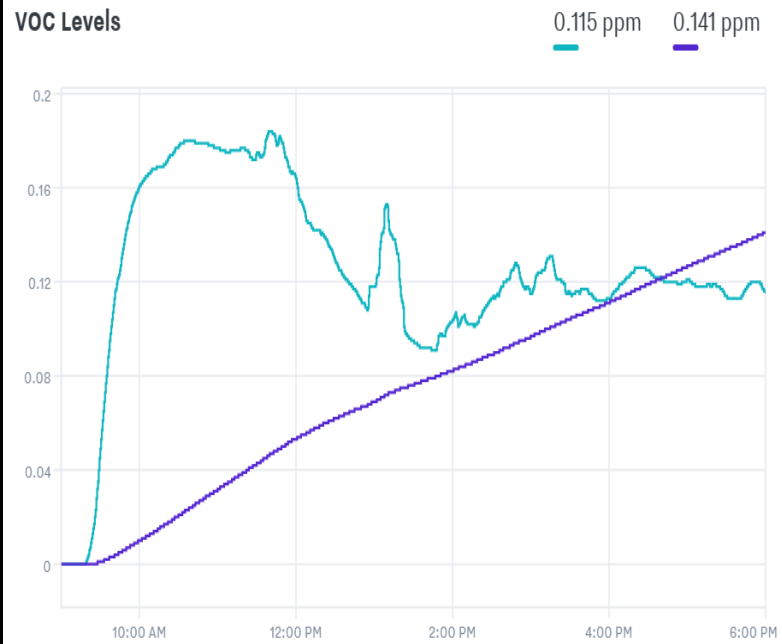

CAMP:
Upwind Particulates

Dust Levels


0.026 mg/m³ 0.025 mg/m³ 0.15

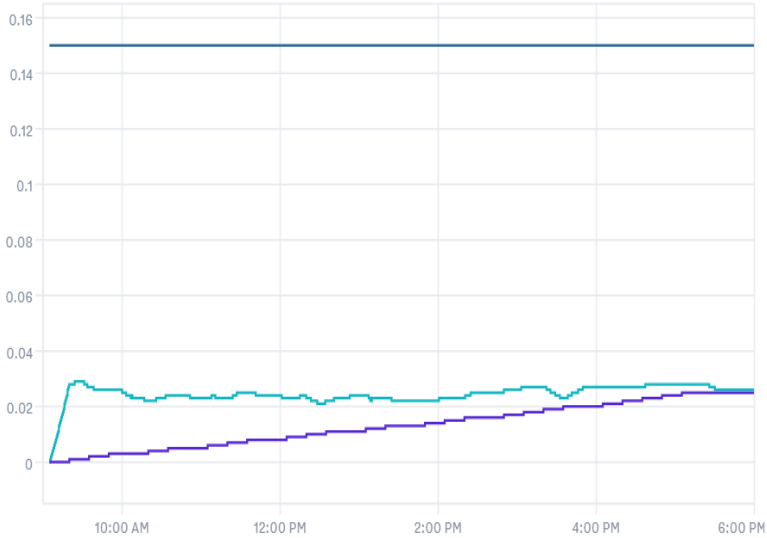

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

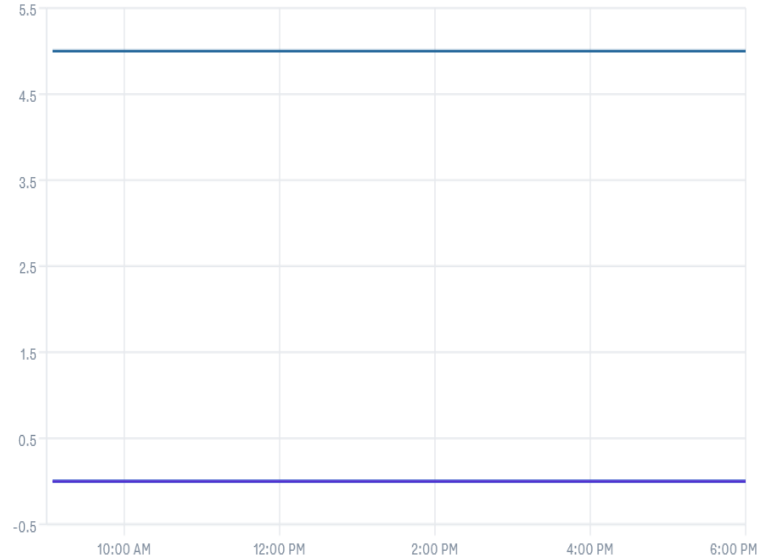

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/26/2024 9:10	3/26/2024 9:20	0.150	0.001	5	0
DW 2024	3/26/2024 9:20	3/26/2024 9:30	0.150	0.002	5	0.001
DW 2024	3/26/2024 9:30	3/26/2024 9:40	0.150	0.002	5	0.003
DW 2024	3/26/2024 9:40	3/26/2024 9:50	0.150	0.002	5	0.007
DW 2024	3/26/2024 9:50	3/26/2024 10:00	0.150	0.003	5	0.01
DW 2024	3/26/2024 10:00	3/26/2024 10:10	0.150	0.003	5	0.013
DW 2024	3/26/2024 10:10	3/26/2024 10:20	0.150	0.003	5	0.017
DW 2024	3/26/2024 10:20	3/26/2024 10:30	0.150	0.004	5	0.021
DW 2024	3/26/2024 10:30	3/26/2024 10:40	0.150	0.004	5	0.024
DW 2024	3/26/2024 10:40	3/26/2024 10:50	0.150	0.004	5	0.028
DW 2024	3/26/2024 10:50	3/26/2024 11:00	0.150	0.004	5	0.032
DW 2024	3/26/2024 11:00	3/26/2024 11:10	0.150	0.005	5	0.035
DW 2024	3/26/2024 11:10	3/26/2024 11:20	0.150	0.005	5	0.039
DW 2024	3/26/2024 11:20	3/26/2024 11:30	0.150	0.005	5	0.043
DW 2024	3/26/2024 11:30	3/26/2024 11:40	0.150	0.006	5	0.047
DW 2024	3/26/2024 11:40	3/26/2024 11:50	0.150	0.006	5	0.05
DW 2024	3/26/2024 11:50	3/26/2024 12:00	0.150	0.006	5	0.053
DW 2024	3/26/2024 12:00	3/26/2024 12:10	0.150	0.006	5	0.056
DW 2024	3/26/2024 12:10	3/26/2024 12:20	0.150	0.007	5	0.059
DW 2024	3/26/2024 12:20	3/26/2024 12:30	0.150	0.007	5	0.062
DW 2024	3/26/2024 12:30	3/26/2024 12:40	0.150	0.007	5	0.064
DW 2024	3/26/2024 12:40	3/26/2024 12:50	0.150	0.007	5	0.067
DW 2024	3/26/2024 12:50	3/26/2024 13:00	0.150	0.008	5	0.069
DW 2024	3/26/2024 13:00	3/26/2024 13:10	0.150	0.008	5	0.072
DW 2024	3/26/2024 13:10	3/26/2024 13:20	0.150	0.008	5	0.075
DW 2024	3/26/2024 13:20	3/26/2024 13:30	0.150	0.009	5	0.076
DW 2024	3/26/2024 13:30	3/26/2024 13:40	0.150	0.009	5	0.078
DW 2024	3/26/2024 13:40	3/26/2024 13:50	0.150	0.009	5	0.08
DW 2024	3/26/2024 13:50	3/26/2024 14:00	0.150	0.009	5	0.082
DW 2024	3/26/2024 14:00	3/26/2024 14:10	0.150	0.01	5	0.085
DW 2024	3/26/2024 14:10	3/26/2024 14:20	0.150	0.01	5	0.087
DW 2024	3/26/2024 14:20	3/26/2024 14:30	0.150	0.011	5	0.089
DW 2024	3/26/2024 14:30	3/26/2024 14:40	0.150	0.011	5	0.092
DW 2024	3/26/2024 14:40	3/26/2024 14:50	0.150	0.012	5	0.094
DW 2024	3/26/2024 14:50	3/26/2024 15:00	0.150	0.012	5	0.097
DW 2024	3/26/2024 15:00	3/26/2024 15:10	0.150	0.013	5	0.099
DW 2024	3/26/2024 15:10	3/26/2024 15:20	0.150	0.013	5	0.102
DW 2024	3/26/2024 15:20	3/26/2024 15:30	0.150	0.013	5	0.104
DW 2024	3/26/2024 15:30	3/26/2024 15:40	0.150	0.014	5	0.107
DW 2024	3/26/2024 15:40	3/26/2024 15:50	0.150	0.014	5	0.109
DW 2024	3/26/2024 15:50	3/26/2024 16:00	0.150	0.014	5	0.111
DW 2024	3/26/2024 16:00	3/26/2024 16:10	0.150	0.015	5	0.114
DW 2024	3/26/2024 16:10	3/26/2024 16:20	0.150	0.015	5	0.117
DW 2024	3/26/2024 16:20	3/26/2024 16:30	0.150	0.016	5	0.119
DW 2024	3/26/2024 16:30	3/26/2024 16:40	0.150	0.016	5	0.122
DW 2024	3/26/2024 16:40	3/26/2024 16:50	0.150	0.016	5	0.124
DW 2024	3/26/2024 16:50	3/26/2024 17:00	0.150	0.017	5	0.127
DW 2024	3/26/2024 17:00	3/26/2024 17:10	0.150	0.017	5	0.129
DW 2024	3/26/2024 17:10	3/26/2024 17:20	0.150	0.017	5	0.131
DW 2024	3/26/2024 17:20	3/26/2024 17:30	0.150	0.017	5	0.134
DW 2024	3/26/2024 17:30	3/26/2024 17:40	0.150	0.017	5	0.136
DW 2024	3/26/2024 17:40	3/26/2024 17:50	0.150	0.017	5	0.139
DW 2024	3/26/2024 17:50	3/26/2024 18:00	0.150	0.017	5	0.141

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/26/2024 9:00	3/26/2024 9:10	0.150	0	5	0
UW 2024	3/26/2024 9:10	3/26/2024 9:20	0.150	0.001	5	0
UW 2024	3/26/2024 9:20	3/26/2024 9:30	0.150	0.001	5	0
UW 2024	3/26/2024 9:30	3/26/2024 9:40	0.150	0.002	5	0
UW 2024	3/26/2024 9:40	3/26/2024 9:50	0.150	0.003	5	0
UW 2024	3/26/2024 9:50	3/26/2024 10:00	0.150	0.003	5	0
UW 2024	3/26/2024 10:00	3/26/2024 10:10	0.150	0.003	5	0
UW 2024	3/26/2024 10:10	3/26/2024 10:20	0.150	0.004	5	0
UW 2024	3/26/2024 10:20	3/26/2024 10:30	0.150	0.004	5	0
UW 2024	3/26/2024 10:30	3/26/2024 10:40	0.150	0.005	5	0
UW 2024	3/26/2024 10:40	3/26/2024 10:50	0.150	0.005	5	0
UW 2024	3/26/2024 10:50	3/26/2024 11:00	0.150	0.005	5	0
UW 2024	3/26/2024 11:00	3/26/2024 11:10	0.150	0.006	5	0
UW 2024	3/26/2024 11:10	3/26/2024 11:20	0.150	0.007	5	0
UW 2024	3/26/2024 11:20	3/26/2024 11:30	0.150	0.007	5	0
UW 2024	3/26/2024 11:30	3/26/2024 11:40	0.150	0.008	5	0
UW 2024	3/26/2024 11:40	3/26/2024 11:50	0.150	0.008	5	0
UW 2024	3/26/2024 11:50	3/26/2024 12:00	0.150	0.008	5	0
UW 2024	3/26/2024 12:00	3/26/2024 12:10	0.150	0.009	5	0
UW 2024	3/26/2024 12:10	3/26/2024 12:20	0.150	0.01	5	0
UW 2024	3/26/2024 12:20	3/26/2024 12:30	0.150	0.01	5	0
UW 2024	3/26/2024 12:30	3/26/2024 12:40	0.150	0.011	5	0
UW 2024	3/26/2024 12:40	3/26/2024 12:50	0.150	0.011	5	0
UW 2024	3/26/2024 12:50	3/26/2024 13:00	0.150	0.011	5	0
UW 2024	3/26/2024 13:00	3/26/2024 13:10	0.150	0.012	5	0
UW 2024	3/26/2024 13:10	3/26/2024 13:20	0.150	0.013	5	0
UW 2024	3/26/2024 13:20	3/26/2024 13:30	0.150	0.013	5	0
UW 2024	3/26/2024 13:30	3/26/2024 13:40	0.150	0.013	5	0
UW 2024	3/26/2024 13:40	3/26/2024 13:50	0.150	0.014	5	0
UW 2024	3/26/2024 13:50	3/26/2024 14:00	0.150	0.014	5	0
UW 2024	3/26/2024 14:00	3/26/2024 14:10	0.150	0.015	5	0
UW 2024	3/26/2024 14:10	3/26/2024 14:20	0.150	0.016	5	0
UW 2024	3/26/2024 14:20	3/26/2024 14:30	0.150	0.016	5	0
UW 2024	3/26/2024 14:30	3/26/2024 14:40	0.150	0.016	5	0
UW 2024	3/26/2024 14:40	3/26/2024 14:50	0.150	0.017	5	0
UW 2024	3/26/2024 14:50	3/26/2024 15:00	0.150	0.017	5	0
UW 2024	3/26/2024 15:00	3/26/2024 15:10	0.150	0.018	5	0
UW 2024	3/26/2024 15:10	3/26/2024 15:20	0.150	0.019	5	0
UW 2024	3/26/2024 15:20	3/26/2024 15:30	0.150	0.019	5	0
UW 2024	3/26/2024 15:30	3/26/2024 15:40	0.150	0.02	5	0
UW 2024	3/26/2024 15:40	3/26/2024 15:50	0.150	0.02	5	0
UW 2024	3/26/2024 15:50	3/26/2024 16:00	0.150	0.02	5	0
UW 2024	3/26/2024 16:00	3/26/2024 16:10	0.150	0.021	5	0
UW 2024	3/26/2024 16:10	3/26/2024 16:20	0.150	0.022	5	0
UW 2024	3/26/2024 16:20	3/26/2024 16:30	0.150	0.022	5	0
UW 2024	3/26/2024 16:30	3/26/2024 16:40	0.150	0.023	5	0
UW 2024	3/26/2024 16:40	3/26/2024 16:50	0.150	0.024	5	0
UW 2024	3/26/2024 16:50	3/26/2024 17:00	0.150	0.024	5	0
UW 2024	3/26/2024 17:00	3/26/2024 17:10	0.150	0.025	5	0
UW 2024	3/26/2024 17:10	3/26/2024 17:20	0.150	0.025	5	0
UW 2024	3/26/2024 17:20	3/26/2024 17:30	0.150	0.025	5	0
UW 2024	3/26/2024 17:30	3/26/2024 17:40	0.150	0.025	5	0
UW 2024	3/26/2024 17:40	3/26/2024 17:50	0.150	0.025	5	0
UW 2024	3/26/2024 17:50	3/26/2024 18:00	0.150	0.025	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/26/2024 9:00	3/26/2024 9:10	0.150	0.001	5	0
HS South	3/26/2024 9:10	3/26/2024 9:20	0.150	0.001	5	0
HS South	3/26/2024 9:20	3/26/2024 9:30	0.150	0.001	5	0
HS South	3/26/2024 9:30	3/26/2024 9:40	0.150	0.002	5	0
HS South	3/26/2024 9:40	3/26/2024 9:50	0.150	0.002	5	0
HS South	3/26/2024 9:50	3/26/2024 10:00	0.150	0.002	5	0
HS South	3/26/2024 10:00	3/26/2024 10:10	0.150	0.003	5	0
HS South	3/26/2024 10:10	3/26/2024 10:20	0.150	0.003	5	0
HS South	3/26/2024 10:20	3/26/2024 10:30	0.150	0.003	5	0
HS South	3/26/2024 10:30	3/26/2024 10:40	0.150	0.003	5	0
HS South	3/26/2024 10:40	3/26/2024 10:50	0.150	0.003	5	0
HS South	3/26/2024 10:50	3/26/2024 11:00	0.150	0.003	5	0
HS South	3/26/2024 11:00	3/26/2024 11:10	0.150	0.004	5	0
HS South	3/26/2024 11:10	3/26/2024 11:20	0.150	0.004	5	0
HS South	3/26/2024 11:20	3/26/2024 11:30	0.150	0.004	5	0
HS South	3/26/2024 11:30	3/26/2024 11:40	0.150	0.004	5	0
HS South	3/26/2024 11:40	3/26/2024 11:50	0.150	0.004	5	0
HS South	3/26/2024 11:50	3/26/2024 12:00	0.150	0.004	5	0
HS South	3/26/2024 12:00	3/26/2024 12:10	0.150	0.004	5	0
HS South	3/26/2024 12:10	3/26/2024 12:20	0.150	0.004	5	0
HS South	3/26/2024 12:20	3/26/2024 12:30	0.150	0.005	5	0
HS South	3/26/2024 12:30	3/26/2024 12:40	0.150	0.005	5	0
HS South	3/26/2024 12:40	3/26/2024 12:50	0.150	0.005	5	0
HS South	3/26/2024 12:50	3/26/2024 13:00	0.150	0.005	5	0
HS South	3/26/2024 13:00	3/26/2024 13:10	0.150	0.005	5	0
HS South	3/26/2024 13:10	3/26/2024 13:20	0.150	0.005	5	0
HS South	3/26/2024 13:20	3/26/2024 13:30	0.150	0.005	5	0
HS South	3/26/2024 13:30	3/26/2024 13:40	0.150	0.005	5	0
HS South	3/26/2024 13:40	3/26/2024 13:50	0.150	0.005	5	0
HS South	3/26/2024 13:50	3/26/2024 14:00	0.150	0.005	5	0
HS South	3/26/2024 14:00	3/26/2024 14:10	0.150	0.005	5	0
HS South	3/26/2024 14:10	3/26/2024 14:20	0.150	0.006	5	0
HS South	3/26/2024 14:20	3/26/2024 14:30	0.150	0.006	5	0
HS South	3/26/2024 14:30	3/26/2024 14:40	0.150	0.006	5	0
HS South	3/26/2024 14:40	3/26/2024 14:50	0.150	0.006	5	0
HS South	3/26/2024 14:50	3/26/2024 15:00	0.150	0.006	5	0
HS South	3/26/2024 15:00	3/26/2024 15:10	0.150	0.006	5	0
HS South	3/26/2024 15:10	3/26/2024 15:20	0.150	0.007	5	0
HS South	3/26/2024 15:20	3/26/2024 15:30	0.150	0.007	5	0
HS South	3/26/2024 15:30	3/26/2024 15:40	0.150	0.007	5	0
HS South	3/26/2024 15:40	3/26/2024 15:50	0.150	0.007	5	0
HS South	3/26/2024 15:50	3/26/2024 16:00	0.150	0.007	5	0
HS South	3/26/2024 16:00	3/26/2024 16:10	0.150	0.008	5	0
HS South	3/26/2024 16:10	3/26/2024 16:20	0.150	0.008	5	0
HS South	3/26/2024 16:20	3/26/2024 16:30	0.150	0.008	5	0
HS South	3/26/2024 16:30	3/26/2024 16:40	0.150	0.008	5	0
HS South	3/26/2024 16:40	3/26/2024 16:50	0.150	0.008	5	0
HS South	3/26/2024 16:50	3/26/2024 17:00	0.150	0.008	5	0
HS South	3/26/2024 17:00	3/26/2024 17:10	0.150	0.008	5	0
HS South	3/26/2024 17:10	3/26/2024 17:20	0.150	0.008	5	0
HS South	3/26/2024 17:20	3/26/2024 17:30	0.150	0.008	5	0
HS South	3/26/2024 17:30	3/26/2024 17:40	0.150	0.008	5	0
HS South	3/26/2024 17:40	3/26/2024 17:50	0.150	0.008	5	0
HS South	3/26/2024 17:50	3/26/2024 18:00	0.150	0.008	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/26/2024 9:00	3/26/2024 9:10	0.150	0.002	5	0.001
PER1 2024	3/26/2024 9:10	3/26/2024 9:20	0.150	0.002	5	0.001
PER1 2024	3/26/2024 9:20	3/26/2024 9:30	0.150	0.003	5	0.001
PER1 2024	3/26/2024 9:30	3/26/2024 9:40	0.150	0.004	5	0.001
PER1 2024	3/26/2024 9:40	3/26/2024 9:50	0.150	0.004	5	0.005
PER1 2024	3/26/2024 9:50	3/26/2024 10:00	0.150	0.005	5	0.005
PER1 2024	3/26/2024 10:00	3/26/2024 10:10	0.150	0.006	5	0.005
PER1 2024	3/26/2024 10:10	3/26/2024 10:20	0.150	0.006	5	0.005
PER1 2024	3/26/2024 10:20	3/26/2024 10:30	0.150	0.007	5	0.005
PER1 2024	3/26/2024 10:30	3/26/2024 10:40	0.150	0.008	5	0.005
PER1 2024	3/26/2024 10:40	3/26/2024 10:50	0.150	0.008	5	0.005
PER1 2024	3/26/2024 10:50	3/26/2024 11:00	0.150	0.01	5	0.005
PER1 2024	3/26/2024 11:00	3/26/2024 11:10	0.150	0.011	5	0.005
PER1 2024	3/26/2024 11:10	3/26/2024 11:20	0.150	0.012	5	0.005
PER1 2024	3/26/2024 11:20	3/26/2024 11:30	0.150	0.012	5	0.005
PER1 2024	3/26/2024 11:30	3/26/2024 11:40	0.150	0.013	5	0.005
PER1 2024	3/26/2024 11:40	3/26/2024 11:50	0.150	0.019	5	0.005
PER1 2024	3/26/2024 11:50	3/26/2024 12:00	0.150	0.019	5	0.005
PER1 2024	3/26/2024 12:00	3/26/2024 12:10	0.150	0.02	5	0.005
PER1 2024	3/26/2024 12:10	3/26/2024 12:20	0.150	0.02	5	0.005
PER1 2024	3/26/2024 12:20	3/26/2024 12:30	0.150	0.02	5	0.005
PER1 2024	3/26/2024 12:30	3/26/2024 12:40	0.150	0.021	5	0.005
PER1 2024	3/26/2024 12:40	3/26/2024 12:50	0.150	0.021	5	0.005
PER1 2024	3/26/2024 12:50	3/26/2024 13:00	0.150	0.022	5	0.005
PER1 2024	3/26/2024 13:00	3/26/2024 13:10	0.150	0.022	5	0.005
PER1 2024	3/26/2024 13:10	3/26/2024 13:20	0.150	0.023	5	0.005
PER1 2024	3/26/2024 13:20	3/26/2024 13:30	0.150	0.023	5	0.005
PER1 2024	3/26/2024 13:30	3/26/2024 13:40	0.150	0.024	5	0.005
PER1 2024	3/26/2024 13:40	3/26/2024 13:50	0.150	0.024	5	0.005
PER1 2024	3/26/2024 13:50	3/26/2024 14:00	0.150	0.025	5	0.005
PER1 2024	3/26/2024 14:00	3/26/2024 14:10	0.150	0.025	5	0.005
PER1 2024	3/26/2024 14:10	3/26/2024 14:20	0.150	0.026	5	0.005
PER1 2024	3/26/2024 14:20	3/26/2024 14:30	0.150	0.027	5	0.005
PER1 2024	3/26/2024 14:30	3/26/2024 14:40	0.150	0.027	5	0.005
PER1 2024	3/26/2024 14:40	3/26/2024 14:50	0.150	0.028	5	0.005
PER1 2024	3/26/2024 14:50	3/26/2024 15:00	0.150	0.028	5	0.005
PER1 2024	3/26/2024 15:00	3/26/2024 15:10	0.150	0.029	5	0.005
PER1 2024	3/26/2024 15:10	3/26/2024 15:20	0.150	0.03	5	0.005
PER1 2024	3/26/2024 15:20	3/26/2024 15:30	0.150	0.03	5	0.005
PER1 2024	3/26/2024 15:30	3/26/2024 15:40	0.150	0.031	5	0.007
PER1 2024	3/26/2024 15:40	3/26/2024 15:50	0.150	0.033	5	0.008
PER1 2024	3/26/2024 15:50	3/26/2024 16:00	0.150	0.033	5	0.008
PER1 2024	3/26/2024 16:00	3/26/2024 16:10	0.150	0.034	5	0.008
PER1 2024	3/26/2024 16:10	3/26/2024 16:20	0.150	0.035	5	0.008
PER1 2024	3/26/2024 16:20	3/26/2024 16:30	0.150	0.036	5	0.008
PER1 2024	3/26/2024 16:30	3/26/2024 16:40	0.150	0.036	5	0.008
PER1 2024	3/26/2024 16:40	3/26/2024 16:50	0.150	0.037	5	0.008
PER1 2024	3/26/2024 16:50	3/26/2024 17:00	0.150	0.037	5	0.008
PER1 2024	3/26/2024 17:00	3/26/2024 17:10	0.150	0.037	5	0.008
PER1 2024	3/26/2024 17:10	3/26/2024 17:20	0.150	0.037	5	0.008
PER1 2024	3/26/2024 17:20	3/26/2024 17:30	0.150	0.037	5	0.008
PER1 2024	3/26/2024 17:30	3/26/2024 17:40	0.150	0.037	5	0.008
PER1 2024	3/26/2024 17:40	3/26/2024 17:50	0.150	0.037	5	0.008
PER1 2024	3/26/2024 17:50	3/26/2024 18:00	0.150	0.037	5	0.008

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/26/2024 9:00	3/26/2024 9:10	0.150	0	5	0
PER2 2024	3/26/2024 9:10	3/26/2024 9:20	0.150	0	5	0
PER2 2024	3/26/2024 9:20	3/26/2024 9:30	0.150	0.001	5	0
PER2 2024	3/26/2024 9:30	3/26/2024 9:40	0.150	0.001	5	0
PER2 2024	3/26/2024 9:40	3/26/2024 9:50	0.150	0.001	5	0
PER2 2024	3/26/2024 9:50	3/26/2024 10:00	0.150	0.002	5	0
PER2 2024	3/26/2024 10:00	3/26/2024 10:10	0.150	0.002	5	0
PER2 2024	3/26/2024 10:10	3/26/2024 10:20	0.150	0.002	5	0
PER2 2024	3/26/2024 10:20	3/26/2024 10:30	0.150	0.002	5	0
PER2 2024	3/26/2024 10:30	3/26/2024 10:40	0.150	0.002	5	0
PER2 2024	3/26/2024 10:40	3/26/2024 10:50	0.150	0.003	5	0
PER2 2024	3/26/2024 10:50	3/26/2024 11:00	0.150	0.003	5	0
PER2 2024	3/26/2024 11:00	3/26/2024 11:10	0.150	0.003	5	0
PER2 2024	3/26/2024 11:10	3/26/2024 11:20	0.150	0.003	5	0
PER2 2024	3/26/2024 11:20	3/26/2024 11:30	0.150	0.003	5	0
PER2 2024	3/26/2024 11:30	3/26/2024 11:40	0.150	0.004	5	0
PER2 2024	3/26/2024 11:40	3/26/2024 11:50	0.150	0.004	5	0
PER2 2024	3/26/2024 11:50	3/26/2024 12:00	0.150	0.004	5	0
PER2 2024	3/26/2024 12:00	3/26/2024 12:10	0.150	0.004	5	0
PER2 2024	3/26/2024 12:10	3/26/2024 12:20	0.150	0.005	5	0
PER2 2024	3/26/2024 12:20	3/26/2024 12:30	0.150	0.005	5	0
PER2 2024	3/26/2024 12:30	3/26/2024 12:40	0.150	0.005	5	0
PER2 2024	3/26/2024 12:40	3/26/2024 12:50	0.150	0.005	5	0
PER2 2024	3/26/2024 12:50	3/26/2024 13:00	0.150	0.005	5	0
PER2 2024	3/26/2024 13:00	3/26/2024 13:10	0.150	0.006	5	0
PER2 2024	3/26/2024 13:10	3/26/2024 13:20	0.150	0.006	5	0
PER2 2024	3/26/2024 13:20	3/26/2024 13:30	0.150	0.006	5	0
PER2 2024	3/26/2024 13:30	3/26/2024 13:40	0.150	0.007	5	0
PER2 2024	3/26/2024 13:40	3/26/2024 13:50	0.150	0.007	5	0
PER2 2024	3/26/2024 13:50	3/26/2024 14:00	0.150	0.007	5	0
PER2 2024	3/26/2024 14:00	3/26/2024 14:10	0.150	0.007	5	0
PER2 2024	3/26/2024 14:10	3/26/2024 14:20	0.150	0.008	5	0
PER2 2024	3/26/2024 14:20	3/26/2024 14:30	0.150	0.008	5	0
PER2 2024	3/26/2024 14:30	3/26/2024 14:40	0.150	0.008	5	0
PER2 2024	3/26/2024 14:40	3/26/2024 14:50	0.150	0.009	5	0
PER2 2024	3/26/2024 14:50	3/26/2024 15:00	0.150	0.009	5	0
PER2 2024	3/26/2024 15:00	3/26/2024 15:10	0.150	0.01	5	0
PER2 2024	3/26/2024 15:10	3/26/2024 15:20	0.150	0.01	5	0
PER2 2024	3/26/2024 15:20	3/26/2024 15:30	0.150	0.011	5	0
PER2 2024	3/26/2024 15:30	3/26/2024 15:40	0.150	0.011	5	0
PER2 2024	3/26/2024 15:40	3/26/2024 15:50	0.150	0.011	5	0
PER2 2024	3/26/2024 15:50	3/26/2024 16:00	0.150	0.012	5	0
PER2 2024	3/26/2024 16:00	3/26/2024 16:10	0.150	0.012	5	0
PER2 2024	3/26/2024 16:10	3/26/2024 16:20	0.150	0.012	5	0
PER2 2024	3/26/2024 16:20	3/26/2024 16:30	0.150	0.013	5	0
PER2 2024	3/26/2024 16:30	3/26/2024 16:40	0.150	0.013	5	0
PER2 2024	3/26/2024 16:40	3/26/2024 16:50	0.150	0.014	5	0
PER2 2024	3/26/2024 16:50	3/26/2024 17:00	0.150	0.014	5	0
PER2 2024	3/26/2024 17:00	3/26/2024 17:10	0.150	0.014	5	0
PER2 2024	3/26/2024 17:10	3/26/2024 17:20	0.150	0.014	5	0
PER2 2024	3/26/2024 17:20	3/26/2024 17:30	0.150	0.014	5	0
PER2 2024	3/26/2024 17:30	3/26/2024 17:40	0.150	0.014	5	0
PER2 2024	3/26/2024 17:40	3/26/2024 17:50	0.150	0.014	5	0
PER2 2024	3/26/2024 17:50	3/26/2024 18:00	0.150	0.014	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/27/2024

Weather: 40 deg. F, Overcast


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation and foundation development. 2) ECD was not on-Site and no remedial excavation work was completed. 3) NYSDEC PM Erick Bower on-Site for Site visit.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP tables and graphs are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	7285	1520	2620

Site Layout Map and Excavation Figures

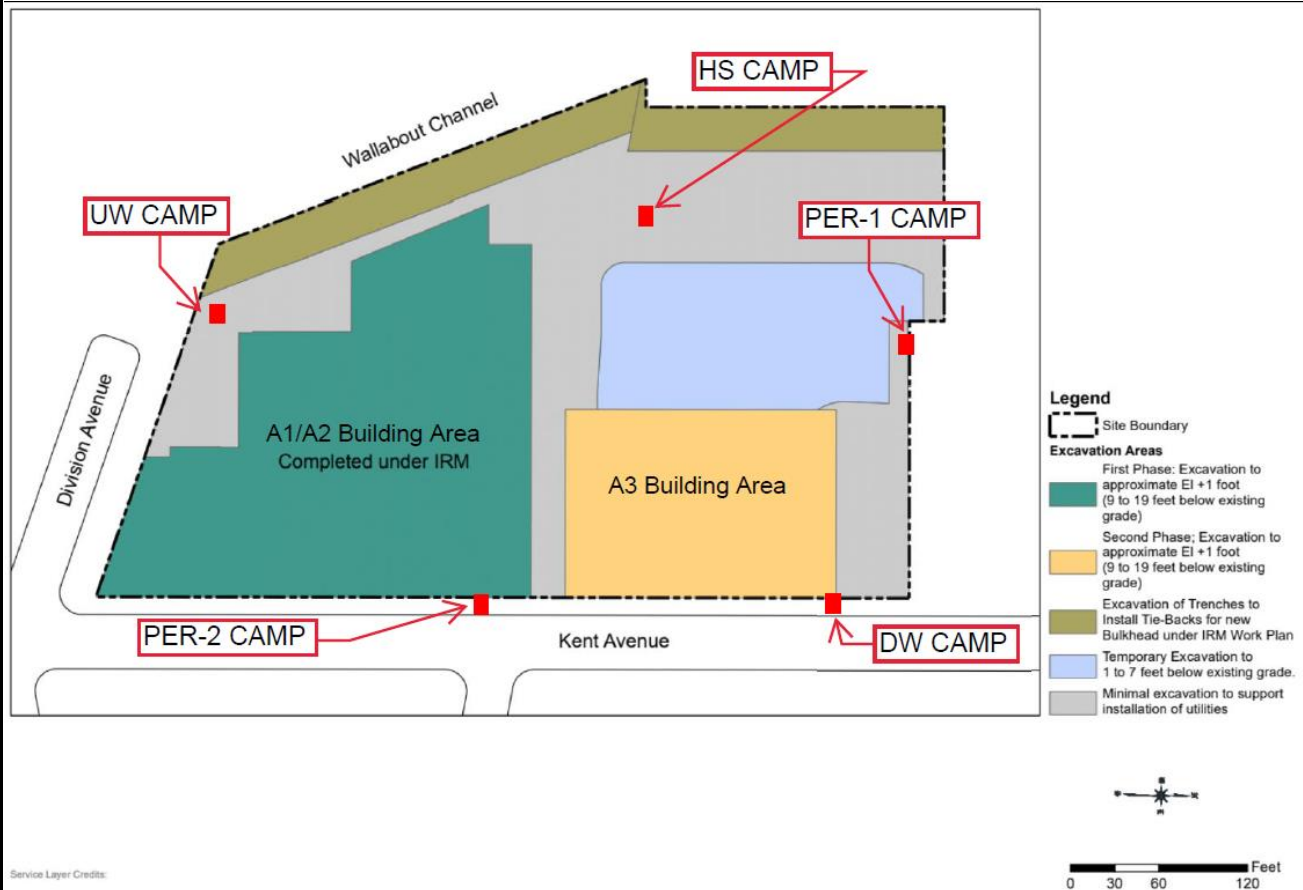

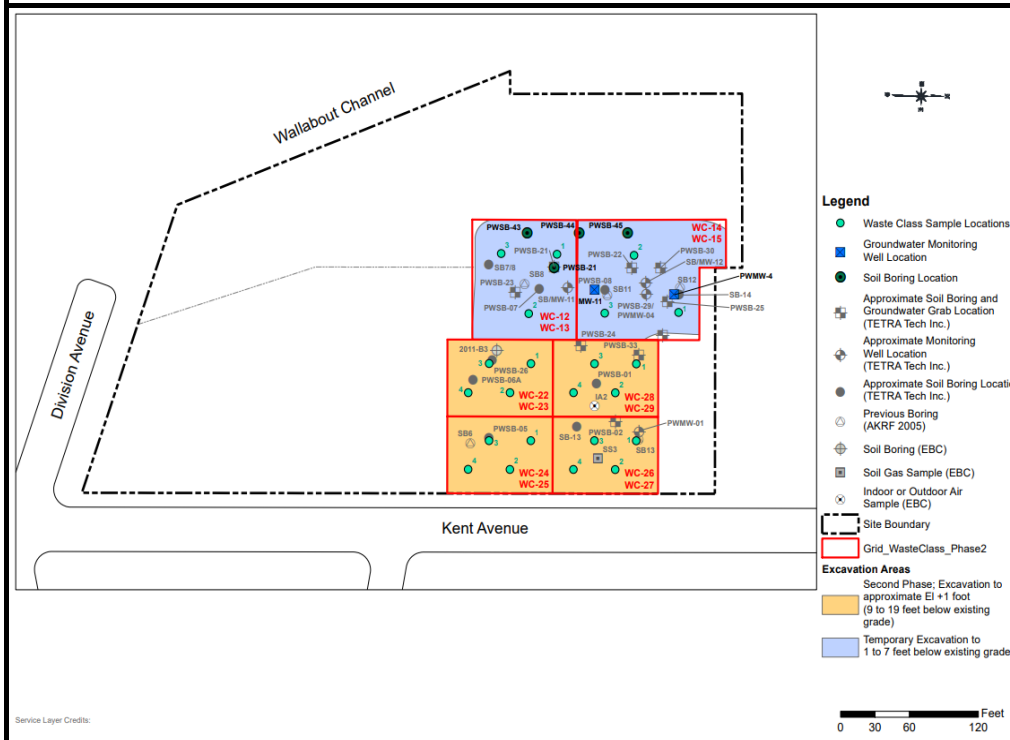
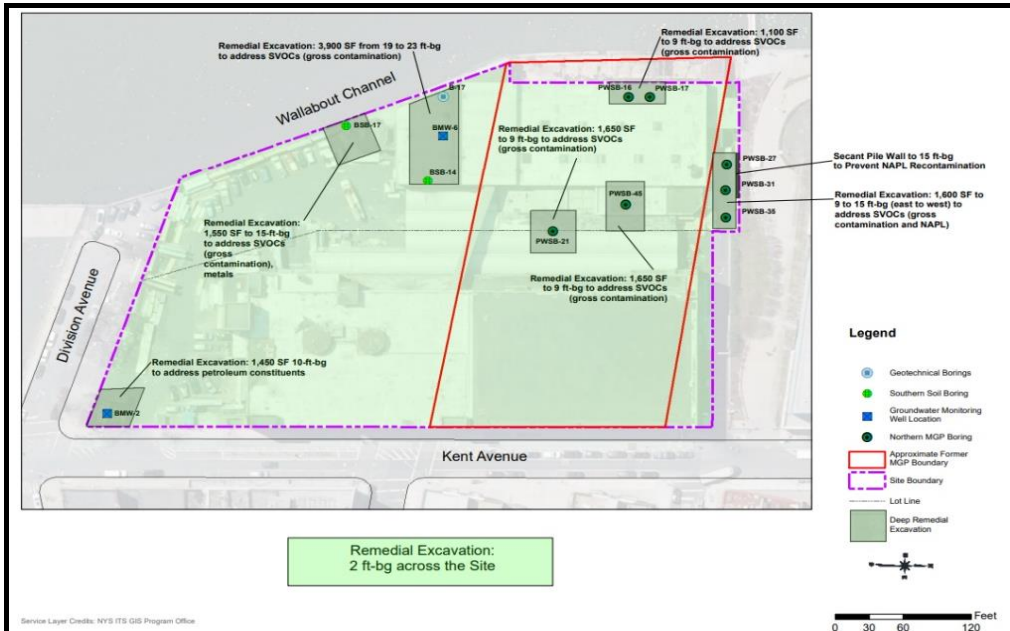


Photo 1:
View of Site conditions
and activities facing
northwest..



Photo 2:
View of the dewatering
outfall after corrective
actions were completed.

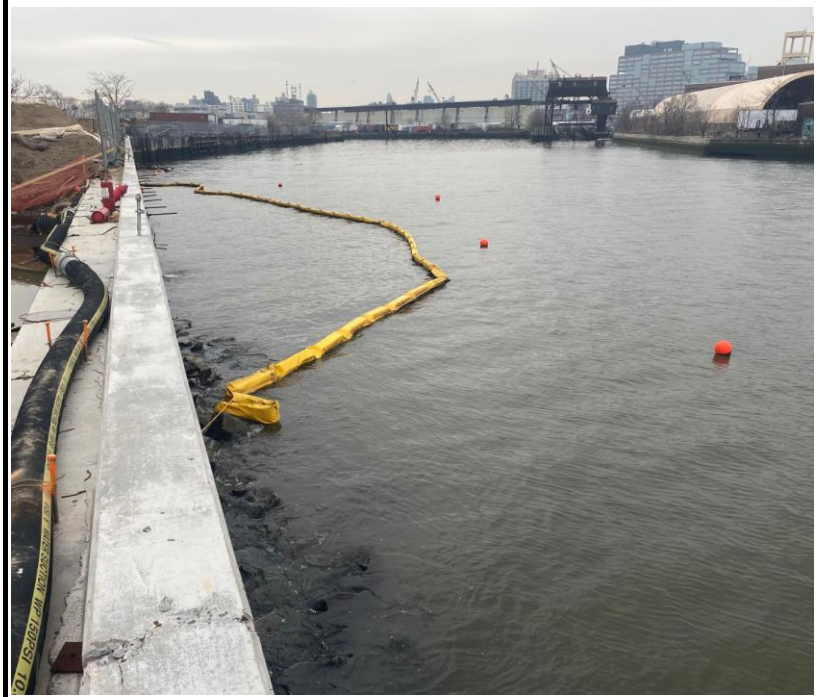
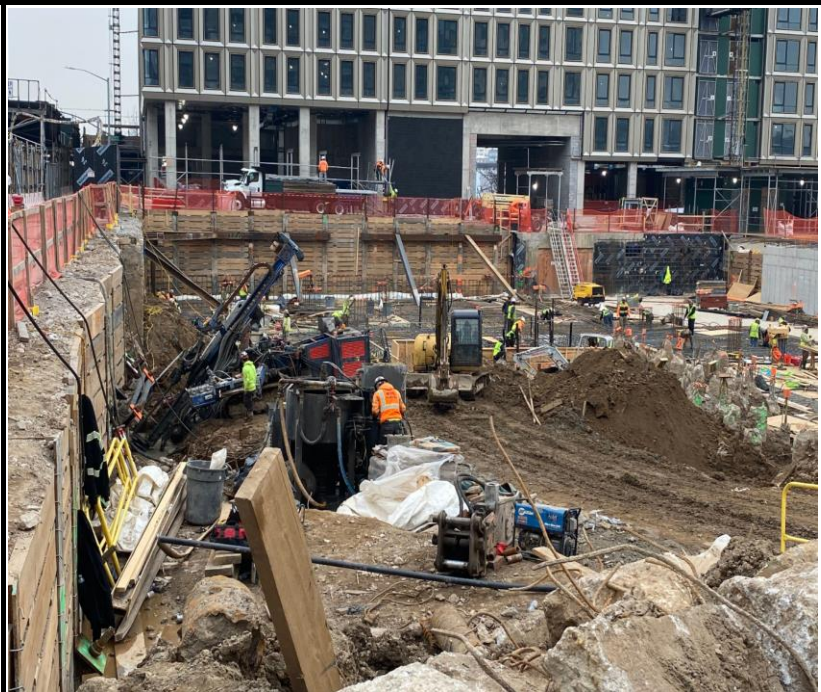


Photo 3:
View of Site activities
and SOE installation.

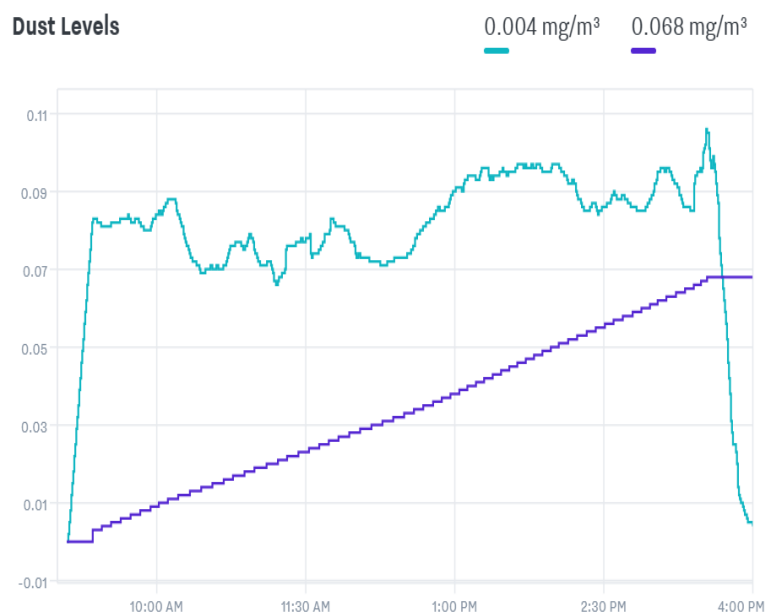


Photo 4:
View of Site
conditions and
activities facing
south.




CAMP:
Downwind
Particulates

Dust Levels



CAMP:
Downwind VOCs


VOC Levels

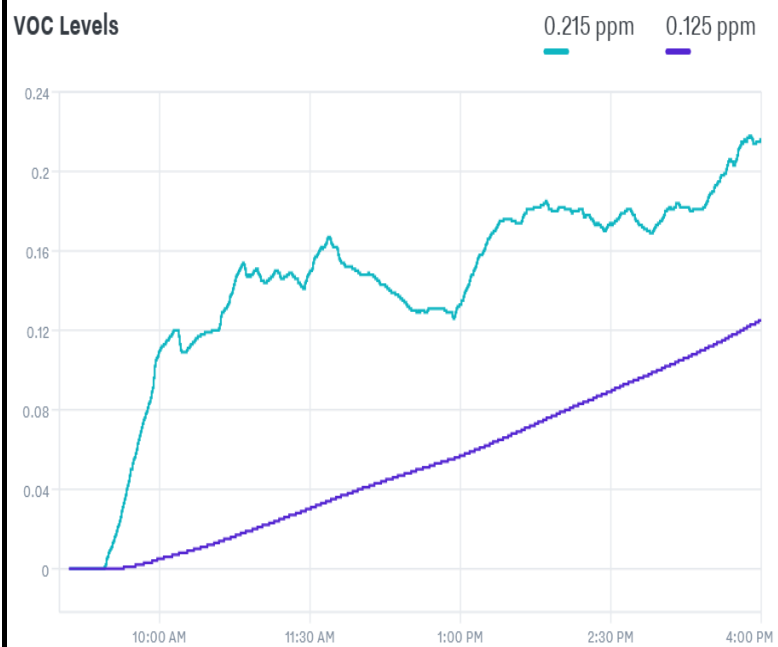

CAMP:
Upwind Particulates

Dust Levels


0.075 mg/m³ 0.076 mg/m³ 0.15

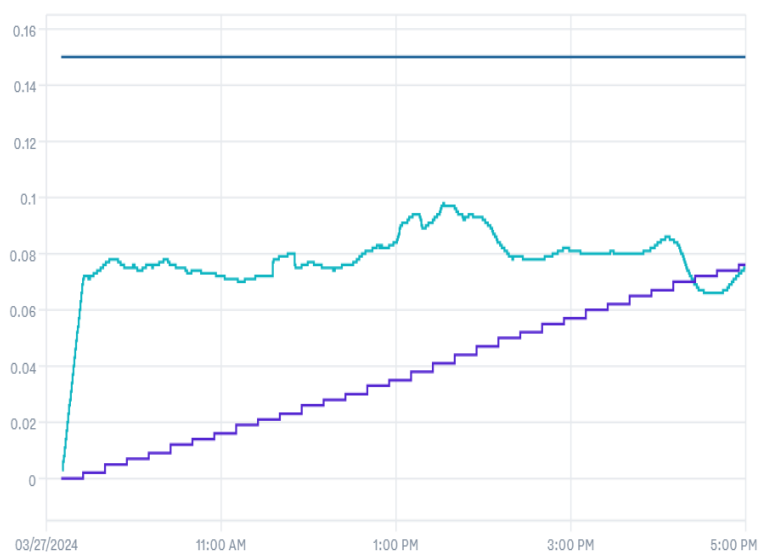

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm 5

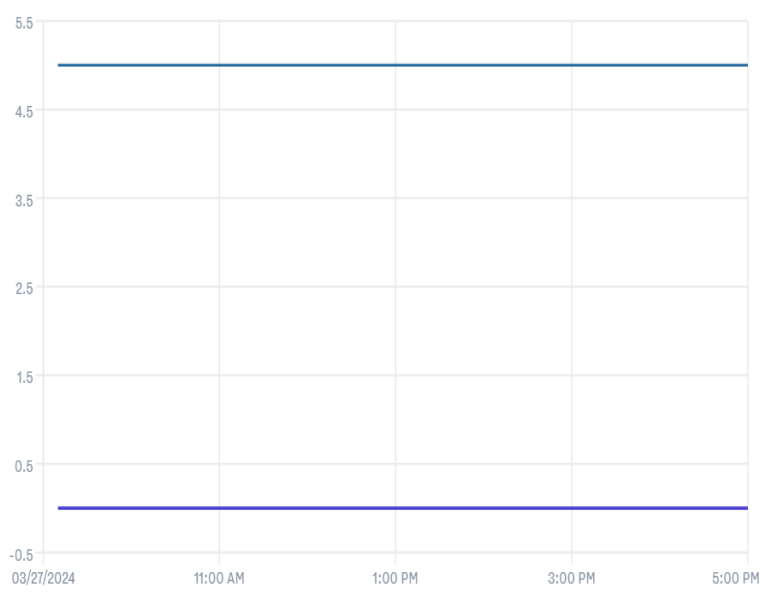

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	3/27/2024 9:00	3/27/2024 9:10	0.150	0	5	0
DW 2024	3/27/2024 9:10	3/27/2024 9:20	0.150	0	5	0
DW 2024	3/27/2024 9:20	3/27/2024 9:30	0.150	0.004	5	0
DW 2024	3/27/2024 9:30	3/27/2024 9:40	0.150	0.006	5	0.001
DW 2024	3/27/2024 9:40	3/27/2024 9:50	0.150	0.007	5	0.002
DW 2024	3/27/2024 9:50	3/27/2024 10:00	0.150	0.009	5	0.005
DW 2024	3/27/2024 10:00	3/27/2024 10:10	0.150	0.011	5	0.007
DW 2024	3/27/2024 10:10	3/27/2024 10:20	0.150	0.012	5	0.009
DW 2024	3/27/2024 10:20	3/27/2024 10:30	0.150	0.014	5	0.012
DW 2024	3/27/2024 10:30	3/27/2024 10:40	0.150	0.015	5	0.015
DW 2024	3/27/2024 10:40	3/27/2024 10:50	0.150	0.017	5	0.018
DW 2024	3/27/2024 10:50	3/27/2024 11:00	0.150	0.019	5	0.021
DW 2024	3/27/2024 11:00	3/27/2024 11:10	0.150	0.02	5	0.024
DW 2024	3/27/2024 11:10	3/27/2024 11:20	0.150	0.022	5	0.027
DW 2024	3/27/2024 11:20	3/27/2024 11:30	0.150	0.023	5	0.03
DW 2024	3/27/2024 11:30	3/27/2024 11:40	0.150	0.025	5	0.034
DW 2024	3/27/2024 11:40	3/27/2024 11:50	0.150	0.027	5	0.037
DW 2024	3/27/2024 11:50	3/27/2024 12:00	0.150	0.028	5	0.04
DW 2024	3/27/2024 12:00	3/27/2024 12:10	0.150	0.03	5	0.043
DW 2024	3/27/2024 12:10	3/27/2024 12:20	0.150	0.031	5	0.046
DW 2024	3/27/2024 12:20	3/27/2024 12:30	0.150	0.033	5	0.048
DW 2024	3/27/2024 12:30	3/27/2024 12:40	0.150	0.034	5	0.051
DW 2024	3/27/2024 12:40	3/27/2024 12:50	0.150	0.036	5	0.054
DW 2024	3/27/2024 12:50	3/27/2024 13:00	0.150	0.038	5	0.057
DW 2024	3/27/2024 13:00	3/27/2024 13:10	0.150	0.04	5	0.06
DW 2024	3/27/2024 13:10	3/27/2024 13:20	0.150	0.042	5	0.064
DW 2024	3/27/2024 13:20	3/27/2024 13:30	0.150	0.044	5	0.067
DW 2024	3/27/2024 13:30	3/27/2024 13:40	0.150	0.046	5	0.071
DW 2024	3/27/2024 13:40	3/27/2024 13:50	0.150	0.048	5	0.075
DW 2024	3/27/2024 13:50	3/27/2024 14:00	0.150	0.05	5	0.079
DW 2024	3/27/2024 14:00	3/27/2024 14:10	0.150	0.052	5	0.082
DW 2024	3/27/2024 14:10	3/27/2024 14:20	0.150	0.054	5	0.086
DW 2024	3/27/2024 14:20	3/27/2024 14:30	0.150	0.055	5	0.089
DW 2024	3/27/2024 14:30	3/27/2024 14:40	0.150	0.057	5	0.093
DW 2024	3/27/2024 14:40	3/27/2024 14:50	0.150	0.059	5	0.097
DW 2024	3/27/2024 14:50	3/27/2024 15:00	0.150	0.061	5	0.1
DW 2024	3/27/2024 15:00	3/27/2024 15:10	0.150	0.063	5	0.104
DW 2024	3/27/2024 15:10	3/27/2024 15:20	0.150	0.065	5	0.108
DW 2024	3/27/2024 15:20	3/27/2024 15:30	0.150	0.067	5	0.112
DW 2024	3/27/2024 15:30	3/27/2024 15:40	0.150	0.068	5	0.116
DW 2024	3/27/2024 15:40	3/27/2024 15:50	0.150	0.068	5	0.121
DW 2024	3/27/2024 15:50	3/27/2024 16:00	0.150	0.068	5	0.125
DW 2024	3/27/2024 16:00	3/27/2024 16:10	0.150	0.068	5	0.129
DW 2024	3/27/2024 16:10	3/27/2024 16:20	0.150	0.068	5	0.133
DW 2024	3/27/2024 16:20	3/27/2024 16:30	0.150	0.068	5	0.137
DW 2024	3/27/2024 16:30	3/27/2024 16:40	0.150	0.068	5	0.142
DW 2024	3/27/2024 16:40	3/27/2024 16:50	0.150	0.068	5	0.146
DW 2024	3/27/2024 16:50	3/27/2024 17:00	0.150	0.068	5	0.151

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	3/27/2024 9:00	3/27/2024 9:10	0.150	0	5	0
UW 2024	3/27/2024 9:10	3/27/2024 9:20	0.150	0	5	0
UW 2024	3/27/2024 9:20	3/27/2024 9:30	0.150	0.002	5	0
UW 2024	3/27/2024 9:30	3/27/2024 9:40	0.150	0.002	5	0
UW 2024	3/27/2024 9:40	3/27/2024 9:50	0.150	0.005	5	0
UW 2024	3/27/2024 9:50	3/27/2024 10:00	0.150	0.007	5	0
UW 2024	3/27/2024 10:00	3/27/2024 10:10	0.150	0.007	5	0
UW 2024	3/27/2024 10:10	3/27/2024 10:20	0.150	0.009	5	0
UW 2024	3/27/2024 10:20	3/27/2024 10:30	0.150	0.012	5	0
UW 2024	3/27/2024 10:30	3/27/2024 10:40	0.150	0.012	5	0
UW 2024	3/27/2024 10:40	3/27/2024 10:50	0.150	0.014	5	0
UW 2024	3/27/2024 10:50	3/27/2024 11:00	0.150	0.016	5	0
UW 2024	3/27/2024 11:00	3/27/2024 11:10	0.150	0.016	5	0
UW 2024	3/27/2024 11:10	3/27/2024 11:20	0.150	0.019	5	0
UW 2024	3/27/2024 11:20	3/27/2024 11:30	0.150	0.021	5	0
UW 2024	3/27/2024 11:30	3/27/2024 11:40	0.150	0.021	5	0
UW 2024	3/27/2024 11:40	3/27/2024 11:50	0.150	0.023	5	0
UW 2024	3/27/2024 11:50	3/27/2024 12:00	0.150	0.026	5	0
UW 2024	3/27/2024 12:00	3/27/2024 12:10	0.150	0.026	5	0
UW 2024	3/27/2024 12:10	3/27/2024 12:20	0.150	0.028	5	0
UW 2024	3/27/2024 12:20	3/27/2024 12:30	0.150	0.03	5	0
UW 2024	3/27/2024 12:30	3/27/2024 12:40	0.150	0.03	5	0
UW 2024	3/27/2024 12:40	3/27/2024 12:50	0.150	0.033	5	0
UW 2024	3/27/2024 12:50	3/27/2024 13:00	0.150	0.035	5	0
UW 2024	3/27/2024 13:00	3/27/2024 13:10	0.150	0.035	5	0
UW 2024	3/27/2024 13:10	3/27/2024 13:20	0.150	0.038	5	0
UW 2024	3/27/2024 13:20	3/27/2024 13:30	0.150	0.041	5	0
UW 2024	3/27/2024 13:30	3/27/2024 13:40	0.150	0.041	5	0
UW 2024	3/27/2024 13:40	3/27/2024 13:50	0.150	0.044	5	0
UW 2024	3/27/2024 13:50	3/27/2024 14:00	0.150	0.047	5	0
UW 2024	3/27/2024 14:00	3/27/2024 14:10	0.150	0.047	5	0
UW 2024	3/27/2024 14:10	3/27/2024 14:20	0.150	0.05	5	0
UW 2024	3/27/2024 14:20	3/27/2024 14:30	0.150	0.052	5	0
UW 2024	3/27/2024 14:30	3/27/2024 14:40	0.150	0.052	5	0
UW 2024	3/27/2024 14:40	3/27/2024 14:50	0.150	0.055	5	0
UW 2024	3/27/2024 14:50	3/27/2024 15:00	0.150	0.057	5	0
UW 2024	3/27/2024 15:00	3/27/2024 15:10	0.150	0.057	5	0
UW 2024	3/27/2024 15:10	3/27/2024 15:20	0.150	0.06	5	0
UW 2024	3/27/2024 15:20	3/27/2024 15:30	0.150	0.062	5	0
UW 2024	3/27/2024 15:30	3/27/2024 15:40	0.150	0.062	5	0
UW 2024	3/27/2024 15:40	3/27/2024 15:50	0.150	0.065	5	0
UW 2024	3/27/2024 15:50	3/27/2024 16:00	0.150	0.067	5	0
UW 2024	3/27/2024 16:00	3/27/2024 16:10	0.150	0.067	5	0
UW 2024	3/27/2024 16:10	3/27/2024 16:20	0.150	0.07	5	0
UW 2024	3/27/2024 16:20	3/27/2024 16:30	0.150	0.072	5	0
UW 2024	3/27/2024 16:30	3/27/2024 16:40	0.150	0.072	5	0
UW 2024	3/27/2024 16:40	3/27/2024 16:50	0.150	0.074	5	0
UW 2024	3/27/2024 16:50	3/27/2024 17:00	0.150	0.076	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	3/27/2024 9:00	3/27/2024 9:10	0.150	0.008	5	0
HS South	3/27/2024 9:10	3/27/2024 9:20	0.150	0.008	5	0
HS South	3/27/2024 9:20	3/27/2024 9:30	0.150	0.008	5	0
HS South	3/27/2024 9:30	3/27/2024 9:40	0.150	0.008	5	0
HS South	3/27/2024 9:40	3/27/2024 9:50	0.150	0	5	0
HS South	3/27/2024 9:50	3/27/2024 10:00	0.150	0	5	0
HS South	3/27/2024 10:00	3/27/2024 10:10	0.150	0.004	5	0
HS South	3/27/2024 10:10	3/27/2024 10:20	0.150	0.006	5	0
HS South	3/27/2024 10:20	3/27/2024 10:30	0.150	0.008	5	0
HS South	3/27/2024 10:30	3/27/2024 10:40	0.150	0.009	5	0
HS South	3/27/2024 10:40	3/27/2024 10:50	0.150	0.011	5	0
HS South	3/27/2024 10:50	3/27/2024 11:00	0.150	0.012	5	0
HS South	3/27/2024 11:00	3/27/2024 11:10	0.150	0.014	5	0
HS South	3/27/2024 11:10	3/27/2024 11:20	0.150	0.015	5	0
HS South	3/27/2024 11:20	3/27/2024 11:30	0.150	0.016	5	0
HS South	3/27/2024 11:30	3/27/2024 11:40	0.150	0.018	5	0
HS South	3/27/2024 11:40	3/27/2024 11:50	0.150	0.019	5	0
HS South	3/27/2024 11:50	3/27/2024 12:00	0.150	0.021	5	0
HS South	3/27/2024 12:00	3/27/2024 12:10	0.150	0.022	5	0
HS South	3/27/2024 12:10	3/27/2024 12:20	0.150	0.024	5	0
HS South	3/27/2024 12:20	3/27/2024 12:30	0.150	0.025	5	0
HS South	3/27/2024 12:30	3/27/2024 12:40	0.150	0.027	5	0
HS South	3/27/2024 12:40	3/27/2024 12:50	0.150	0.029	5	0
HS South	3/27/2024 12:50	3/27/2024 13:00	0.150	0.03	5	0
HS South	3/27/2024 13:00	3/27/2024 13:10	0.150	0.032	5	0
HS South	3/27/2024 13:10	3/27/2024 13:20	0.150	0.034	5	0
HS South	3/27/2024 13:20	3/27/2024 13:30	0.150	0.036	5	0
HS South	3/27/2024 13:30	3/27/2024 13:40	0.150	0.037	5	0
HS South	3/27/2024 13:40	3/27/2024 13:50	0.150	0.039	5	0
HS South	3/27/2024 13:50	3/27/2024 14:00	0.150	0.041	5	0
HS South	3/27/2024 14:00	3/27/2024 14:10	0.150	0.043	5	0
HS South	3/27/2024 14:10	3/27/2024 14:20	0.150	0.044	5	0
HS South	3/27/2024 14:20	3/27/2024 14:30	0.150	0.046	5	0
HS South	3/27/2024 14:30	3/27/2024 14:40	0.150	0.047	5	0
HS South	3/27/2024 14:40	3/27/2024 14:50	0.150	0.049	5	0
HS South	3/27/2024 14:50	3/27/2024 15:00	0.150	0.05	5	0
HS South	3/27/2024 15:00	3/27/2024 15:10	0.150	0.052	5	0
HS South	3/27/2024 15:10	3/27/2024 15:20	0.150	0.054	5	0
HS South	3/27/2024 15:20	3/27/2024 15:30	0.150	0.055	5	0
HS South	3/27/2024 15:30	3/27/2024 15:40	0.150	0.057	5	0
HS South	3/27/2024 15:40	3/27/2024 15:50	0.150	0.058	5	0
HS South	3/27/2024 15:50	3/27/2024 16:00	0.150	0.06	5	0
HS South	3/27/2024 16:00	3/27/2024 16:10	0.150	0.062	5	0
HS South	3/27/2024 16:10	3/27/2024 16:20	0.150	0.063	5	0
HS South	3/27/2024 16:20	3/27/2024 16:30	0.150	0.064	5	0
HS South	3/27/2024 16:30	3/27/2024 16:40	0.150	0.066	5	0
HS South	3/27/2024 16:40	3/27/2024 16:50	0.150	0.067	5	0
HS South	3/27/2024 16:50	3/27/2024 17:00	0.150	0.068	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	3/27/2024 9:00	3/27/2024 9:10	0.150	0	5	0
PER1 2024	3/27/2024 9:10	3/27/2024 9:20	0.150	0.003	5	0
PER1 2024	3/27/2024 9:20	3/27/2024 9:30	0.150	0.004	5	0
PER1 2024	3/27/2024 9:30	3/27/2024 9:40	0.150	0.006	5	0
PER1 2024	3/27/2024 9:40	3/27/2024 9:50	0.150	0.007	5	0
PER1 2024	3/27/2024 9:50	3/27/2024 10:00	0.150	0.009	5	0
PER1 2024	3/27/2024 10:00	3/27/2024 10:10	0.150	0.011	5	0
PER1 2024	3/27/2024 10:10	3/27/2024 10:20	0.150	0.012	5	0
PER1 2024	3/27/2024 10:20	3/27/2024 10:30	0.150	0.013	5	0
PER1 2024	3/27/2024 10:30	3/27/2024 10:40	0.150	0.015	5	0
PER1 2024	3/27/2024 10:40	3/27/2024 10:50	0.150	0.016	5	0
PER1 2024	3/27/2024 10:50	3/27/2024 11:00	0.150	0.018	5	0
PER1 2024	3/27/2024 11:00	3/27/2024 11:10	0.150	0.019	5	0
PER1 2024	3/27/2024 11:10	3/27/2024 11:20	0.150	0.02	5	0
PER1 2024	3/27/2024 11:20	3/27/2024 11:30	0.150	0.022	5	0
PER1 2024	3/27/2024 11:30	3/27/2024 11:40	0.150	0.023	5	0
PER1 2024	3/27/2024 11:40	3/27/2024 11:50	0.150	0.025	5	0
PER1 2024	3/27/2024 11:50	3/27/2024 12:00	0.150	0.026	5	0
PER1 2024	3/27/2024 12:00	3/27/2024 12:10	0.150	0.028	5	0
PER1 2024	3/27/2024 12:10	3/27/2024 12:20	0.150	0.029	5	0
PER1 2024	3/27/2024 12:20	3/27/2024 12:30	0.150	0.031	5	0
PER1 2024	3/27/2024 12:30	3/27/2024 12:40	0.150	0.033	5	0
PER1 2024	3/27/2024 12:40	3/27/2024 12:50	0.150	0.034	5	0
PER1 2024	3/27/2024 12:50	3/27/2024 13:00	0.150	0.036	5	0
PER1 2024	3/27/2024 13:00	3/27/2024 13:10	0.150	0.038	5	0
PER1 2024	3/27/2024 13:10	3/27/2024 13:20	0.150	0.04	5	0
PER1 2024	3/27/2024 13:20	3/27/2024 13:30	0.150	0.041	5	0
PER1 2024	3/27/2024 13:30	3/27/2024 13:40	0.150	0.043	5	0
PER1 2024	3/27/2024 13:40	3/27/2024 13:50	0.150	0.045	5	0
PER1 2024	3/27/2024 13:50	3/27/2024 14:00	0.150	0.047	5	0
PER1 2024	3/27/2024 14:00	3/27/2024 14:10	0.150	0.049	5	0
PER1 2024	3/27/2024 14:10	3/27/2024 14:20	0.150	0.05	5	0
PER1 2024	3/27/2024 14:20	3/27/2024 14:30	0.150	0.052	5	0
PER1 2024	3/27/2024 14:30	3/27/2024 14:40	0.150	0.054	5	0
PER1 2024	3/27/2024 14:40	3/27/2024 14:50	0.150	0.055	5	0
PER1 2024	3/27/2024 14:50	3/27/2024 15:00	0.150	0.057	5	0
PER1 2024	3/27/2024 15:00	3/27/2024 15:10	0.150	0.059	5	0
PER1 2024	3/27/2024 15:10	3/27/2024 15:20	0.150	0.06	5	0
PER1 2024	3/27/2024 15:20	3/27/2024 15:30	0.150	0.062	5	0
PER1 2024	3/27/2024 15:30	3/27/2024 15:40	0.150	0.064	5	0
PER1 2024	3/27/2024 15:40	3/27/2024 15:50	0.150	0.066	5	0
PER1 2024	3/27/2024 15:50	3/27/2024 16:00	0.150	0.067	5	0
PER1 2024	3/27/2024 16:00	3/27/2024 16:10	0.150	0.069	5	0
PER1 2024	3/27/2024 16:10	3/27/2024 16:20	0.150	0.07	5	0
PER1 2024	3/27/2024 16:20	3/27/2024 16:30	0.150	0.072	5	0
PER1 2024	3/27/2024 16:30	3/27/2024 16:40	0.150	0.073	5	0
PER1 2024	3/27/2024 16:40	3/27/2024 16:50	0.150	0.075	5	0
PER1 2024	3/27/2024 16:50	3/27/2024 17:00	0.150	0.076	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	3/27/2024 9:00	3/27/2024 9:10	0.150	0	5	0
PER2 2024	3/27/2024 9:10	3/27/2024 9:20	0.150	0	5	0
PER2 2024	3/27/2024 9:20	3/27/2024 9:30	0.150	0.004	5	0
PER2 2024	3/27/2024 9:30	3/27/2024 9:40	0.150	0.006	5	0
PER2 2024	3/27/2024 9:40	3/27/2024 9:50	0.150	0.007	5	0
PER2 2024	3/27/2024 9:50	3/27/2024 10:00	0.150	0.009	5	0
PER2 2024	3/27/2024 10:00	3/27/2024 10:10	0.150	0.01	5	0
PER2 2024	3/27/2024 10:10	3/27/2024 10:20	0.150	0.012	5	0
PER2 2024	3/27/2024 10:20	3/27/2024 10:30	0.150	0.013	5	0
PER2 2024	3/27/2024 10:30	3/27/2024 10:40	0.150	0.014	5	0
PER2 2024	3/27/2024 10:40	3/27/2024 10:50	0.150	0.016	5	0
PER2 2024	3/27/2024 10:50	3/27/2024 11:00	0.150	0.017	5	0
PER2 2024	3/27/2024 11:00	3/27/2024 11:10	0.150	0.019	5	0
PER2 2024	3/27/2024 11:10	3/27/2024 11:20	0.150	0.02	5	0
PER2 2024	3/27/2024 11:20	3/27/2024 11:30	0.150	0.022	5	0
PER2 2024	3/27/2024 11:30	3/27/2024 11:40	0.150	0.024	5	0
PER2 2024	3/27/2024 11:40	3/27/2024 11:50	0.150	0.025	5	0
PER2 2024	3/27/2024 11:50	3/27/2024 12:00	0.150	0.027	5	0
PER2 2024	3/27/2024 12:00	3/27/2024 12:10	0.150	0.028	5	0
PER2 2024	3/27/2024 12:10	3/27/2024 12:20	0.150	0.03	5	0
PER2 2024	3/27/2024 12:20	3/27/2024 12:30	0.150	0.032	5	0
PER2 2024	3/27/2024 12:30	3/27/2024 12:40	0.150	0.033	5	0
PER2 2024	3/27/2024 12:40	3/27/2024 12:50	0.150	0.035	5	0
PER2 2024	3/27/2024 12:50	3/27/2024 13:00	0.150	0.037	5	0
PER2 2024	3/27/2024 13:00	3/27/2024 13:10	0.150	0.039	5	0
PER2 2024	3/27/2024 13:10	3/27/2024 13:20	0.150	0.041	5	0
PER2 2024	3/27/2024 13:20	3/27/2024 13:30	0.150	0.044	5	0
PER2 2024	3/27/2024 13:30	3/27/2024 13:40	0.150	0.046	5	0
PER2 2024	3/27/2024 13:40	3/27/2024 13:50	0.150	0.048	5	0
PER2 2024	3/27/2024 13:50	3/27/2024 14:00	0.150	0.05	5	0
PER2 2024	3/27/2024 14:00	3/27/2024 14:10	0.150	0.052	5	0
PER2 2024	3/27/2024 14:10	3/27/2024 14:20	0.150	0.054	5	0
PER2 2024	3/27/2024 14:20	3/27/2024 14:30	0.150	0.056	5	0
PER2 2024	3/27/2024 14:30	3/27/2024 14:40	0.150	0.058	5	0
PER2 2024	3/27/2024 14:40	3/27/2024 14:50	0.150	0.06	5	0
PER2 2024	3/27/2024 14:50	3/27/2024 15:00	0.150	0.062	5	0
PER2 2024	3/27/2024 15:00	3/27/2024 15:10	0.150	0.064	5	0
PER2 2024	3/27/2024 15:10	3/27/2024 15:20	0.150	0.066	5	0
PER2 2024	3/27/2024 15:20	3/27/2024 15:30	0.150	0.068	5	0
PER2 2024	3/27/2024 15:30	3/27/2024 15:40	0.150	0.069	5	0
PER2 2024	3/27/2024 15:40	3/27/2024 15:50	0.150	0.071	5	0
PER2 2024	3/27/2024 15:50	3/27/2024 16:00	0.150	0.073	5	0
PER2 2024	3/27/2024 16:00	3/27/2024 16:10	0.150	0.075	5	0
PER2 2024	3/27/2024 16:10	3/27/2024 16:20	0.150	0.077	5	0
PER2 2024	3/27/2024 16:20	3/27/2024 16:30	0.150	0.078	5	0
PER2 2024	3/27/2024 16:30	3/27/2024 16:40	0.150	0.08	5	0
PER2 2024	3/27/2024 16:40	3/27/2024 16:50	0.150	0.081	5	0
PER2 2024	3/27/2024 16:50	3/27/2024 17:00	0.150	0.083	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 3/28/2024

Weather: 30 deg. F, Rain


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation and foundation development. 2) ECD was not on-Site and no remedial excavation work was completed. 3) Alba exported 9 loads (~180 CY) of material for off-Site disposal at the MSM facility. 3) The Site is closed tomorrow, 3/29. Work will resume on Monday 4/1.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP stations were not turned on due to heavy rain throughout the entirety of the workday.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation and SOE installation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	180	0	0
Total:(CY)	4485	0	7465	1520	2620

Site Layout Map and Excavation Figures

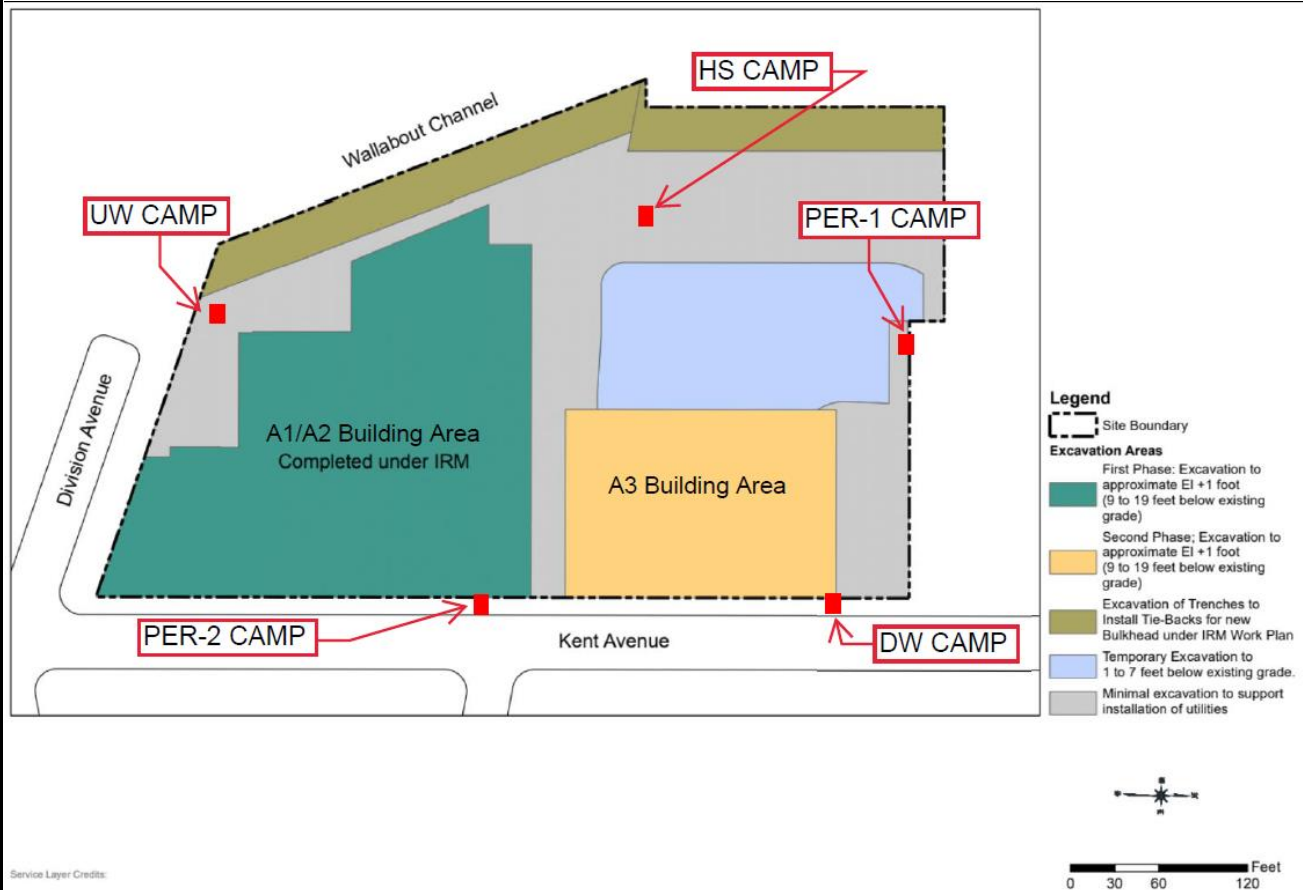

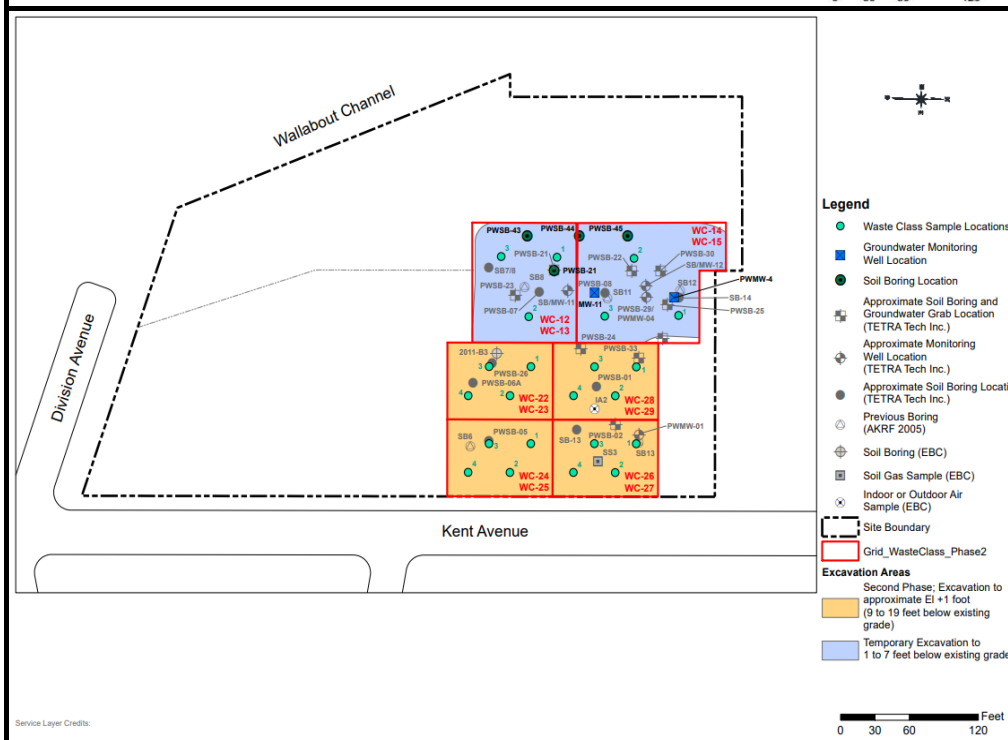
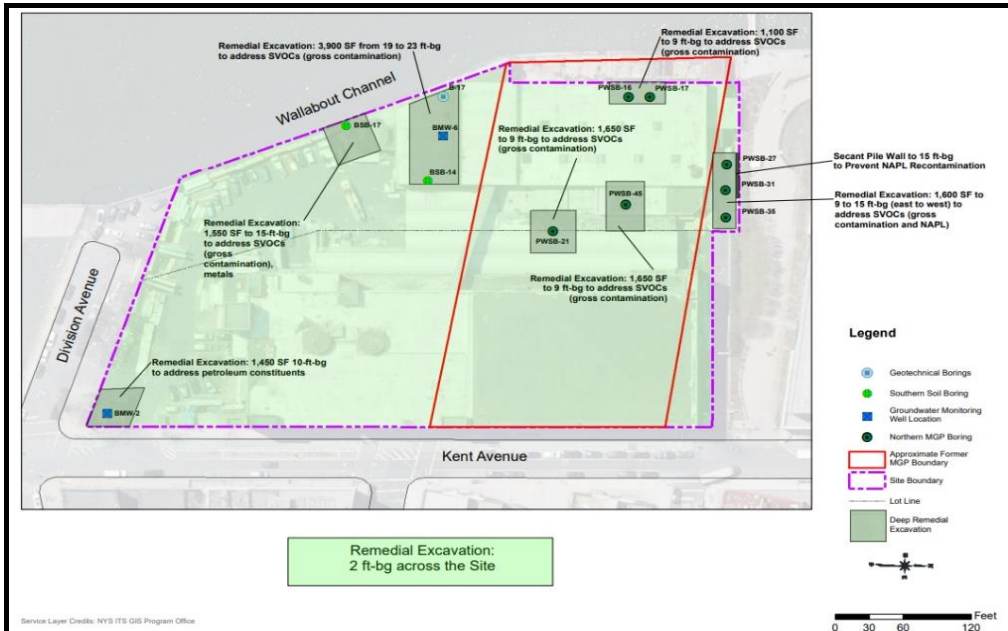


Photo 1:
View of Site conditions
and activities facing
northwest.

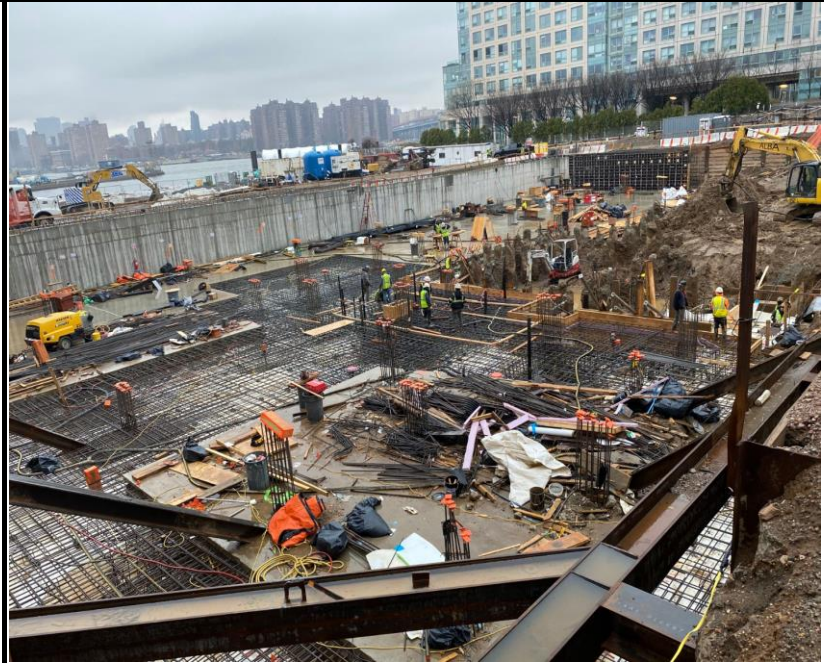


Photo 2:
View of Site conditions
and soil excavation
facing east.


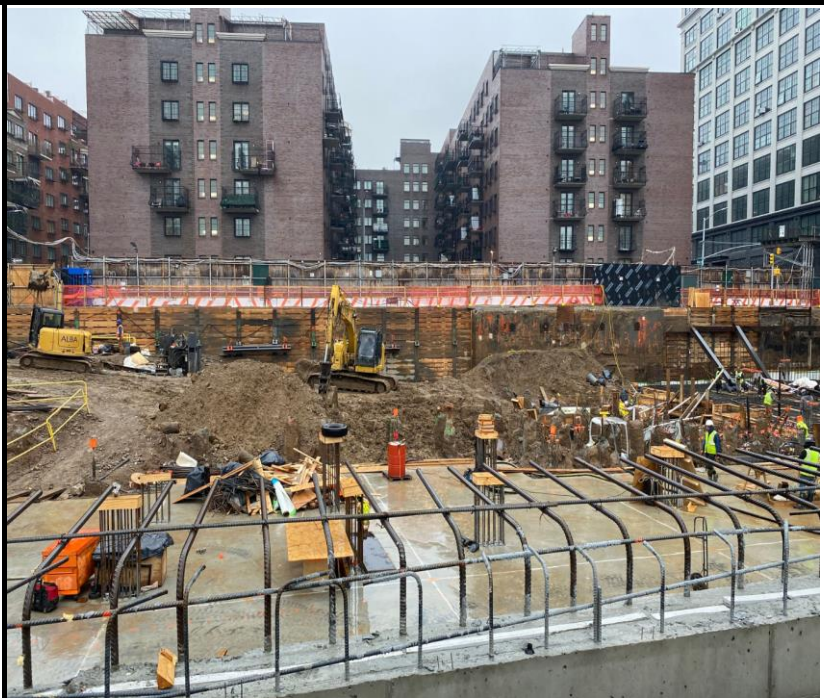


Photo 3:
View of Site activities facing south.



Photo 4:
View of the remedial excavation facing west.

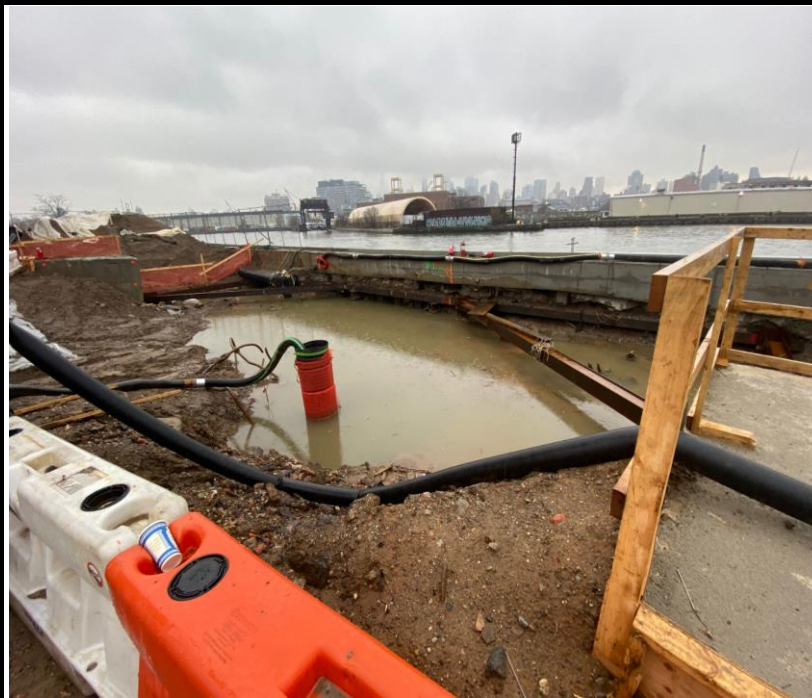

CAMP: Downwind Particulates	NA
CAMP: Downwind VOCs	NA

CAMP: Upwind Particulates	NA
CAMP: Upwind VOCs	NA
