

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/01/2024

Weather: 75 deg. F, Partly cloudy


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development. 2) The dewatering contractor, GWTT, on-site to complete dewatering system maintenance.	
Is the dewatering system operating: YES NO *see below	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: *The dewatering system will be restarted on the following work day, May 2nd, following system maintenance completion.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8365	1520	3980

Site Layout Map and Excavation Figures

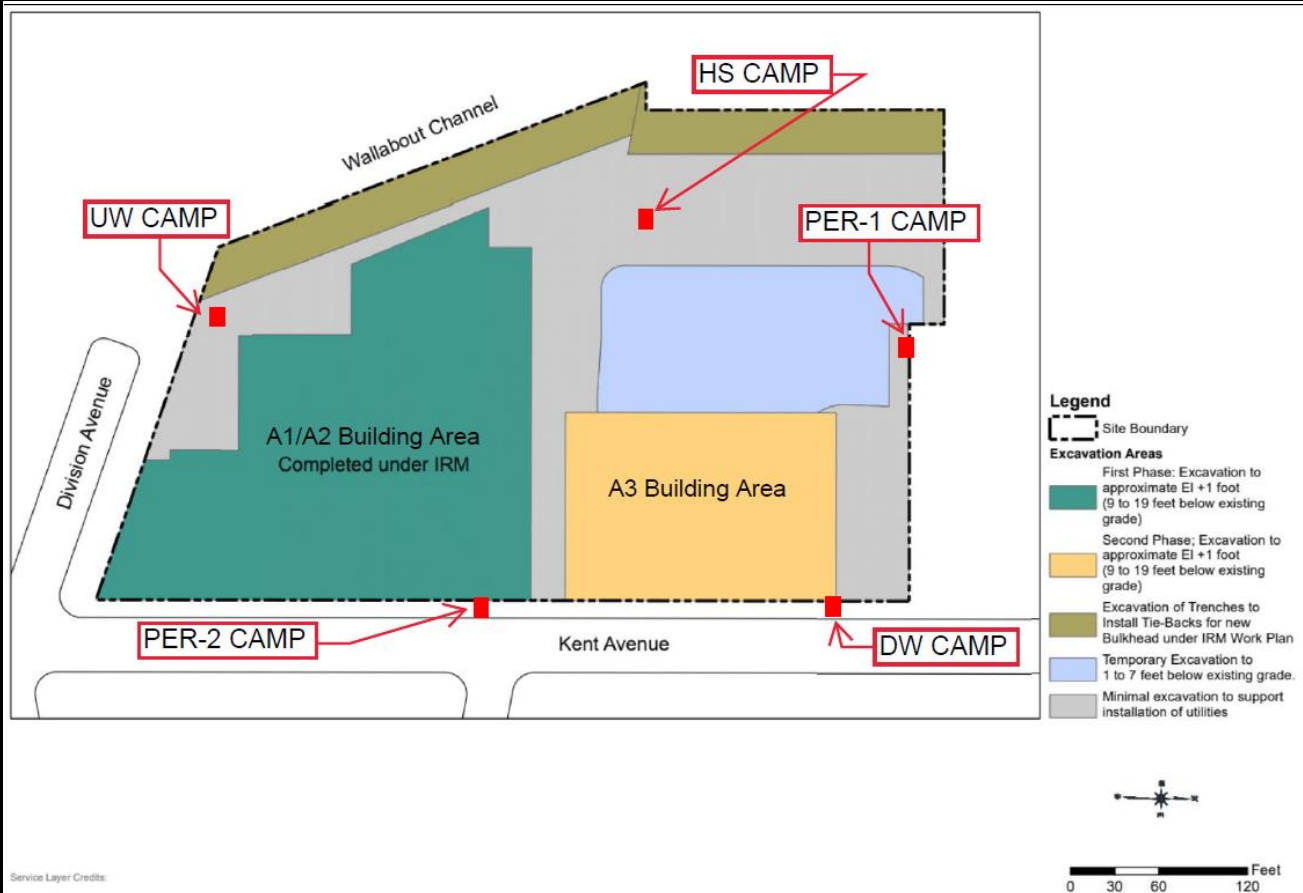

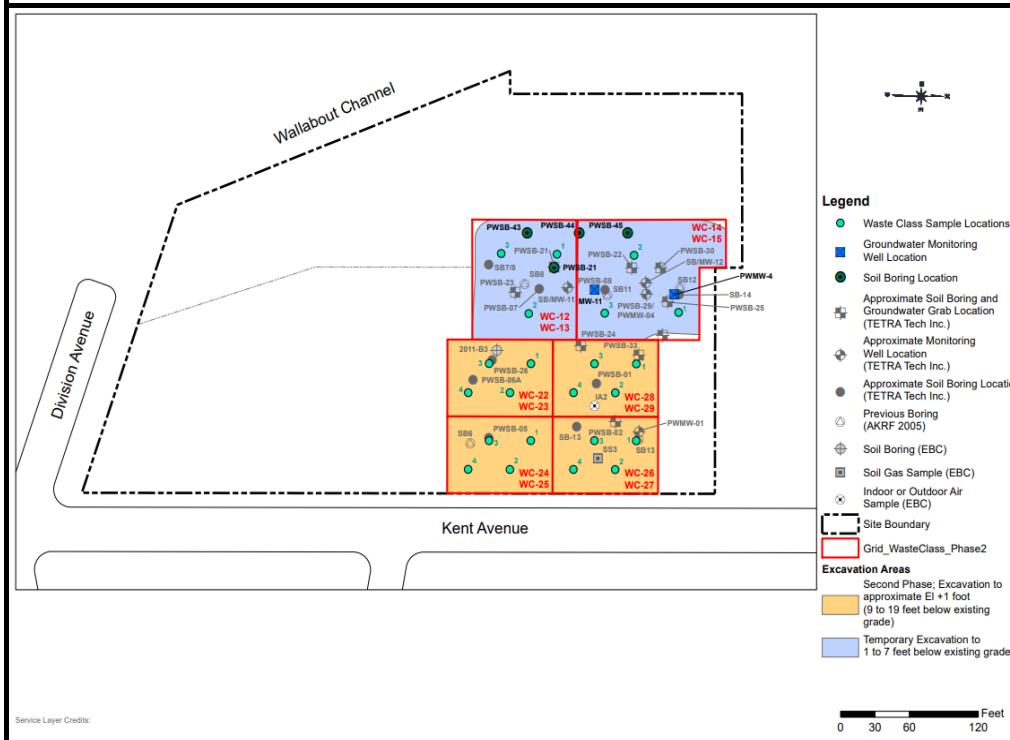
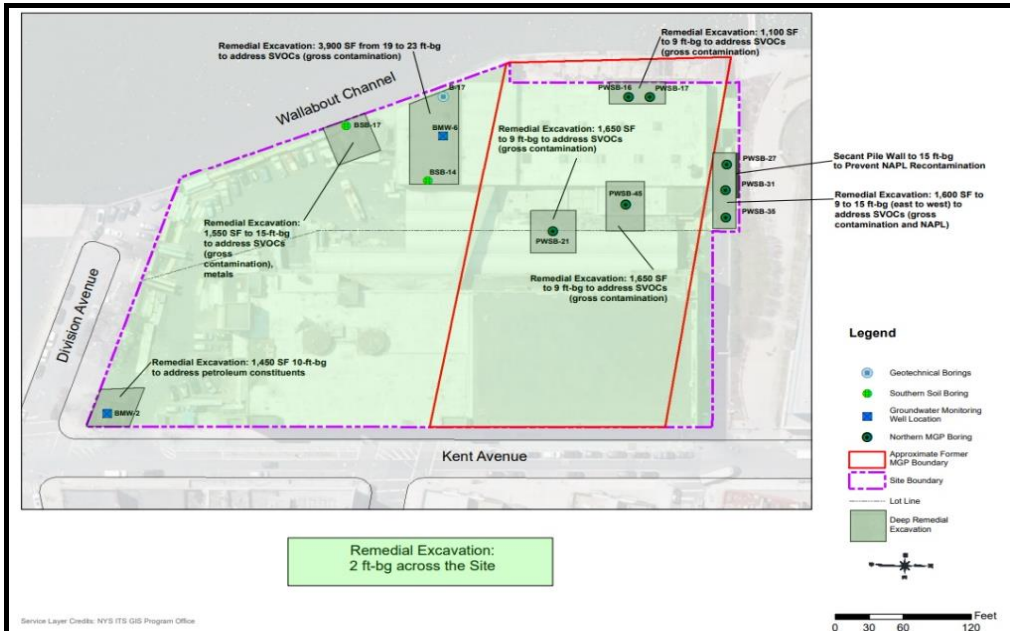


Photo 1:

View of site conditions and activities, including waterproofing installation, facing east.



Photo 2:

View of soil excavation and Ste conditions facing northeast.

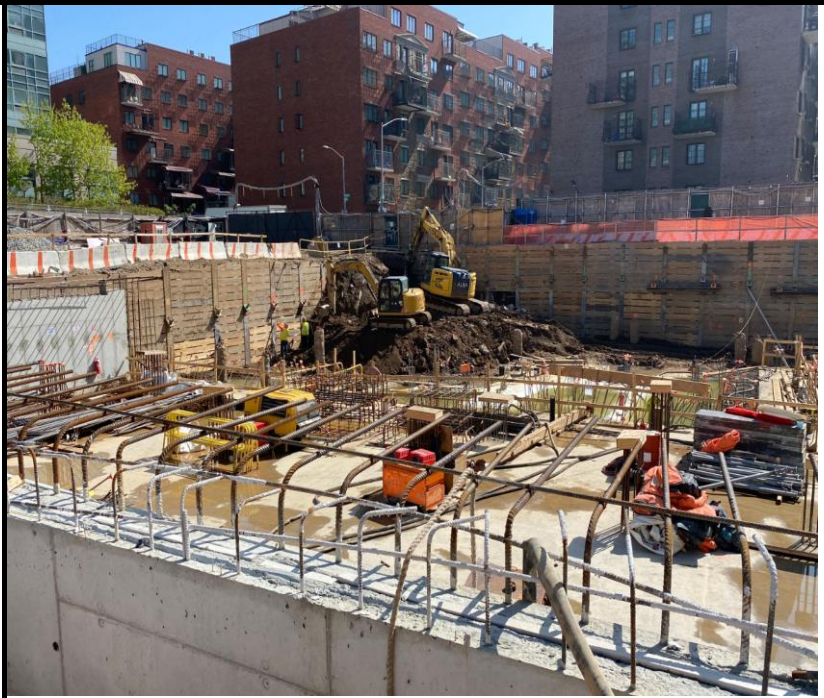


Photo 3:
View of Site
conditions facing
north.

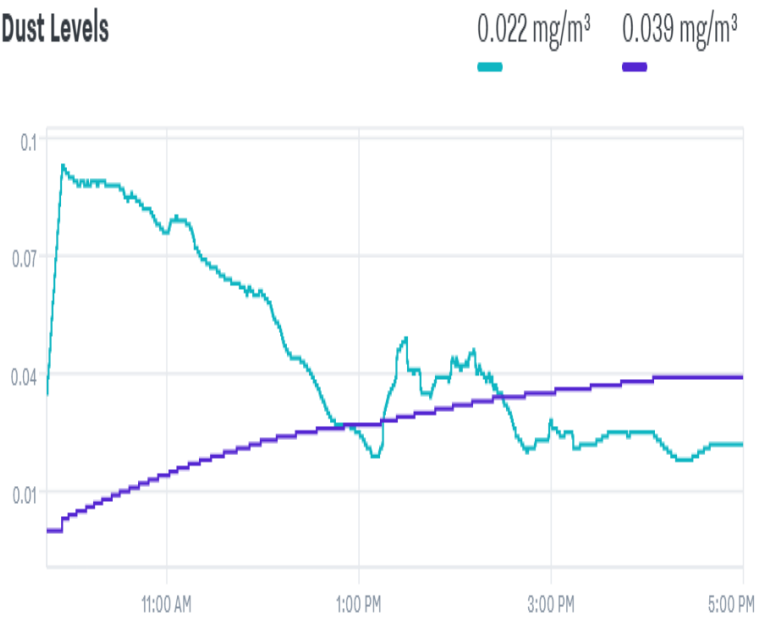


Photo 4:
View of additional
settling tank brought
on-site by GWTT,
the dewatering
contractor, for
additional sediment
removal.




CAMP:
Downwind
Particulates

Dust Levels



CAMP:
Downwind VOCs


VOC Levels

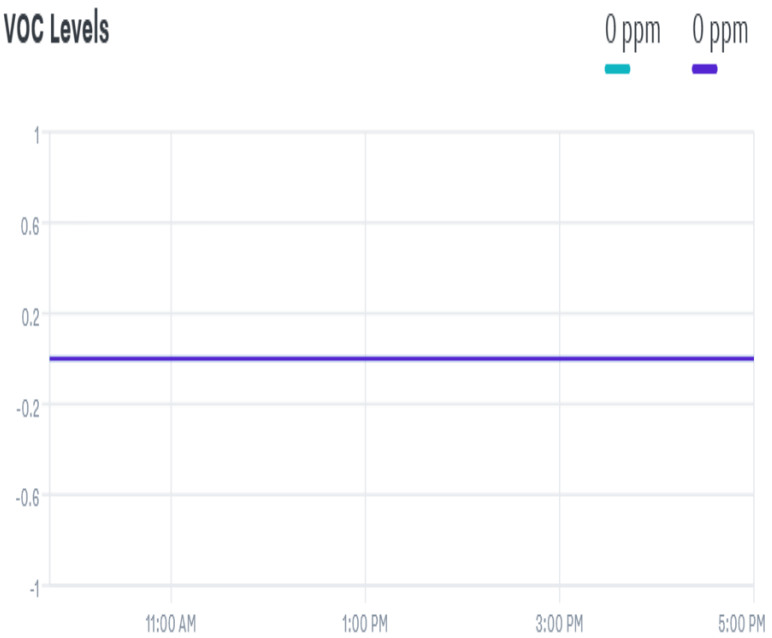

CAMP:
Upwind Particulates

Dust Levels


0.033 mg/m³ 0.05 mg/m³

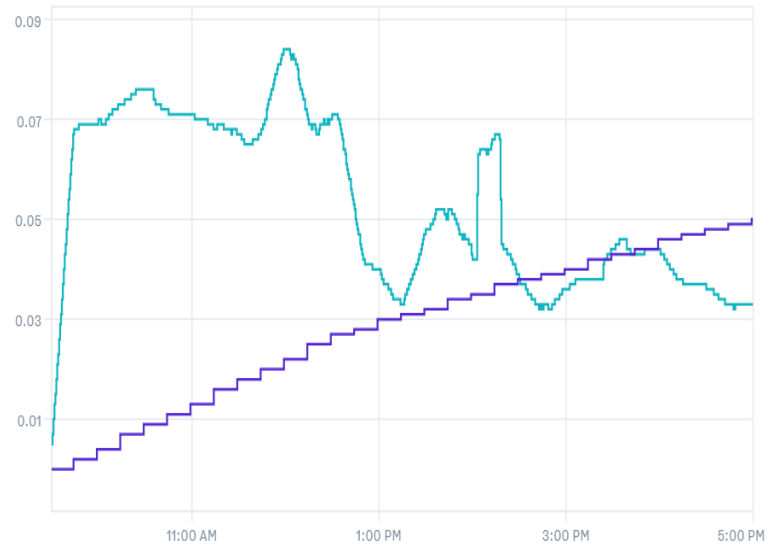

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

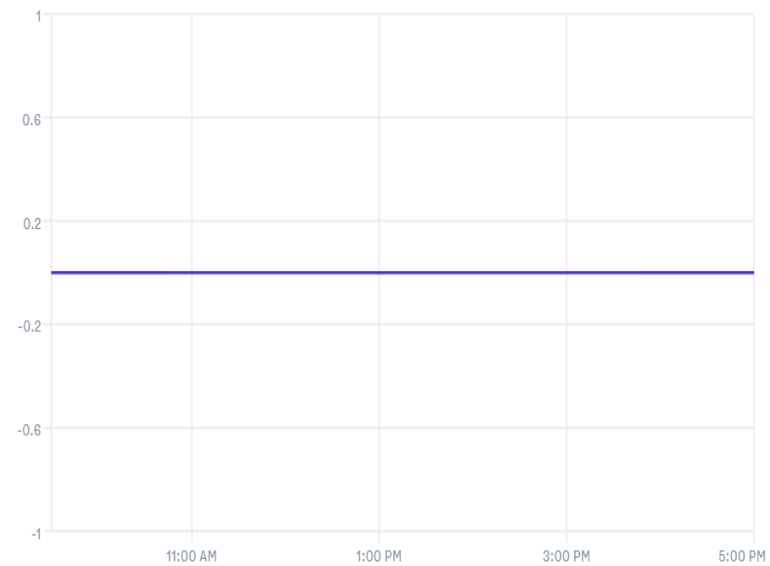

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/1/2024 9:40	5/1/2024 9:50	0.150	0	5	0
DW 2024	5/1/2024 9:50	5/1/2024 10:00	0.150	0.004	5	0
DW 2024	5/1/2024 10:00	5/1/2024 10:10	0.150	0.006	5	0
DW 2024	5/1/2024 10:10	5/1/2024 10:20	0.150	0.008	5	0
DW 2024	5/1/2024 10:20	5/1/2024 10:30	0.150	0.009	5	0
DW 2024	5/1/2024 10:30	5/1/2024 10:40	0.150	0.011	5	0
DW 2024	5/1/2024 10:40	5/1/2024 10:50	0.150	0.013	5	0
DW 2024	5/1/2024 10:50	5/1/2024 11:00	0.150	0.014	5	0
DW 2024	5/1/2024 11:00	5/1/2024 11:10	0.150	0.016	5	0
DW 2024	5/1/2024 11:10	5/1/2024 11:20	0.150	0.017	5	0
DW 2024	5/1/2024 11:20	5/1/2024 11:30	0.150	0.019	5	0
DW 2024	5/1/2024 11:30	5/1/2024 11:40	0.150	0.02	5	0
DW 2024	5/1/2024 11:40	5/1/2024 11:50	0.150	0.021	5	0
DW 2024	5/1/2024 11:50	5/1/2024 12:00	0.150	0.023	5	0
DW 2024	5/1/2024 12:00	5/1/2024 12:10	0.150	0.024	5	0
DW 2024	5/1/2024 12:10	5/1/2024 12:20	0.150	0.024	5	0
DW 2024	5/1/2024 12:20	5/1/2024 12:30	0.150	0.025	5	0
DW 2024	5/1/2024 12:30	5/1/2024 12:40	0.150	0.026	5	0
DW 2024	5/1/2024 12:40	5/1/2024 12:50	0.150	0.026	5	0
DW 2024	5/1/2024 12:50	5/1/2024 13:00	0.150	0.027	5	0
DW 2024	5/1/2024 13:00	5/1/2024 13:10	0.150	0.027	5	0
DW 2024	5/1/2024 13:10	5/1/2024 13:20	0.150	0.028	5	0
DW 2024	5/1/2024 13:20	5/1/2024 13:30	0.150	0.029	5	0
DW 2024	5/1/2024 13:30	5/1/2024 13:40	0.150	0.03	5	0
DW 2024	5/1/2024 13:40	5/1/2024 13:50	0.150	0.031	5	0
DW 2024	5/1/2024 13:50	5/1/2024 14:00	0.150	0.032	5	0
DW 2024	5/1/2024 14:00	5/1/2024 14:10	0.150	0.032	5	0
DW 2024	5/1/2024 14:10	5/1/2024 14:20	0.150	0.033	5	0
DW 2024	5/1/2024 14:20	5/1/2024 14:30	0.150	0.034	5	0
DW 2024	5/1/2024 14:30	5/1/2024 14:40	0.150	0.034	5	0
DW 2024	5/1/2024 14:40	5/1/2024 14:50	0.150	0.035	5	0
DW 2024	5/1/2024 14:50	5/1/2024 15:00	0.150	0.035	5	0
DW 2024	5/1/2024 15:00	5/1/2024 15:10	0.150	0.036	5	0
DW 2024	5/1/2024 15:10	5/1/2024 15:20	0.150	0.036	5	0
DW 2024	5/1/2024 15:20	5/1/2024 15:30	0.150	0.037	5	0
DW 2024	5/1/2024 15:30	5/1/2024 15:40	0.150	0.037	5	0
DW 2024	5/1/2024 15:40	5/1/2024 15:50	0.150	0.038	5	0
DW 2024	5/1/2024 15:50	5/1/2024 16:00	0.150	0.038	5	0
DW 2024	5/1/2024 16:00	5/1/2024 16:10	0.150	0.039	5	0
DW 2024	5/1/2024 16:10	5/1/2024 16:20	0.150	0.039	5	0
DW 2024	5/1/2024 16:20	5/1/2024 16:30	0.150	0.039	5	0
DW 2024	5/1/2024 16:30	5/1/2024 16:40	0.150	0.039	5	0
DW 2024	5/1/2024 16:40	5/1/2024 16:50	0.150	0.039	5	0
DW 2024	5/1/2024 16:50	5/1/2024 17:00	0.150	0.039	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/1/2024 9:30	5/1/2024 9:40	0.150	0	5	0
UW 2024	5/1/2024 9:40	5/1/2024 9:50	0.150	0.002	5	0
UW 2024	5/1/2024 9:50	5/1/2024 10:00	0.150	0.004	5	0
UW 2024	5/1/2024 10:00	5/1/2024 10:10	0.150	0.004	5	0
UW 2024	5/1/2024 10:10	5/1/2024 10:20	0.150	0.007	5	0
UW 2024	5/1/2024 10:20	5/1/2024 10:30	0.150	0.009	5	0
UW 2024	5/1/2024 10:30	5/1/2024 10:40	0.150	0.009	5	0
UW 2024	5/1/2024 10:40	5/1/2024 10:50	0.150	0.011	5	0
UW 2024	5/1/2024 10:50	5/1/2024 11:00	0.150	0.013	5	0
UW 2024	5/1/2024 11:00	5/1/2024 11:10	0.150	0.013	5	0
UW 2024	5/1/2024 11:10	5/1/2024 11:20	0.150	0.016	5	0
UW 2024	5/1/2024 11:20	5/1/2024 11:30	0.150	0.018	5	0
UW 2024	5/1/2024 11:30	5/1/2024 11:40	0.150	0.018	5	0
UW 2024	5/1/2024 11:40	5/1/2024 11:50	0.150	0.02	5	0
UW 2024	5/1/2024 11:50	5/1/2024 12:00	0.150	0.022	5	0
UW 2024	5/1/2024 12:00	5/1/2024 12:10	0.150	0.022	5	0
UW 2024	5/1/2024 12:10	5/1/2024 12:20	0.150	0.025	5	0
UW 2024	5/1/2024 12:20	5/1/2024 12:30	0.150	0.027	5	0
UW 2024	5/1/2024 12:30	5/1/2024 12:40	0.150	0.027	5	0
UW 2024	5/1/2024 12:40	5/1/2024 12:50	0.150	0.028	5	0
UW 2024	5/1/2024 12:50	5/1/2024 13:00	0.150	0.03	5	0
UW 2024	5/1/2024 13:00	5/1/2024 13:10	0.150	0.03	5	0
UW 2024	5/1/2024 13:10	5/1/2024 13:20	0.150	0.031	5	0
UW 2024	5/1/2024 13:20	5/1/2024 13:30	0.150	0.032	5	0
UW 2024	5/1/2024 13:30	5/1/2024 13:40	0.150	0.032	5	0
UW 2024	5/1/2024 13:40	5/1/2024 13:50	0.150	0.034	5	0
UW 2024	5/1/2024 13:50	5/1/2024 14:00	0.150	0.035	5	0
UW 2024	5/1/2024 14:00	5/1/2024 14:10	0.150	0.035	5	0
UW 2024	5/1/2024 14:10	5/1/2024 14:20	0.150	0.037	5	0
UW 2024	5/1/2024 14:20	5/1/2024 14:30	0.150	0.038	5	0
UW 2024	5/1/2024 14:30	5/1/2024 14:40	0.150	0.038	5	0
UW 2024	5/1/2024 14:40	5/1/2024 14:50	0.150	0.039	5	0
UW 2024	5/1/2024 14:50	5/1/2024 15:00	0.150	0.04	5	0
UW 2024	5/1/2024 15:00	5/1/2024 15:10	0.150	0.04	5	0
UW 2024	5/1/2024 15:10	5/1/2024 15:20	0.150	0.042	5	0
UW 2024	5/1/2024 15:20	5/1/2024 15:30	0.150	0.043	5	0
UW 2024	5/1/2024 15:30	5/1/2024 15:40	0.150	0.043	5	0
UW 2024	5/1/2024 15:40	5/1/2024 15:50	0.150	0.044	5	0
UW 2024	5/1/2024 15:50	5/1/2024 16:00	0.150	0.046	5	0
UW 2024	5/1/2024 16:00	5/1/2024 16:10	0.150	0.046	5	0
UW 2024	5/1/2024 16:10	5/1/2024 16:20	0.150	0.047	5	0
UW 2024	5/1/2024 16:20	5/1/2024 16:30	0.150	0.048	5	0
UW 2024	5/1/2024 16:30	5/1/2024 16:40	0.150	0.048	5	0
UW 2024	5/1/2024 16:40	5/1/2024 16:50	0.150	0.049	5	0
UW 2024	5/1/2024 16:50	5/1/2024 17:00	0.150	0.05	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/1/2024 10:10	5/1/2024 10:20	0.150	0	5	0
HS South	5/1/2024 10:20	5/1/2024 10:30	0.150	0.004	5	0
HS South	5/1/2024 10:30	5/1/2024 10:40	0.150	0.007	5	0
HS South	5/1/2024 10:40	5/1/2024 10:50	0.150	0.009	5	0
HS South	5/1/2024 10:50	5/1/2024 11:00	0.150	0.011	5	0
HS South	5/1/2024 11:00	5/1/2024 11:10	0.150	0.013	5	0
HS South	5/1/2024 11:10	5/1/2024 11:20	0.150	0.015	5	0
HS South	5/1/2024 11:20	5/1/2024 11:30	0.150	0.016	5	0
HS South	5/1/2024 11:30	5/1/2024 11:40	0.150	0.018	5	0
HS South	5/1/2024 11:40	5/1/2024 11:50	0.150	0.02	5	0
HS South	5/1/2024 11:50	5/1/2024 12:00	0.150	0.022	5	0
HS South	5/1/2024 12:00	5/1/2024 12:10	0.150	0.024	5	0
HS South	5/1/2024 12:10	5/1/2024 12:20	0.150	0.025	5	0
HS South	5/1/2024 12:20	5/1/2024 12:30	0.150	0.027	5	0
HS South	5/1/2024 12:30	5/1/2024 12:40	0.150	0.028	5	0
HS South	5/1/2024 12:40	5/1/2024 12:50	0.150	0.029	5	0
HS South	5/1/2024 12:50	5/1/2024 13:00	0.150	0.03	5	0
HS South	5/1/2024 13:00	5/1/2024 13:10	0.150	0.031	5	0
HS South	5/1/2024 13:10	5/1/2024 13:20	0.150	0.032	5	0
HS South	5/1/2024 13:20	5/1/2024 13:30	0.150	0.034	5	0
HS South	5/1/2024 13:30	5/1/2024 13:40	0.150	0.035	5	0
HS South	5/1/2024 13:40	5/1/2024 13:50	0.150	0.036	5	0
HS South	5/1/2024 13:50	5/1/2024 14:00	0.150	0.038	5	0
HS South	5/1/2024 14:00	5/1/2024 14:10	0.150	0.04	5	0
HS South	5/1/2024 14:10	5/1/2024 14:20	0.150	0.041	5	0
HS South	5/1/2024 14:20	5/1/2024 14:30	0.150	0.042	5	0
HS South	5/1/2024 14:30	5/1/2024 14:40	0.150	0.044	5	0
HS South	5/1/2024 14:40	5/1/2024 14:50	0.150	0.045	5	0
HS South	5/1/2024 14:50	5/1/2024 15:00	0.150	0.046	5	0
HS South	5/1/2024 15:00	5/1/2024 15:10	0.150	0.047	5	0
HS South	5/1/2024 15:10	5/1/2024 15:20	0.150	0.049	5	0
HS South	5/1/2024 15:20	5/1/2024 15:30	0.150	0.05	5	0
HS South	5/1/2024 15:30	5/1/2024 15:40	0.150	0.052	5	0
HS South	5/1/2024 15:40	5/1/2024 15:50	0.150	0.053	5	0
HS South	5/1/2024 15:50	5/1/2024 16:00	0.150	0.054	5	0
HS South	5/1/2024 16:00	5/1/2024 16:10	0.150	0.056	5	0
HS South	5/1/2024 16:10	5/1/2024 16:20	0.150	0.057	5	0
HS South	5/1/2024 16:20	5/1/2024 16:30	0.150	0.057	5	0
HS South	5/1/2024 16:30	5/1/2024 16:40	0.150	0.057	5	0
HS South	5/1/2024 16:40	5/1/2024 16:50	0.150	0.057	5	0
HS South	5/1/2024 16:50	5/1/2024 17:00	0.150	0.057	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/1/2024 9:50	5/1/2024 10:00	0.150	0.024	5	0
PER2 2024	5/1/2024 10:00	5/1/2024 10:10	0.150	0.006	5	0
PER2 2024	5/1/2024 10:10	5/1/2024 10:20	0.150	0.008	5	0
PER2 2024	5/1/2024 10:20	5/1/2024 10:30	0.150	0.009	5	0
PER2 2024	5/1/2024 10:30	5/1/2024 10:40	0.150	0.011	5	0
PER2 2024	5/1/2024 10:40	5/1/2024 10:50	0.150	0.012	5	0
PER2 2024	5/1/2024 10:50	5/1/2024 11:00	0.150	0.014	5	0
PER2 2024	5/1/2024 11:00	5/1/2024 11:10	0.150	0.015	5	0
PER2 2024	5/1/2024 11:10	5/1/2024 11:20	0.150	0.017	5	0
PER2 2024	5/1/2024 11:20	5/1/2024 11:30	0.150	0.018	5	0
PER2 2024	5/1/2024 11:30	5/1/2024 11:40	0.150	0.019	5	0
PER2 2024	5/1/2024 11:40	5/1/2024 11:50	0.150	0.02	5	0
PER2 2024	5/1/2024 11:50	5/1/2024 12:00	0.150	0.021	5	0
PER2 2024	5/1/2024 12:00	5/1/2024 12:10	0.150	0.023	5	0
PER2 2024	5/1/2024 12:10	5/1/2024 12:20	0.150	0.024	5	0
PER2 2024	5/1/2024 12:20	5/1/2024 12:30	0.150	0.024	5	0
PER2 2024	5/1/2024 12:30	5/1/2024 12:40	0.150	0.025	5	0
PER2 2024	5/1/2024 12:40	5/1/2024 12:50	0.150	0.026	5	0
PER2 2024	5/1/2024 12:50	5/1/2024 13:00	0.150	0.027	5	0
PER2 2024	5/1/2024 13:00	5/1/2024 13:10	0.150	0.027	5	0
PER2 2024	5/1/2024 13:10	5/1/2024 13:20	0.150	0.028	5	0
PER2 2024	5/1/2024 13:20	5/1/2024 13:30	0.150	0.029	5	0
PER2 2024	5/1/2024 13:30	5/1/2024 13:40	0.150	0.029	5	0
PER2 2024	5/1/2024 13:40	5/1/2024 13:50	0.150	0.03	5	0
PER2 2024	5/1/2024 13:50	5/1/2024 14:00	0.150	0.031	5	0
PER2 2024	5/1/2024 14:00	5/1/2024 14:10	0.150	0.032	5	0
PER2 2024	5/1/2024 14:10	5/1/2024 14:20	0.150	0.033	5	0
PER2 2024	5/1/2024 14:20	5/1/2024 14:30	0.150	0.034	5	0
PER2 2024	5/1/2024 14:30	5/1/2024 14:40	0.150	0.034	5	0
PER2 2024	5/1/2024 14:40	5/1/2024 14:50	0.150	0.035	5	0
PER2 2024	5/1/2024 14:50	5/1/2024 15:00	0.150	0.036	5	0
PER2 2024	5/1/2024 15:00	5/1/2024 15:10	0.150	0.036	5	0
PER2 2024	5/1/2024 15:10	5/1/2024 15:20	0.150	0.037	5	0
PER2 2024	5/1/2024 15:20	5/1/2024 15:30	0.150	0.037	5	0
PER2 2024	5/1/2024 15:30	5/1/2024 15:40	0.150	0.037	5	0
PER2 2024	5/1/2024 15:40	5/1/2024 15:50	0.150	0.037	5	0
PER2 2024	5/1/2024 15:50	5/1/2024 16:00	0.150	0.037	5	0
PER2 2024	5/1/2024 16:00	5/1/2024 16:10	0.150	0.037	5	0
PER2 2024	5/1/2024 16:10	5/1/2024 16:20	0.150	0.037	5	0
PER2 2024	5/1/2024 16:20	5/1/2024 16:30	0.150	0.037	5	0
PER2 2024	5/1/2024 16:30	5/1/2024 16:40	0.150	0.037	5	0
PER2 2024	5/1/2024 16:40	5/1/2024 16:50	0.150	0.037	5	0
PER2 2024	5/1/2024 16:50	5/1/2024 17:00	0.150	0.037	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/1/2024 10:00	5/1/2024 10:10	0.150	0	5	0
PER1 2024	5/1/2024 10:10	5/1/2024 10:20	0.150	0.004	5	0
PER1 2024	5/1/2024 10:20	5/1/2024 10:30	0.150	0.006	5	0
PER1 2024	5/1/2024 10:30	5/1/2024 10:40	0.150	0.007	5	0
PER1 2024	5/1/2024 10:40	5/1/2024 10:50	0.150	0.008	5	0
PER1 2024	5/1/2024 10:50	5/1/2024 11:00	0.150	0.009	5	0
PER1 2024	5/1/2024 11:00	5/1/2024 11:10	0.150	0.011	5	0
PER1 2024	5/1/2024 11:10	5/1/2024 11:20	0.150	0.012	5	0
PER1 2024	5/1/2024 11:20	5/1/2024 11:30	0.150	0.013	5	0
PER1 2024	5/1/2024 11:30	5/1/2024 11:40	0.150	0.014	5	0
PER1 2024	5/1/2024 11:40	5/1/2024 11:50	0.150	0.015	5	0
PER1 2024	5/1/2024 11:50	5/1/2024 12:00	0.150	0.016	5	0
PER1 2024	5/1/2024 12:00	5/1/2024 12:10	0.150	0.016	5	0
PER1 2024	5/1/2024 12:10	5/1/2024 12:20	0.150	0.017	5	0
PER1 2024	5/1/2024 12:20	5/1/2024 12:30	0.150	0.018	5	0
PER1 2024	5/1/2024 12:30	5/1/2024 12:40	0.150	0.018	5	0
PER1 2024	5/1/2024 12:40	5/1/2024 12:50	0.150	0.019	5	0
PER1 2024	5/1/2024 12:50	5/1/2024 13:00	0.150	0.019	5	0
PER1 2024	5/1/2024 13:00	5/1/2024 13:10	0.150	0.02	5	0
PER1 2024	5/1/2024 13:10	5/1/2024 13:20	0.150	0.021	5	0
PER1 2024	5/1/2024 13:20	5/1/2024 13:30	0.150	0.021	5	0
PER1 2024	5/1/2024 13:30	5/1/2024 13:40	0.150	0.022	5	0
PER1 2024	5/1/2024 13:40	5/1/2024 13:50	0.150	0.022	5	0
PER1 2024	5/1/2024 13:50	5/1/2024 14:00	0.150	0.023	5	0
PER1 2024	5/1/2024 14:00	5/1/2024 14:10	0.150	0.023	5	0
PER1 2024	5/1/2024 14:10	5/1/2024 14:20	0.150	0.024	5	0
PER1 2024	5/1/2024 14:20	5/1/2024 14:30	0.150	0.024	5	0
PER1 2024	5/1/2024 14:30	5/1/2024 14:40	0.150	0.025	5	0
PER1 2024	5/1/2024 14:40	5/1/2024 14:50	0.150	0.025	5	0
PER1 2024	5/1/2024 14:50	5/1/2024 15:00	0.150	0.025	5	0
PER1 2024	5/1/2024 15:00	5/1/2024 15:10	0.150	0.026	5	0
PER1 2024	5/1/2024 15:10	5/1/2024 15:20	0.150	0.026	5	0
PER1 2024	5/1/2024 15:20	5/1/2024 15:30	0.150	0.027	5	0
PER1 2024	5/1/2024 15:30	5/1/2024 15:40	0.150	0.027	5	0
PER1 2024	5/1/2024 15:40	5/1/2024 15:50	0.150	0.028	5	0
PER1 2024	5/1/2024 15:50	5/1/2024 16:00	0.150	0.029	5	0
PER1 2024	5/1/2024 16:00	5/1/2024 16:10	0.150	0.029	5	0
PER1 2024	5/1/2024 16:10	5/1/2024 16:20	0.150	0.03	5	0
PER1 2024	5/1/2024 16:20	5/1/2024 16:30	0.150	0.03	5	0
PER1 2024	5/1/2024 16:30	5/1/2024 16:40	0.150	0	5	0
PER1 2024	5/1/2024 16:40	5/1/2024 16:50	0.150	0	5	0
PER1 2024	5/1/2024 16:50	5/1/2024 17:00	0.150	0	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/02/2024

Weather: 80 deg. F, Clear/overcast


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development. 2) Export 8 loads (~160 CY) of material from WC-27 for off-site disposal at the MCUA facility. 3) The NYSDEC Department of Water was on-site to complete a follow-up inspection after the NYSDEC Environmental Conservation Police Officer visit on 4/30.	
Is the dewatering system operating: YES NO *see below	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: *Maintenance was completed on the dewatering system and the system was restarted in the morning.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	160
Total:(CY)	4485	0	8365	1520	4140

Site Layout Map and Excavation Figures

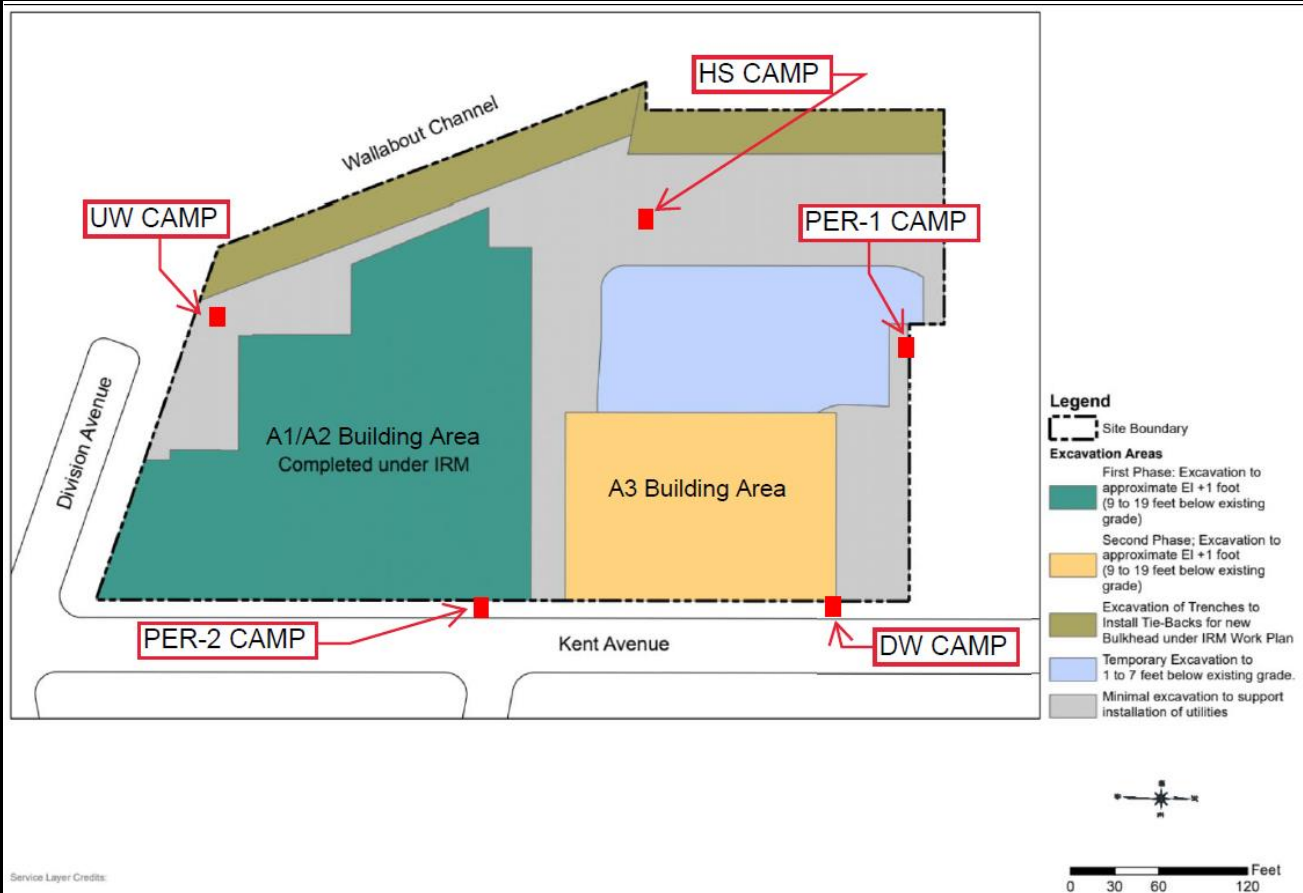

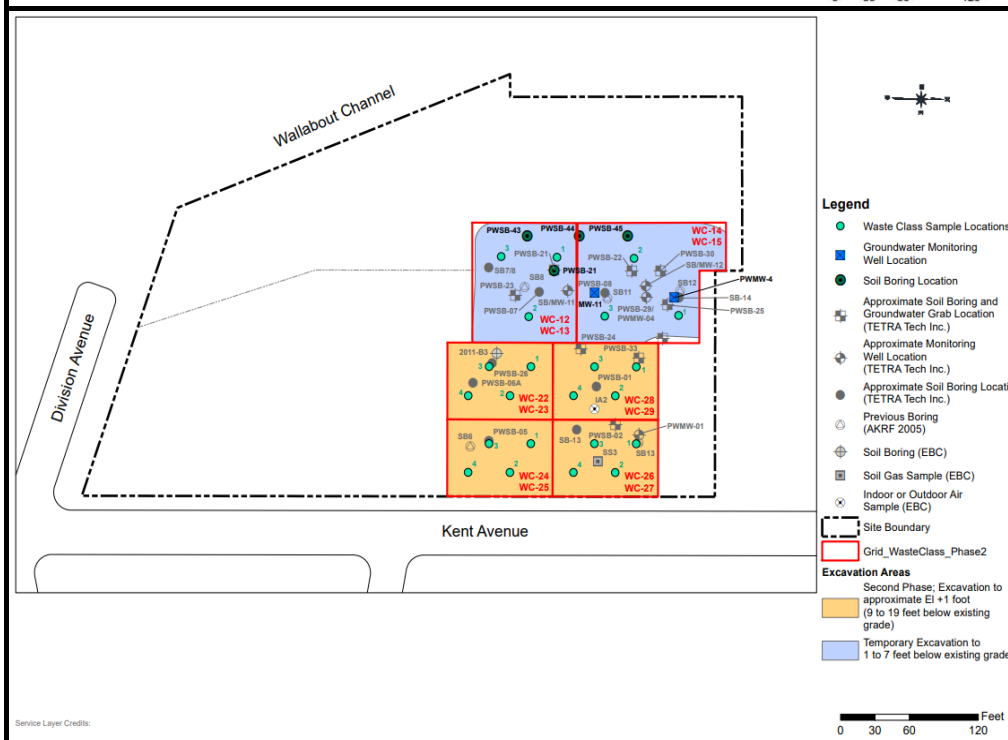
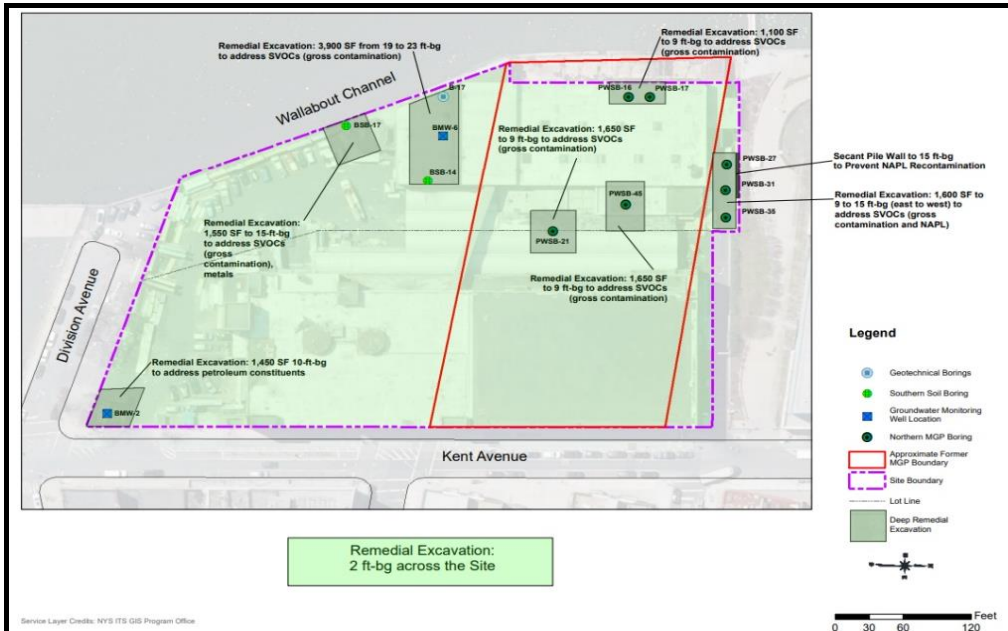


Photo 1:
View of Site conditions
and activities facing
southeast.



Photo 2:
View of soil excavation
and truck loading for off-
site soil disposal.



Photo 3:
View of the
dewatering effluent,
following system
maintenance
completion.




Photo 4:
View of soil
excavation facing
east.



CAMP:
Downwind
Particulates

Dust Levels


0.043 mg/m³ 0.047 mg/m³

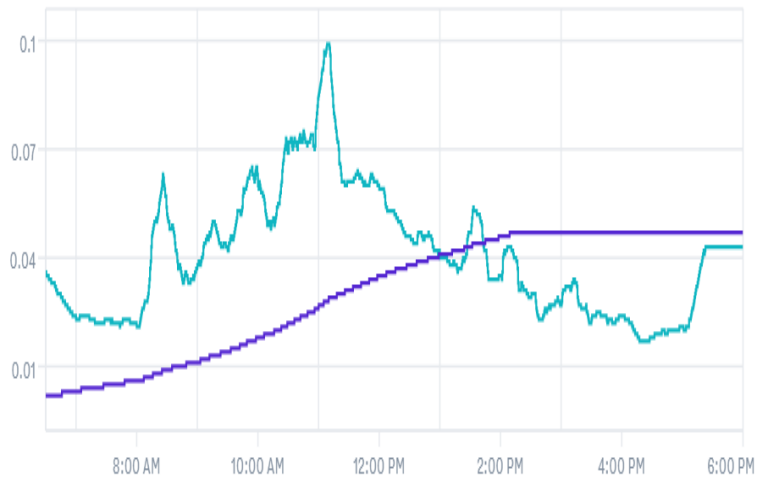

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm

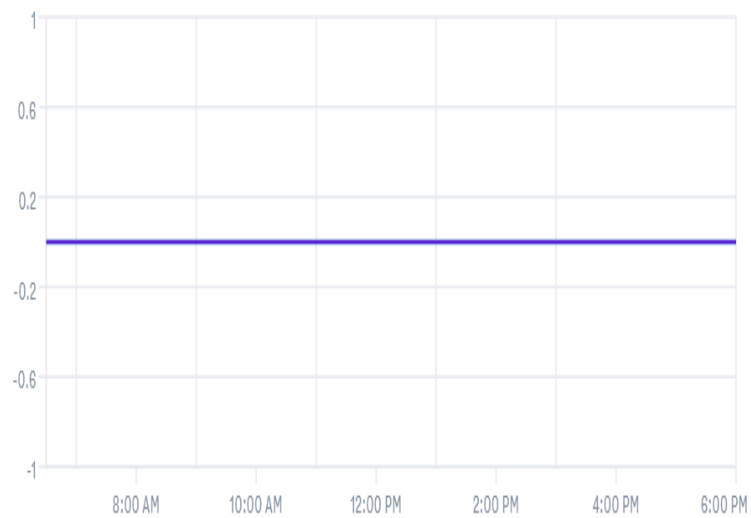

CAMP:
Upwind Particulates

Dust Levels


0.038 mg/m³ 0.048 mg/m³

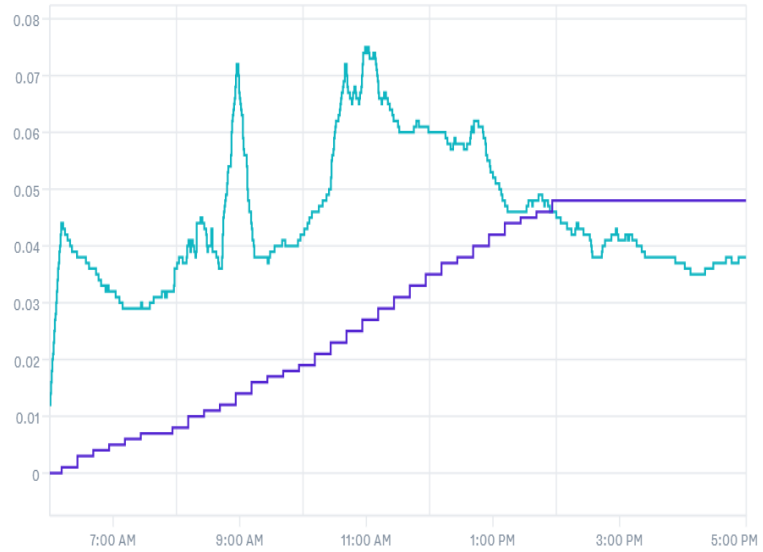

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

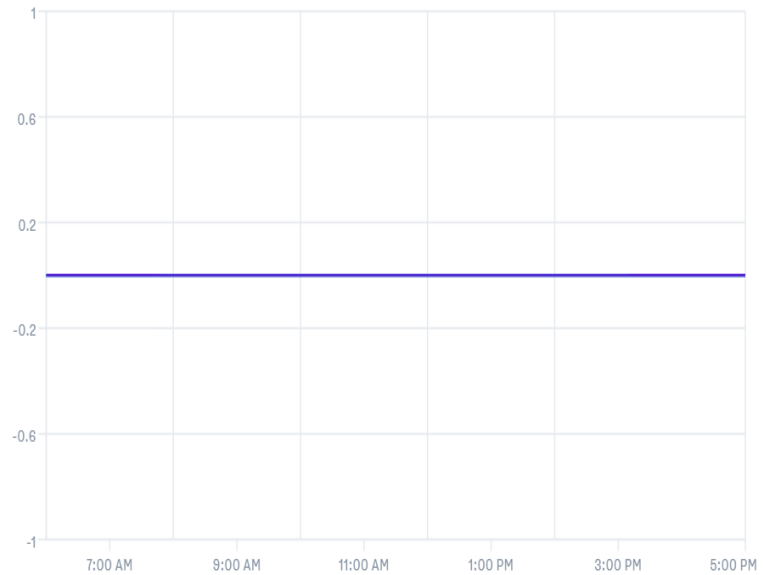

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/2/2024 6:00	5/2/2024 6:10	0.150	0	5	0
DW 2024	5/2/2024 6:10	5/2/2024 6:20	0.150	0	5	0
DW 2024	5/2/2024 6:20	5/2/2024 6:30	0.150	0.002	5	0
DW 2024	5/2/2024 6:30	5/2/2024 6:40	0.150	0.002	5	0
DW 2024	5/2/2024 6:40	5/2/2024 6:50	0.150	0.003	5	0
DW 2024	5/2/2024 6:50	5/2/2024 7:00	0.150	0.003	5	0
DW 2024	5/2/2024 7:00	5/2/2024 7:10	0.150	0.004	5	0
DW 2024	5/2/2024 7:10	5/2/2024 7:20	0.150	0.004	5	0
DW 2024	5/2/2024 7:20	5/2/2024 7:30	0.150	0.005	5	0
DW 2024	5/2/2024 7:30	5/2/2024 7:40	0.150	0.005	5	0
DW 2024	5/2/2024 7:40	5/2/2024 7:50	0.150	0.006	5	0
DW 2024	5/2/2024 7:50	5/2/2024 8:00	0.150	0.006	5	0
DW 2024	5/2/2024 8:00	5/2/2024 8:10	0.150	0.007	5	0
DW 2024	5/2/2024 8:10	5/2/2024 8:20	0.150	0.008	5	0
DW 2024	5/2/2024 8:20	5/2/2024 8:30	0.150	0.009	5	0
DW 2024	5/2/2024 8:30	5/2/2024 8:40	0.150	0.01	5	0
DW 2024	5/2/2024 8:40	5/2/2024 8:50	0.150	0.011	5	0
DW 2024	5/2/2024 8:50	5/2/2024 9:00	0.150	0.011	5	0
DW 2024	5/2/2024 9:00	5/2/2024 9:10	0.150	0.012	5	0
DW 2024	5/2/2024 9:10	5/2/2024 9:20	0.150	0.013	5	0
DW 2024	5/2/2024 9:20	5/2/2024 9:30	0.150	0.014	5	0
DW 2024	5/2/2024 9:30	5/2/2024 9:40	0.150	0.015	5	0
DW 2024	5/2/2024 9:40	5/2/2024 9:50	0.150	0.017	5	0
DW 2024	5/2/2024 9:50	5/2/2024 10:00	0.150	0.018	5	0
DW 2024	5/2/2024 10:00	5/2/2024 10:10	0.150	0.019	5	0
DW 2024	5/2/2024 10:10	5/2/2024 10:20	0.150	0.02	5	0
DW 2024	5/2/2024 10:20	5/2/2024 10:30	0.150	0.022	5	0
DW 2024	5/2/2024 10:30	5/2/2024 10:40	0.150	0.023	5	0
DW 2024	5/2/2024 10:40	5/2/2024 10:50	0.150	0.025	5	0
DW 2024	5/2/2024 10:50	5/2/2024 11:00	0.150	0.026	5	0
DW 2024	5/2/2024 11:00	5/2/2024 11:10	0.150	0.028	5	0
DW 2024	5/2/2024 11:10	5/2/2024 11:20	0.150	0.03	5	0
DW 2024	5/2/2024 11:20	5/2/2024 11:30	0.150	0.031	5	0
DW 2024	5/2/2024 11:30	5/2/2024 11:40	0.150	0.032	5	0
DW 2024	5/2/2024 11:40	5/2/2024 11:50	0.150	0.033	5	0
DW 2024	5/2/2024 11:50	5/2/2024 12:00	0.150	0.035	5	0
DW 2024	5/2/2024 12:00	5/2/2024 12:10	0.150	0.036	5	0
DW 2024	5/2/2024 12:10	5/2/2024 12:20	0.150	0.037	5	0
DW 2024	5/2/2024 12:20	5/2/2024 12:30	0.150	0.038	5	0
DW 2024	5/2/2024 12:30	5/2/2024 12:40	0.150	0.039	5	0
DW 2024	5/2/2024 12:40	5/2/2024 12:50	0.150	0.04	5	0
DW 2024	5/2/2024 12:50	5/2/2024 13:00	0.150	0.041	5	0
DW 2024	5/2/2024 13:00	5/2/2024 13:10	0.150	0.041	5	0
DW 2024	5/2/2024 13:10	5/2/2024 13:20	0.150	0.042	5	0
DW 2024	5/2/2024 13:20	5/2/2024 13:30	0.150	0.043	5	0
DW 2024	5/2/2024 13:30	5/2/2024 13:40	0.150	0.044	5	0
DW 2024	5/2/2024 13:40	5/2/2024 13:50	0.150	0.045	5	0
DW 2024	5/2/2024 13:50	5/2/2024 14:00	0.150	0.046	5	0
DW 2024	5/2/2024 14:00	5/2/2024 14:10	0.150	0.047	5	0
DW 2024	5/2/2024 14:10	5/2/2024 14:20	0.150	0.047	5	0
DW 2024	5/2/2024 14:20	5/2/2024 14:30	0.150	0.047	5	0
DW 2024	5/2/2024 14:30	5/2/2024 14:40	0.150	0.047	5	0
DW 2024	5/2/2024 14:40	5/2/2024 14:50	0.150	0.047	5	0
DW 2024	5/2/2024 14:50	5/2/2024 15:00	0.150	0.047	5	0
DW 2024	5/2/2024 15:00	5/2/2024 15:10	0.150	0.047	5	0
DW 2024	5/2/2024 15:10	5/2/2024 15:20	0.150	0.047	5	0
DW 2024	5/2/2024 15:20	5/2/2024 15:30	0.150	0.047	5	0
DW 2024	5/2/2024 15:30	5/2/2024 15:40	0.150	0.047	5	0
DW 2024	5/2/2024 15:40	5/2/2024 15:50	0.150	0.047	5	0
DW 2024	5/2/2024 15:50	5/2/2024 16:00	0.150	0.047	5	0
DW 2024	5/2/2024 16:00	5/2/2024 16:10	0.150	0.047	5	0
DW 2024	5/2/2024 16:10	5/2/2024 16:20	0.150	0.047	5	0
DW 2024	5/2/2024 16:20	5/2/2024 16:30	0.150	0.047	5	0
DW 2024	5/2/2024 16:30	5/2/2024 16:40	0.150	0.047	5	0
DW 2024	5/2/2024 16:40	5/2/2024 16:50	0.150	0.047	5	0
DW 2024	5/2/2024 16:50	5/2/2024 17:00	0.150	0.047	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/2/2024 6:00	5/2/2024 6:10	0.150	0	5	0
UW 2024	5/2/2024 6:10	5/2/2024 6:20	0.150	0.001	5	0
UW 2024	5/2/2024 6:20	5/2/2024 6:30	0.150	0.003	5	0
UW 2024	5/2/2024 6:30	5/2/2024 6:40	0.150	0.003	5	0
UW 2024	5/2/2024 6:40	5/2/2024 6:50	0.150	0.004	5	0
UW 2024	5/2/2024 6:50	5/2/2024 7:00	0.150	0.005	5	0
UW 2024	5/2/2024 7:00	5/2/2024 7:10	0.150	0.005	5	0
UW 2024	5/2/2024 7:10	5/2/2024 7:20	0.150	0.006	5	0
UW 2024	5/2/2024 7:20	5/2/2024 7:30	0.150	0.007	5	0
UW 2024	5/2/2024 7:30	5/2/2024 7:40	0.150	0.007	5	0
UW 2024	5/2/2024 7:40	5/2/2024 7:50	0.150	0.007	5	0
UW 2024	5/2/2024 7:50	5/2/2024 8:00	0.150	0.008	5	0
UW 2024	5/2/2024 8:00	5/2/2024 8:10	0.150	0.008	5	0
UW 2024	5/2/2024 8:10	5/2/2024 8:20	0.150	0.01	5	0
UW 2024	5/2/2024 8:20	5/2/2024 8:30	0.150	0.011	5	0
UW 2024	5/2/2024 8:30	5/2/2024 8:40	0.150	0.011	5	0
UW 2024	5/2/2024 8:40	5/2/2024 8:50	0.150	0.012	5	0
UW 2024	5/2/2024 8:50	5/2/2024 9:00	0.150	0.014	5	0
UW 2024	5/2/2024 9:00	5/2/2024 9:10	0.150	0.014	5	0
UW 2024	5/2/2024 9:10	5/2/2024 9:20	0.150	0.016	5	0
UW 2024	5/2/2024 9:20	5/2/2024 9:30	0.150	0.017	5	0
UW 2024	5/2/2024 9:30	5/2/2024 9:40	0.150	0.017	5	0
UW 2024	5/2/2024 9:40	5/2/2024 9:50	0.150	0.018	5	0
UW 2024	5/2/2024 9:50	5/2/2024 10:00	0.150	0.019	5	0
UW 2024	5/2/2024 10:00	5/2/2024 10:10	0.150	0.019	5	0
UW 2024	5/2/2024 10:10	5/2/2024 10:20	0.150	0.021	5	0
UW 2024	5/2/2024 10:20	5/2/2024 10:30	0.150	0.023	5	0
UW 2024	5/2/2024 10:30	5/2/2024 10:40	0.150	0.023	5	0
UW 2024	5/2/2024 10:40	5/2/2024 10:50	0.150	0.025	5	0
UW 2024	5/2/2024 10:50	5/2/2024 11:00	0.150	0.027	5	0
UW 2024	5/2/2024 11:00	5/2/2024 11:10	0.150	0.027	5	0
UW 2024	5/2/2024 11:10	5/2/2024 11:20	0.150	0.029	5	0
UW 2024	5/2/2024 11:20	5/2/2024 11:30	0.150	0.031	5	0
UW 2024	5/2/2024 11:30	5/2/2024 11:40	0.150	0.031	5	0
UW 2024	5/2/2024 11:40	5/2/2024 11:50	0.150	0.033	5	0
UW 2024	5/2/2024 11:50	5/2/2024 12:00	0.150	0.035	5	0
UW 2024	5/2/2024 12:00	5/2/2024 12:10	0.150	0.035	5	0
UW 2024	5/2/2024 12:10	5/2/2024 12:20	0.150	0.037	5	0
UW 2024	5/2/2024 12:20	5/2/2024 12:30	0.150	0.038	5	0
UW 2024	5/2/2024 12:30	5/2/2024 12:40	0.150	0.038	5	0
UW 2024	5/2/2024 12:40	5/2/2024 12:50	0.150	0.04	5	0
UW 2024	5/2/2024 12:50	5/2/2024 13:00	0.150	0.042	5	0
UW 2024	5/2/2024 13:00	5/2/2024 13:10	0.150	0.042	5	0
UW 2024	5/2/2024 13:10	5/2/2024 13:20	0.150	0.044	5	0
UW 2024	5/2/2024 13:20	5/2/2024 13:30	0.150	0.045	5	0
UW 2024	5/2/2024 13:30	5/2/2024 13:40	0.150	0.045	5	0
UW 2024	5/2/2024 13:40	5/2/2024 13:50	0.150	0.046	5	0
UW 2024	5/2/2024 13:50	5/2/2024 14:00	0.150	0.048	5	0
UW 2024	5/2/2024 14:00	5/2/2024 14:10	0.150	0.048	5	0
UW 2024	5/2/2024 14:10	5/2/2024 14:20	0.150	0.048	5	0
UW 2024	5/2/2024 14:20	5/2/2024 14:30	0.150	0.048	5	0
UW 2024	5/2/2024 14:30	5/2/2024 14:40	0.150	0.048	5	0
UW 2024	5/2/2024 14:40	5/2/2024 14:50	0.150	0.048	5	0
UW 2024	5/2/2024 14:50	5/2/2024 15:00	0.150	0.048	5	0
UW 2024	5/2/2024 15:00	5/2/2024 15:10	0.150	0.048	5	0
UW 2024	5/2/2024 15:10	5/2/2024 15:20	0.150	0.048	5	0
UW 2024	5/2/2024 15:20	5/2/2024 15:30	0.150	0.048	5	0
UW 2024	5/2/2024 15:30	5/2/2024 15:40	0.150	0.048	5	0
UW 2024	5/2/2024 15:40	5/2/2024 15:50	0.150	0.048	5	0
UW 2024	5/2/2024 15:50	5/2/2024 16:00	0.150	0.048	5	0
UW 2024	5/2/2024 16:00	5/2/2024 16:10	0.150	0.048	5	0
UW 2024	5/2/2024 16:10	5/2/2024 16:20	0.150	0.048	5	0
UW 2024	5/2/2024 16:20	5/2/2024 16:30	0.150	0.048	5	0
UW 2024	5/2/2024 16:30	5/2/2024 16:40	0.150	0.048	5	0
UW 2024	5/2/2024 16:40	5/2/2024 16:50	0.150	0.048	5	0
UW 2024	5/2/2024 16:50	5/2/2024 17:00	0.150	0.048	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/2/2024 6:20	5/2/2024 6:30	0.150	0	5	0.015
HS South	5/2/2024 6:30	5/2/2024 6:40	0.150	0.002	5	0.015
HS South	5/2/2024 6:40	5/2/2024 6:50	0.150	0.003	5	0.015
HS South	5/2/2024 6:50	5/2/2024 7:00	0.150	0.004	5	0.015
HS South	5/2/2024 7:00	5/2/2024 7:10	0.150	0.004	5	0.015
HS South	5/2/2024 7:10	5/2/2024 7:20	0.150	0.005	5	0.015
HS South	5/2/2024 7:20	5/2/2024 7:30	0.150	0.006	5	0.015
HS South	5/2/2024 7:30	5/2/2024 7:40	0.150	0.006	5	0.015
HS South	5/2/2024 7:40	5/2/2024 7:50	0.150	0.007	5	0.015
HS South	5/2/2024 7:50	5/2/2024 8:00	0.150	0.008	5	0.015
HS South	5/2/2024 8:00	5/2/2024 8:10	0.150	0.009	5	0.015
HS South	5/2/2024 8:10	5/2/2024 8:20	0.150	0.01	5	0.015
HS South	5/2/2024 8:20	5/2/2024 8:30	0.150	0.011	5	0.015
HS South	5/2/2024 8:30	5/2/2024 8:40	0.150	0.011	5	0.015
HS South	5/2/2024 8:40	5/2/2024 8:50	0.150	0.012	5	0.015
HS South	5/2/2024 8:50	5/2/2024 9:00	0.150	0.013	5	0.015
HS South	5/2/2024 9:00	5/2/2024 9:10	0.150	0.014	5	0.015
HS South	5/2/2024 9:10	5/2/2024 9:20	0.150	0.015	5	0.015
HS South	5/2/2024 9:20	5/2/2024 9:30	0.150	0.016	5	0.015
HS South	5/2/2024 9:30	5/2/2024 9:40	0.150	0.017	5	0.015
HS South	5/2/2024 9:40	5/2/2024 9:50	0.150	0.018	5	0.015
HS South	5/2/2024 9:50	5/2/2024 10:00	0.150	0.02	5	0.015
HS South	5/2/2024 10:00	5/2/2024 10:10	0.150	0.021	5	0.015
HS South	5/2/2024 10:10	5/2/2024 10:20	0.150	0.022	5	0.015
HS South	5/2/2024 10:20	5/2/2024 10:30	0.150	0.024	5	0.015
HS South	5/2/2024 10:30	5/2/2024 10:40	0.150	0.026	5	0.015
HS South	5/2/2024 10:40	5/2/2024 10:50	0.150	0.028	5	0.015
HS South	5/2/2024 10:50	5/2/2024 11:00	0.150	0.03	5	0.015
HS South	5/2/2024 11:00	5/2/2024 11:10	0.150	0.032	5	0.015
HS South	5/2/2024 11:10	5/2/2024 11:20	0.150	0.032	5	0.015
HS South	5/2/2024 11:20	5/2/2024 11:30	0.150	0.032	5	0.015
HS South	5/2/2024 11:30	5/2/2024 11:40	0.150	0.032	5	0.015
HS South	5/2/2024 11:40	5/2/2024 11:50	0.150	0.032	5	0.015
HS South	5/2/2024 11:50	5/2/2024 12:00	0.150	0.032	5	0.015
HS South	5/2/2024 12:00	5/2/2024 12:10	0.150	0.032	5	0.015
HS South	5/2/2024 12:10	5/2/2024 12:20	0.150	0.032	5	0.015
HS South	5/2/2024 12:20	5/2/2024 12:30	0.150	0.032	5	0.015
HS South	5/2/2024 12:30	5/2/2024 12:40	0.150	0.032	5	0.015
HS South	5/2/2024 12:40	5/2/2024 12:50	0.150	0.032	5	0.015
HS South	5/2/2024 12:50	5/2/2024 13:00	0.150	0.032	5	0.015
HS South	5/2/2024 13:00	5/2/2024 13:10	0.150	0.053	5	0.015
HS South	5/2/2024 13:10	5/2/2024 13:20	0.150	0.056	5	0.015
HS South	5/2/2024 13:20	5/2/2024 13:30	0.150	0.058	5	0.015
HS South	5/2/2024 13:30	5/2/2024 13:40	0.150	0.06	5	0.015
HS South	5/2/2024 13:40	5/2/2024 13:50	0.150	0.062	5	0.015
HS South	5/2/2024 13:50	5/2/2024 14:00	0.150	0.064	5	0.015
HS South	5/2/2024 14:00	5/2/2024 14:10	0.150	0.065	5	0.015
HS South	5/2/2024 14:10	5/2/2024 14:20	0.150	0.066	5	0.015
HS South	5/2/2024 14:20	5/2/2024 14:30	0.150	0.066	5	0.015
HS South	5/2/2024 14:30	5/2/2024 14:40	0.150	0.066	5	0.015
HS South	5/2/2024 14:40	5/2/2024 14:50	0.150	0.066	5	0.015
HS South	5/2/2024 14:50	5/2/2024 15:00	0.150	0.066	5	0.015
HS South	5/2/2024 15:00	5/2/2024 15:10	0.150	0.066	5	0.015
HS South	5/2/2024 15:10	5/2/2024 15:20	0.150	0.066	5	0.015
HS South	5/2/2024 15:20	5/2/2024 15:30	0.150	0.066	5	0.015
HS South	5/2/2024 15:30	5/2/2024 15:40	0.150	0.066	5	0.015
HS South	5/2/2024 15:40	5/2/2024 15:50	0.150	0.066	5	0.015
HS South	5/2/2024 15:50	5/2/2024 16:00	0.150	0.066	5	0.015
HS South	5/2/2024 16:00	5/2/2024 16:10	0.150	0.066	5	0.015
HS South	5/2/2024 16:10	5/2/2024 16:20	0.150	0.066	5	0.015
HS South	5/2/2024 16:20	5/2/2024 16:30	0.150	0.066	5	0.015
HS South	5/2/2024 16:30	5/2/2024 16:40	0.150	0.066	5	0.015
HS South	5/2/2024 16:40	5/2/2024 16:50	0.150	0.066	5	0.015
HS South	5/2/2024 16:50	5/2/2024 17:00	0.150	0.066	5	0.015

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/2/2024 6:10	5/2/2024 6:20	0.150	0	5	0
PER2 2024	5/2/2024 6:20	5/2/2024 6:30	0.150	0.002	5	0
PER2 2024	5/2/2024 6:30	5/2/2024 6:40	0.150	0.003	5	0
PER2 2024	5/2/2024 6:40	5/2/2024 6:50	0.150	0.003	5	0
PER2 2024	5/2/2024 6:50	5/2/2024 7:00	0.150	0.004	5	0
PER2 2024	5/2/2024 7:00	5/2/2024 7:10	0.150	0.004	5	0
PER2 2024	5/2/2024 7:10	5/2/2024 7:20	0.150	0.004	5	0
PER2 2024	5/2/2024 7:20	5/2/2024 7:30	0.150	0.005	5	0
PER2 2024	5/2/2024 7:30	5/2/2024 7:40	0.150	0.005	5	0
PER2 2024	5/2/2024 7:40	5/2/2024 7:50	0.150	0.005	5	0
PER2 2024	5/2/2024 7:50	5/2/2024 8:00	0.150	0.006	5	0
PER2 2024	5/2/2024 8:00	5/2/2024 8:10	0.150	0.006	5	0
PER2 2024	5/2/2024 8:10	5/2/2024 8:20	0.150	0.007	5	0
PER2 2024	5/2/2024 8:20	5/2/2024 8:30	0.150	0.007	5	0
PER2 2024	5/2/2024 8:30	5/2/2024 8:40	0.150	0.007	5	0
PER2 2024	5/2/2024 8:40	5/2/2024 8:50	0.150	0.008	5	0
PER2 2024	5/2/2024 8:50	5/2/2024 9:00	0.150	0.009	5	0
PER2 2024	5/2/2024 9:00	5/2/2024 9:10	0.150	0.009	5	0
PER2 2024	5/2/2024 9:10	5/2/2024 9:20	0.150	0.01	5	0
PER2 2024	5/2/2024 9:20	5/2/2024 9:30	0.150	0.01	5	0
PER2 2024	5/2/2024 9:30	5/2/2024 9:40	0.150	0.011	5	0
PER2 2024	5/2/2024 9:40	5/2/2024 9:50	0.150	0.012	5	0
PER2 2024	5/2/2024 9:50	5/2/2024 10:00	0.150	0.012	5	0
PER2 2024	5/2/2024 10:00	5/2/2024 10:10	0.150	0.013	5	0
PER2 2024	5/2/2024 10:10	5/2/2024 10:20	0.150	0.014	5	0
PER2 2024	5/2/2024 10:20	5/2/2024 10:30	0.150	0.015	5	0
PER2 2024	5/2/2024 10:30	5/2/2024 10:40	0.150	0.016	5	0
PER2 2024	5/2/2024 10:40	5/2/2024 10:50	0.150	0.017	5	0
PER2 2024	5/2/2024 10:50	5/2/2024 11:00	0.150	0.019	5	0
PER2 2024	5/2/2024 11:00	5/2/2024 11:10	0.150	0.02	5	0
PER2 2024	5/2/2024 11:10	5/2/2024 11:20	0.150	0.021	5	0
PER2 2024	5/2/2024 11:20	5/2/2024 11:30	0.150	0.022	5	0
PER2 2024	5/2/2024 11:30	5/2/2024 11:40	0.150	0.024	5	0
PER2 2024	5/2/2024 11:40	5/2/2024 11:50	0.150	0.025	5	0
PER2 2024	5/2/2024 11:50	5/2/2024 12:00	0.150	0.026	5	0
PER2 2024	5/2/2024 12:00	5/2/2024 12:10	0.150	0.027	5	0
PER2 2024	5/2/2024 12:10	5/2/2024 12:20	0.150	0.028	5	0
PER2 2024	5/2/2024 12:20	5/2/2024 12:30	0.150	0.029	5	0
PER2 2024	5/2/2024 12:30	5/2/2024 12:40	0.150	0.03	5	0
PER2 2024	5/2/2024 12:40	5/2/2024 12:50	0.150	0.031	5	0
PER2 2024	5/2/2024 12:50	5/2/2024 13:00	0.150	0.032	5	0
PER2 2024	5/2/2024 13:00	5/2/2024 13:10	0.150	0.033	5	0
PER2 2024	5/2/2024 13:10	5/2/2024 13:20	0.150	0.034	5	0
PER2 2024	5/2/2024 13:20	5/2/2024 13:30	0.150	0.035	5	0
PER2 2024	5/2/2024 13:30	5/2/2024 13:40	0.150	0.035	5	0
PER2 2024	5/2/2024 13:40	5/2/2024 13:50	0.150	0.036	5	0
PER2 2024	5/2/2024 13:50	5/2/2024 14:00	0.150	0.037	5	0
PER2 2024	5/2/2024 14:00	5/2/2024 14:10	0.150	0.038	5	0
PER2 2024	5/2/2024 14:10	5/2/2024 14:20	0.150	0.038	5	0
PER2 2024	5/2/2024 14:20	5/2/2024 14:30	0.150	0.038	5	0
PER2 2024	5/2/2024 14:30	5/2/2024 14:40	0.150	0.038	5	0
PER2 2024	5/2/2024 14:40	5/2/2024 14:50	0.150	0.038	5	0
PER2 2024	5/2/2024 14:50	5/2/2024 15:00	0.150	0.038	5	0
PER2 2024	5/2/2024 15:00	5/2/2024 15:10	0.150	0.038	5	0
PER2 2024	5/2/2024 15:10	5/2/2024 15:20	0.150	0.038	5	0
PER2 2024	5/2/2024 15:20	5/2/2024 15:30	0.150	0.038	5	0
PER2 2024	5/2/2024 15:30	5/2/2024 15:40	0.150	0.038	5	0
PER2 2024	5/2/2024 15:40	5/2/2024 15:50	0.150	0.038	5	0
PER2 2024	5/2/2024 15:50	5/2/2024 16:00	0.150	0.038	5	0
PER2 2024	5/2/2024 16:00	5/2/2024 16:10	0.150	0.038	5	0
PER2 2024	5/2/2024 16:10	5/2/2024 16:20	0.150	0.038	5	0
PER2 2024	5/2/2024 16:20	5/2/2024 16:30	0.150	0.038	5	0
PER2 2024	5/2/2024 16:30	5/2/2024 16:40	0.150	0.038	5	0
PER2 2024	5/2/2024 16:40	5/2/2024 16:50	0.150	0.038	5	0
PER2 2024	5/2/2024 16:50	5/2/2024 17:00	0.150	0.038	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/2/2024 6:00	5/2/2024 6:10	0.150	0.001	5	0
PER1 2024	5/2/2024 6:10	5/2/2024 6:20	0.150	0.002	5	0
PER1 2024	5/2/2024 6:20	5/2/2024 6:30	0.150	0.003	5	0
PER1 2024	5/2/2024 6:30	5/2/2024 6:40	0.150	0.003	5	0
PER1 2024	5/2/2024 6:40	5/2/2024 6:50	0.150	0.003	5	0
PER1 2024	5/2/2024 6:50	5/2/2024 7:00	0.150	0.004	5	0
PER1 2024	5/2/2024 7:00	5/2/2024 7:10	0.150	0.004	5	0
PER1 2024	5/2/2024 7:10	5/2/2024 7:20	0.150	0.005	5	0
PER1 2024	5/2/2024 7:20	5/2/2024 7:30	0.150	0.005	5	0
PER1 2024	5/2/2024 7:30	5/2/2024 7:40	0.150	0.005	5	0
PER1 2024	5/2/2024 7:40	5/2/2024 7:50	0.150	0.006	5	0
PER1 2024	5/2/2024 7:50	5/2/2024 8:00	0.150	0.006	5	0
PER1 2024	5/2/2024 8:00	5/2/2024 8:10	0.150	0.006	5	0
PER1 2024	5/2/2024 8:10	5/2/2024 8:20	0.150	0.007	5	0
PER1 2024	5/2/2024 8:20	5/2/2024 8:30	0.150	0.007	5	0
PER1 2024	5/2/2024 8:30	5/2/2024 8:40	0.150	0.008	5	0
PER1 2024	5/2/2024 8:40	5/2/2024 8:50	0.150	0.008	5	0
PER1 2024	5/2/2024 8:50	5/2/2024 9:00	0.150	0.009	5	0
PER1 2024	5/2/2024 9:00	5/2/2024 9:10	0.150	0.009	5	0
PER1 2024	5/2/2024 9:10	5/2/2024 9:20	0.150	0.01	5	0
PER1 2024	5/2/2024 9:20	5/2/2024 9:30	0.150	0.01	5	0
PER1 2024	5/2/2024 9:30	5/2/2024 9:40	0.150	0.011	5	0
PER1 2024	5/2/2024 9:40	5/2/2024 9:50	0.150	0.011	5	0
PER1 2024	5/2/2024 9:50	5/2/2024 10:00	0.150	0.012	5	0
PER1 2024	5/2/2024 10:00	5/2/2024 10:10	0.150	0.013	5	0
PER1 2024	5/2/2024 10:10	5/2/2024 10:20	0.150	0.013	5	0
PER1 2024	5/2/2024 10:20	5/2/2024 10:30	0.150	0.014	5	0
PER1 2024	5/2/2024 10:30	5/2/2024 10:40	0.150	0.015	5	0
PER1 2024	5/2/2024 10:40	5/2/2024 10:50	0.150	0.016	5	0
PER1 2024	5/2/2024 10:50	5/2/2024 11:00	0.150	0.018	5	0
PER1 2024	5/2/2024 11:00	5/2/2024 11:10	0.150	0.019	5	0
PER1 2024	5/2/2024 11:10	5/2/2024 11:20	0.150	0.02	5	0
PER1 2024	5/2/2024 11:20	5/2/2024 11:30	0.150	0.021	5	0
PER1 2024	5/2/2024 11:30	5/2/2024 11:40	0.150	0.022	5	0
PER1 2024	5/2/2024 11:40	5/2/2024 11:50	0.150	0.023	5	0
PER1 2024	5/2/2024 11:50	5/2/2024 12:00	0.150	0.024	5	0
PER1 2024	5/2/2024 12:00	5/2/2024 12:10	0.150	0.025	5	0
PER1 2024	5/2/2024 12:10	5/2/2024 12:20	0.150	0.025	5	0
PER1 2024	5/2/2024 12:20	5/2/2024 12:30	0.150	0.025	5	0
PER1 2024	5/2/2024 12:30	5/2/2024 12:40	0.150	0.025	5	0
PER1 2024	5/2/2024 12:40	5/2/2024 12:50	0.150	0.025	5	0
PER1 2024	5/2/2024 12:50	5/2/2024 13:00	0.150	0.025	5	0
PER1 2024	5/2/2024 13:00	5/2/2024 13:10	0.150	0.025	5	0
PER1 2024	5/2/2024 13:10	5/2/2024 13:20	0.150	0.025	5	0
PER1 2024	5/2/2024 13:20	5/2/2024 13:30	0.150	0.025	5	0
PER1 2024	5/2/2024 13:30	5/2/2024 13:40	0.150	0.025	5	0
PER1 2024	5/2/2024 13:40	5/2/2024 13:50	0.150	0.025	5	0
PER1 2024	5/2/2024 13:50	5/2/2024 14:00	0.150	0.025	5	0
PER1 2024	5/2/2024 14:00	5/2/2024 14:10	0.150	0.025	5	0
PER1 2024	5/2/2024 14:10	5/2/2024 14:20	0.150	0.032	5	0
PER1 2024	5/2/2024 14:20	5/2/2024 14:30	0.150	0.032	5	0
PER1 2024	5/2/2024 14:30	5/2/2024 14:40	0.150	0.032	5	0
PER1 2024	5/2/2024 14:40	5/2/2024 14:50	0.150	0.032	5	0
PER1 2024	5/2/2024 14:50	5/2/2024 15:00	0.150	0.032	5	0
PER1 2024	5/2/2024 15:00	5/2/2024 15:10	0.150	0.032	5	0
PER1 2024	5/2/2024 15:10	5/2/2024 15:20	0.150	0.032	5	0
PER1 2024	5/2/2024 15:20	5/2/2024 15:30	0.150	0.032	5	0
PER1 2024	5/2/2024 15:30	5/2/2024 15:40	0.150	0.032	5	0
PER1 2024	5/2/2024 15:40	5/2/2024 15:50	0.150	0.032	5	0
PER1 2024	5/2/2024 15:50	5/2/2024 16:00	0.150	0.032	5	0
PER1 2024	5/2/2024 16:00	5/2/2024 16:10	0.150	0.032	5	0
PER1 2024	5/2/2024 16:10	5/2/2024 16:20	0.150	0.032	5	0
PER1 2024	5/2/2024 16:20	5/2/2024 16:30	0.150	0.032	5	0
PER1 2024	5/2/2024 16:30	5/2/2024 16:40	0.150	0.032	5	0
PER1 2024	5/2/2024 16:40	5/2/2024 16:50	0.150	0.032	5	0
PER1 2024	5/2/2024 16:50	5/2/2024 17:00	0.150	0.032	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/03/2024

Weather: 60 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development. 2) ECD on-site to backfill stormwater pipelines. 3) Collect endpoint samples EP-84 and EP-85.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): EP-84 and EP-85	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below. The Site had a delayed start and CAMP stations were not turned on until approximately 11AM.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal, endpoint sample collection and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8365	1520	4140

Site Layout Map and Excavation Figures

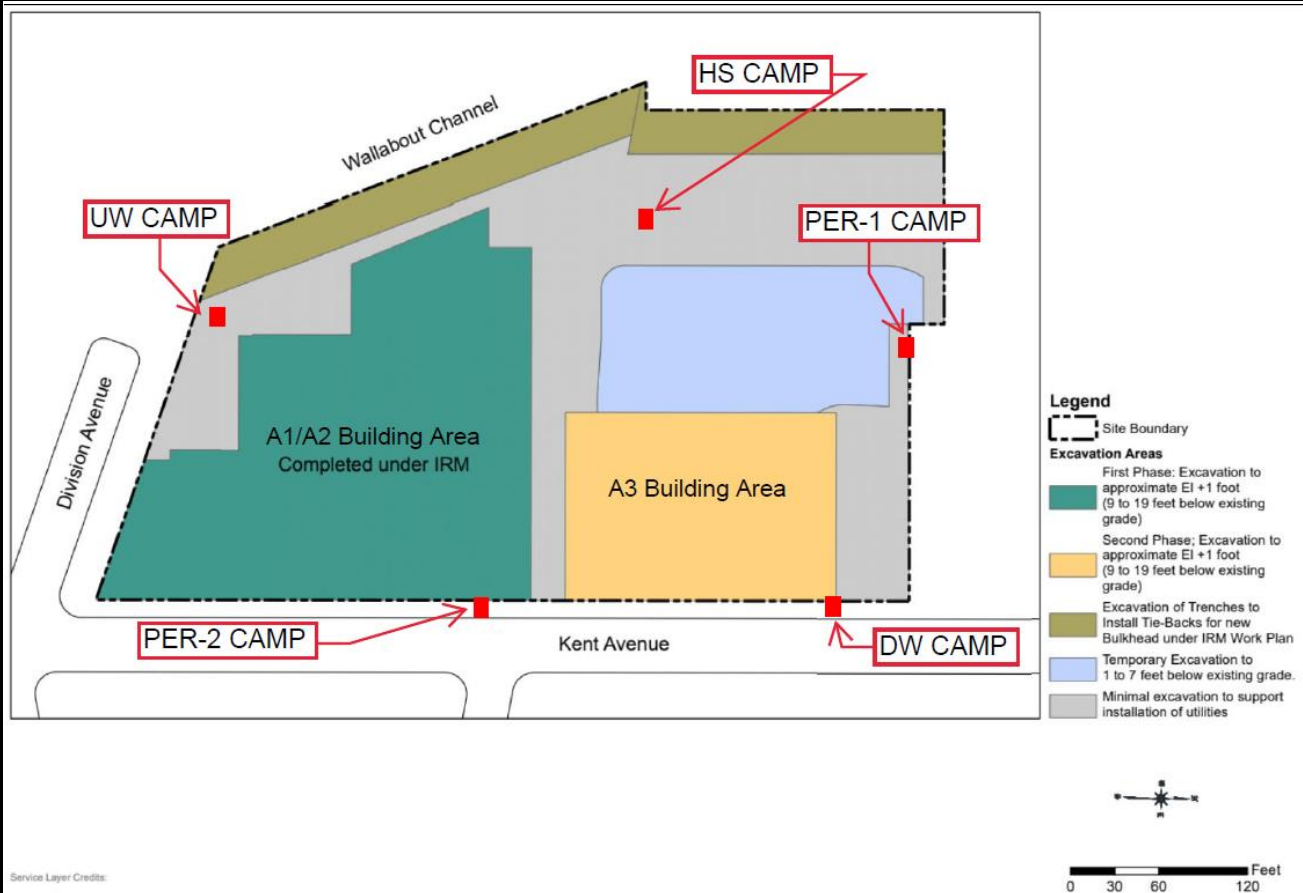

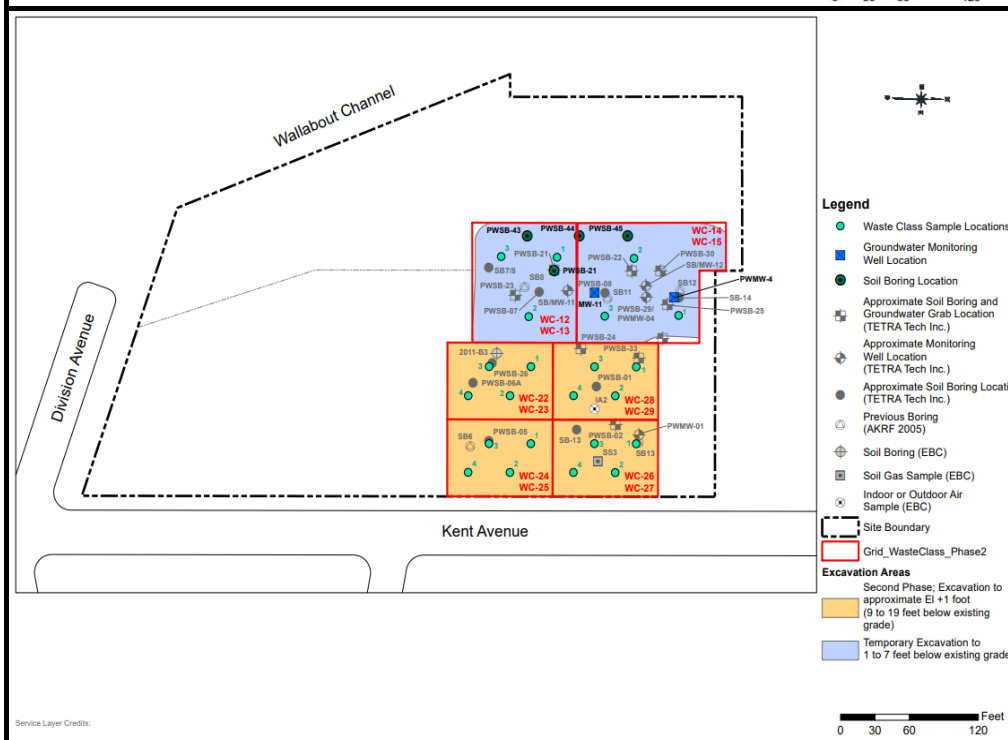
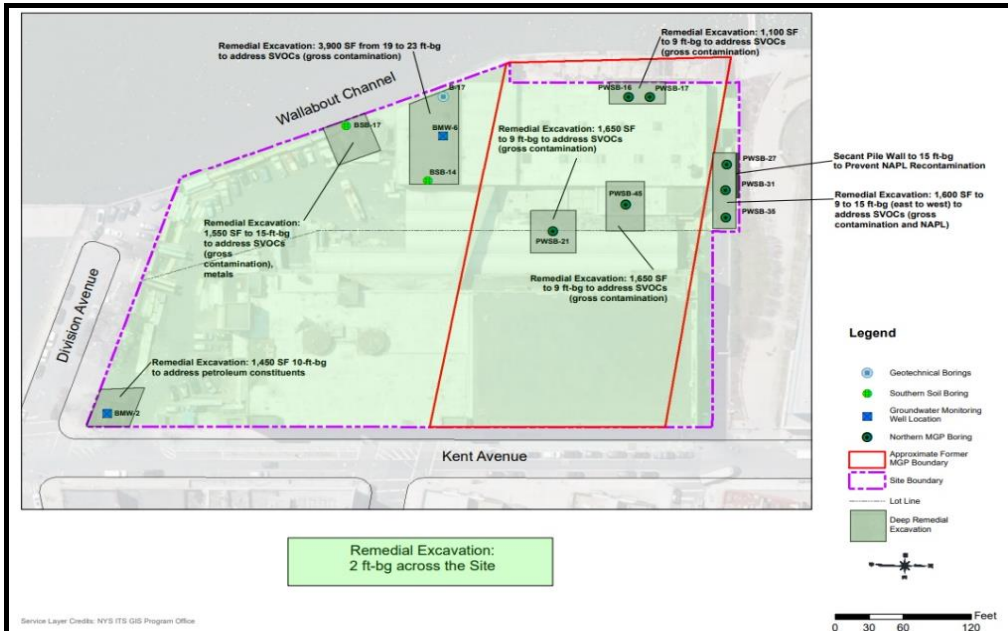


Photo 1:
View of Site conditions
and activities facing
southeast.




Photo 2:
View of stone refreshing
in truck wash pad, facing
west.



Photo 3:
View of covered soil
stockpile in
preparation for off-
site soil disposal.




Photo 4:
View of the
dewatering effluent
and turbidity curtain.

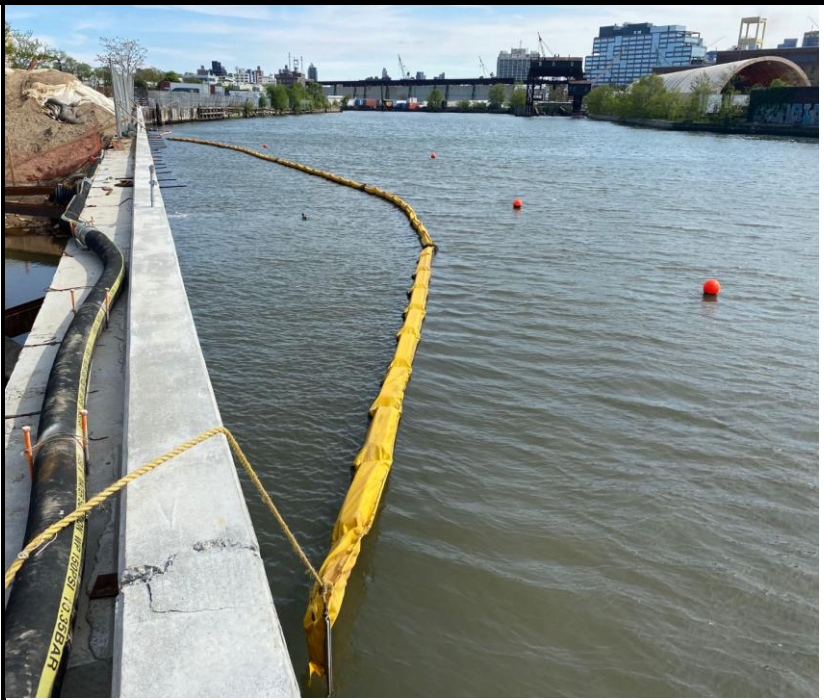


CAMP:
Downwind
Particulates

Dust Levels

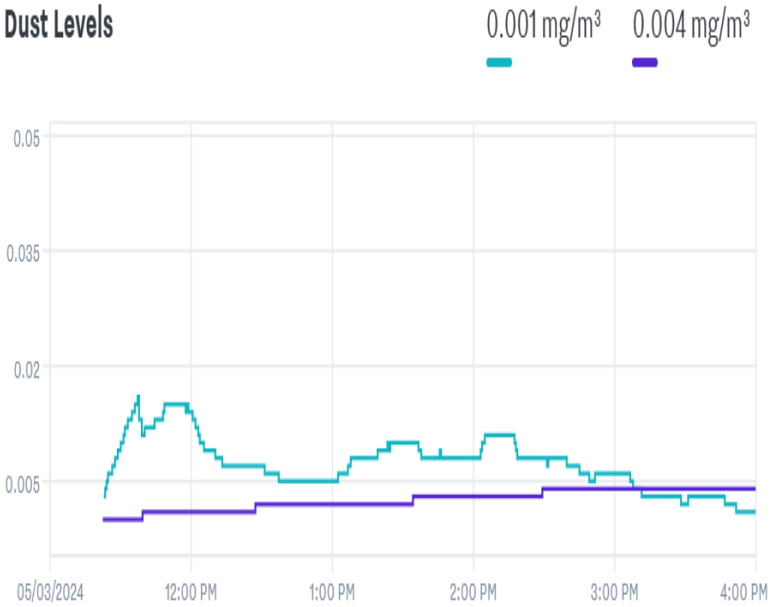

CAMP:
Downwind VOCs


VOC Levels

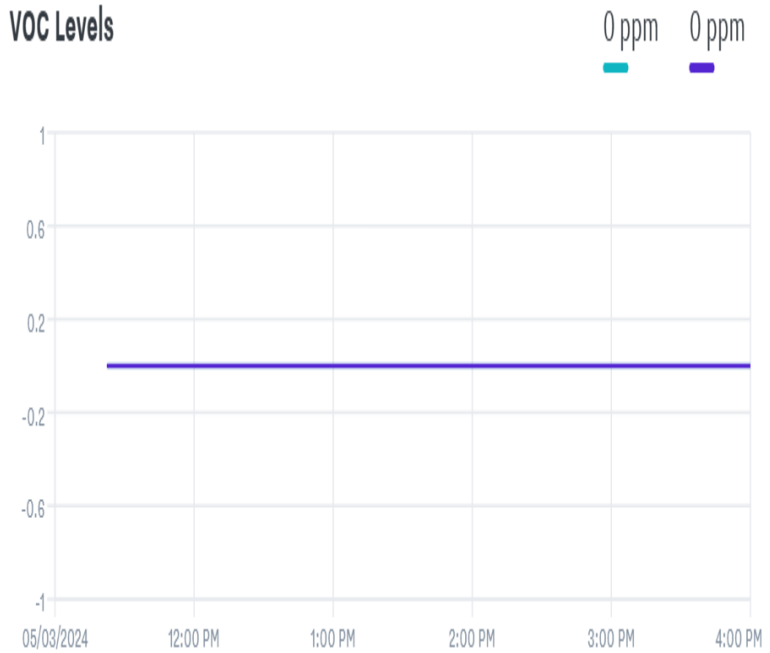

CAMP:
Upwind Particulates

Dust Levels


0.018 mg/m³ 0.012 mg/m³

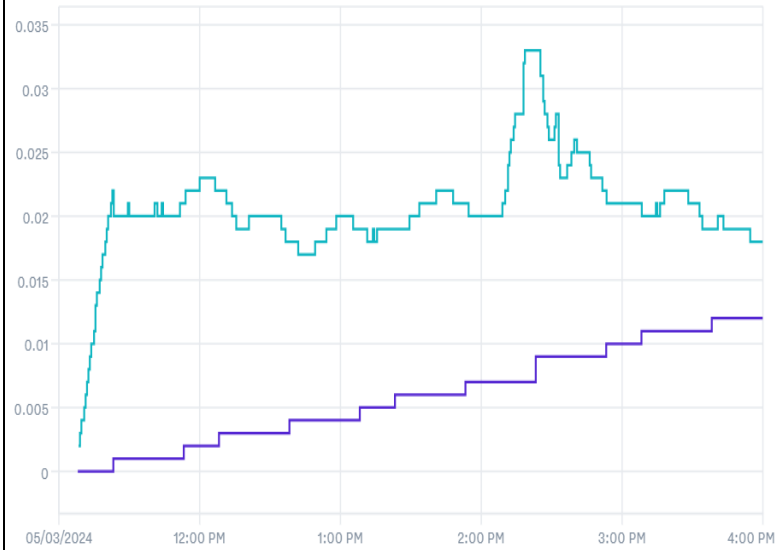

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

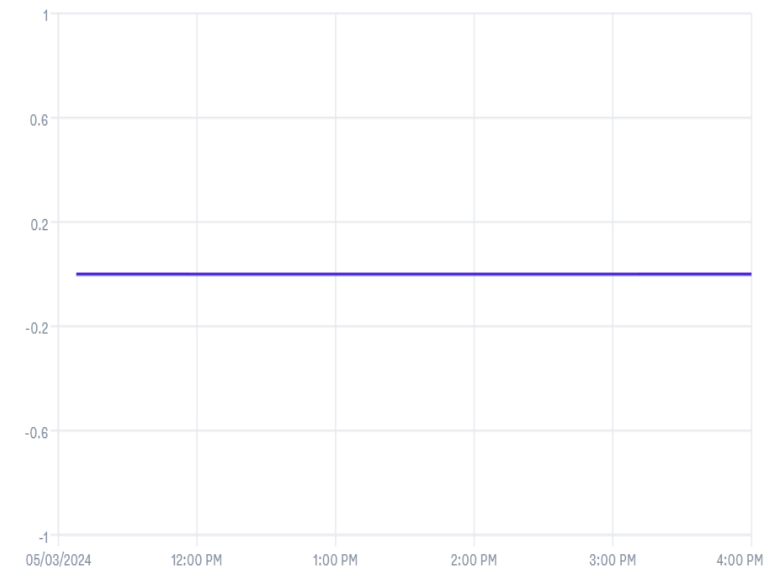

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/3/2024 11:00	5/3/2024 11:10	0.150	0.047	5	0
DW 2024	5/3/2024 11:10	5/3/2024 11:20	0.150	0.047	5	0
DW 2024	5/3/2024 11:20	5/3/2024 11:30	0.150	0	5	0
DW 2024	5/3/2024 11:30	5/3/2024 11:40	0.150	0.001	5	0
DW 2024	5/3/2024 11:40	5/3/2024 11:50	0.150	0.001	5	0
DW 2024	5/3/2024 11:50	5/3/2024 12:00	0.150	0.001	5	0
DW 2024	5/3/2024 12:00	5/3/2024 12:10	0.150	0.001	5	0
DW 2024	5/3/2024 12:10	5/3/2024 12:20	0.150	0.001	5	0
DW 2024	5/3/2024 12:20	5/3/2024 12:30	0.150	0.002	5	0
DW 2024	5/3/2024 12:30	5/3/2024 12:40	0.150	0.002	5	0
DW 2024	5/3/2024 12:40	5/3/2024 12:50	0.150	0.002	5	0
DW 2024	5/3/2024 12:50	5/3/2024 13:00	0.150	0.002	5	0
DW 2024	5/3/2024 13:00	5/3/2024 13:10	0.150	0.002	5	0
DW 2024	5/3/2024 13:10	5/3/2024 13:20	0.150	0.002	5	0
DW 2024	5/3/2024 13:20	5/3/2024 13:30	0.150	0.002	5	0
DW 2024	5/3/2024 13:30	5/3/2024 13:40	0.150	0.003	5	0
DW 2024	5/3/2024 13:40	5/3/2024 13:50	0.150	0.003	5	0
DW 2024	5/3/2024 13:50	5/3/2024 14:00	0.150	0.003	5	0
DW 2024	5/3/2024 14:00	5/3/2024 14:10	0.150	0.003	5	0
DW 2024	5/3/2024 14:10	5/3/2024 14:20	0.150	0.003	5	0
DW 2024	5/3/2024 14:20	5/3/2024 14:30	0.150	0.004	5	0
DW 2024	5/3/2024 14:30	5/3/2024 14:40	0.150	0.004	5	0
DW 2024	5/3/2024 14:40	5/3/2024 14:50	0.150	0.004	5	0
DW 2024	5/3/2024 14:50	5/3/2024 15:00	0.150	0.004	5	0
DW 2024	5/3/2024 15:00	5/3/2024 15:10	0.150	0.004	5	0
DW 2024	5/3/2024 15:10	5/3/2024 15:20	0.150	0.004	5	0
DW 2024	5/3/2024 15:20	5/3/2024 15:30	0.150	0.004	5	0
DW 2024	5/3/2024 15:30	5/3/2024 15:40	0.150	0.004	5	0
DW 2024	5/3/2024 15:40	5/3/2024 15:50	0.150	0.004	5	0
DW 2024	5/3/2024 15:50	5/3/2024 16:00	0.150	0.004	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/3/2024 11:00	5/3/2024 11:10	0.150	0	5	0
UW 2024	5/3/2024 11:10	5/3/2024 11:20	0.150	0	5	0
UW 2024	5/3/2024 11:20	5/3/2024 11:30	0.150	0.001	5	0
UW 2024	5/3/2024 11:30	5/3/2024 11:40	0.150	0.001	5	0
UW 2024	5/3/2024 11:40	5/3/2024 11:50	0.150	0.001	5	0
UW 2024	5/3/2024 11:50	5/3/2024 12:00	0.150	0.002	5	0
UW 2024	5/3/2024 12:00	5/3/2024 12:10	0.150	0.003	5	0
UW 2024	5/3/2024 12:10	5/3/2024 12:20	0.150	0.003	5	0
UW 2024	5/3/2024 12:20	5/3/2024 12:30	0.150	0.003	5	0
UW 2024	5/3/2024 12:30	5/3/2024 12:40	0.150	0.004	5	0
UW 2024	5/3/2024 12:40	5/3/2024 12:50	0.150	0.004	5	0
UW 2024	5/3/2024 12:50	5/3/2024 13:00	0.150	0.004	5	0
UW 2024	5/3/2024 13:00	5/3/2024 13:10	0.150	0.005	5	0
UW 2024	5/3/2024 13:10	5/3/2024 13:20	0.150	0.005	5	0
UW 2024	5/3/2024 13:20	5/3/2024 13:30	0.150	0.006	5	0
UW 2024	5/3/2024 13:30	5/3/2024 13:40	0.150	0.006	5	0
UW 2024	5/3/2024 13:40	5/3/2024 13:50	0.150	0.006	5	0
UW 2024	5/3/2024 13:50	5/3/2024 14:00	0.150	0.007	5	0
UW 2024	5/3/2024 14:00	5/3/2024 14:10	0.150	0.007	5	0
UW 2024	5/3/2024 14:10	5/3/2024 14:20	0.150	0.007	5	0
UW 2024	5/3/2024 14:20	5/3/2024 14:30	0.150	0.009	5	0
UW 2024	5/3/2024 14:30	5/3/2024 14:40	0.150	0.009	5	0
UW 2024	5/3/2024 14:40	5/3/2024 14:50	0.150	0.009	5	0
UW 2024	5/3/2024 14:50	5/3/2024 15:00	0.150	0.01	5	0
UW 2024	5/3/2024 15:00	5/3/2024 15:10	0.150	0.011	5	0
UW 2024	5/3/2024 15:10	5/3/2024 15:20	0.150	0.011	5	0
UW 2024	5/3/2024 15:20	5/3/2024 15:30	0.150	0.011	5	0
UW 2024	5/3/2024 15:30	5/3/2024 15:40	0.150	0.012	5	0
UW 2024	5/3/2024 15:40	5/3/2024 15:50	0.150	0.012	5	0
UW 2024	5/3/2024 15:50	5/3/2024 16:00	0.150	0.012	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/3/2024 11:00	5/3/2024 11:10	0.150	0	5	0
HS South	5/3/2024 11:10	5/3/2024 11:20	0.150	0	5	0
HS South	5/3/2024 11:20	5/3/2024 11:30	0.150	0	5	0
HS South	5/3/2024 11:30	5/3/2024 11:40	0.150	0.001	5	0
HS South	5/3/2024 11:40	5/3/2024 11:50	0.150	0.002	5	0
HS South	5/3/2024 11:50	5/3/2024 12:00	0.150	0.002	5	0
HS South	5/3/2024 12:00	5/3/2024 12:10	0.150	0.002	5	0
HS South	5/3/2024 12:10	5/3/2024 12:20	0.150	0.003	5	0
HS South	5/3/2024 12:20	5/3/2024 12:30	0.150	0.003	5	0
HS South	5/3/2024 12:30	5/3/2024 12:40	0.150	0.004	5	0
HS South	5/3/2024 12:40	5/3/2024 12:50	0.150	0.004	5	0
HS South	5/3/2024 12:50	5/3/2024 13:00	0.150	0.005	5	0
HS South	5/3/2024 13:00	5/3/2024 13:10	0.150	0.005	5	0
HS South	5/3/2024 13:10	5/3/2024 13:20	0.150	0.006	5	0
HS South	5/3/2024 13:20	5/3/2024 13:30	0.150	0.006	5	0
HS South	5/3/2024 13:30	5/3/2024 13:40	0.150	0.007	5	0
HS South	5/3/2024 13:40	5/3/2024 13:50	0.150	0.007	5	0
HS South	5/3/2024 13:50	5/3/2024 14:00	0.150	0.008	5	0
HS South	5/3/2024 14:00	5/3/2024 14:10	0.150	0.009	5	0
HS South	5/3/2024 14:10	5/3/2024 14:20	0.150	0.01	5	0
HS South	5/3/2024 14:20	5/3/2024 14:30	0.150	0.011	5	0
HS South	5/3/2024 14:30	5/3/2024 14:40	0.150	0.011	5	0
HS South	5/3/2024 14:40	5/3/2024 14:50	0.150	0.012	5	0
HS South	5/3/2024 14:50	5/3/2024 15:00	0.150	0.013	5	0
HS South	5/3/2024 15:00	5/3/2024 15:10	0.150	0.013	5	0
HS South	5/3/2024 15:10	5/3/2024 15:20	0.150	0.014	5	0
HS South	5/3/2024 15:20	5/3/2024 15:30	0.150	0.015	5	0
HS South	5/3/2024 15:30	5/3/2024 15:40	0.150	0.015	5	0
HS South	5/3/2024 15:40	5/3/2024 15:50	0.150	0.016	5	0
HS South	5/3/2024 15:50	5/3/2024 16:00	0.150	0.016	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/3/2024 11:20	5/3/2024 11:30	0.150	0	5	0
PER2 2024	5/3/2024 11:30	5/3/2024 11:40	0.150	0	5	0
PER2 2024	5/3/2024 11:40	5/3/2024 11:50	0.150	0	5	0
PER2 2024	5/3/2024 11:50	5/3/2024 12:00	0.150	0.001	5	0
PER2 2024	5/3/2024 12:00	5/3/2024 12:10	0.150	0.001	5	0
PER2 2024	5/3/2024 12:10	5/3/2024 12:20	0.150	0.001	5	0
PER2 2024	5/3/2024 12:20	5/3/2024 12:30	0.150	0.001	5	0
PER2 2024	5/3/2024 12:30	5/3/2024 12:40	0.150	0.001	5	0
PER2 2024	5/3/2024 12:40	5/3/2024 12:50	0.150	0.001	5	0
PER2 2024	5/3/2024 12:50	5/3/2024 13:00	0.150	0.001	5	0
PER2 2024	5/3/2024 13:00	5/3/2024 13:10	0.150	0.001	5	0
PER2 2024	5/3/2024 13:10	5/3/2024 13:20	0.150	0.002	5	0
PER2 2024	5/3/2024 13:20	5/3/2024 13:30	0.150	0.002	5	0
PER2 2024	5/3/2024 13:30	5/3/2024 13:40	0.150	0.002	5	0
PER2 2024	5/3/2024 13:40	5/3/2024 13:50	0.150	0.002	5	0
PER2 2024	5/3/2024 13:50	5/3/2024 14:00	0.150	0.003	5	0
PER2 2024	5/3/2024 14:00	5/3/2024 14:10	0.150	0.003	5	0
PER2 2024	5/3/2024 14:10	5/3/2024 14:20	0.150	0.003	5	0
PER2 2024	5/3/2024 14:20	5/3/2024 14:30	0.150	0.003	5	0
PER2 2024	5/3/2024 14:30	5/3/2024 14:40	0.150	0.004	5	0
PER2 2024	5/3/2024 14:40	5/3/2024 14:50	0.150	0.004	5	0
PER2 2024	5/3/2024 14:50	5/3/2024 15:00	0.150	0.004	5	0
PER2 2024	5/3/2024 15:00	5/3/2024 15:10	0.150	0.004	5	0
PER2 2024	5/3/2024 15:10	5/3/2024 15:20	0.150	0.004	5	0
PER2 2024	5/3/2024 15:20	5/3/2024 15:30	0.150	0.004	5	0
PER2 2024	5/3/2024 15:30	5/3/2024 15:40	0.150	0.005	5	0
PER2 2024	5/3/2024 15:40	5/3/2024 15:50	0.150	0.005	5	0
PER2 2024	5/3/2024 15:50	5/3/2024 16:00	0.150	0.005	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/3/2024 11:00	5/3/2024 11:10	0.150	0	5	0
PER1 2024	5/3/2024 11:10	5/3/2024 11:20	0.150	0	5	0
PER1 2024	5/3/2024 11:20	5/3/2024 11:30	0.150	0	5	0
PER1 2024	5/3/2024 11:30	5/3/2024 11:40	0.150	0	5	0
PER1 2024	5/3/2024 11:40	5/3/2024 11:50	0.150	0	5	0
PER1 2024	5/3/2024 11:50	5/3/2024 12:00	0.150	0	5	0
PER1 2024	5/3/2024 12:00	5/3/2024 12:10	0.150	0	5	0
PER1 2024	5/3/2024 12:10	5/3/2024 12:20	0.150	0	5	0
PER1 2024	5/3/2024 12:20	5/3/2024 12:30	0.150	0	5	0
PER1 2024	5/3/2024 12:30	5/3/2024 12:40	0.150	0	5	0
PER1 2024	5/3/2024 12:40	5/3/2024 12:50	0.150	0	5	0
PER1 2024	5/3/2024 12:50	5/3/2024 13:00	0.150	0	5	0
PER1 2024	5/3/2024 13:00	5/3/2024 13:10	0.150	0	5	0
PER1 2024	5/3/2024 13:10	5/3/2024 13:20	0.150	0	5	0
PER1 2024	5/3/2024 13:20	5/3/2024 13:30	0.150	0.004	5	0
PER1 2024	5/3/2024 13:30	5/3/2024 13:40	0.150	0.004	5	0
PER1 2024	5/3/2024 13:40	5/3/2024 13:50	0.150	0.004	5	0
PER1 2024	5/3/2024 13:50	5/3/2024 14:00	0.150	0.004	5	0
PER1 2024	5/3/2024 14:00	5/3/2024 14:10	0.150	0.004	5	0
PER1 2024	5/3/2024 14:10	5/3/2024 14:20	0.150	0.005	5	0
PER1 2024	5/3/2024 14:20	5/3/2024 14:30	0.150	0.005	5	0
PER1 2024	5/3/2024 14:30	5/3/2024 14:40	0.150	0.005	5	0
PER1 2024	5/3/2024 14:40	5/3/2024 14:50	0.150	0.005	5	0
PER1 2024	5/3/2024 14:50	5/3/2024 15:00	0.150	0.005	5	0
PER1 2024	5/3/2024 15:00	5/3/2024 15:10	0.150	0.005	5	0
PER1 2024	5/3/2024 15:10	5/3/2024 15:20	0.150	0.005	5	0
PER1 2024	5/3/2024 15:20	5/3/2024 15:30	0.150	0.005	5	0
PER1 2024	5/3/2024 15:30	5/3/2024 15:40	0.150	0.005	5	0
PER1 2024	5/3/2024 15:40	5/3/2024 15:50	0.150	0.006	5	0
PER1 2024	5/3/2024 15:50	5/3/2024 16:00	0.150	0.006	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/06/2024

Weather: 60 deg. F, Clear/rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development.
- 2) Export of 11 loads (~220 CY) of material from WC-27 for off-site disposal at the MSM facility.
- 3) NYSDEC PM Erick Bower on-site for site visit.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	220	0	0
Total:(CY)	4485	0	8585	1520	4140

Site Layout Map and Excavation Figures

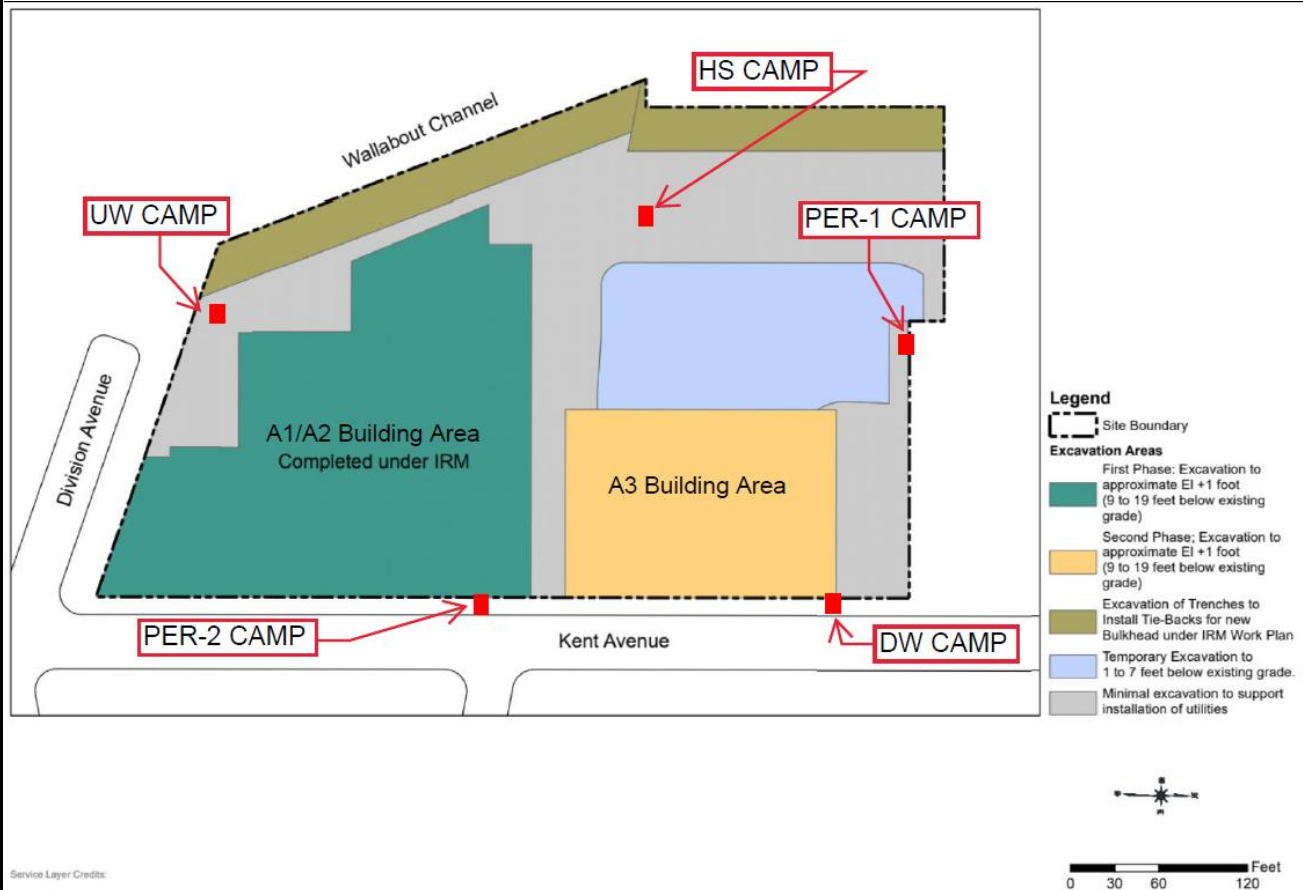

Service Layer Credits:

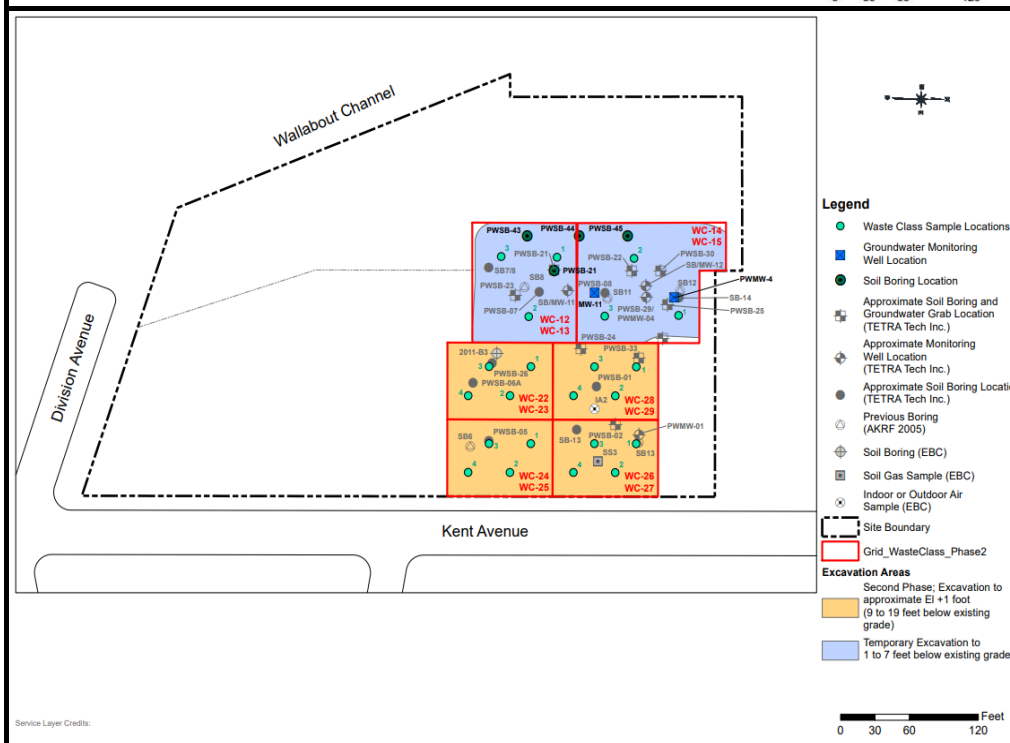
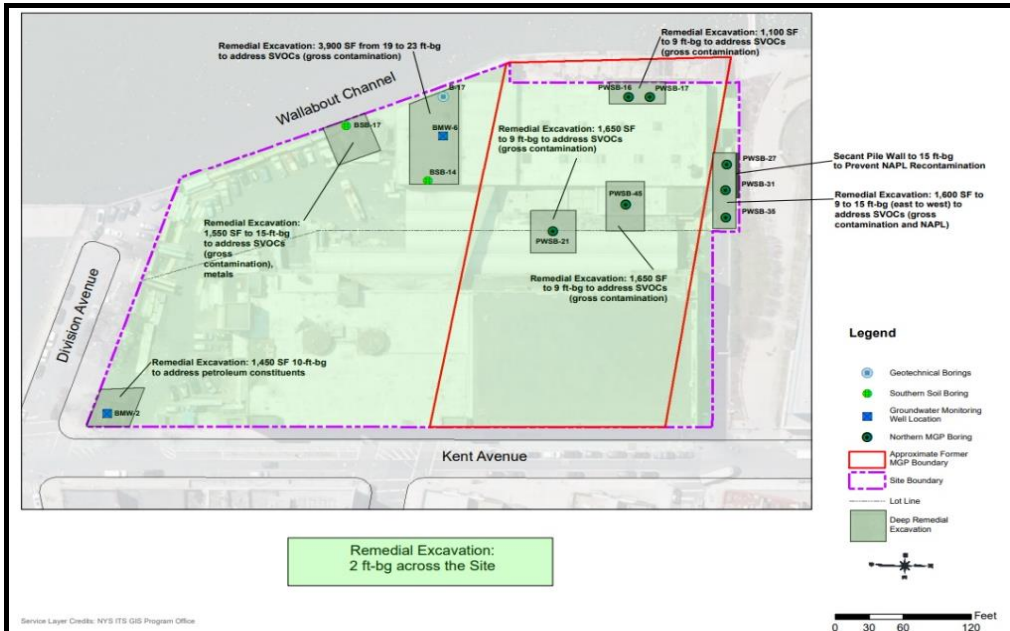


Photo 1:
View of Site conditions
and activities facing
southeast.



Photo 2:
View of waterproofing
installation.



Photo 3:
View of truck
washing prior to
truck leaving the
Site.




Photo 4:
View of the
dewatering effluent
and turbidity curtain.



CAMP:
Downwind
Particulates

Dust Levels


0.084 mg/m³ 0.077 mg/m³

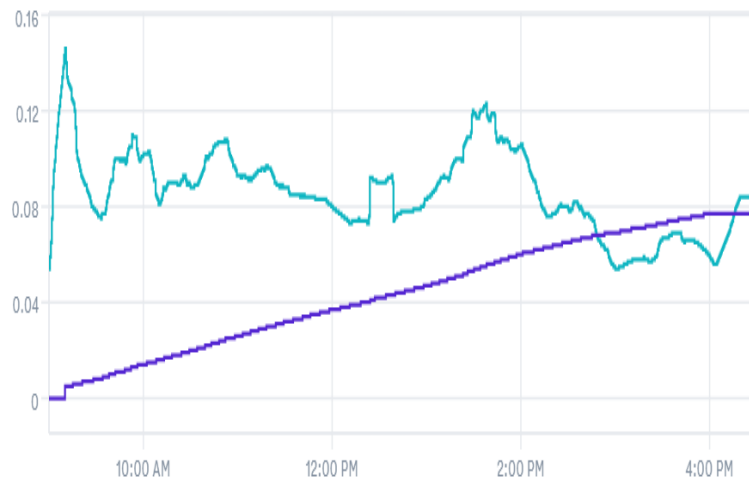

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm

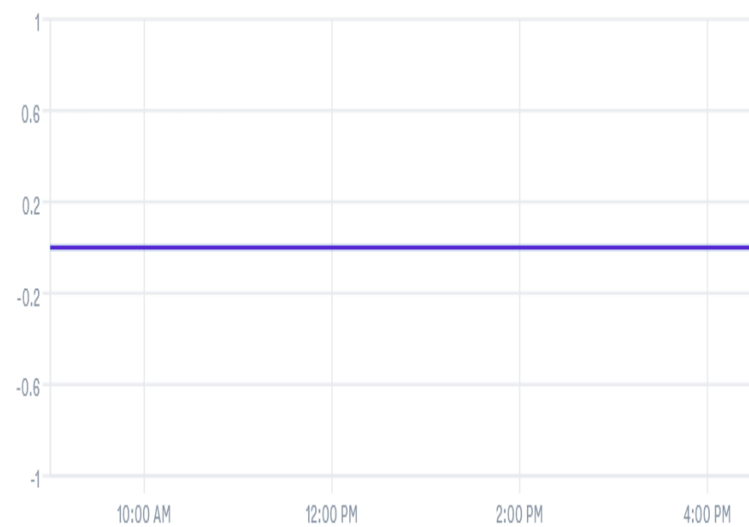

CAMP:
Upwind Particulates

Dust Levels


0.051 mg/m³ 0.11 mg/m³

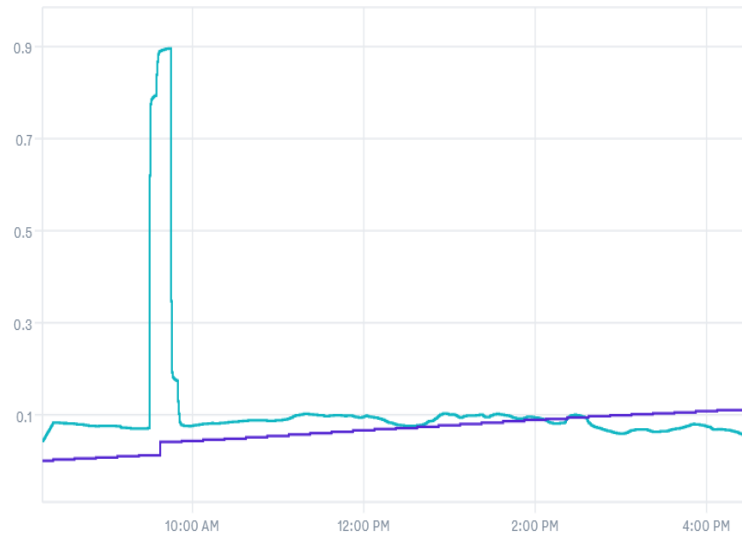

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

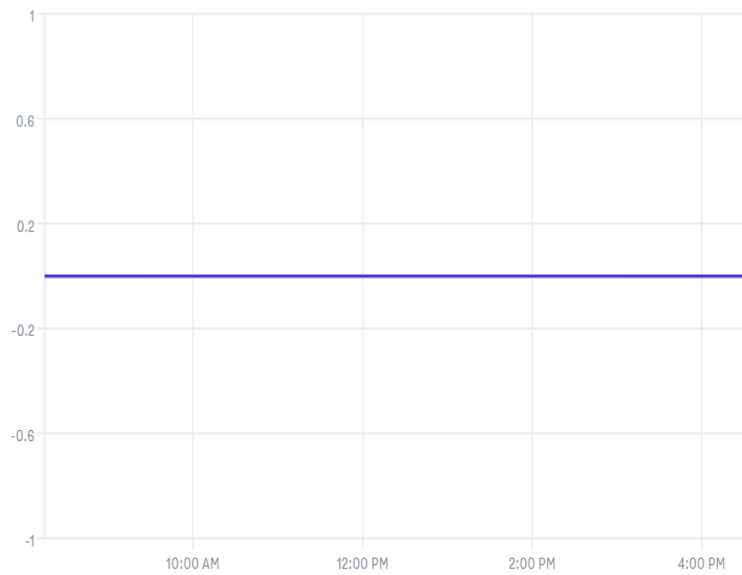

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/6/2024 8:55	5/6/2024 9:05	0.150	0	5	0
DW 2024	5/6/2024 9:05	5/6/2024 9:15	0.150	0.005	5	0
DW 2024	5/6/2024 9:15	5/6/2024 9:25	0.150	0.007	5	0
DW 2024	5/6/2024 9:25	5/6/2024 9:35	0.150	0.009	5	0
DW 2024	5/6/2024 9:35	5/6/2024 9:45	0.150	0.011	5	0
DW 2024	5/6/2024 9:45	5/6/2024 9:55	0.150	0.013	5	0
DW 2024	5/6/2024 9:55	5/6/2024 10:05	0.150	0.015	5	0
DW 2024	5/6/2024 10:05	5/6/2024 10:15	0.150	0.017	5	0
DW 2024	5/6/2024 10:15	5/6/2024 10:25	0.150	0.019	5	0
DW 2024	5/6/2024 10:25	5/6/2024 10:35	0.150	0.021	5	0
DW 2024	5/6/2024 10:35	5/6/2024 10:45	0.150	0.023	5	0
DW 2024	5/6/2024 10:45	5/6/2024 10:55	0.150	0.025	5	0
DW 2024	5/6/2024 10:55	5/6/2024 11:05	0.150	0.027	5	0
DW 2024	5/6/2024 11:05	5/6/2024 11:15	0.150	0.029	5	0
DW 2024	5/6/2024 11:15	5/6/2024 11:25	0.150	0.031	5	0
DW 2024	5/6/2024 11:25	5/6/2024 11:35	0.150	0.032	5	0
DW 2024	5/6/2024 11:35	5/6/2024 11:45	0.150	0.034	5	0
DW 2024	5/6/2024 11:45	5/6/2024 11:55	0.150	0.036	5	0
DW 2024	5/6/2024 11:55	5/6/2024 12:05	0.150	0.037	5	0
DW 2024	5/6/2024 12:05	5/6/2024 12:15	0.150	0.039	5	0
DW 2024	5/6/2024 12:15	5/6/2024 12:25	0.150	0.041	5	0
DW 2024	5/6/2024 12:25	5/6/2024 12:35	0.150	0.043	5	0
DW 2024	5/6/2024 12:35	5/6/2024 12:45	0.150	0.044	5	0
DW 2024	5/6/2024 12:45	5/6/2024 12:55	0.150	0.046	5	0
DW 2024	5/6/2024 12:55	5/6/2024 13:05	0.150	0.048	5	0
DW 2024	5/6/2024 13:05	5/6/2024 13:15	0.150	0.05	5	0
DW 2024	5/6/2024 13:15	5/6/2024 13:25	0.150	0.052	5	0
DW 2024	5/6/2024 13:25	5/6/2024 13:35	0.150	0.055	5	0
DW 2024	5/6/2024 13:35	5/6/2024 13:45	0.150	0.057	5	0
DW 2024	5/6/2024 13:45	5/6/2024 13:55	0.150	0.059	5	0
DW 2024	5/6/2024 13:55	5/6/2024 14:05	0.150	0.061	5	0
DW 2024	5/6/2024 14:05	5/6/2024 14:15	0.150	0.063	5	0
DW 2024	5/6/2024 14:15	5/6/2024 14:25	0.150	0.064	5	0
DW 2024	5/6/2024 14:25	5/6/2024 14:35	0.150	0.066	5	0
DW 2024	5/6/2024 14:35	5/6/2024 14:45	0.150	0.067	5	0
DW 2024	5/6/2024 14:45	5/6/2024 14:55	0.150	0.069	5	0
DW 2024	5/6/2024 14:55	5/6/2024 15:05	0.150	0.07	5	0
DW 2024	5/6/2024 15:05	5/6/2024 15:15	0.150	0.071	5	0
DW 2024	5/6/2024 15:15	5/6/2024 15:25	0.150	0.072	5	0
DW 2024	5/6/2024 15:25	5/6/2024 15:35	0.150	0.074	5	0
DW 2024	5/6/2024 15:35	5/6/2024 15:45	0.150	0.075	5	0
DW 2024	5/6/2024 15:45	5/6/2024 15:55	0.150	0.076	5	0
DW 2024	5/6/2024 15:55	5/6/2024 16:05	0.150	0.077	5	0
DW 2024	5/6/2024 16:05	5/6/2024 16:15	0.150	0.077	5	0
DW 2024	5/6/2024 16:15	5/6/2024 16:25	0.150	0.077	5	0
DW 2024	5/6/2024 16:25	5/6/2024 16:30	0.150	0.077	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/6/2024 8:15	5/6/2024 8:25	0.150	0.003	5	0
UW 2024	5/6/2024 8:25	5/6/2024 8:35	0.150	0.003	5	0
UW 2024	5/6/2024 8:35	5/6/2024 8:45	0.150	0.005	5	0
UW 2024	5/6/2024 8:45	5/6/2024 8:55	0.150	0.007	5	0
UW 2024	5/6/2024 8:55	5/6/2024 9:05	0.150	0.007	5	0
UW 2024	5/6/2024 9:05	5/6/2024 9:15	0.150	0.01	5	0
UW 2024	5/6/2024 9:15	5/6/2024 9:25	0.150	0.012	5	0
UW 2024	5/6/2024 9:25	5/6/2024 9:35	0.150	0.012	5	0
UW 2024	5/6/2024 9:35	5/6/2024 9:45	0.150	0.041	5	0
UW 2024	5/6/2024 9:45	5/6/2024 9:55	0.150	0.043	5	0
UW 2024	5/6/2024 9:55	5/6/2024 10:05	0.150	0.043	5	0
UW 2024	5/6/2024 10:05	5/6/2024 10:15	0.150	0.046	5	0
UW 2024	5/6/2024 10:15	5/6/2024 10:25	0.150	0.048	5	0
UW 2024	5/6/2024 10:25	5/6/2024 10:35	0.150	0.048	5	0
UW 2024	5/6/2024 10:35	5/6/2024 10:45	0.150	0.051	5	0
UW 2024	5/6/2024 10:45	5/6/2024 10:55	0.150	0.054	5	0
UW 2024	5/6/2024 10:55	5/6/2024 11:05	0.150	0.054	5	0
UW 2024	5/6/2024 11:05	5/6/2024 11:15	0.150	0.057	5	0
UW 2024	5/6/2024 11:15	5/6/2024 11:25	0.150	0.06	5	0
UW 2024	5/6/2024 11:25	5/6/2024 11:35	0.150	0.06	5	0
UW 2024	5/6/2024 11:35	5/6/2024 11:45	0.150	0.063	5	0
UW 2024	5/6/2024 11:45	5/6/2024 11:55	0.150	0.066	5	0
UW 2024	5/6/2024 11:55	5/6/2024 12:05	0.150	0.066	5	0
UW 2024	5/6/2024 12:05	5/6/2024 12:15	0.150	0.069	5	0
UW 2024	5/6/2024 12:15	5/6/2024 12:25	0.150	0.071	5	0
UW 2024	5/6/2024 12:25	5/6/2024 12:35	0.150	0.071	5	0
UW 2024	5/6/2024 12:35	5/6/2024 12:45	0.150	0.074	5	0
UW 2024	5/6/2024 12:45	5/6/2024 12:55	0.150	0.077	5	0
UW 2024	5/6/2024 12:55	5/6/2024 13:05	0.150	0.077	5	0
UW 2024	5/6/2024 13:05	5/6/2024 13:15	0.150	0.08	5	0
UW 2024	5/6/2024 13:15	5/6/2024 13:25	0.150	0.083	5	0
UW 2024	5/6/2024 13:25	5/6/2024 13:35	0.150	0.083	5	0
UW 2024	5/6/2024 13:35	5/6/2024 13:45	0.150	0.086	5	0
UW 2024	5/6/2024 13:45	5/6/2024 13:55	0.150	0.089	5	0
UW 2024	5/6/2024 13:55	5/6/2024 14:05	0.150	0.089	5	0
UW 2024	5/6/2024 14:05	5/6/2024 14:15	0.150	0.091	5	0
UW 2024	5/6/2024 14:15	5/6/2024 14:25	0.150	0.094	5	0
UW 2024	5/6/2024 14:25	5/6/2024 14:35	0.150	0.094	5	0
UW 2024	5/6/2024 14:35	5/6/2024 14:45	0.150	0.097	5	0
UW 2024	5/6/2024 14:45	5/6/2024 14:55	0.150	0.099	5	0
UW 2024	5/6/2024 14:55	5/6/2024 15:05	0.150	0.099	5	0
UW 2024	5/6/2024 15:05	5/6/2024 15:15	0.150	0.101	5	0
UW 2024	5/6/2024 15:15	5/6/2024 15:25	0.150	0.103	5	0
UW 2024	5/6/2024 15:25	5/6/2024 15:35	0.150	0.103	5	0
UW 2024	5/6/2024 15:35	5/6/2024 15:45	0.150	0.105	5	0
UW 2024	5/6/2024 15:45	5/6/2024 15:55	0.150	0.108	5	0
UW 2024	5/6/2024 15:55	5/6/2024 16:05	0.150	0.108	5	0
UW 2024	5/6/2024 16:05	5/6/2024 16:15	0.150	0.11	5	0
UW 2024	5/6/2024 16:15	5/6/2024 16:25	0.150	0.11	5	0
UW 2024	5/6/2024 16:25	5/6/2024 16:30	0.150	0.11	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/6/2024 8:25	5/6/2024 8:35	0.150	0	5	0.137
HS South	5/6/2024 8:35	5/6/2024 8:45	0.150	0.005	5	0.141
HS South	5/6/2024 8:45	5/6/2024 8:55	0.150	0.007	5	0.141
HS South	5/6/2024 8:55	5/6/2024 9:05	0.150	0.009	5	0.141
HS South	5/6/2024 9:05	5/6/2024 9:15	0.150	0.011	5	0.141
HS South	5/6/2024 9:15	5/6/2024 9:25	0.150	0.013	5	0.141
HS South	5/6/2024 9:25	5/6/2024 9:35	0.150	0.015	5	0.141
HS South	5/6/2024 9:35	5/6/2024 9:45	0.150	0.017	5	0.141
HS South	5/6/2024 9:45	5/6/2024 9:55	0.150	0.019	5	0.141
HS South	5/6/2024 9:55	5/6/2024 10:05	0.150	0.021	5	0.141
HS South	5/6/2024 10:05	5/6/2024 10:15	0.150	0.023	5	0.141
HS South	5/6/2024 10:15	5/6/2024 10:25	0.150	0.026	5	0.141
HS South	5/6/2024 10:25	5/6/2024 10:35	0.150	0.028	5	0.141
HS South	5/6/2024 10:35	5/6/2024 10:45	0.150	0.031	5	0.141
HS South	5/6/2024 10:45	5/6/2024 10:55	0.150	0.033	5	0.141
HS South	5/6/2024 10:55	5/6/2024 11:05	0.150	0.036	5	0.141
HS South	5/6/2024 11:05	5/6/2024 11:15	0.150	0.038	5	0.141
HS South	5/6/2024 11:15	5/6/2024 11:25	0.150	0.041	5	0.141
HS South	5/6/2024 11:25	5/6/2024 11:35	0.150	0.043	5	0.141
HS South	5/6/2024 11:35	5/6/2024 11:45	0.150	0.046	5	0.141
HS South	5/6/2024 11:45	5/6/2024 11:55	0.150	0.049	5	0.141
HS South	5/6/2024 11:55	5/6/2024 12:05	0.150	0.051	5	0.141
HS South	5/6/2024 12:05	5/6/2024 12:15	0.150	0.053	5	0.141
HS South	5/6/2024 12:15	5/6/2024 12:25	0.150	0.056	5	0.141
HS South	5/6/2024 12:25	5/6/2024 12:35	0.150	0.058	5	0.141
HS South	5/6/2024 12:35	5/6/2024 12:45	0.150	0.06	5	0.141
HS South	5/6/2024 12:45	5/6/2024 12:55	0.150	0.063	5	0.141
HS South	5/6/2024 12:55	5/6/2024 13:05	0.150	0.066	5	0.141
HS South	5/6/2024 13:05	5/6/2024 13:15	0.150	0.069	5	0.141
HS South	5/6/2024 13:15	5/6/2024 13:25	0.150	0.072	5	0.141
HS South	5/6/2024 13:25	5/6/2024 13:35	0.150	0.075	5	0.141
HS South	5/6/2024 13:35	5/6/2024 13:45	0.150	0.078	5	0.141
HS South	5/6/2024 13:45	5/6/2024 13:55	0.150	0.081	5	0.141
HS South	5/6/2024 13:55	5/6/2024 14:05	0.150	0.083	5	0.141
HS South	5/6/2024 14:05	5/6/2024 14:15	0.150	0.086	5	0.141
HS South	5/6/2024 14:15	5/6/2024 14:25	0.150	0.089	5	0.141
HS South	5/6/2024 14:25	5/6/2024 14:35	0.150	0.091	5	0.141
HS South	5/6/2024 14:35	5/6/2024 14:45	0.150	0.093	5	0.141
HS South	5/6/2024 14:45	5/6/2024 14:55	0.150	0.095	5	0.141
HS South	5/6/2024 14:55	5/6/2024 15:05	0.150	0.097	5	0.141
HS South	5/6/2024 15:05	5/6/2024 15:15	0.150	0.099	5	0.141
HS South	5/6/2024 15:15	5/6/2024 15:25	0.150	0.101	5	0.141
HS South	5/6/2024 15:25	5/6/2024 15:35	0.150	0.103	5	0.141
HS South	5/6/2024 15:35	5/6/2024 15:45	0.150	0.106	5	0.141
HS South	5/6/2024 15:45	5/6/2024 15:55	0.150	0.106	5	0.141
HS South	5/6/2024 15:55	5/6/2024 16:05	0.150	0.106	5	0.141
HS South	5/6/2024 16:05	5/6/2024 16:15	0.150	0.106	5	0.141
HS South	5/6/2024 16:15	5/6/2024 16:25	0.150	0.106	5	0.141
HS South	5/6/2024 16:25	5/6/2024 16:30	0.150	0.106	5	0.141

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/6/2024 8:15	5/6/2024 8:25	0.150	0.005	5	0
PER2 2024	5/6/2024 8:25	5/6/2024 8:35	0.150	0.005	5	0
PER2 2024	5/6/2024 8:35	5/6/2024 8:45	0.150	0.005	5	0
PER2 2024	5/6/2024 8:45	5/6/2024 8:55	0.150	0.005	5	0
PER2 2024	5/6/2024 8:55	5/6/2024 9:05	0.150	0.005	5	0
PER2 2024	5/6/2024 9:05	5/6/2024 9:15	0.150	0.005	5	0
PER2 2024	5/6/2024 9:15	5/6/2024 9:25	0.150	0.003	5	0
PER2 2024	5/6/2024 9:25	5/6/2024 9:35	0.150	0.005	5	0
PER2 2024	5/6/2024 9:35	5/6/2024 9:45	0.150	0.006	5	0
PER2 2024	5/6/2024 9:45	5/6/2024 9:55	0.150	0.008	5	0
PER2 2024	5/6/2024 9:55	5/6/2024 10:05	0.150	0.009	5	0
PER2 2024	5/6/2024 10:05	5/6/2024 10:15	0.150	0.011	5	0
PER2 2024	5/6/2024 10:15	5/6/2024 10:25	0.150	0.012	5	0
PER2 2024	5/6/2024 10:25	5/6/2024 10:35	0.150	0.014	5	0
PER2 2024	5/6/2024 10:35	5/6/2024 10:45	0.150	0.016	5	0
PER2 2024	5/6/2024 10:45	5/6/2024 10:55	0.150	0.017	5	0
PER2 2024	5/6/2024 10:55	5/6/2024 11:05	0.150	0.019	5	0
PER2 2024	5/6/2024 11:05	5/6/2024 11:15	0.150	0.021	5	0
PER2 2024	5/6/2024 11:15	5/6/2024 11:25	0.150	0.023	5	0
PER2 2024	5/6/2024 11:25	5/6/2024 11:35	0.150	0.024	5	0
PER2 2024	5/6/2024 11:35	5/6/2024 11:45	0.150	0.026	5	0
PER2 2024	5/6/2024 11:45	5/6/2024 11:55	0.150	0.028	5	0
PER2 2024	5/6/2024 11:55	5/6/2024 12:05	0.150	0.03	5	0
PER2 2024	5/6/2024 12:05	5/6/2024 12:15	0.150	0.031	5	0
PER2 2024	5/6/2024 12:15	5/6/2024 12:25	0.150	0.033	5	0
PER2 2024	5/6/2024 12:25	5/6/2024 12:35	0.150	0.034	5	0
PER2 2024	5/6/2024 12:35	5/6/2024 12:45	0.150	0.036	5	0
PER2 2024	5/6/2024 12:45	5/6/2024 12:55	0.150	0.038	5	0
PER2 2024	5/6/2024 12:55	5/6/2024 13:05	0.150	0.039	5	0
PER2 2024	5/6/2024 13:05	5/6/2024 13:15	0.150	0.041	5	0
PER2 2024	5/6/2024 13:15	5/6/2024 13:25	0.150	0.043	5	0
PER2 2024	5/6/2024 13:25	5/6/2024 13:35	0.150	0.045	5	0
PER2 2024	5/6/2024 13:35	5/6/2024 13:45	0.150	0.047	5	0
PER2 2024	5/6/2024 13:45	5/6/2024 13:55	0.150	0.049	5	0
PER2 2024	5/6/2024 13:55	5/6/2024 14:05	0.150	0.051	5	0
PER2 2024	5/6/2024 14:05	5/6/2024 14:15	0.150	0.053	5	0
PER2 2024	5/6/2024 14:15	5/6/2024 14:25	0.150	0.055	5	0
PER2 2024	5/6/2024 14:25	5/6/2024 14:35	0.150	0.056	5	0
PER2 2024	5/6/2024 14:35	5/6/2024 14:45	0.150	0.057	5	0
PER2 2024	5/6/2024 14:45	5/6/2024 14:55	0.150	0.059	5	0
PER2 2024	5/6/2024 14:55	5/6/2024 15:05	0.150	0.06	5	0
PER2 2024	5/6/2024 15:05	5/6/2024 15:15	0.150	0.061	5	0
PER2 2024	5/6/2024 15:15	5/6/2024 15:25	0.150	0.062	5	0
PER2 2024	5/6/2024 15:25	5/6/2024 15:35	0.150	0.063	5	0
PER2 2024	5/6/2024 15:35	5/6/2024 15:45	0.150	0.065	5	0
PER2 2024	5/6/2024 15:45	5/6/2024 15:55	0.150	0.066	5	0
PER2 2024	5/6/2024 15:55	5/6/2024 16:05	0.150	0.068	5	0
PER2 2024	5/6/2024 16:05	5/6/2024 16:15	0.150	0.068	5	0
PER2 2024	5/6/2024 16:15	5/6/2024 16:25	0.150	0.068	5	0
PER2 2024	5/6/2024 16:25	5/6/2024 16:30	0.150	0.068	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/6/2024 8:15	5/6/2024 8:25	0.150	0.005	5	0
PER1 2024	5/6/2024 8:25	5/6/2024 8:35	0.150	0.006	5	0
PER1 2024	5/6/2024 8:35	5/6/2024 8:45	0.150	0.007	5	0
PER1 2024	5/6/2024 8:45	5/6/2024 8:55	0.150	0.008	5	0
PER1 2024	5/6/2024 8:55	5/6/2024 9:05	0.150	0.009	5	0
PER1 2024	5/6/2024 9:05	5/6/2024 9:15	0.150	0.011	5	0
PER1 2024	5/6/2024 9:15	5/6/2024 9:25	0.150	0.012	5	0
PER1 2024	5/6/2024 9:25	5/6/2024 9:35	0.150	0.013	5	0
PER1 2024	5/6/2024 9:35	5/6/2024 9:45	0.150	0.014	5	0
PER1 2024	5/6/2024 9:45	5/6/2024 9:55	0.150	0.015	5	0
PER1 2024	5/6/2024 9:55	5/6/2024 10:05	0.150	0.017	5	0
PER1 2024	5/6/2024 10:05	5/6/2024 10:15	0.150	0.018	5	0
PER1 2024	5/6/2024 10:15	5/6/2024 10:25	0.150	0.019	5	0
PER1 2024	5/6/2024 10:25	5/6/2024 10:35	0.150	0.021	5	0
PER1 2024	5/6/2024 10:35	5/6/2024 10:45	0.150	0.022	5	0
PER1 2024	5/6/2024 10:45	5/6/2024 10:55	0.150	0.024	5	0
PER1 2024	5/6/2024 10:55	5/6/2024 11:05	0.150	0.025	5	0
PER1 2024	5/6/2024 11:05	5/6/2024 11:15	0.150	0.027	5	0
PER1 2024	5/6/2024 11:15	5/6/2024 11:25	0.150	0.029	5	0
PER1 2024	5/6/2024 11:25	5/6/2024 11:35	0.150	0.03	5	0
PER1 2024	5/6/2024 11:35	5/6/2024 11:45	0.150	0.032	5	0
PER1 2024	5/6/2024 11:45	5/6/2024 11:55	0.150	0.033	5	0
PER1 2024	5/6/2024 11:55	5/6/2024 12:05	0.150	0.034	5	0
PER1 2024	5/6/2024 12:05	5/6/2024 12:15	0.150	0.036	5	0
PER1 2024	5/6/2024 12:15	5/6/2024 12:25	0.150	0.037	5	0
PER1 2024	5/6/2024 12:25	5/6/2024 12:35	0.150	0.038	5	0
PER1 2024	5/6/2024 12:35	5/6/2024 12:45	0.150	0.04	5	0
PER1 2024	5/6/2024 12:45	5/6/2024 12:55	0.150	0.041	5	0
PER1 2024	5/6/2024 12:55	5/6/2024 13:05	0.150	0.043	5	0
PER1 2024	5/6/2024 13:05	5/6/2024 13:15	0.150	0.044	5	0
PER1 2024	5/6/2024 13:15	5/6/2024 13:25	0.150	0.046	5	0
PER1 2024	5/6/2024 13:25	5/6/2024 13:35	0.150	0.048	5	0
PER1 2024	5/6/2024 13:35	5/6/2024 13:45	0.150	0.049	5	0
PER1 2024	5/6/2024 13:45	5/6/2024 13:55	0.150	0.051	5	0
PER1 2024	5/6/2024 13:55	5/6/2024 14:05	0.150	0.053	5	0
PER1 2024	5/6/2024 14:05	5/6/2024 14:15	0.150	0.054	5	0
PER1 2024	5/6/2024 14:15	5/6/2024 14:25	0.150	0.056	5	0
PER1 2024	5/6/2024 14:25	5/6/2024 14:35	0.150	0.057	5	0
PER1 2024	5/6/2024 14:35	5/6/2024 14:45	0.150	0.058	5	0
PER1 2024	5/6/2024 14:45	5/6/2024 14:55	0.150	0.059	5	0
PER1 2024	5/6/2024 14:55	5/6/2024 15:05	0.150	0.061	5	0
PER1 2024	5/6/2024 15:05	5/6/2024 15:15	0.150	0.062	5	0
PER1 2024	5/6/2024 15:15	5/6/2024 15:25	0.150	0.063	5	0
PER1 2024	5/6/2024 15:25	5/6/2024 15:35	0.150	0.064	5	0
PER1 2024	5/6/2024 15:35	5/6/2024 15:45	0.150	0.066	5	0
PER1 2024	5/6/2024 15:45	5/6/2024 15:55	0.150	0.066	5	0
PER1 2024	5/6/2024 15:55	5/6/2024 16:05	0.150	0.066	5	0
PER1 2024	5/6/2024 16:05	5/6/2024 16:15	0.150	0	5	0
PER1 2024	5/6/2024 16:15	5/6/2024 16:25	0.150	0	5	0
PER1 2024	5/6/2024 16:25	5/6/2024 16:30	0.150	0	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/07/2024

Weather: 80 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development.

Is the dewatering system operating: YES NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.

Upwind VOC data is not available for the workday, the UW PID was used for soil screening .


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8585	1520	4140

Site Layout Map and Excavation Figures

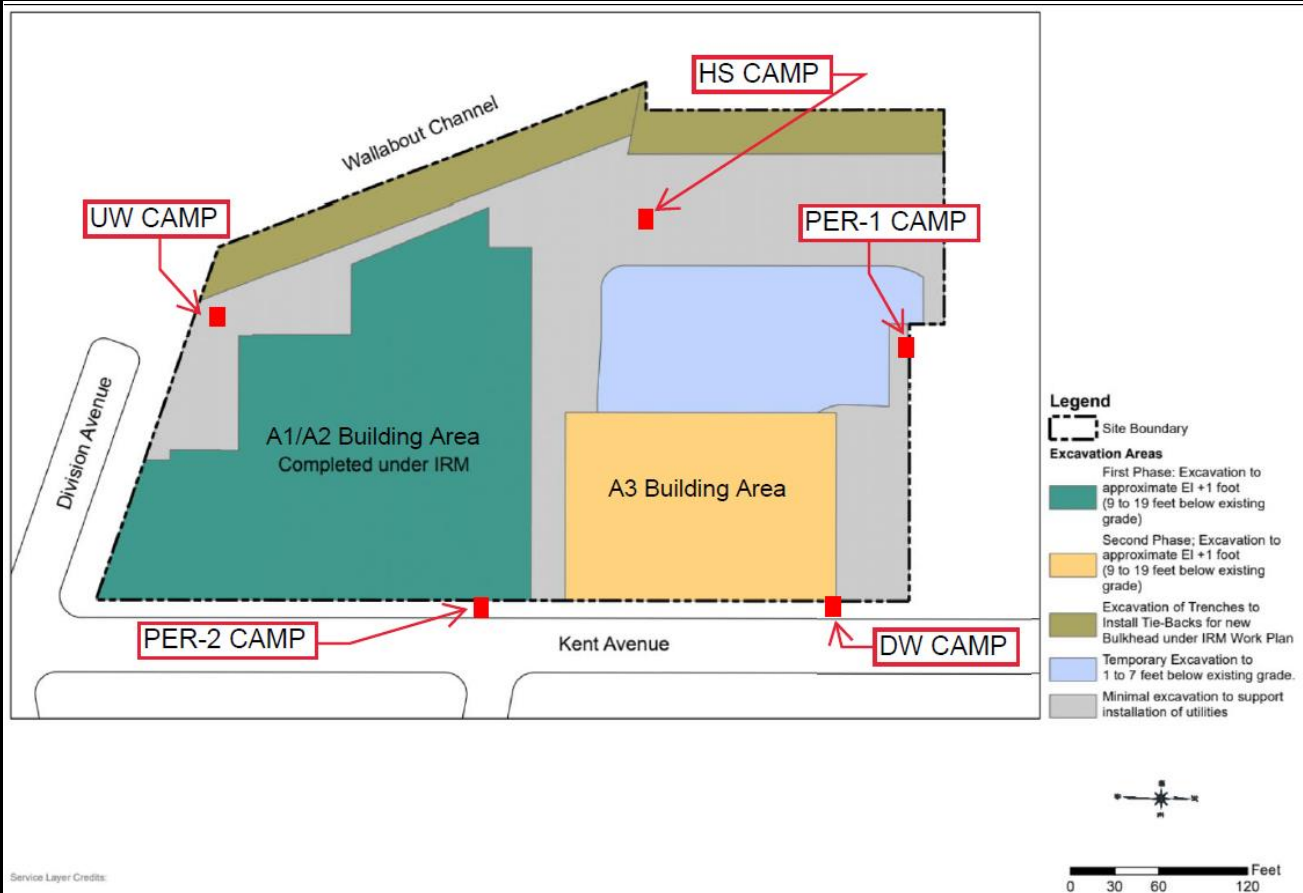

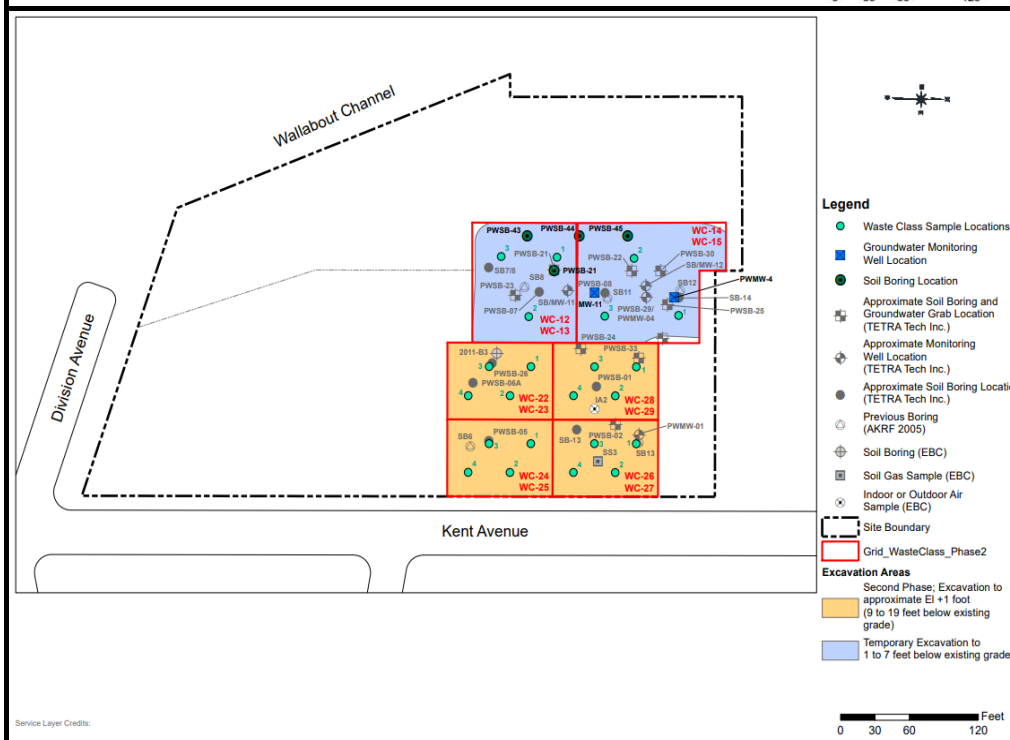
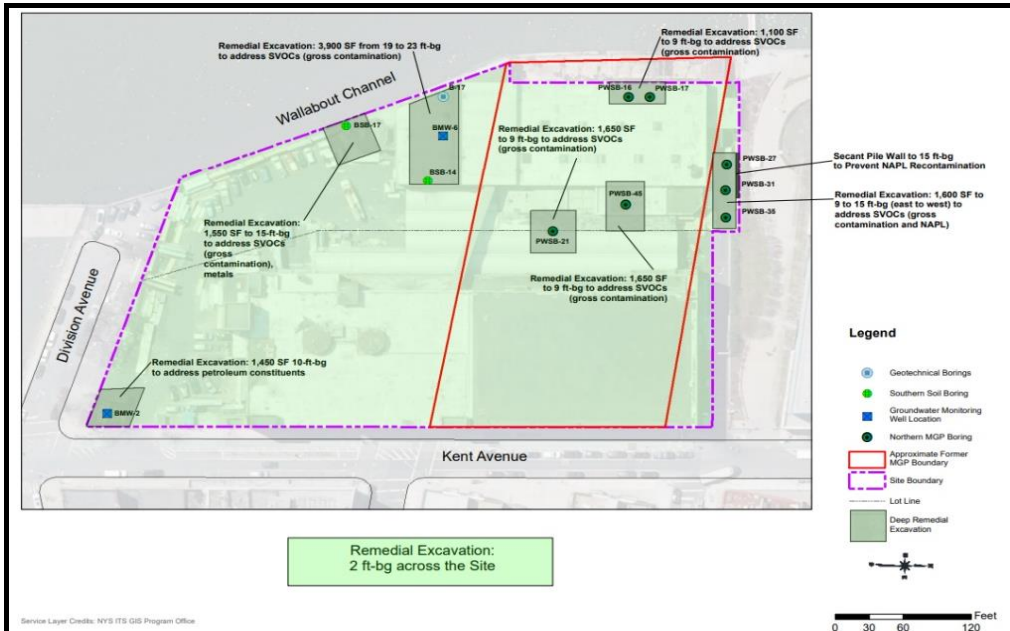


Photo 1:
View of Site conditions
and activities facing
northeast.




Photo 2:
View of Site conditions
facing southeast.



Photo 3:
View of Site
activities and
waterproofing
installation.




Photo 4:
View of Site
activities and
waterproofing
installation.

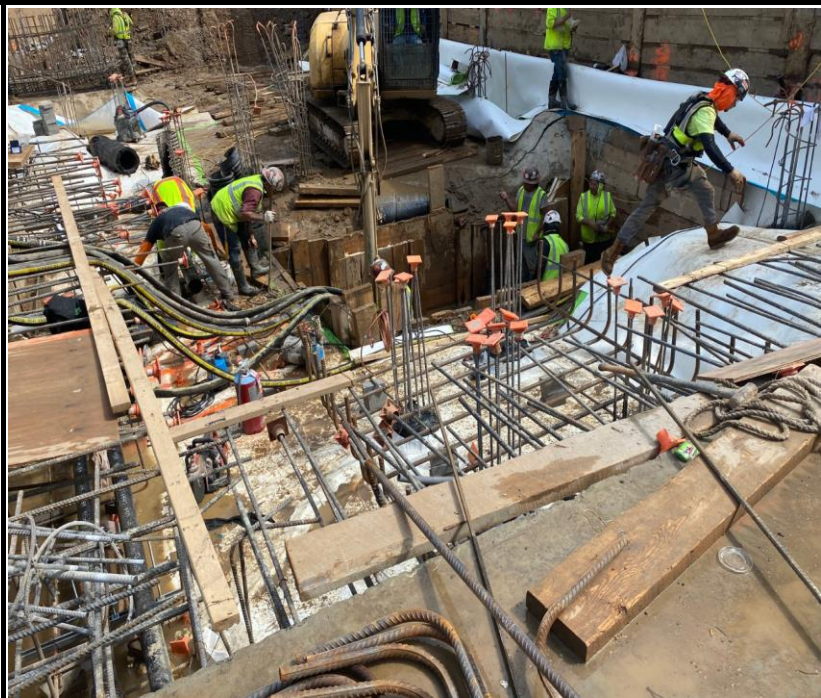

CAMP:
Downwind
Particulates

Dust Levels


0.003 mg/m³ 0.008 mg/m³

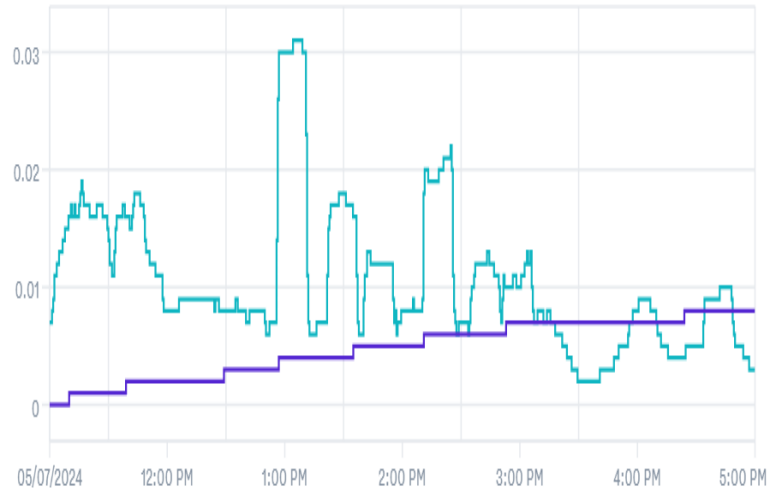

CAMP:
Downwind VOCs


VOC Levels

0 ppm 0 ppm

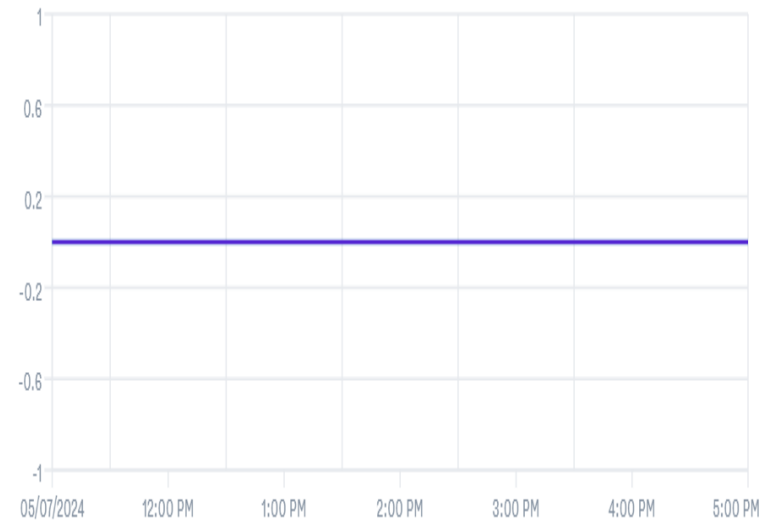

CAMP:
Upwind Particulates

Dust Levels

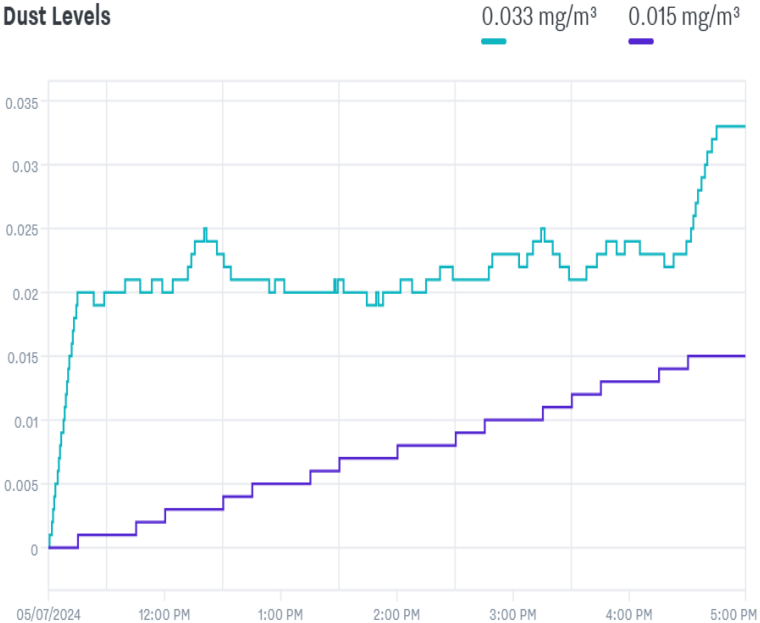

CAMP:
Upwind VOCs

NA

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/7/2024 11:00	5/7/2024 11:10	0.150	0.001	5	0
DW 2024	5/7/2024 11:10	5/7/2024 11:20	0.150	0.001	5	0
DW 2024	5/7/2024 11:20	5/7/2024 11:30	0.150	0.001	5	0
DW 2024	5/7/2024 11:30	5/7/2024 11:40	0.150	0.002	5	0
DW 2024	5/7/2024 11:40	5/7/2024 11:50	0.150	0.002	5	0
DW 2024	5/7/2024 11:50	5/7/2024 12:00	0.150	0.002	5	0
DW 2024	5/7/2024 12:00	5/7/2024 12:10	0.150	0.002	5	0
DW 2024	5/7/2024 12:10	5/7/2024 12:20	0.150	0.002	5	0
DW 2024	5/7/2024 12:20	5/7/2024 12:30	0.150	0.003	5	0
DW 2024	5/7/2024 12:30	5/7/2024 12:40	0.150	0.003	5	0
DW 2024	5/7/2024 12:40	5/7/2024 12:50	0.150	0.003	5	0
DW 2024	5/7/2024 12:50	5/7/2024 13:00	0.150	0.004	5	0
DW 2024	5/7/2024 13:00	5/7/2024 13:10	0.150	0.004	5	0
DW 2024	5/7/2024 13:10	5/7/2024 13:20	0.150	0.004	5	0
DW 2024	5/7/2024 13:20	5/7/2024 13:30	0.150	0.004	5	0
DW 2024	5/7/2024 13:30	5/7/2024 13:40	0.150	0.005	5	0
DW 2024	5/7/2024 13:40	5/7/2024 13:50	0.150	0.005	5	0
DW 2024	5/7/2024 13:50	5/7/2024 14:00	0.150	0.005	5	0
DW 2024	5/7/2024 14:00	5/7/2024 14:10	0.150	0.005	5	0
DW 2024	5/7/2024 14:10	5/7/2024 14:20	0.150	0.006	5	0
DW 2024	5/7/2024 14:20	5/7/2024 14:30	0.150	0.006	5	0
DW 2024	5/7/2024 14:30	5/7/2024 14:40	0.150	0.006	5	0
DW 2024	5/7/2024 14:40	5/7/2024 14:50	0.150	0.006	5	0
DW 2024	5/7/2024 14:50	5/7/2024 15:00	0.150	0.007	5	0
DW 2024	5/7/2024 15:00	5/7/2024 15:10	0.150	0.007	5	0
DW 2024	5/7/2024 15:10	5/7/2024 15:20	0.150	0.007	5	0
DW 2024	5/7/2024 15:20	5/7/2024 15:30	0.150	0.007	5	0
DW 2024	5/7/2024 15:30	5/7/2024 15:40	0.150	0.007	5	0
DW 2024	5/7/2024 15:40	5/7/2024 15:50	0.150	0.007	5	0
DW 2024	5/7/2024 15:50	5/7/2024 16:00	0.150	0.007	5	0
DW 2024	5/7/2024 16:00	5/7/2024 16:10	0.150	0.007	5	0
DW 2024	5/7/2024 16:10	5/7/2024 16:20	0.150	0.007	5	0
DW 2024	5/7/2024 16:20	5/7/2024 16:30	0.150	0.008	5	0
DW 2024	5/7/2024 16:30	5/7/2024 16:40	0.150	0.008	5	0
DW 2024	5/7/2024 16:40	5/7/2024 16:50	0.150	0.008	5	0
DW 2024	5/7/2024 16:50	5/7/2024 17:00	0.150	0.008	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/7/2024 11:00	5/7/2024 11:10	0.150	0	5	0
UW 2024	5/7/2024 11:10	5/7/2024 11:20	0.150	0.001	5	0
UW 2024	5/7/2024 11:20	5/7/2024 11:30	0.150	0.001	5	0
UW 2024	5/7/2024 11:30	5/7/2024 11:40	0.150	0.001	5	0
UW 2024	5/7/2024 11:40	5/7/2024 11:50	0.150	0.002	5	0
UW 2024	5/7/2024 11:50	5/7/2024 12:00	0.150	0.002	5	0
UW 2024	5/7/2024 12:00	5/7/2024 12:10	0.150	0.003	5	0
UW 2024	5/7/2024 12:10	5/7/2024 12:20	0.150	0.003	5	0
UW 2024	5/7/2024 12:20	5/7/2024 12:30	0.150	0.003	5	0
UW 2024	5/7/2024 12:30	5/7/2024 12:40	0.150	0.004	5	0
UW 2024	5/7/2024 12:40	5/7/2024 12:50	0.150	0.005	5	0
UW 2024	5/7/2024 12:50	5/7/2024 13:00	0.150	0.005	5	0
UW 2024	5/7/2024 13:00	5/7/2024 13:10	0.150	0.005	5	0
UW 2024	5/7/2024 13:10	5/7/2024 13:20	0.150	0.006	5	0
UW 2024	5/7/2024 13:20	5/7/2024 13:30	0.150	0.006	5	0
UW 2024	5/7/2024 13:30	5/7/2024 13:40	0.150	0.007	5	0
UW 2024	5/7/2024 13:40	5/7/2024 13:50	0.150	0.007	5	0
UW 2024	5/7/2024 13:50	5/7/2024 14:00	0.150	0.007	5	0
UW 2024	5/7/2024 14:00	5/7/2024 14:10	0.150	0.008	5	0
UW 2024	5/7/2024 14:10	5/7/2024 14:20	0.150	0.008	5	0
UW 2024	5/7/2024 14:20	5/7/2024 14:30	0.150	0.008	5	0
UW 2024	5/7/2024 14:30	5/7/2024 14:40	0.150	0.009	5	0
UW 2024	5/7/2024 14:40	5/7/2024 14:50	0.150	0.01	5	0
UW 2024	5/7/2024 14:50	5/7/2024 15:00	0.150	0.01	5	0
UW 2024	5/7/2024 15:00	5/7/2024 15:10	0.150	0.01	5	0
UW 2024	5/7/2024 15:10	5/7/2024 15:20	0.150	0.011	5	0
UW 2024	5/7/2024 15:20	5/7/2024 15:30	0.150	0.011	5	0
UW 2024	5/7/2024 15:30	5/7/2024 15:40	0.150	0.012	5	0
UW 2024	5/7/2024 15:40	5/7/2024 15:50	0.150	0.013	5	0
UW 2024	5/7/2024 15:50	5/7/2024 16:00	0.150	0.013	5	0
UW 2024	5/7/2024 16:00	5/7/2024 16:10	0.150	0.013	5	0
UW 2024	5/7/2024 16:10	5/7/2024 16:20	0.150	0.014	5	0
UW 2024	5/7/2024 16:20	5/7/2024 16:30	0.150	0.014	5	0
UW 2024	5/7/2024 16:30	5/7/2024 16:40	0.150	0.015	5	0
UW 2024	5/7/2024 16:40	5/7/2024 16:50	0.150	0.015	5	0
UW 2024	5/7/2024 16:50	5/7/2024 17:00	0.150	0.015	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/7/2024 11:20	5/7/2024 11:30	0.150	0	5	0
HS South	5/7/2024 11:30	5/7/2024 11:40	0.150	0.001	5	0
HS South	5/7/2024 11:40	5/7/2024 11:50	0.150	0.001	5	0
HS South	5/7/2024 11:50	5/7/2024 12:00	0.150	0.002	5	0
HS South	5/7/2024 12:00	5/7/2024 12:10	0.150	0.003	5	0
HS South	5/7/2024 12:10	5/7/2024 12:20	0.150	0.003	5	0
HS South	5/7/2024 12:20	5/7/2024 12:30	0.150	0.004	5	0
HS South	5/7/2024 12:30	5/7/2024 12:40	0.150	0.005	5	0
HS South	5/7/2024 12:40	5/7/2024 12:50	0.150	0.005	5	0
HS South	5/7/2024 12:50	5/7/2024 13:00	0.150	0.006	5	0
HS South	5/7/2024 13:00	5/7/2024 13:10	0.150	0.006	5	0
HS South	5/7/2024 13:10	5/7/2024 13:20	0.150	0.007	5	0
HS South	5/7/2024 13:20	5/7/2024 13:30	0.150	0.008	5	0
HS South	5/7/2024 13:30	5/7/2024 13:40	0.150	0.008	5	0
HS South	5/7/2024 13:40	5/7/2024 13:50	0.150	0.009	5	0
HS South	5/7/2024 13:50	5/7/2024 14:00	0.150	0.01	5	0
HS South	5/7/2024 14:00	5/7/2024 14:10	0.150	0.011	5	0
HS South	5/7/2024 14:10	5/7/2024 14:20	0.150	0.011	5	0
HS South	5/7/2024 14:20	5/7/2024 14:30	0.150	0.012	5	0
HS South	5/7/2024 14:30	5/7/2024 14:40	0.150	0.013	5	0
HS South	5/7/2024 14:40	5/7/2024 14:50	0.150	0.014	5	0
HS South	5/7/2024 14:50	5/7/2024 15:00	0.150	0.014	5	0
HS South	5/7/2024 15:00	5/7/2024 15:10	0.150	0.015	5	0
HS South	5/7/2024 15:10	5/7/2024 15:20	0.150	0.016	5	0
HS South	5/7/2024 15:20	5/7/2024 15:30	0.150	0.017	5	0
HS South	5/7/2024 15:30	5/7/2024 15:40	0.150	0.018	5	0
HS South	5/7/2024 15:40	5/7/2024 15:50	0.150	0.019	5	0
HS South	5/7/2024 15:50	5/7/2024 16:00	0.150	0.02	5	0
HS South	5/7/2024 16:00	5/7/2024 16:10	0.150	0.021	5	0
HS South	5/7/2024 16:10	5/7/2024 16:20	0.150	0.021	5	0
HS South	5/7/2024 16:20	5/7/2024 16:30	0.150	0.022	5	0
HS South	5/7/2024 16:30	5/7/2024 16:40	0.150	0.023	5	0
HS South	5/7/2024 16:40	5/7/2024 16:50	0.150	0.023	5	0
HS South	5/7/2024 16:50	5/7/2024 17:00	0.150	0.023	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/7/2024 11:20	5/7/2024 11:30	0.150	0	5	0
PER2 2024	5/7/2024 11:30	5/7/2024 11:40	0.150	0.001	5	0
PER2 2024	5/7/2024 11:40	5/7/2024 11:50	0.150	0.001	5	0
PER2 2024	5/7/2024 11:50	5/7/2024 12:00	0.150	0.001	5	0
PER2 2024	5/7/2024 12:00	5/7/2024 12:10	0.150	0.001	5	0
PER2 2024	5/7/2024 12:10	5/7/2024 12:20	0.150	0.001	5	0
PER2 2024	5/7/2024 12:20	5/7/2024 12:30	0.150	0.001	5	0
PER2 2024	5/7/2024 12:30	5/7/2024 12:40	0.150	0.001	5	0
PER2 2024	5/7/2024 12:40	5/7/2024 12:50	0.150	0.002	5	0
PER2 2024	5/7/2024 12:50	5/7/2024 13:00	0.150	0.002	5	0
PER2 2024	5/7/2024 13:00	5/7/2024 13:10	0.150	0.002	5	0
PER2 2024	5/7/2024 13:10	5/7/2024 13:20	0.150	0.002	5	0
PER2 2024	5/7/2024 13:20	5/7/2024 13:30	0.150	0.002	5	0
PER2 2024	5/7/2024 13:30	5/7/2024 13:40	0.150	0.003	5	0
PER2 2024	5/7/2024 13:40	5/7/2024 13:50	0.150	0.003	5	0
PER2 2024	5/7/2024 13:50	5/7/2024 14:00	0.150	0.003	5	0
PER2 2024	5/7/2024 14:00	5/7/2024 14:10	0.150	0.003	5	0
PER2 2024	5/7/2024 14:10	5/7/2024 14:20	0.150	0.004	5	0
PER2 2024	5/7/2024 14:20	5/7/2024 14:30	0.150	0.004	5	0
PER2 2024	5/7/2024 14:30	5/7/2024 14:40	0.150	0.005	5	0
PER2 2024	5/7/2024 14:40	5/7/2024 14:50	0.150	0.005	5	0
PER2 2024	5/7/2024 14:50	5/7/2024 15:00	0.150	0.005	5	0
PER2 2024	5/7/2024 15:00	5/7/2024 15:10	0.150	0.006	5	0
PER2 2024	5/7/2024 15:10	5/7/2024 15:20	0.150	0.006	5	0
PER2 2024	5/7/2024 15:20	5/7/2024 15:30	0.150	0.006	5	0
PER2 2024	5/7/2024 15:30	5/7/2024 15:40	0.150	0.006	5	0
PER2 2024	5/7/2024 15:40	5/7/2024 15:50	0.150	0.006	5	0
PER2 2024	5/7/2024 15:50	5/7/2024 16:00	0.150	0.006	5	0
PER2 2024	5/7/2024 16:00	5/7/2024 16:10	0.150	0.006	5	0
PER2 2024	5/7/2024 16:10	5/7/2024 16:20	0.150	0.006	5	0
PER2 2024	5/7/2024 16:20	5/7/2024 16:30	0.150	0.006	5	0
PER2 2024	5/7/2024 16:30	5/7/2024 16:40	0.150	0.006	5	0
PER2 2024	5/7/2024 16:40	5/7/2024 16:50	0.150	0.006	5	0
PER2 2024	5/7/2024 16:50	5/7/2024 17:00	0.150	0.006	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/7/2024 11:20	5/7/2024 11:30	0.150	0	5	0
PER1 2024	5/7/2024 11:30	5/7/2024 11:40	0.150	0.001	5	0
PER1 2024	5/7/2024 11:40	5/7/2024 11:50	0.150	0.001	5	0
PER1 2024	5/7/2024 11:50	5/7/2024 12:00	0.150	0.001	5	0
PER1 2024	5/7/2024 12:00	5/7/2024 12:10	0.150	0.001	5	0
PER1 2024	5/7/2024 12:10	5/7/2024 12:20	0.150	0.001	5	0
PER1 2024	5/7/2024 12:20	5/7/2024 12:30	0.150	0.001	5	0
PER1 2024	5/7/2024 12:30	5/7/2024 12:40	0.150	0.002	5	0
PER1 2024	5/7/2024 12:40	5/7/2024 12:50	0.150	0.002	5	0
PER1 2024	5/7/2024 12:50	5/7/2024 13:00	0.150	0.002	5	0
PER1 2024	5/7/2024 13:00	5/7/2024 13:10	0.150	0.002	5	0
PER1 2024	5/7/2024 13:10	5/7/2024 13:20	0.150	0.002	5	0
PER1 2024	5/7/2024 13:20	5/7/2024 13:30	0.150	0.002	5	0
PER1 2024	5/7/2024 13:30	5/7/2024 13:40	0.150	0.003	5	0
PER1 2024	5/7/2024 13:40	5/7/2024 13:50	0.150	0.003	5	0
PER1 2024	5/7/2024 13:50	5/7/2024 14:00	0.150	0.003	5	0
PER1 2024	5/7/2024 14:00	5/7/2024 14:10	0.150	0.003	5	0
PER1 2024	5/7/2024 14:10	5/7/2024 14:20	0.150	0.003	5	0
PER1 2024	5/7/2024 14:20	5/7/2024 14:30	0.150	0.003	5	0.002
PER1 2024	5/7/2024 14:30	5/7/2024 14:40	0.150	0.003	5	0.009
PER1 2024	5/7/2024 14:40	5/7/2024 14:50	0.150	0.004	5	0.009
PER1 2024	5/7/2024 14:50	5/7/2024 15:00	0.150	0.004	5	0.032
PER1 2024	5/7/2024 15:00	5/7/2024 15:10	0.150	0.004	5	0.034
PER1 2024	5/7/2024 15:10	5/7/2024 15:20	0.150	0.004	5	0.043
PER1 2024	5/7/2024 15:20	5/7/2024 15:30	0.150	0.004	5	0.047
PER1 2024	5/7/2024 15:30	5/7/2024 15:40	0.150	0.004	5	0.05
PER1 2024	5/7/2024 15:40	5/7/2024 15:50	0.150	0.005	5	0.052
PER1 2024	5/7/2024 15:50	5/7/2024 16:00	0.150	0.005	5	0.054
PER1 2024	5/7/2024 16:00	5/7/2024 16:10	0.150	0.005	5	0.054
PER1 2024	5/7/2024 16:10	5/7/2024 16:20	0.150	0.005	5	0.054
PER1 2024	5/7/2024 16:20	5/7/2024 16:30	0.150	0.006	5	0.054
PER1 2024	5/7/2024 16:30	5/7/2024 16:40	0.150	0.006	5	0.054
PER1 2024	5/7/2024 16:40	5/7/2024 16:50	0.150	0.006	5	0
PER1 2024	5/7/2024 16:50	5/7/2024 17:00	0.150	0	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/08/2024

Weather: 80 deg. F, Rain/Party cloudy

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development.
- 2) Export of 2 loads (~40 CY) of material from WC-27 for off-site disposal at the MSM facility.
- 3) Export of 1 load (~20 CY) of mixed demolition debris for off-site disposal at the MSM facility.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	60	0	0
Total:(CY)	4485	0	8645	1520	4140

Site Layout Map and Excavation Figures

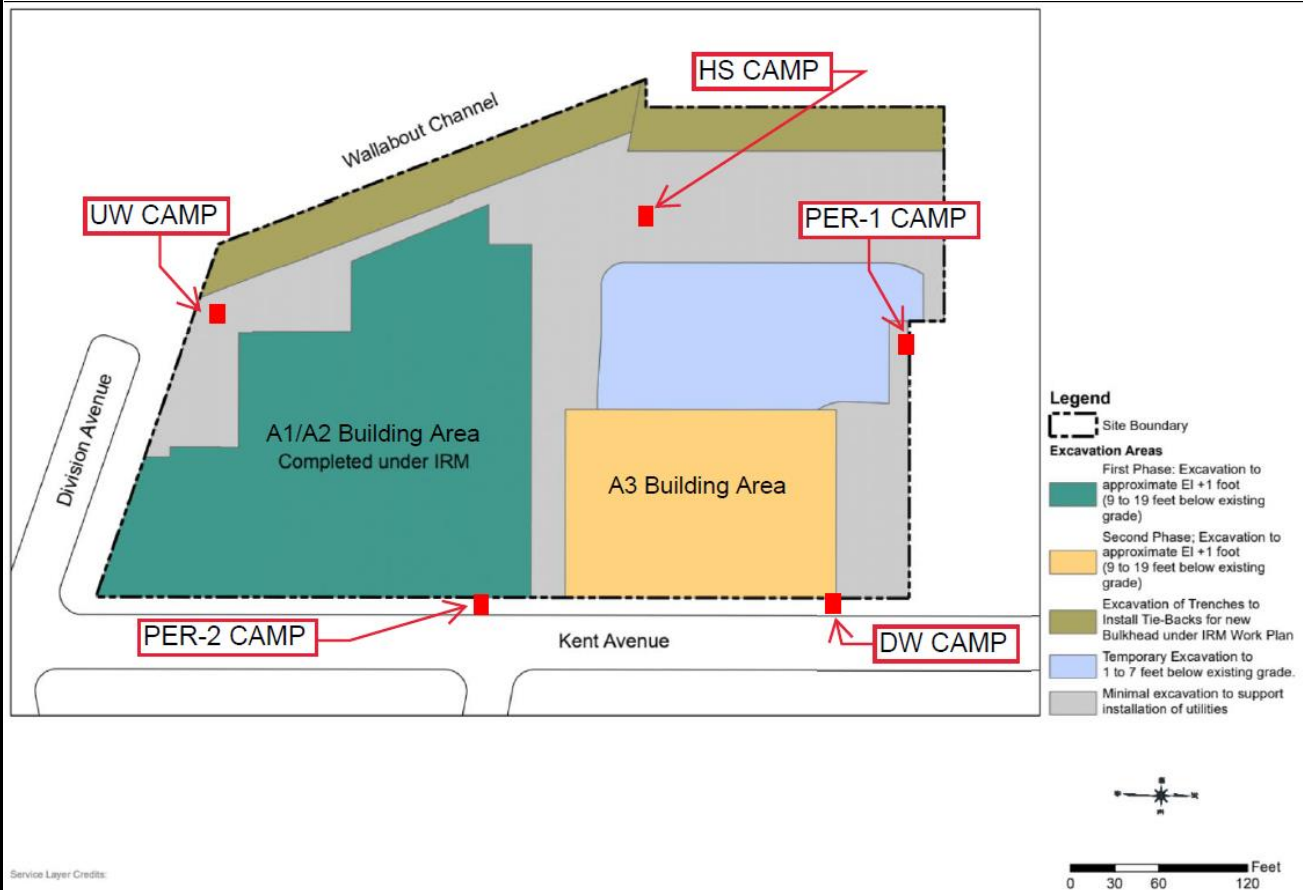

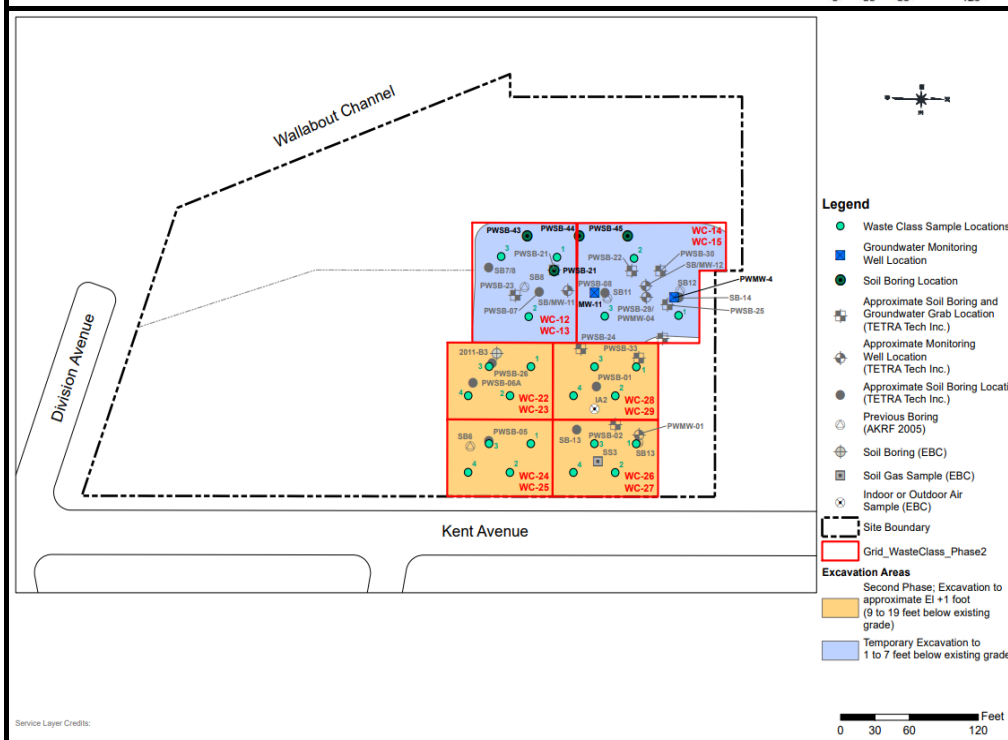
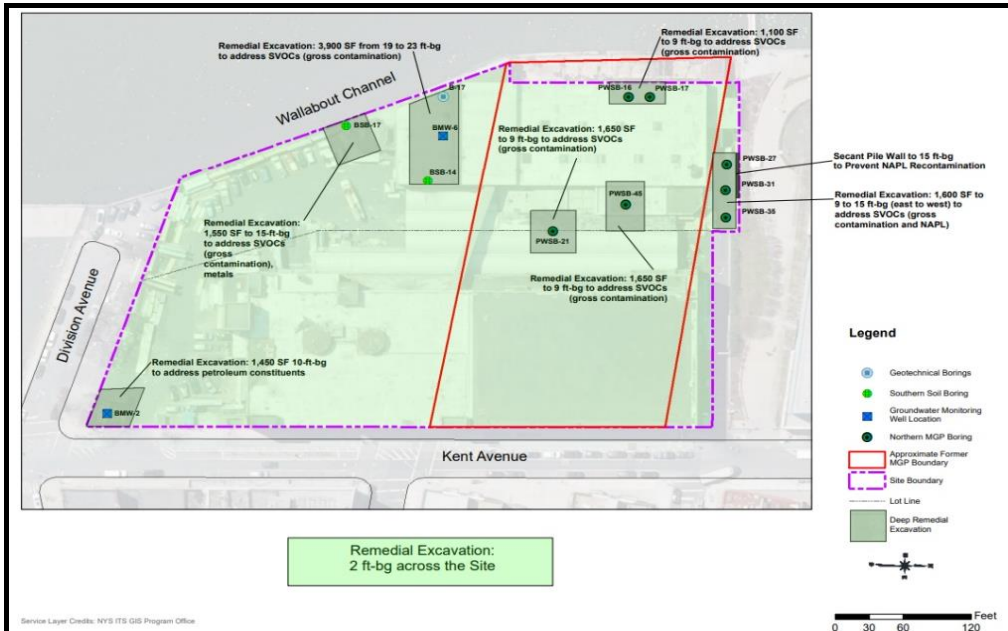


Photo 1:
View of Site conditions
and concrete pouring
facing northeast.



Photo 2:
View of Site conditions
and soil excavation
facing north.

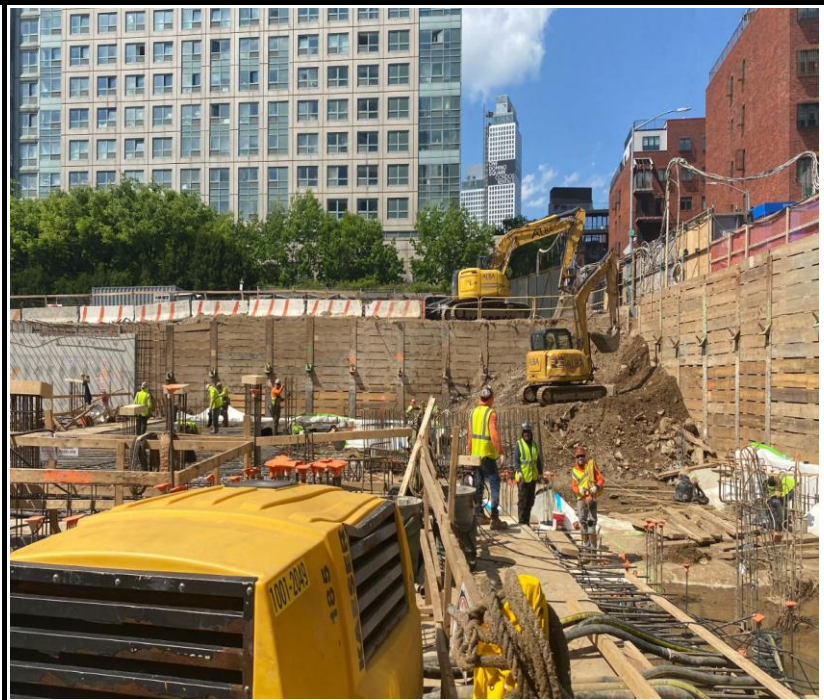


Photo 3:
View of rebar
installation facing
northeast.

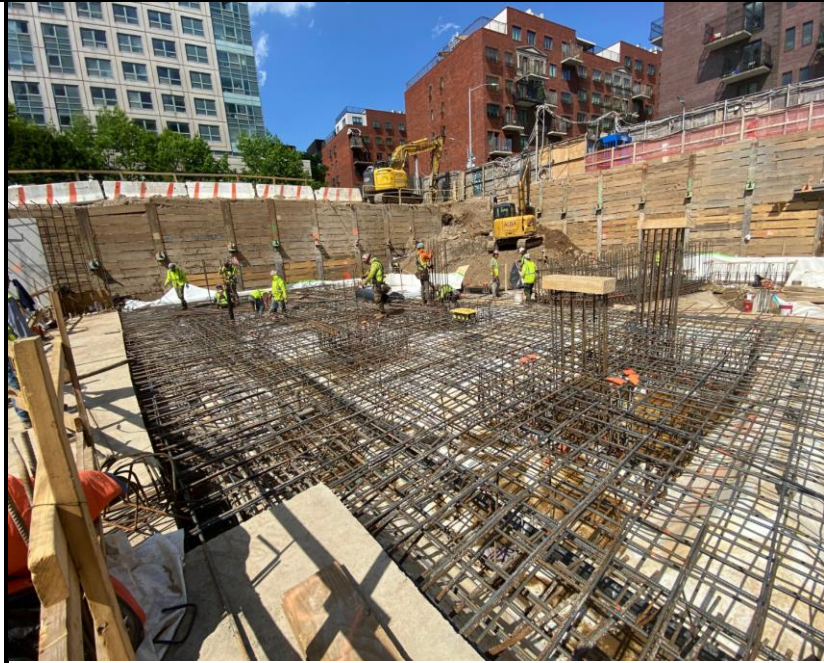



Photo 4:
View of Site
activities and
waterproofing
installation.



CAMP:
Downwind
Particulates

Dust Levels


0.008 mg/m³ 0.037 mg/m³

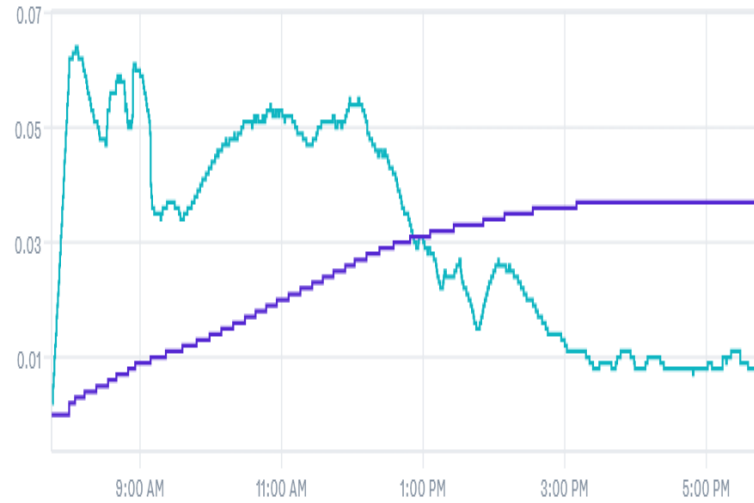

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm

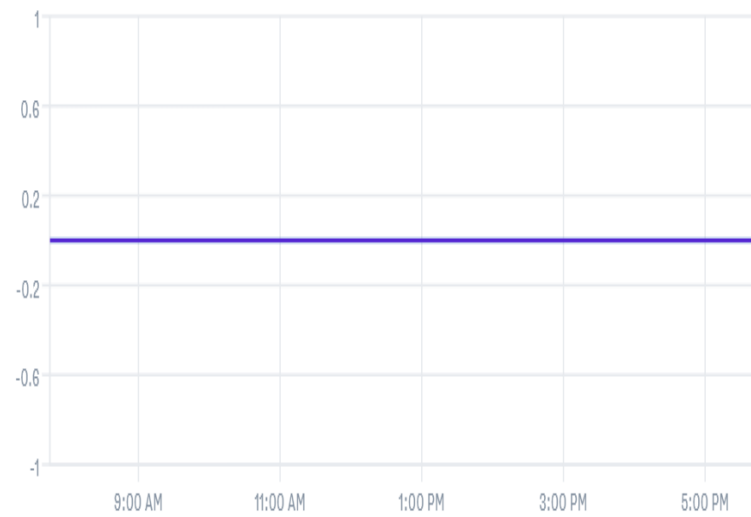

CAMP:
Upwind Particulates

Dust Levels


0.027 mg/m³ 0.044 mg/m³

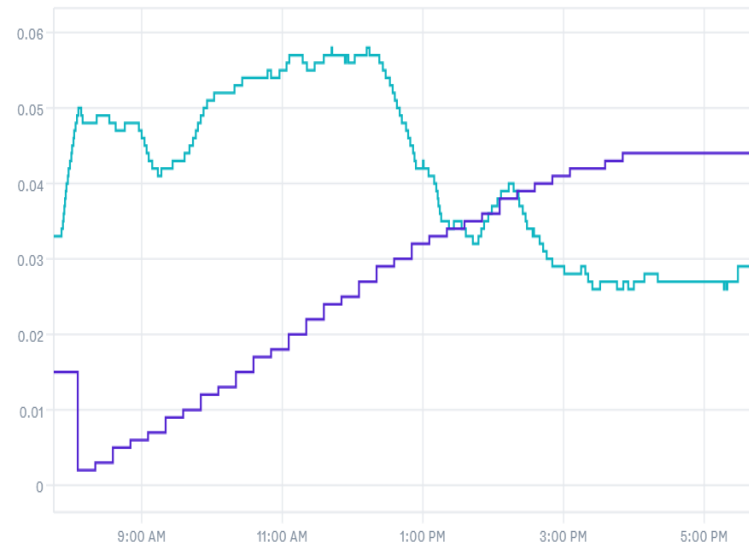

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

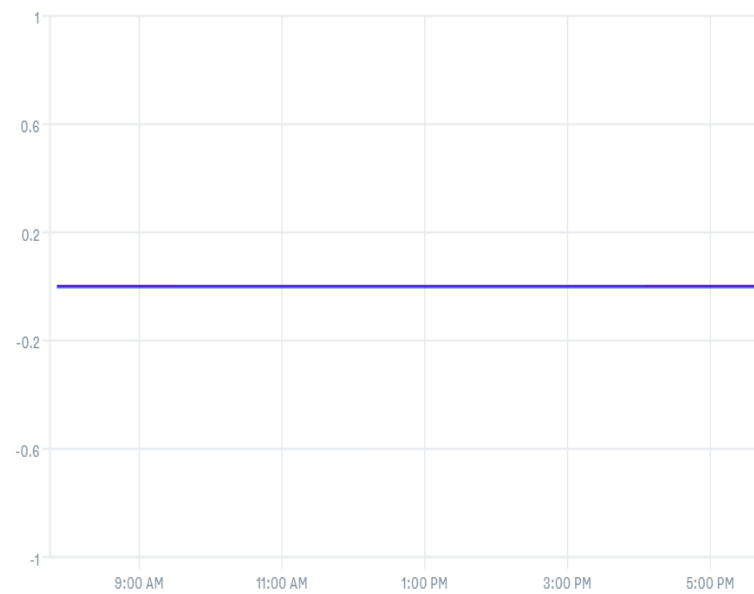

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/8/2024 7:45	5/8/2024 7:55	0.150	0	5	0
DW 2024	5/8/2024 7:55	5/8/2024 8:05	0.150	0.003	5	0
DW 2024	5/8/2024 8:05	5/8/2024 8:15	0.150	0.004	5	0
DW 2024	5/8/2024 8:15	5/8/2024 8:25	0.150	0.005	5	0
DW 2024	5/8/2024 8:25	5/8/2024 8:35	0.150	0.006	5	0
DW 2024	5/8/2024 8:35	5/8/2024 8:45	0.150	0.007	5	0
DW 2024	5/8/2024 8:45	5/8/2024 8:55	0.150	0.008	5	0
DW 2024	5/8/2024 8:55	5/8/2024 9:05	0.150	0.009	5	0
DW 2024	5/8/2024 9:05	5/8/2024 9:15	0.150	0.01	5	0
DW 2024	5/8/2024 9:15	5/8/2024 9:25	0.150	0.011	5	0
DW 2024	5/8/2024 9:25	5/8/2024 9:35	0.150	0.011	5	0
DW 2024	5/8/2024 9:35	5/8/2024 9:45	0.150	0.012	5	0
DW 2024	5/8/2024 9:45	5/8/2024 9:55	0.150	0.013	5	0
DW 2024	5/8/2024 9:55	5/8/2024 10:05	0.150	0.014	5	0
DW 2024	5/8/2024 10:05	5/8/2024 10:15	0.150	0.015	5	0
DW 2024	5/8/2024 10:15	5/8/2024 10:25	0.150	0.016	5	0
DW 2024	5/8/2024 10:25	5/8/2024 10:35	0.150	0.017	5	0
DW 2024	5/8/2024 10:35	5/8/2024 10:45	0.150	0.018	5	0
DW 2024	5/8/2024 10:45	5/8/2024 10:55	0.150	0.019	5	0
DW 2024	5/8/2024 10:55	5/8/2024 11:05	0.150	0.02	5	0
DW 2024	5/8/2024 11:05	5/8/2024 11:15	0.150	0.021	5	0
DW 2024	5/8/2024 11:15	5/8/2024 11:25	0.150	0.022	5	0
DW 2024	5/8/2024 11:25	5/8/2024 11:35	0.150	0.024	5	0
DW 2024	5/8/2024 11:35	5/8/2024 11:45	0.150	0.025	5	0
DW 2024	5/8/2024 11:45	5/8/2024 11:55	0.150	0.026	5	0
DW 2024	5/8/2024 11:55	5/8/2024 12:05	0.150	0.027	5	0
DW 2024	5/8/2024 12:05	5/8/2024 12:15	0.150	0.028	5	0
DW 2024	5/8/2024 12:15	5/8/2024 12:25	0.150	0.029	5	0
DW 2024	5/8/2024 12:25	5/8/2024 12:35	0.150	0.03	5	0
DW 2024	5/8/2024 12:35	5/8/2024 12:45	0.150	0.03	5	0
DW 2024	5/8/2024 12:45	5/8/2024 12:55	0.150	0.031	5	0
DW 2024	5/8/2024 12:55	5/8/2024 13:05	0.150	0.031	5	0
DW 2024	5/8/2024 13:05	5/8/2024 13:15	0.150	0.032	5	0
DW 2024	5/8/2024 13:15	5/8/2024 13:25	0.150	0.032	5	0
DW 2024	5/8/2024 13:25	5/8/2024 13:35	0.150	0.033	5	0
DW 2024	5/8/2024 13:35	5/8/2024 13:45	0.150	0.033	5	0
DW 2024	5/8/2024 13:45	5/8/2024 13:55	0.150	0.034	5	0
DW 2024	5/8/2024 13:55	5/8/2024 14:05	0.150	0.034	5	0
DW 2024	5/8/2024 14:05	5/8/2024 14:15	0.150	0.035	5	0
DW 2024	5/8/2024 14:15	5/8/2024 14:25	0.150	0.035	5	0
DW 2024	5/8/2024 14:25	5/8/2024 14:35	0.150	0.036	5	0
DW 2024	5/8/2024 14:35	5/8/2024 14:45	0.150	0.036	5	0
DW 2024	5/8/2024 14:45	5/8/2024 14:55	0.150	0.036	5	0
DW 2024	5/8/2024 14:55	5/8/2024 15:05	0.150	0.036	5	0
DW 2024	5/8/2024 15:05	5/8/2024 15:15	0.150	0.037	5	0
DW 2024	5/8/2024 15:15	5/8/2024 15:25	0.150	0.037	5	0
DW 2024	5/8/2024 15:25	5/8/2024 15:35	0.150	0.037	5	0
DW 2024	5/8/2024 15:35	5/8/2024 15:45	0.150	0.037	5	0
DW 2024	5/8/2024 15:45	5/8/2024 15:55	0.150	0.037	5	0
DW 2024	5/8/2024 15:55	5/8/2024 16:05	0.150	0.037	5	0
DW 2024	5/8/2024 16:05	5/8/2024 16:15	0.150	0.037	5	0
DW 2024	5/8/2024 16:15	5/8/2024 16:25	0.150	0.037	5	0
DW 2024	5/8/2024 16:25	5/8/2024 16:35	0.150	0.037	5	0
DW 2024	5/8/2024 16:35	5/8/2024 16:45	0.150	0.037	5	0
DW 2024	5/8/2024 16:45	5/8/2024 16:55	0.150	0.037	5	0
DW 2024	5/8/2024 16:55	5/8/2024 17:05	0.150	0.037	5	0
DW 2024	5/8/2024 17:05	5/8/2024 17:15	0.150	0.037	5	0
DW 2024	5/8/2024 17:15	5/8/2024 17:25	0.150	0.037	5	0
DW 2024	5/8/2024 17:25	5/8/2024 17:35	0.150	0.037	5	0
DW 2024	5/8/2024 17:35	5/8/2024 17:45	0.150	0.037	5	0
DW 2024	5/8/2024 17:45	5/8/2024 17:55	0.150	0.037	5	0
DW 2024	5/8/2024 17:55	5/8/2024 18:00	0.150	0.037	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/8/2024 7:45	5/8/2024 7:55	0.150	0.015	5	0
UW 2024	5/8/2024 7:55	5/8/2024 8:05	0.150	0.015	5	0
UW 2024	5/8/2024 8:05	5/8/2024 8:15	0.150	0.015	5	0
UW 2024	5/8/2024 8:15	5/8/2024 8:25	0.150	0.003	5	0
UW 2024	5/8/2024 8:25	5/8/2024 8:35	0.150	0.003	5	0
UW 2024	5/8/2024 8:35	5/8/2024 8:45	0.150	0.005	5	0
UW 2024	5/8/2024 8:45	5/8/2024 8:55	0.150	0.006	5	0
UW 2024	5/8/2024 8:55	5/8/2024 9:05	0.150	0.006	5	0
UW 2024	5/8/2024 9:05	5/8/2024 9:15	0.150	0.007	5	0
UW 2024	5/8/2024 9:15	5/8/2024 9:25	0.150	0.009	5	0
UW 2024	5/8/2024 9:25	5/8/2024 9:35	0.150	0.009	5	0
UW 2024	5/8/2024 9:35	5/8/2024 9:45	0.150	0.01	5	0
UW 2024	5/8/2024 9:45	5/8/2024 9:55	0.150	0.012	5	0
UW 2024	5/8/2024 9:55	5/8/2024 10:05	0.150	0.012	5	0
UW 2024	5/8/2024 10:05	5/8/2024 10:15	0.150	0.013	5	0
UW 2024	5/8/2024 10:15	5/8/2024 10:25	0.150	0.015	5	0
UW 2024	5/8/2024 10:25	5/8/2024 10:35	0.150	0.015	5	0
UW 2024	5/8/2024 10:35	5/8/2024 10:45	0.150	0.017	5	0
UW 2024	5/8/2024 10:45	5/8/2024 10:55	0.150	0.018	5	0
UW 2024	5/8/2024 10:55	5/8/2024 11:05	0.150	0.018	5	0
UW 2024	5/8/2024 11:05	5/8/2024 11:15	0.150	0.02	5	0
UW 2024	5/8/2024 11:15	5/8/2024 11:25	0.150	0.022	5	0
UW 2024	5/8/2024 11:25	5/8/2024 11:35	0.150	0.022	5	0
UW 2024	5/8/2024 11:35	5/8/2024 11:45	0.150	0.024	5	0
UW 2024	5/8/2024 11:45	5/8/2024 11:55	0.150	0.025	5	0
UW 2024	5/8/2024 11:55	5/8/2024 12:05	0.150	0.025	5	0
UW 2024	5/8/2024 12:05	5/8/2024 12:15	0.150	0.027	5	0
UW 2024	5/8/2024 12:15	5/8/2024 12:25	0.150	0.029	5	0
UW 2024	5/8/2024 12:25	5/8/2024 12:35	0.150	0.029	5	0
UW 2024	5/8/2024 12:35	5/8/2024 12:45	0.150	0.03	5	0
UW 2024	5/8/2024 12:45	5/8/2024 12:55	0.150	0.032	5	0
UW 2024	5/8/2024 12:55	5/8/2024 13:05	0.150	0.032	5	0
UW 2024	5/8/2024 13:05	5/8/2024 13:15	0.150	0.033	5	0
UW 2024	5/8/2024 13:15	5/8/2024 13:25	0.150	0.034	5	0
UW 2024	5/8/2024 13:25	5/8/2024 13:35	0.150	0.034	5	0
UW 2024	5/8/2024 13:35	5/8/2024 13:45	0.150	0.035	5	0
UW 2024	5/8/2024 13:45	5/8/2024 13:55	0.150	0.036	5	0
UW 2024	5/8/2024 13:55	5/8/2024 14:05	0.150	0.036	5	0
UW 2024	5/8/2024 14:05	5/8/2024 14:15	0.150	0.038	5	0
UW 2024	5/8/2024 14:15	5/8/2024 14:25	0.150	0.039	5	0
UW 2024	5/8/2024 14:25	5/8/2024 14:35	0.150	0.039	5	0
UW 2024	5/8/2024 14:35	5/8/2024 14:45	0.150	0.04	5	0
UW 2024	5/8/2024 14:45	5/8/2024 14:55	0.150	0.041	5	0
UW 2024	5/8/2024 14:55	5/8/2024 15:05	0.150	0.041	5	0
UW 2024	5/8/2024 15:05	5/8/2024 15:15	0.150	0.042	5	0
UW 2024	5/8/2024 15:15	5/8/2024 15:25	0.150	0.042	5	0
UW 2024	5/8/2024 15:25	5/8/2024 15:35	0.150	0.042	5	0
UW 2024	5/8/2024 15:35	5/8/2024 15:45	0.150	0.043	5	0
UW 2024	5/8/2024 15:45	5/8/2024 15:55	0.150	0.044	5	0
UW 2024	5/8/2024 15:55	5/8/2024 16:05	0.150	0.044	5	0
UW 2024	5/8/2024 16:05	5/8/2024 16:15	0.150	0.044	5	0
UW 2024	5/8/2024 16:15	5/8/2024 16:25	0.150	0.044	5	0
UW 2024	5/8/2024 16:25	5/8/2024 16:35	0.150	0.044	5	0
UW 2024	5/8/2024 16:35	5/8/2024 16:45	0.150	0.044	5	0
UW 2024	5/8/2024 16:45	5/8/2024 16:55	0.150	0.044	5	0
UW 2024	5/8/2024 16:55	5/8/2024 17:05	0.150	0.044	5	0
UW 2024	5/8/2024 17:05	5/8/2024 17:15	0.150	0.044	5	0
UW 2024	5/8/2024 17:15	5/8/2024 17:25	0.150	0.044	5	0
UW 2024	5/8/2024 17:25	5/8/2024 17:35	0.150	0.044	5	0
UW 2024	5/8/2024 17:35	5/8/2024 17:45	0.150	0.044	5	0
UW 2024	5/8/2024 17:45	5/8/2024 17:55	0.150	0.044	5	0
UW 2024	5/8/2024 17:55	5/8/2024 18:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/8/2024 7:45	5/8/2024 7:55	0.150	0.023	5	0
HS South	5/8/2024 7:55	5/8/2024 8:05	0.150	0.023	5	0
HS South	5/8/2024 8:05	5/8/2024 8:15	0.150	0.023	5	0
HS South	5/8/2024 8:15	5/8/2024 8:25	0.150	0.023	5	0
HS South	5/8/2024 8:25	5/8/2024 8:35	0.150	0.023	5	0
HS South	5/8/2024 8:35	5/8/2024 8:45	0.150	0.023	5	0
HS South	5/8/2024 8:45	5/8/2024 8:55	0.150	0.023	5	0
HS South	5/8/2024 8:55	5/8/2024 9:05	0.150	0.023	5	0
HS South	5/8/2024 9:05	5/8/2024 9:15	0.150	0.023	5	0
HS South	5/8/2024 9:15	5/8/2024 9:25	0.150	0.023	5	0
HS South	5/8/2024 9:25	5/8/2024 9:35	0.150	0.023	5	0
HS South	5/8/2024 9:35	5/8/2024 9:45	0.150	0.023	5	0
HS South	5/8/2024 9:45	5/8/2024 9:55	0.150	0.023	5	0
HS South	5/8/2024 9:55	5/8/2024 10:05	0.150	0	5	0.214
HS South	5/8/2024 10:05	5/8/2024 10:15	0.150	0	5	0.313
HS South	5/8/2024 10:15	5/8/2024 10:25	0.150	0.003	5	0.313
HS South	5/8/2024 10:25	5/8/2024 10:35	0.150	0.005	5	0.313
HS South	5/8/2024 10:35	5/8/2024 10:45	0.150	0.007	5	0.313
HS South	5/8/2024 10:45	5/8/2024 10:55	0.150	0.008	5	0.313
HS South	5/8/2024 10:55	5/8/2024 11:05	0.150	0.01	5	0.313
HS South	5/8/2024 11:05	5/8/2024 11:15	0.150	0.012	5	0.313
HS South	5/8/2024 11:15	5/8/2024 11:25	0.150	0.013	5	0.313
HS South	5/8/2024 11:25	5/8/2024 11:35	0.150	0.015	5	0.313
HS South	5/8/2024 11:35	5/8/2024 11:45	0.150	0.017	5	0.313
HS South	5/8/2024 11:45	5/8/2024 11:55	0.150	0.019	5	0.313
HS South	5/8/2024 11:55	5/8/2024 12:05	0.150	0.021	5	0.313
HS South	5/8/2024 12:05	5/8/2024 12:15	0.150	0.023	5	0.313
HS South	5/8/2024 12:15	5/8/2024 12:25	0.150	0.024	5	0.313
HS South	5/8/2024 12:25	5/8/2024 12:35	0.150	0.026	5	0.313
HS South	5/8/2024 12:35	5/8/2024 12:45	0.150	0.027	5	0.313
HS South	5/8/2024 12:45	5/8/2024 12:55	0.150	0.029	5	0.313
HS South	5/8/2024 12:55	5/8/2024 13:05	0.150	0.03	5	0.313
HS South	5/8/2024 13:05	5/8/2024 13:15	0.150	0.031	5	0.313
HS South	5/8/2024 13:15	5/8/2024 13:25	0.150	0.032	5	0.313
HS South	5/8/2024 13:25	5/8/2024 13:35	0.150	0.034	5	0.313
HS South	5/8/2024 13:35	5/8/2024 13:45	0.150	0.035	5	0.313
HS South	5/8/2024 13:45	5/8/2024 13:55	0.150	0.036	5	0.313
HS South	5/8/2024 13:55	5/8/2024 14:05	0.150	0.037	5	0.313
HS South	5/8/2024 14:05	5/8/2024 14:15	0.150	0.038	5	0.313
HS South	5/8/2024 14:15	5/8/2024 14:25	0.150	0.039	5	0.313
HS South	5/8/2024 14:25	5/8/2024 14:35	0.150	0.041	5	0.313
HS South	5/8/2024 14:35	5/8/2024 14:45	0.150	0.042	5	0.313
HS South	5/8/2024 14:45	5/8/2024 14:55	0.150	0.043	5	0.313
HS South	5/8/2024 14:55	5/8/2024 15:05	0.150	0.044	5	0.313
HS South	5/8/2024 15:05	5/8/2024 15:15	0.150	0.045	5	0.313
HS South	5/8/2024 15:15	5/8/2024 15:25	0.150	0.045	5	0.313
HS South	5/8/2024 15:25	5/8/2024 15:35	0.150	0.046	5	0.313
HS South	5/8/2024 15:35	5/8/2024 15:45	0.150	0.047	5	0.313
HS South	5/8/2024 15:45	5/8/2024 15:55	0.150	0.048	5	0.313
HS South	5/8/2024 15:55	5/8/2024 16:05	0.150	0.049	5	0.313
HS South	5/8/2024 16:05	5/8/2024 16:15	0.150	0.05	5	0.313
HS South	5/8/2024 16:15	5/8/2024 16:25	0.150	0.051	5	0.313
HS South	5/8/2024 16:25	5/8/2024 16:35	0.150	0.052	5	0.313
HS South	5/8/2024 16:35	5/8/2024 16:45	0.150	0.053	5	0.313
HS South	5/8/2024 16:45	5/8/2024 16:55	0.150	0.054	5	0.313
HS South	5/8/2024 16:55	5/8/2024 17:05	0.150	0.055	5	0.313
HS South	5/8/2024 17:05	5/8/2024 17:15	0.150	0.056	5	0.313
HS South	5/8/2024 17:15	5/8/2024 17:25	0.150	0.056	5	0.313
HS South	5/8/2024 17:25	5/8/2024 17:35	0.150	0.056	5	0.313
HS South	5/8/2024 17:35	5/8/2024 17:45	0.150	0.056	5	0.313
HS South	5/8/2024 17:45	5/8/2024 17:55	0.150	0.056	5	0.313
HS South	5/8/2024 17:55	5/8/2024 18:00	0.150	0.056	5	0.313

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/8/2024 7:45	5/8/2024 7:55	0.150	0.006	5	0
PER2 2024	5/8/2024 7:55	5/8/2024 8:05	0.150	0.002	5	0
PER2 2024	5/8/2024 8:05	5/8/2024 8:15	0.150	0.003	5	0
PER2 2024	5/8/2024 8:15	5/8/2024 8:25	0.150	0.004	5	0
PER2 2024	5/8/2024 8:25	5/8/2024 8:35	0.150	0.005	5	0
PER2 2024	5/8/2024 8:35	5/8/2024 8:45	0.150	0.006	5	0
PER2 2024	5/8/2024 8:45	5/8/2024 8:55	0.150	0.006	5	0
PER2 2024	5/8/2024 8:55	5/8/2024 9:05	0.150	0.007	5	0
PER2 2024	5/8/2024 9:05	5/8/2024 9:15	0.150	0.008	5	0
PER2 2024	5/8/2024 9:15	5/8/2024 9:25	0.150	0.008	5	0
PER2 2024	5/8/2024 9:25	5/8/2024 9:35	0.150	0.009	5	0
PER2 2024	5/8/2024 9:35	5/8/2024 9:45	0.150	0.01	5	0
PER2 2024	5/8/2024 9:45	5/8/2024 9:55	0.150	0.011	5	0
PER2 2024	5/8/2024 9:55	5/8/2024 10:05	0.150	0.012	5	0
PER2 2024	5/8/2024 10:05	5/8/2024 10:15	0.150	0.013	5	0
PER2 2024	5/8/2024 10:15	5/8/2024 10:25	0.150	0.013	5	0
PER2 2024	5/8/2024 10:25	5/8/2024 10:35	0.150	0.014	5	0
PER2 2024	5/8/2024 10:35	5/8/2024 10:45	0.150	0.015	5	0
PER2 2024	5/8/2024 10:45	5/8/2024 10:55	0.150	0.016	5	0
PER2 2024	5/8/2024 10:55	5/8/2024 11:05	0.150	0.017	5	0
PER2 2024	5/8/2024 11:05	5/8/2024 11:15	0.150	0.018	5	0
PER2 2024	5/8/2024 11:15	5/8/2024 11:25	0.150	0.019	5	0
PER2 2024	5/8/2024 11:25	5/8/2024 11:35	0.150	0.02	5	0
PER2 2024	5/8/2024 11:35	5/8/2024 11:45	0.150	0.021	5	0
PER2 2024	5/8/2024 11:45	5/8/2024 11:55	0.150	0.022	5	0
PER2 2024	5/8/2024 11:55	5/8/2024 12:05	0.150	0.023	5	0
PER2 2024	5/8/2024 12:05	5/8/2024 12:15	0.150	0.024	5	0
PER2 2024	5/8/2024 12:15	5/8/2024 12:25	0.150	0.025	5	0
PER2 2024	5/8/2024 12:25	5/8/2024 12:35	0.150	0.026	5	0
PER2 2024	5/8/2024 12:35	5/8/2024 12:45	0.150	0.026	5	0
PER2 2024	5/8/2024 12:45	5/8/2024 12:55	0.150	0.027	5	0
PER2 2024	5/8/2024 12:55	5/8/2024 13:05	0.150	0.028	5	0
PER2 2024	5/8/2024 13:05	5/8/2024 13:15	0.150	0.028	5	0
PER2 2024	5/8/2024 13:15	5/8/2024 13:25	0.150	0.029	5	0
PER2 2024	5/8/2024 13:25	5/8/2024 13:35	0.150	0.029	5	0
PER2 2024	5/8/2024 13:35	5/8/2024 13:45	0.150	0.029	5	0
PER2 2024	5/8/2024 13:45	5/8/2024 13:55	0.150	0.03	5	0
PER2 2024	5/8/2024 13:55	5/8/2024 14:05	0.150	0.031	5	0
PER2 2024	5/8/2024 14:05	5/8/2024 14:15	0.150	0.032	5	0
PER2 2024	5/8/2024 14:15	5/8/2024 14:25	0.150	0.032	5	0
PER2 2024	5/8/2024 14:25	5/8/2024 14:35	0.150	0.033	5	0
PER2 2024	5/8/2024 14:35	5/8/2024 14:45	0.150	0.033	5	0
PER2 2024	5/8/2024 14:45	5/8/2024 14:55	0.150	0.034	5	0
PER2 2024	5/8/2024 14:55	5/8/2024 15:05	0.150	0.034	5	0
PER2 2024	5/8/2024 15:05	5/8/2024 15:15	0.150	0.034	5	0
PER2 2024	5/8/2024 15:15	5/8/2024 15:25	0.150	0.035	5	0
PER2 2024	5/8/2024 15:25	5/8/2024 15:35	0.150	0.035	5	0
PER2 2024	5/8/2024 15:35	5/8/2024 15:45	0.150	0.035	5	0
PER2 2024	5/8/2024 15:45	5/8/2024 15:55	0.150	0.035	5	0
PER2 2024	5/8/2024 15:55	5/8/2024 16:05	0.150	0.035	5	0
PER2 2024	5/8/2024 16:05	5/8/2024 16:15	0.150	0.035	5	0
PER2 2024	5/8/2024 16:15	5/8/2024 16:25	0.150	0.035	5	0
PER2 2024	5/8/2024 16:25	5/8/2024 16:35	0.150	0.035	5	0
PER2 2024	5/8/2024 16:35	5/8/2024 16:45	0.150	0.035	5	0
PER2 2024	5/8/2024 16:45	5/8/2024 16:55	0.150	0.035	5	0
PER2 2024	5/8/2024 16:55	5/8/2024 17:05	0.150	0.035	5	0
PER2 2024	5/8/2024 17:05	5/8/2024 17:15	0.150	0.035	5	0
PER2 2024	5/8/2024 17:15	5/8/2024 17:25	0.150	0.035	5	0
PER2 2024	5/8/2024 17:25	5/8/2024 17:35	0.150	0.035	5	0
PER2 2024	5/8/2024 17:35	5/8/2024 17:45	0.150	0.035	5	0
PER2 2024	5/8/2024 17:45	5/8/2024 17:55	0.150	0.035	5	0
PER2 2024	5/8/2024 17:55	5/8/2024 18:00	0.150	0.035	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/8/2024 7:45	5/8/2024 7:55	0.150	0.002	5	0
PER1 2024	5/8/2024 7:55	5/8/2024 8:05	0.150	0.003	5	0
PER1 2024	5/8/2024 8:05	5/8/2024 8:15	0.150	0.003	5	0
PER1 2024	5/8/2024 8:15	5/8/2024 8:25	0.150	0.004	5	0
PER1 2024	5/8/2024 8:25	5/8/2024 8:35	0.150	0.005	5	0
PER1 2024	5/8/2024 8:35	5/8/2024 8:45	0.150	0.006	5	0
PER1 2024	5/8/2024 8:45	5/8/2024 8:55	0.150	0.007	5	0
PER1 2024	5/8/2024 8:55	5/8/2024 9:05	0.150	0.008	5	0
PER1 2024	5/8/2024 9:05	5/8/2024 9:15	0.150	0.008	5	0
PER1 2024	5/8/2024 9:15	5/8/2024 9:25	0.150	0.009	5	0
PER1 2024	5/8/2024 9:25	5/8/2024 9:35	0.150	0.01	5	0
PER1 2024	5/8/2024 9:35	5/8/2024 9:45	0.150	0.01	5	0
PER1 2024	5/8/2024 9:45	5/8/2024 9:55	0.150	0.011	5	0
PER1 2024	5/8/2024 9:55	5/8/2024 10:05	0.150	0.012	5	0
PER1 2024	5/8/2024 10:05	5/8/2024 10:15	0.150	0.013	5	0
PER1 2024	5/8/2024 10:15	5/8/2024 10:25	0.150	0.014	5	0
PER1 2024	5/8/2024 10:25	5/8/2024 10:35	0.150	0.015	5	0
PER1 2024	5/8/2024 10:35	5/8/2024 10:45	0.150	0.015	5	0
PER1 2024	5/8/2024 10:45	5/8/2024 10:55	0.150	0.016	5	0
PER1 2024	5/8/2024 10:55	5/8/2024 11:05	0.150	0.017	5	0
PER1 2024	5/8/2024 11:05	5/8/2024 11:15	0.150	0.018	5	0
PER1 2024	5/8/2024 11:15	5/8/2024 11:25	0.150	0.019	5	0
PER1 2024	5/8/2024 11:25	5/8/2024 11:35	0.150	0.02	5	0
PER1 2024	5/8/2024 11:35	5/8/2024 11:45	0.150	0.021	5	0
PER1 2024	5/8/2024 11:45	5/8/2024 11:55	0.150	0.022	5	0
PER1 2024	5/8/2024 11:55	5/8/2024 12:05	0.150	0.023	5	0
PER1 2024	5/8/2024 12:05	5/8/2024 12:15	0.150	0.023	5	0
PER1 2024	5/8/2024 12:15	5/8/2024 12:25	0.150	0.024	5	0
PER1 2024	5/8/2024 12:25	5/8/2024 12:35	0.150	0.025	5	0
PER1 2024	5/8/2024 12:35	5/8/2024 12:45	0.150	0.026	5	0
PER1 2024	5/8/2024 12:45	5/8/2024 12:55	0.150	0.026	5	0
PER1 2024	5/8/2024 12:55	5/8/2024 13:05	0.150	0.027	5	0
PER1 2024	5/8/2024 13:05	5/8/2024 13:15	0.150	0.027	5	0
PER1 2024	5/8/2024 13:15	5/8/2024 13:25	0.150	0.028	5	0
PER1 2024	5/8/2024 13:25	5/8/2024 13:35	0.150	0.028	5	0
PER1 2024	5/8/2024 13:35	5/8/2024 13:45	0.150	0.029	5	0
PER1 2024	5/8/2024 13:45	5/8/2024 13:55	0.150	0.029	5	0
PER1 2024	5/8/2024 13:55	5/8/2024 14:05	0.150	0.03	5	0
PER1 2024	5/8/2024 14:05	5/8/2024 14:15	0.150	0.03	5	0
PER1 2024	5/8/2024 14:15	5/8/2024 14:25	0.150	0.031	5	0
PER1 2024	5/8/2024 14:25	5/8/2024 14:35	0.150	0.031	5	0
PER1 2024	5/8/2024 14:35	5/8/2024 14:45	0.150	0.031	5	0
PER1 2024	5/8/2024 14:45	5/8/2024 14:55	0.150	0.032	5	0
PER1 2024	5/8/2024 14:55	5/8/2024 15:05	0.150	0.032	5	0
PER1 2024	5/8/2024 15:05	5/8/2024 15:15	0.150	0.032	5	0
PER1 2024	5/8/2024 15:15	5/8/2024 15:25	0.150	0.032	5	0
PER1 2024	5/8/2024 15:25	5/8/2024 15:35	0.150	0.033	5	0
PER1 2024	5/8/2024 15:35	5/8/2024 15:45	0.150	0.033	5	0
PER1 2024	5/8/2024 15:45	5/8/2024 15:55	0.150	0.033	5	0
PER1 2024	5/8/2024 15:55	5/8/2024 16:05	0.150	0.033	5	0
PER1 2024	5/8/2024 16:05	5/8/2024 16:15	0.150	0.033	5	0
PER1 2024	5/8/2024 16:15	5/8/2024 16:25	0.150	0.033	5	0
PER1 2024	5/8/2024 16:25	5/8/2024 16:35	0.150	0.033	5	0
PER1 2024	5/8/2024 16:35	5/8/2024 16:45	0.150	0.033	5	0
PER1 2024	5/8/2024 16:45	5/8/2024 16:55	0.150	0.033	5	0
PER1 2024	5/8/2024 16:55	5/8/2024 17:05	0.150	0.033	5	0
PER1 2024	5/8/2024 17:05	5/8/2024 17:15	0.150	0.033	5	0
PER1 2024	5/8/2024 17:15	5/8/2024 17:25	0.150	0	5	0
PER1 2024	5/8/2024 17:25	5/8/2024 17:35	0.150	0	5	0
PER1 2024	5/8/2024 17:35	5/8/2024 17:45	0.150	0	5	0
PER1 2024	5/8/2024 17:45	5/8/2024 17:55	0.150	0	5	0
PER1 2024	5/8/2024 17:55	5/8/2024 18:00	0.150	0	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/09/2024

Weather: 65 deg. F, Partly Cloudy


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development. 2) Collect dewatering influent and effluent samples, see below.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): Influent_20240509 and Effluent_20240509	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8645	1520	4140

Site Layout Map and Excavation Figures

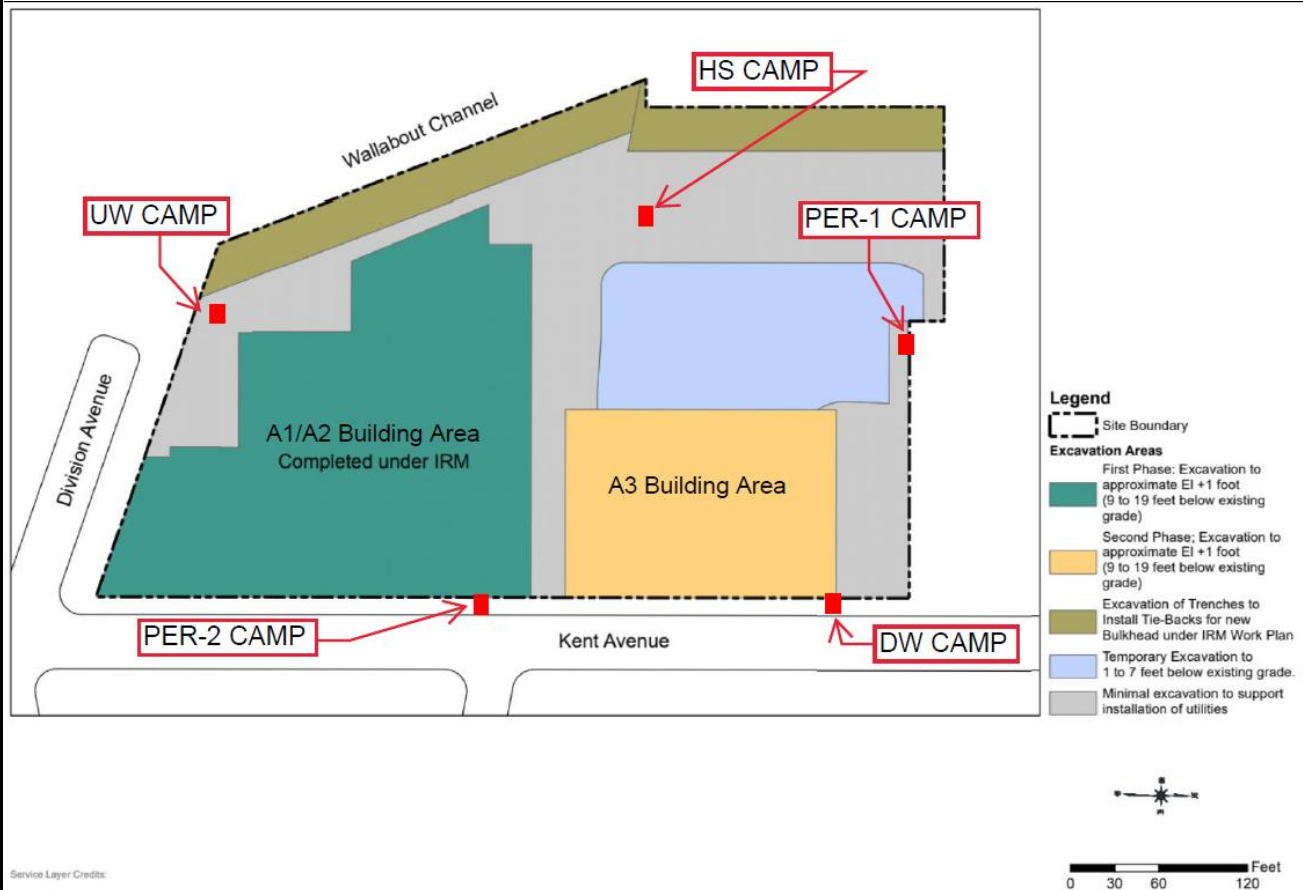

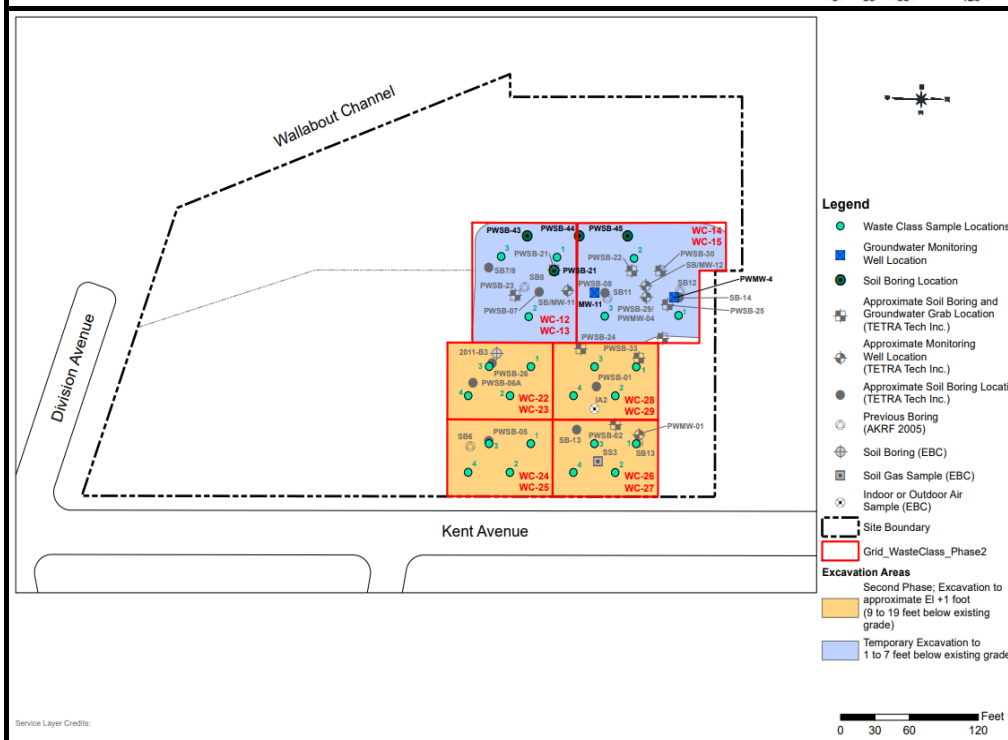
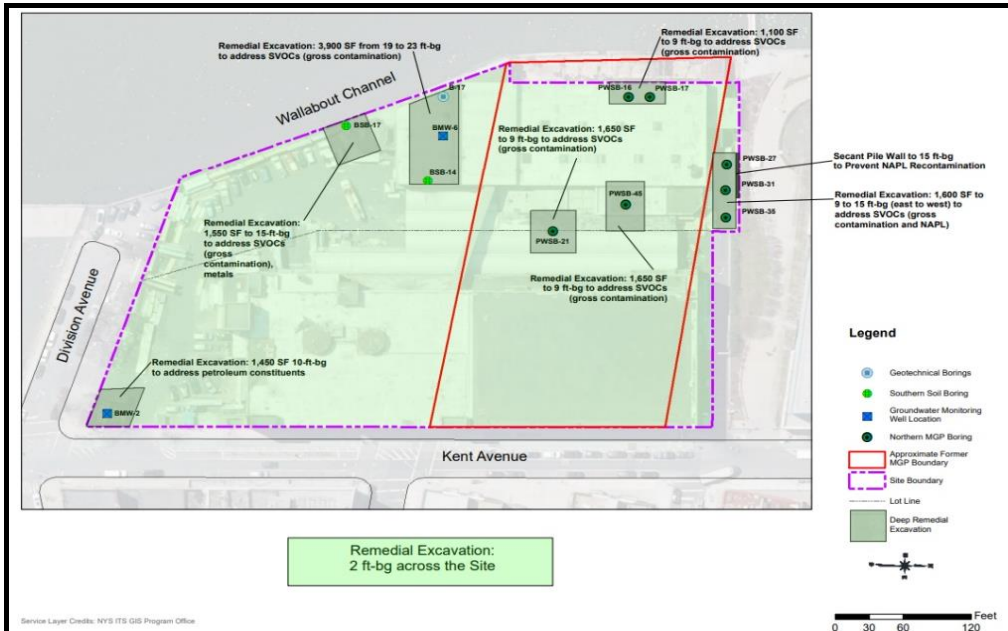


Photo 1:
View of Site conditions
and soil excavation
facing northeast.



Photo 2:
View of Site conditions
facing east.



Photo 3:
View of rebar
installation.


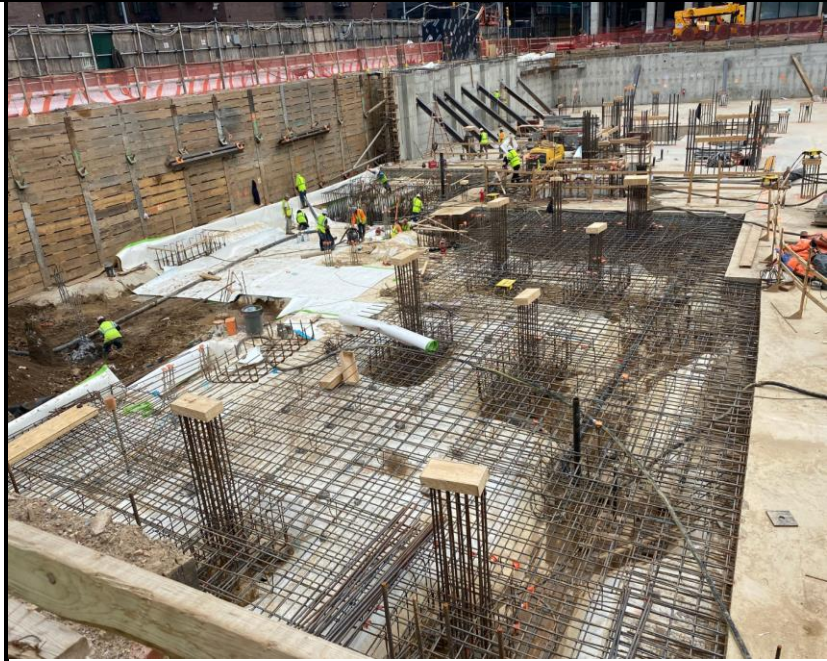



Photo 4:
View of Site
activities and
waterproofing
installation.



CAMP:
Downwind
Particulates

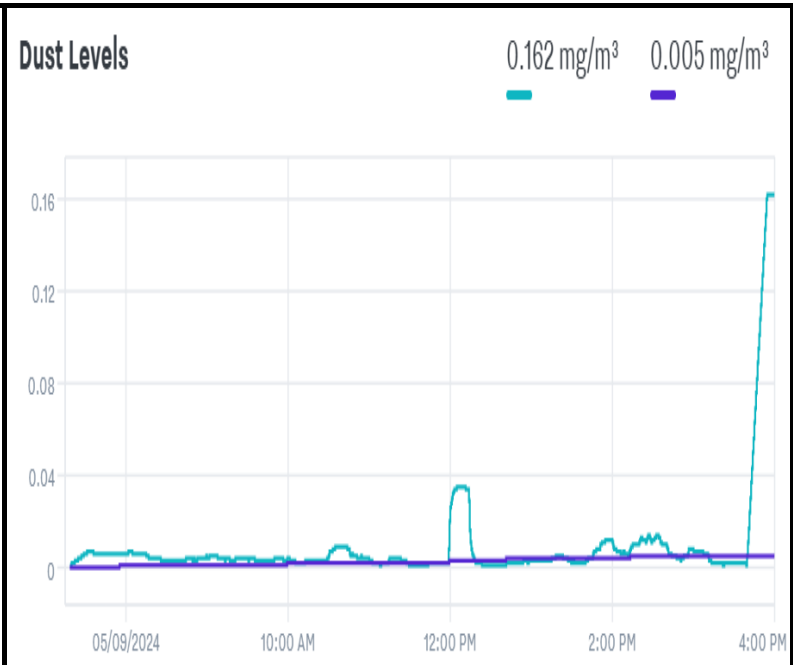


CAMP:
Downwind VOCs

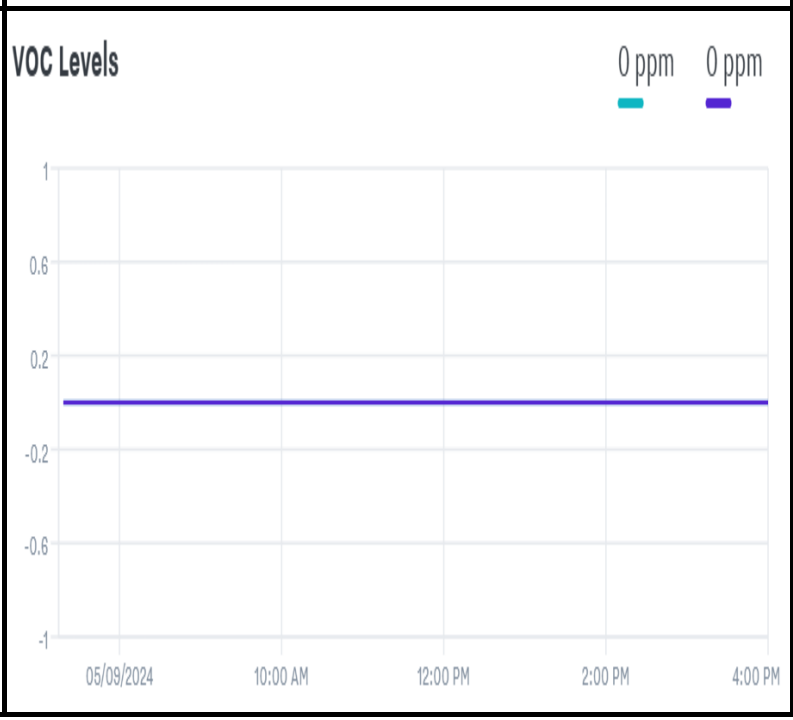

CAMP:
Upwind Particulates

Dust Levels


0.019 mg/m³ 0.018 mg/m³

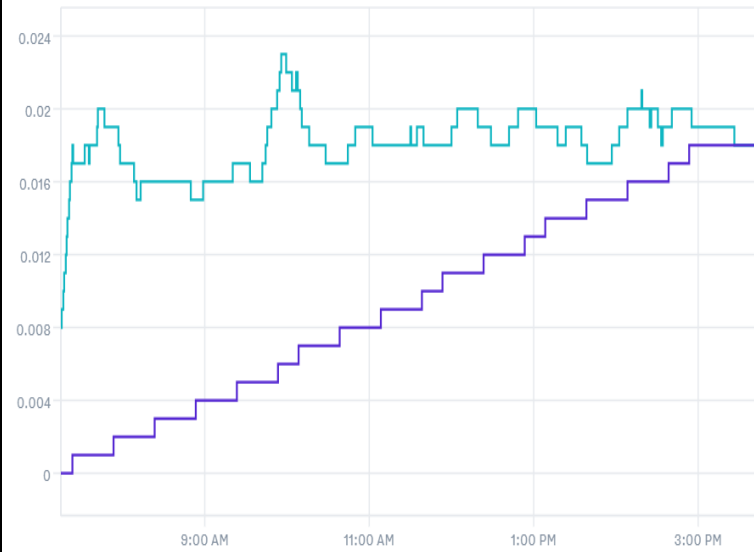

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

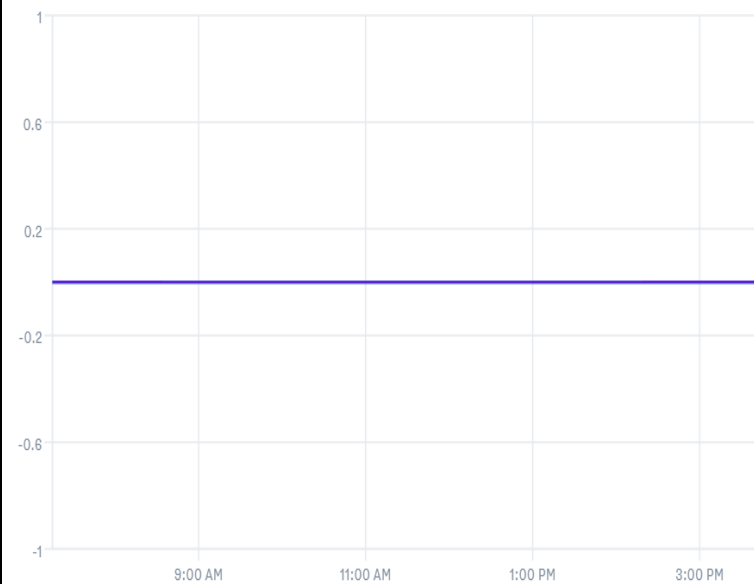

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/9/2024 7:45	5/9/2024 7:55	0.150	0	5	0
DW 2024	5/9/2024 7:55	5/9/2024 8:05	0.150	0.001	5	0
DW 2024	5/9/2024 8:05	5/9/2024 8:15	0.150	0.001	5	0
DW 2024	5/9/2024 8:15	5/9/2024 8:25	0.150	0.001	5	0
DW 2024	5/9/2024 8:25	5/9/2024 8:35	0.150	0.001	5	0
DW 2024	5/9/2024 8:35	5/9/2024 8:45	0.150	0.001	5	0
DW 2024	5/9/2024 8:45	5/9/2024 8:55	0.150	0.001	5	0
DW 2024	5/9/2024 8:55	5/9/2024 9:05	0.150	0.001	5	0
DW 2024	5/9/2024 9:05	5/9/2024 9:15	0.150	0.001	5	0
DW 2024	5/9/2024 9:15	5/9/2024 9:25	0.150	0.001	5	0
DW 2024	5/9/2024 9:25	5/9/2024 9:35	0.150	0.001	5	0
DW 2024	5/9/2024 9:35	5/9/2024 9:45	0.150	0.001	5	0
DW 2024	5/9/2024 9:45	5/9/2024 9:55	0.150	0.001	5	0
DW 2024	5/9/2024 9:55	5/9/2024 10:05	0.150	0.002	5	0
DW 2024	5/9/2024 10:05	5/9/2024 10:15	0.150	0.002	5	0
DW 2024	5/9/2024 10:15	5/9/2024 10:25	0.150	0.002	5	0
DW 2024	5/9/2024 10:25	5/9/2024 10:35	0.150	0.002	5	0
DW 2024	5/9/2024 10:35	5/9/2024 10:45	0.150	0.002	5	0
DW 2024	5/9/2024 10:45	5/9/2024 10:55	0.150	0.002	5	0
DW 2024	5/9/2024 10:55	5/9/2024 11:05	0.150	0.002	5	0
DW 2024	5/9/2024 11:05	5/9/2024 11:15	0.150	0.002	5	0
DW 2024	5/9/2024 11:15	5/9/2024 11:25	0.150	0.002	5	0
DW 2024	5/9/2024 11:25	5/9/2024 11:35	0.150	0.002	5	0
DW 2024	5/9/2024 11:35	5/9/2024 11:45	0.150	0.002	5	0
DW 2024	5/9/2024 11:45	5/9/2024 11:55	0.150	0.002	5	0
DW 2024	5/9/2024 11:55	5/9/2024 12:05	0.150	0.003	5	0
DW 2024	5/9/2024 12:05	5/9/2024 12:15	0.150	0.003	5	0
DW 2024	5/9/2024 12:15	5/9/2024 12:25	0.150	0.003	5	0
DW 2024	5/9/2024 12:25	5/9/2024 12:35	0.150	0.003	5	0
DW 2024	5/9/2024 12:35	5/9/2024 12:45	0.150	0.004	5	0
DW 2024	5/9/2024 12:45	5/9/2024 12:55	0.150	0.004	5	0
DW 2024	5/9/2024 12:55	5/9/2024 13:05	0.150	0.004	5	0
DW 2024	5/9/2024 13:05	5/9/2024 13:15	0.150	0.004	5	0
DW 2024	5/9/2024 13:15	5/9/2024 13:25	0.150	0.004	5	0
DW 2024	5/9/2024 13:25	5/9/2024 13:35	0.150	0.004	5	0
DW 2024	5/9/2024 13:35	5/9/2024 13:45	0.150	0.004	5	0
DW 2024	5/9/2024 13:45	5/9/2024 13:55	0.150	0.004	5	0
DW 2024	5/9/2024 13:55	5/9/2024 14:05	0.150	0.004	5	0
DW 2024	5/9/2024 14:05	5/9/2024 14:15	0.150	0.005	5	0
DW 2024	5/9/2024 14:15	5/9/2024 14:25	0.150	0.005	5	0
DW 2024	5/9/2024 14:25	5/9/2024 14:35	0.150	0.005	5	0
DW 2024	5/9/2024 14:35	5/9/2024 14:45	0.150	0.005	5	0
DW 2024	5/9/2024 14:45	5/9/2024 14:55	0.150	0.005	5	0
DW 2024	5/9/2024 14:55	5/9/2024 15:05	0.150	0.005	5	0
DW 2024	5/9/2024 15:05	5/9/2024 15:15	0.150	0.005	5	0
DW 2024	5/9/2024 15:15	5/9/2024 15:25	0.150	0.005	5	0
DW 2024	5/9/2024 15:25	5/9/2024 15:35	0.150	0.005	5	0
DW 2024	5/9/2024 15:35	5/9/2024 15:45	0.150	0.005	5	0
DW 2024	5/9/2024 15:45	5/9/2024 15:55	0.150	0.005	5	0
DW 2024	5/9/2024 15:55	5/9/2024 16:00	0.150	0.005	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/9/2024 7:15	5/9/2024 7:25	0.150	0.001	5	0
UW 2024	5/9/2024 7:25	5/9/2024 7:35	0.150	0.001	5	0
UW 2024	5/9/2024 7:35	5/9/2024 7:45	0.150	0.001	5	0
UW 2024	5/9/2024 7:45	5/9/2024 7:55	0.150	0.002	5	0
UW 2024	5/9/2024 7:55	5/9/2024 8:05	0.150	0.002	5	0
UW 2024	5/9/2024 8:05	5/9/2024 8:15	0.150	0.002	5	0
UW 2024	5/9/2024 8:15	5/9/2024 8:25	0.150	0.003	5	0
UW 2024	5/9/2024 8:25	5/9/2024 8:35	0.150	0.003	5	0
UW 2024	5/9/2024 8:35	5/9/2024 8:45	0.150	0.003	5	0
UW 2024	5/9/2024 8:45	5/9/2024 8:55	0.150	0.004	5	0
UW 2024	5/9/2024 8:55	5/9/2024 9:05	0.150	0.004	5	0
UW 2024	5/9/2024 9:05	5/9/2024 9:15	0.150	0.004	5	0
UW 2024	5/9/2024 9:15	5/9/2024 9:25	0.150	0.005	5	0
UW 2024	5/9/2024 9:25	5/9/2024 9:35	0.150	0.005	5	0
UW 2024	5/9/2024 9:35	5/9/2024 9:45	0.150	0.005	5	0
UW 2024	5/9/2024 9:45	5/9/2024 9:55	0.150	0.006	5	0
UW 2024	5/9/2024 9:55	5/9/2024 10:05	0.150	0.006	5	0
UW 2024	5/9/2024 10:05	5/9/2024 10:15	0.150	0.007	5	0
UW 2024	5/9/2024 10:15	5/9/2024 10:25	0.150	0.007	5	0
UW 2024	5/9/2024 10:25	5/9/2024 10:35	0.150	0.007	5	0
UW 2024	5/9/2024 10:35	5/9/2024 10:45	0.150	0.008	5	0
UW 2024	5/9/2024 10:45	5/9/2024 10:55	0.150	0.008	5	0
UW 2024	5/9/2024 10:55	5/9/2024 11:05	0.150	0.008	5	0
UW 2024	5/9/2024 11:05	5/9/2024 11:15	0.150	0.009	5	0
UW 2024	5/9/2024 11:15	5/9/2024 11:25	0.150	0.009	5	0
UW 2024	5/9/2024 11:25	5/9/2024 11:35	0.150	0.009	5	0
UW 2024	5/9/2024 11:35	5/9/2024 11:45	0.150	0.01	5	0
UW 2024	5/9/2024 11:45	5/9/2024 11:55	0.150	0.011	5	0
UW 2024	5/9/2024 11:55	5/9/2024 12:05	0.150	0.011	5	0
UW 2024	5/9/2024 12:05	5/9/2024 12:15	0.150	0.011	5	0
UW 2024	5/9/2024 12:15	5/9/2024 12:25	0.150	0.012	5	0
UW 2024	5/9/2024 12:25	5/9/2024 12:35	0.150	0.012	5	0
UW 2024	5/9/2024 12:35	5/9/2024 12:45	0.150	0.012	5	0
UW 2024	5/9/2024 12:45	5/9/2024 12:55	0.150	0.013	5	0
UW 2024	5/9/2024 12:55	5/9/2024 13:05	0.150	0.013	5	0
UW 2024	5/9/2024 13:05	5/9/2024 13:15	0.150	0.014	5	0
UW 2024	5/9/2024 13:15	5/9/2024 13:25	0.150	0.014	5	0
UW 2024	5/9/2024 13:25	5/9/2024 13:35	0.150	0.014	5	0
UW 2024	5/9/2024 13:35	5/9/2024 13:45	0.150	0.015	5	0
UW 2024	5/9/2024 13:45	5/9/2024 13:55	0.150	0.015	5	0
UW 2024	5/9/2024 13:55	5/9/2024 14:05	0.150	0.015	5	0
UW 2024	5/9/2024 14:05	5/9/2024 14:15	0.150	0.016	5	0
UW 2024	5/9/2024 14:15	5/9/2024 14:25	0.150	0.016	5	0
UW 2024	5/9/2024 14:25	5/9/2024 14:35	0.150	0.016	5	0
UW 2024	5/9/2024 14:35	5/9/2024 14:45	0.150	0.017	5	0
UW 2024	5/9/2024 14:45	5/9/2024 14:55	0.150	0.018	5	0
UW 2024	5/9/2024 14:55	5/9/2024 15:05	0.150	0.018	5	0
UW 2024	5/9/2024 15:05	5/9/2024 15:15	0.150	0.018	5	0
UW 2024	5/9/2024 15:15	5/9/2024 15:25	0.150	0.018	5	0
UW 2024	5/9/2024 15:25	5/9/2024 15:35	0.150	0.018	5	0
UW 2024	5/9/2024 15:35	5/9/2024 15:45	0.150	0.018	5	0
UW 2024	5/9/2024 15:45	5/9/2024 15:55	0.150	0.018	5	0
UW 2024	5/9/2024 15:55	5/9/2024 16:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/9/2024 7:35	5/9/2024 7:45	0.150	0	5	0
HS South	5/9/2024 7:45	5/9/2024 7:55	0.150	0.001	5	0
HS South	5/9/2024 7:55	5/9/2024 8:05	0.150	0.001	5	0
HS South	5/9/2024 8:05	5/9/2024 8:15	0.150	0.001	5	0
HS South	5/9/2024 8:15	5/9/2024 8:25	0.150	0.001	5	0
HS South	5/9/2024 8:25	5/9/2024 8:35	0.150	0.002	5	0
HS South	5/9/2024 8:35	5/9/2024 8:45	0.150	0.002	5	0
HS South	5/9/2024 8:45	5/9/2024 8:55	0.150	0.003	5	0
HS South	5/9/2024 8:55	5/9/2024 9:05	0.150	0.003	5	0
HS South	5/9/2024 9:05	5/9/2024 9:15	0.150	0.003	5	0
HS South	5/9/2024 9:15	5/9/2024 9:25	0.150	0.004	5	0
HS South	5/9/2024 9:25	5/9/2024 9:35	0.150	0.004	5	0
HS South	5/9/2024 9:35	5/9/2024 9:45	0.150	0.005	5	0
HS South	5/9/2024 9:45	5/9/2024 9:55	0.150	0.005	5	0
HS South	5/9/2024 9:55	5/9/2024 10:05	0.150	0.006	5	0
HS South	5/9/2024 10:05	5/9/2024 10:15	0.150	0.007	5	0
HS South	5/9/2024 10:15	5/9/2024 10:25	0.150	0.007	5	0
HS South	5/9/2024 10:25	5/9/2024 10:35	0.150	0.007	5	0
HS South	5/9/2024 10:35	5/9/2024 10:45	0.150	0.008	5	0
HS South	5/9/2024 10:45	5/9/2024 10:55	0.150	0.008	5	0
HS South	5/9/2024 10:55	5/9/2024 11:05	0.150	0.009	5	0
HS South	5/9/2024 11:05	5/9/2024 11:15	0.150	0.01	5	0
HS South	5/9/2024 11:15	5/9/2024 11:25	0.150	0.01	5	0
HS South	5/9/2024 11:25	5/9/2024 11:35	0.150	0.011	5	0
HS South	5/9/2024 11:35	5/9/2024 11:45	0.150	0.011	5	0
HS South	5/9/2024 11:45	5/9/2024 11:55	0.150	0.012	5	0
HS South	5/9/2024 11:55	5/9/2024 12:05	0.150	0.013	5	0
HS South	5/9/2024 12:05	5/9/2024 12:15	0.150	0.013	5	0
HS South	5/9/2024 12:15	5/9/2024 12:25	0.150	0.014	5	0
HS South	5/9/2024 12:25	5/9/2024 12:35	0.150	0.014	5	0
HS South	5/9/2024 12:35	5/9/2024 12:45	0.150	0.015	5	0
HS South	5/9/2024 12:45	5/9/2024 12:55	0.150	0.016	5	0
HS South	5/9/2024 12:55	5/9/2024 13:05	0.150	0.016	5	0
HS South	5/9/2024 13:05	5/9/2024 13:15	0.150	0.017	5	0
HS South	5/9/2024 13:15	5/9/2024 13:25	0.150	0.017	5	0
HS South	5/9/2024 13:25	5/9/2024 13:35	0.150	0.018	5	0
HS South	5/9/2024 13:35	5/9/2024 13:45	0.150	0.018	5	0
HS South	5/9/2024 13:45	5/9/2024 13:55	0.150	0.019	5	0
HS South	5/9/2024 13:55	5/9/2024 14:05	0.150	0.019	5	0
HS South	5/9/2024 14:05	5/9/2024 14:15	0.150	0.02	5	0
HS South	5/9/2024 14:15	5/9/2024 14:25	0.150	0.02	5	0
HS South	5/9/2024 14:25	5/9/2024 14:35	0.150	0.021	5	0
HS South	5/9/2024 14:35	5/9/2024 14:45	0.150	0.022	5	0
HS South	5/9/2024 14:45	5/9/2024 14:55	0.150	0.022	5	0
HS South	5/9/2024 14:55	5/9/2024 15:05	0.150	0.023	5	0
HS South	5/9/2024 15:05	5/9/2024 15:15	0.150	0.023	5	0
HS South	5/9/2024 15:15	5/9/2024 15:25	0.150	0.024	5	0
HS South	5/9/2024 15:25	5/9/2024 15:35	0.150	0.024	5	0
HS South	5/9/2024 15:35	5/9/2024 15:45	0.150	0.024	5	0
HS South	5/9/2024 15:45	5/9/2024 15:55	0.150	0.024	5	0
HS South	5/9/2024 15:55	5/9/2024 16:00	0.150	0.024	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/9/2024 9:05	5/9/2024 9:15	0.150	0	5	0
PER2 2024	5/9/2024 9:15	5/9/2024 9:25	0.150	0.001	5	0
PER2 2024	5/9/2024 9:25	5/9/2024 9:35	0.150	0.001	5	0
PER2 2024	5/9/2024 9:35	5/9/2024 9:45	0.150	0.001	5	0
PER2 2024	5/9/2024 9:45	5/9/2024 9:55	0.150	0.001	5	0
PER2 2024	5/9/2024 9:55	5/9/2024 10:05	0.150	0.001	5	0
PER2 2024	5/9/2024 10:05	5/9/2024 10:15	0.150	0.001	5	0
PER2 2024	5/9/2024 10:15	5/9/2024 10:25	0.150	0.001	5	0
PER2 2024	5/9/2024 10:25	5/9/2024 10:35	0.150	0.001	5	0
PER2 2024	5/9/2024 10:35	5/9/2024 10:45	0.150	0.001	5	0
PER2 2024	5/9/2024 10:45	5/9/2024 10:55	0.150	0.001	5	0
PER2 2024	5/9/2024 10:55	5/9/2024 11:05	0.150	0.001	5	0
PER2 2024	5/9/2024 11:05	5/9/2024 11:15	0.150	0.001	5	0
PER2 2024	5/9/2024 11:15	5/9/2024 11:25	0.150	0.001	5	0
PER2 2024	5/9/2024 11:25	5/9/2024 11:35	0.150	0.001	5	0
PER2 2024	5/9/2024 11:35	5/9/2024 11:45	0.150	0.001	5	0
PER2 2024	5/9/2024 11:45	5/9/2024 11:55	0.150	0.001	5	0
PER2 2024	5/9/2024 11:55	5/9/2024 12:05	0.150	0.001	5	0
PER2 2024	5/9/2024 12:05	5/9/2024 12:15	0.150	0.001	5	0
PER2 2024	5/9/2024 12:15	5/9/2024 12:25	0.150	0.002	5	0
PER2 2024	5/9/2024 12:25	5/9/2024 12:35	0.150	0.002	5	0
PER2 2024	5/9/2024 12:35	5/9/2024 12:45	0.150	0.002	5	0
PER2 2024	5/9/2024 12:45	5/9/2024 12:55	0.150	0.002	5	0
PER2 2024	5/9/2024 12:55	5/9/2024 13:05	0.150	0.002	5	0
PER2 2024	5/9/2024 13:05	5/9/2024 13:15	0.150	0.002	5	0
PER2 2024	5/9/2024 13:15	5/9/2024 13:25	0.150	0.002	5	0
PER2 2024	5/9/2024 13:25	5/9/2024 13:35	0.150	0.002	5	0
PER2 2024	5/9/2024 13:35	5/9/2024 13:45	0.150	0.002	5	0
PER2 2024	5/9/2024 13:45	5/9/2024 13:55	0.150	0.002	5	0
PER2 2024	5/9/2024 13:55	5/9/2024 14:05	0.150	0.002	5	0
PER2 2024	5/9/2024 14:05	5/9/2024 14:15	0.150	0.002	5	0
PER2 2024	5/9/2024 14:15	5/9/2024 14:25	0.150	0.002	5	0
PER2 2024	5/9/2024 14:25	5/9/2024 14:35	0.150	0.002	5	0
PER2 2024	5/9/2024 14:35	5/9/2024 14:45	0.150	0.002	5	0
PER2 2024	5/9/2024 14:45	5/9/2024 14:55	0.150	0.002	5	0
PER2 2024	5/9/2024 14:55	5/9/2024 15:05	0.150	0.002	5	0
PER2 2024	5/9/2024 15:05	5/9/2024 15:15	0.150	0.002	5	0
PER2 2024	5/9/2024 15:15	5/9/2024 15:25	0.150	0.002	5	0
PER2 2024	5/9/2024 15:25	5/9/2024 15:35	0.150	0.002	5	0
PER2 2024	5/9/2024 15:35	5/9/2024 15:45	0.150	0.002	5	0
PER2 2024	5/9/2024 15:45	5/9/2024 15:55	0.150	0.002	5	0
PER2 2024	5/9/2024 15:55	5/9/2024 16:00	0.150	0.002	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/9/2024 7:35	5/9/2024 7:45	0.150	0	5	0
PER1 2024	5/9/2024 7:45	5/9/2024 7:55	0.150	0.001	5	0
PER1 2024	5/9/2024 7:55	5/9/2024 8:05	0.150	0.001	5	0
PER1 2024	5/9/2024 8:05	5/9/2024 8:15	0.150	0.001	5	0
PER1 2024	5/9/2024 8:15	5/9/2024 8:25	0.150	0.001	5	0
PER1 2024	5/9/2024 8:25	5/9/2024 8:35	0.150	0.001	5	0
PER1 2024	5/9/2024 8:35	5/9/2024 8:45	0.150	0.001	5	0
PER1 2024	5/9/2024 8:45	5/9/2024 8:55	0.150	0.001	5	0
PER1 2024	5/9/2024 8:55	5/9/2024 9:05	0.150	0.001	5	0
PER1 2024	5/9/2024 9:05	5/9/2024 9:15	0.150	0.002	5	0
PER1 2024	5/9/2024 9:15	5/9/2024 9:25	0.150	0.002	5	0
PER1 2024	5/9/2024 9:25	5/9/2024 9:35	0.150	0.002	5	0
PER1 2024	5/9/2024 9:35	5/9/2024 9:45	0.150	0.002	5	0
PER1 2024	5/9/2024 9:45	5/9/2024 9:55	0.150	0.002	5	0
PER1 2024	5/9/2024 9:55	5/9/2024 10:05	0.150	0.002	5	0
PER1 2024	5/9/2024 10:05	5/9/2024 10:15	0.150	0.002	5	0
PER1 2024	5/9/2024 10:15	5/9/2024 10:25	0.150	0.002	5	0
PER1 2024	5/9/2024 10:25	5/9/2024 10:35	0.150	0.002	5	0
PER1 2024	5/9/2024 10:35	5/9/2024 10:45	0.150	0.002	5	0
PER1 2024	5/9/2024 10:45	5/9/2024 10:55	0.150	0.002	5	0
PER1 2024	5/9/2024 10:55	5/9/2024 11:05	0.150	0.002	5	0
PER1 2024	5/9/2024 11:05	5/9/2024 11:15	0.150	0.002	5	0
PER1 2024	5/9/2024 11:15	5/9/2024 11:25	0.150	0.002	5	0
PER1 2024	5/9/2024 11:25	5/9/2024 11:35	0.150	0.003	5	0
PER1 2024	5/9/2024 11:35	5/9/2024 11:45	0.150	0.003	5	0
PER1 2024	5/9/2024 11:45	5/9/2024 11:55	0.150	0.003	5	0
PER1 2024	5/9/2024 11:55	5/9/2024 12:05	0.150	0.003	5	0
PER1 2024	5/9/2024 12:05	5/9/2024 12:15	0.150	0.003	5	0
PER1 2024	5/9/2024 12:15	5/9/2024 12:25	0.150	0.003	5	0
PER1 2024	5/9/2024 12:25	5/9/2024 12:35	0.150	0.003	5	0
PER1 2024	5/9/2024 12:35	5/9/2024 12:45	0.150	0.003	5	0
PER1 2024	5/9/2024 12:45	5/9/2024 12:55	0.150	0.004	5	0.011
PER1 2024	5/9/2024 12:55	5/9/2024 13:05	0.150	0.004	5	0.011
PER1 2024	5/9/2024 13:05	5/9/2024 13:15	0.150	0.004	5	0.011
PER1 2024	5/9/2024 13:15	5/9/2024 13:25	0.150	0.004	5	0.011
PER1 2024	5/9/2024 13:25	5/9/2024 13:35	0.150	0.004	5	0.011
PER1 2024	5/9/2024 13:35	5/9/2024 13:45	0.150	0.004	5	0.011
PER1 2024	5/9/2024 13:45	5/9/2024 13:55	0.150	0.004	5	0.011
PER1 2024	5/9/2024 13:55	5/9/2024 14:05	0.150	0.004	5	0.011
PER1 2024	5/9/2024 14:05	5/9/2024 14:15	0.150	0.004	5	0.011
PER1 2024	5/9/2024 14:15	5/9/2024 14:25	0.150	0.004	5	0.011
PER1 2024	5/9/2024 14:25	5/9/2024 14:35	0.150	0.005	5	0.011
PER1 2024	5/9/2024 14:35	5/9/2024 14:45	0.150	0.005	5	0.011
PER1 2024	5/9/2024 14:45	5/9/2024 14:55	0.150	0.005	5	0.011
PER1 2024	5/9/2024 14:55	5/9/2024 15:05	0.150	0.005	5	0.011
PER1 2024	5/9/2024 15:05	5/9/2024 15:15	0.150	0.005	5	0.011
PER1 2024	5/9/2024 15:15	5/9/2024 15:25	0.150	0.005	5	0.011
PER1 2024	5/9/2024 15:25	5/9/2024 15:35	0.150	0.005	5	0.011
PER1 2024	5/9/2024 15:35	5/9/2024 15:45	0.150	0.005	5	0
PER1 2024	5/9/2024 15:45	5/9/2024 15:55	0.150	0	5	0
PER1 2024	5/9/2024 15:55	5/9/2024 16:00	0.150	0	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/10/2024

Weather: 50 deg. F, Rain/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continues excavation, soil stockpiling for off-site disposal, rebar installation and building foundation development.
- 2) Delayed start time due to heavy rain in the morning. The concrete pour was cancelled for the day.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below. The air monitoring start time was delayed due to heavy rain in the morning.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8645	1520	4140

Site Layout Map and Excavation Figures

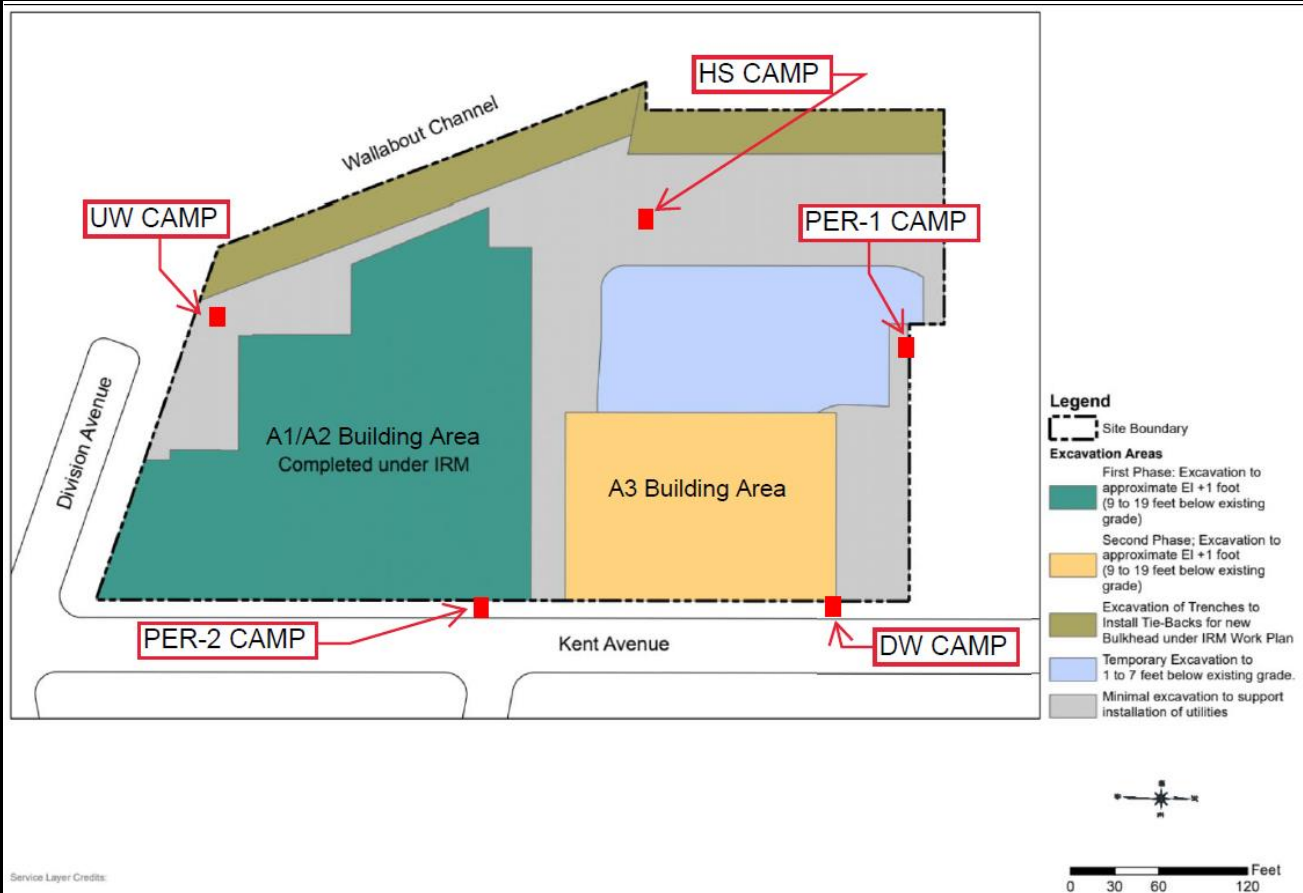

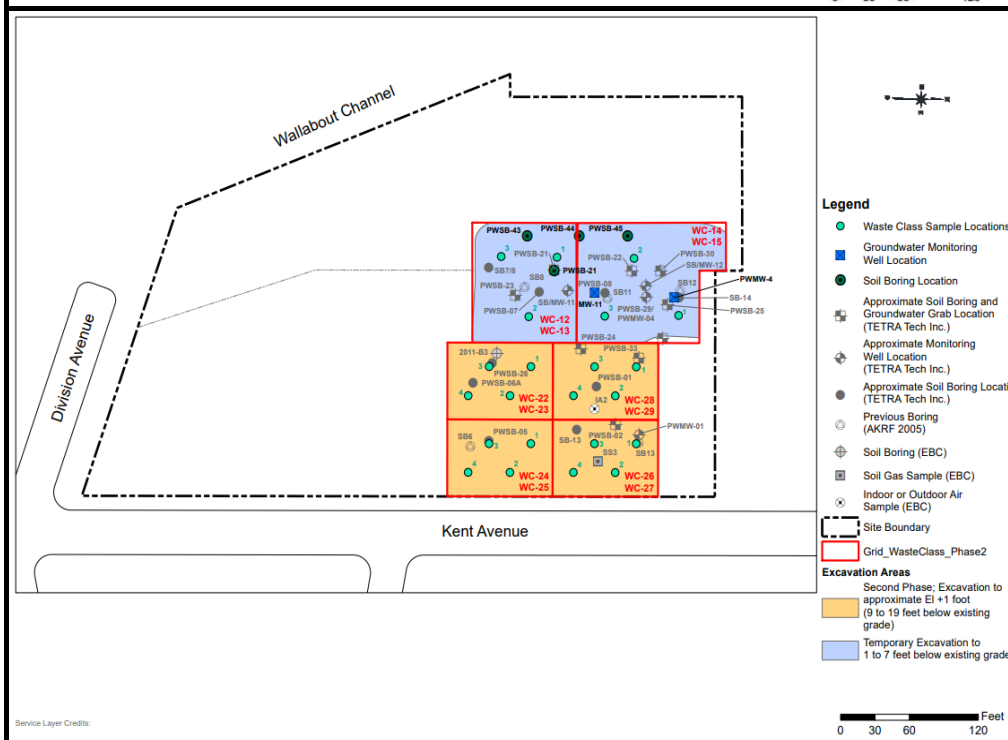
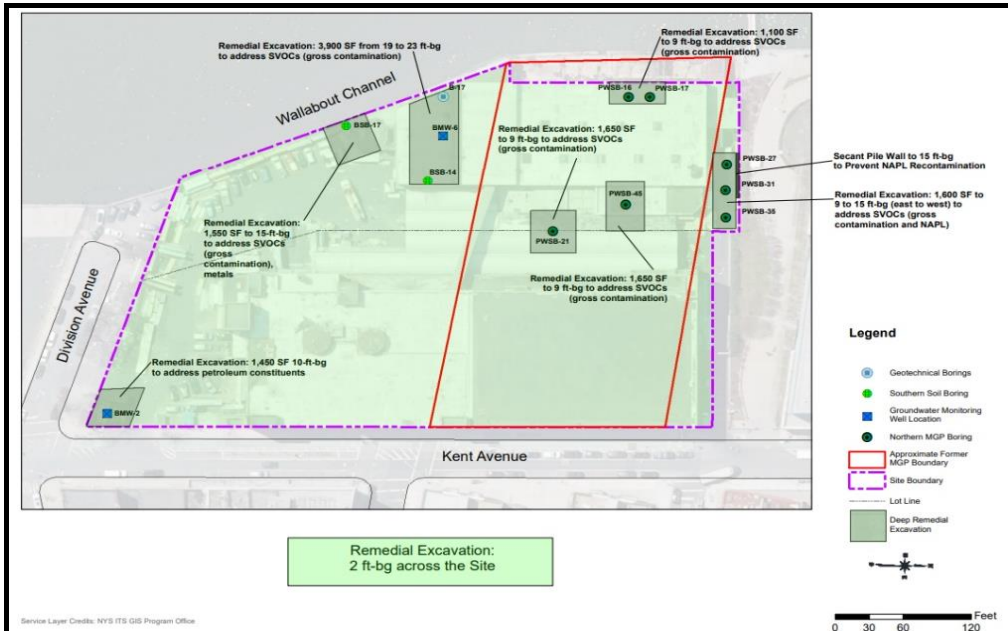


Photo 1:
View of Site conditions
facing south.

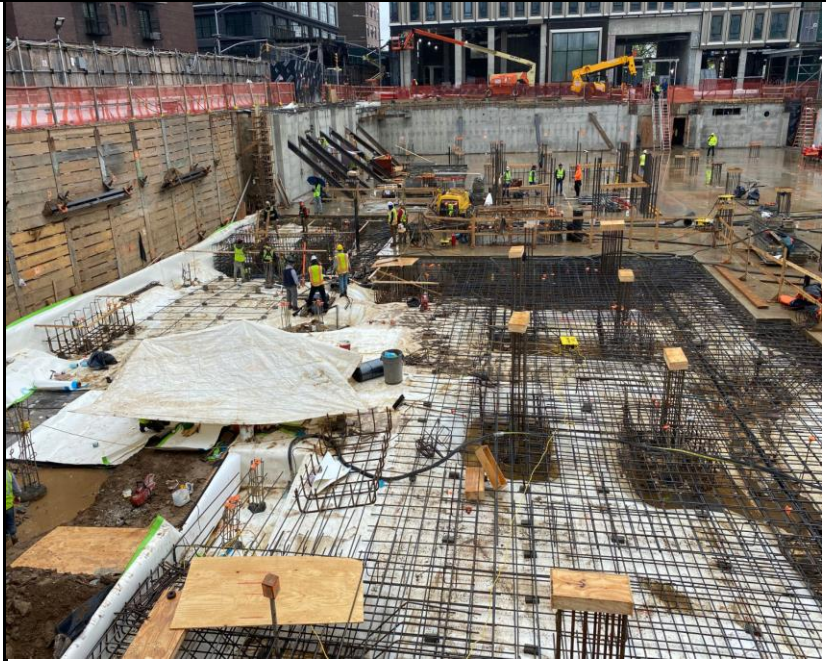


Photo 2:
View of Site conditions
and foundation
development facing east.

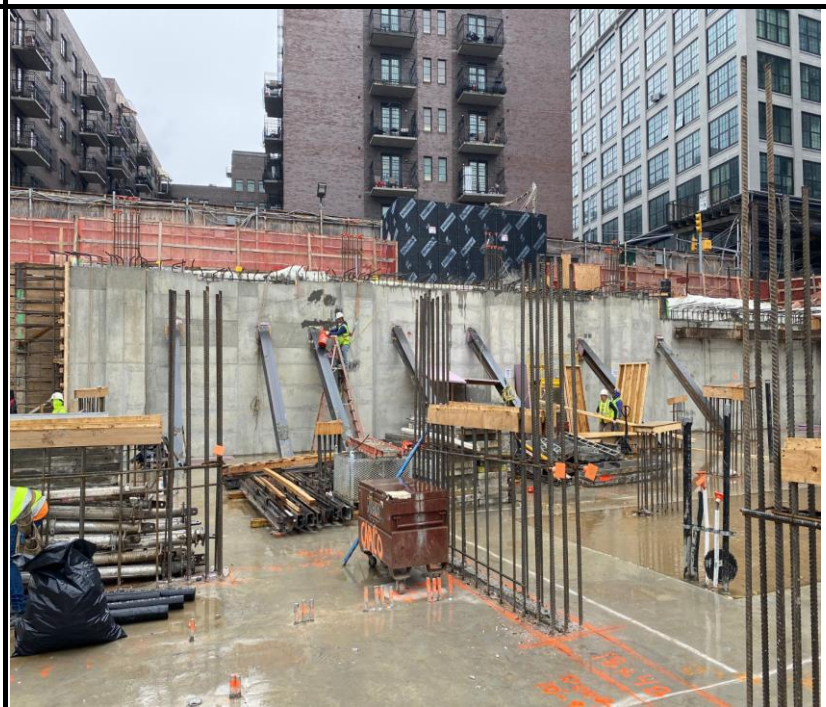


Photo 3:
View of remaining
soil for off-site
disposal.




Photo 4:
View of staged
excavators.



CAMP:
Downwind
Particulates

Dust Levels


0.003 mg/m³ 0.002 mg/m³

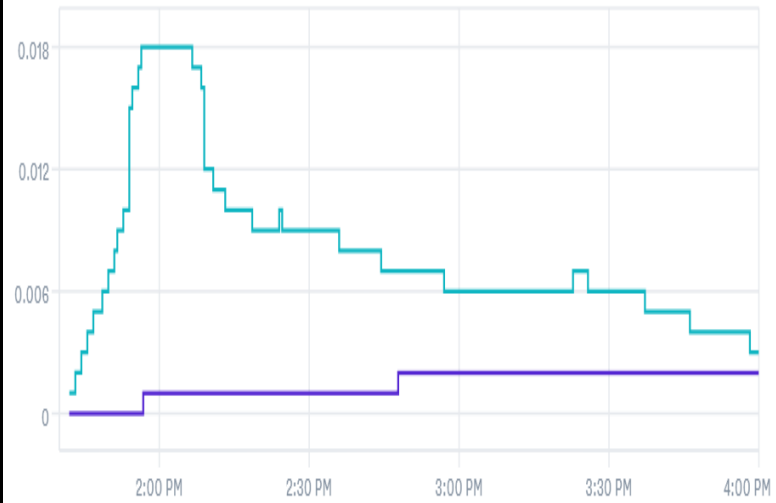

CAMP:
Downwind VOCs


VOC Levels

0 ppm 0 ppm

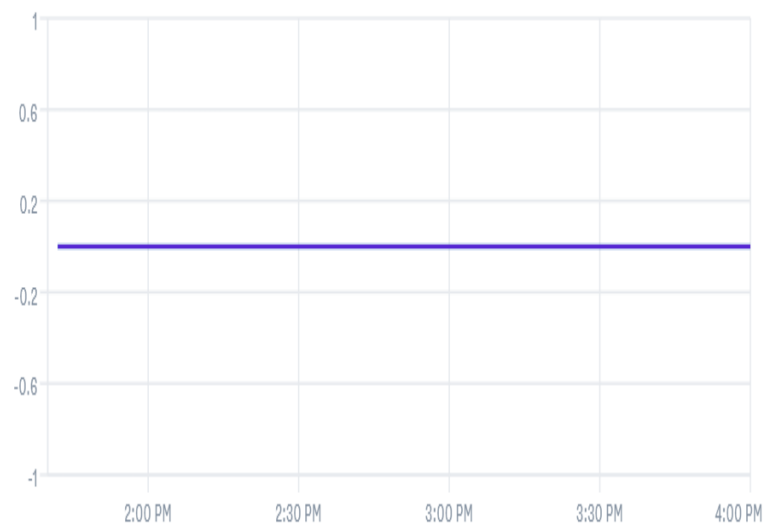


CAMP:
Upwind Particulates

Dust Levels

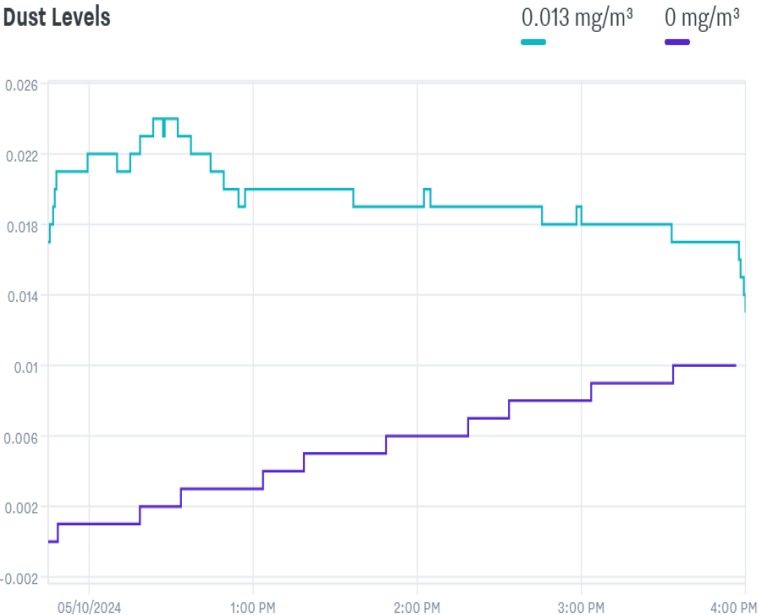

CAMP:
Upwind VOCs

VOC Levels

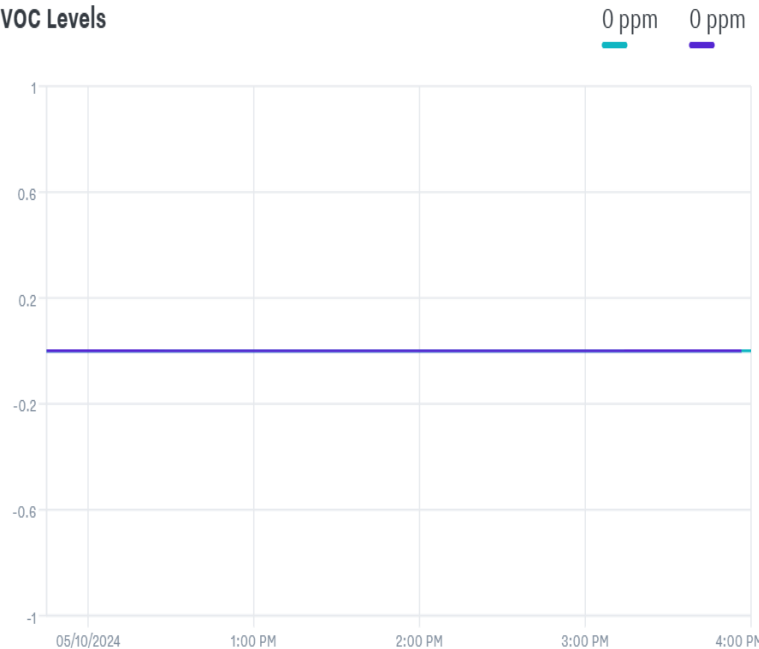

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/10/2024 13:40	5/10/2024 13:50	0.150	0	5	0
DW 2024	5/10/2024 13:50	5/10/2024 14:00	0.150	0.001	5	0
DW 2024	5/10/2024 14:00	5/10/2024 14:10	0.150	0.001	5	0
DW 2024	5/10/2024 14:10	5/10/2024 14:20	0.150	0.001	5	0
DW 2024	5/10/2024 14:20	5/10/2024 14:30	0.150	0.001	5	0
DW 2024	5/10/2024 14:30	5/10/2024 14:40	0.150	0.001	5	0
DW 2024	5/10/2024 14:40	5/10/2024 14:50	0.150	0.002	5	0
DW 2024	5/10/2024 14:50	5/10/2024 15:00	0.150	0.002	5	0
DW 2024	5/10/2024 15:00	5/10/2024 15:10	0.150	0.002	5	0
DW 2024	5/10/2024 15:10	5/10/2024 15:20	0.150	0.002	5	0
DW 2024	5/10/2024 15:20	5/10/2024 15:30	0.150	0.002	5	0
DW 2024	5/10/2024 15:30	5/10/2024 15:40	0.150	0.002	5	0
DW 2024	5/10/2024 15:40	5/10/2024 15:50	0.150	0.002	5	0
DW 2024	5/10/2024 15:50	5/10/2024 16:00	0.150	0.002	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/10/2024 11:30	5/10/2024 11:40	0.150	0	5	0
UW 2024	5/10/2024 11:40	5/10/2024 11:50	0.150	0.001	5	0
UW 2024	5/10/2024 11:50	5/10/2024 12:00	0.150	0.001	5	0
UW 2024	5/10/2024 12:00	5/10/2024 12:10	0.150	0.001	5	0
UW 2024	5/10/2024 12:10	5/10/2024 12:20	0.150	0.002	5	0
UW 2024	5/10/2024 12:20	5/10/2024 12:30	0.150	0.002	5	0
UW 2024	5/10/2024 12:30	5/10/2024 12:40	0.150	0.003	5	0
UW 2024	5/10/2024 12:40	5/10/2024 12:50	0.150	0.003	5	0
UW 2024	5/10/2024 12:50	5/10/2024 13:00	0.150	0.003	5	0
UW 2024	5/10/2024 13:00	5/10/2024 13:10	0.150	0.004	5	0
UW 2024	5/10/2024 13:10	5/10/2024 13:20	0.150	0.005	5	0
UW 2024	5/10/2024 13:20	5/10/2024 13:30	0.150	0.005	5	0
UW 2024	5/10/2024 13:30	5/10/2024 13:40	0.150	0.005	5	0
UW 2024	5/10/2024 13:40	5/10/2024 13:50	0.150	0.006	5	0
UW 2024	5/10/2024 13:50	5/10/2024 14:00	0.150	0.006	5	0
UW 2024	5/10/2024 14:00	5/10/2024 14:10	0.150	0.006	5	0
UW 2024	5/10/2024 14:10	5/10/2024 14:20	0.150	0.007	5	0
UW 2024	5/10/2024 14:20	5/10/2024 14:30	0.150	0.007	5	0
UW 2024	5/10/2024 14:30	5/10/2024 14:40	0.150	0.008	5	0
UW 2024	5/10/2024 14:40	5/10/2024 14:50	0.150	0.008	5	0
UW 2024	5/10/2024 14:50	5/10/2024 15:00	0.150	0.008	5	0
UW 2024	5/10/2024 15:00	5/10/2024 15:10	0.150	0.009	5	0
UW 2024	5/10/2024 15:10	5/10/2024 15:20	0.150	0.009	5	0
UW 2024	5/10/2024 15:20	5/10/2024 15:30	0.150	0.009	5	0
UW 2024	5/10/2024 15:30	5/10/2024 15:40	0.150	0.01	5	0
UW 2024	5/10/2024 15:40	5/10/2024 15:50	0.150	0.01	5	0
UW 2024	5/10/2024 15:50	5/10/2024 16:00	0.150	0.01	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/10/2024 13:50	5/10/2024 14:00	0.150	0	5	0
HS South	5/10/2024 14:00	5/10/2024 14:10	0.150	0.001	5	0
HS South	5/10/2024 14:10	5/10/2024 14:20	0.150	0.001	5	0
HS South	5/10/2024 14:20	5/10/2024 14:30	0.150	0.001	5	0
HS South	5/10/2024 14:30	5/10/2024 14:40	0.150	0.001	5	0
HS South	5/10/2024 14:40	5/10/2024 14:50	0.150	0.002	5	0
HS South	5/10/2024 14:50	5/10/2024 15:00	0.150	0.002	5	0
HS South	5/10/2024 15:00	5/10/2024 15:10	0.150	0.002	5	0
HS South	5/10/2024 15:10	5/10/2024 15:20	0.150	0.003	5	0
HS South	5/10/2024 15:20	5/10/2024 15:30	0.150	0.003	5	0
HS South	5/10/2024 15:30	5/10/2024 15:40	0.150	0.003	5	0
HS South	5/10/2024 15:40	5/10/2024 15:50	0.150	0.003	5	0
HS South	5/10/2024 15:50	5/10/2024 16:00	0.150	0.004	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/10/2024 14:10	5/10/2024 14:20	0.150	0	5	0
PER2 2024	5/10/2024 14:20	5/10/2024 14:30	0.150	0.001	5	0
PER2 2024	5/10/2024 14:30	5/10/2024 14:40	0.150	0.001	5	0
PER2 2024	5/10/2024 14:40	5/10/2024 14:50	0.150	0.001	5	0
PER2 2024	5/10/2024 14:50	5/10/2024 15:00	0.150	0.001	5	0
PER2 2024	5/10/2024 15:00	5/10/2024 15:10	0.150	0.001	5	0
PER2 2024	5/10/2024 15:10	5/10/2024 15:20	0.150	0.001	5	0
PER2 2024	5/10/2024 15:20	5/10/2024 15:30	0.150	0.001	5	0
PER2 2024	5/10/2024 15:30	5/10/2024 15:40	0.150	0.001	5	0
PER2 2024	5/10/2024 15:40	5/10/2024 15:50	0.150	0.001	5	0
PER2 2024	5/10/2024 15:50	5/10/2024 16:00	0.150	0.001	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/10/2024 14:00	5/10/2024 14:10	0.150	0	5	0
PER1 2024	5/10/2024 14:10	5/10/2024 14:20	0.150	0.001	5	0
PER1 2024	5/10/2024 14:20	5/10/2024 14:30	0.150	0.001	5	0
PER1 2024	5/10/2024 14:30	5/10/2024 14:40	0.150	0.001	5	0
PER1 2024	5/10/2024 14:40	5/10/2024 14:50	0.150	0.001	5	0
PER1 2024	5/10/2024 14:50	5/10/2024 15:00	0.150	0.001	5	0
PER1 2024	5/10/2024 15:00	5/10/2024 15:10	0.150	0.001	5	0
PER1 2024	5/10/2024 15:10	5/10/2024 15:20	0.150	0.002	5	0
PER1 2024	5/10/2024 15:20	5/10/2024 15:30	0.150	0.002	5	0
PER1 2024	5/10/2024 15:30	5/10/2024 15:40	0.150	0.002	5	0
PER1 2024	5/10/2024 15:40	5/10/2024 15:50	0.150	0.002	5	0
PER1 2024	5/10/2024 15:50	5/10/2024 16:00	0.150	0.002	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/13/2024

Weather: 70 deg. F, Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

- 1) Alba continued rebar and waterproofing installation for the foundation development.
- 2) Casino, the structural contractor, was on-site to begin mobilization.
- 3) Complete over-excavation and collect additional endpoint samples for EP-84, see below for details.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red)

Were there any changes to the H&S Plan? YES NO NA

Were there any CAMP exceedances at the perimeter above action levels: YES NO NA

Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): EP-84 E, EP-84 N, EP-84 S, EP-84 W and EP-84 C

Air Monitoring (Since Last Report): CAMP graphs and tables are included below. The downwind CAMP station experienced battery issues. The field personnel was able to remedy the issue and get the station back on-line prior to the end of work.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8645	1520	4140

Site Layout Map and Excavation Figures

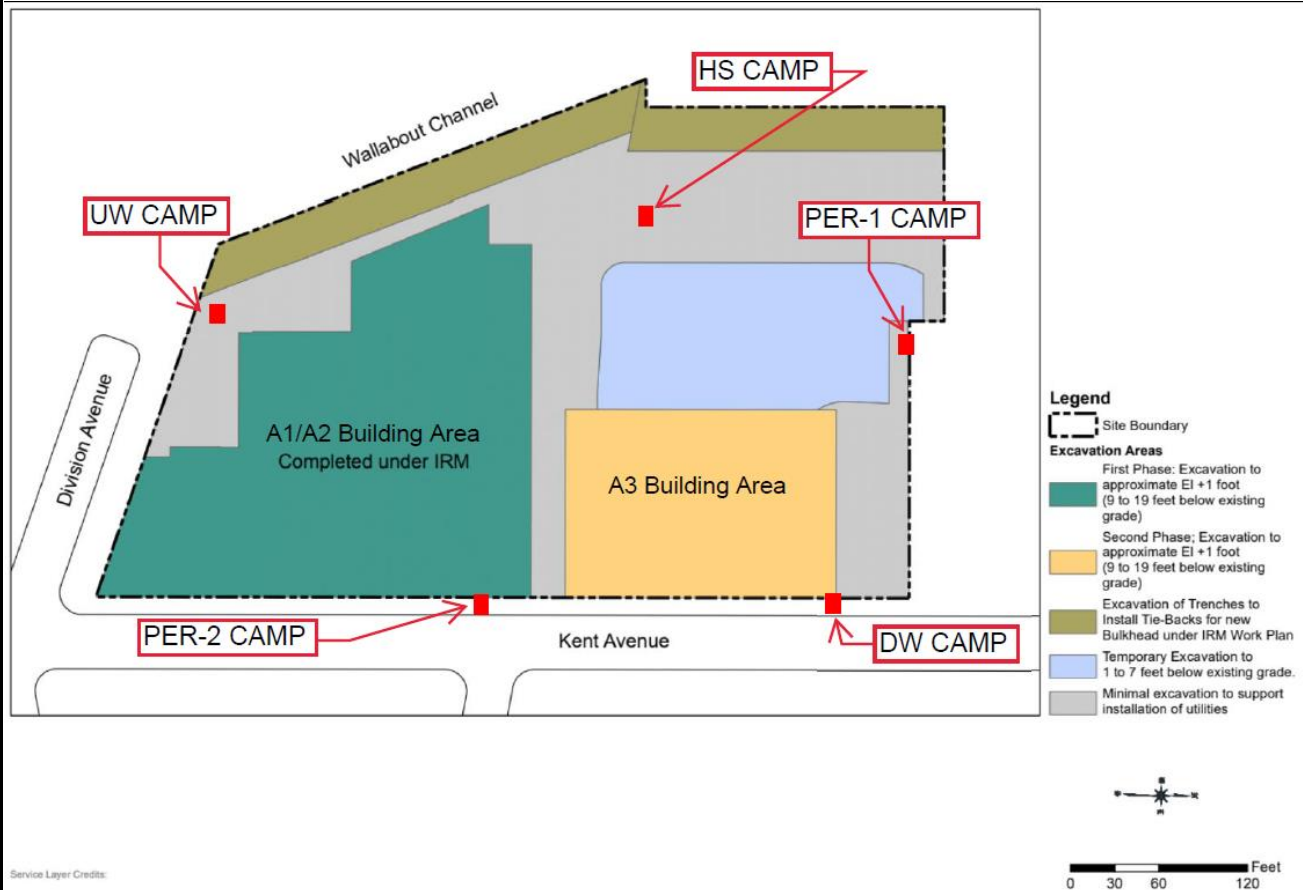

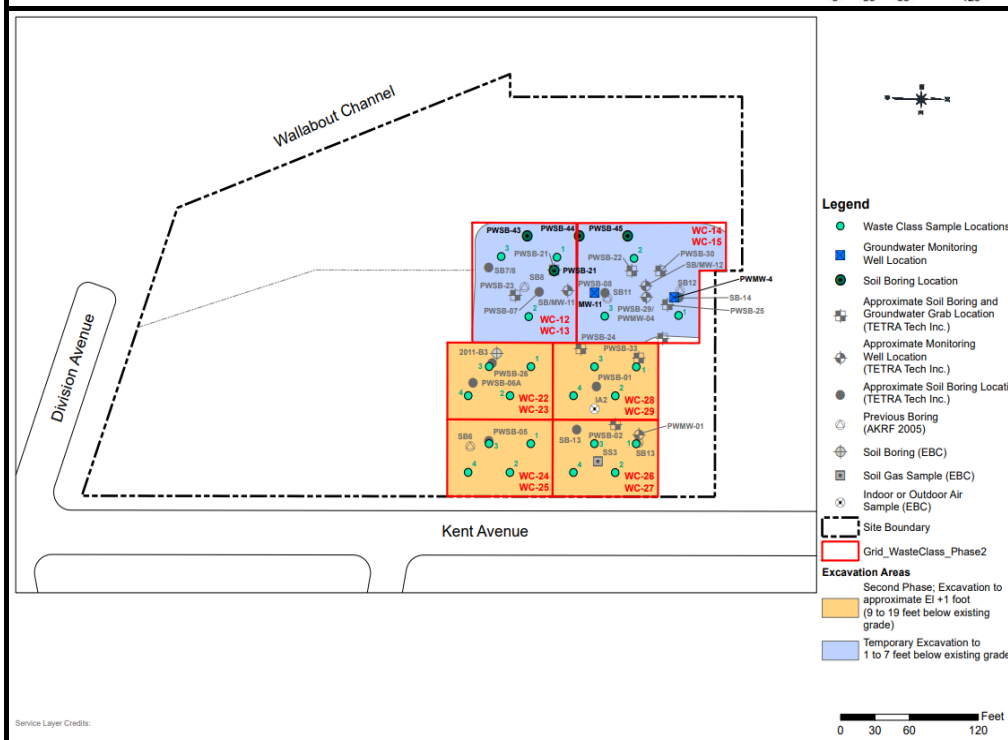
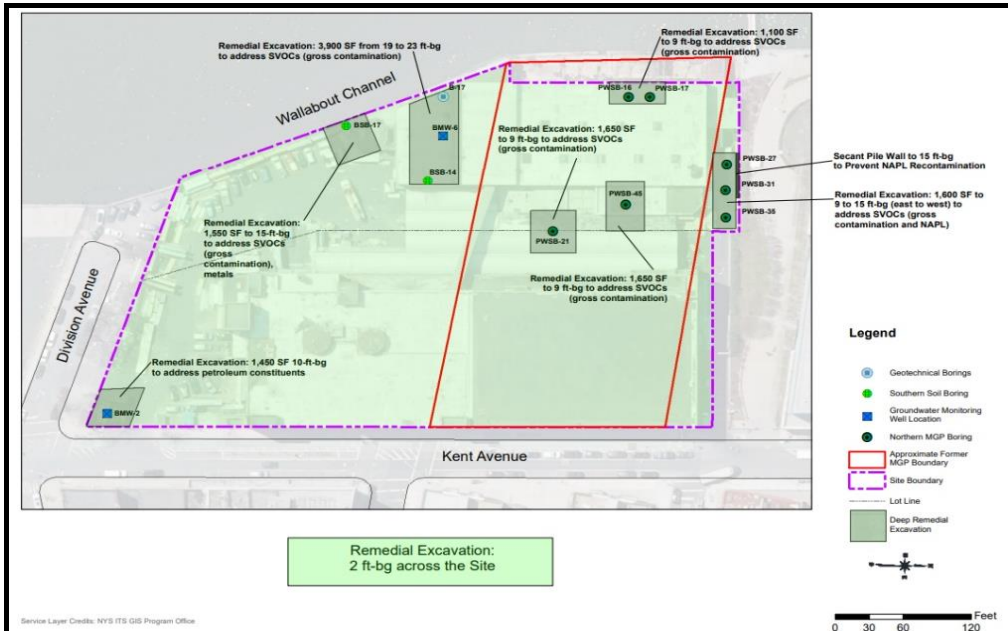


Photo 1:
View of Site conditions
facing southeast.

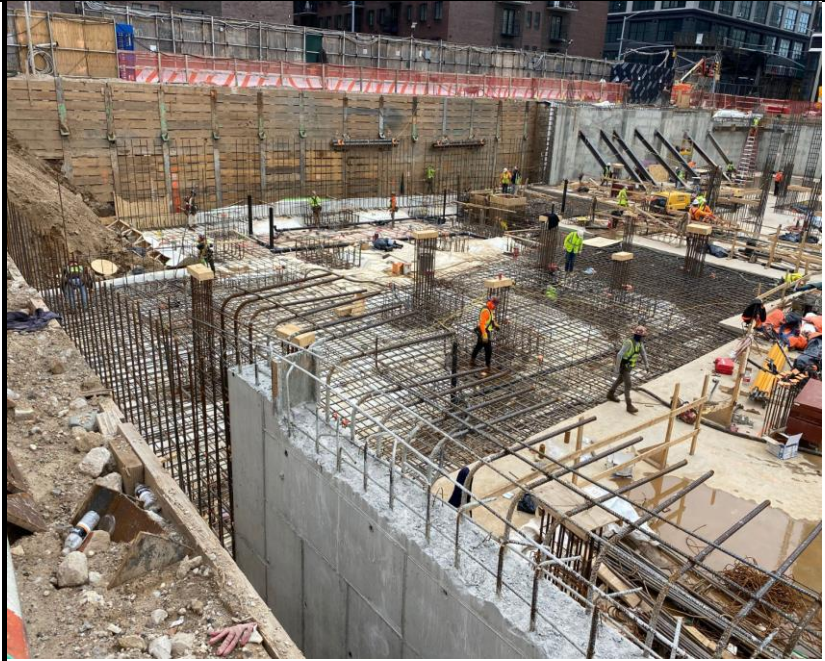


Photo 2:
View of Site conditions
and foundation
development facing
south.



Photo 3:
View of Site
conditions facing
north.




Photo 4:
View of truck
washing prior to off-
site departure of
vehicle.



CAMP:
Downwind
Particulates

Dust Levels


0.018 mg/m³ 0.013 mg/m³

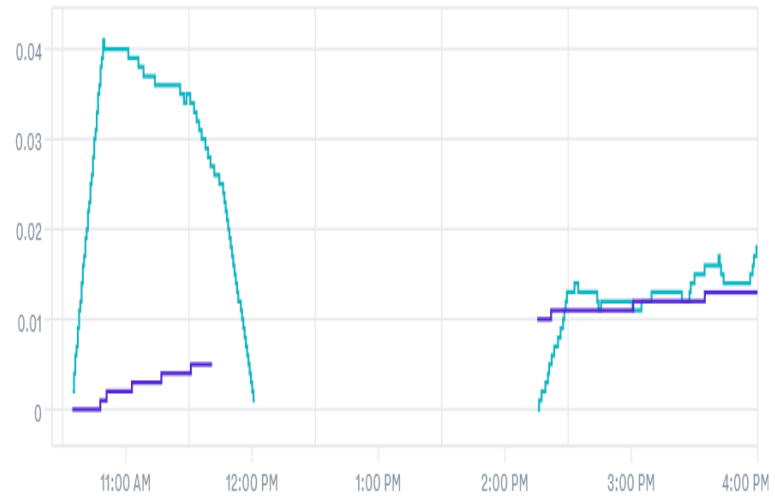


CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm

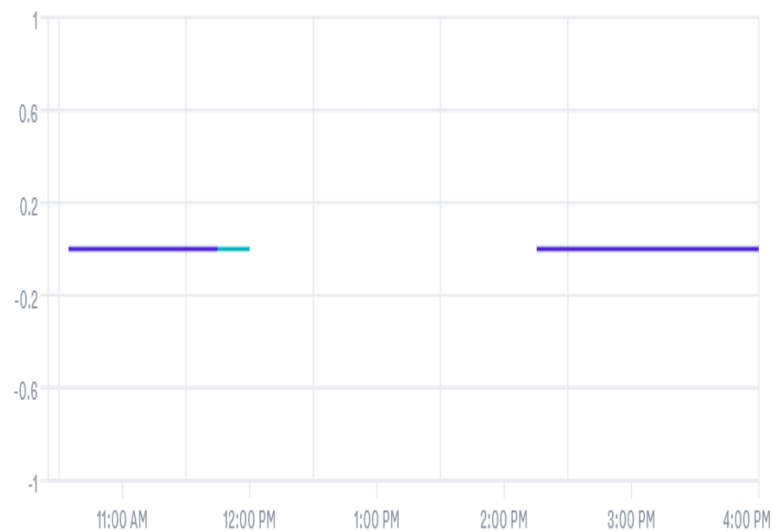

CAMP:
Upwind Particulates

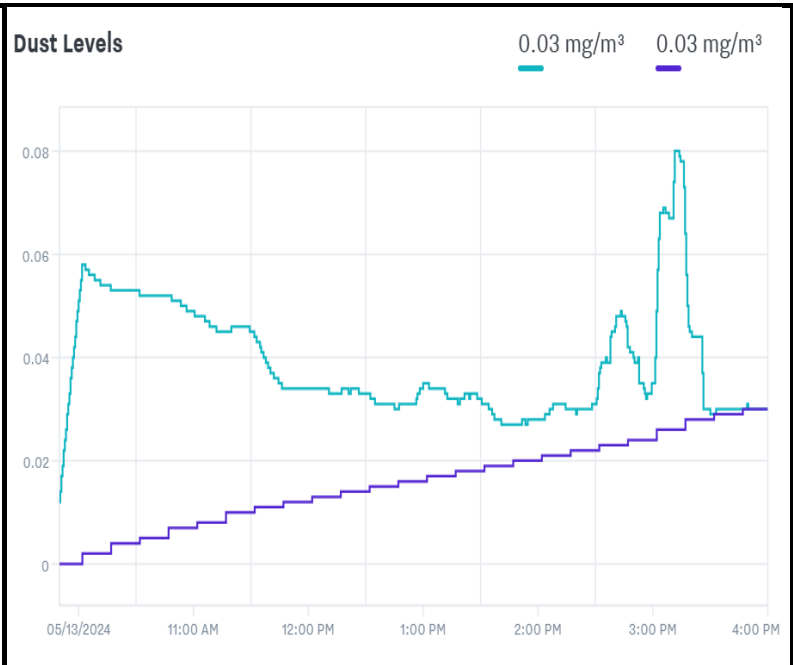

CAMP:
Upwind VOCs

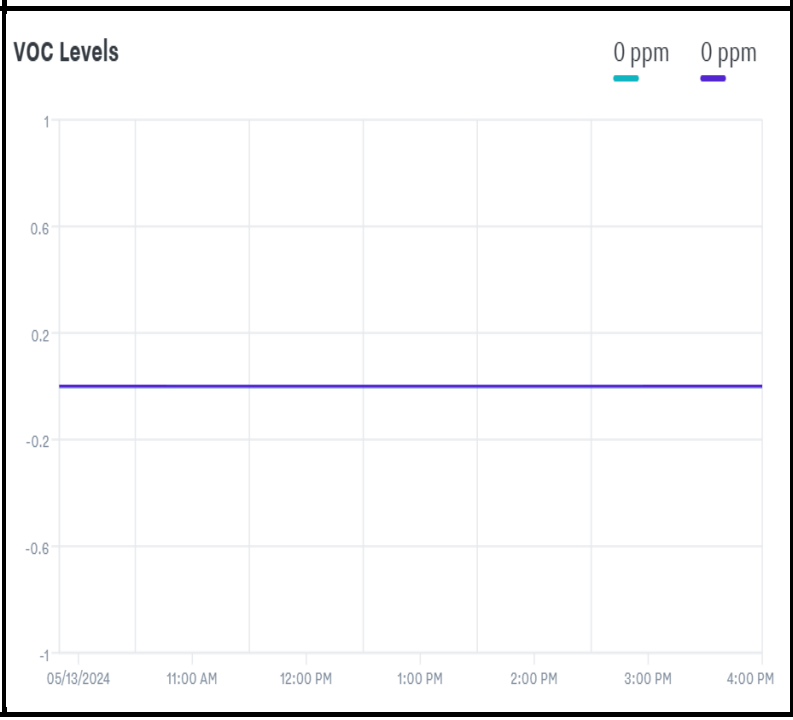

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/13/2024 10:30	5/13/2024 10:40	0.150	0	5	0
DW 2024	5/13/2024 10:40	5/13/2024 10:50	0.150	0.001	5	0
DW 2024	5/13/2024 10:50	5/13/2024 11:00	0.150	0.002	5	0
DW 2024	5/13/2024 11:00	5/13/2024 11:10	0.150	0.003	5	0
DW 2024	5/13/2024 11:10	5/13/2024 11:20	0.150	0.004	5	0
DW 2024	5/13/2024 11:20	5/13/2024 11:30	0.150	0.004	5	0
DW 2024	5/13/2024 11:30	5/13/2024 11:40	0.150	0.005	5	0
DW 2024	5/13/2024 11:40	5/13/2024 11:50	0.150	0.005	5	0
DW 2024	5/13/2024 11:50	5/13/2024 12:00	0.150	0.005	5	0
DW 2024	5/13/2024 12:00	5/13/2024 12:10	0.150	0.005	5	0
DW 2024	5/13/2024 12:10	5/13/2024 12:20	0.150	0.005	5	0
DW 2024	5/13/2024 12:20	5/13/2024 12:30	0.150	0.005	5	0
DW 2024	5/13/2024 12:30	5/13/2024 12:40	0.150	0.005	5	0
DW 2024	5/13/2024 12:40	5/13/2024 12:50	0.150	0.005	5	0
DW 2024	5/13/2024 12:50	5/13/2024 13:00	0.150	0.005	5	0
DW 2024	5/13/2024 13:00	5/13/2024 13:10	0.150	0.005	5	0
DW 2024	5/13/2024 13:10	5/13/2024 13:20	0.150	0.005	5	0
DW 2024	5/13/2024 13:20	5/13/2024 13:30	0.150	0.005	5	0
DW 2024	5/13/2024 13:30	5/13/2024 13:40	0.150	0.005	5	0
DW 2024	5/13/2024 13:40	5/13/2024 13:50	0.150	0.005	5	0
DW 2024	5/13/2024 13:50	5/13/2024 14:00	0.150	0.005	5	0
DW 2024	5/13/2024 14:00	5/13/2024 14:10	0.150	0.005	5	0
DW 2024	5/13/2024 14:10	5/13/2024 14:20	0.150	0.01	5	0
DW 2024	5/13/2024 14:20	5/13/2024 14:30	0.150	0.011	5	0
DW 2024	5/13/2024 14:30	5/13/2024 14:40	0.150	0.011	5	0
DW 2024	5/13/2024 14:40	5/13/2024 14:50	0.150	0.011	5	0
DW 2024	5/13/2024 14:50	5/13/2024 15:00	0.150	0.011	5	0
DW 2024	5/13/2024 15:00	5/13/2024 15:10	0.150	0.012	5	0
DW 2024	5/13/2024 15:10	5/13/2024 15:20	0.150	0.012	5	0
DW 2024	5/13/2024 15:20	5/13/2024 15:30	0.150	0.012	5	0
DW 2024	5/13/2024 15:30	5/13/2024 15:40	0.150	0.013	5	0
DW 2024	5/13/2024 15:40	5/13/2024 15:50	0.150	0.013	5	0
DW 2024	5/13/2024 15:50	5/13/2024 16:00	0.150	0.013	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/13/2024 9:50	5/13/2024 10:00	0.150	0	5	0
UW 2024	5/13/2024 10:00	5/13/2024 10:10	0.150	0.002	5	0
UW 2024	5/13/2024 10:10	5/13/2024 10:20	0.150	0.004	5	0
UW 2024	5/13/2024 10:20	5/13/2024 10:30	0.150	0.004	5	0
UW 2024	5/13/2024 10:30	5/13/2024 10:40	0.150	0.005	5	0
UW 2024	5/13/2024 10:40	5/13/2024 10:50	0.150	0.007	5	0
UW 2024	5/13/2024 10:50	5/13/2024 11:00	0.150	0.007	5	0
UW 2024	5/13/2024 11:00	5/13/2024 11:10	0.150	0.008	5	0
UW 2024	5/13/2024 11:10	5/13/2024 11:20	0.150	0.01	5	0
UW 2024	5/13/2024 11:20	5/13/2024 11:30	0.150	0.01	5	0
UW 2024	5/13/2024 11:30	5/13/2024 11:40	0.150	0.011	5	0
UW 2024	5/13/2024 11:40	5/13/2024 11:50	0.150	0.012	5	0
UW 2024	5/13/2024 11:50	5/13/2024 12:00	0.150	0.012	5	0
UW 2024	5/13/2024 12:00	5/13/2024 12:10	0.150	0.013	5	0
UW 2024	5/13/2024 12:10	5/13/2024 12:20	0.150	0.014	5	0
UW 2024	5/13/2024 12:20	5/13/2024 12:30	0.150	0.014	5	0
UW 2024	5/13/2024 12:30	5/13/2024 12:40	0.150	0.015	5	0
UW 2024	5/13/2024 12:40	5/13/2024 12:50	0.150	0.016	5	0
UW 2024	5/13/2024 12:50	5/13/2024 13:00	0.150	0.016	5	0
UW 2024	5/13/2024 13:00	5/13/2024 13:10	0.150	0.017	5	0
UW 2024	5/13/2024 13:10	5/13/2024 13:20	0.150	0.018	5	0
UW 2024	5/13/2024 13:20	5/13/2024 13:30	0.150	0.018	5	0
UW 2024	5/13/2024 13:30	5/13/2024 13:40	0.150	0.019	5	0
UW 2024	5/13/2024 13:40	5/13/2024 13:50	0.150	0.02	5	0
UW 2024	5/13/2024 13:50	5/13/2024 14:00	0.150	0.02	5	0
UW 2024	5/13/2024 14:00	5/13/2024 14:10	0.150	0.021	5	0
UW 2024	5/13/2024 14:10	5/13/2024 14:20	0.150	0.022	5	0
UW 2024	5/13/2024 14:20	5/13/2024 14:30	0.150	0.022	5	0
UW 2024	5/13/2024 14:30	5/13/2024 14:40	0.150	0.023	5	0
UW 2024	5/13/2024 14:40	5/13/2024 14:50	0.150	0.024	5	0
UW 2024	5/13/2024 14:50	5/13/2024 15:00	0.150	0.024	5	0
UW 2024	5/13/2024 15:00	5/13/2024 15:10	0.150	0.026	5	0
UW 2024	5/13/2024 15:10	5/13/2024 15:20	0.150	0.028	5	0
UW 2024	5/13/2024 15:20	5/13/2024 15:30	0.150	0.028	5	0
UW 2024	5/13/2024 15:30	5/13/2024 15:40	0.150	0.029	5	0
UW 2024	5/13/2024 15:40	5/13/2024 15:50	0.150	0.03	5	0
UW 2024	5/13/2024 15:50	5/13/2024 16:00	0.150	0.03	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/13/2024 9:00	5/13/2024 9:10	0.150	0.004	5	0
HS South	5/13/2024 9:10	5/13/2024 9:20	0.150	0.004	5	0
HS South	5/13/2024 9:20	5/13/2024 9:30	0.150	0.004	5	0
HS South	5/13/2024 9:30	5/13/2024 9:40	0.150	0.004	5	0
HS South	5/13/2024 9:40	5/13/2024 9:50	0.150	0.004	5	0
HS South	5/13/2024 9:50	5/13/2024 10:00	0.150	0.004	5	0
HS South	5/13/2024 10:00	5/13/2024 10:10	0.150	0.004	5	0
HS South	5/13/2024 10:10	5/13/2024 10:20	0.150	0.004	5	0
HS South	5/13/2024 10:20	5/13/2024 10:30	0.150	0.004	5	0
HS South	5/13/2024 10:30	5/13/2024 10:40	0.150	0.004	5	0
HS South	5/13/2024 10:40	5/13/2024 10:50	0.150	0.004	5	0
HS South	5/13/2024 10:50	5/13/2024 11:00	0.150	0.002	5	0
HS South	5/13/2024 11:00	5/13/2024 11:10	0.150	0.003	5	0
HS South	5/13/2024 11:10	5/13/2024 11:20	0.150	0.004	5	0
HS South	5/13/2024 11:20	5/13/2024 11:30	0.150	0.005	5	0
HS South	5/13/2024 11:30	5/13/2024 11:40	0.150	0.006	5	0
HS South	5/13/2024 11:40	5/13/2024 11:50	0.150	0.007	5	0
HS South	5/13/2024 11:50	5/13/2024 12:00	0.150	0.008	5	0
HS South	5/13/2024 12:00	5/13/2024 12:10	0.150	0.009	5	0
HS South	5/13/2024 12:10	5/13/2024 12:20	0.150	0.01	5	0
HS South	5/13/2024 12:20	5/13/2024 12:30	0.150	0.011	5	0
HS South	5/13/2024 12:30	5/13/2024 12:40	0.150	0.011	5	0
HS South	5/13/2024 12:40	5/13/2024 12:50	0.150	0.012	5	0
HS South	5/13/2024 12:50	5/13/2024 13:00	0.150	0.013	5	0
HS South	5/13/2024 13:00	5/13/2024 13:10	0.150	0.014	5	0
HS South	5/13/2024 13:10	5/13/2024 13:20	0.150	0.015	5	0
HS South	5/13/2024 13:20	5/13/2024 13:30	0.150	0.016	5	0
HS South	5/13/2024 13:30	5/13/2024 13:40	0.150	0.016	5	0
HS South	5/13/2024 13:40	5/13/2024 13:50	0.150	0.017	5	0
HS South	5/13/2024 13:50	5/13/2024 14:00	0.150	0.018	5	0
HS South	5/13/2024 14:00	5/13/2024 14:10	0.150	0.019	5	0
HS South	5/13/2024 14:10	5/13/2024 14:20	0.150	0.019	5	0
HS South	5/13/2024 14:20	5/13/2024 14:30	0.150	0.02	5	0
HS South	5/13/2024 14:30	5/13/2024 14:40	0.150	0.021	5	0
HS South	5/13/2024 14:40	5/13/2024 14:50	0.150	0.022	5	0
HS South	5/13/2024 14:50	5/13/2024 15:00	0.150	0.022	5	0
HS South	5/13/2024 15:00	5/13/2024 15:10	0.150	0.023	5	0
HS South	5/13/2024 15:10	5/13/2024 15:20	0.150	0.024	5	0
HS South	5/13/2024 15:20	5/13/2024 15:30	0.150	0.025	5	0
HS South	5/13/2024 15:30	5/13/2024 15:40	0.150	0.026	5	0
HS South	5/13/2024 15:40	5/13/2024 15:50	0.150	0.027	5	0
HS South	5/13/2024 15:50	5/13/2024 16:00	0.150	0.027	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/13/2024 10:30	5/13/2024 10:40	0.150	0	5	0
PER2 2024	5/13/2024 10:40	5/13/2024 10:50	0.150	0.002	5	0
PER2 2024	5/13/2024 10:50	5/13/2024 11:00	0.150	0.002	5	0
PER2 2024	5/13/2024 11:00	5/13/2024 11:10	0.150	0.003	5	0
PER2 2024	5/13/2024 11:10	5/13/2024 11:20	0.150	0.004	5	0
PER2 2024	5/13/2024 11:20	5/13/2024 11:30	0.150	0.004	5	0
PER2 2024	5/13/2024 11:30	5/13/2024 11:40	0.150	0.005	5	0
PER2 2024	5/13/2024 11:40	5/13/2024 11:50	0.150	0.005	5	0
PER2 2024	5/13/2024 11:50	5/13/2024 12:00	0.150	0.005	5	0
PER2 2024	5/13/2024 12:00	5/13/2024 12:10	0.150	0.006	5	0
PER2 2024	5/13/2024 12:10	5/13/2024 12:20	0.150	0.006	5	0
PER2 2024	5/13/2024 12:20	5/13/2024 12:30	0.150	0.006	5	0
PER2 2024	5/13/2024 12:30	5/13/2024 12:40	0.150	0.007	5	0
PER2 2024	5/13/2024 12:40	5/13/2024 12:50	0.150	0.007	5	0
PER2 2024	5/13/2024 12:50	5/13/2024 13:00	0.150	0.007	5	0
PER2 2024	5/13/2024 13:00	5/13/2024 13:10	0.150	0.008	5	0
PER2 2024	5/13/2024 13:10	5/13/2024 13:20	0.150	0.008	5	0
PER2 2024	5/13/2024 13:20	5/13/2024 13:30	0.150	0.008	5	0
PER2 2024	5/13/2024 13:30	5/13/2024 13:40	0.150	0.008	5	0
PER2 2024	5/13/2024 13:40	5/13/2024 13:50	0.150	0.009	5	0
PER2 2024	5/13/2024 13:50	5/13/2024 14:00	0.150	0.009	5	0
PER2 2024	5/13/2024 14:00	5/13/2024 14:10	0.150	0.009	5	0
PER2 2024	5/13/2024 14:10	5/13/2024 14:20	0.150	0.009	5	0
PER2 2024	5/13/2024 14:20	5/13/2024 14:30	0.150	0.01	5	0
PER2 2024	5/13/2024 14:30	5/13/2024 14:40	0.150	0.01	5	0
PER2 2024	5/13/2024 14:40	5/13/2024 14:50	0.150	0.01	5	0
PER2 2024	5/13/2024 14:50	5/13/2024 15:00	0.150	0.01	5	0
PER2 2024	5/13/2024 15:00	5/13/2024 15:10	0.150	0.011	5	0
PER2 2024	5/13/2024 15:10	5/13/2024 15:20	0.150	0.011	5	0
PER2 2024	5/13/2024 15:20	5/13/2024 15:30	0.150	0.011	5	0
PER2 2024	5/13/2024 15:30	5/13/2024 15:40	0.150	0.011	5	0
PER2 2024	5/13/2024 15:40	5/13/2024 15:50	0.150	0.012	5	0
PER2 2024	5/13/2024 15:50	5/13/2024 16:00	0.150	0.012	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/13/2024 10:40	5/13/2024 10:50	0.150	0	5	0
PER1 2024	5/13/2024 10:50	5/13/2024 11:00	0.150	0.002	5	0
PER1 2024	5/13/2024 11:00	5/13/2024 11:10	0.150	0.002	5	0
PER1 2024	5/13/2024 11:10	5/13/2024 11:20	0.150	0.003	5	0
PER1 2024	5/13/2024 11:20	5/13/2024 11:30	0.150	0.004	5	0
PER1 2024	5/13/2024 11:30	5/13/2024 11:40	0.150	0.004	5	0
PER1 2024	5/13/2024 11:40	5/13/2024 11:50	0.150	0.005	5	0
PER1 2024	5/13/2024 11:50	5/13/2024 12:00	0.150	0.005	5	0
PER1 2024	5/13/2024 12:00	5/13/2024 12:10	0.150	0.006	5	0
PER1 2024	5/13/2024 12:10	5/13/2024 12:20	0.150	0.006	5	0
PER1 2024	5/13/2024 12:20	5/13/2024 12:30	0.150	0.006	5	0
PER1 2024	5/13/2024 12:30	5/13/2024 12:40	0.150	0.007	5	0
PER1 2024	5/13/2024 12:40	5/13/2024 12:50	0.150	0.007	5	0
PER1 2024	5/13/2024 12:50	5/13/2024 13:00	0.150	0.007	5	0
PER1 2024	5/13/2024 13:00	5/13/2024 13:10	0.150	0.008	5	0
PER1 2024	5/13/2024 13:10	5/13/2024 13:20	0.150	0.008	5	0
PER1 2024	5/13/2024 13:20	5/13/2024 13:30	0.150	0.008	5	0
PER1 2024	5/13/2024 13:30	5/13/2024 13:40	0.150	0.009	5	0
PER1 2024	5/13/2024 13:40	5/13/2024 13:50	0.150	0.009	5	0
PER1 2024	5/13/2024 13:50	5/13/2024 14:00	0.150	0.009	5	0
PER1 2024	5/13/2024 14:00	5/13/2024 14:10	0.150	0.009	5	0
PER1 2024	5/13/2024 14:10	5/13/2024 14:20	0.150	0.01	5	0
PER1 2024	5/13/2024 14:20	5/13/2024 14:30	0.150	0.01	5	0
PER1 2024	5/13/2024 14:30	5/13/2024 14:40	0.150	0.01	5	0
PER1 2024	5/13/2024 14:40	5/13/2024 14:50	0.150	0.01	5	0
PER1 2024	5/13/2024 14:50	5/13/2024 15:00	0.150	0.011	5	0
PER1 2024	5/13/2024 15:00	5/13/2024 15:10	0.150	0.011	5	0
PER1 2024	5/13/2024 15:10	5/13/2024 15:20	0.150	0.011	5	0
PER1 2024	5/13/2024 15:20	5/13/2024 15:30	0.150	0.012	5	0
PER1 2024	5/13/2024 15:30	5/13/2024 15:40	0.150	0.012	5	0
PER1 2024	5/13/2024 15:40	5/13/2024 15:50	0.150	0.012	5	0
PER1 2024	5/13/2024 15:50	5/13/2024 16:00	0.150	0.012	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/14/2024 Weather: 60 deg. F, Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA

Work Activities Performed: 1) Alba continued minor excavation, rebar and waterproofing installation for the foundation development.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None
--

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.
--

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8645	1520	4140

Site Layout Map and Excavation Figures

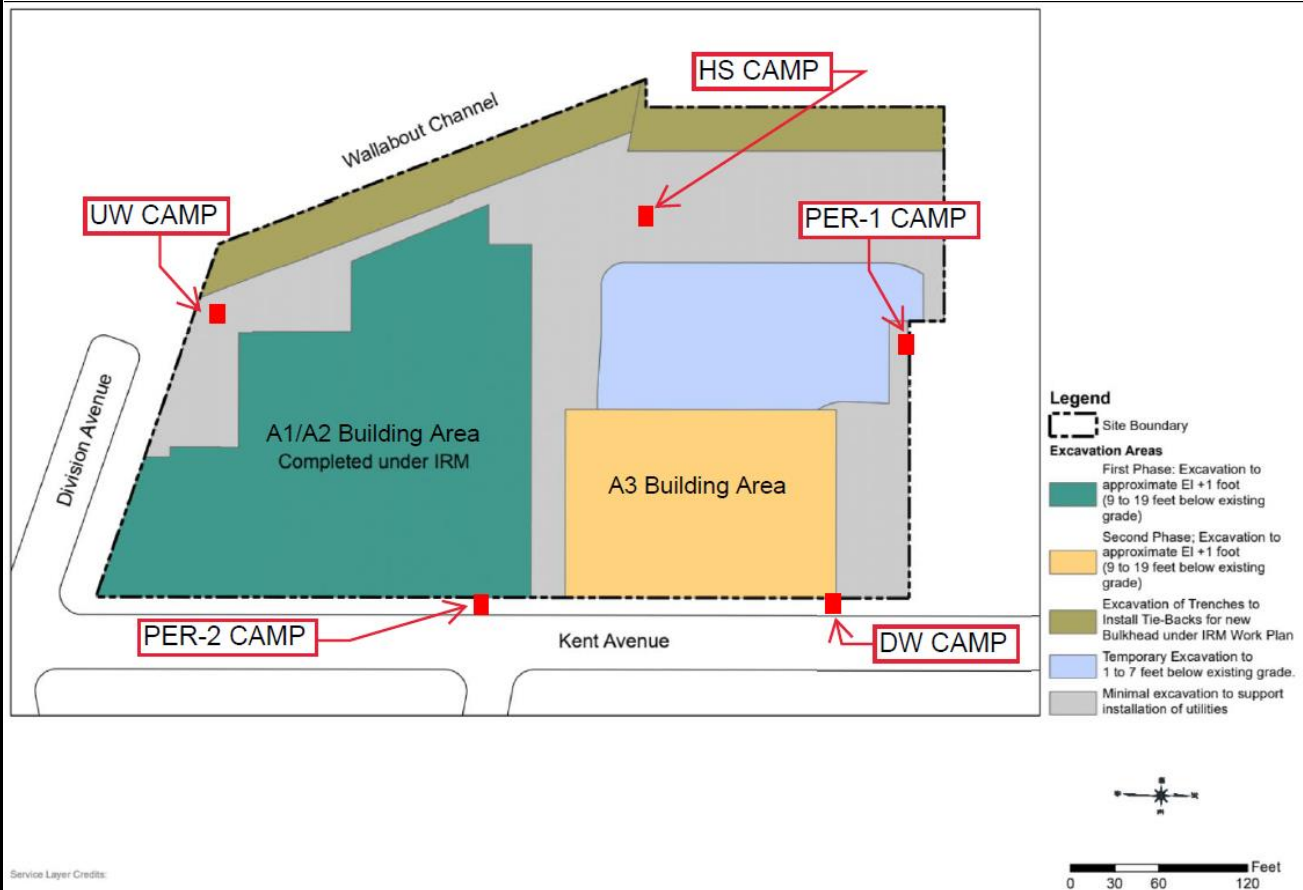

Service Layer Credits:

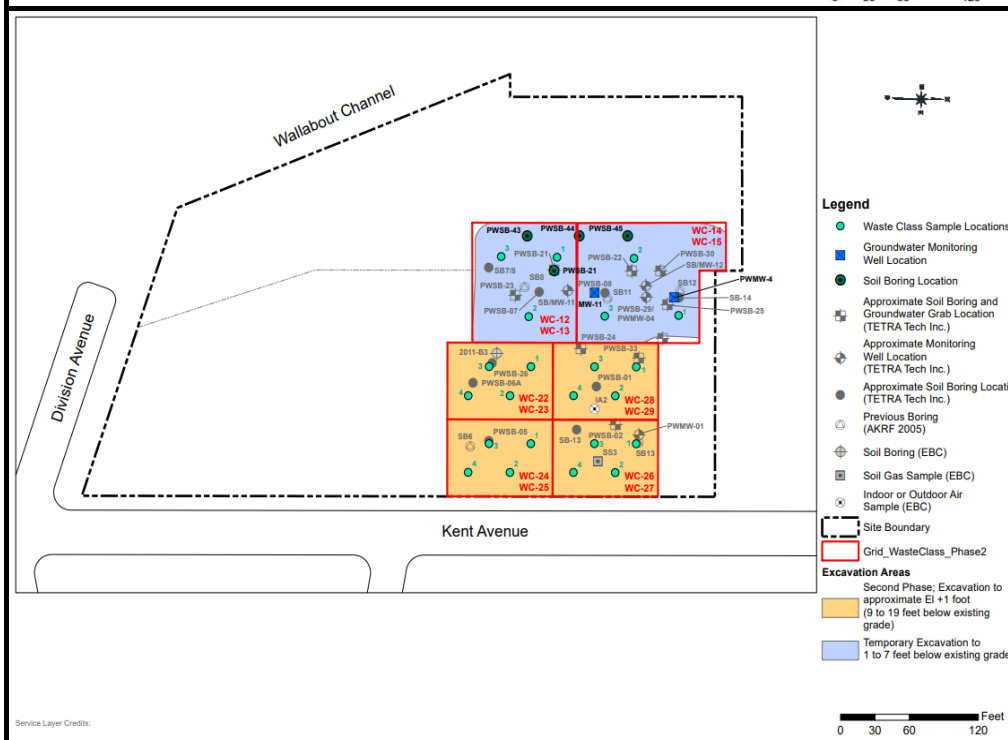
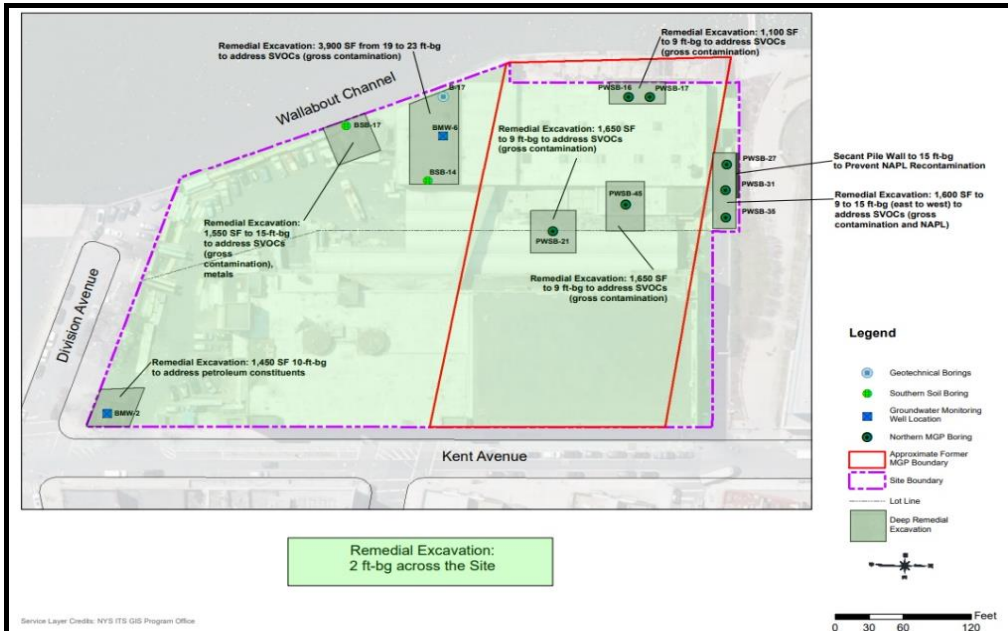


Photo 1:
View of Site conditions
facing northwest.

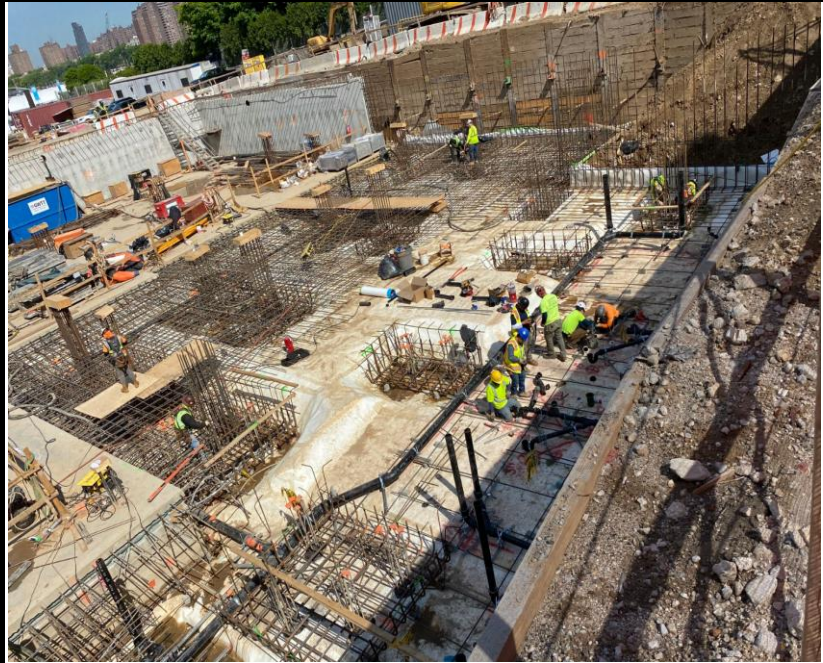


Photo 2:
View of Site conditions
and foundation
development facing
south.



Photo 3:
View of rebar
installation facing
northeast.




Photo 4:
View of site
conditions and
continued A1/A2
building
construction.



CAMP:
Downwind
Particulates

Dust Levels


0.014 mg/m³ 0.013 mg/m³

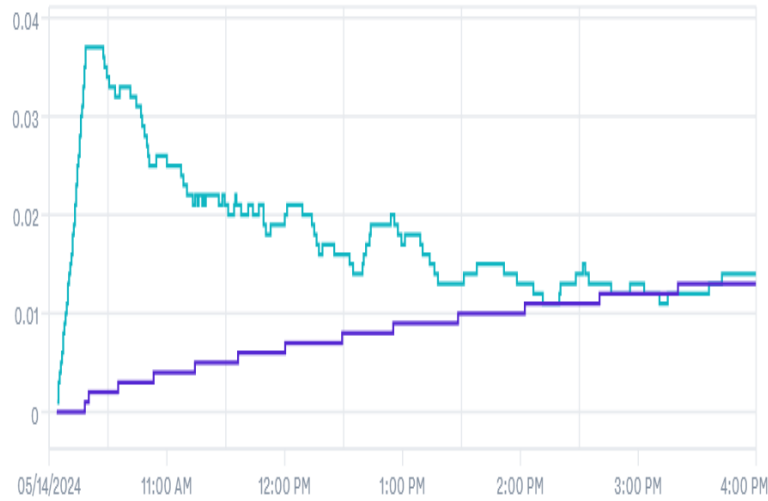

CAMP:
Downwind VOCs


VOC Levels

0 ppm 0 ppm

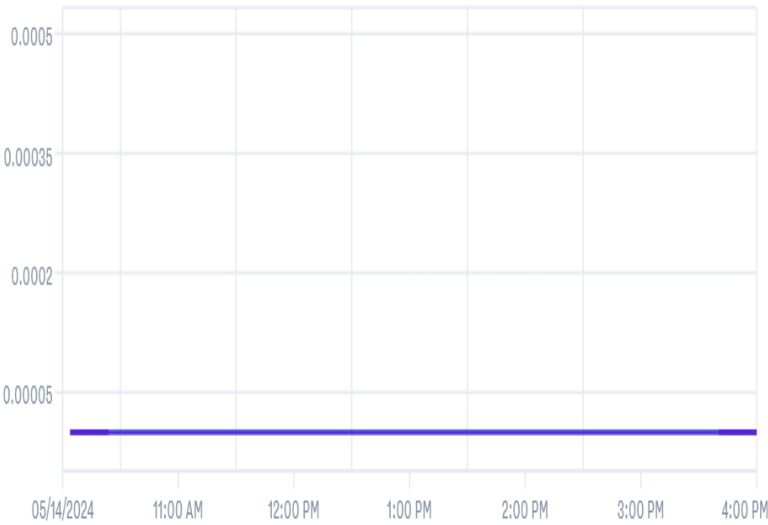


CAMP:
Upwind Particulates

Dust Levels

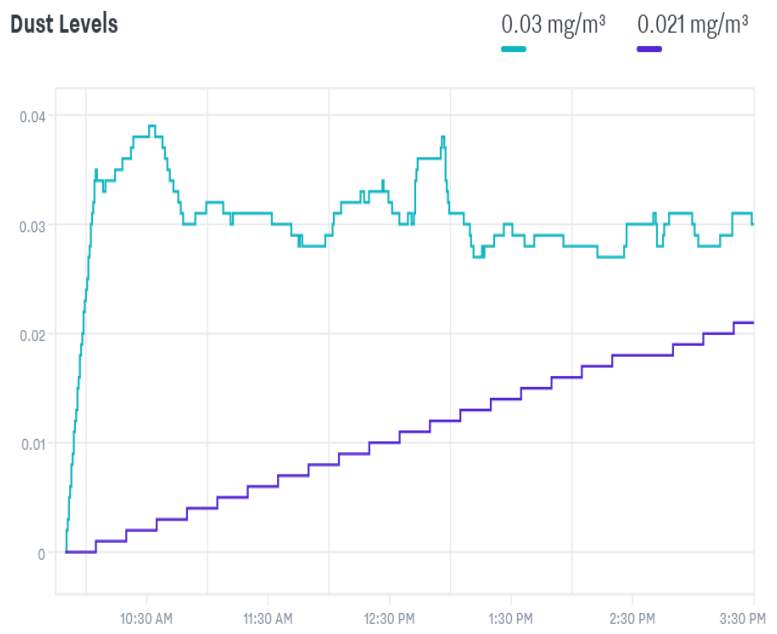

CAMP:
Upwind VOCs

VOC Levels

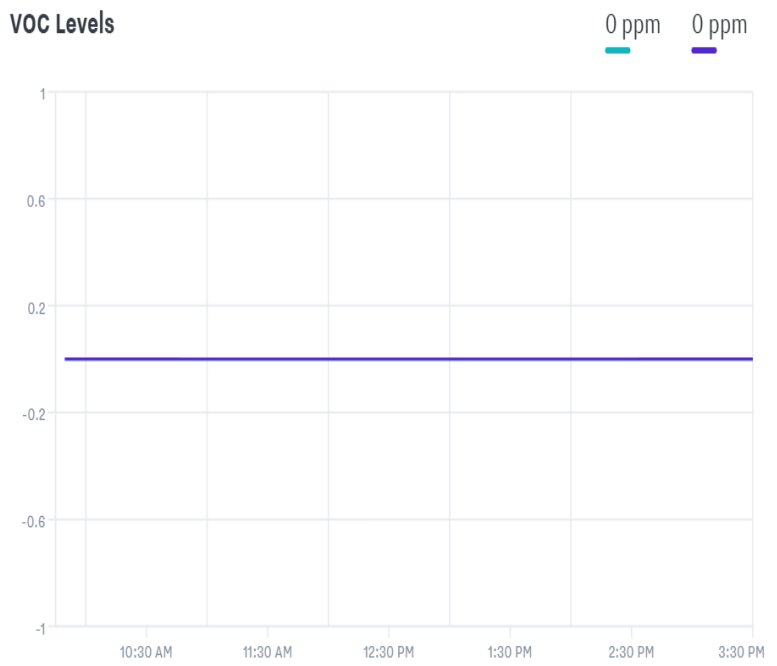

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/14/2024 10:00	5/14/2024 10:10	0.150	0	5	0
DW 2024	5/14/2024 10:10	5/14/2024 10:20	0.150	0.001	5	0
DW 2024	5/14/2024 10:20	5/14/2024 10:30	0.150	0.002	5	0
DW 2024	5/14/2024 10:30	5/14/2024 10:40	0.150	0.003	5	0
DW 2024	5/14/2024 10:40	5/14/2024 10:50	0.150	0.003	5	0
DW 2024	5/14/2024 10:50	5/14/2024 11:00	0.150	0.004	5	0
DW 2024	5/14/2024 11:00	5/14/2024 11:10	0.150	0.004	5	0
DW 2024	5/14/2024 11:10	5/14/2024 11:20	0.150	0.005	5	0
DW 2024	5/14/2024 11:20	5/14/2024 11:30	0.150	0.005	5	0
DW 2024	5/14/2024 11:30	5/14/2024 11:40	0.150	0.006	5	0
DW 2024	5/14/2024 11:40	5/14/2024 11:50	0.150	0.006	5	0
DW 2024	5/14/2024 11:50	5/14/2024 12:00	0.150	0.006	5	0
DW 2024	5/14/2024 12:00	5/14/2024 12:10	0.150	0.007	5	0
DW 2024	5/14/2024 12:10	5/14/2024 12:20	0.150	0.007	5	0
DW 2024	5/14/2024 12:20	5/14/2024 12:30	0.150	0.008	5	0
DW 2024	5/14/2024 12:30	5/14/2024 12:40	0.150	0.008	5	0
DW 2024	5/14/2024 12:40	5/14/2024 12:50	0.150	0.008	5	0
DW 2024	5/14/2024 12:50	5/14/2024 13:00	0.150	0.009	5	0
DW 2024	5/14/2024 13:00	5/14/2024 13:10	0.150	0.009	5	0
DW 2024	5/14/2024 13:10	5/14/2024 13:20	0.150	0.009	5	0
DW 2024	5/14/2024 13:20	5/14/2024 13:30	0.150	0.01	5	0
DW 2024	5/14/2024 13:30	5/14/2024 13:40	0.150	0.01	5	0
DW 2024	5/14/2024 13:40	5/14/2024 13:50	0.150	0.01	5	0
DW 2024	5/14/2024 13:50	5/14/2024 14:00	0.150	0.01	5	0
DW 2024	5/14/2024 14:00	5/14/2024 14:10	0.150	0.011	5	0
DW 2024	5/14/2024 14:10	5/14/2024 14:20	0.150	0.011	5	0
DW 2024	5/14/2024 14:20	5/14/2024 14:30	0.150	0.011	5	0
DW 2024	5/14/2024 14:30	5/14/2024 14:40	0.150	0.011	5	0
DW 2024	5/14/2024 14:40	5/14/2024 14:50	0.150	0.012	5	0
DW 2024	5/14/2024 14:50	5/14/2024 15:00	0.150	0.012	5	0
DW 2024	5/14/2024 15:00	5/14/2024 15:10	0.150	0.012	5	0
DW 2024	5/14/2024 15:10	5/14/2024 15:20	0.150	0.012	5	0
DW 2024	5/14/2024 15:20	5/14/2024 15:30	0.150	0.013	5	0
DW 2024	5/14/2024 15:30	5/14/2024 15:40	0.150	0.013	5	0
DW 2024	5/14/2024 15:40	5/14/2024 15:50	0.150	0.013	5	0
DW 2024	5/14/2024 15:50	5/14/2024 16:00	0.150	0.013	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/14/2024 9:00	5/14/2024 9:10	0.150	0	5	0
UW 2024	5/14/2024 9:10	5/14/2024 9:20	0.150	0	5	0
UW 2024	5/14/2024 9:20	5/14/2024 9:30	0.150	0	5	0
UW 2024	5/14/2024 9:30	5/14/2024 9:40	0.150	0	5	0
UW 2024	5/14/2024 9:40	5/14/2024 9:50	0.150	0	5	0
UW 2024	5/14/2024 9:50	5/14/2024 10:00	0.150	0	5	0
UW 2024	5/14/2024 10:00	5/14/2024 10:10	0.150	0.001	5	0
UW 2024	5/14/2024 10:10	5/14/2024 10:20	0.150	0.002	5	0
UW 2024	5/14/2024 10:20	5/14/2024 10:30	0.150	0.002	5	0
UW 2024	5/14/2024 10:30	5/14/2024 10:40	0.150	0.003	5	0
UW 2024	5/14/2024 10:40	5/14/2024 10:50	0.150	0.004	5	0
UW 2024	5/14/2024 10:50	5/14/2024 11:00	0.150	0.004	5	0
UW 2024	5/14/2024 11:00	5/14/2024 11:10	0.150	0.005	5	0
UW 2024	5/14/2024 11:10	5/14/2024 11:20	0.150	0.006	5	0
UW 2024	5/14/2024 11:20	5/14/2024 11:30	0.150	0.006	5	0
UW 2024	5/14/2024 11:30	5/14/2024 11:40	0.150	0.007	5	0
UW 2024	5/14/2024 11:40	5/14/2024 11:50	0.150	0.008	5	0
UW 2024	5/14/2024 11:50	5/14/2024 12:00	0.150	0.008	5	0
UW 2024	5/14/2024 12:00	5/14/2024 12:10	0.150	0.009	5	0
UW 2024	5/14/2024 12:10	5/14/2024 12:20	0.150	0.01	5	0
UW 2024	5/14/2024 12:20	5/14/2024 12:30	0.150	0.01	5	0
UW 2024	5/14/2024 12:30	5/14/2024 12:40	0.150	0.011	5	0
UW 2024	5/14/2024 12:40	5/14/2024 12:50	0.150	0.012	5	0
UW 2024	5/14/2024 12:50	5/14/2024 13:00	0.150	0.012	5	0
UW 2024	5/14/2024 13:00	5/14/2024 13:10	0.150	0.013	5	0
UW 2024	5/14/2024 13:10	5/14/2024 13:20	0.150	0.014	5	0
UW 2024	5/14/2024 13:20	5/14/2024 13:30	0.150	0.014	5	0
UW 2024	5/14/2024 13:30	5/14/2024 13:40	0.150	0.015	5	0
UW 2024	5/14/2024 13:40	5/14/2024 13:50	0.150	0.016	5	0
UW 2024	5/14/2024 13:50	5/14/2024 14:00	0.150	0.016	5	0
UW 2024	5/14/2024 14:00	5/14/2024 14:10	0.150	0.017	5	0
UW 2024	5/14/2024 14:10	5/14/2024 14:20	0.150	0.018	5	0
UW 2024	5/14/2024 14:20	5/14/2024 14:30	0.150	0.018	5	0
UW 2024	5/14/2024 14:30	5/14/2024 14:40	0.150	0.018	5	0
UW 2024	5/14/2024 14:40	5/14/2024 14:50	0.150	0.019	5	0
UW 2024	5/14/2024 14:50	5/14/2024 15:00	0.150	0.019	5	0
UW 2024	5/14/2024 15:00	5/14/2024 15:10	0.150	0.02	5	0
UW 2024	5/14/2024 15:10	5/14/2024 15:20	0.150	0.021	5	0
UW 2024	5/14/2024 15:20	5/14/2024 15:30	0.150	0.021	5	0
UW 2024	5/14/2024 15:30	5/14/2024 15:40	0.150	0.022	5	0
UW 2024	5/14/2024 15:40	5/14/2024 15:50	0.150	0.022	5	0
UW 2024	5/14/2024 15:50	5/14/2024 16:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/14/2024 9:50	5/14/2024 10:00	0.150	0	5	0
HS South	5/14/2024 10:00	5/14/2024 10:10	0.150	0	5	0
HS South	5/14/2024 10:10	5/14/2024 10:20	0.150	0.002	5	0
HS South	5/14/2024 10:20	5/14/2024 10:30	0.150	0.003	5	0
HS South	5/14/2024 10:30	5/14/2024 10:40	0.150	0.004	5	0
HS South	5/14/2024 10:40	5/14/2024 10:50	0.150	0.005	5	0
HS South	5/14/2024 10:50	5/14/2024 11:00	0.150	0.006	5	0
HS South	5/14/2024 11:00	5/14/2024 11:10	0.150	0.007	5	0
HS South	5/14/2024 11:10	5/14/2024 11:20	0.150	0.008	5	0
HS South	5/14/2024 11:20	5/14/2024 11:30	0.150	0.009	5	0
HS South	5/14/2024 11:30	5/14/2024 11:40	0.150	0.01	5	0
HS South	5/14/2024 11:40	5/14/2024 11:50	0.150	0.011	5	0
HS South	5/14/2024 11:50	5/14/2024 12:00	0.150	0.012	5	0
HS South	5/14/2024 12:00	5/14/2024 12:10	0.150	0.013	5	0
HS South	5/14/2024 12:10	5/14/2024 12:20	0.150	0.014	5	0
HS South	5/14/2024 12:20	5/14/2024 12:30	0.150	0.015	5	0
HS South	5/14/2024 12:30	5/14/2024 12:40	0.150	0.016	5	0
HS South	5/14/2024 12:40	5/14/2024 12:50	0.150	0.017	5	0
HS South	5/14/2024 12:50	5/14/2024 13:00	0.150	0.018	5	0
HS South	5/14/2024 13:00	5/14/2024 13:10	0.150	0.019	5	0
HS South	5/14/2024 13:10	5/14/2024 13:20	0.150	0.019	5	0
HS South	5/14/2024 13:20	5/14/2024 13:30	0.150	0.02	5	0
HS South	5/14/2024 13:30	5/14/2024 13:40	0.150	0.021	5	0
HS South	5/14/2024 13:40	5/14/2024 13:50	0.150	0.022	5	0
HS South	5/14/2024 13:50	5/14/2024 14:00	0.150	0.023	5	0
HS South	5/14/2024 14:00	5/14/2024 14:10	0.150	0.025	5	0
HS South	5/14/2024 14:10	5/14/2024 14:20	0.150	0.026	5	0
HS South	5/14/2024 14:20	5/14/2024 14:30	0.150	0.027	5	0
HS South	5/14/2024 14:30	5/14/2024 14:40	0.150	0.028	5	0
HS South	5/14/2024 14:40	5/14/2024 14:50	0.150	0.029	5	0
HS South	5/14/2024 14:50	5/14/2024 15:00	0.150	0.03	5	0
HS South	5/14/2024 15:00	5/14/2024 15:10	0.150	0.031	5	0
HS South	5/14/2024 15:10	5/14/2024 15:20	0.150	0.032	5	0
HS South	5/14/2024 15:20	5/14/2024 15:30	0.150	0.033	5	0
HS South	5/14/2024 15:30	5/14/2024 15:40	0.150	0.033	5	0
HS South	5/14/2024 15:40	5/14/2024 15:50	0.150	0.033	5	0
HS South	5/14/2024 15:50	5/14/2024 16:00	0.150	0.033	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/14/2024 9:00	5/14/2024 9:10	0.150	0.012	5	0
PER2 2024	5/14/2024 9:10	5/14/2024 9:20	0.150	0.012	5	0
PER2 2024	5/14/2024 9:20	5/14/2024 9:30	0.150	0.012	5	0
PER2 2024	5/14/2024 9:30	5/14/2024 9:40	0.150	0.012	5	0
PER2 2024	5/14/2024 9:40	5/14/2024 9:50	0.150	0.012	5	0
PER2 2024	5/14/2024 9:50	5/14/2024 10:00	0.150	0.012	5	0
PER2 2024	5/14/2024 10:00	5/14/2024 10:10	0.150	0.012	5	0
PER2 2024	5/14/2024 10:10	5/14/2024 10:20	0.150	0.012	5	0
PER2 2024	5/14/2024 10:20	5/14/2024 10:30	0.150	0.012	5	0
PER2 2024	5/14/2024 10:30	5/14/2024 10:40	0.150	0.012	5	0
PER2 2024	5/14/2024 10:40	5/14/2024 10:50	0.150	0.012	5	0
PER2 2024	5/14/2024 10:50	5/14/2024 11:00	0.150	0.012	5	0
PER2 2024	5/14/2024 11:00	5/14/2024 11:10	0.150	0.012	5	0
PER2 2024	5/14/2024 11:10	5/14/2024 11:20	0.150	0.012	5	0
PER2 2024	5/14/2024 11:20	5/14/2024 11:30	0.150	0.012	5	0
PER2 2024	5/14/2024 11:30	5/14/2024 11:40	0.150	0	5	0
PER2 2024	5/14/2024 11:40	5/14/2024 11:50	0.150	0.001	5	0
PER2 2024	5/14/2024 11:50	5/14/2024 12:00	0.150	0.001	5	0
PER2 2024	5/14/2024 12:00	5/14/2024 12:10	0.150	0.001	5	0
PER2 2024	5/14/2024 12:10	5/14/2024 12:20	0.150	0.002	5	0
PER2 2024	5/14/2024 12:20	5/14/2024 12:30	0.150	0.002	5	0
PER2 2024	5/14/2024 12:30	5/14/2024 12:40	0.150	0.002	5	0
PER2 2024	5/14/2024 12:40	5/14/2024 12:50	0.150	0.003	5	0
PER2 2024	5/14/2024 12:50	5/14/2024 13:00	0.150	0.003	5	0
PER2 2024	5/14/2024 13:00	5/14/2024 13:10	0.150	0.004	5	0
PER2 2024	5/14/2024 13:10	5/14/2024 13:20	0.150	0.004	5	0
PER2 2024	5/14/2024 13:20	5/14/2024 13:30	0.150	0.004	5	0
PER2 2024	5/14/2024 13:30	5/14/2024 13:40	0.150	0.004	5	0
PER2 2024	5/14/2024 13:40	5/14/2024 13:50	0.150	0.005	5	0
PER2 2024	5/14/2024 13:50	5/14/2024 14:00	0.150	0.005	5	0
PER2 2024	5/14/2024 14:00	5/14/2024 14:10	0.150	0.005	5	0
PER2 2024	5/14/2024 14:10	5/14/2024 14:20	0.150	0.005	5	0
PER2 2024	5/14/2024 14:20	5/14/2024 14:30	0.150	0.006	5	0
PER2 2024	5/14/2024 14:30	5/14/2024 14:40	0.150	0.006	5	0
PER2 2024	5/14/2024 14:40	5/14/2024 14:50	0.150	0.006	5	0
PER2 2024	5/14/2024 14:50	5/14/2024 15:00	0.150	0.006	5	0
PER2 2024	5/14/2024 15:00	5/14/2024 15:10	0.150	0.007	5	0
PER2 2024	5/14/2024 15:10	5/14/2024 15:20	0.150	0.007	5	0
PER2 2024	5/14/2024 15:20	5/14/2024 15:30	0.150	0.007	5	0
PER2 2024	5/14/2024 15:30	5/14/2024 15:40	0.150	0.007	5	0
PER2 2024	5/14/2024 15:40	5/14/2024 15:50	0.150	0.007	5	0
PER2 2024	5/14/2024 15:50	5/14/2024 16:00	0.150	0.007	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/14/2024 9:00	5/14/2024 9:10	0.150	0	5	0
PER1 2024	5/14/2024 9:10	5/14/2024 9:20	0.150	0	5	0
PER1 2024	5/14/2024 9:20	5/14/2024 9:30	0.150	0	5	0
PER1 2024	5/14/2024 9:30	5/14/2024 9:40	0.150	0	5	0
PER1 2024	5/14/2024 9:40	5/14/2024 9:50	0.150	0	5	0
PER1 2024	5/14/2024 9:50	5/14/2024 10:00	0.150	0.001	5	0
PER1 2024	5/14/2024 10:00	5/14/2024 10:10	0.150	0.001	5	0
PER1 2024	5/14/2024 10:10	5/14/2024 10:20	0.150	0.002	5	0
PER1 2024	5/14/2024 10:20	5/14/2024 10:30	0.150	0.002	5	0
PER1 2024	5/14/2024 10:30	5/14/2024 10:40	0.150	0.002	5	0
PER1 2024	5/14/2024 10:40	5/14/2024 10:50	0.150	0.003	5	0
PER1 2024	5/14/2024 10:50	5/14/2024 11:00	0.150	0.003	5	0
PER1 2024	5/14/2024 11:00	5/14/2024 11:10	0.150	0.004	5	0
PER1 2024	5/14/2024 11:10	5/14/2024 11:20	0.150	0.004	5	0
PER1 2024	5/14/2024 11:20	5/14/2024 11:30	0.150	0.004	5	0
PER1 2024	5/14/2024 11:30	5/14/2024 11:40	0.150	0.005	5	0
PER1 2024	5/14/2024 11:40	5/14/2024 11:50	0.150	0.005	5	0
PER1 2024	5/14/2024 11:50	5/14/2024 12:00	0.150	0.005	5	0
PER1 2024	5/14/2024 12:00	5/14/2024 12:10	0.150	0.005	5	0
PER1 2024	5/14/2024 12:10	5/14/2024 12:20	0.150	0.006	5	0
PER1 2024	5/14/2024 12:20	5/14/2024 12:30	0.150	0.006	5	0
PER1 2024	5/14/2024 12:30	5/14/2024 12:40	0.150	0.006	5	0
PER1 2024	5/14/2024 12:40	5/14/2024 12:50	0.150	0.006	5	0
PER1 2024	5/14/2024 12:50	5/14/2024 13:00	0.150	0.007	5	0
PER1 2024	5/14/2024 13:00	5/14/2024 13:10	0.150	0.007	5	0
PER1 2024	5/14/2024 13:10	5/14/2024 13:20	0.150	0.007	5	0
PER1 2024	5/14/2024 13:20	5/14/2024 13:30	0.150	0.008	5	0
PER1 2024	5/14/2024 13:30	5/14/2024 13:40	0.150	0.008	5	0
PER1 2024	5/14/2024 13:40	5/14/2024 13:50	0.150	0.008	5	0
PER1 2024	5/14/2024 13:50	5/14/2024 14:00	0.150	0.008	5	0
PER1 2024	5/14/2024 14:00	5/14/2024 14:10	0.150	0.009	5	0
PER1 2024	5/14/2024 14:10	5/14/2024 14:20	0.150	0.009	5	0
PER1 2024	5/14/2024 14:20	5/14/2024 14:30	0.150	0.009	5	0
PER1 2024	5/14/2024 14:30	5/14/2024 14:40	0.150	0.009	5	0
PER1 2024	5/14/2024 14:40	5/14/2024 14:50	0.150	0.01	5	0
PER1 2024	5/14/2024 14:50	5/14/2024 15:00	0.150	0.01	5	0
PER1 2024	5/14/2024 15:00	5/14/2024 15:10	0.150	0.01	5	0
PER1 2024	5/14/2024 15:10	5/14/2024 15:20	0.150	0.01	5	0
PER1 2024	5/14/2024 15:20	5/14/2024 15:30	0.150	0.011	5	0
PER1 2024	5/14/2024 15:30	5/14/2024 15:40	0.150	0.011	5	0
PER1 2024	5/14/2024 15:40	5/14/2024 15:50	0.150	0	5	0
PER1 2024	5/14/2024 15:50	5/14/2024 16:00	0.150	0	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/15/2024 Weather: 55 deg. F, Rain

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA

Work Activities Performed: 1) Alba continued minor excavation, rebar and waterproofing installation for the foundation development. 2) Complete additional excavation and collect EP-84-W_20240515 3) Alba exports 2 loads (~40 CY) of material from WC-27 for off-site disposal at the MSM facility.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): EP-84-W_20240515
--

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.
--

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	40	0	0
Total:(CY)	4485	0	8685	1520	4140

Site Layout Map and Excavation Figures

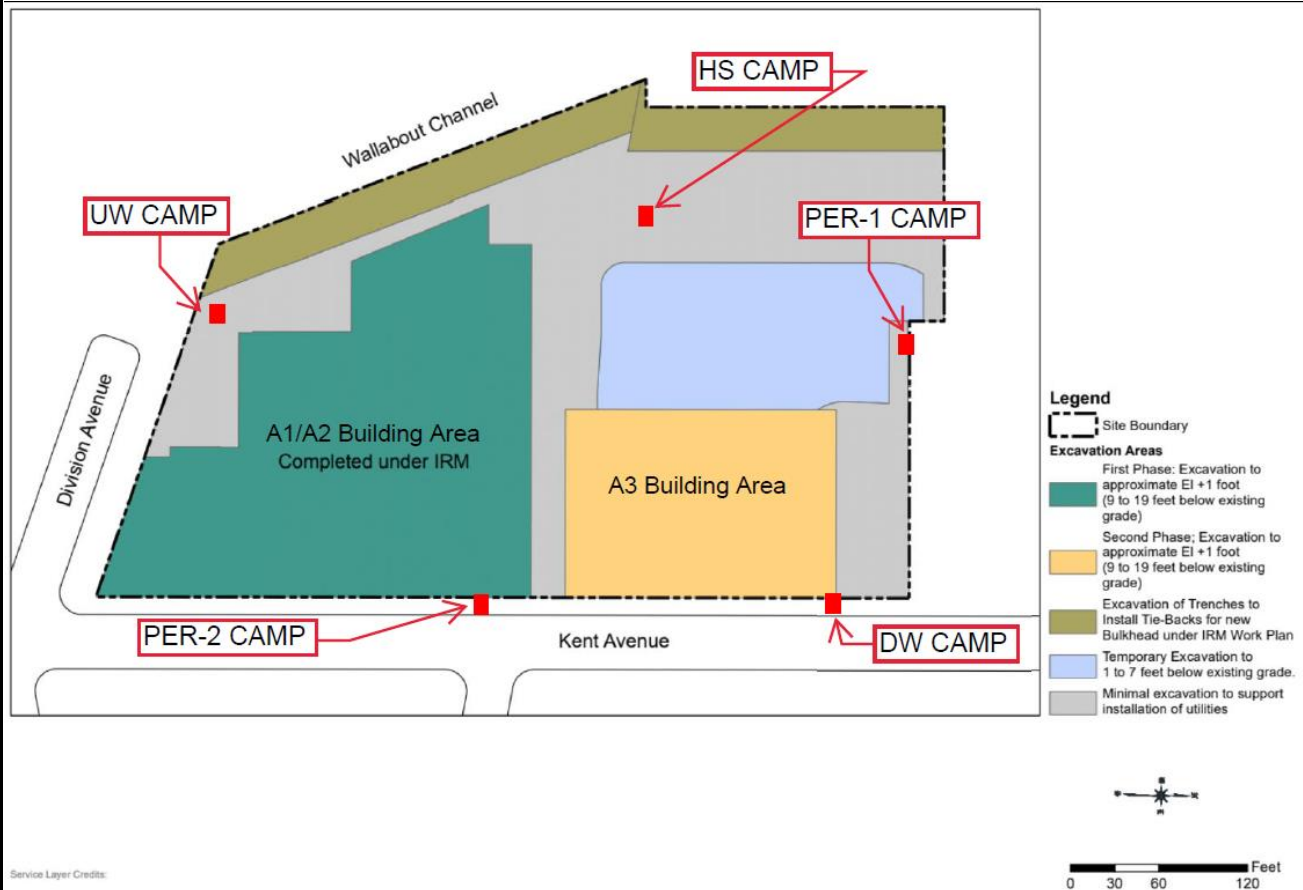

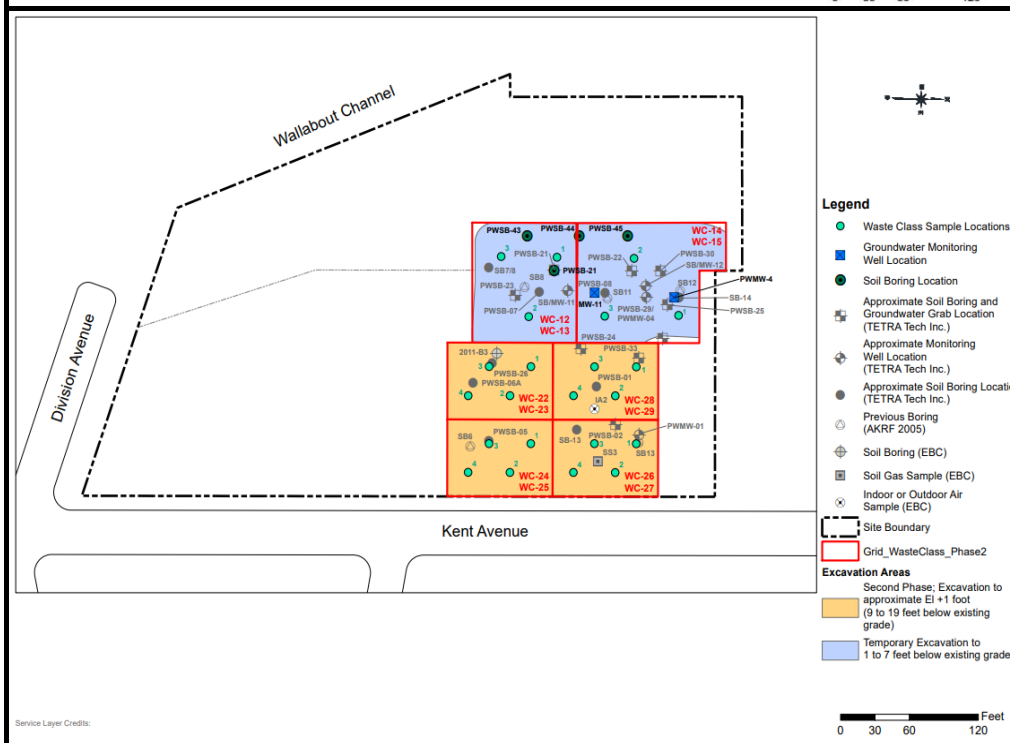
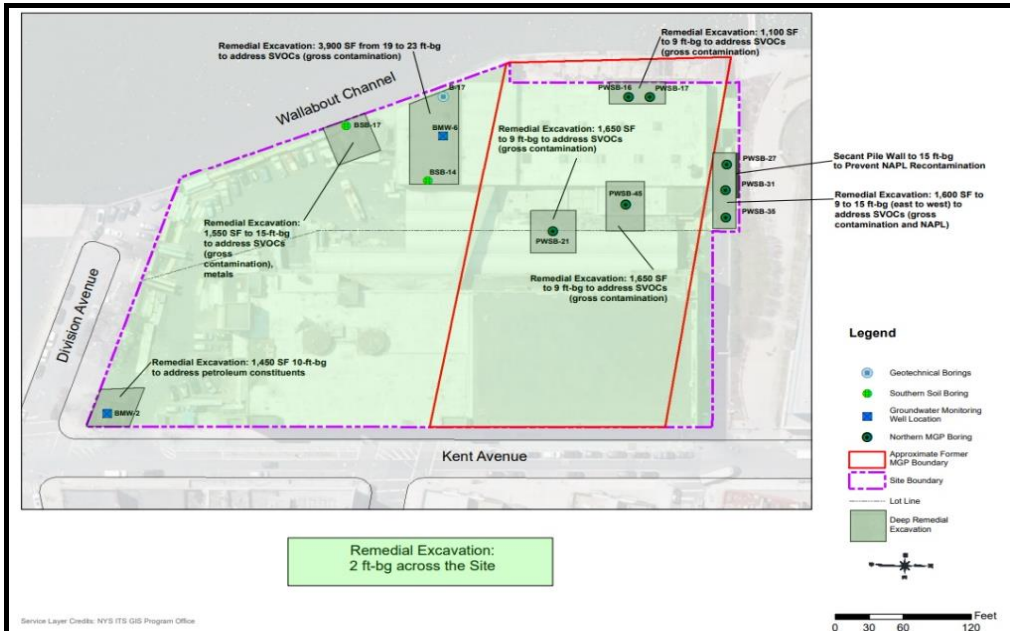


Photo 1:
View of Site conditions
facing northeast.

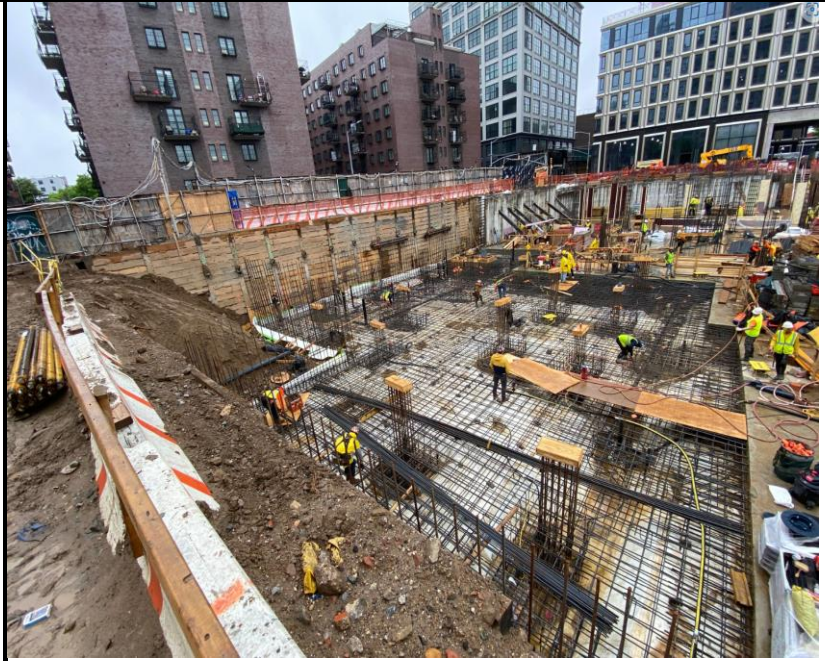


Photo 2:
View of Site conditions
and foundation
development facing
south.



Photo 3:
View of rebar
installation facing
southwest.

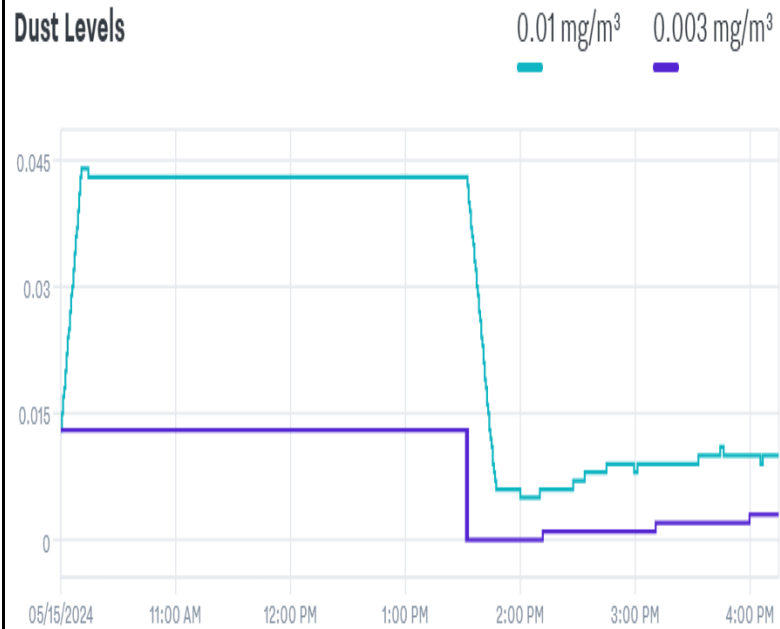


Photo 4:
View of rebar and
waterproofing
installation.




CAMP:
Downwind
Particulates

Dust Levels



CAMP:
Downwind VOCs


VOC Levels

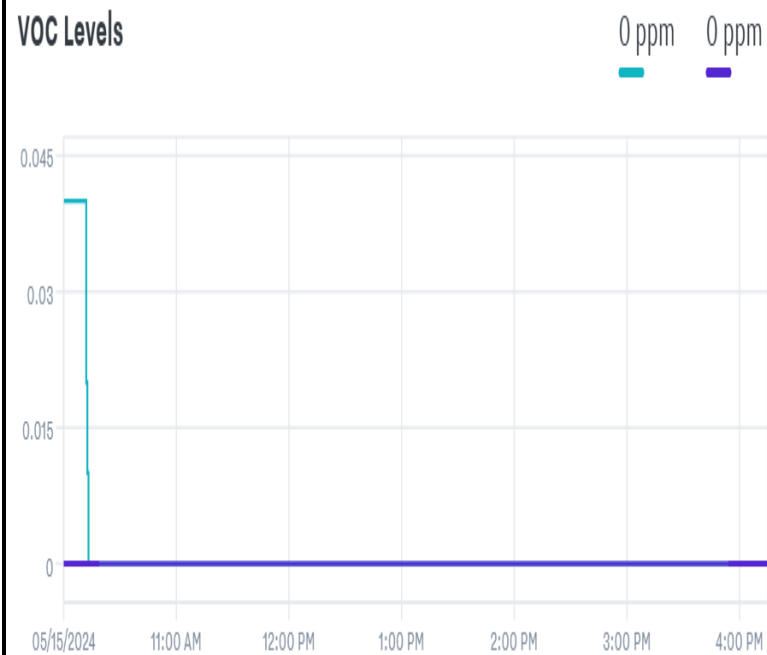

CAMP:
Upwind Particulates

Dust Levels


0.027 mg/m³ 0.024 mg/m³

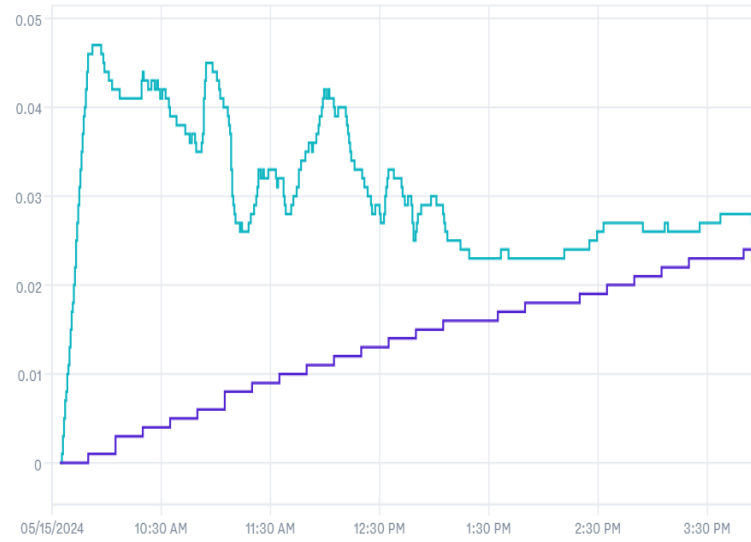

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

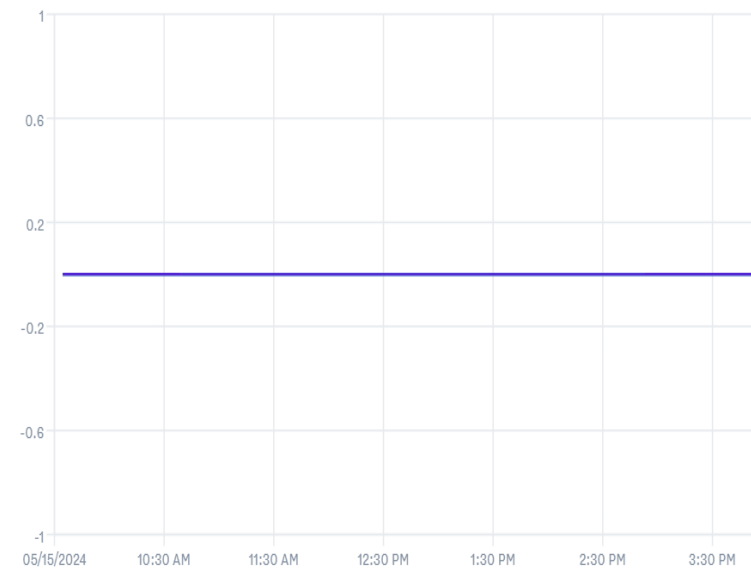

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/15/2024 8:00	5/15/2024 8:10	0.150	0.013	5	0
DW 2024	5/15/2024 8:10	5/15/2024 8:20	0.150	0.013	5	0
DW 2024	5/15/2024 8:20	5/15/2024 8:30	0.150	0.013	5	0
DW 2024	5/15/2024 8:30	5/15/2024 8:40	0.150	0.013	5	0
DW 2024	5/15/2024 8:40	5/15/2024 8:50	0.150	0.013	5	0
DW 2024	5/15/2024 8:50	5/15/2024 9:00	0.150	0.013	5	0
DW 2024	5/15/2024 9:00	5/15/2024 9:10	0.150	0.013	5	0
DW 2024	5/15/2024 9:10	5/15/2024 9:20	0.150	0.013	5	0
DW 2024	5/15/2024 9:20	5/15/2024 9:30	0.150	0.013	5	0
DW 2024	5/15/2024 9:30	5/15/2024 9:40	0.150	0.013	5	0
DW 2024	5/15/2024 9:40	5/15/2024 9:50	0.150	0.013	5	0
DW 2024	5/15/2024 9:50	5/15/2024 10:00	0.150	0.013	5	0.003
DW 2024	5/15/2024 10:00	5/15/2024 10:10	0.150	0.013	5	0.003
DW 2024	5/15/2024 10:10	5/15/2024 10:20	0.150	0.013	5	0.003
DW 2024	5/15/2024 10:20	5/15/2024 10:30	0.150	0.013	5	0.003
DW 2024	5/15/2024 10:30	5/15/2024 10:40	0.150	0.013	5	0.003
DW 2024	5/15/2024 10:40	5/15/2024 10:50	0.150	0.013	5	0.003
DW 2024	5/15/2024 10:50	5/15/2024 11:00	0.150	0.013	5	0.003
DW 2024	5/15/2024 11:00	5/15/2024 11:10	0.150	0.013	5	0.003
DW 2024	5/15/2024 11:10	5/15/2024 11:20	0.150	0.013	5	0.003
DW 2024	5/15/2024 11:20	5/15/2024 11:30	0.150	0.013	5	0.003
DW 2024	5/15/2024 11:30	5/15/2024 11:40	0.150	0.013	5	0.003
DW 2024	5/15/2024 11:40	5/15/2024 11:50	0.150	0.013	5	0.003
DW 2024	5/15/2024 11:50	5/15/2024 12:00	0.150	0.013	5	0.003
DW 2024	5/15/2024 12:00	5/15/2024 12:10	0.150	0.013	5	0.003
DW 2024	5/15/2024 12:10	5/15/2024 12:20	0.150	0.013	5	0.003
DW 2024	5/15/2024 12:20	5/15/2024 12:30	0.150	0.013	5	0.003
DW 2024	5/15/2024 12:30	5/15/2024 12:40	0.150	0.013	5	0.003
DW 2024	5/15/2024 12:40	5/15/2024 12:50	0.150	0.013	5	0.003
DW 2024	5/15/2024 12:50	5/15/2024 13:00	0.150	0.013	5	0.003
DW 2024	5/15/2024 13:00	5/15/2024 13:10	0.150	0.013	5	0.003
DW 2024	5/15/2024 13:10	5/15/2024 13:20	0.150	0.013	5	0.003
DW 2024	5/15/2024 13:20	5/15/2024 13:30	0.150	0.013	5	0.003
DW 2024	5/15/2024 13:30	5/15/2024 13:40	0.150	0.013	5	0.003
DW 2024	5/15/2024 13:40	5/15/2024 13:50	0.150	0	5	0.003
DW 2024	5/15/2024 13:50	5/15/2024 14:00	0.150	0	5	0.003
DW 2024	5/15/2024 14:00	5/15/2024 14:10	0.150	0	5	0.003
DW 2024	5/15/2024 14:10	5/15/2024 14:20	0.150	0.001	5	0.003
DW 2024	5/15/2024 14:20	5/15/2024 14:30	0.150	0.001	5	0.003
DW 2024	5/15/2024 14:30	5/15/2024 14:40	0.150	0.001	5	0.003
DW 2024	5/15/2024 14:40	5/15/2024 14:50	0.150	0.001	5	0.003
DW 2024	5/15/2024 14:50	5/15/2024 15:00	0.150	0.001	5	0.003
DW 2024	5/15/2024 15:00	5/15/2024 15:10	0.150	0.001	5	0.003
DW 2024	5/15/2024 15:10	5/15/2024 15:20	0.150	0.002	5	0.003
DW 2024	5/15/2024 15:20	5/15/2024 15:30	0.150	0.002	5	0.003
DW 2024	5/15/2024 15:30	5/15/2024 15:40	0.150	0.002	5	0.003
DW 2024	5/15/2024 15:40	5/15/2024 15:50	0.150	0.002	5	0.003
DW 2024	5/15/2024 15:50	5/15/2024 16:00	0.150	0.003	5	0.003

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/15/2024 8:00	5/15/2024 8:10	0.150	0	5	0
UW 2024	5/15/2024 8:10	5/15/2024 8:20	0.150	0	5	0
UW 2024	5/15/2024 8:20	5/15/2024 8:30	0.150	0	5	0
UW 2024	5/15/2024 8:30	5/15/2024 8:40	0.150	0	5	0
UW 2024	5/15/2024 8:40	5/15/2024 8:50	0.150	0	5	0
UW 2024	5/15/2024 8:50	5/15/2024 9:00	0.150	0	5	0
UW 2024	5/15/2024 9:00	5/15/2024 9:10	0.150	0	5	0
UW 2024	5/15/2024 9:10	5/15/2024 9:20	0.150	0	5	0
UW 2024	5/15/2024 9:20	5/15/2024 9:30	0.150	0	5	0
UW 2024	5/15/2024 9:30	5/15/2024 9:40	0.150	0	5	0
UW 2024	5/15/2024 9:40	5/15/2024 9:50	0.150	0.001	5	0
UW 2024	5/15/2024 9:50	5/15/2024 10:00	0.150	0.001	5	0
UW 2024	5/15/2024 10:00	5/15/2024 10:10	0.150	0.003	5	0
UW 2024	5/15/2024 10:10	5/15/2024 10:20	0.150	0.004	5	0
UW 2024	5/15/2024 10:20	5/15/2024 10:30	0.150	0.004	5	0
UW 2024	5/15/2024 10:30	5/15/2024 10:40	0.150	0.005	5	0
UW 2024	5/15/2024 10:40	5/15/2024 10:50	0.150	0.006	5	0
UW 2024	5/15/2024 10:50	5/15/2024 11:00	0.150	0.006	5	0
UW 2024	5/15/2024 11:00	5/15/2024 11:10	0.150	0.008	5	0
UW 2024	5/15/2024 11:10	5/15/2024 11:20	0.150	0.009	5	0
UW 2024	5/15/2024 11:20	5/15/2024 11:30	0.150	0.009	5	0
UW 2024	5/15/2024 11:30	5/15/2024 11:40	0.150	0.01	5	0
UW 2024	5/15/2024 11:40	5/15/2024 11:50	0.150	0.011	5	0
UW 2024	5/15/2024 11:50	5/15/2024 12:00	0.150	0.011	5	0
UW 2024	5/15/2024 12:00	5/15/2024 12:10	0.150	0.012	5	0
UW 2024	5/15/2024 12:10	5/15/2024 12:20	0.150	0.013	5	0
UW 2024	5/15/2024 12:20	5/15/2024 12:30	0.150	0.013	5	0
UW 2024	5/15/2024 12:30	5/15/2024 12:40	0.150	0.014	5	0
UW 2024	5/15/2024 12:40	5/15/2024 12:50	0.150	0.015	5	0
UW 2024	5/15/2024 12:50	5/15/2024 13:00	0.150	0.015	5	0
UW 2024	5/15/2024 13:00	5/15/2024 13:10	0.150	0.016	5	0
UW 2024	5/15/2024 13:10	5/15/2024 13:20	0.150	0.016	5	0
UW 2024	5/15/2024 13:20	5/15/2024 13:30	0.150	0.016	5	0
UW 2024	5/15/2024 13:30	5/15/2024 13:40	0.150	0.017	5	0
UW 2024	5/15/2024 13:40	5/15/2024 13:50	0.150	0.018	5	0
UW 2024	5/15/2024 13:50	5/15/2024 14:00	0.150	0.018	5	0
UW 2024	5/15/2024 14:00	5/15/2024 14:10	0.150	0.018	5	0
UW 2024	5/15/2024 14:10	5/15/2024 14:20	0.150	0.019	5	0
UW 2024	5/15/2024 14:20	5/15/2024 14:30	0.150	0.019	5	0
UW 2024	5/15/2024 14:30	5/15/2024 14:40	0.150	0.02	5	0
UW 2024	5/15/2024 14:40	5/15/2024 14:50	0.150	0.021	5	0
UW 2024	5/15/2024 14:50	5/15/2024 15:00	0.150	0.021	5	0
UW 2024	5/15/2024 15:00	5/15/2024 15:10	0.150	0.022	5	0
UW 2024	5/15/2024 15:10	5/15/2024 15:20	0.150	0.023	5	0
UW 2024	5/15/2024 15:20	5/15/2024 15:30	0.150	0.023	5	0
UW 2024	5/15/2024 15:30	5/15/2024 15:40	0.150	0.023	5	0
UW 2024	5/15/2024 15:40	5/15/2024 15:50	0.150	0.024	5	0
UW 2024	5/15/2024 15:50	5/15/2024 16:00	0.150	0.024	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/15/2024 8:00	5/15/2024 8:10	0.150	0.033	5	0
HS South	5/15/2024 8:10	5/15/2024 8:20	0.150	0.033	5	0
HS South	5/15/2024 8:20	5/15/2024 8:30	0.150	0.033	5	0
HS South	5/15/2024 8:30	5/15/2024 8:40	0.150	0.033	5	0
HS South	5/15/2024 8:40	5/15/2024 8:50	0.150	0.033	5	0
HS South	5/15/2024 8:50	5/15/2024 9:00	0.150	0.033	5	0
HS South	5/15/2024 9:00	5/15/2024 9:10	0.150	0.033	5	0
HS South	5/15/2024 9:10	5/15/2024 9:20	0.150	0.033	5	0
HS South	5/15/2024 9:20	5/15/2024 9:30	0.150	0.033	5	0
HS South	5/15/2024 9:30	5/15/2024 9:40	0.150	0.033	5	0
HS South	5/15/2024 9:40	5/15/2024 9:50	0.150	0	5	0.122
HS South	5/15/2024 9:50	5/15/2024 10:00	0.150	0.002	5	0.277
HS South	5/15/2024 10:00	5/15/2024 10:10	0.150	0.003	5	0.305
HS South	5/15/2024 10:10	5/15/2024 10:20	0.150	0.004	5	0.305
HS South	5/15/2024 10:20	5/15/2024 10:30	0.150	0.005	5	0.305
HS South	5/15/2024 10:30	5/15/2024 10:40	0.150	0.006	5	0.305
HS South	5/15/2024 10:40	5/15/2024 10:50	0.150	0.006	5	0.305
HS South	5/15/2024 10:50	5/15/2024 11:00	0.150	0.007	5	0.305
HS South	5/15/2024 11:00	5/15/2024 11:10	0.150	0.007	5	0.305
HS South	5/15/2024 11:10	5/15/2024 11:20	0.150	0.008	5	0.305
HS South	5/15/2024 11:20	5/15/2024 11:30	0.150	0.008	5	0.305
HS South	5/15/2024 11:30	5/15/2024 11:40	0.150	0.009	5	0.305
HS South	5/15/2024 11:40	5/15/2024 11:50	0.150	0.009	5	0.305
HS South	5/15/2024 11:50	5/15/2024 12:00	0.150	0.01	5	0.305
HS South	5/15/2024 12:00	5/15/2024 12:10	0.150	0.011	5	0.305
HS South	5/15/2024 12:10	5/15/2024 12:20	0.150	0.011	5	0.305
HS South	5/15/2024 12:20	5/15/2024 12:30	0.150	0.012	5	0.305
HS South	5/15/2024 12:30	5/15/2024 12:40	0.150	0.012	5	0.305
HS South	5/15/2024 12:40	5/15/2024 12:50	0.150	0.013	5	0.305
HS South	5/15/2024 12:50	5/15/2024 13:00	0.150	0.013	5	0.305
HS South	5/15/2024 13:00	5/15/2024 13:10	0.150	0.014	5	0.305
HS South	5/15/2024 13:10	5/15/2024 13:20	0.150	0.015	5	0.305
HS South	5/15/2024 13:20	5/15/2024 13:30	0.150	0.015	5	0.305
HS South	5/15/2024 13:30	5/15/2024 13:40	0.150	0.016	5	0.305
HS South	5/15/2024 13:40	5/15/2024 13:50	0.150	0.016	5	0.305
HS South	5/15/2024 13:50	5/15/2024 14:00	0.150	0.017	5	0.305
HS South	5/15/2024 14:00	5/15/2024 14:10	0.150	0.018	5	0.305
HS South	5/15/2024 14:10	5/15/2024 14:20	0.150	0.018	5	0.305
HS South	5/15/2024 14:20	5/15/2024 14:30	0.150	0.019	5	0.305
HS South	5/15/2024 14:30	5/15/2024 14:40	0.150	0.02	5	0.305
HS South	5/15/2024 14:40	5/15/2024 14:50	0.150	0.02	5	0.305
HS South	5/15/2024 14:50	5/15/2024 15:00	0.150	0.021	5	0.305
HS South	5/15/2024 15:00	5/15/2024 15:10	0.150	0.022	5	0.305
HS South	5/15/2024 15:10	5/15/2024 15:20	0.150	0.022	5	0.305
HS South	5/15/2024 15:20	5/15/2024 15:30	0.150	0.023	5	0.305
HS South	5/15/2024 15:30	5/15/2024 15:40	0.150	0.024	5	0.305
HS South	5/15/2024 15:40	5/15/2024 15:50	0.150	0.025	5	0.305
HS South	5/15/2024 15:50	5/15/2024 16:00	0.150	0.025	5	0.305

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/15/2024 8:00	5/15/2024 8:10	0.150	0.007	5	0
PER2 2024	5/15/2024 8:10	5/15/2024 8:20	0.150	0.007	5	0
PER2 2024	5/15/2024 8:20	5/15/2024 8:30	0.150	0.007	5	0
PER2 2024	5/15/2024 8:30	5/15/2024 8:40	0.150	0.007	5	0
PER2 2024	5/15/2024 8:40	5/15/2024 8:50	0.150	0.007	5	0
PER2 2024	5/15/2024 8:50	5/15/2024 9:00	0.150	0.007	5	0
PER2 2024	5/15/2024 9:00	5/15/2024 9:10	0.150	0.007	5	0
PER2 2024	5/15/2024 9:10	5/15/2024 9:20	0.150	0.007	5	0
PER2 2024	5/15/2024 9:20	5/15/2024 9:30	0.150	0.007	5	0
PER2 2024	5/15/2024 9:30	5/15/2024 9:40	0.150	0.007	5	0
PER2 2024	5/15/2024 9:40	5/15/2024 9:50	0.150	0.007	5	0
PER2 2024	5/15/2024 9:50	5/15/2024 10:00	0.150	0	5	0
PER2 2024	5/15/2024 10:00	5/15/2024 10:10	0.150	0	5	0
PER2 2024	5/15/2024 10:10	5/15/2024 10:20	0.150	0.001	5	0
PER2 2024	5/15/2024 10:20	5/15/2024 10:30	0.150	0.002	5	0
PER2 2024	5/15/2024 10:30	5/15/2024 10:40	0.150	0.002	5	0
PER2 2024	5/15/2024 10:40	5/15/2024 10:50	0.150	0.002	5	0
PER2 2024	5/15/2024 10:50	5/15/2024 11:00	0.150	0.002	5	0
PER2 2024	5/15/2024 11:00	5/15/2024 11:10	0.150	0.002	5	0
PER2 2024	5/15/2024 11:10	5/15/2024 11:20	0.150	0.002	5	0
PER2 2024	5/15/2024 11:20	5/15/2024 11:30	0.150	0.002	5	0
PER2 2024	5/15/2024 11:30	5/15/2024 11:40	0.150	0.003	5	0
PER2 2024	5/15/2024 11:40	5/15/2024 11:50	0.150	0.003	5	0
PER2 2024	5/15/2024 11:50	5/15/2024 12:00	0.150	0.003	5	0
PER2 2024	5/15/2024 12:00	5/15/2024 12:10	0.150	0.003	5	0
PER2 2024	5/15/2024 12:10	5/15/2024 12:20	0.150	0.003	5	0
PER2 2024	5/15/2024 12:20	5/15/2024 12:30	0.150	0.003	5	0
PER2 2024	5/15/2024 12:30	5/15/2024 12:40	0.150	0.003	5	0
PER2 2024	5/15/2024 12:40	5/15/2024 12:50	0.150	0.003	5	0
PER2 2024	5/15/2024 12:50	5/15/2024 13:00	0.150	0.003	5	0
PER2 2024	5/15/2024 13:00	5/15/2024 13:10	0.150	0.003	5	0
PER2 2024	5/15/2024 13:10	5/15/2024 13:20	0.150	0.003	5	0
PER2 2024	5/15/2024 13:20	5/15/2024 13:30	0.150	0.003	5	0
PER2 2024	5/15/2024 13:30	5/15/2024 13:40	0.150	0.003	5	0
PER2 2024	5/15/2024 13:40	5/15/2024 13:50	0.150	0.003	5	0
PER2 2024	5/15/2024 13:50	5/15/2024 14:00	0.150	0.003	5	0
PER2 2024	5/15/2024 14:00	5/15/2024 14:10	0.150	0.003	5	0
PER2 2024	5/15/2024 14:10	5/15/2024 14:20	0.150	0.003	5	0
PER2 2024	5/15/2024 14:20	5/15/2024 14:30	0.150	0.003	5	0
PER2 2024	5/15/2024 14:30	5/15/2024 14:40	0.150	0.003	5	0
PER2 2024	5/15/2024 14:40	5/15/2024 14:50	0.150	0.003	5	0
PER2 2024	5/15/2024 14:50	5/15/2024 15:00	0.150	0.003	5	0
PER2 2024	5/15/2024 15:00	5/15/2024 15:10	0.150	0.003	5	0
PER2 2024	5/15/2024 15:10	5/15/2024 15:20	0.150	0.003	5	0
PER2 2024	5/15/2024 15:20	5/15/2024 15:30	0.150	0.003	5	0
PER2 2024	5/15/2024 15:30	5/15/2024 15:40	0.150	0.003	5	0
PER2 2024	5/15/2024 15:40	5/15/2024 15:50	0.150	0.003	5	0
PER2 2024	5/15/2024 15:50	5/15/2024 16:00	0.150	0.003	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/15/2024 8:00	5/15/2024 8:10	0.150	0	5	0
PER1 2024	5/15/2024 8:10	5/15/2024 8:20	0.150	0	5	0
PER1 2024	5/15/2024 8:20	5/15/2024 8:30	0.150	0	5	0
PER1 2024	5/15/2024 8:30	5/15/2024 8:40	0.150	0	5	0
PER1 2024	5/15/2024 8:40	5/15/2024 8:50	0.150	0	5	0
PER1 2024	5/15/2024 8:50	5/15/2024 9:00	0.150	0	5	0
PER1 2024	5/15/2024 9:00	5/15/2024 9:10	0.150	0	5	0
PER1 2024	5/15/2024 9:10	5/15/2024 9:20	0.150	0	5	0
PER1 2024	5/15/2024 9:20	5/15/2024 9:30	0.150	0	5	0
PER1 2024	5/15/2024 9:30	5/15/2024 9:40	0.150	0	5	0
PER1 2024	5/15/2024 9:40	5/15/2024 9:50	0.150	0	5	0
PER1 2024	5/15/2024 9:50	5/15/2024 10:00	0.150	0	5	0
PER1 2024	5/15/2024 10:00	5/15/2024 10:10	0.150	0.002	5	0
PER1 2024	5/15/2024 10:10	5/15/2024 10:20	0.150	0.002	5	0
PER1 2024	5/15/2024 10:20	5/15/2024 10:30	0.150	0.003	5	0
PER1 2024	5/15/2024 10:30	5/15/2024 10:40	0.150	0.003	5	0
PER1 2024	5/15/2024 10:40	5/15/2024 10:50	0.150	0.003	5	0
PER1 2024	5/15/2024 10:50	5/15/2024 11:00	0.150	0.003	5	0
PER1 2024	5/15/2024 11:00	5/15/2024 11:10	0.150	0.004	5	0
PER1 2024	5/15/2024 11:10	5/15/2024 11:20	0.150	0.004	5	0
PER1 2024	5/15/2024 11:20	5/15/2024 11:30	0.150	0	5	0
PER1 2024	5/15/2024 11:30	5/15/2024 11:40	0.150	0	5	0
PER1 2024	5/15/2024 11:40	5/15/2024 11:50	0.150	0	5	0
PER1 2024	5/15/2024 11:50	5/15/2024 12:00	0.150	0.001	5	0
PER1 2024	5/15/2024 12:00	5/15/2024 12:10	0.150	0.001	5	0
PER1 2024	5/15/2024 12:10	5/15/2024 12:20	0.150	0.001	5	0
PER1 2024	5/15/2024 12:20	5/15/2024 12:30	0.150	0.001	5	0
PER1 2024	5/15/2024 12:30	5/15/2024 12:40	0.150	0.001	5	0
PER1 2024	5/15/2024 12:40	5/15/2024 12:50	0.150	0.002	5	0
PER1 2024	5/15/2024 12:50	5/15/2024 13:00	0.150	0.002	5	0
PER1 2024	5/15/2024 13:00	5/15/2024 13:10	0.150	0.002	5	0
PER1 2024	5/15/2024 13:10	5/15/2024 13:20	0.150	0.002	5	0
PER1 2024	5/15/2024 13:20	5/15/2024 13:30	0.150	0.002	5	0
PER1 2024	5/15/2024 13:30	5/15/2024 13:40	0.150	0.002	5	0
PER1 2024	5/15/2024 13:40	5/15/2024 13:50	0.150	0.002	5	0
PER1 2024	5/15/2024 13:50	5/15/2024 14:00	0.150	0.003	5	0
PER1 2024	5/15/2024 14:00	5/15/2024 14:10	0.150	0.003	5	0
PER1 2024	5/15/2024 14:10	5/15/2024 14:20	0.150	0.003	5	0
PER1 2024	5/15/2024 14:20	5/15/2024 14:30	0.150	0.003	5	0
PER1 2024	5/15/2024 14:30	5/15/2024 14:40	0.150	0.003	5	0
PER1 2024	5/15/2024 14:40	5/15/2024 14:50	0.150	0.004	5	0
PER1 2024	5/15/2024 14:50	5/15/2024 15:00	0.150	0.004	5	0
PER1 2024	5/15/2024 15:00	5/15/2024 15:10	0.150	0.004	5	0
PER1 2024	5/15/2024 15:10	5/15/2024 15:20	0.150	0.004	5	0
PER1 2024	5/15/2024 15:20	5/15/2024 15:30	0.150	0.004	5	0
PER1 2024	5/15/2024 15:30	5/15/2024 15:40	0.150	0.004	5	0
PER1 2024	5/15/2024 15:40	5/15/2024 15:50	0.150	0.004	5	0
PER1 2024	5/15/2024 15:50	5/15/2024 16:00	0.150	0.004	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/16/2024 Weather: 60 deg. F, Rain/Overcast

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA

Work Activities Performed: 1) Alba continued minor excavation, rebar and waterproofing installation for the foundation development. 2) Collect additional remedial excavation samples, see below. 3) ECD imported 5 loads (~100 CY) of 3/4" stone for use as backfill in the remedial excavation. 4) ECD begins backfilling the completed portion of the BMW-6/B-17 remedial excavation.

Is the dewatering system operating: YES NO

Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): REBMW6_BOT1_20240516, REBMW6_SW1_20240516 and REBMW6_SW1_20240516
--

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.
--

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8685	1520	4140

Site Layout Map and Excavation Figures

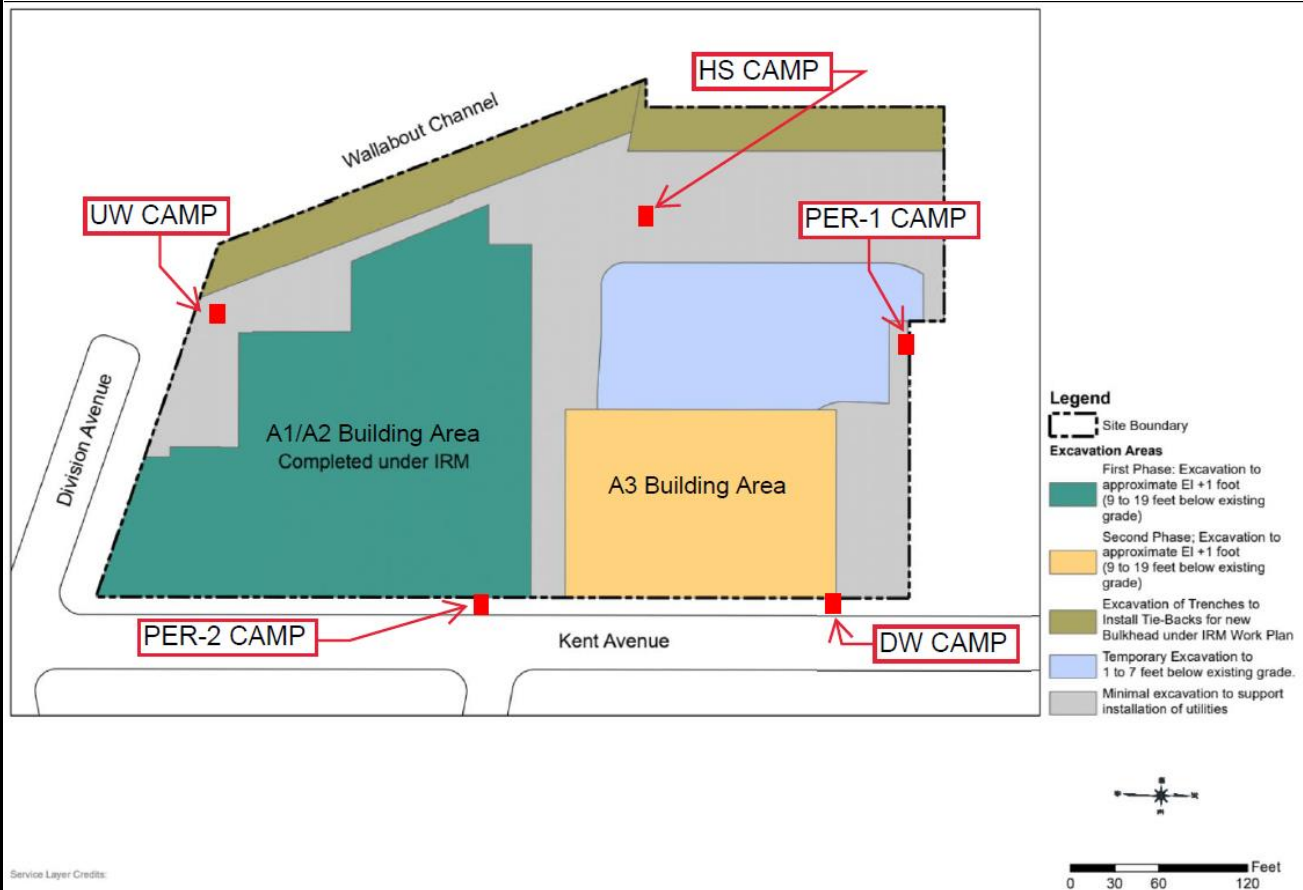

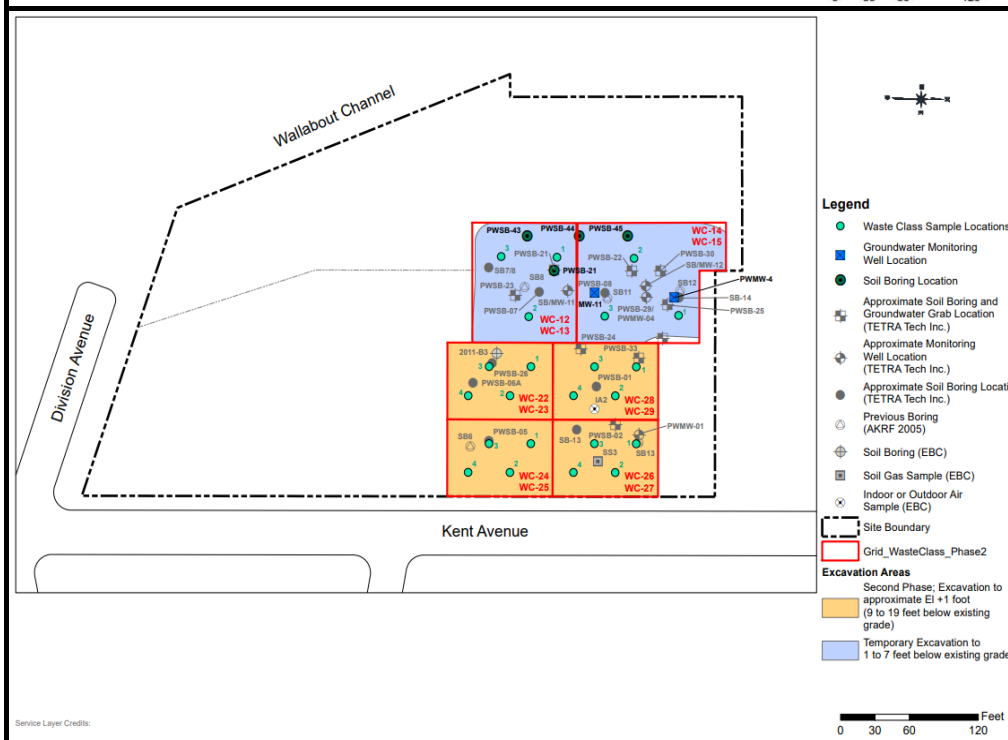
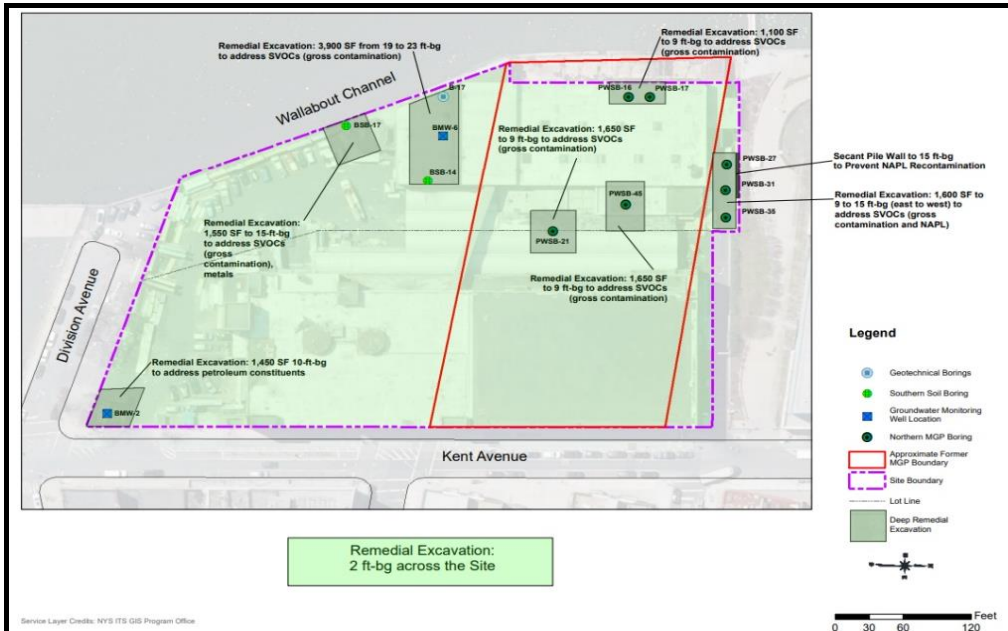


Photo 1:
View of Site conditions
and concrete pouring
facing southwest.




Photo 2:
View of Site conditions
and foundation
development facing
northwest.




Photo 3:
View of concrete
pouring for concrete
building slab
development facing
northeast.




Photo 4:
View of stone
backfilling the
remedial excavation.

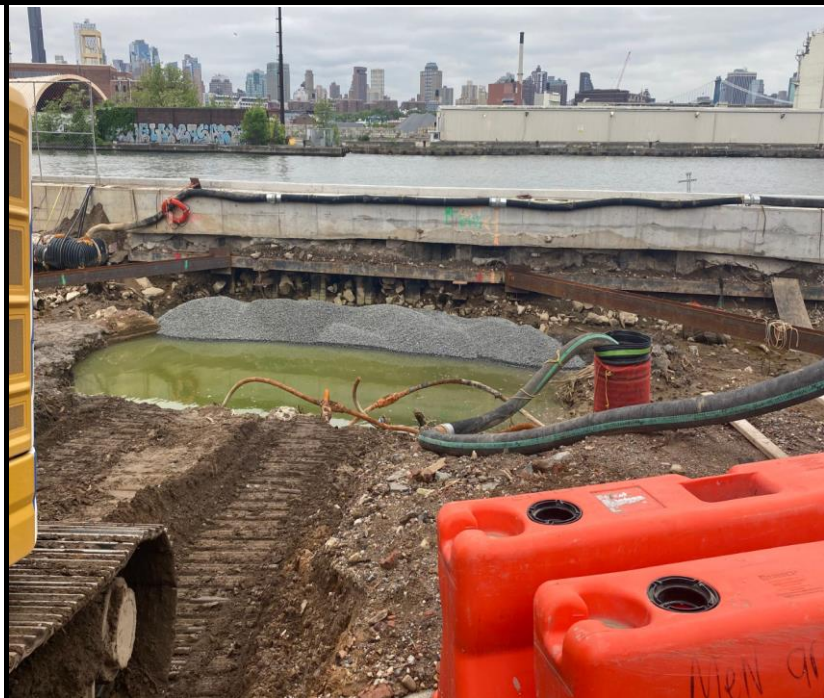

CAMP:
Downwind
Particulates

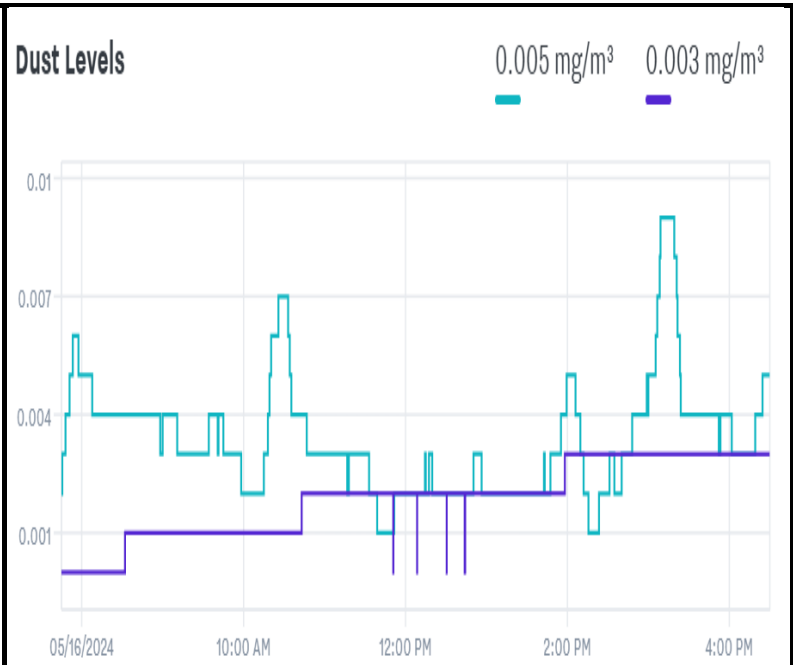


CAMP:
Downwind VOCs

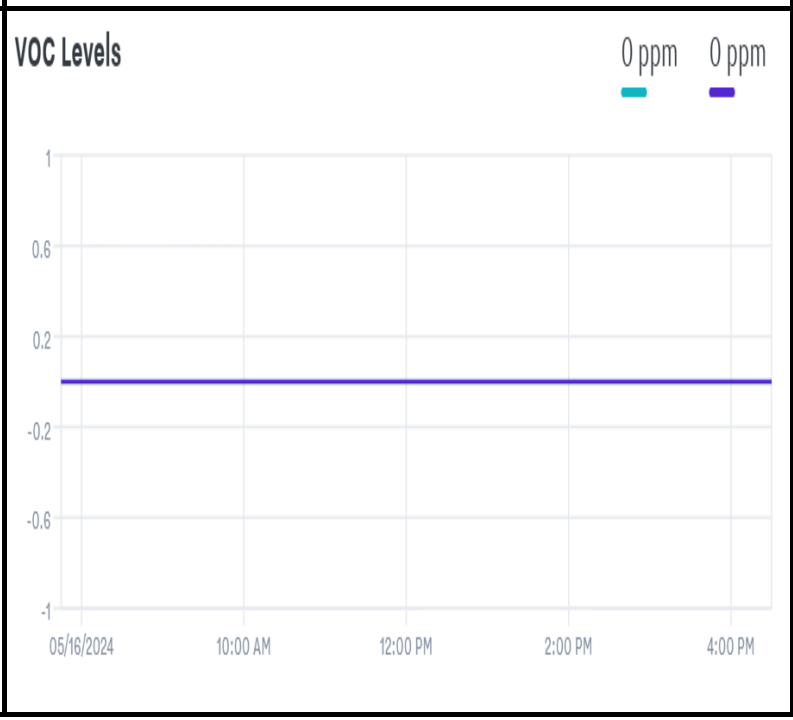


CAMP:
Upwind Particulates

Dust Levels

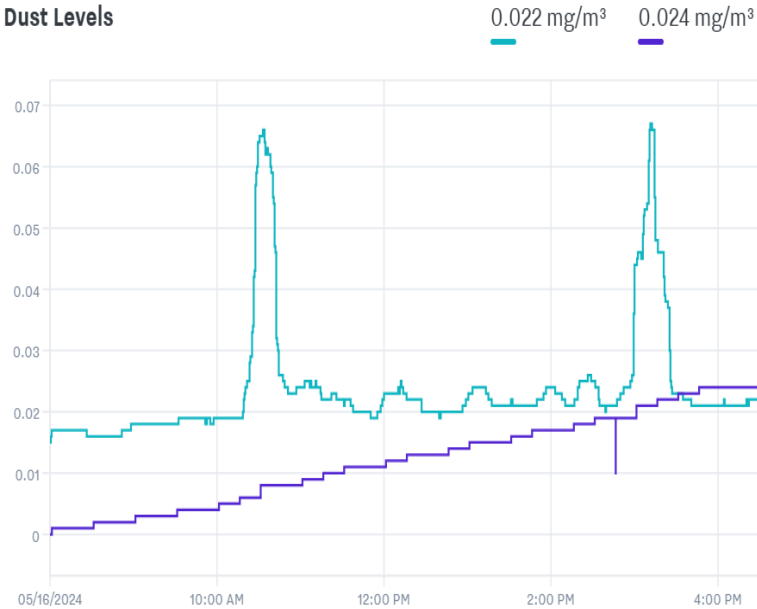

CAMP:
Upwind VOCs

VOC Levels

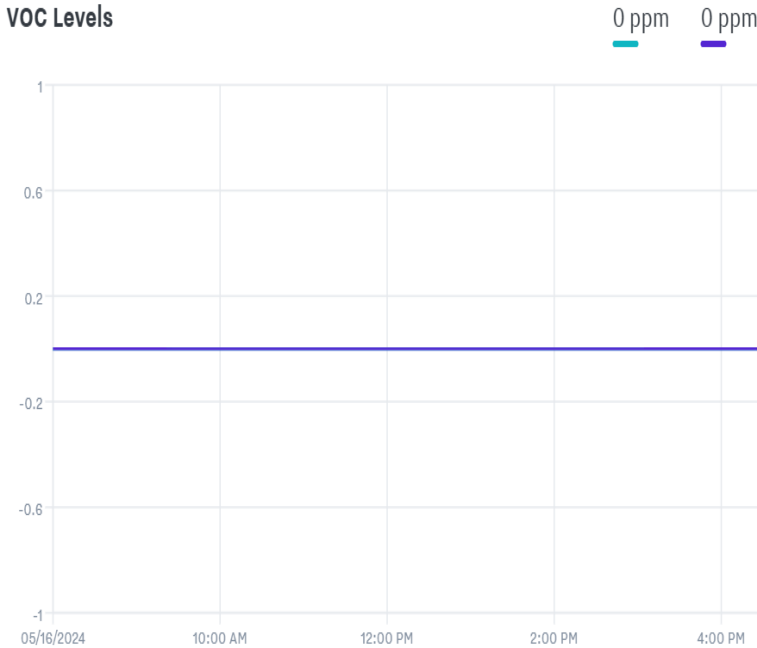

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/16/2024 8:00	5/16/2024 8:10	0.150	0	5	0
DW 2024	5/16/2024 8:10	5/16/2024 8:20	0.150	0	5	0
DW 2024	5/16/2024 8:20	5/16/2024 8:30	0.150	0	5	0
DW 2024	5/16/2024 8:30	5/16/2024 8:40	0.150	0.001	5	0
DW 2024	5/16/2024 8:40	5/16/2024 8:50	0.150	0.001	5	0
DW 2024	5/16/2024 8:50	5/16/2024 9:00	0.150	0.001	5	0
DW 2024	5/16/2024 9:00	5/16/2024 9:10	0.150	0.001	5	0
DW 2024	5/16/2024 9:10	5/16/2024 9:20	0.150	0.001	5	0
DW 2024	5/16/2024 9:20	5/16/2024 9:30	0.150	0.001	5	0
DW 2024	5/16/2024 9:30	5/16/2024 9:40	0.150	0.001	5	0
DW 2024	5/16/2024 9:40	5/16/2024 9:50	0.150	0.001	5	0
DW 2024	5/16/2024 9:50	5/16/2024 10:00	0.150	0.001	5	0
DW 2024	5/16/2024 10:00	5/16/2024 10:10	0.150	0.001	5	0
DW 2024	5/16/2024 10:10	5/16/2024 10:20	0.150	0.001	5	0
DW 2024	5/16/2024 10:20	5/16/2024 10:30	0.150	0.001	5	0
DW 2024	5/16/2024 10:30	5/16/2024 10:40	0.150	0.001	5	0
DW 2024	5/16/2024 10:40	5/16/2024 10:50	0.150	0.002	5	0
DW 2024	5/16/2024 10:50	5/16/2024 11:00	0.150	0.002	5	0
DW 2024	5/16/2024 11:00	5/16/2024 11:10	0.150	0.002	5	0
DW 2024	5/16/2024 11:10	5/16/2024 11:20	0.150	0.002	5	0
DW 2024	5/16/2024 11:20	5/16/2024 11:30	0.150	0.002	5	0
DW 2024	5/16/2024 11:30	5/16/2024 11:40	0.150	0.002	5	0
DW 2024	5/16/2024 11:40	5/16/2024 11:50	0.150	0.002	5	0
DW 2024	5/16/2024 11:50	5/16/2024 12:00	0.150	0.002	5	0
DW 2024	5/16/2024 12:00	5/16/2024 12:10	0.150	0.002	5	0
DW 2024	5/16/2024 12:10	5/16/2024 12:20	0.150	0.002	5	0
DW 2024	5/16/2024 12:20	5/16/2024 12:30	0.150	0.002	5	0
DW 2024	5/16/2024 12:30	5/16/2024 12:40	0.150	0.002	5	0
DW 2024	5/16/2024 12:40	5/16/2024 12:50	0.150	0.002	5	0
DW 2024	5/16/2024 12:50	5/16/2024 13:00	0.150	0.002	5	0
DW 2024	5/16/2024 13:00	5/16/2024 13:10	0.150	0.002	5	0
DW 2024	5/16/2024 13:10	5/16/2024 13:20	0.150	0.002	5	0
DW 2024	5/16/2024 13:20	5/16/2024 13:30	0.150	0.002	5	0
DW 2024	5/16/2024 13:30	5/16/2024 13:40	0.150	0.002	5	0
DW 2024	5/16/2024 13:40	5/16/2024 13:50	0.150	0.002	5	0
DW 2024	5/16/2024 13:50	5/16/2024 14:00	0.150	0.003	5	0
DW 2024	5/16/2024 14:00	5/16/2024 14:10	0.150	0.003	5	0
DW 2024	5/16/2024 14:10	5/16/2024 14:20	0.150	0.003	5	0
DW 2024	5/16/2024 14:20	5/16/2024 14:30	0.150	0.003	5	0
DW 2024	5/16/2024 14:30	5/16/2024 14:40	0.150	0.003	5	0
DW 2024	5/16/2024 14:40	5/16/2024 14:50	0.150	0.003	5	0
DW 2024	5/16/2024 14:50	5/16/2024 15:00	0.150	0.003	5	0
DW 2024	5/16/2024 15:00	5/16/2024 15:10	0.150	0.003	5	0
DW 2024	5/16/2024 15:10	5/16/2024 15:20	0.150	0.003	5	0
DW 2024	5/16/2024 15:20	5/16/2024 15:30	0.150	0.003	5	0
DW 2024	5/16/2024 15:30	5/16/2024 15:40	0.150	0.003	5	0
DW 2024	5/16/2024 15:40	5/16/2024 15:50	0.150	0.003	5	0
DW 2024	5/16/2024 15:50	5/16/2024 16:00	0.150	0.003	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/16/2024 8:00	5/16/2024 8:10	0.150	0.001	5	0
UW 2024	5/16/2024 8:10	5/16/2024 8:20	0.150	0.001	5	0
UW 2024	5/16/2024 8:20	5/16/2024 8:30	0.150	0.001	5	0
UW 2024	5/16/2024 8:30	5/16/2024 8:40	0.150	0.002	5	0
UW 2024	5/16/2024 8:40	5/16/2024 8:50	0.150	0.002	5	0
UW 2024	5/16/2024 8:50	5/16/2024 9:00	0.150	0.002	5	0
UW 2024	5/16/2024 9:00	5/16/2024 9:10	0.150	0.003	5	0
UW 2024	5/16/2024 9:10	5/16/2024 9:20	0.150	0.003	5	0
UW 2024	5/16/2024 9:20	5/16/2024 9:30	0.150	0.003	5	0
UW 2024	5/16/2024 9:30	5/16/2024 9:40	0.150	0.004	5	0
UW 2024	5/16/2024 9:40	5/16/2024 9:50	0.150	0.004	5	0
UW 2024	5/16/2024 9:50	5/16/2024 10:00	0.150	0.004	5	0
UW 2024	5/16/2024 10:00	5/16/2024 10:10	0.150	0.005	5	0
UW 2024	5/16/2024 10:10	5/16/2024 10:20	0.150	0.006	5	0
UW 2024	5/16/2024 10:20	5/16/2024 10:30	0.150	0.006	5	0
UW 2024	5/16/2024 10:30	5/16/2024 10:40	0.150	0.008	5	0
UW 2024	5/16/2024 10:40	5/16/2024 10:50	0.150	0.008	5	0
UW 2024	5/16/2024 10:50	5/16/2024 11:00	0.150	0.008	5	0
UW 2024	5/16/2024 11:00	5/16/2024 11:10	0.150	0.009	5	0
UW 2024	5/16/2024 11:10	5/16/2024 11:20	0.150	0.01	5	0
UW 2024	5/16/2024 11:20	5/16/2024 11:30	0.150	0.01	5	0
UW 2024	5/16/2024 11:30	5/16/2024 11:40	0.150	0.011	5	0
UW 2024	5/16/2024 11:40	5/16/2024 11:50	0.150	0.011	5	0
UW 2024	5/16/2024 11:50	5/16/2024 12:00	0.150	0.011	5	0
UW 2024	5/16/2024 12:00	5/16/2024 12:10	0.150	0.012	5	0
UW 2024	5/16/2024 12:10	5/16/2024 12:20	0.150	0.013	5	0
UW 2024	5/16/2024 12:20	5/16/2024 12:30	0.150	0.013	5	0
UW 2024	5/16/2024 12:30	5/16/2024 12:40	0.150	0.013	5	0
UW 2024	5/16/2024 12:40	5/16/2024 12:50	0.150	0.014	5	0
UW 2024	5/16/2024 12:50	5/16/2024 13:00	0.150	0.014	5	0
UW 2024	5/16/2024 13:00	5/16/2024 13:10	0.150	0.015	5	0
UW 2024	5/16/2024 13:10	5/16/2024 13:20	0.150	0.015	5	0
UW 2024	5/16/2024 13:20	5/16/2024 13:30	0.150	0.015	5	0
UW 2024	5/16/2024 13:30	5/16/2024 13:40	0.150	0.016	5	0
UW 2024	5/16/2024 13:40	5/16/2024 13:50	0.150	0.017	5	0
UW 2024	5/16/2024 13:50	5/16/2024 14:00	0.150	0.017	5	0
UW 2024	5/16/2024 14:00	5/16/2024 14:10	0.150	0.017	5	0
UW 2024	5/16/2024 14:10	5/16/2024 14:20	0.150	0.018	5	0
UW 2024	5/16/2024 14:20	5/16/2024 14:30	0.150	0.018	5	0
UW 2024	5/16/2024 14:30	5/16/2024 14:40	0.150	0.019	5	0
UW 2024	5/16/2024 14:40	5/16/2024 14:50	0.150	0.019	5	0
UW 2024	5/16/2024 14:50	5/16/2024 15:00	0.150	0.019	5	0
UW 2024	5/16/2024 15:00	5/16/2024 15:10	0.150	0.021	5	0
UW 2024	5/16/2024 15:10	5/16/2024 15:20	0.150	0.022	5	0
UW 2024	5/16/2024 15:20	5/16/2024 15:30	0.150	0.022	5	0
UW 2024	5/16/2024 15:30	5/16/2024 15:40	0.150	0.023	5	0
UW 2024	5/16/2024 15:40	5/16/2024 15:50	0.150	0.024	5	0
UW 2024	5/16/2024 15:50	5/16/2024 16:00	0.150	0.024	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/16/2024 8:00	5/16/2024 8:10	0.150	0.026	5	0.01
HS South	5/16/2024 8:10	5/16/2024 8:20	0.150	0.026	5	0.01
HS South	5/16/2024 8:20	5/16/2024 8:30	0.150	0	5	0.01
HS South	5/16/2024 8:30	5/16/2024 8:40	0.150	0	5	0.01
HS South	5/16/2024 8:40	5/16/2024 8:50	0.150	0.001	5	0.01
HS South	5/16/2024 8:50	5/16/2024 9:00	0.150	0.001	5	0.01
HS South	5/16/2024 9:00	5/16/2024 9:10	0.150	0.001	5	0.01
HS South	5/16/2024 9:10	5/16/2024 9:20	0.150	0.002	5	0.01
HS South	5/16/2024 9:20	5/16/2024 9:30	0.150	0.002	5	0.01
HS South	5/16/2024 9:30	5/16/2024 9:40	0.150	0.002	5	0.01
HS South	5/16/2024 9:40	5/16/2024 9:50	0.150	0.003	5	0.01
HS South	5/16/2024 9:50	5/16/2024 10:00	0.150	0.003	5	0.01
HS South	5/16/2024 10:00	5/16/2024 10:10	0.150	0.003	5	0.01
HS South	5/16/2024 10:10	5/16/2024 10:20	0.150	0.004	5	0.01
HS South	5/16/2024 10:20	5/16/2024 10:30	0.150	0.004	5	0.01
HS South	5/16/2024 10:30	5/16/2024 10:40	0.150	0.005	5	0.01
HS South	5/16/2024 10:40	5/16/2024 10:50	0.150	0.005	5	0.01
HS South	5/16/2024 10:50	5/16/2024 11:00	0.150	0.006	5	0.01
HS South	5/16/2024 11:00	5/16/2024 11:10	0.150	0.006	5	0.01
HS South	5/16/2024 11:10	5/16/2024 11:20	0.150	0.007	5	0.01
HS South	5/16/2024 11:20	5/16/2024 11:30	0.150	0.007	5	0.01
HS South	5/16/2024 11:30	5/16/2024 11:40	0.150	0.008	5	0.01
HS South	5/16/2024 11:40	5/16/2024 11:50	0.150	0.008	5	0.01
HS South	5/16/2024 11:50	5/16/2024 12:00	0.150	0.009	5	0.01
HS South	5/16/2024 12:00	5/16/2024 12:10	0.150	0.009	5	0.01
HS South	5/16/2024 12:10	5/16/2024 12:20	0.150	0.01	5	0.01
HS South	5/16/2024 12:20	5/16/2024 12:30	0.150	0.01	5	0.01
HS South	5/16/2024 12:30	5/16/2024 12:40	0.150	0.01	5	0.01
HS South	5/16/2024 12:40	5/16/2024 12:50	0.150	0.011	5	0.01
HS South	5/16/2024 12:50	5/16/2024 13:00	0.150	0.011	5	0.01
HS South	5/16/2024 13:00	5/16/2024 13:10	0.150	0.012	5	0.01
HS South	5/16/2024 13:10	5/16/2024 13:20	0.150	0.012	5	0.01
HS South	5/16/2024 13:20	5/16/2024 13:30	0.150	0.013	5	0.01
HS South	5/16/2024 13:30	5/16/2024 13:40	0.150	0.013	5	0.01
HS South	5/16/2024 13:40	5/16/2024 13:50	0.150	0.014	5	0.01
HS South	5/16/2024 13:50	5/16/2024 14:00	0.150	0.014	5	0.01
HS South	5/16/2024 14:00	5/16/2024 14:10	0.150	0.015	5	0.01
HS South	5/16/2024 14:10	5/16/2024 14:20	0.150	0.015	5	0.01
HS South	5/16/2024 14:20	5/16/2024 14:30	0.150	0.016	5	0.01
HS South	5/16/2024 14:30	5/16/2024 14:40	0.150	0.016	5	0.01
HS South	5/16/2024 14:40	5/16/2024 14:50	0.150	0.017	5	0.01
HS South	5/16/2024 14:50	5/16/2024 15:00	0.150	0.017	5	0.01
HS South	5/16/2024 15:00	5/16/2024 15:10	0.150	0.018	5	0.01
HS South	5/16/2024 15:10	5/16/2024 15:20	0.150	0.018	5	0.01
HS South	5/16/2024 15:20	5/16/2024 15:30	0.150	0.019	5	0.01
HS South	5/16/2024 15:30	5/16/2024 15:40	0.150	0.019	5	0.01
HS South	5/16/2024 15:40	5/16/2024 15:50	0.150	0.02	5	0.01
HS South	5/16/2024 15:50	5/16/2024 16:00	0.150	0.02	5	0.01

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/16/2024 8:00	5/16/2024 8:10	0.150	0	5	0
PER2 2024	5/16/2024 8:10	5/16/2024 8:20	0.150	0	5	0
PER2 2024	5/16/2024 8:20	5/16/2024 8:30	0.150	0	5	0
PER2 2024	5/16/2024 8:30	5/16/2024 8:40	0.150	0	5	0
PER2 2024	5/16/2024 8:40	5/16/2024 8:50	0.150	0	5	0
PER2 2024	5/16/2024 8:50	5/16/2024 9:00	0.150	0	5	0
PER2 2024	5/16/2024 9:00	5/16/2024 9:10	0.150	0	5	0
PER2 2024	5/16/2024 9:10	5/16/2024 9:20	0.150	0	5	0
PER2 2024	5/16/2024 9:20	5/16/2024 9:30	0.150	0	5	0
PER2 2024	5/16/2024 9:30	5/16/2024 9:40	0.150	0	5	0
PER2 2024	5/16/2024 9:40	5/16/2024 9:50	0.150	0	5	0
PER2 2024	5/16/2024 9:50	5/16/2024 10:00	0.150	0	5	0
PER2 2024	5/16/2024 10:00	5/16/2024 10:10	0.150	0	5	0
PER2 2024	5/16/2024 10:10	5/16/2024 10:20	0.150	0	5	0
PER2 2024	5/16/2024 10:20	5/16/2024 10:30	0.150	0	5	0
PER2 2024	5/16/2024 10:30	5/16/2024 10:40	0.150	0	5	0
PER2 2024	5/16/2024 10:40	5/16/2024 10:50	0.150	0	5	0
PER2 2024	5/16/2024 10:50	5/16/2024 11:00	0.150	0	5	0
PER2 2024	5/16/2024 11:00	5/16/2024 11:10	0.150	0	5	0
PER2 2024	5/16/2024 11:10	5/16/2024 11:20	0.150	0	5	0
PER2 2024	5/16/2024 11:20	5/16/2024 11:30	0.150	0	5	0
PER2 2024	5/16/2024 11:30	5/16/2024 11:40	0.150	0	5	0
PER2 2024	5/16/2024 11:40	5/16/2024 11:50	0.150	0	5	0
PER2 2024	5/16/2024 11:50	5/16/2024 12:00	0.150	0	5	0
PER2 2024	5/16/2024 12:00	5/16/2024 12:10	0.150	0	5	0
PER2 2024	5/16/2024 12:10	5/16/2024 12:20	0.150	0	5	0
PER2 2024	5/16/2024 12:20	5/16/2024 12:30	0.150	0.001	5	0
PER2 2024	5/16/2024 12:30	5/16/2024 12:40	0.150	0.001	5	0
PER2 2024	5/16/2024 12:40	5/16/2024 12:50	0.150	0.001	5	0
PER2 2024	5/16/2024 12:50	5/16/2024 13:00	0.150	0.001	5	0
PER2 2024	5/16/2024 13:00	5/16/2024 13:10	0.150	0.001	5	0
PER2 2024	5/16/2024 13:10	5/16/2024 13:20	0.150	0.001	5	0
PER2 2024	5/16/2024 13:20	5/16/2024 13:30	0.150	0.001	5	0
PER2 2024	5/16/2024 13:30	5/16/2024 13:40	0.150	0.001	5	0
PER2 2024	5/16/2024 13:40	5/16/2024 13:50	0.150	0.001	5	0
PER2 2024	5/16/2024 13:50	5/16/2024 14:00	0.150	0.001	5	0
PER2 2024	5/16/2024 14:00	5/16/2024 14:10	0.150	0.001	5	0
PER2 2024	5/16/2024 14:10	5/16/2024 14:20	0.150	0.001	5	0
PER2 2024	5/16/2024 14:20	5/16/2024 14:30	0.150	0.001	5	0
PER2 2024	5/16/2024 14:30	5/16/2024 14:40	0.150	0.001	5	0
PER2 2024	5/16/2024 14:40	5/16/2024 14:50	0.150	0.002	5	0
PER2 2024	5/16/2024 14:50	5/16/2024 15:00	0.150	0.002	5	0
PER2 2024	5/16/2024 15:00	5/16/2024 15:10	0.150	0.002	5	0
PER2 2024	5/16/2024 15:10	5/16/2024 15:20	0.150	0.002	5	0
PER2 2024	5/16/2024 15:20	5/16/2024 15:30	0.150	0.002	5	0
PER2 2024	5/16/2024 15:30	5/16/2024 15:40	0.150	0.002	5	0
PER2 2024	5/16/2024 15:40	5/16/2024 15:50	0.150	0.002	5	0
PER2 2024	5/16/2024 15:50	5/16/2024 16:00	0.150	0.002	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/16/2024 8:00	5/16/2024 8:10	0.150	0	5	0
PER1 2024	5/16/2024 8:10	5/16/2024 8:20	0.150	0	5	0
PER1 2024	5/16/2024 8:20	5/16/2024 8:30	0.150	0	5	0
PER1 2024	5/16/2024 8:30	5/16/2024 8:40	0.150	0	5	0
PER1 2024	5/16/2024 8:40	5/16/2024 8:50	0.150	0.001	5	0
PER1 2024	5/16/2024 8:50	5/16/2024 9:00	0.150	0.001	5	0
PER1 2024	5/16/2024 9:00	5/16/2024 9:10	0.150	0.001	5	0
PER1 2024	5/16/2024 9:10	5/16/2024 9:20	0.150	0.001	5	0
PER1 2024	5/16/2024 9:20	5/16/2024 9:30	0.150	0.002	5	0
PER1 2024	5/16/2024 9:30	5/16/2024 9:40	0.150	0.002	5	0
PER1 2024	5/16/2024 9:40	5/16/2024 9:50	0.150	0.002	5	0
PER1 2024	5/16/2024 9:50	5/16/2024 10:00	0.150	0.003	5	0
PER1 2024	5/16/2024 10:00	5/16/2024 10:10	0.150	0.003	5	0
PER1 2024	5/16/2024 10:10	5/16/2024 10:20	0.150	0.003	5	0
PER1 2024	5/16/2024 10:20	5/16/2024 10:30	0.150	0.003	5	0
PER1 2024	5/16/2024 10:30	5/16/2024 10:40	0.150	0.004	5	0
PER1 2024	5/16/2024 10:40	5/16/2024 10:50	0.150	0.004	5	0
PER1 2024	5/16/2024 10:50	5/16/2024 11:00	0.150	0.004	5	0
PER1 2024	5/16/2024 11:00	5/16/2024 11:10	0.150	0.004	5	0
PER1 2024	5/16/2024 11:10	5/16/2024 11:20	0.150	0.005	5	0
PER1 2024	5/16/2024 11:20	5/16/2024 11:30	0.150	0.005	5	0
PER1 2024	5/16/2024 11:30	5/16/2024 11:40	0.150	0.005	5	0
PER1 2024	5/16/2024 11:40	5/16/2024 11:50	0.150	0.005	5	0
PER1 2024	5/16/2024 11:50	5/16/2024 12:00	0.150	0.006	5	0
PER1 2024	5/16/2024 12:00	5/16/2024 12:10	0.150	0.006	5	0
PER1 2024	5/16/2024 12:10	5/16/2024 12:20	0.150	0.006	5	0
PER1 2024	5/16/2024 12:20	5/16/2024 12:30	0.150	0.006	5	0
PER1 2024	5/16/2024 12:30	5/16/2024 12:40	0.150	0.007	5	0
PER1 2024	5/16/2024 12:40	5/16/2024 12:50	0.150	0.007	5	0
PER1 2024	5/16/2024 12:50	5/16/2024 13:00	0.150	0.007	5	0
PER1 2024	5/16/2024 13:00	5/16/2024 13:10	0.150	0.007	5	0
PER1 2024	5/16/2024 13:10	5/16/2024 13:20	0.150	0.008	5	0
PER1 2024	5/16/2024 13:20	5/16/2024 13:30	0.150	0.008	5	0
PER1 2024	5/16/2024 13:30	5/16/2024 13:40	0.150	0.008	5	0
PER1 2024	5/16/2024 13:40	5/16/2024 13:50	0.150	0.008	5	0
PER1 2024	5/16/2024 13:50	5/16/2024 14:00	0.150	0.009	5	0
PER1 2024	5/16/2024 14:00	5/16/2024 14:10	0.150	0.009	5	0
PER1 2024	5/16/2024 14:10	5/16/2024 14:20	0.150	0.009	5	0
PER1 2024	5/16/2024 14:20	5/16/2024 14:30	0.150	0.01	5	0
PER1 2024	5/16/2024 14:30	5/16/2024 14:40	0.150	0.01	5	0
PER1 2024	5/16/2024 14:40	5/16/2024 14:50	0.150	0.01	5	0
PER1 2024	5/16/2024 14:50	5/16/2024 15:00	0.150	0.01	5	0
PER1 2024	5/16/2024 15:00	5/16/2024 15:10	0.150	0.011	5	0
PER1 2024	5/16/2024 15:10	5/16/2024 15:20	0.150	0.011	5	0
PER1 2024	5/16/2024 15:20	5/16/2024 15:30	0.150	0.011	5	0
PER1 2024	5/16/2024 15:30	5/16/2024 15:40	0.150	0.011	5	0
PER1 2024	5/16/2024 15:40	5/16/2024 15:50	0.150	0.012	5	0
PER1 2024	5/16/2024 15:50	5/16/2024 16:00	0.150	0.012	5	0

Daily Status Report

Prepared by: C. Zaccheo

Date: 05/17/2024

Weather: 70 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer:
Matthew Carroll, P.E.
Tenen Environmental, LLC

Safety Manager:
Claire Zaccheo
Tenen Environmental, LLC

Structural Contractor:
New Line Services

Excavation Contractor:
ALBA

Work Activities Performed:

1) Alba continued minor excavation, rebar and waterproofing installation for the foundation development.

Is the dewatering system operating: YES NO

Health & Safety: (answer in **red**)

Were there any changes to the H&S Plan? YES **NO** NA

Were there any CAMP exceedances at the perimeter above action levels: YES **NO** NA

Were there any dust or odor issues observed on this date? YES **NO** NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8685	1520	4140

Site Layout Map and Excavation Figures

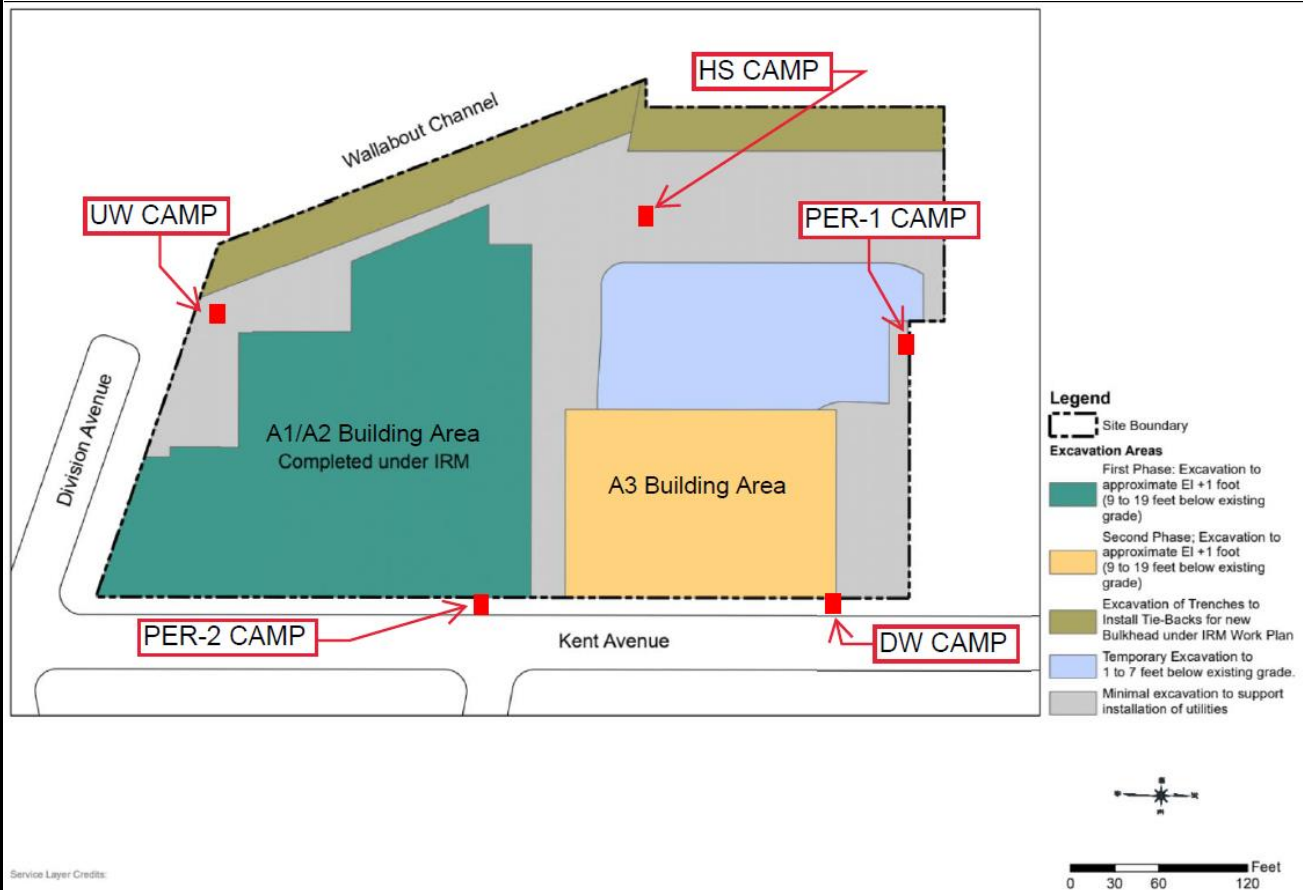

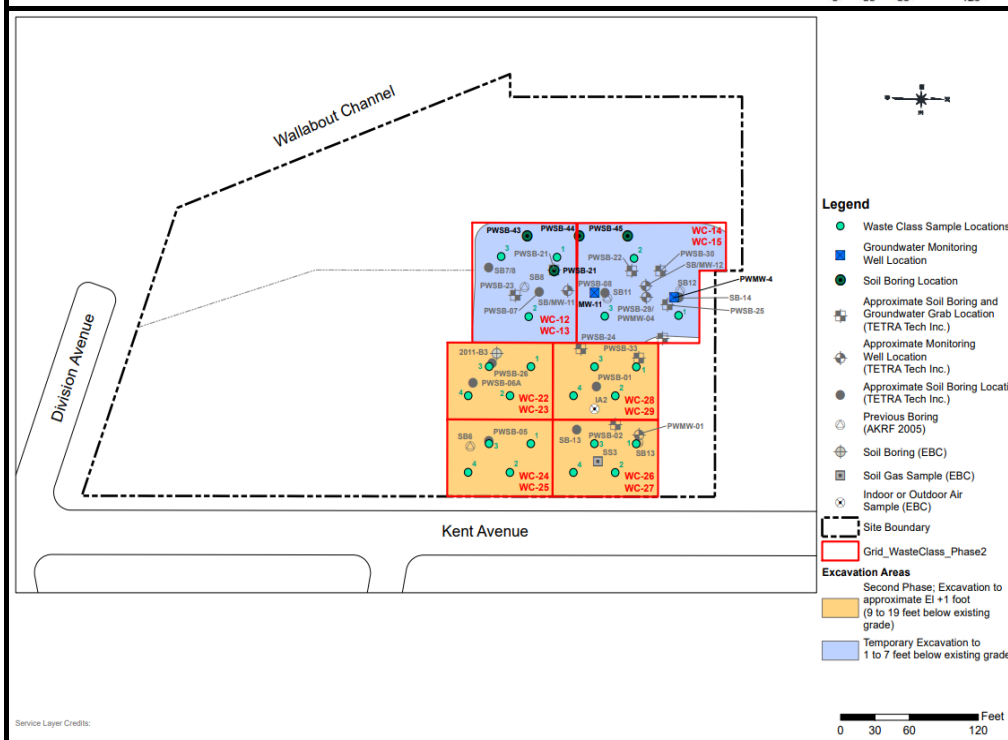
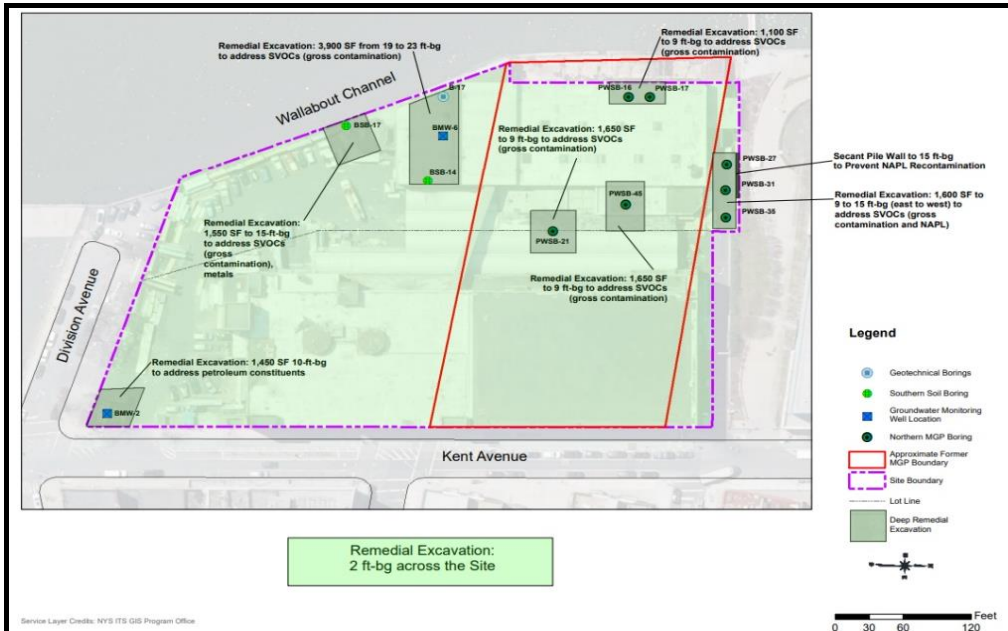


Photo 1:

View of 3/4" stone imported for use as backfill in the remedial excavation.



Photo 2:


View of the remedial excavation facing west.




Photo 3:
View of Site
conditions facing
southwest.




Photo 4:
View of Site
conditions facing
northwest.

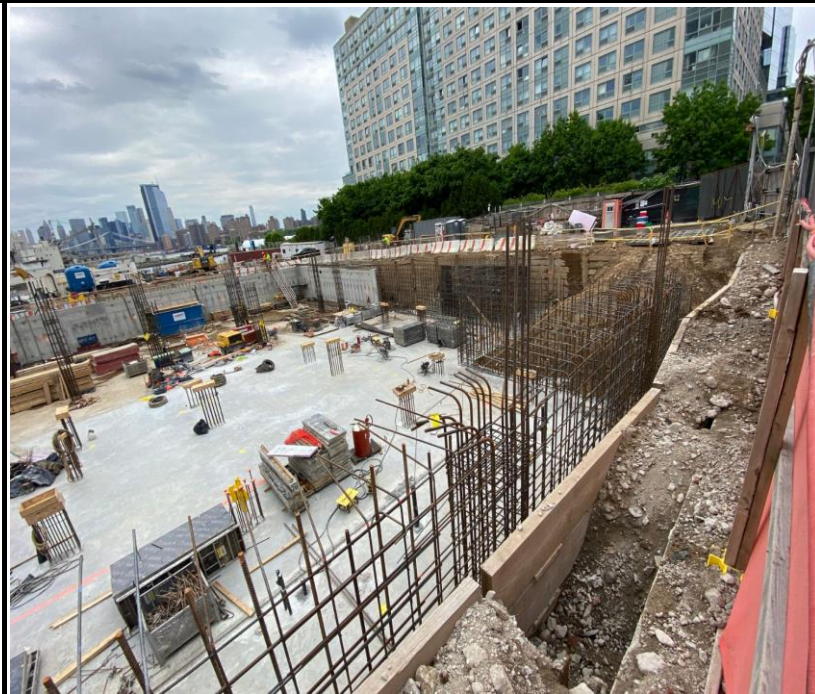

CAMP:
Downwind
Particulates

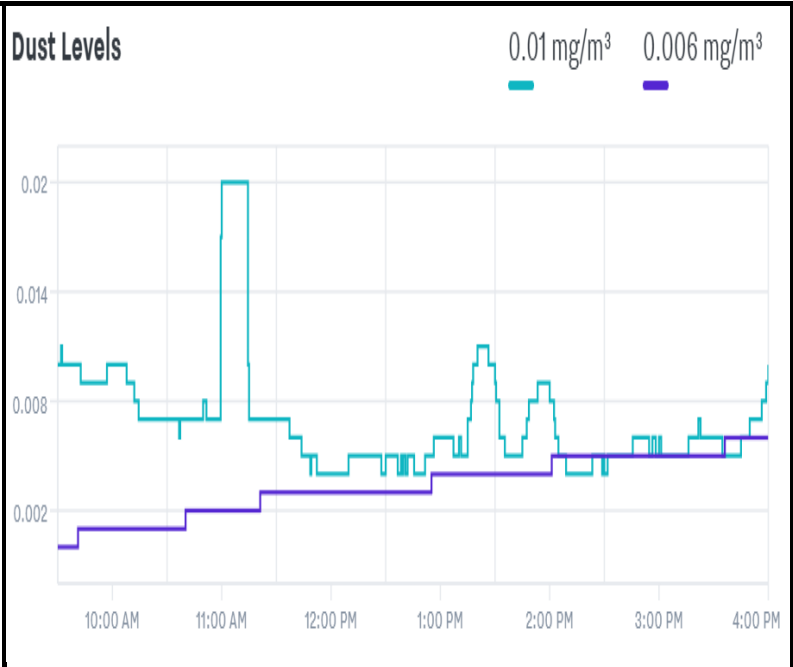


CAMP:
Downwind VOCs

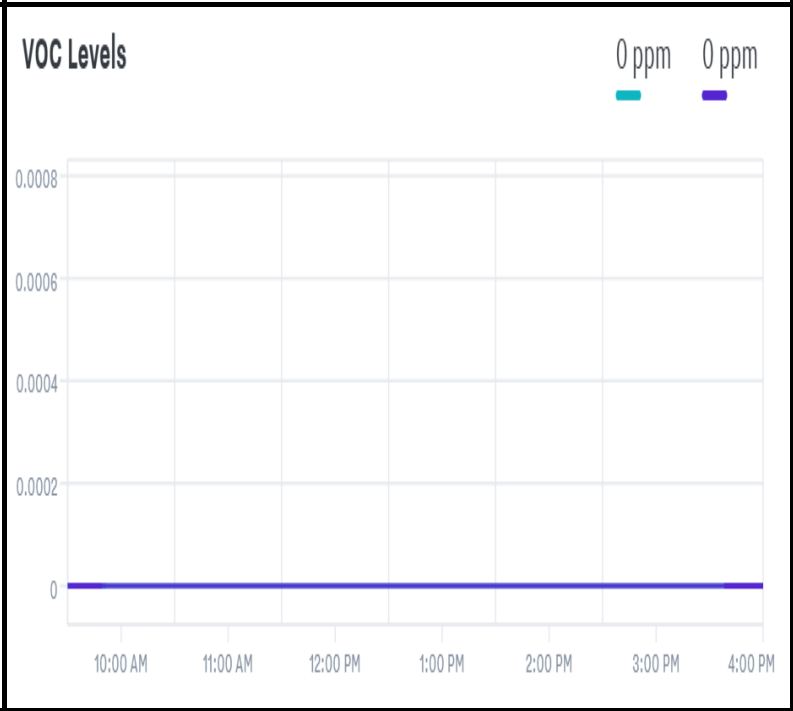

CAMP:
Upwind Particulates

Dust Levels


0.024 mg/m³ 0.021 mg/m³

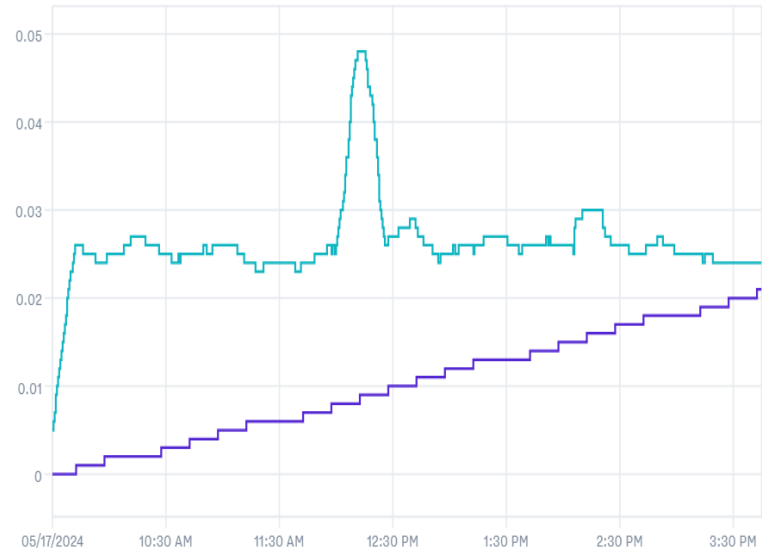

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

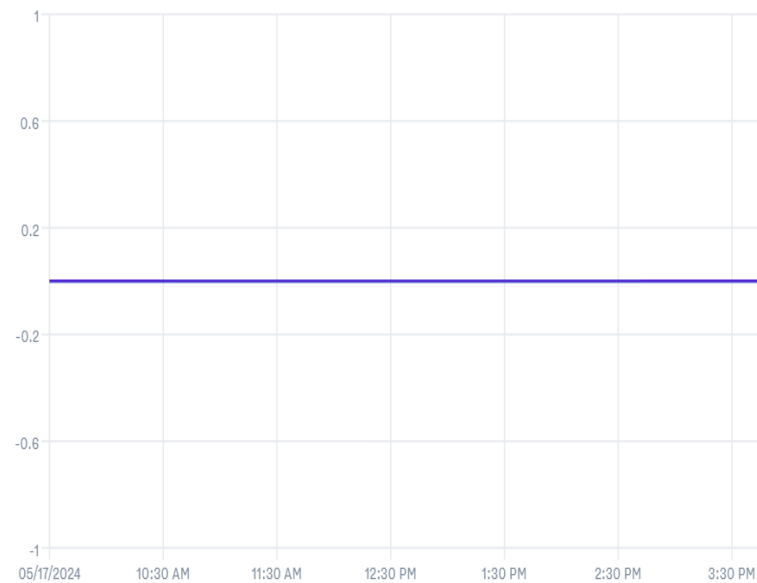

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/17/2024 9:40	5/17/2024 9:50	0.150	0	5	0
DW 2024	5/17/2024 9:50	5/17/2024 10:00	0.150	0	5	0
DW 2024	5/17/2024 10:00	5/17/2024 10:10	0.150	0.002	5	0
DW 2024	5/17/2024 10:10	5/17/2024 10:20	0.150	0.002	5	0
DW 2024	5/17/2024 10:20	5/17/2024 10:30	0.150	0.003	5	0
DW 2024	5/17/2024 10:30	5/17/2024 10:40	0.150	0.003	5	0
DW 2024	5/17/2024 10:40	5/17/2024 10:50	0.150	0.004	5	0
DW 2024	5/17/2024 10:50	5/17/2024 11:00	0.150	0.004	5	0
DW 2024	5/17/2024 11:00	5/17/2024 11:10	0.150	0.005	5	0
DW 2024	5/17/2024 11:10	5/17/2024 11:20	0.150	0.006	5	0
DW 2024	5/17/2024 11:20	5/17/2024 11:30	0.150	0.006	5	0
DW 2024	5/17/2024 11:30	5/17/2024 11:40	0.150	0.007	5	0
DW 2024	5/17/2024 11:40	5/17/2024 11:50	0.150	0.007	5	0
DW 2024	5/17/2024 11:50	5/17/2024 12:00	0.150	0.008	5	0
DW 2024	5/17/2024 12:00	5/17/2024 12:10	0.150	0.009	5	0
DW 2024	5/17/2024 12:10	5/17/2024 12:20	0.150	0.009	5	0
DW 2024	5/17/2024 12:20	5/17/2024 12:30	0.150	0.01	5	0
DW 2024	5/17/2024 12:30	5/17/2024 12:40	0.150	0.01	5	0
DW 2024	5/17/2024 12:40	5/17/2024 12:50	0.150	0.011	5	0
DW 2024	5/17/2024 12:50	5/17/2024 13:00	0.150	0.012	5	0
DW 2024	5/17/2024 13:00	5/17/2024 13:10	0.150	0.013	5	0
DW 2024	5/17/2024 13:10	5/17/2024 13:20	0.150	0.014	5	0
DW 2024	5/17/2024 13:20	5/17/2024 13:30	0.150	0.015	5	0
DW 2024	5/17/2024 13:30	5/17/2024 13:40	0.150	0.015	5	0
DW 2024	5/17/2024 13:40	5/17/2024 13:50	0.150	0.016	5	0
DW 2024	5/17/2024 13:50	5/17/2024 14:00	0.150	0.017	5	0
DW 2024	5/17/2024 14:00	5/17/2024 14:10	0.150	0.018	5	0
DW 2024	5/17/2024 14:10	5/17/2024 14:20	0.150	0.018	5	0
DW 2024	5/17/2024 14:20	5/17/2024 14:30	0.150	0.019	5	0
DW 2024	5/17/2024 14:30	5/17/2024 14:40	0.150	0.02	5	0
DW 2024	5/17/2024 14:40	5/17/2024 14:50	0.150	0.02	5	0
DW 2024	5/17/2024 14:50	5/17/2024 15:00	0.150	0.021	5	0
DW 2024	5/17/2024 15:00	5/17/2024 15:10	0.150	0.022	5	0
DW 2024	5/17/2024 15:10	5/17/2024 15:20	0.150	0.023	5	0
DW 2024	5/17/2024 15:20	5/17/2024 15:30	0.150	0.023	5	0
DW 2024	5/17/2024 15:30	5/17/2024 15:40	0.150	0.024	5	0
DW 2024	5/17/2024 15:40	5/17/2024 15:50	0.150	0.025	5	0
DW 2024	5/17/2024 15:50	5/17/2024 16:00	0.150	0.026	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/17/2024 9:20	5/17/2024 9:30	0.150	0	5	0
UW 2024	5/17/2024 9:30	5/17/2024 9:40	0.150	0	5	0
UW 2024	5/17/2024 9:40	5/17/2024 9:50	0.150	0.001	5	0
UW 2024	5/17/2024 9:50	5/17/2024 10:00	0.150	0.002	5	0
UW 2024	5/17/2024 10:00	5/17/2024 10:10	0.150	0.002	5	0
UW 2024	5/17/2024 10:10	5/17/2024 10:20	0.150	0.002	5	0
UW 2024	5/17/2024 10:20	5/17/2024 10:30	0.150	0.003	5	0
UW 2024	5/17/2024 10:30	5/17/2024 10:40	0.150	0.003	5	0
UW 2024	5/17/2024 10:40	5/17/2024 10:50	0.150	0.004	5	0
UW 2024	5/17/2024 10:50	5/17/2024 11:00	0.150	0.005	5	0
UW 2024	5/17/2024 11:00	5/17/2024 11:10	0.150	0.005	5	0
UW 2024	5/17/2024 11:10	5/17/2024 11:20	0.150	0.006	5	0
UW 2024	5/17/2024 11:20	5/17/2024 11:30	0.150	0.006	5	0
UW 2024	5/17/2024 11:30	5/17/2024 11:40	0.150	0.006	5	0
UW 2024	5/17/2024 11:40	5/17/2024 11:50	0.150	0.007	5	0
UW 2024	5/17/2024 11:50	5/17/2024 12:00	0.150	0.008	5	0
UW 2024	5/17/2024 12:00	5/17/2024 12:10	0.150	0.008	5	0
UW 2024	5/17/2024 12:10	5/17/2024 12:20	0.150	0.009	5	0
UW 2024	5/17/2024 12:20	5/17/2024 12:30	0.150	0.01	5	0
UW 2024	5/17/2024 12:30	5/17/2024 12:40	0.150	0.01	5	0
UW 2024	5/17/2024 12:40	5/17/2024 12:50	0.150	0.011	5	0
UW 2024	5/17/2024 12:50	5/17/2024 13:00	0.150	0.012	5	0
UW 2024	5/17/2024 13:00	5/17/2024 13:10	0.150	0.012	5	0
UW 2024	5/17/2024 13:10	5/17/2024 13:20	0.150	0.013	5	0
UW 2024	5/17/2024 13:20	5/17/2024 13:30	0.150	0.013	5	0
UW 2024	5/17/2024 13:30	5/17/2024 13:40	0.150	0.013	5	0
UW 2024	5/17/2024 13:40	5/17/2024 13:50	0.150	0.014	5	0
UW 2024	5/17/2024 13:50	5/17/2024 14:00	0.150	0.015	5	0
UW 2024	5/17/2024 14:00	5/17/2024 14:10	0.150	0.015	5	0
UW 2024	5/17/2024 14:10	5/17/2024 14:20	0.150	0.016	5	0
UW 2024	5/17/2024 14:20	5/17/2024 14:30	0.150	0.017	5	0
UW 2024	5/17/2024 14:30	5/17/2024 14:40	0.150	0.017	5	0
UW 2024	5/17/2024 14:40	5/17/2024 14:50	0.150	0.018	5	0
UW 2024	5/17/2024 14:50	5/17/2024 15:00	0.150	0.018	5	0
UW 2024	5/17/2024 15:00	5/17/2024 15:10	0.150	0.018	5	0
UW 2024	5/17/2024 15:10	5/17/2024 15:20	0.150	0.019	5	0
UW 2024	5/17/2024 15:20	5/17/2024 15:30	0.150	0.02	5	0
UW 2024	5/17/2024 15:30	5/17/2024 15:40	0.150	0.02	5	0
UW 2024	5/17/2024 15:40	5/17/2024 15:50	0.150	0.021	5	0
UW 2024	5/17/2024 15:50	5/17/2024 16:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/17/2024 9:20	5/17/2024 9:30	0.150	0	5	0
HS South	5/17/2024 9:30	5/17/2024 9:40	0.150	0	5	0
HS South	5/17/2024 9:40	5/17/2024 9:50	0.150	0	5	0
HS South	5/17/2024 9:50	5/17/2024 10:00	0.150	0.001	5	0
HS South	5/17/2024 10:00	5/17/2024 10:10	0.150	0.001	5	0
HS South	5/17/2024 10:10	5/17/2024 10:20	0.150	0.001	5	0
HS South	5/17/2024 10:20	5/17/2024 10:30	0.150	0.001	5	0
HS South	5/17/2024 10:30	5/17/2024 10:40	0.150	0.001	5	0
HS South	5/17/2024 10:40	5/17/2024 10:50	0.150	0.001	5	0
HS South	5/17/2024 10:50	5/17/2024 11:00	0.150	0.001	5	0
HS South	5/17/2024 11:00	5/17/2024 11:10	0.150	0.001	5	0
HS South	5/17/2024 11:10	5/17/2024 11:20	0.150	0.002	5	0
HS South	5/17/2024 11:20	5/17/2024 11:30	0.150	0.002	5	0
HS South	5/17/2024 11:30	5/17/2024 11:40	0.150	0.002	5	0
HS South	5/17/2024 11:40	5/17/2024 11:50	0.150	0.002	5	0
HS South	5/17/2024 11:50	5/17/2024 12:00	0.150	0.002	5	0
HS South	5/17/2024 12:00	5/17/2024 12:10	0.150	0.002	5	0
HS South	5/17/2024 12:10	5/17/2024 12:20	0.150	0.002	5	0
HS South	5/17/2024 12:20	5/17/2024 12:30	0.150	0.002	5	0
HS South	5/17/2024 12:30	5/17/2024 12:40	0.150	0.002	5	0
HS South	5/17/2024 12:40	5/17/2024 12:50	0.150	0.002	5	0
HS South	5/17/2024 12:50	5/17/2024 13:00	0.150	0.002	5	0
HS South	5/17/2024 13:00	5/17/2024 13:10	0.150	0.002	5	0
HS South	5/17/2024 13:10	5/17/2024 13:20	0.150	0.002	5	0
HS South	5/17/2024 13:20	5/17/2024 13:30	0.150	0.002	5	0
HS South	5/17/2024 13:30	5/17/2024 13:40	0.150	0.002	5	0
HS South	5/17/2024 13:40	5/17/2024 13:50	0.150	0.002	5	0
HS South	5/17/2024 13:50	5/17/2024 14:00	0.150	0.002	5	0
HS South	5/17/2024 14:00	5/17/2024 14:10	0.150	0.002	5	0
HS South	5/17/2024 14:10	5/17/2024 14:20	0.150	0.002	5	0
HS South	5/17/2024 14:20	5/17/2024 14:30	0.150	0.002	5	0
HS South	5/17/2024 14:30	5/17/2024 14:40	0.150	0.002	5	0
HS South	5/17/2024 14:40	5/17/2024 14:50	0.150	0.004	5	0
HS South	5/17/2024 14:50	5/17/2024 15:00	0.150	0.005	5	0
HS South	5/17/2024 15:00	5/17/2024 15:10	0.150	0.005	5	0
HS South	5/17/2024 15:10	5/17/2024 15:20	0.150	0.005	5	0
HS South	5/17/2024 15:20	5/17/2024 15:30	0.150	0.005	5	0
HS South	5/17/2024 15:30	5/17/2024 15:40	0.150	0.005	5	0
HS South	5/17/2024 15:40	5/17/2024 15:50	0.150	0.006	5	0
HS South	5/17/2024 15:50	5/17/2024 16:00	0.150	0.006	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/17/2024 9:20	5/17/2024 9:30	0.150	0	5	0
PER2 2024	5/17/2024 9:30	5/17/2024 9:40	0.150	0	5	0
PER2 2024	5/17/2024 9:40	5/17/2024 9:50	0.150	0	5	0
PER2 2024	5/17/2024 9:50	5/17/2024 10:00	0.150	0	5	0
PER2 2024	5/17/2024 10:00	5/17/2024 10:10	0.150	0	5	0
PER2 2024	5/17/2024 10:10	5/17/2024 10:20	0.150	0	5	0
PER2 2024	5/17/2024 10:20	5/17/2024 10:30	0.150	0	5	0
PER2 2024	5/17/2024 10:30	5/17/2024 10:40	0.150	0	5	0
PER2 2024	5/17/2024 10:40	5/17/2024 10:50	0.150	0	5	0
PER2 2024	5/17/2024 10:50	5/17/2024 11:00	0.150	0	5	0
PER2 2024	5/17/2024 11:00	5/17/2024 11:10	0.150	0	5	0
PER2 2024	5/17/2024 11:10	5/17/2024 11:20	0.150	0	5	0
PER2 2024	5/17/2024 11:20	5/17/2024 11:30	0.150	0	5	0
PER2 2024	5/17/2024 11:30	5/17/2024 11:40	0.150	0	5	0
PER2 2024	5/17/2024 11:40	5/17/2024 11:50	0.150	0	5	0
PER2 2024	5/17/2024 11:50	5/17/2024 12:00	0.150	0	5	0
PER2 2024	5/17/2024 12:00	5/17/2024 12:10	0.150	0	5	0
PER2 2024	5/17/2024 12:10	5/17/2024 12:20	0.150	0	5	0
PER2 2024	5/17/2024 12:20	5/17/2024 12:30	0.150	0	5	0
PER2 2024	5/17/2024 12:30	5/17/2024 12:40	0.150	0	5	0
PER2 2024	5/17/2024 12:40	5/17/2024 12:50	0.150	0	5	0
PER2 2024	5/17/2024 12:50	5/17/2024 13:00	0.150	0	5	0
PER2 2024	5/17/2024 13:00	5/17/2024 13:10	0.150	0	5	0
PER2 2024	5/17/2024 13:10	5/17/2024 13:20	0.150	0	5	0
PER2 2024	5/17/2024 13:20	5/17/2024 13:30	0.150	0	5	0
PER2 2024	5/17/2024 13:30	5/17/2024 13:40	0.150	0	5	0
PER2 2024	5/17/2024 13:40	5/17/2024 13:50	0.150	0.001	5	0
PER2 2024	5/17/2024 13:50	5/17/2024 14:00	0.150	0.001	5	0
PER2 2024	5/17/2024 14:00	5/17/2024 14:10	0.150	0.001	5	0
PER2 2024	5/17/2024 14:10	5/17/2024 14:20	0.150	0.001	5	0
PER2 2024	5/17/2024 14:20	5/17/2024 14:30	0.150	0.001	5	0
PER2 2024	5/17/2024 14:30	5/17/2024 14:40	0.150	0.001	5	0
PER2 2024	5/17/2024 14:40	5/17/2024 14:50	0.150	0.001	5	0
PER2 2024	5/17/2024 14:50	5/17/2024 15:00	0.150	0.001	5	0
PER2 2024	5/17/2024 15:00	5/17/2024 15:10	0.150	0.001	5	0
PER2 2024	5/17/2024 15:10	5/17/2024 15:20	0.150	0.001	5	0
PER2 2024	5/17/2024 15:20	5/17/2024 15:30	0.150	0.001	5	0
PER2 2024	5/17/2024 15:30	5/17/2024 15:40	0.150	0.001	5	0
PER2 2024	5/17/2024 15:40	5/17/2024 15:50	0.150	0.001	5	0
PER2 2024	5/17/2024 15:50	5/17/2024 16:00	0.150	0.001	5	0
PER2 2024	5/16/2024 14:40	5/16/2024 14:50	0.150	0.002	5	0
PER2 2024	5/16/2024 14:50	5/16/2024 15:00	0.150	0.002	5	0
PER2 2024	5/16/2024 15:00	5/16/2024 15:10	0.150	0.002	5	0
PER2 2024	5/16/2024 15:10	5/16/2024 15:20	0.150	0.002	5	0
PER2 2024	5/16/2024 15:20	5/16/2024 15:30	0.150	0.002	5	0
PER2 2024	5/16/2024 15:30	5/16/2024 15:40	0.150	0.002	5	0
PER2 2024	5/16/2024 15:40	5/16/2024 15:50	0.150	0.002	5	0
PER2 2024	5/16/2024 15:50	5/16/2024 16:00	0.150	0.002	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/17/2024 9:20	5/17/2024 9:30	0.150	0	5	0
PER1 2024	5/17/2024 9:30	5/17/2024 9:40	0.150	0	5	0
PER1 2024	5/17/2024 9:40	5/17/2024 9:50	0.150	0	5	0
PER1 2024	5/17/2024 9:50	5/17/2024 10:00	0.150	0	5	0
PER1 2024	5/17/2024 10:00	5/17/2024 10:10	0.150	0	5	0
PER1 2024	5/17/2024 10:10	5/17/2024 10:20	0.150	0.001	5	0
PER1 2024	5/17/2024 10:20	5/17/2024 10:30	0.150	0.001	5	0
PER1 2024	5/17/2024 10:30	5/17/2024 10:40	0.150	0.001	5	0
PER1 2024	5/17/2024 10:40	5/17/2024 10:50	0.150	0.001	5	0
PER1 2024	5/17/2024 10:50	5/17/2024 11:00	0.150	0.002	5	0
PER1 2024	5/17/2024 11:00	5/17/2024 11:10	0.150	0.002	5	0
PER1 2024	5/17/2024 11:10	5/17/2024 11:20	0.150	0.002	5	0
PER1 2024	5/17/2024 11:20	5/17/2024 11:30	0.150	0.003	5	0
PER1 2024	5/17/2024 11:30	5/17/2024 11:40	0.150	0.003	5	0
PER1 2024	5/17/2024 11:40	5/17/2024 11:50	0.150	0.003	5	0
PER1 2024	5/17/2024 11:50	5/17/2024 12:00	0.150	0.003	5	0
PER1 2024	5/17/2024 12:00	5/17/2024 12:10	0.150	0.004	5	0
PER1 2024	5/17/2024 12:10	5/17/2024 12:20	0.150	0.004	5	0
PER1 2024	5/17/2024 12:20	5/17/2024 12:30	0.150	0.004	5	0
PER1 2024	5/17/2024 12:30	5/17/2024 12:40	0.150	0.004	5	0
PER1 2024	5/17/2024 12:40	5/17/2024 12:50	0.150	0.005	5	0
PER1 2024	5/17/2024 12:50	5/17/2024 13:00	0.150	0.005	5	0
PER1 2024	5/17/2024 13:00	5/17/2024 13:10	0.150	0.005	5	0
PER1 2024	5/17/2024 13:10	5/17/2024 13:20	0.150	0.005	5	0
PER1 2024	5/17/2024 13:20	5/17/2024 13:30	0.150	0.006	5	0
PER1 2024	5/17/2024 13:30	5/17/2024 13:40	0.150	0.006	5	0
PER1 2024	5/17/2024 13:40	5/17/2024 13:50	0.150	0.006	5	0
PER1 2024	5/17/2024 13:50	5/17/2024 14:00	0.150	0.006	5	0
PER1 2024	5/17/2024 14:00	5/17/2024 14:10	0.150	0.007	5	0
PER1 2024	5/17/2024 14:10	5/17/2024 14:20	0.150	0.007	5	0
PER1 2024	5/17/2024 14:20	5/17/2024 14:30	0.150	0.007	5	0
PER1 2024	5/17/2024 14:30	5/17/2024 14:40	0.150	0.008	5	0
PER1 2024	5/17/2024 14:40	5/17/2024 14:50	0.150	0.008	5	0
PER1 2024	5/17/2024 14:50	5/17/2024 15:00	0.150	0.008	5	0
PER1 2024	5/17/2024 15:00	5/17/2024 15:10	0.150	0.009	5	0
PER1 2024	5/17/2024 15:10	5/17/2024 15:20	0.150	0.009	5	0
PER1 2024	5/17/2024 15:20	5/17/2024 15:30	0.150	0.009	5	0
PER1 2024	5/17/2024 15:30	5/17/2024 15:40	0.150	0.01	5	0
PER1 2024	5/17/2024 15:40	5/17/2024 15:50	0.150	0.01	5	0
PER1 2024	5/17/2024 15:50	5/17/2024 16:00	0.150	0.01	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/20/2024 Weather: 80 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued minor excavation, rebar and waterproofing installation for the foundation development. 2) ECD advanced the remedial excavation 15 ft. east and collect endpoint samples, see below.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): REB_MW6_BOT2_20240520, REB_MW6_SW2_20240520 and REB_MW6_SW5_20240520	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	100	0
Total:(CY)	4485	0	8685	1620	4140

Site Layout Map and Excavation Figures

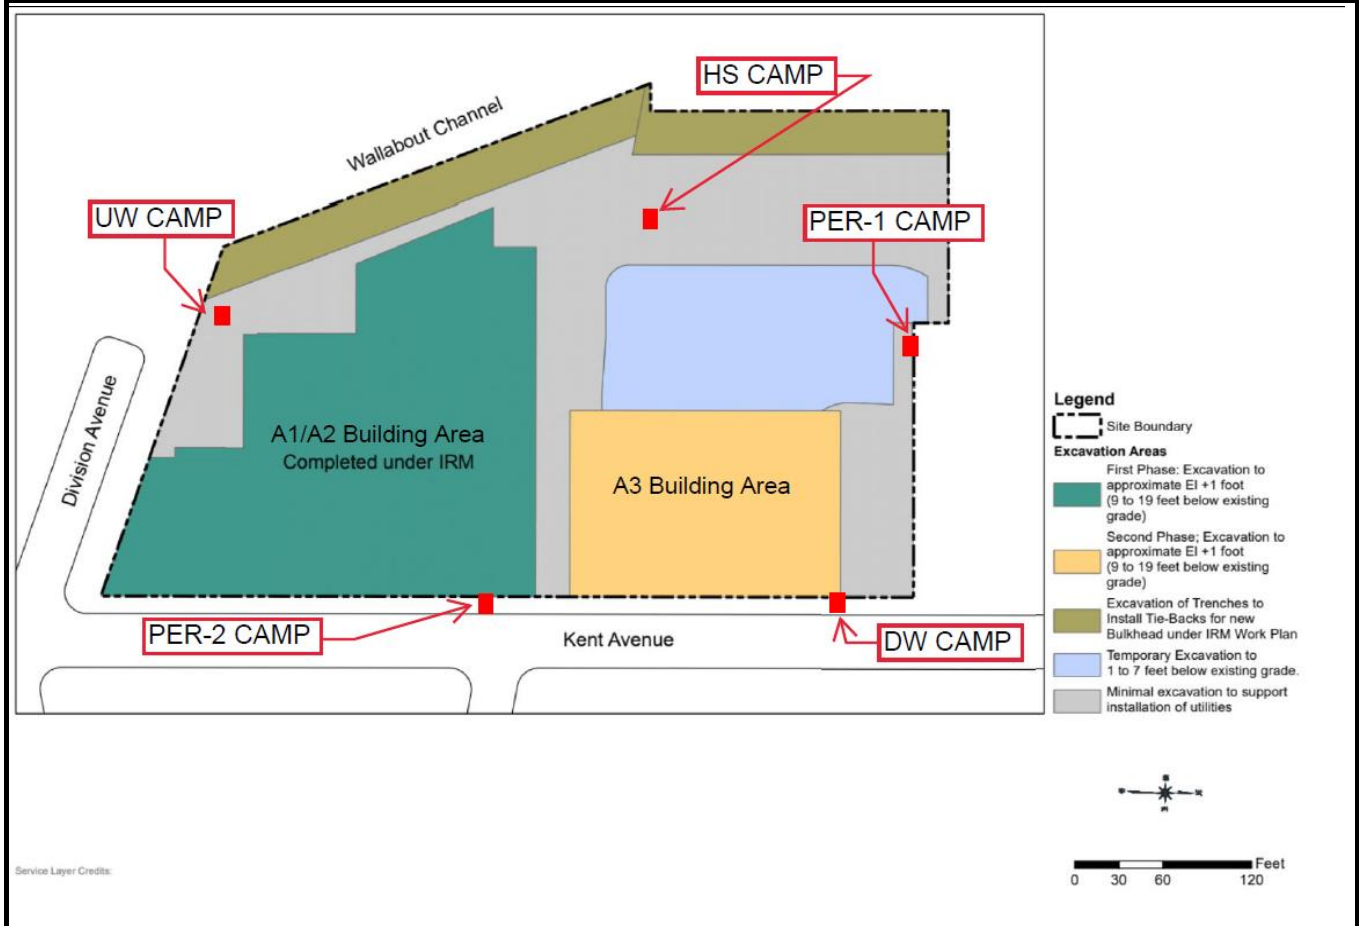

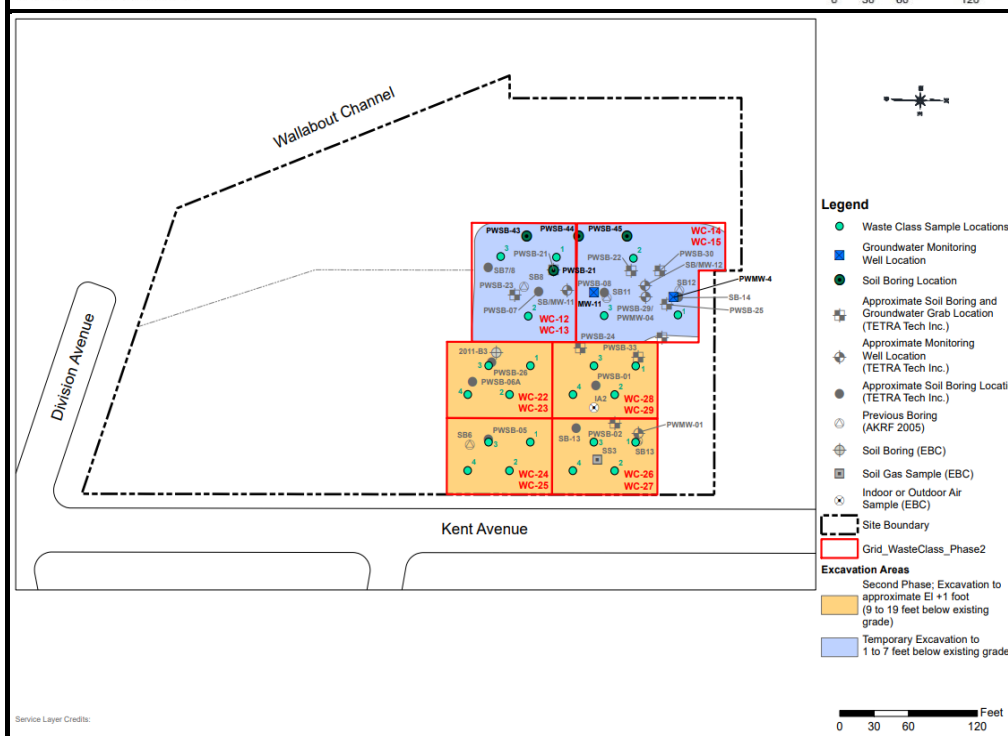
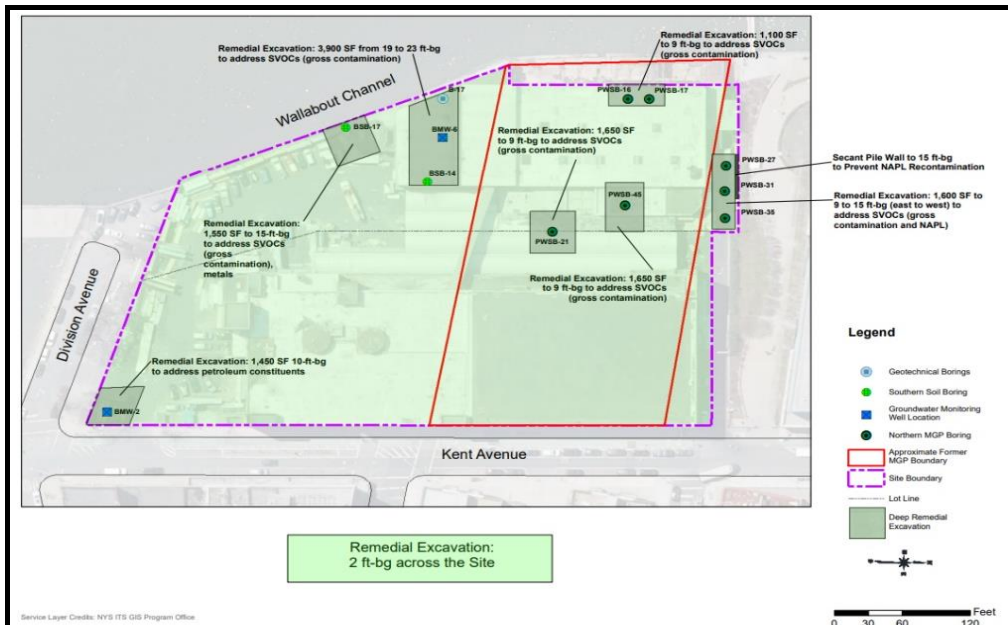


Photo 1:
View of Site conditions
and foundation
development facing
southwest.




Photo 2:
View of soil excavation
and disposal from the
remedial excavation.



Photo 3:
View of truck loading
with soil from
remedial excavation
for off-site soil
disposal.




Photo 4:
View of Site
conditions facing
northwest.

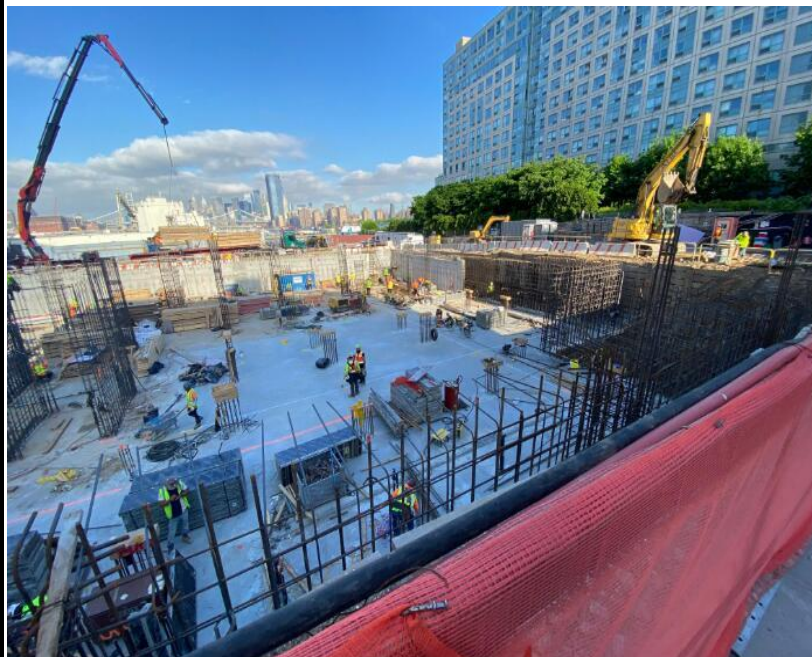


CAMP:
Downwind
Particulates

Dust Levels

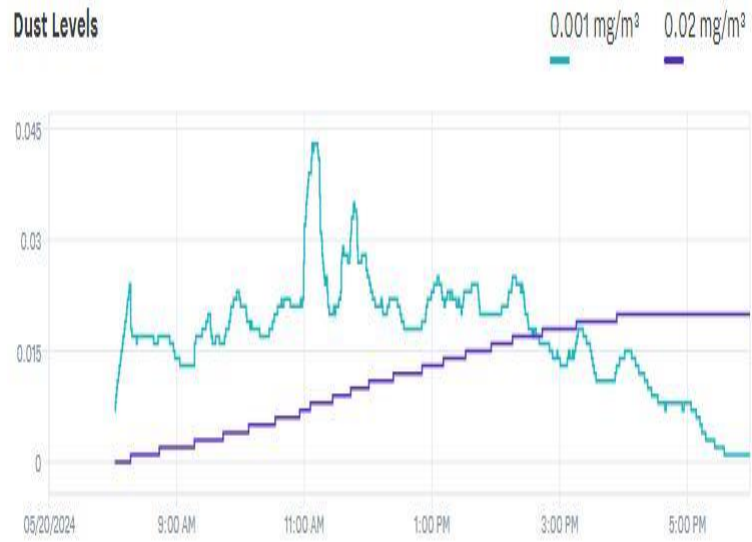


CAMP:
Downwind VOCs


VOC Levels

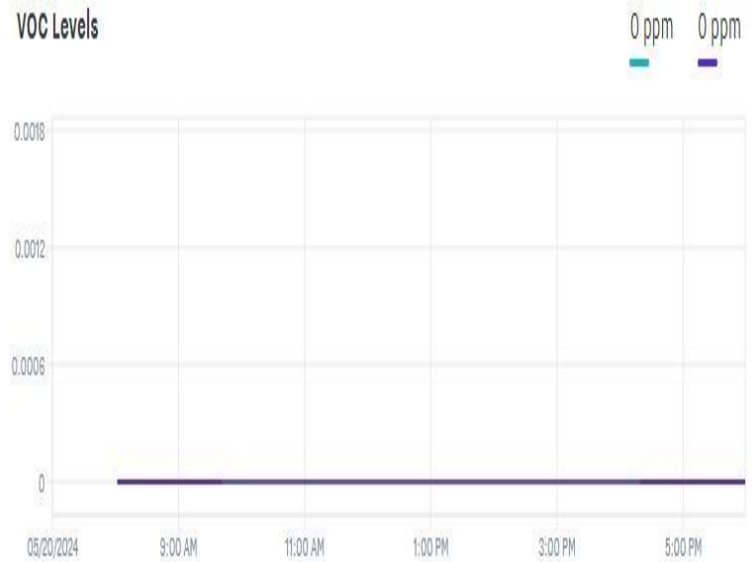

CAMP:
Upwind Particulates

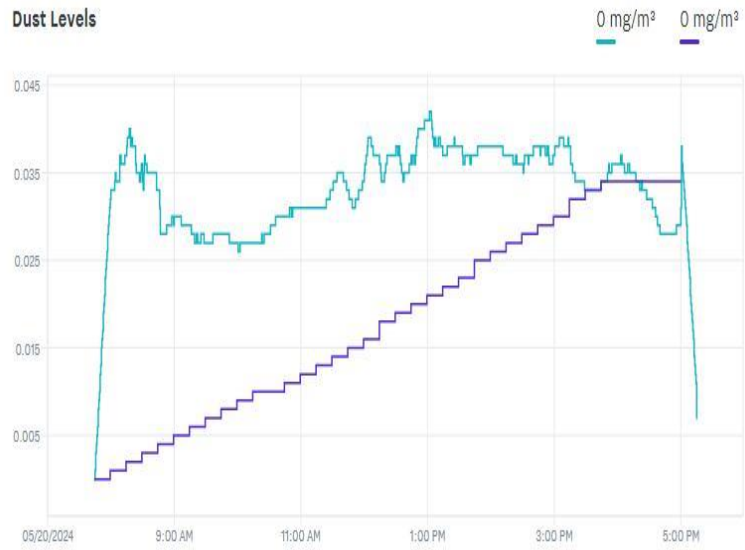

CAMP:
Upwind VOCs

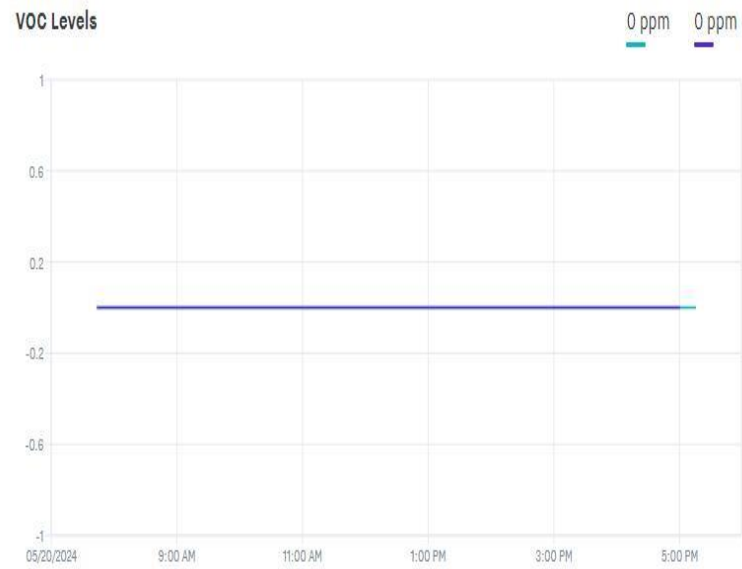

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/20/2024 8:00	5/20/2024 8:10	0.150	0	5	0
DW 2024	5/20/2024 8:10	5/20/2024 8:20	0.150	0.001	5	0
DW 2024	5/20/2024 8:20	5/20/2024 8:30	0.150	0.001	5	0
DW 2024	5/20/2024 8:30	5/20/2024 8:40	0.150	0.001	5	0
DW 2024	5/20/2024 8:40	5/20/2024 8:50	0.150	0.002	5	0
DW 2024	5/20/2024 8:50	5/20/2024 9:00	0.150	0.002	5	0
DW 2024	5/20/2024 9:00	5/20/2024 9:10	0.150	0.002	5	0
DW 2024	5/20/2024 9:10	5/20/2024 9:20	0.150	0.003	5	0
DW 2024	5/20/2024 9:20	5/20/2024 9:30	0.150	0.003	5	0
DW 2024	5/20/2024 9:30	5/20/2024 9:40	0.150	0.003	5	0
DW 2024	5/20/2024 9:40	5/20/2024 9:50	0.150	0.004	5	0
DW 2024	5/20/2024 9:50	5/20/2024 10:00	0.150	0.004	5	0
DW 2024	5/20/2024 10:00	5/20/2024 10:10	0.150	0.005	5	0
DW 2024	5/20/2024 10:10	5/20/2024 10:20	0.150	0.005	5	0
DW 2024	5/20/2024 10:20	5/20/2024 10:30	0.150	0.005	5	0
DW 2024	5/20/2024 10:30	5/20/2024 10:40	0.150	0.006	5	0
DW 2024	5/20/2024 10:40	5/20/2024 10:50	0.150	0.006	5	0
DW 2024	5/20/2024 10:50	5/20/2024 11:00	0.150	0.007	5	0
DW 2024	5/20/2024 11:00	5/20/2024 11:10	0.150	0.008	5	0
DW 2024	5/20/2024 11:10	5/20/2024 11:20	0.150	0.008	5	0
DW 2024	5/20/2024 11:20	5/20/2024 11:30	0.150	0.009	5	0
DW 2024	5/20/2024 11:30	5/20/2024 11:40	0.150	0.009	5	0
DW 2024	5/20/2024 11:40	5/20/2024 11:50	0.150	0.01	5	0
DW 2024	5/20/2024 11:50	5/20/2024 12:00	0.150	0.01	5	0
DW 2024	5/20/2024 12:00	5/20/2024 12:10	0.150	0.011	5	0
DW 2024	5/20/2024 12:10	5/20/2024 12:20	0.150	0.011	5	0
DW 2024	5/20/2024 12:20	5/20/2024 12:30	0.150	0.012	5	0
DW 2024	5/20/2024 12:30	5/20/2024 12:40	0.150	0.012	5	0
DW 2024	5/20/2024 12:40	5/20/2024 12:50	0.150	0.012	5	0
DW 2024	5/20/2024 12:50	5/20/2024 13:00	0.150	0.013	5	0
DW 2024	5/20/2024 13:00	5/20/2024 13:10	0.150	0.013	5	0
DW 2024	5/20/2024 13:10	5/20/2024 13:20	0.150	0.014	5	0
DW 2024	5/20/2024 13:20	5/20/2024 13:30	0.150	0.014	5	0
DW 2024	5/20/2024 13:30	5/20/2024 13:40	0.150	0.015	5	0
DW 2024	5/20/2024 13:40	5/20/2024 13:50	0.150	0.015	5	0
DW 2024	5/20/2024 13:50	5/20/2024 14:00	0.150	0.016	5	0
DW 2024	5/20/2024 14:00	5/20/2024 14:10	0.150	0.016	5	0
DW 2024	5/20/2024 14:10	5/20/2024 14:20	0.150	0.017	5	0
DW 2024	5/20/2024 14:20	5/20/2024 14:30	0.150	0.017	5	0
DW 2024	5/20/2024 14:30	5/20/2024 14:40	0.150	0.017	5	0
DW 2024	5/20/2024 14:40	5/20/2024 14:50	0.150	0.018	5	0
DW 2024	5/20/2024 14:50	5/20/2024 15:00	0.150	0.018	5	0
DW 2024	5/20/2024 15:00	5/20/2024 15:10	0.150	0.018	5	0
DW 2024	5/20/2024 15:10	5/20/2024 15:20	0.150	0.019	5	0
DW 2024	5/20/2024 15:20	5/20/2024 15:30	0.150	0.019	5	0
DW 2024	5/20/2024 15:30	5/20/2024 15:40	0.150	0.019	5	0
DW 2024	5/20/2024 15:40	5/20/2024 15:50	0.150	0.019	5	0
DW 2024	5/20/2024 15:50	5/20/2024 16:00	0.150	0.02	5	0
DW 2024	5/20/2024 16:00	5/20/2024 16:10	0.150	0.02	5	0
DW 2024	5/20/2024 16:10	5/20/2024 16:20	0.150	0.02	5	0
DW 2024	5/20/2024 16:20	5/20/2024 16:30	0.150	0.02	5	0
DW 2024	5/20/2024 16:30	5/20/2024 16:40	0.150	0.02	5	0
DW 2024	5/20/2024 16:40	5/20/2024 16:50	0.150	0.02	5	0
DW 2024	5/20/2024 16:50	5/20/2024 17:00	0.150	0.02	5	0
DW 2024	5/20/2024 17:00	5/20/2024 17:10	0.150	0.02	5	0
DW 2024	5/20/2024 17:10	5/20/2024 17:20	0.150	0.02	5	0
DW 2024	5/20/2024 17:20	5/20/2024 17:30	0.150	0.02	5	0
DW 2024	5/20/2024 17:30	5/20/2024 17:40	0.150	0.02	5	0
DW 2024	5/20/2024 17:40	5/20/2024 17:50	0.150	0.02	5	0
DW 2024	5/20/2024 17:50	5/20/2024 17:59	0.150	0.02	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/20/2024 7:40	5/20/2024 7:50	0.150	0	5	0
UW 2024	5/20/2024 7:50	5/20/2024 8:00	0.150	0.001	5	0
UW 2024	5/20/2024 8:00	5/20/2024 8:10	0.150	0.001	5	0
UW 2024	5/20/2024 8:10	5/20/2024 8:20	0.150	0.002	5	0
UW 2024	5/20/2024 8:20	5/20/2024 8:30	0.150	0.003	5	0
UW 2024	5/20/2024 8:30	5/20/2024 8:40	0.150	0.003	5	0
UW 2024	5/20/2024 8:40	5/20/2024 8:50	0.150	0.004	5	0
UW 2024	5/20/2024 8:50	5/20/2024 9:00	0.150	0.005	5	0
UW 2024	5/20/2024 9:00	5/20/2024 9:10	0.150	0.005	5	0
UW 2024	5/20/2024 9:10	5/20/2024 9:20	0.150	0.006	5	0
UW 2024	5/20/2024 9:20	5/20/2024 9:30	0.150	0.007	5	0
UW 2024	5/20/2024 9:30	5/20/2024 9:40	0.150	0.007	5	0
UW 2024	5/20/2024 9:40	5/20/2024 9:50	0.150	0.008	5	0
UW 2024	5/20/2024 9:50	5/20/2024 10:00	0.150	0.009	5	0
UW 2024	5/20/2024 10:00	5/20/2024 10:10	0.150	0.009	5	0
UW 2024	5/20/2024 10:10	5/20/2024 10:20	0.150	0.01	5	0
UW 2024	5/20/2024 10:20	5/20/2024 10:30	0.150	0.01	5	0
UW 2024	5/20/2024 10:30	5/20/2024 10:40	0.150	0.01	5	0
UW 2024	5/20/2024 10:40	5/20/2024 10:50	0.150	0.011	5	0
UW 2024	5/20/2024 10:50	5/20/2024 11:00	0.150	0.012	5	0
UW 2024	5/20/2024 11:00	5/20/2024 11:10	0.150	0.012	5	0
UW 2024	5/20/2024 11:10	5/20/2024 11:20	0.150	0.013	5	0
UW 2024	5/20/2024 11:20	5/20/2024 11:30	0.150	0.014	5	0
UW 2024	5/20/2024 11:30	5/20/2024 11:40	0.150	0.014	5	0
UW 2024	5/20/2024 11:40	5/20/2024 11:50	0.150	0.015	5	0
UW 2024	5/20/2024 11:50	5/20/2024 12:00	0.150	0.016	5	0
UW 2024	5/20/2024 12:00	5/20/2024 12:10	0.150	0.016	5	0
UW 2024	5/20/2024 12:10	5/20/2024 12:20	0.150	0.018	5	0
UW 2024	5/20/2024 12:20	5/20/2024 12:30	0.150	0.019	5	0
UW 2024	5/20/2024 12:30	5/20/2024 12:40	0.150	0.019	5	0
UW 2024	5/20/2024 12:40	5/20/2024 12:50	0.150	0.02	5	0
UW 2024	5/20/2024 12:50	5/20/2024 13:00	0.150	0.021	5	0
UW 2024	5/20/2024 13:00	5/20/2024 13:10	0.150	0.021	5	0
UW 2024	5/20/2024 13:10	5/20/2024 13:20	0.150	0.022	5	0
UW 2024	5/20/2024 13:20	5/20/2024 13:30	0.150	0.023	5	0
UW 2024	5/20/2024 13:30	5/20/2024 13:40	0.150	0.023	5	0
UW 2024	5/20/2024 13:40	5/20/2024 13:50	0.150	0.025	5	0
UW 2024	5/20/2024 13:50	5/20/2024 14:00	0.150	0.026	5	0
UW 2024	5/20/2024 14:00	5/20/2024 14:10	0.150	0.026	5	0
UW 2024	5/20/2024 14:10	5/20/2024 14:20	0.150	0.027	5	0
UW 2024	5/20/2024 14:20	5/20/2024 14:30	0.150	0.028	5	0
UW 2024	5/20/2024 14:30	5/20/2024 14:40	0.150	0.028	5	0
UW 2024	5/20/2024 14:40	5/20/2024 14:50	0.150	0.029	5	0
UW 2024	5/20/2024 14:50	5/20/2024 15:00	0.150	0.03	5	0
UW 2024	5/20/2024 15:00	5/20/2024 15:10	0.150	0.03	5	0
UW 2024	5/20/2024 15:10	5/20/2024 15:20	0.150	0.032	5	0
UW 2024	5/20/2024 15:20	5/20/2024 15:30	0.150	0.033	5	0
UW 2024	5/20/2024 15:30	5/20/2024 15:40	0.150	0.033	5	0
UW 2024	5/20/2024 15:40	5/20/2024 15:50	0.150	0.034	5	0
UW 2024	5/20/2024 15:50	5/20/2024 16:00	0.150	0.034	5	0
UW 2024	5/20/2024 16:00	5/20/2024 16:10	0.150	0.034	5	0
UW 2024	5/20/2024 16:10	5/20/2024 16:20	0.150	0.034	5	0
UW 2024	5/20/2024 16:20	5/20/2024 16:30	0.150	0.034	5	0
UW 2024	5/20/2024 16:30	5/20/2024 16:40	0.150	0.034	5	0
UW 2024	5/20/2024 16:40	5/20/2024 16:50	0.150	0.034	5	0
UW 2024	5/20/2024 16:50	5/20/2024 17:00	0.150	0.034	5	0
UW 2024	5/20/2024 17:00	5/20/2024 17:10	0.150	0.034	5	0
UW 2024	5/20/2024 17:10	5/20/2024 17:20	0.150	0	5	0
UW 2024	5/20/2024 17:20	5/20/2024 17:30	0.150	0	5	0
UW 2024	5/20/2024 17:30	5/20/2024 17:40	0.150	0	5	0
UW 2024	5/20/2024 17:40	5/20/2024 17:50	0.150	0	5	0
UW 2024	5/20/2024 17:50	5/20/2024 17:59	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/20/2024 7:50	5/20/2024 8:00	0.150	0	5	0
HS South	5/20/2024 8:00	5/20/2024 8:10	0.150	0.001	5	0
HS South	5/20/2024 8:10	5/20/2024 8:20	0.150	0.002	5	0
HS South	5/20/2024 8:20	5/20/2024 8:30	0.150	0.002	5	0
HS South	5/20/2024 8:30	5/20/2024 8:40	0.150	0.004	5	0
HS South	5/20/2024 8:40	5/20/2024 8:50	0.150	0.005	5	0
HS South	5/20/2024 8:50	5/20/2024 9:00	0.150	0.005	5	0
HS South	5/20/2024 9:00	5/20/2024 9:10	0.150	0.006	5	0
HS South	5/20/2024 9:10	5/20/2024 9:20	0.150	0.007	5	0
HS South	5/20/2024 9:20	5/20/2024 9:30	0.150	0.007	5	0
HS South	5/20/2024 9:30	5/20/2024 9:40	0.150	0.008	5	0
HS South	5/20/2024 9:40	5/20/2024 9:50	0.150	0.009	5	0
HS South	5/20/2024 9:50	5/20/2024 10:00	0.150	0.01	5	0
HS South	5/20/2024 10:00	5/20/2024 10:10	0.150	0.01	5	0
HS South	5/20/2024 10:10	5/20/2024 10:20	0.150	0.011	5	0
HS South	5/20/2024 10:20	5/20/2024 10:30	0.150	0.012	5	0
HS South	5/20/2024 10:30	5/20/2024 10:40	0.150	0.016	5	0
HS South	5/20/2024 10:40	5/20/2024 10:50	0.150	0.017	5	0
HS South	5/20/2024 10:50	5/20/2024 11:00	0.150	0.019	5	0
HS South	5/20/2024 11:00	5/20/2024 11:10	0.150	0.02	5	0
HS South	5/20/2024 11:10	5/20/2024 11:20	0.150	0.021	5	0
HS South	5/20/2024 11:20	5/20/2024 11:30	0.150	0.022	5	0
HS South	5/20/2024 11:30	5/20/2024 11:40	0.150	0.023	5	0
HS South	5/20/2024 11:40	5/20/2024 11:50	0.150	0.025	5	0
HS South	5/20/2024 11:50	5/20/2024 12:00	0.150	0.026	5	0
HS South	5/20/2024 12:00	5/20/2024 12:10	0.150	0.027	5	0
HS South	5/20/2024 12:10	5/20/2024 12:20	0.150	0.028	5	0
HS South	5/20/2024 12:20	5/20/2024 12:30	0.150	0.029	5	0
HS South	5/20/2024 12:30	5/20/2024 12:40	0.150	0.03	5	0
HS South	5/20/2024 12:40	5/20/2024 12:50	0.150	0.032	5	0
HS South	5/20/2024 12:50	5/20/2024 13:00	0.150	0.033	5	0
HS South	5/20/2024 13:00	5/20/2024 13:10	0.150	0.034	5	0
HS South	5/20/2024 13:10	5/20/2024 13:20	0.150	0.035	5	0
HS South	5/20/2024 13:20	5/20/2024 13:30	0.150	0.037	5	0
HS South	5/20/2024 13:30	5/20/2024 13:40	0.150	0.038	5	0
HS South	5/20/2024 13:40	5/20/2024 13:50	0.150	0.039	5	0
HS South	5/20/2024 13:50	5/20/2024 14:00	0.150	0.041	5	0
HS South	5/20/2024 14:00	5/20/2024 14:10	0.150	0.042	5	0
HS South	5/20/2024 14:10	5/20/2024 14:20	0.150	0.044	5	0
HS South	5/20/2024 14:20	5/20/2024 14:30	0.150	0.046	5	0
HS South	5/20/2024 14:30	5/20/2024 14:40	0.150	0.047	5	0
HS South	5/20/2024 14:40	5/20/2024 14:50	0.150	0.049	5	0
HS South	5/20/2024 14:50	5/20/2024 15:00	0.150	0.05	5	0
HS South	5/20/2024 15:00	5/20/2024 15:10	0.150	0.051	5	0
HS South	5/20/2024 15:10	5/20/2024 15:20	0.150	0.053	5	0
HS South	5/20/2024 15:20	5/20/2024 15:30	0.150	0.054	5	0
HS South	5/20/2024 15:30	5/20/2024 15:40	0.150	0.055	5	0
HS South	5/20/2024 15:40	5/20/2024 15:50	0.150	0.057	5	0
HS South	5/20/2024 15:50	5/20/2024 16:00	0.150	0.057	5	0
HS South	5/20/2024 16:00	5/20/2024 16:10	0.150	0.057	5	0
HS South	5/20/2024 16:10	5/20/2024 16:20	0.150	0.057	5	0
HS South	5/20/2024 16:20	5/20/2024 16:30	0.150	0.057	5	0
HS South	5/20/2024 16:30	5/20/2024 16:40	0.150	0.057	5	0
HS South	5/20/2024 16:40	5/20/2024 16:50	0.150	0.057	5	0
HS South	5/20/2024 16:50	5/20/2024 17:00	0.150	0.057	5	0
HS South	5/20/2024 17:00	5/20/2024 17:10	0.150	0.057	5	0
HS South	5/20/2024 17:10	5/20/2024 17:20	0.150	0.057	5	0
HS South	5/20/2024 17:20	5/20/2024 17:30	0.150	0.057	5	0
HS South	5/20/2024 17:30	5/20/2024 17:40	0.150	0.057	5	0
HS South	5/20/2024 17:40	5/20/2024 17:50	0.150	0.057	5	0
HS South	5/20/2024 17:50	5/20/2024 17:59	0.150	0.057	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/20/2024 7:30	5/20/2024 7:40	0.150	0.001	5	0
PER1 2024	5/20/2024 7:40	5/20/2024 7:50	0.150	0.002	5	0
PER1 2024	5/20/2024 7:50	5/20/2024 8:00	0.150	0.003	5	0
PER1 2024	5/20/2024 8:00	5/20/2024 8:10	0.150	0.003	5	0
PER1 2024	5/20/2024 8:10	5/20/2024 8:20	0.150	0.003	5	0
PER1 2024	5/20/2024 8:20	5/20/2024 8:30	0.150	0.004	5	0
PER1 2024	5/20/2024 8:30	5/20/2024 8:40	0.150	0.004	5	0
PER1 2024	5/20/2024 8:40	5/20/2024 8:50	0.150	0.005	5	0
PER1 2024	5/20/2024 8:50	5/20/2024 9:00	0.150	0.005	5	0
PER1 2024	5/20/2024 9:00	5/20/2024 9:10	0.150	0.006	5	0
PER1 2024	5/20/2024 9:10	5/20/2024 9:20	0.150	0.006	5	0
PER1 2024	5/20/2024 9:20	5/20/2024 9:30	0.150	0.007	5	0
PER1 2024	5/20/2024 9:30	5/20/2024 9:40	0.150	0.007	5	0
PER1 2024	5/20/2024 9:40	5/20/2024 9:50	0.150	0.008	5	0
PER1 2024	5/20/2024 9:50	5/20/2024 10:00	0.150	0.008	5	0
PER1 2024	5/20/2024 10:00	5/20/2024 10:10	0.150	0.01	5	0
PER1 2024	5/20/2024 10:10	5/20/2024 10:20	0.150	0.01	5	0
PER1 2024	5/20/2024 10:20	5/20/2024 10:30	0.150	0.011	5	0
PER1 2024	5/20/2024 10:30	5/20/2024 10:40	0.150	0.012	5	0
PER1 2024	5/20/2024 10:40	5/20/2024 10:50	0.150	0.014	5	0
PER1 2024	5/20/2024 10:50	5/20/2024 11:00	0.150	0.015	5	0
PER1 2024	5/20/2024 11:00	5/20/2024 11:10	0.150	0.015	5	0
PER1 2024	5/20/2024 11:10	5/20/2024 11:20	0.150	0.016	5	0
PER1 2024	5/20/2024 11:20	5/20/2024 11:30	0.150	0.017	5	0
PER1 2024	5/20/2024 11:30	5/20/2024 11:40	0.150	0.017	5	0
PER1 2024	5/20/2024 11:40	5/20/2024 11:50	0.150	0.018	5	0
PER1 2024	5/20/2024 11:50	5/20/2024 12:00	0.150	0.019	5	0
PER1 2024	5/20/2024 12:00	5/20/2024 12:10	0.150	0.019	5	0
PER1 2024	5/20/2024 12:10	5/20/2024 12:20	0.150	0.02	5	0
PER1 2024	5/20/2024 12:20	5/20/2024 12:30	0.150	0.02	5	0
PER1 2024	5/20/2024 12:30	5/20/2024 12:40	0.150	0.021	5	0
PER1 2024	5/20/2024 12:40	5/20/2024 12:50	0.150	0.021	5	0
PER1 2024	5/20/2024 12:50	5/20/2024 13:00	0.150	0.022	5	0
PER1 2024	5/20/2024 13:00	5/20/2024 13:10	0.150	0.023	5	0
PER1 2024	5/20/2024 13:10	5/20/2024 13:20	0.150	0.024	5	0
PER1 2024	5/20/2024 13:20	5/20/2024 13:30	0.150	0.024	5	0
PER1 2024	5/20/2024 13:30	5/20/2024 13:40	0.150	0.025	5	0
PER1 2024	5/20/2024 13:40	5/20/2024 13:50	0.150	0.026	5	0
PER1 2024	5/20/2024 13:50	5/20/2024 14:00	0.150	0.027	5	0
PER1 2024	5/20/2024 14:00	5/20/2024 14:10	0.150	0.028	5	0
PER1 2024	5/20/2024 14:10	5/20/2024 14:20	0.150	0.028	5	0
PER1 2024	5/20/2024 14:20	5/20/2024 14:30	0.150	0.029	5	0
PER1 2024	5/20/2024 14:30	5/20/2024 14:40	0.150	0.03	5	0
PER1 2024	5/20/2024 14:40	5/20/2024 14:50	0.150	0.031	5	0
PER1 2024	5/20/2024 14:50	5/20/2024 15:00	0.150	0.031	5	0
PER1 2024	5/20/2024 15:00	5/20/2024 15:10	0.150	0.032	5	0
PER1 2024	5/20/2024 15:10	5/20/2024 15:20	0.150	0.032	5	0
PER1 2024	5/20/2024 15:20	5/20/2024 15:30	0.150	0.032	5	0
PER1 2024	5/20/2024 15:30	5/20/2024 15:40	0.150	0.032	5	0
PER1 2024	5/20/2024 15:40	5/20/2024 15:50	0.150	0.032	5	0
PER1 2024	5/20/2024 15:50	5/20/2024 16:00	0.150	0.032	5	0
PER1 2024	5/20/2024 16:00	5/20/2024 16:10	0.150	0.032	5	0
PER1 2024	5/20/2024 16:10	5/20/2024 16:20	0.150	0.032	5	0
PER1 2024	5/20/2024 16:20	5/20/2024 16:30	0.150	0.032	5	0
PER1 2024	5/20/2024 16:30	5/20/2024 16:40	0.150	0.032	5	0
PER1 2024	5/20/2024 16:40	5/20/2024 16:50	0.150	0.032	5	0
PER1 2024	5/20/2024 16:50	5/20/2024 17:00	0.150	0.032	5	0
PER1 2024	5/20/2024 17:00	5/20/2024 17:10	0.150	0.032	5	0
PER1 2024	5/20/2024 17:10	5/20/2024 17:20	0.150	0.032	5	0
PER1 2024	5/20/2024 17:20	5/20/2024 17:30	0.150	0	5	0
PER1 2024	5/20/2024 17:30	5/20/2024 17:40	0.150	0	5	0
PER1 2024	5/20/2024 17:40	5/20/2024 17:50	0.150	0	5	0
PER1 2024	5/20/2024 17:50	5/20/2024 17:59	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/20/2024 8:20	5/20/2024 8:30	0.150	0.001	5	0
PER2 2024	5/20/2024 8:30	5/20/2024 8:40	0.150	0.001	5	0
PER2 2024	5/20/2024 8:40	5/20/2024 8:50	0.150	0.001	5	0
PER2 2024	5/20/2024 8:50	5/20/2024 9:00	0.150	0.001	5	0
PER2 2024	5/20/2024 9:00	5/20/2024 9:10	0.150	0.002	5	0
PER2 2024	5/20/2024 9:10	5/20/2024 9:20	0.150	0.002	5	0
PER2 2024	5/20/2024 9:20	5/20/2024 9:30	0.150	0.002	5	0
PER2 2024	5/20/2024 9:30	5/20/2024 9:40	0.150	0.003	5	0
PER2 2024	5/20/2024 9:40	5/20/2024 9:50	0.150	0.003	5	0
PER2 2024	5/20/2024 9:50	5/20/2024 10:00	0.150	0.005	5	0
PER2 2024	5/20/2024 10:00	5/20/2024 10:10	0.150	0.005	5	0
PER2 2024	5/20/2024 10:10	5/20/2024 10:20	0.150	0.006	5	0
PER2 2024	5/20/2024 10:20	5/20/2024 10:30	0.150	0.006	5	0
PER2 2024	5/20/2024 10:30	5/20/2024 10:40	0.150	0.007	5	0
PER2 2024	5/20/2024 10:40	5/20/2024 10:50	0.150	0.008	5	0
PER2 2024	5/20/2024 10:50	5/20/2024 11:00	0.150	0.008	5	0
PER2 2024	5/20/2024 11:00	5/20/2024 11:10	0.150	0.009	5	0
PER2 2024	5/20/2024 11:10	5/20/2024 11:20	0.150	0.009	5	0
PER2 2024	5/20/2024 11:20	5/20/2024 11:30	0.150	0.01	5	0
PER2 2024	5/20/2024 11:30	5/20/2024 11:40	0.150	0.01	5	0
PER2 2024	5/20/2024 11:40	5/20/2024 11:50	0.150	0.011	5	0
PER2 2024	5/20/2024 11:50	5/20/2024 12:00	0.150	0.012	5	0
PER2 2024	5/20/2024 12:00	5/20/2024 12:10	0.150	0.012	5	0
PER2 2024	5/20/2024 12:10	5/20/2024 12:20	0.150	0.013	5	0
PER2 2024	5/20/2024 12:20	5/20/2024 12:30	0.150	0.013	5	0
PER2 2024	5/20/2024 12:30	5/20/2024 12:40	0.150	0.014	5	0
PER2 2024	5/20/2024 12:40	5/20/2024 12:50	0.150	0.014	5	0
PER2 2024	5/20/2024 12:50	5/20/2024 13:00	0.150	0.014	5	0
PER2 2024	5/20/2024 13:00	5/20/2024 13:10	0.150	0.015	5	0
PER2 2024	5/20/2024 13:10	5/20/2024 13:20	0.150	0.015	5	0
PER2 2024	5/20/2024 13:20	5/20/2024 13:30	0.150	0.016	5	0
PER2 2024	5/20/2024 13:30	5/20/2024 13:40	0.150	0.016	5	0
PER2 2024	5/20/2024 13:40	5/20/2024 13:50	0.150	0.017	5	0
PER2 2024	5/20/2024 13:50	5/20/2024 14:00	0.150	0.017	5	0
PER2 2024	5/20/2024 14:00	5/20/2024 14:10	0.150	0.018	5	0
PER2 2024	5/20/2024 14:10	5/20/2024 14:20	0.150	0.018	5	0
PER2 2024	5/20/2024 14:20	5/20/2024 14:30	0.150	0.019	5	0
PER2 2024	5/20/2024 14:30	5/20/2024 14:40	0.150	0.019	5	0
PER2 2024	5/20/2024 14:40	5/20/2024 14:50	0.150	0.02	5	0
PER2 2024	5/20/2024 14:50	5/20/2024 15:00	0.150	0.02	5	0
PER2 2024	5/20/2024 15:00	5/20/2024 15:10	0.150	0.021	5	0
PER2 2024	5/20/2024 15:10	5/20/2024 15:20	0.150	0.021	5	0
PER2 2024	5/20/2024 15:20	5/20/2024 15:30	0.150	0.022	5	0
PER2 2024	5/20/2024 15:30	5/20/2024 15:40	0.150	0.022	5	0
PER2 2024	5/20/2024 15:40	5/20/2024 15:50	0.150	0.022	5	0
PER2 2024	5/20/2024 15:50	5/20/2024 16:00	0.150	0.023	5	0
PER2 2024	5/20/2024 16:00	5/20/2024 16:10	0.150	0.023	5	0
PER2 2024	5/20/2024 16:10	5/20/2024 16:20	0.150	0.023	5	0
PER2 2024	5/20/2024 16:20	5/20/2024 16:30	0.150	0.023	5	0
PER2 2024	5/20/2024 16:30	5/20/2024 16:40	0.150	0.023	5	0
PER2 2024	5/20/2024 16:40	5/20/2024 16:50	0.150	0.023	5	0
PER2 2024	5/20/2024 16:50	5/20/2024 17:00	0.150	0.023	5	0
PER2 2024	5/20/2024 17:00	5/20/2024 17:10	0.150	0.023	5	0
PER2 2024	5/20/2024 17:10	5/20/2024 17:20	0.150	0.023	5	0
PER2 2024	5/20/2024 17:20	5/20/2024 17:30	0.150	0.023	5	0
PER2 2024	5/20/2024 17:30	5/20/2024 17:40	0.150	0.023	5	0
PER2 2024	5/20/2024 17:40	5/20/2024 17:50	0.150	0.023	5	0
PER2 2024	5/20/2024 17:50	5/20/2024 17:59	0.150	0.023	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/21/2024 Weather: 80 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued minor excavation, rebar and waterproofing installation for the foundation development. 2) ECD continued excavation and backfill in remedial excavation.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	100	0
Total:(CY)	4485	0	8685	1720	4140

Site Layout Map and Excavation Figures

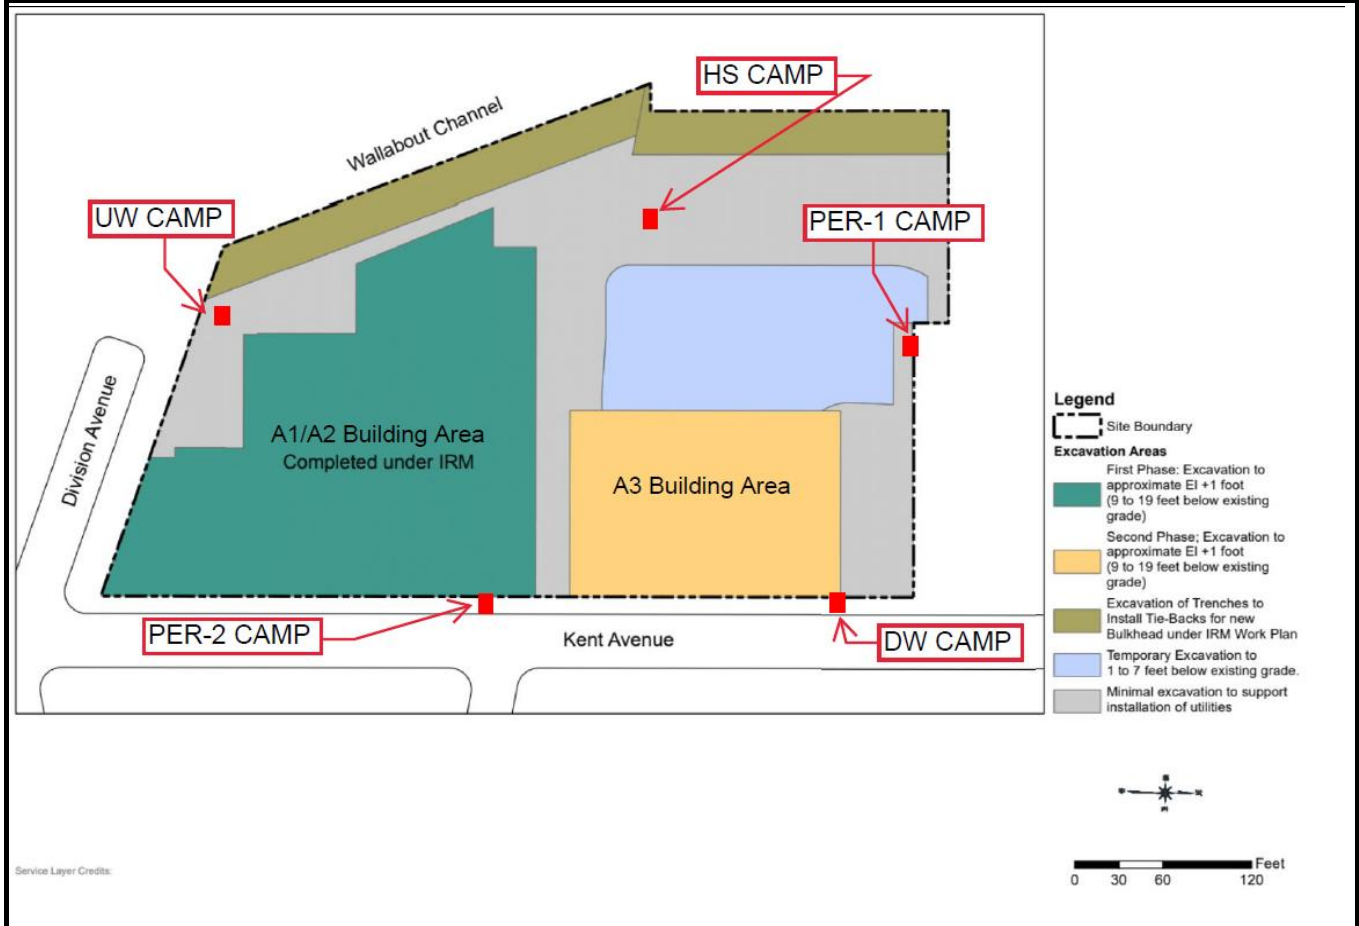

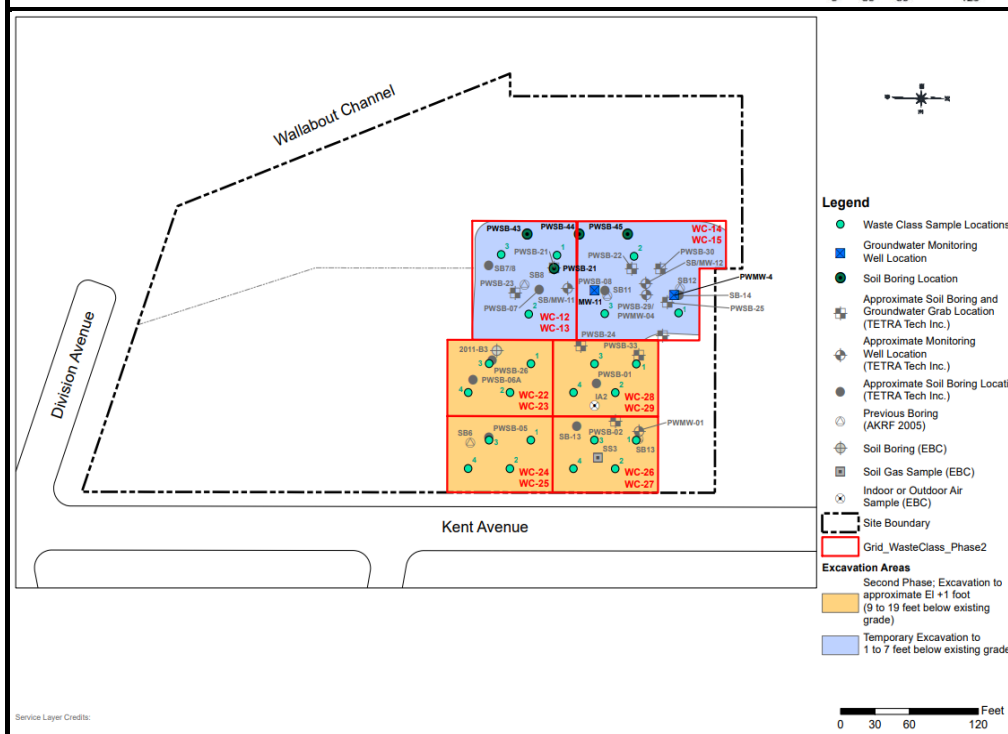
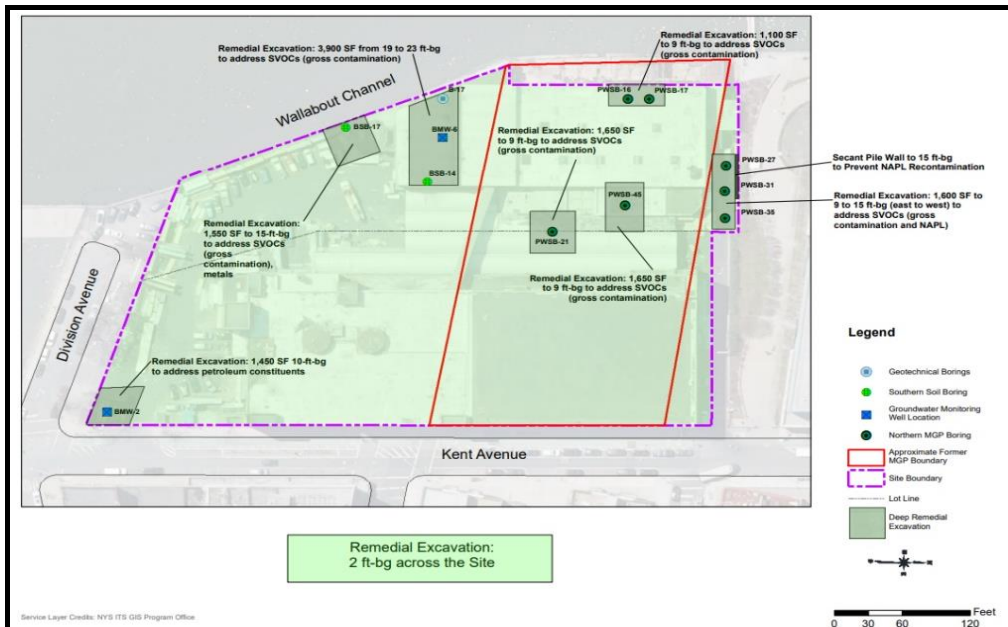


Photo 1:

View of truck loading
with demolished concrete
for off-site disposal.



Photo 2:

View of hotspot facing
west.



Photo 3:
View of Site
conditions facing
northeast.


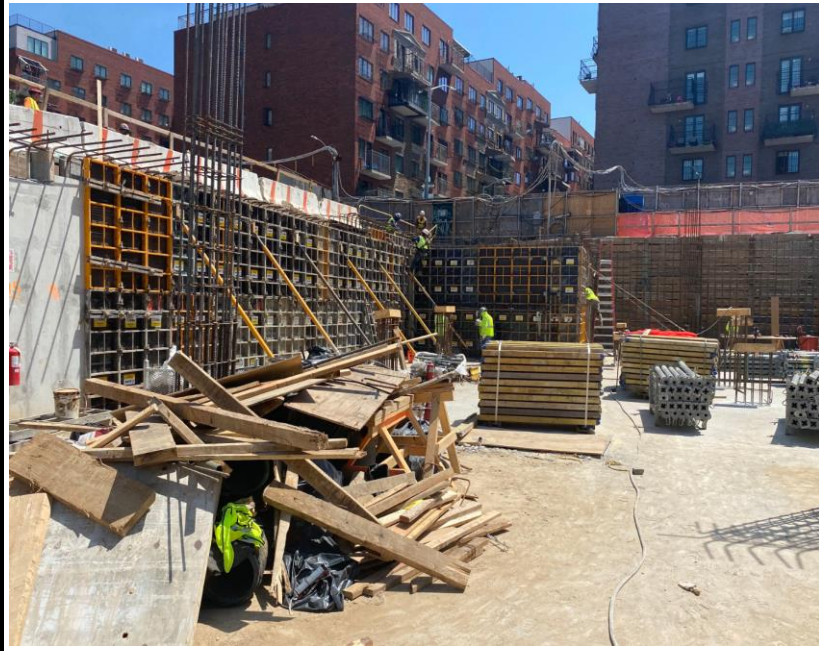


Photo 4:
View of Site
conditions facing
east.



CAMP:
Downwind
Particulates

Dust Levels

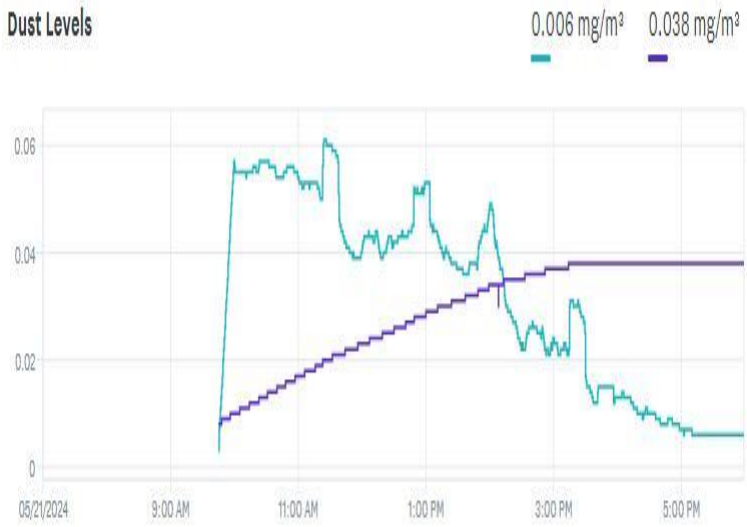


CAMP:
Downwind VOCs


VOC Levels



CAMP:
Upwind Particulates

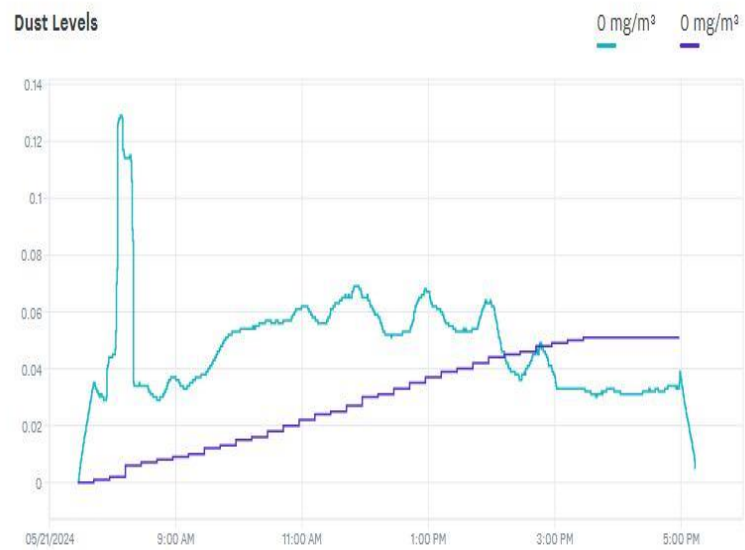

CAMP:
Upwind VOCs

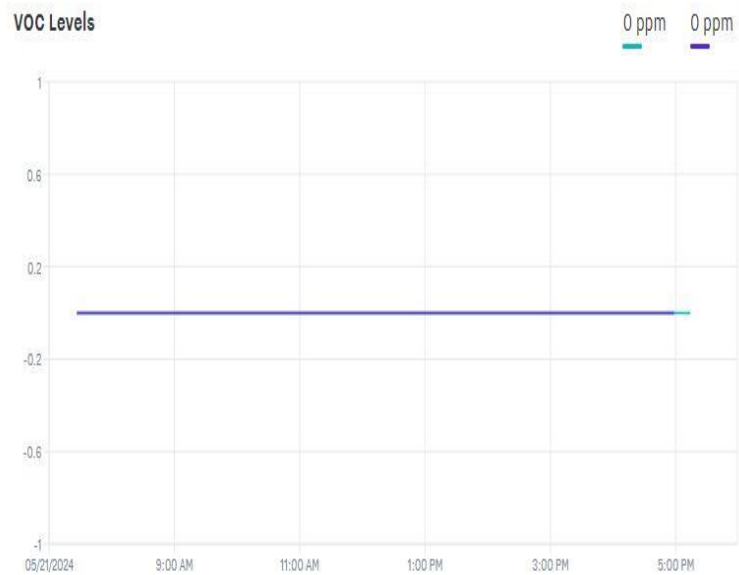

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/21/2024 7:00	5/21/2024 7:10	0.150	0.02	5	0
DW 2024	5/21/2024 7:10	5/21/2024 7:20	0.150	0.02	5	0
DW 2024	5/21/2024 7:20	5/21/2024 7:30	0.150	0.02	5	0
DW 2024	5/21/2024 7:30	5/21/2024 7:40	0.150	0.02	5	0
DW 2024	5/21/2024 7:40	5/21/2024 7:50	0.150	0.02	5	0
DW 2024	5/21/2024 7:50	5/21/2024 8:00	0.150	0.02	5	0
DW 2024	5/21/2024 8:00	5/21/2024 8:10	0.150	0.02	5	0
DW 2024	5/21/2024 8:10	5/21/2024 8:20	0.150	0.02	5	0
DW 2024	5/21/2024 8:20	5/21/2024 8:30	0.150	0.02	5	0
DW 2024	5/21/2024 8:30	5/21/2024 8:40	0.150	0.02	5	0
DW 2024	5/21/2024 8:40	5/21/2024 8:50	0.150	0.02	5	0
DW 2024	5/21/2024 8:50	5/21/2024 9:00	0.150	0.02	5	0
DW 2024	5/21/2024 9:00	5/21/2024 9:10	0.150	0.02	5	0
DW 2024	5/21/2024 9:10	5/21/2024 9:20	0.150	0.02	5	0
DW 2024	5/21/2024 9:20	5/21/2024 9:30	0.150	0.02	5	0
DW 2024	5/21/2024 9:30	5/21/2024 9:40	0.150	0.02	5	0
DW 2024	5/21/2024 9:40	5/21/2024 9:50	0.150	0.009	5	0
DW 2024	5/21/2024 9:50	5/21/2024 10:00	0.150	0.01	5	0
DW 2024	5/21/2024 10:00	5/21/2024 10:10	0.150	0.011	5	0
DW 2024	5/21/2024 10:10	5/21/2024 10:20	0.150	0.012	5	0
DW 2024	5/21/2024 10:20	5/21/2024 10:30	0.150	0.013	5	0
DW 2024	5/21/2024 10:30	5/21/2024 10:40	0.150	0.015	5	0
DW 2024	5/21/2024 10:40	5/21/2024 10:50	0.150	0.016	5	0
DW 2024	5/21/2024 10:50	5/21/2024 11:00	0.150	0.017	5	0
DW 2024	5/21/2024 11:00	5/21/2024 11:10	0.150	0.018	5	0
DW 2024	5/21/2024 11:10	5/21/2024 11:20	0.150	0.019	5	0
DW 2024	5/21/2024 11:20	5/21/2024 11:30	0.150	0.02	5	0
DW 2024	5/21/2024 11:30	5/21/2024 11:40	0.150	0.021	5	0
DW 2024	5/21/2024 11:40	5/21/2024 11:50	0.150	0.022	5	0
DW 2024	5/21/2024 11:50	5/21/2024 12:00	0.150	0.023	5	0
DW 2024	5/21/2024 12:00	5/21/2024 12:10	0.150	0.024	5	0
DW 2024	5/21/2024 12:10	5/21/2024 12:20	0.150	0.025	5	0
DW 2024	5/21/2024 12:20	5/21/2024 12:30	0.150	0.025	5	0
DW 2024	5/21/2024 12:30	5/21/2024 12:40	0.150	0.026	5	0
DW 2024	5/21/2024 12:40	5/21/2024 12:50	0.150	0.028	5	0
DW 2024	5/21/2024 12:50	5/21/2024 13:00	0.150	0.029	5	0
DW 2024	5/21/2024 13:00	5/21/2024 13:10	0.150	0.029	5	0
DW 2024	5/21/2024 13:10	5/21/2024 13:20	0.150	0.03	5	0
DW 2024	5/21/2024 13:20	5/21/2024 13:30	0.150	0.031	5	0
DW 2024	5/21/2024 13:30	5/21/2024 13:40	0.150	0.032	5	0
DW 2024	5/21/2024 13:40	5/21/2024 13:50	0.150	0.033	5	0
DW 2024	5/21/2024 13:50	5/21/2024 14:00	0.150	0.034	5	0
DW 2024	5/21/2024 14:00	5/21/2024 14:10	0.150	0.034	5	0
DW 2024	5/21/2024 14:10	5/21/2024 14:20	0.150	0.035	5	0
DW 2024	5/21/2024 14:20	5/21/2024 14:30	0.150	0.035	5	0
DW 2024	5/21/2024 14:30	5/21/2024 14:40	0.150	0.036	5	0
DW 2024	5/21/2024 14:40	5/21/2024 14:50	0.150	0.036	5	0
DW 2024	5/21/2024 14:50	5/21/2024 15:00	0.150	0.037	5	0
DW 2024	5/21/2024 15:00	5/21/2024 15:10	0.150	0.037	5	0
DW 2024	5/21/2024 15:10	5/21/2024 15:20	0.150	0.038	5	0
DW 2024	5/21/2024 15:20	5/21/2024 15:30	0.150	0.038	5	0
DW 2024	5/21/2024 15:30	5/21/2024 15:40	0.150	0.038	5	0
DW 2024	5/21/2024 15:40	5/21/2024 15:50	0.150	0.038	5	0
DW 2024	5/21/2024 15:50	5/21/2024 16:00	0.150	0.038	5	0
DW 2024	5/21/2024 16:00	5/21/2024 16:10	0.150	0.038	5	0
DW 2024	5/21/2024 16:10	5/21/2024 16:20	0.150	0.038	5	0
DW 2024	5/21/2024 16:20	5/21/2024 16:30	0.150	0.038	5	0
DW 2024	5/21/2024 16:30	5/21/2024 16:40	0.150	0.038	5	0
DW 2024	5/21/2024 16:40	5/21/2024 16:50	0.150	0.038	5	0
DW 2024	5/21/2024 16:50	5/21/2024 17:00	0.150	0.038	5	0
DW 2024	5/21/2024 17:00	5/21/2024 17:10	0.150	0.038	5	0
DW 2024	5/21/2024 17:10	5/21/2024 17:20	0.150	0.038	5	0
DW 2024	5/21/2024 17:20	5/21/2024 17:30	0.150	0.038	5	0
DW 2024	5/21/2024 17:30	5/21/2024 17:40	0.150	0.038	5	0
DW 2024	5/21/2024 17:40	5/21/2024 17:50	0.150	0.038	5	0
DW 2024	5/21/2024 17:50	5/21/2024 17:59	0.150	0.038	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/21/2024 7:00	5/21/2024 7:10	0.150	0	5	0
UW 2024	5/21/2024 7:10	5/21/2024 7:20	0.150	0	5	0
UW 2024	5/21/2024 7:20	5/21/2024 7:30	0.150	0	5	0
UW 2024	5/21/2024 7:30	5/21/2024 7:40	0.150	0	5	0
UW 2024	5/21/2024 7:40	5/21/2024 7:50	0.150	0.001	5	0
UW 2024	5/21/2024 7:50	5/21/2024 8:00	0.150	0.002	5	0
UW 2024	5/21/2024 8:00	5/21/2024 8:10	0.150	0.002	5	0
UW 2024	5/21/2024 8:10	5/21/2024 8:20	0.150	0.006	5	0
UW 2024	5/21/2024 8:20	5/21/2024 8:30	0.150	0.007	5	0
UW 2024	5/21/2024 8:30	5/21/2024 8:40	0.150	0.007	5	0
UW 2024	5/21/2024 8:40	5/21/2024 8:50	0.150	0.008	5	0
UW 2024	5/21/2024 8:50	5/21/2024 9:00	0.150	0.009	5	0
UW 2024	5/21/2024 9:00	5/21/2024 9:10	0.150	0.009	5	0
UW 2024	5/21/2024 9:10	5/21/2024 9:20	0.150	0.01	5	0
UW 2024	5/21/2024 9:20	5/21/2024 9:30	0.150	0.012	5	0
UW 2024	5/21/2024 9:30	5/21/2024 9:40	0.150	0.012	5	0
UW 2024	5/21/2024 9:40	5/21/2024 9:50	0.150	0.013	5	0
UW 2024	5/21/2024 9:50	5/21/2024 10:00	0.150	0.015	5	0
UW 2024	5/21/2024 10:00	5/21/2024 10:10	0.150	0.015	5	0
UW 2024	5/21/2024 10:10	5/21/2024 10:20	0.150	0.016	5	0
UW 2024	5/21/2024 10:20	5/21/2024 10:30	0.150	0.018	5	0
UW 2024	5/21/2024 10:30	5/21/2024 10:40	0.150	0.018	5	0
UW 2024	5/21/2024 10:40	5/21/2024 10:50	0.150	0.02	5	0
UW 2024	5/21/2024 10:50	5/21/2024 11:00	0.150	0.022	5	0
UW 2024	5/21/2024 11:00	5/21/2024 11:10	0.150	0.022	5	0
UW 2024	5/21/2024 11:10	5/21/2024 11:20	0.150	0.024	5	0
UW 2024	5/21/2024 11:20	5/21/2024 11:30	0.150	0.025	5	0
UW 2024	5/21/2024 11:30	5/21/2024 11:40	0.150	0.025	5	0
UW 2024	5/21/2024 11:40	5/21/2024 11:50	0.150	0.027	5	0
UW 2024	5/21/2024 11:50	5/21/2024 12:00	0.150	0.03	5	0
UW 2024	5/21/2024 12:00	5/21/2024 12:10	0.150	0.03	5	0
UW 2024	5/21/2024 12:10	5/21/2024 12:20	0.150	0.031	5	0
UW 2024	5/21/2024 12:20	5/21/2024 12:30	0.150	0.033	5	0
UW 2024	5/21/2024 12:30	5/21/2024 12:40	0.150	0.033	5	0
UW 2024	5/21/2024 12:40	5/21/2024 12:50	0.150	0.035	5	0
UW 2024	5/21/2024 12:50	5/21/2024 13:00	0.150	0.037	5	0
UW 2024	5/21/2024 13:00	5/21/2024 13:10	0.150	0.037	5	0
UW 2024	5/21/2024 13:10	5/21/2024 13:20	0.150	0.039	5	0
UW 2024	5/21/2024 13:20	5/21/2024 13:30	0.150	0.04	5	0
UW 2024	5/21/2024 13:30	5/21/2024 13:40	0.150	0.04	5	0
UW 2024	5/21/2024 13:40	5/21/2024 13:50	0.150	0.042	5	0
UW 2024	5/21/2024 13:50	5/21/2024 14:00	0.150	0.044	5	0
UW 2024	5/21/2024 14:00	5/21/2024 14:10	0.150	0.044	5	0
UW 2024	5/21/2024 14:10	5/21/2024 14:20	0.150	0.045	5	0
UW 2024	5/21/2024 14:20	5/21/2024 14:30	0.150	0.046	5	0
UW 2024	5/21/2024 14:30	5/21/2024 14:40	0.150	0.046	5	0
UW 2024	5/21/2024 14:40	5/21/2024 14:50	0.150	0.048	5	0
UW 2024	5/21/2024 14:50	5/21/2024 15:00	0.150	0.049	5	0
UW 2024	5/21/2024 15:00	5/21/2024 15:10	0.150	0.049	5	0
UW 2024	5/21/2024 15:10	5/21/2024 15:20	0.150	0.05	5	0
UW 2024	5/21/2024 15:20	5/21/2024 15:30	0.150	0.051	5	0
UW 2024	5/21/2024 15:30	5/21/2024 15:40	0.150	0.051	5	0
UW 2024	5/21/2024 15:40	5/21/2024 15:50	0.150	0.051	5	0
UW 2024	5/21/2024 15:50	5/21/2024 16:00	0.150	0.051	5	0
UW 2024	5/21/2024 16:00	5/21/2024 16:10	0.150	0.051	5	0
UW 2024	5/21/2024 16:10	5/21/2024 16:20	0.150	0.051	5	0
UW 2024	5/21/2024 16:20	5/21/2024 16:30	0.150	0.051	5	0
UW 2024	5/21/2024 16:30	5/21/2024 16:40	0.150	0.051	5	0
UW 2024	5/21/2024 16:40	5/21/2024 16:50	0.150	0.051	5	0
UW 2024	5/21/2024 16:50	5/21/2024 17:00	0.150	0.051	5	0
UW 2024	5/21/2024 17:00	5/21/2024 17:10	0.150	0	5	0
UW 2024	5/21/2024 17:10	5/21/2024 17:20	0.150	0	5	0
UW 2024	5/21/2024 17:20	5/21/2024 17:30	0.150	0	5	0
UW 2024	5/21/2024 17:30	5/21/2024 17:40	0.150	0	5	0
UW 2024	5/21/2024 17:40	5/21/2024 17:50	0.150	0	5	0
UW 2024	5/21/2024 17:50	5/21/2024 17:59	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/21/2024 7:00	5/21/2024 7:10	0.150	0.057	5	0
HS South	5/21/2024 7:10	5/21/2024 7:20	0.150	0.057	5	0
HS South	5/21/2024 7:20	5/21/2024 7:30	0.150	0.057	5	0
HS South	5/21/2024 7:30	5/21/2024 7:40	0.150	0.057	5	0
HS South	5/21/2024 7:40	5/21/2024 7:50	0.150	0.057	5	0
HS South	5/21/2024 7:50	5/21/2024 8:00	0.150	0	5	0
HS South	5/21/2024 8:00	5/21/2024 8:10	0.150	0	5	0
HS South	5/21/2024 8:10	5/21/2024 8:20	0.150	0.001	5	0
HS South	5/21/2024 8:20	5/21/2024 8:30	0.150	0.002	5	0
HS South	5/21/2024 8:30	5/21/2024 8:40	0.150	0.003	5	0
HS South	5/21/2024 8:40	5/21/2024 8:50	0.150	0.004	5	0
HS South	5/21/2024 8:50	5/21/2024 9:00	0.150	0.005	5	0
HS South	5/21/2024 9:00	5/21/2024 9:10	0.150	0.006	5	0
HS South	5/21/2024 9:10	5/21/2024 9:20	0.150	0.009	5	0
HS South	5/21/2024 9:20	5/21/2024 9:30	0.150	0.01	5	0
HS South	5/21/2024 9:30	5/21/2024 9:40	0.150	0.012	5	0
HS South	5/21/2024 9:40	5/21/2024 9:50	0.150	0.016	5	0
HS South	5/21/2024 9:50	5/21/2024 10:00	0.150	0.021	5	0
HS South	5/21/2024 10:00	5/21/2024 10:10	0.150	0.022	5	0
HS South	5/21/2024 10:10	5/21/2024 10:20	0.150	0.024	5	0
HS South	5/21/2024 10:20	5/21/2024 10:30	0.150	0.026	5	0
HS South	5/21/2024 10:30	5/21/2024 10:40	0.150	0.027	5	0
HS South	5/21/2024 10:40	5/21/2024 10:50	0.150	0.029	5	0
HS South	5/21/2024 10:50	5/21/2024 11:00	0.150	0.032	5	0
HS South	5/21/2024 11:00	5/21/2024 11:10	0.150	0.034	5	0
HS South	5/21/2024 11:10	5/21/2024 11:20	0.150	0.036	5	0
HS South	5/21/2024 11:20	5/21/2024 11:30	0.150	0.038	5	0
HS South	5/21/2024 11:30	5/21/2024 11:40	0.150	0.041	5	0
HS South	5/21/2024 11:40	5/21/2024 11:50	0.150	0.043	5	0
HS South	5/21/2024 11:50	5/21/2024 12:00	0.150	0.045	5	0
HS South	5/21/2024 12:00	5/21/2024 12:10	0.150	0.047	5	0
HS South	5/21/2024 12:10	5/21/2024 12:20	0.150	0.048	5	0
HS South	5/21/2024 12:20	5/21/2024 12:30	0.150	0.05	5	0
HS South	5/21/2024 12:30	5/21/2024 12:40	0.150	0.052	5	0
HS South	5/21/2024 12:40	5/21/2024 12:50	0.150	0.055	5	0
HS South	5/21/2024 12:50	5/21/2024 13:00	0.150	0.057	5	0
HS South	5/21/2024 13:00	5/21/2024 13:10	0.150	0.059	5	0
HS South	5/21/2024 13:10	5/21/2024 13:20	0.150	0.062	5	0
HS South	5/21/2024 13:20	5/21/2024 13:30	0.150	0.064	5	0
HS South	5/21/2024 13:30	5/21/2024 13:40	0.150	0.065	5	0
HS South	5/21/2024 13:40	5/21/2024 13:50	0.150	0.067	5	0
HS South	5/21/2024 13:50	5/21/2024 14:00	0.150	0.069	5	0
HS South	5/21/2024 14:00	5/21/2024 14:10	0.150	0.071	5	0
HS South	5/21/2024 14:10	5/21/2024 14:20	0.150	0.072	5	0
HS South	5/21/2024 14:20	5/21/2024 14:30	0.150	0.074	5	0
HS South	5/21/2024 14:30	5/21/2024 14:40	0.150	0.076	5	0
HS South	5/21/2024 14:40	5/21/2024 14:50	0.150	0.078	5	0
HS South	5/21/2024 14:50	5/21/2024 15:00	0.150	0.08	5	0
HS South	5/21/2024 15:00	5/21/2024 15:10	0.150	0.082	5	0
HS South	5/21/2024 15:10	5/21/2024 15:20	0.150	0.084	5	0
HS South	5/21/2024 15:20	5/21/2024 15:30	0.150	0.085	5	0
HS South	5/21/2024 15:30	5/21/2024 15:40	0.150	0.087	5	0
HS South	5/21/2024 15:40	5/21/2024 15:50	0.150	0.089	5	0
HS South	5/21/2024 15:50	5/21/2024 16:00	0.150	0.091	5	0
HS South	5/21/2024 16:00	5/21/2024 16:10	0.150	0.091	5	0
HS South	5/21/2024 16:10	5/21/2024 16:20	0.150	0.091	5	0
HS South	5/21/2024 16:20	5/21/2024 16:30	0.150	0.091	5	0
HS South	5/21/2024 16:30	5/21/2024 16:40	0.150	0.091	5	0
HS South	5/21/2024 16:40	5/21/2024 16:50	0.150	0.091	5	0
HS South	5/21/2024 16:50	5/21/2024 17:00	0.150	0.091	5	0
HS South	5/21/2024 17:00	5/21/2024 17:10	0.150	0.091	5	0
HS South	5/21/2024 17:10	5/21/2024 17:20	0.150	0.091	5	0
HS South	5/21/2024 17:20	5/21/2024 17:30	0.150	0.091	5	0
HS South	5/21/2024 17:30	5/21/2024 17:40	0.150	0.091	5	0
HS South	5/21/2024 17:40	5/21/2024 17:50	0.150	0.091	5	0
HS South	5/21/2024 17:50	5/21/2024 17:59	0.150	0.091	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/21/2024 7:00	5/21/2024 7:10	0.150	0	5	0
PER1 2024	5/21/2024 7:10	5/21/2024 7:20	0.150	0	5	0
PER1 2024	5/21/2024 7:20	5/21/2024 7:30	0.150	0	5	0
PER1 2024	5/21/2024 7:30	5/21/2024 7:40	0.150	0	5	0
PER1 2024	5/21/2024 7:40	5/21/2024 7:50	0.150	0	5	0
PER1 2024	5/21/2024 7:50	5/21/2024 8:00	0.150	0	5	0
PER1 2024	5/21/2024 8:00	5/21/2024 8:10	0.150	0	5	0
PER1 2024	5/21/2024 8:10	5/21/2024 8:20	0.150	0	5	0
PER1 2024	5/21/2024 8:20	5/21/2024 8:30	0.150	0	5	0
PER1 2024	5/21/2024 8:30	5/21/2024 8:40	0.150	0	5	0
PER1 2024	5/21/2024 8:40	5/21/2024 8:50	0.150	0.001	5	0
PER1 2024	5/21/2024 8:50	5/21/2024 9:00	0.150	0.001	5	0
PER1 2024	5/21/2024 9:00	5/21/2024 9:10	0.150	0.001	5	0
PER1 2024	5/21/2024 9:10	5/21/2024 9:20	0.150	0.001	5	0
PER1 2024	5/21/2024 9:20	5/21/2024 9:30	0.150	0.001	5	0
PER1 2024	5/21/2024 9:30	5/21/2024 9:40	0.150	0.002	5	0
PER1 2024	5/21/2024 9:40	5/21/2024 9:50	0.150	0.002	5	0
PER1 2024	5/21/2024 9:50	5/21/2024 10:00	0.150	0.003	5	0
PER1 2024	5/21/2024 10:00	5/21/2024 10:10	0.150	0.004	5	0
PER1 2024	5/21/2024 10:10	5/21/2024 10:20	0.150	0.004	5	0
PER1 2024	5/21/2024 10:20	5/21/2024 10:30	0.150	0.005	5	0
PER1 2024	5/21/2024 10:30	5/21/2024 10:40	0.150	0.006	5	0
PER1 2024	5/21/2024 10:40	5/21/2024 10:50	0.150	0.006	5	0
PER1 2024	5/21/2024 10:50	5/21/2024 11:00	0.150	0.007	5	0
PER1 2024	5/21/2024 11:00	5/21/2024 11:10	0.150	0.008	5	0
PER1 2024	5/21/2024 11:10	5/21/2024 11:20	0.150	0.009	5	0
PER1 2024	5/21/2024 11:20	5/21/2024 11:30	0.150	0.01	5	0
PER1 2024	5/21/2024 11:30	5/21/2024 11:40	0.150	0.01	5	0
PER1 2024	5/21/2024 11:40	5/21/2024 11:50	0.150	0.011	5	0
PER1 2024	5/21/2024 11:50	5/21/2024 12:00	0.150	0.012	5	0
PER1 2024	5/21/2024 12:00	5/21/2024 12:10	0.150	0.012	5	0
PER1 2024	5/21/2024 12:10	5/21/2024 12:20	0.150	0.012	5	0
PER1 2024	5/21/2024 12:20	5/21/2024 12:30	0.150	0.012	5	0
PER1 2024	5/21/2024 12:30	5/21/2024 12:40	0.150	0.012	5	0
PER1 2024	5/21/2024 12:40	5/21/2024 12:50	0.150	0.012	5	0
PER1 2024	5/21/2024 12:50	5/21/2024 13:00	0.150	0.012	5	0
PER1 2024	5/21/2024 13:00	5/21/2024 13:10	0.150	0.012	5	0
PER1 2024	5/21/2024 13:10	5/21/2024 13:20	0.150	0.012	5	0
PER1 2024	5/21/2024 13:20	5/21/2024 13:30	0.150	0.012	5	0
PER1 2024	5/21/2024 13:30	5/21/2024 13:40	0.150	0.012	5	0
PER1 2024	5/21/2024 13:40	5/21/2024 13:50	0.150	0.012	5	0
PER1 2024	5/21/2024 13:50	5/21/2024 14:00	0.150	0.012	5	0
PER1 2024	5/21/2024 14:00	5/21/2024 14:10	0.150	0.012	5	0
PER1 2024	5/21/2024 14:10	5/21/2024 14:20	0.150	0.012	5	0
PER1 2024	5/21/2024 14:20	5/21/2024 14:30	0.150	0.012	5	0
PER1 2024	5/21/2024 14:30	5/21/2024 14:40	0.150	0.012	5	0
PER1 2024	5/21/2024 14:40	5/21/2024 14:50	0.150	0.012	5	0
PER1 2024	5/21/2024 14:50	5/21/2024 15:00	0.150	0.012	5	0
PER1 2024	5/21/2024 15:00	5/21/2024 15:10	0.150	0.012	5	0
PER1 2024	5/21/2024 15:10	5/21/2024 15:20	0.150	0.012	5	0
PER1 2024	5/21/2024 15:20	5/21/2024 15:30	0.150	0.012	5	0
PER1 2024	5/21/2024 15:30	5/21/2024 15:40	0.150	0.012	5	0
PER1 2024	5/21/2024 15:40	5/21/2024 15:50	0.150	0.012	5	0
PER1 2024	5/21/2024 15:50	5/21/2024 16:00	0.150	0.012	5	0
PER1 2024	5/21/2024 16:00	5/21/2024 16:10	0.150	0.012	5	0
PER1 2024	5/21/2024 16:10	5/21/2024 16:20	0.150	0.012	5	0
PER1 2024	5/21/2024 16:20	5/21/2024 16:30	0.150	0.012	5	0
PER1 2024	5/21/2024 16:30	5/21/2024 16:40	0.150	0.012	5	0
PER1 2024	5/21/2024 16:40	5/21/2024 16:50	0.150	0.012	5	0
PER1 2024	5/21/2024 16:50	5/21/2024 17:00	0.150	0.012	5	0
PER1 2024	5/21/2024 17:00	5/21/2024 17:10	0.150	0.012	5	0
PER1 2024	5/21/2024 17:10	5/21/2024 17:20	0.150	0.012	5	0
PER1 2024	5/21/2024 17:20	5/21/2024 17:30	0.150	0.012	5	0
PER1 2024	5/21/2024 17:30	5/21/2024 17:40	0.150	0.012	5	0
PER1 2024	5/21/2024 17:40	5/21/2024 17:50	0.150	0.012	5	0
PER1 2024	5/21/2024 17:50	5/21/2024 17:59	0.150	0.012	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/21/2024 7:00	5/21/2024 7:10	0.150	0.023	5	0
PER2 2024	5/21/2024 7:10	5/21/2024 7:20	0.150	0.023	5	0
PER2 2024	5/21/2024 7:20	5/21/2024 7:30	0.150	0	5	0
PER2 2024	5/21/2024 7:30	5/21/2024 7:40	0.150	0.001	5	0
PER2 2024	5/21/2024 7:40	5/21/2024 7:50	0.150	0.001	5	0
PER2 2024	5/21/2024 7:50	5/21/2024 8:00	0.150	0.002	5	0
PER2 2024	5/21/2024 8:00	5/21/2024 8:10	0.150	0.002	5	0
PER2 2024	5/21/2024 8:10	5/21/2024 8:20	0.150	0.002	5	0
PER2 2024	5/21/2024 8:20	5/21/2024 8:30	0.150	0.003	5	0
PER2 2024	5/21/2024 8:30	5/21/2024 8:40	0.150	0.003	5	0
PER2 2024	5/21/2024 8:40	5/21/2024 8:50	0.150	0.004	5	0
PER2 2024	5/21/2024 8:50	5/21/2024 9:00	0.150	0.005	5	0
PER2 2024	5/21/2024 9:00	5/21/2024 9:10	0.150	0.005	5	0
PER2 2024	5/21/2024 9:10	5/21/2024 9:20	0.150	0.006	5	0
PER2 2024	5/21/2024 9:20	5/21/2024 9:30	0.150	0.006	5	0
PER2 2024	5/21/2024 9:30	5/21/2024 9:40	0.150	0.007	5	0
PER2 2024	5/21/2024 9:40	5/21/2024 9:50	0.150	0.008	5	0
PER2 2024	5/21/2024 9:50	5/21/2024 10:00	0.150	0.009	5	0
PER2 2024	5/21/2024 10:00	5/21/2024 10:10	0.150	0.01	5	0
PER2 2024	5/21/2024 10:10	5/21/2024 10:20	0.150	0.011	5	0
PER2 2024	5/21/2024 10:20	5/21/2024 10:30	0.150	0.012	5	0
PER2 2024	5/21/2024 10:30	5/21/2024 10:40	0.150	0.013	5	0
PER2 2024	5/21/2024 10:40	5/21/2024 10:50	0.150	0.014	5	0
PER2 2024	5/21/2024 10:50	5/21/2024 11:00	0.150	0.015	5	0
PER2 2024	5/21/2024 11:00	5/21/2024 11:10	0.150	0.017	5	0
PER2 2024	5/21/2024 11:10	5/21/2024 11:20	0.150	0.018	5	0
PER2 2024	5/21/2024 11:20	5/21/2024 11:30	0.150	0.019	5	0
PER2 2024	5/21/2024 11:30	5/21/2024 11:40	0.150	0.02	5	0
PER2 2024	5/21/2024 11:40	5/21/2024 11:50	0.150	0.021	5	0
PER2 2024	5/21/2024 11:50	5/21/2024 12:00	0.150	0.022	5	0
PER2 2024	5/21/2024 12:00	5/21/2024 12:10	0.150	0.023	5	0
PER2 2024	5/21/2024 12:10	5/21/2024 12:20	0.150	0.024	5	0
PER2 2024	5/21/2024 12:20	5/21/2024 12:30	0.150	0.025	5	0
PER2 2024	5/21/2024 12:30	5/21/2024 12:40	0.150	0.025	5	0
PER2 2024	5/21/2024 12:40	5/21/2024 12:50	0.150	0.026	5	0
PER2 2024	5/21/2024 12:50	5/21/2024 13:00	0.150	0.027	5	0
PER2 2024	5/21/2024 13:00	5/21/2024 13:10	0.150	0.028	5	0
PER2 2024	5/21/2024 13:10	5/21/2024 13:20	0.150	0.029	5	0
PER2 2024	5/21/2024 13:20	5/21/2024 13:30	0.150	0.03	5	0
PER2 2024	5/21/2024 13:30	5/21/2024 13:40	0.150	0.031	5	0
PER2 2024	5/21/2024 13:40	5/21/2024 13:50	0.150	0.032	5	0
PER2 2024	5/21/2024 13:50	5/21/2024 14:00	0.150	0.034	5	0
PER2 2024	5/21/2024 14:00	5/21/2024 14:10	0.150	0.034	5	0
PER2 2024	5/21/2024 14:10	5/21/2024 14:20	0.150	0.035	5	0
PER2 2024	5/21/2024 14:20	5/21/2024 14:30	0.150	0.035	5	0
PER2 2024	5/21/2024 14:30	5/21/2024 14:40	0.150	0.036	5	0
PER2 2024	5/21/2024 14:40	5/21/2024 14:50	0.150	0.036	5	0
PER2 2024	5/21/2024 14:50	5/21/2024 15:00	0.150	0.037	5	0
PER2 2024	5/21/2024 15:00	5/21/2024 15:10	0.150	0.037	5	0
PER2 2024	5/21/2024 15:10	5/21/2024 15:20	0.150	0.038	5	0
PER2 2024	5/21/2024 15:20	5/21/2024 15:30	0.150	0.038	5	0
PER2 2024	5/21/2024 15:30	5/21/2024 15:40	0.150	0.038	5	0
PER2 2024	5/21/2024 15:40	5/21/2024 15:50	0.150	0.038	5	0
PER2 2024	5/21/2024 15:50	5/21/2024 16:00	0.150	0.038	5	0
PER2 2024	5/21/2024 16:00	5/21/2024 16:10	0.150	0.038	5	0
PER2 2024	5/21/2024 16:10	5/21/2024 16:20	0.150	0.038	5	0
PER2 2024	5/21/2024 16:20	5/21/2024 16:30	0.150	0.038	5	0
PER2 2024	5/21/2024 16:30	5/21/2024 16:40	0.150	0.038	5	0
PER2 2024	5/21/2024 16:40	5/21/2024 16:50	0.150	0.038	5	0
PER2 2024	5/21/2024 16:50	5/21/2024 17:00	0.150	0.038	5	0
PER2 2024	5/21/2024 17:00	5/21/2024 17:10	0.150	0.038	5	0
PER2 2024	5/21/2024 17:10	5/21/2024 17:20	0.150	0.038	5	0
PER2 2024	5/21/2024 17:20	5/21/2024 17:30	0.150	0.038	5	0
PER2 2024	5/21/2024 17:30	5/21/2024 17:40	0.150	0.038	5	0
PER2 2024	5/21/2024 17:40	5/21/2024 17:50	0.150	0.038	5	0
PER2 2024	5/21/2024 17:50	5/21/2024 17:59	0.150	0.038	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/22/2024 Weather: 80 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued minor excavation, rebar and waterproofing installation for the foundation development. 2) Landscaping contractor Let It Grow mobilizes to complete work in southwest corner of the Site. 3) Over excavate and recollect remedial excavation end point samples, see below.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): REB_MW6_BOT2_20240522 and REB_MW6_SW2_202405022.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8685	1720	4140

Site Layout Map and Excavation Figures

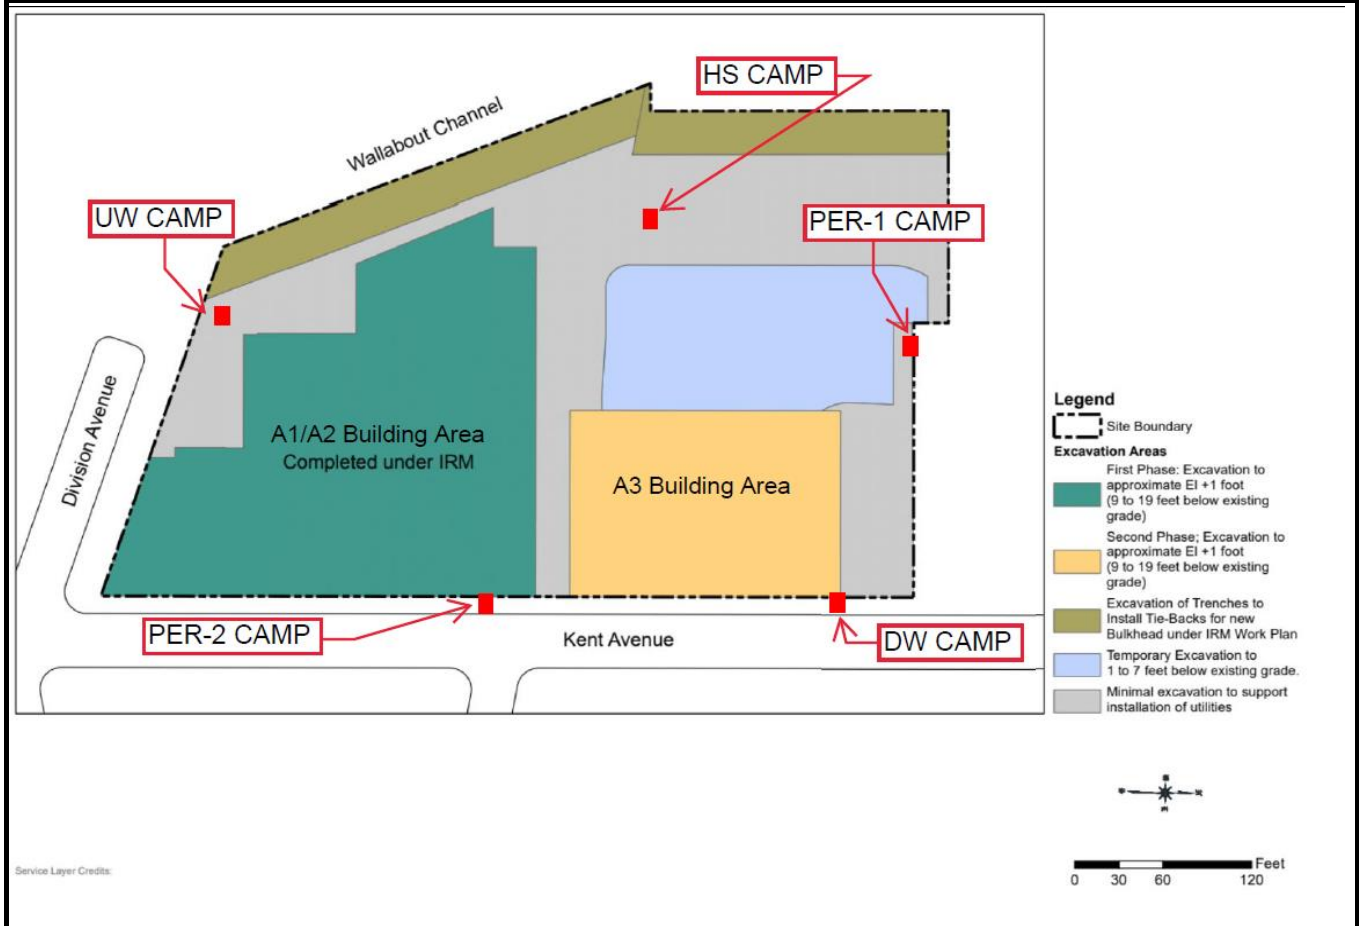

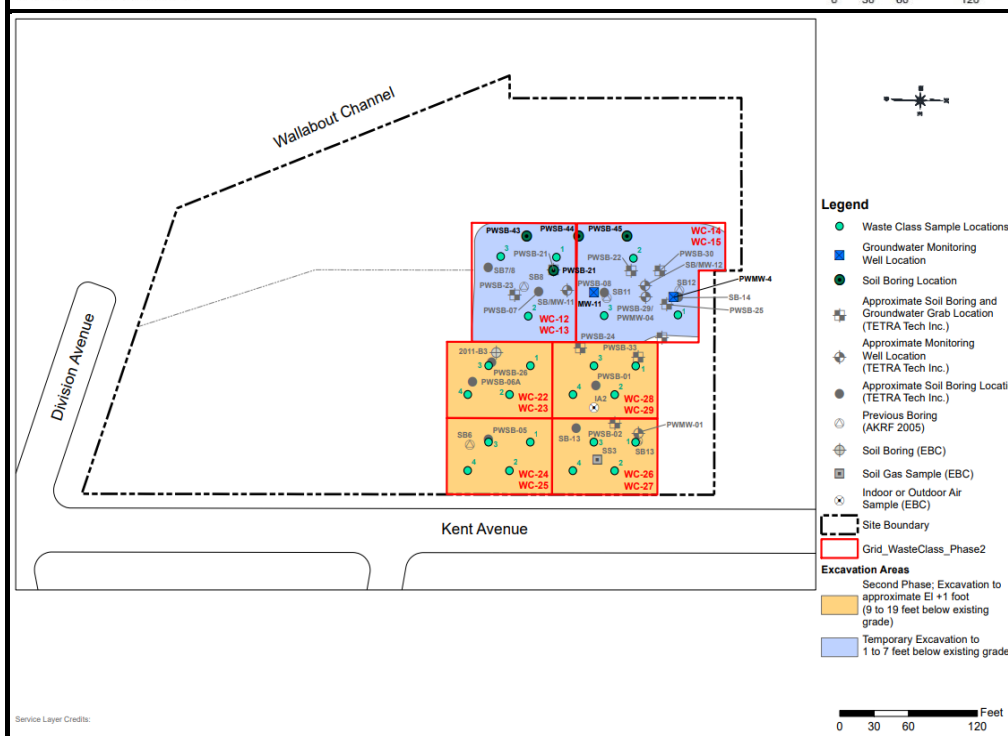
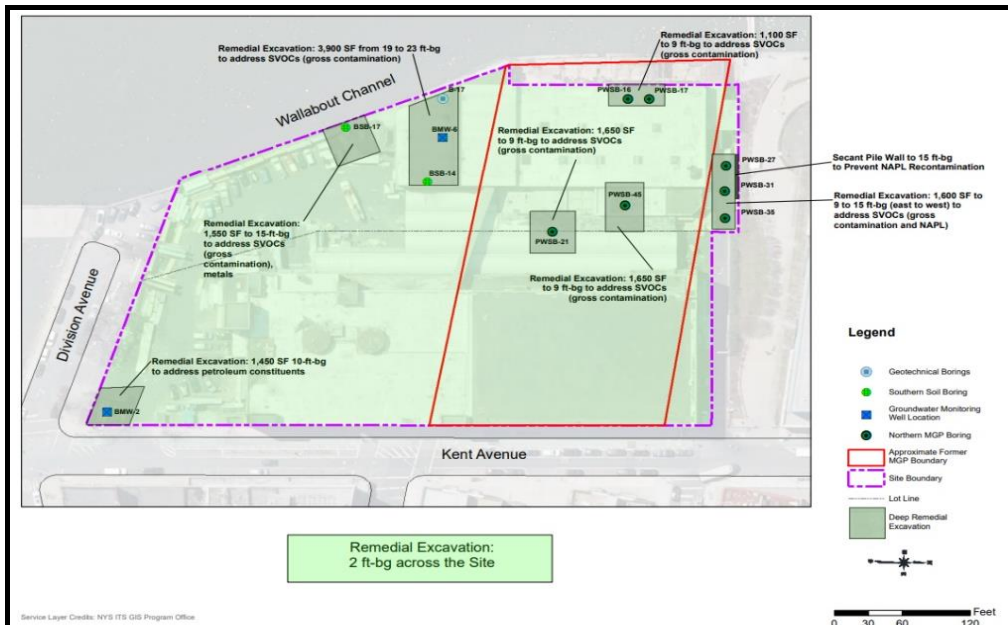


Photo 1:
View of Site conditions
facing east.



Photo 2:
View of the marine front
along building A2, facing
southwest.

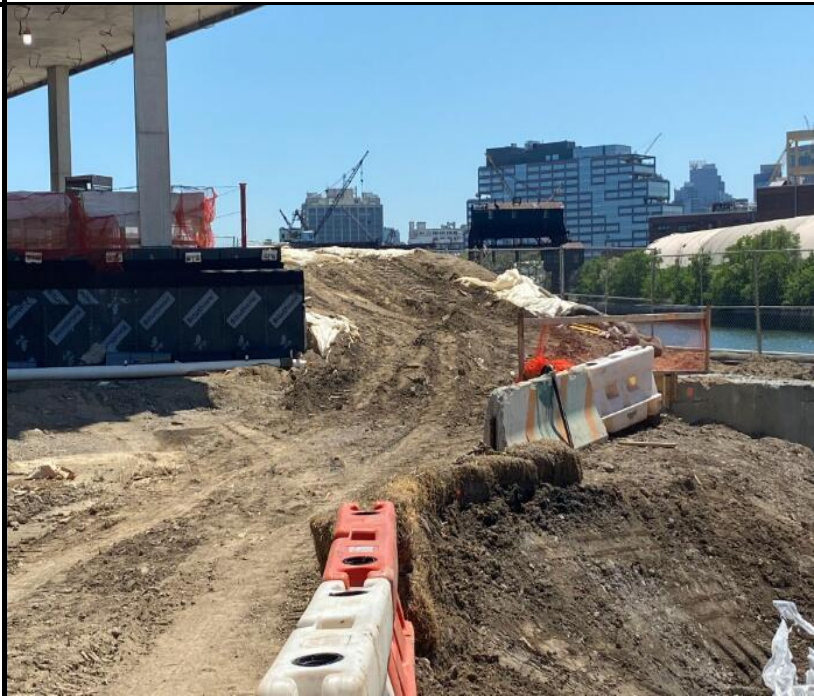


Photo 3:
View of excavation
work on the
southwest portion of
the Site for
landscaping.


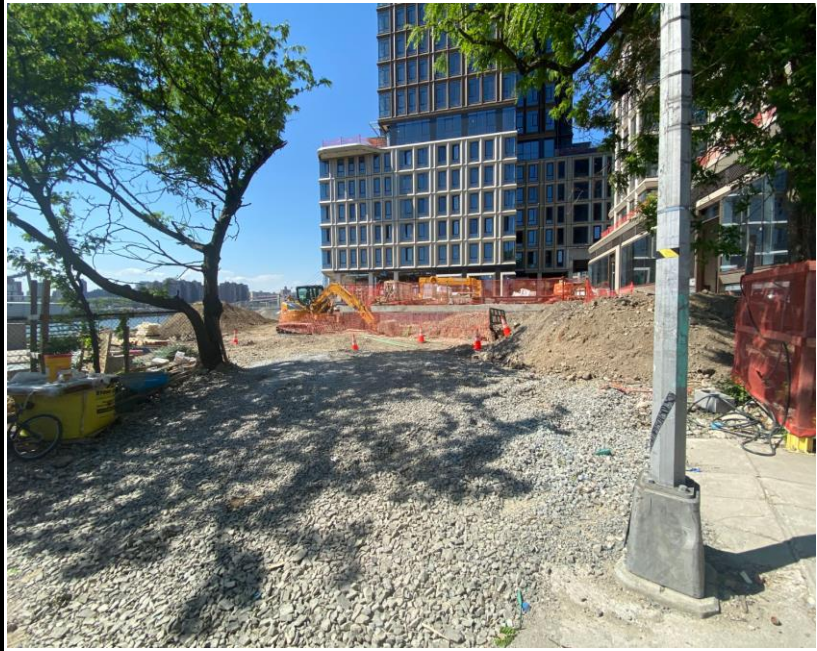


Photo 4:
View of the remedial
excavation facing
west.




CAMP:
Downwind
Particulates

Dust Levels

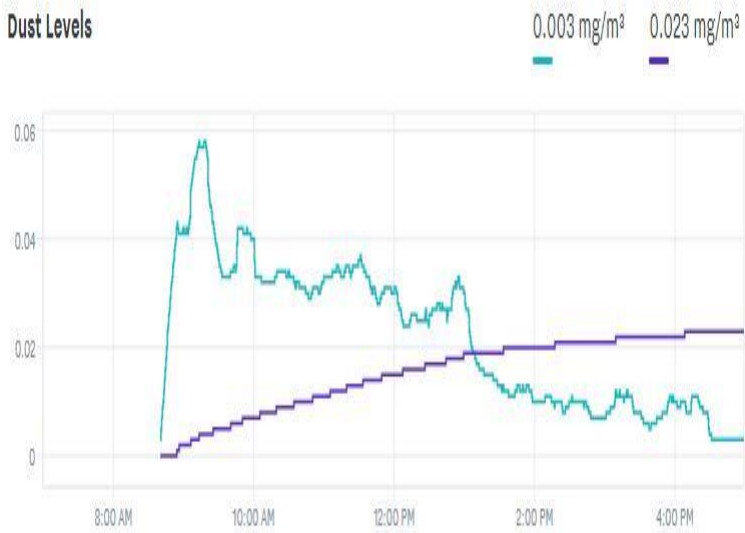

CAMP:
Downwind VOCs

VOC Levels

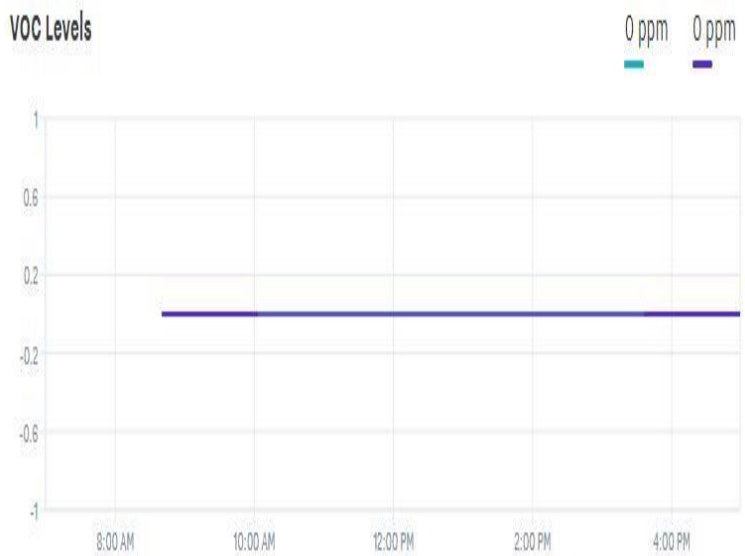


CAMP:
Upwind Particulates

Dust Levels



CAMP:
Upwind VOCs

VOC Levels

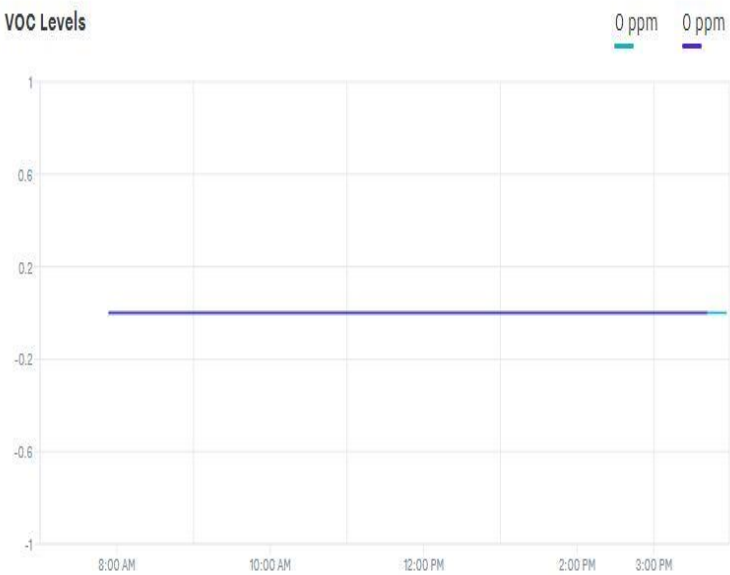

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/22/2024 8:40	5/22/2024 8:50	0.150	0	5	0
DW 2024	5/22/2024 8:50	5/22/2024 9:00	0.150	0.002	5	0
DW 2024	5/22/2024 9:00	5/22/2024 9:10	0.150	0.003	5	0
DW 2024	5/22/2024 9:10	5/22/2024 9:20	0.150	0.004	5	0
DW 2024	5/22/2024 9:20	5/22/2024 9:30	0.150	0.005	5	0
DW 2024	5/22/2024 9:30	5/22/2024 9:40	0.150	0.005	5	0
DW 2024	5/22/2024 9:40	5/22/2024 9:50	0.150	0.006	5	0
DW 2024	5/22/2024 9:50	5/22/2024 10:00	0.150	0.007	5	0
DW 2024	5/22/2024 10:00	5/22/2024 10:10	0.150	0.008	5	0
DW 2024	5/22/2024 10:10	5/22/2024 10:20	0.150	0.009	5	0
DW 2024	5/22/2024 10:20	5/22/2024 10:30	0.150	0.009	5	0
DW 2024	5/22/2024 10:30	5/22/2024 10:40	0.150	0.01	5	0
DW 2024	5/22/2024 10:40	5/22/2024 10:50	0.150	0.01	5	0
DW 2024	5/22/2024 10:50	5/22/2024 11:00	0.150	0.011	5	0
DW 2024	5/22/2024 11:00	5/22/2024 11:10	0.150	0.012	5	0
DW 2024	5/22/2024 11:10	5/22/2024 11:20	0.150	0.013	5	0
DW 2024	5/22/2024 11:20	5/22/2024 11:30	0.150	0.013	5	0
DW 2024	5/22/2024 11:30	5/22/2024 11:40	0.150	0.014	5	0
DW 2024	5/22/2024 11:40	5/22/2024 11:50	0.150	0.015	5	0
DW 2024	5/22/2024 11:50	5/22/2024 12:00	0.150	0.015	5	0
DW 2024	5/22/2024 12:00	5/22/2024 12:10	0.150	0.016	5	0
DW 2024	5/22/2024 12:10	5/22/2024 12:20	0.150	0.016	5	0
DW 2024	5/22/2024 12:20	5/22/2024 12:30	0.150	0.017	5	0
DW 2024	5/22/2024 12:30	5/22/2024 12:40	0.150	0.017	5	0
DW 2024	5/22/2024 12:40	5/22/2024 12:50	0.150	0.018	5	0
DW 2024	5/22/2024 12:50	5/22/2024 13:00	0.150	0.019	5	0
DW 2024	5/22/2024 13:00	5/22/2024 13:10	0.150	0.019	5	0
DW 2024	5/22/2024 13:10	5/22/2024 13:20	0.150	0.019	5	0
DW 2024	5/22/2024 13:20	5/22/2024 13:30	0.150	0.019	5	0
DW 2024	5/22/2024 13:30	5/22/2024 13:40	0.150	0.02	5	0
DW 2024	5/22/2024 13:40	5/22/2024 13:50	0.150	0.02	5	0
DW 2024	5/22/2024 13:50	5/22/2024 14:00	0.150	0.02	5	0
DW 2024	5/22/2024 14:00	5/22/2024 14:10	0.150	0.02	5	0
DW 2024	5/22/2024 14:10	5/22/2024 14:20	0.150	0.021	5	0
DW 2024	5/22/2024 14:20	5/22/2024 14:30	0.150	0.021	5	0
DW 2024	5/22/2024 14:30	5/22/2024 14:40	0.150	0.021	5	0
DW 2024	5/22/2024 14:40	5/22/2024 14:50	0.150	0.021	5	0
DW 2024	5/22/2024 14:50	5/22/2024 15:00	0.150	0.021	5	0
DW 2024	5/22/2024 15:00	5/22/2024 15:10	0.150	0.022	5	0
DW 2024	5/22/2024 15:10	5/22/2024 15:20	0.150	0.022	5	0
DW 2024	5/22/2024 15:20	5/22/2024 15:30	0.150	0.022	5	0
DW 2024	5/22/2024 15:30	5/22/2024 15:40	0.150	0.022	5	0
DW 2024	5/22/2024 15:40	5/22/2024 15:50	0.150	0.022	5	0
DW 2024	5/22/2024 15:50	5/22/2024 16:00	0.150	0.022	5	0
DW 2024	5/22/2024 16:00	5/22/2024 16:10	0.150	0.023	5	0
DW 2024	5/22/2024 16:10	5/22/2024 16:20	0.150	0.023	5	0
DW 2024	5/22/2024 16:20	5/22/2024 16:30	0.150	0.023	5	0
DW 2024	5/22/2024 16:30	5/22/2024 16:40	0.150	0.023	5	0
DW 2024	5/22/2024 16:40	5/22/2024 16:50	0.150	0.023	5	0
DW 2024	5/22/2024 16:50	5/22/2024 16:59	0.150	0.023	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/22/2024 8:00	5/22/2024 8:10	0.150	0.002	5	0
UW 2024	5/22/2024 8:10	5/22/2024 8:20	0.150	0.002	5	0
UW 2024	5/22/2024 8:20	5/22/2024 8:30	0.150	0.003	5	0
UW 2024	5/22/2024 8:30	5/22/2024 8:40	0.150	0.005	5	0
UW 2024	5/22/2024 8:40	5/22/2024 8:50	0.150	0.005	5	0
UW 2024	5/22/2024 8:50	5/22/2024 9:00	0.150	0.006	5	0
UW 2024	5/22/2024 9:00	5/22/2024 9:10	0.150	0.008	5	0
UW 2024	5/22/2024 9:10	5/22/2024 9:20	0.150	0.008	5	0
UW 2024	5/22/2024 9:20	5/22/2024 9:30	0.150	0.009	5	0
UW 2024	5/22/2024 9:30	5/22/2024 9:40	0.150	0.011	5	0
UW 2024	5/22/2024 9:40	5/22/2024 9:50	0.150	0.011	5	0
UW 2024	5/22/2024 9:50	5/22/2024 10:00	0.150	0.014	5	0
UW 2024	5/22/2024 10:00	5/22/2024 10:10	0.150	0.015	5	0
UW 2024	5/22/2024 10:10	5/22/2024 10:20	0.150	0.015	5	0
UW 2024	5/22/2024 10:20	5/22/2024 10:30	0.150	0.016	5	0
UW 2024	5/22/2024 10:30	5/22/2024 10:40	0.150	0.017	5	0
UW 2024	5/22/2024 10:40	5/22/2024 10:50	0.150	0.017	5	0
UW 2024	5/22/2024 10:50	5/22/2024 11:00	0.150	0.019	5	0
UW 2024	5/22/2024 11:00	5/22/2024 11:10	0.150	0.02	5	0
UW 2024	5/22/2024 11:10	5/22/2024 11:20	0.150	0.02	5	0
UW 2024	5/22/2024 11:20	5/22/2024 11:30	0.150	0.021	5	0
UW 2024	5/22/2024 11:30	5/22/2024 11:40	0.150	0.023	5	0
UW 2024	5/22/2024 11:40	5/22/2024 11:50	0.150	0.023	5	0
UW 2024	5/22/2024 11:50	5/22/2024 12:00	0.150	0.024	5	0
UW 2024	5/22/2024 12:00	5/22/2024 12:10	0.150	0.025	5	0
UW 2024	5/22/2024 12:10	5/22/2024 12:20	0.150	0.025	5	0
UW 2024	5/22/2024 12:20	5/22/2024 12:30	0.150	0.027	5	0
UW 2024	5/22/2024 12:30	5/22/2024 12:40	0.150	0.029	5	0
UW 2024	5/22/2024 12:40	5/22/2024 12:50	0.150	0.029	5	0
UW 2024	5/22/2024 12:50	5/22/2024 13:00	0.150	0.03	5	0
UW 2024	5/22/2024 13:00	5/22/2024 13:10	0.150	0.031	5	0
UW 2024	5/22/2024 13:10	5/22/2024 13:20	0.150	0.031	5	0
UW 2024	5/22/2024 13:20	5/22/2024 13:30	0.150	0.033	5	0
UW 2024	5/22/2024 13:30	5/22/2024 13:40	0.150	0.034	5	0
UW 2024	5/22/2024 13:40	5/22/2024 13:50	0.150	0.034	5	0
UW 2024	5/22/2024 13:50	5/22/2024 14:00	0.150	0.035	5	0
UW 2024	5/22/2024 14:00	5/22/2024 14:10	0.150	0.036	5	0
UW 2024	5/22/2024 14:10	5/22/2024 14:20	0.150	0.036	5	0
UW 2024	5/22/2024 14:20	5/22/2024 14:30	0.150	0.037	5	0
UW 2024	5/22/2024 14:30	5/22/2024 14:40	0.150	0.038	5	0
UW 2024	5/22/2024 14:40	5/22/2024 14:50	0.150	0.038	5	0
UW 2024	5/22/2024 14:50	5/22/2024 15:00	0.150	0.039	5	0
UW 2024	5/22/2024 15:00	5/22/2024 15:10	0.150	0.04	5	0
UW 2024	5/22/2024 15:10	5/22/2024 15:20	0.150	0.04	5	0
UW 2024	5/22/2024 15:20	5/22/2024 15:30	0.150	0.041	5	0
UW 2024	5/22/2024 15:30	5/22/2024 15:40	0.150	0.042	5	0
UW 2024	5/22/2024 15:40	5/22/2024 15:50	0.150	0.042	5	0
UW 2024	5/22/2024 15:50	5/22/2024 16:00	0.150	0	5	0
UW 2024	5/22/2024 16:00	5/22/2024 16:10	0.150	0	5	0
UW 2024	5/22/2024 16:10	5/22/2024 16:20	0.150	0	5	0
UW 2024	5/22/2024 16:20	5/22/2024 16:30	0.150	0	5	0
UW 2024	5/22/2024 16:30	5/22/2024 16:40	0.150	0	5	0
UW 2024	5/22/2024 16:40	5/22/2024 16:50	0.150	0	5	0
UW 2024	5/22/2024 16:50	5/22/2024 16:59	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/22/2024 8:40	5/22/2024 8:50	0.150	0	5	0
HS South	5/22/2024 8:50	5/22/2024 9:00	0.150	0	5	0
HS South	5/22/2024 9:00	5/22/2024 9:10	0.150	0.003	5	0
HS South	5/22/2024 9:10	5/22/2024 9:20	0.150	0.004	5	0
HS South	5/22/2024 9:20	5/22/2024 9:30	0.150	0.005	5	0
HS South	5/22/2024 9:30	5/22/2024 9:40	0.150	0.006	5	0
HS South	5/22/2024 9:40	5/22/2024 9:50	0.150	0.007	5	0
HS South	5/22/2024 9:50	5/22/2024 10:00	0.150	0.008	5	0
HS South	5/22/2024 10:00	5/22/2024 10:10	0.150	0.009	5	0
HS South	5/22/2024 10:10	5/22/2024 10:20	0.150	0.011	5	0
HS South	5/22/2024 10:20	5/22/2024 10:30	0.150	0.012	5	0
HS South	5/22/2024 10:30	5/22/2024 10:40	0.150	0.013	5	0
HS South	5/22/2024 10:40	5/22/2024 10:50	0.150	0.014	5	0
HS South	5/22/2024 10:50	5/22/2024 11:00	0.150	0.015	5	0
HS South	5/22/2024 11:00	5/22/2024 11:10	0.150	0.016	5	0
HS South	5/22/2024 11:10	5/22/2024 11:20	0.150	0.017	5	0
HS South	5/22/2024 11:20	5/22/2024 11:30	0.150	0.018	5	0
HS South	5/22/2024 11:30	5/22/2024 11:40	0.150	0.019	5	0
HS South	5/22/2024 11:40	5/22/2024 11:50	0.150	0.02	5	0
HS South	5/22/2024 11:50	5/22/2024 12:00	0.150	0.022	5	0
HS South	5/22/2024 12:00	5/22/2024 12:10	0.150	0.023	5	0
HS South	5/22/2024 12:10	5/22/2024 12:20	0.150	0.024	5	0
HS South	5/22/2024 12:20	5/22/2024 12:30	0.150	0.026	5	0
HS South	5/22/2024 12:30	5/22/2024 12:40	0.150	0.027	5	0
HS South	5/22/2024 12:40	5/22/2024 12:50	0.150	0.032	5	0
HS South	5/22/2024 12:50	5/22/2024 13:00	0.150	0.033	5	0
HS South	5/22/2024 13:00	5/22/2024 13:10	0.150	0.034	5	0
HS South	5/22/2024 13:10	5/22/2024 13:20	0.150	0.035	5	0
HS South	5/22/2024 13:20	5/22/2024 13:30	0.150	0.036	5	0
HS South	5/22/2024 13:30	5/22/2024 13:40	0.150	0.037	5	0
HS South	5/22/2024 13:40	5/22/2024 13:50	0.150	0.038	5	0
HS South	5/22/2024 13:50	5/22/2024 14:00	0.150	0.039	5	0
HS South	5/22/2024 14:00	5/22/2024 14:10	0.150	0.041	5	0
HS South	5/22/2024 14:10	5/22/2024 14:20	0.150	0.042	5	0
HS South	5/22/2024 14:20	5/22/2024 14:30	0.150	0.044	5	0
HS South	5/22/2024 14:30	5/22/2024 14:40	0.150	0.046	5	0
HS South	5/22/2024 14:40	5/22/2024 14:50	0.150	0.047	5	0
HS South	5/22/2024 14:50	5/22/2024 15:00	0.150	0.048	5	0
HS South	5/22/2024 15:00	5/22/2024 15:10	0.150	0.053	5	0
HS South	5/22/2024 15:10	5/22/2024 15:20	0.150	0.054	5	0
HS South	5/22/2024 15:20	5/22/2024 15:30	0.150	0.056	5	0
HS South	5/22/2024 15:30	5/22/2024 15:40	0.150	0.057	5	0
HS South	5/22/2024 15:40	5/22/2024 15:50	0.150	0.058	5	0
HS South	5/22/2024 15:50	5/22/2024 16:00	0.150	0.06	5	0
HS South	5/22/2024 16:00	5/22/2024 16:10	0.150	0.061	5	0
HS South	5/22/2024 16:10	5/22/2024 16:20	0.150	0.063	5	0
HS South	5/22/2024 16:20	5/22/2024 16:30	0.150	0.064	5	0
HS South	5/22/2024 16:30	5/22/2024 16:40	0.150	0.064	5	0
HS South	5/22/2024 16:40	5/22/2024 16:50	0.150	0.064	5	0
HS South	5/22/2024 16:50	5/22/2024 16:59	0.150	0.064	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/22/2024 7:30	5/22/2024 7:40	0.150	0.012	5	0
PER1 2024	5/22/2024 7:40	5/22/2024 7:50	0.150	0.012	5	0
PER1 2024	5/22/2024 7:50	5/22/2024 8:00	0.150	0.012	5	0
PER1 2024	5/22/2024 8:00	5/22/2024 8:10	0.150	0.012	5	0
PER1 2024	5/22/2024 8:10	5/22/2024 8:20	0.150	0.012	5	0
PER1 2024	5/22/2024 8:20	5/22/2024 8:30	0.150	0.012	5	0
PER1 2024	5/22/2024 8:30	5/22/2024 8:40	0.150	0.012	5	0
PER1 2024	5/22/2024 8:40	5/22/2024 8:50	0.150	0.012	5	0
PER1 2024	5/22/2024 8:50	5/22/2024 9:00	0.150	0.012	5	0
PER1 2024	5/22/2024 9:00	5/22/2024 9:10	0.150	0.012	5	0
PER1 2024	5/22/2024 9:10	5/22/2024 9:20	0.150	0.012	5	0
PER1 2024	5/22/2024 9:20	5/22/2024 9:30	0.150	0.012	5	0
PER1 2024	5/22/2024 9:30	5/22/2024 9:40	0.150	0.012	5	0
PER1 2024	5/22/2024 9:40	5/22/2024 9:50	0.150	0.012	5	0
PER1 2024	5/22/2024 9:50	5/22/2024 10:00	0.150	0.012	5	0
PER1 2024	5/22/2024 10:00	5/22/2024 10:10	0.150	0.012	5	0
PER1 2024	5/22/2024 10:10	5/22/2024 10:20	0.150	0.012	5	0
PER1 2024	5/22/2024 10:20	5/22/2024 10:30	0.150	0.012	5	0
PER1 2024	5/22/2024 10:30	5/22/2024 10:40	0.150	0.012	5	0
PER1 2024	5/22/2024 10:40	5/22/2024 10:50	0.150	0.012	5	0
PER1 2024	5/22/2024 10:50	5/22/2024 11:00	0.150	0.012	5	0
PER1 2024	5/22/2024 11:00	5/22/2024 11:10	0.150	0.012	5	0
PER1 2024	5/22/2024 11:10	5/22/2024 11:20	0.150	0.012	5	0
PER1 2024	5/22/2024 11:20	5/22/2024 11:30	0.150	0.012	5	0
PER1 2024	5/22/2024 11:30	5/22/2024 11:40	0.150	0.012	5	0
PER1 2024	5/22/2024 11:40	5/22/2024 11:50	0.150	0.012	5	0
PER1 2024	5/22/2024 11:50	5/22/2024 12:00	0.150	0.012	5	0
PER1 2024	5/22/2024 12:00	5/22/2024 12:10	0.150	0.008	5	0
PER1 2024	5/22/2024 12:10	5/22/2024 12:20	0.150	0.008	5	0
PER1 2024	5/22/2024 12:20	5/22/2024 12:30	0.150	0.008	5	0
PER1 2024	5/22/2024 12:30	5/22/2024 12:40	0.150	0.009	5	0
PER1 2024	5/22/2024 12:40	5/22/2024 12:50	0.150	0.01	5	0
PER1 2024	5/22/2024 12:50	5/22/2024 13:00	0.150	0.01	5	0
PER1 2024	5/22/2024 13:00	5/22/2024 13:10	0.150	0.01	5	0
PER1 2024	5/22/2024 13:10	5/22/2024 13:20	0.150	0.01	5	0
PER1 2024	5/22/2024 13:20	5/22/2024 13:30	0.150	0.011	5	0
PER1 2024	5/22/2024 13:30	5/22/2024 13:40	0.150	0.011	5	0
PER1 2024	5/22/2024 13:40	5/22/2024 13:50	0.150	0.011	5	0
PER1 2024	5/22/2024 13:50	5/22/2024 14:00	0.150	0.011	5	0
PER1 2024	5/22/2024 14:00	5/22/2024 14:10	0.150	0.012	5	0
PER1 2024	5/22/2024 14:10	5/22/2024 14:20	0.150	0.012	5	0
PER1 2024	5/22/2024 14:20	5/22/2024 14:30	0.150	0.012	5	0
PER1 2024	5/22/2024 14:30	5/22/2024 14:40	0.150	0.012	5	0
PER1 2024	5/22/2024 14:40	5/22/2024 14:50	0.150	0.013	5	0
PER1 2024	5/22/2024 14:50	5/22/2024 15:00	0.150	0.013	5	0
PER1 2024	5/22/2024 15:00	5/22/2024 15:10	0.150	0.013	5	0
PER1 2024	5/22/2024 15:10	5/22/2024 15:20	0.150	0.013	5	0
PER1 2024	5/22/2024 15:20	5/22/2024 15:30	0.150	0.013	5	0.066
PER1 2024	5/22/2024 15:30	5/22/2024 15:40	0.150	0.013	5	0.066
PER1 2024	5/22/2024 15:40	5/22/2024 15:50	0.150	0.014	5	0.066
PER1 2024	5/22/2024 15:50	5/22/2024 16:00	0.150	0.014	5	0.066
PER1 2024	5/22/2024 16:00	5/22/2024 16:10	0.150	0.014	5	0.066
PER1 2024	5/22/2024 16:10	5/22/2024 16:20	0.150	0.014	5	0.066
PER1 2024	5/22/2024 16:20	5/22/2024 16:30	0.150	0.014	5	0.066
PER1 2024	5/22/2024 16:30	5/22/2024 16:40	0.150	0	5	0.066
PER1 2024	5/22/2024 16:40	5/22/2024 16:50	0.150	0	5	0.066
PER1 2024	5/22/2024 16:50	5/22/2024 16:59	0.150	0	5	0.066

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/22/2024 8:40	5/22/2024 8:50	0.150	0	5	0
PER2 2024	5/22/2024 8:50	5/22/2024 9:00	0.150	0.001	5	0
PER2 2024	5/22/2024 9:00	5/22/2024 9:10	0.150	0.002	5	0
PER2 2024	5/22/2024 9:10	5/22/2024 9:20	0.150	0.003	5	0
PER2 2024	5/22/2024 9:20	5/22/2024 9:30	0.150	0.003	5	0
PER2 2024	5/22/2024 9:30	5/22/2024 9:40	0.150	0.004	5	0
PER2 2024	5/22/2024 9:40	5/22/2024 9:50	0.150	0.004	5	0
PER2 2024	5/22/2024 9:50	5/22/2024 10:00	0.150	0.005	5	0
PER2 2024	5/22/2024 10:00	5/22/2024 10:10	0.150	0.005	5	0
PER2 2024	5/22/2024 10:10	5/22/2024 10:20	0.150	0.006	5	0
PER2 2024	5/22/2024 10:20	5/22/2024 10:30	0.150	0.007	5	0
PER2 2024	5/22/2024 10:30	5/22/2024 10:40	0.150	0.007	5	0
PER2 2024	5/22/2024 10:40	5/22/2024 10:50	0.150	0.008	5	0
PER2 2024	5/22/2024 10:50	5/22/2024 11:00	0.150	0.008	5	0
PER2 2024	5/22/2024 11:00	5/22/2024 11:10	0.150	0.009	5	0
PER2 2024	5/22/2024 11:10	5/22/2024 11:20	0.150	0.01	5	0
PER2 2024	5/22/2024 11:20	5/22/2024 11:30	0.150	0.011	5	0
PER2 2024	5/22/2024 11:30	5/22/2024 11:40	0.150	0.011	5	0
PER2 2024	5/22/2024 11:40	5/22/2024 11:50	0.150	0.012	5	0
PER2 2024	5/22/2024 11:50	5/22/2024 12:00	0.150	0.012	5	0
PER2 2024	5/22/2024 12:00	5/22/2024 12:10	0.150	0.013	5	0
PER2 2024	5/22/2024 12:10	5/22/2024 12:20	0.150	0.013	5	0
PER2 2024	5/22/2024 12:20	5/22/2024 12:30	0.150	0.014	5	0
PER2 2024	5/22/2024 12:30	5/22/2024 12:40	0.150	0.014	5	0
PER2 2024	5/22/2024 12:40	5/22/2024 12:50	0.150	0.015	5	0
PER2 2024	5/22/2024 12:50	5/22/2024 13:00	0.150	0.015	5	0
PER2 2024	5/22/2024 13:00	5/22/2024 13:10	0.150	0.016	5	0
PER2 2024	5/22/2024 13:10	5/22/2024 13:20	0.150	0.016	5	0
PER2 2024	5/22/2024 13:20	5/22/2024 13:30	0.150	0.016	5	0
PER2 2024	5/22/2024 13:30	5/22/2024 13:40	0.150	0.016	5	0
PER2 2024	5/22/2024 13:40	5/22/2024 13:50	0.150	0.017	5	0
PER2 2024	5/22/2024 13:50	5/22/2024 14:00	0.150	0.017	5	0
PER2 2024	5/22/2024 14:00	5/22/2024 14:10	0.150	0.017	5	0
PER2 2024	5/22/2024 14:10	5/22/2024 14:20	0.150	0.017	5	0
PER2 2024	5/22/2024 14:20	5/22/2024 14:30	0.150	0.018	5	0
PER2 2024	5/22/2024 14:30	5/22/2024 14:40	0.150	0.018	5	0
PER2 2024	5/22/2024 14:40	5/22/2024 14:50	0.150	0.018	5	0
PER2 2024	5/22/2024 14:50	5/22/2024 15:00	0.150	0.019	5	0
PER2 2024	5/22/2024 15:00	5/22/2024 15:10	0.150	0.019	5	0
PER2 2024	5/22/2024 15:10	5/22/2024 15:20	0.150	0.019	5	0
PER2 2024	5/22/2024 15:20	5/22/2024 15:30	0.150	0.02	5	0
PER2 2024	5/22/2024 15:30	5/22/2024 15:40	0.150	0.02	5	0
PER2 2024	5/22/2024 15:40	5/22/2024 15:50	0.150	0.021	5	0
PER2 2024	5/22/2024 15:50	5/22/2024 16:00	0.150	0.021	5	0
PER2 2024	5/22/2024 16:00	5/22/2024 16:10	0.150	0.022	5	0
PER2 2024	5/22/2024 16:10	5/22/2024 16:20	0.150	0.022	5	0
PER2 2024	5/22/2024 16:20	5/22/2024 16:30	0.150	0.022	5	0
PER2 2024	5/22/2024 16:30	5/22/2024 16:40	0.150	0.022	5	0
PER2 2024	5/22/2024 16:40	5/22/2024 16:50	0.150	0.022	5	0
PER2 2024	5/22/2024 16:50	5/22/2024 16:59	0.150	0.022	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/23/2024 Weather: 80 deg. F, Rain/Overcast


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued vertical form installation for building construction. 2) ECD continues to advance the remedial excavation to the east. 3) ECD exported 3 loads (~60 CY) of soil for off-site disposal at the Bayshore Soil Management facility. 4) Import of 3 loads of 3/4" stone for remedial excavation backfilling.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation excavation, off-site soil disposal and foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8685	1720	4140

Site Layout Map and Excavation Figures

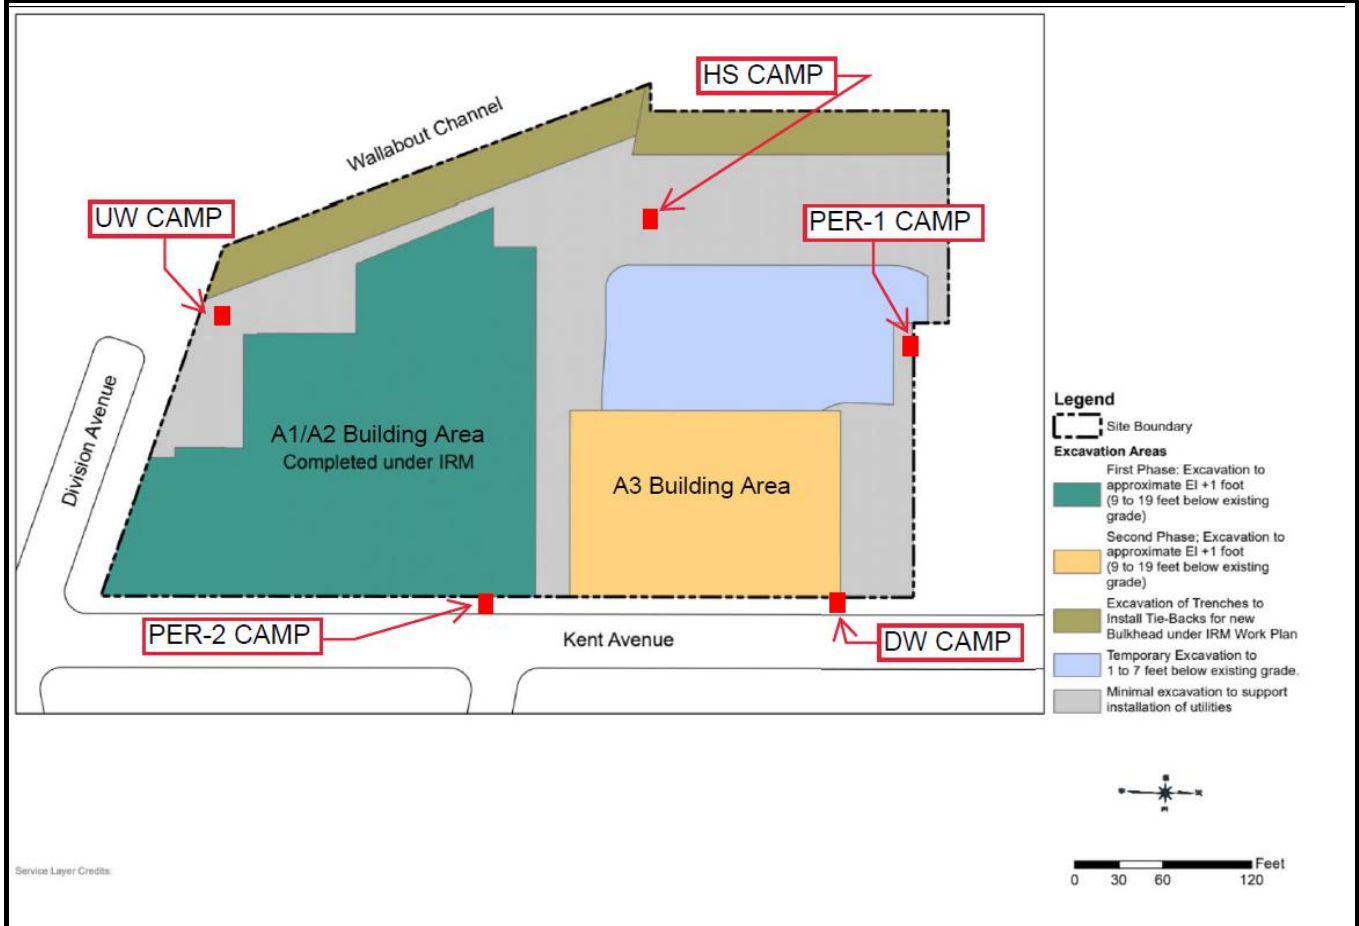

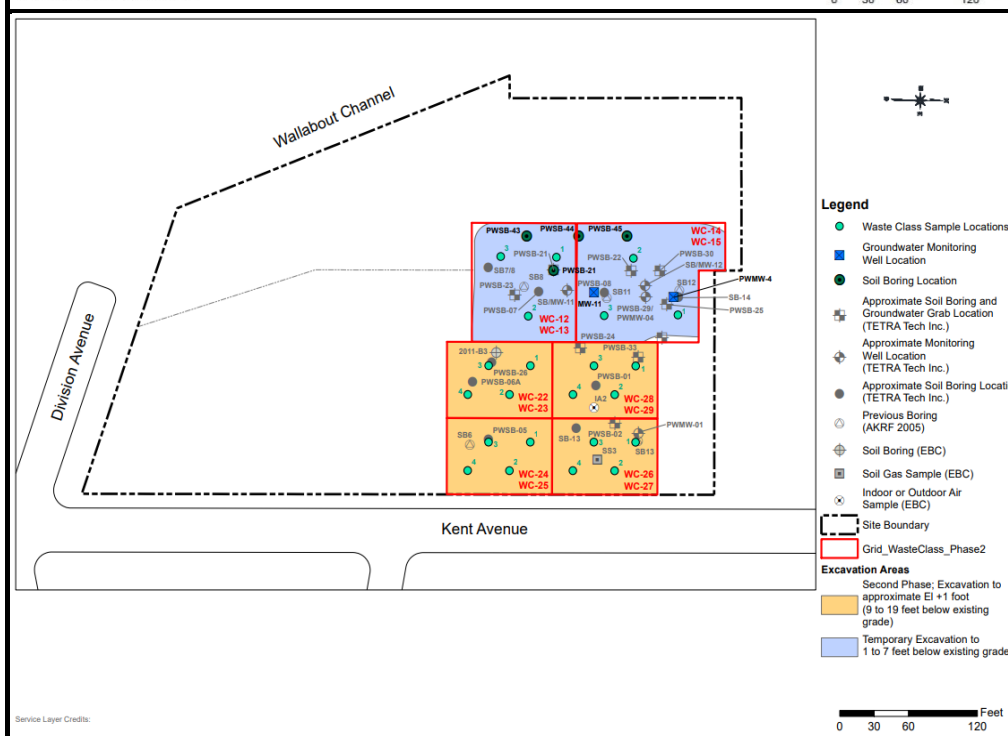
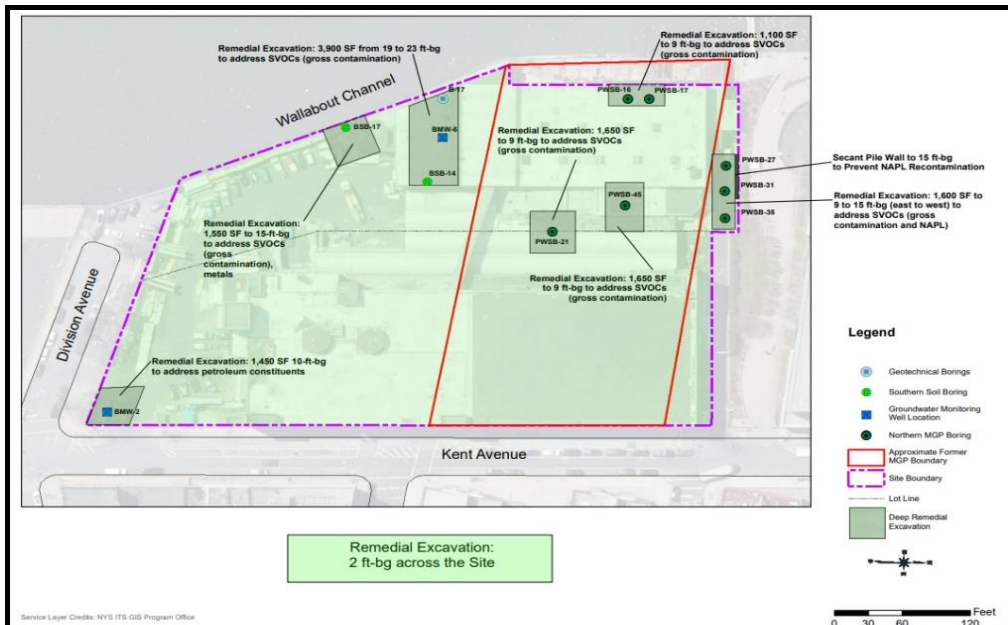


Photo 1:

View of 3/4" stone
import for backfill.



Photo 2:

View of the remedial
excavation facing west.

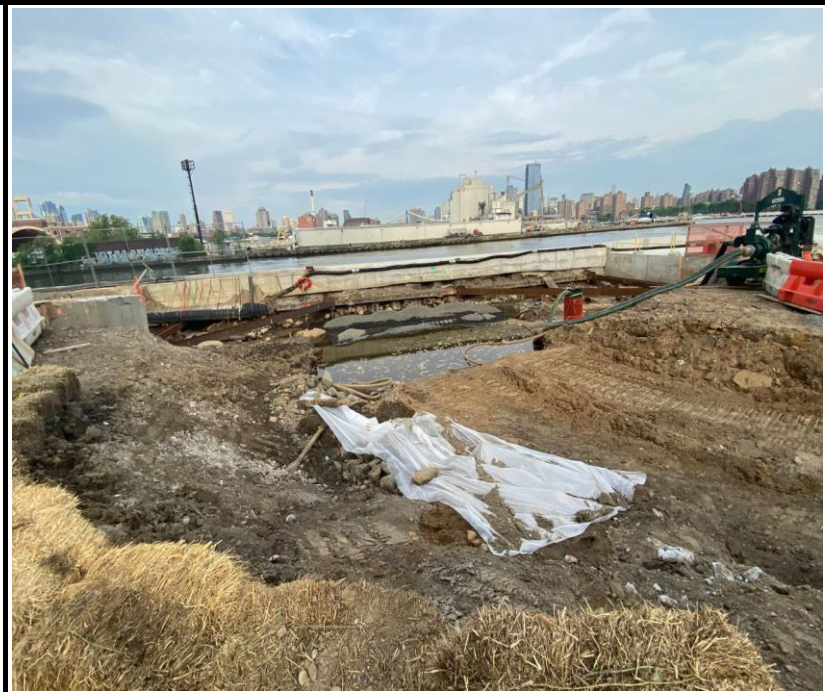


Photo 3:
View of tire washing
prior to trucks
leaving the Site.

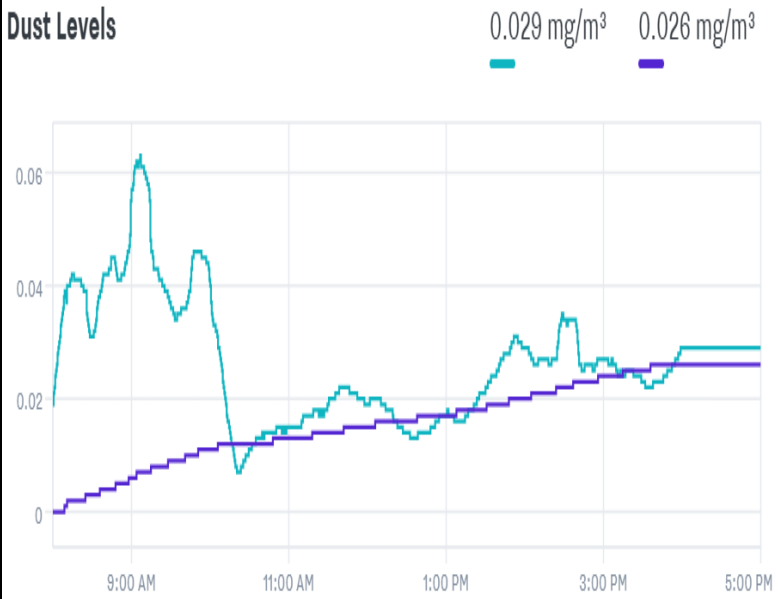


Photo 4:
View of continued
excavation for the
remedial excavation.




CAMP:
Downwind
Particulates

Dust Levels



CAMP:
Downwind VOCs


VOC Levels

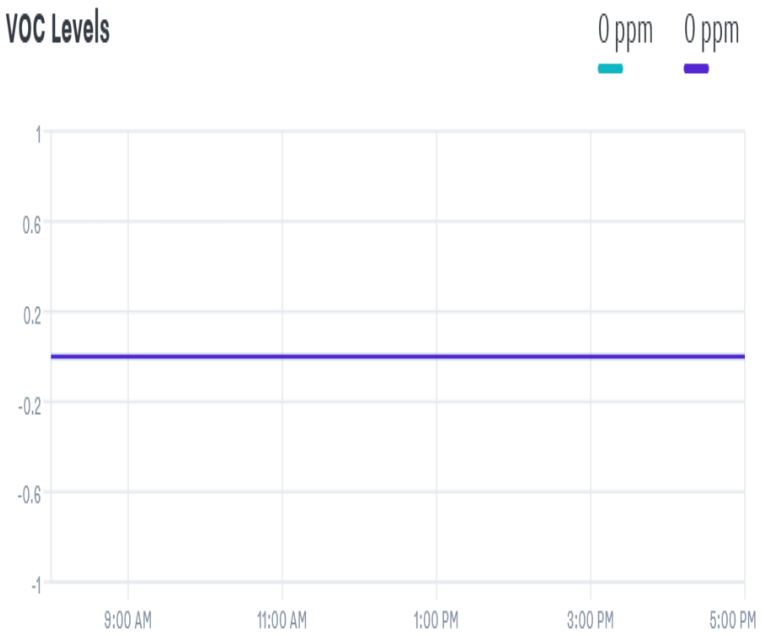

CAMP:
Upwind Particulates

Dust Levels


0.042 mg/m³ 0.039 mg/m³

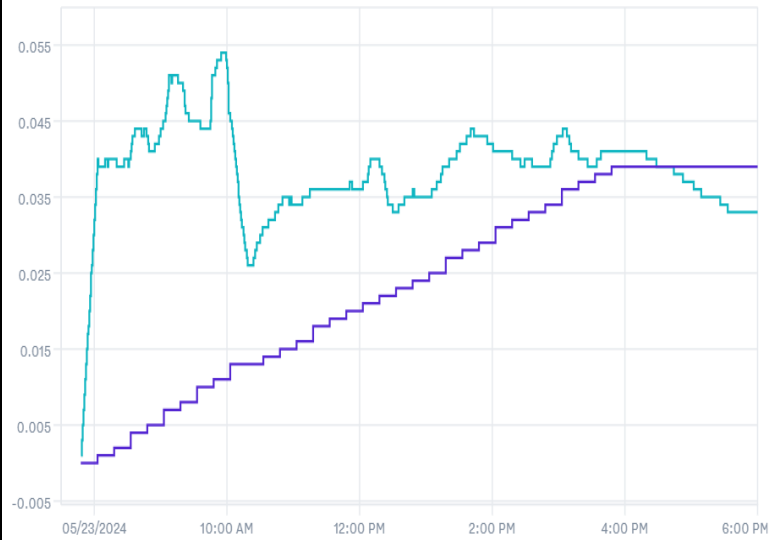

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

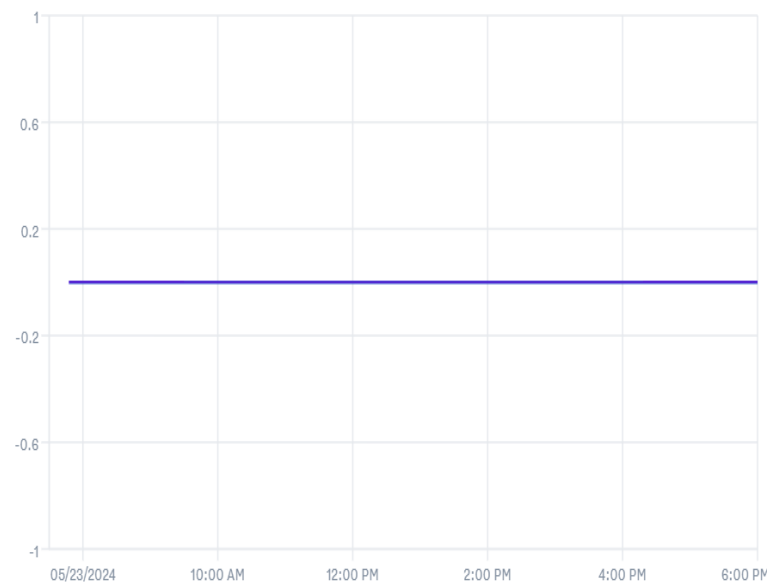

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/23/2024 7:50	5/23/2024 8:00	0.150	0	5	0
DW 2024	5/23/2024 8:00	5/23/2024 8:10	0.150	0.001	5	0
DW 2024	5/23/2024 8:10	5/23/2024 8:20	0.150	0.002	5	0
DW 2024	5/23/2024 8:20	5/23/2024 8:30	0.150	0.003	5	0
DW 2024	5/23/2024 8:30	5/23/2024 8:40	0.150	0.004	5	0
DW 2024	5/23/2024 8:40	5/23/2024 8:50	0.150	0.005	5	0
DW 2024	5/23/2024 8:50	5/23/2024 9:00	0.150	0.006	5	0
DW 2024	5/23/2024 9:00	5/23/2024 9:10	0.150	0.007	5	0
DW 2024	5/23/2024 9:10	5/23/2024 9:20	0.150	0.008	5	0
DW 2024	5/23/2024 9:20	5/23/2024 9:30	0.150	0.009	5	0
DW 2024	5/23/2024 9:30	5/23/2024 9:40	0.150	0.009	5	0
DW 2024	5/23/2024 9:40	5/23/2024 9:50	0.150	0.01	5	0
DW 2024	5/23/2024 9:50	5/23/2024 10:00	0.150	0.011	5	0
DW 2024	5/23/2024 10:00	5/23/2024 10:10	0.150	0.012	5	0
DW 2024	5/23/2024 10:10	5/23/2024 10:20	0.150	0.012	5	0
DW 2024	5/23/2024 10:20	5/23/2024 10:30	0.150	0.012	5	0
DW 2024	5/23/2024 10:30	5/23/2024 10:40	0.150	0.012	5	0
DW 2024	5/23/2024 10:40	5/23/2024 10:50	0.150	0.013	5	0
DW 2024	5/23/2024 10:50	5/23/2024 11:00	0.150	0.013	5	0
DW 2024	5/23/2024 11:00	5/23/2024 11:10	0.150	0.013	5	0
DW 2024	5/23/2024 11:10	5/23/2024 11:20	0.150	0.014	5	0
DW 2024	5/23/2024 11:20	5/23/2024 11:30	0.150	0.014	5	0
DW 2024	5/23/2024 11:30	5/23/2024 11:40	0.150	0.014	5	0
DW 2024	5/23/2024 11:40	5/23/2024 11:50	0.150	0.015	5	0
DW 2024	5/23/2024 11:50	5/23/2024 12:00	0.150	0.015	5	0
DW 2024	5/23/2024 12:00	5/23/2024 12:10	0.150	0.016	5	0
DW 2024	5/23/2024 12:10	5/23/2024 12:20	0.150	0.016	5	0
DW 2024	5/23/2024 12:20	5/23/2024 12:30	0.150	0.016	5	0
DW 2024	5/23/2024 12:30	5/23/2024 12:40	0.150	0.017	5	0
DW 2024	5/23/2024 12:40	5/23/2024 12:50	0.150	0.017	5	0
DW 2024	5/23/2024 12:50	5/23/2024 13:00	0.150	0.017	5	0
DW 2024	5/23/2024 13:00	5/23/2024 13:10	0.150	0.018	5	0
DW 2024	5/23/2024 13:10	5/23/2024 13:20	0.150	0.018	5	0
DW 2024	5/23/2024 13:20	5/23/2024 13:30	0.150	0.018	5	0
DW 2024	5/23/2024 13:30	5/23/2024 13:40	0.150	0.019	5	0
DW 2024	5/23/2024 13:40	5/23/2024 13:50	0.150	0.02	5	0
DW 2024	5/23/2024 13:50	5/23/2024 14:00	0.150	0.02	5	0
DW 2024	5/23/2024 14:00	5/23/2024 14:10	0.150	0.021	5	0
DW 2024	5/23/2024 14:10	5/23/2024 14:20	0.150	0.021	5	0
DW 2024	5/23/2024 14:20	5/23/2024 14:30	0.150	0.022	5	0
DW 2024	5/23/2024 14:30	5/23/2024 14:40	0.150	0.023	5	0
DW 2024	5/23/2024 14:40	5/23/2024 14:50	0.150	0.023	5	0
DW 2024	5/23/2024 14:50	5/23/2024 15:00	0.150	0.024	5	0
DW 2024	5/23/2024 15:00	5/23/2024 15:10	0.150	0.024	5	0
DW 2024	5/23/2024 15:10	5/23/2024 15:20	0.150	0.025	5	0
DW 2024	5/23/2024 15:20	5/23/2024 15:30	0.150	0.025	5	0
DW 2024	5/23/2024 15:30	5/23/2024 15:40	0.150	0.026	5	0
DW 2024	5/23/2024 15:40	5/23/2024 15:50	0.150	0.026	5	0
DW 2024	5/23/2024 15:50	5/23/2024 16:00	0.150	0.026	5	0
DW 2024	5/23/2024 16:00	5/23/2024 16:10	0.150	0.026	5	0
DW 2024	5/23/2024 16:10	5/23/2024 16:20	0.150	0.026	5	0
DW 2024	5/23/2024 16:20	5/23/2024 16:30	0.150	0.026	5	0
DW 2024	5/23/2024 16:30	5/23/2024 16:40	0.150	0.026	5	0
DW 2024	5/23/2024 16:40	5/23/2024 16:50	0.150	0.026	5	0
DW 2024	5/23/2024 16:50	5/23/2024 17:00	0.150	0.026	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/23/2024 7:50	5/23/2024 8:00	0.150	0	5	0
UW 2024	5/23/2024 8:00	5/23/2024 8:10	0.150	0.001	5	0
UW 2024	5/23/2024 8:10	5/23/2024 8:20	0.150	0.002	5	0
UW 2024	5/23/2024 8:20	5/23/2024 8:30	0.150	0.002	5	0
UW 2024	5/23/2024 8:30	5/23/2024 8:40	0.150	0.004	5	0
UW 2024	5/23/2024 8:40	5/23/2024 8:50	0.150	0.005	5	0
UW 2024	5/23/2024 8:50	5/23/2024 9:00	0.150	0.005	5	0
UW 2024	5/23/2024 9:00	5/23/2024 9:10	0.150	0.007	5	0
UW 2024	5/23/2024 9:10	5/23/2024 9:20	0.150	0.008	5	0
UW 2024	5/23/2024 9:20	5/23/2024 9:30	0.150	0.008	5	0
UW 2024	5/23/2024 9:30	5/23/2024 9:40	0.150	0.01	5	0
UW 2024	5/23/2024 9:40	5/23/2024 9:50	0.150	0.011	5	0
UW 2024	5/23/2024 9:50	5/23/2024 10:00	0.150	0.011	5	0
UW 2024	5/23/2024 10:00	5/23/2024 10:10	0.150	0.013	5	0
UW 2024	5/23/2024 10:10	5/23/2024 10:20	0.150	0.013	5	0
UW 2024	5/23/2024 10:20	5/23/2024 10:30	0.150	0.013	5	0
UW 2024	5/23/2024 10:30	5/23/2024 10:40	0.150	0.014	5	0
UW 2024	5/23/2024 10:40	5/23/2024 10:50	0.150	0.015	5	0
UW 2024	5/23/2024 10:50	5/23/2024 11:00	0.150	0.015	5	0
UW 2024	5/23/2024 11:00	5/23/2024 11:10	0.150	0.016	5	0
UW 2024	5/23/2024 11:10	5/23/2024 11:20	0.150	0.018	5	0
UW 2024	5/23/2024 11:20	5/23/2024 11:30	0.150	0.018	5	0
UW 2024	5/23/2024 11:30	5/23/2024 11:40	0.150	0.019	5	0
UW 2024	5/23/2024 11:40	5/23/2024 11:50	0.150	0.02	5	0
UW 2024	5/23/2024 11:50	5/23/2024 12:00	0.150	0.02	5	0
UW 2024	5/23/2024 12:00	5/23/2024 12:10	0.150	0.021	5	0
UW 2024	5/23/2024 12:10	5/23/2024 12:20	0.150	0.022	5	0
UW 2024	5/23/2024 12:20	5/23/2024 12:30	0.150	0.022	5	0
UW 2024	5/23/2024 12:30	5/23/2024 12:40	0.150	0.023	5	0
UW 2024	5/23/2024 12:40	5/23/2024 12:50	0.150	0.024	5	0
UW 2024	5/23/2024 12:50	5/23/2024 13:00	0.150	0.024	5	0
UW 2024	5/23/2024 13:00	5/23/2024 13:10	0.150	0.025	5	0
UW 2024	5/23/2024 13:10	5/23/2024 13:20	0.150	0.027	5	0
UW 2024	5/23/2024 13:20	5/23/2024 13:30	0.150	0.027	5	0
UW 2024	5/23/2024 13:30	5/23/2024 13:40	0.150	0.028	5	0
UW 2024	5/23/2024 13:40	5/23/2024 13:50	0.150	0.029	5	0
UW 2024	5/23/2024 13:50	5/23/2024 14:00	0.150	0.029	5	0
UW 2024	5/23/2024 14:00	5/23/2024 14:10	0.150	0.031	5	0
UW 2024	5/23/2024 14:10	5/23/2024 14:20	0.150	0.032	5	0
UW 2024	5/23/2024 14:20	5/23/2024 14:30	0.150	0.032	5	0
UW 2024	5/23/2024 14:30	5/23/2024 14:40	0.150	0.033	5	0
UW 2024	5/23/2024 14:40	5/23/2024 14:50	0.150	0.034	5	0
UW 2024	5/23/2024 14:50	5/23/2024 15:00	0.150	0.034	5	0
UW 2024	5/23/2024 15:00	5/23/2024 15:10	0.150	0.036	5	0
UW 2024	5/23/2024 15:10	5/23/2024 15:20	0.150	0.037	5	0
UW 2024	5/23/2024 15:20	5/23/2024 15:30	0.150	0.037	5	0
UW 2024	5/23/2024 15:30	5/23/2024 15:40	0.150	0.038	5	0
UW 2024	5/23/2024 15:40	5/23/2024 15:50	0.150	0.039	5	0
UW 2024	5/23/2024 15:50	5/23/2024 16:00	0.150	0.039	5	0
UW 2024	5/23/2024 16:00	5/23/2024 16:10	0.150	0.039	5	0
UW 2024	5/23/2024 16:10	5/23/2024 16:20	0.150	0.039	5	0
UW 2024	5/23/2024 16:20	5/23/2024 16:30	0.150	0.039	5	0
UW 2024	5/23/2024 16:30	5/23/2024 16:40	0.150	0.039	5	0
UW 2024	5/23/2024 16:40	5/23/2024 16:50	0.150	0.039	5	0
UW 2024	5/23/2024 16:50	5/23/2024 17:00	0.150	0.039	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/23/2024 7:40	5/23/2024 7:50	0.150	0	5	0
HS South	5/23/2024 7:50	5/23/2024 8:00	0.150	0.002	5	0
HS South	5/23/2024 8:00	5/23/2024 8:10	0.150	0.003	5	0
HS South	5/23/2024 8:10	5/23/2024 8:20	0.150	0.004	5	0
HS South	5/23/2024 8:20	5/23/2024 8:30	0.150	0.006	5	0
HS South	5/23/2024 8:30	5/23/2024 8:40	0.150	0.007	5	0
HS South	5/23/2024 8:40	5/23/2024 8:50	0.150	0.008	5	0
HS South	5/23/2024 8:50	5/23/2024 9:00	0.150	0.011	5	0
HS South	5/23/2024 9:00	5/23/2024 9:10	0.150	0.013	5	0
HS South	5/23/2024 9:10	5/23/2024 9:20	0.150	0.014	5	0
HS South	5/23/2024 9:20	5/23/2024 9:30	0.150	0.016	5	0
HS South	5/23/2024 9:30	5/23/2024 9:40	0.150	0.017	5	0
HS South	5/23/2024 9:40	5/23/2024 9:50	0.150	0.019	5	0
HS South	5/23/2024 9:50	5/23/2024 10:00	0.150	0.02	5	0
HS South	5/23/2024 10:00	5/23/2024 10:10	0.150	0.021	5	0
HS South	5/23/2024 10:10	5/23/2024 10:20	0.150	0.022	5	0
HS South	5/23/2024 10:20	5/23/2024 10:30	0.150	0.023	5	0
HS South	5/23/2024 10:30	5/23/2024 10:40	0.150	0.024	5	0
HS South	5/23/2024 10:40	5/23/2024 10:50	0.150	0.025	5	0
HS South	5/23/2024 10:50	5/23/2024 11:00	0.150	0.025	5	0
HS South	5/23/2024 11:00	5/23/2024 11:10	0.150	0.026	5	0
HS South	5/23/2024 11:10	5/23/2024 11:20	0.150	0.027	5	0
HS South	5/23/2024 11:20	5/23/2024 11:30	0.150	0.028	5	0
HS South	5/23/2024 11:30	5/23/2024 11:40	0.150	0.029	5	0
HS South	5/23/2024 11:40	5/23/2024 11:50	0.150	0.03	5	0
HS South	5/23/2024 11:50	5/23/2024 12:00	0.150	0.031	5	0
HS South	5/23/2024 12:00	5/23/2024 12:10	0.150	0.032	5	0
HS South	5/23/2024 12:10	5/23/2024 12:20	0.150	0.033	5	0
HS South	5/23/2024 12:20	5/23/2024 12:30	0.150	0.034	5	0
HS South	5/23/2024 12:30	5/23/2024 12:40	0.150	0.035	5	0
HS South	5/23/2024 12:40	5/23/2024 12:50	0.150	0.035	5	0
HS South	5/23/2024 12:50	5/23/2024 13:00	0.150	0.036	5	0
HS South	5/23/2024 13:00	5/23/2024 13:10	0.150	0.037	5	0
HS South	5/23/2024 13:10	5/23/2024 13:20	0.150	0.038	5	0
HS South	5/23/2024 13:20	5/23/2024 13:30	0.150	0.039	5	0
HS South	5/23/2024 13:30	5/23/2024 13:40	0.150	0.041	5	0
HS South	5/23/2024 13:40	5/23/2024 13:50	0.150	0.042	5	0
HS South	5/23/2024 13:50	5/23/2024 14:00	0.150	0.043	5	0
HS South	5/23/2024 14:00	5/23/2024 14:10	0.150	0.044	5	0
HS South	5/23/2024 14:10	5/23/2024 14:20	0.150	0.045	5	0
HS South	5/23/2024 14:20	5/23/2024 14:30	0.150	0.046	5	0
HS South	5/23/2024 14:30	5/23/2024 14:40	0.150	0.048	5	0
HS South	5/23/2024 14:40	5/23/2024 14:50	0.150	0.049	5	0
HS South	5/23/2024 14:50	5/23/2024 15:00	0.150	0.05	5	0
HS South	5/23/2024 15:00	5/23/2024 15:10	0.150	0.052	5	0
HS South	5/23/2024 15:10	5/23/2024 15:20	0.150	0.053	5	0
HS South	5/23/2024 15:20	5/23/2024 15:30	0.150	0.054	5	0
HS South	5/23/2024 15:30	5/23/2024 15:40	0.150	0.055	5	0
HS South	5/23/2024 15:40	5/23/2024 15:50	0.150	0.055	5	0
HS South	5/23/2024 15:50	5/23/2024 16:00	0.150	0.055	5	0
HS South	5/23/2024 16:00	5/23/2024 16:10	0.150	0.055	5	0
HS South	5/23/2024 16:10	5/23/2024 16:20	0.150	0.055	5	0
HS South	5/23/2024 16:20	5/23/2024 16:30	0.150	0.055	5	0
HS South	5/23/2024 16:30	5/23/2024 16:40	0.150	0.055	5	0
HS South	5/23/2024 16:40	5/23/2024 16:50	0.150	0.055	5	0
HS South	5/23/2024 16:50	5/23/2024 17:00	0.150	0.055	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/23/2024 7:50	5/23/2024 8:00	0.150	0	5	0
PER2 2024	5/23/2024 8:00	5/23/2024 8:10	0.150	0.002	5	0
PER2 2024	5/23/2024 8:10	5/23/2024 8:20	0.150	0.003	5	0
PER2 2024	5/23/2024 8:20	5/23/2024 8:30	0.150	0.003	5	0
PER2 2024	5/23/2024 8:30	5/23/2024 8:40	0.150	0.004	5	0
PER2 2024	5/23/2024 8:40	5/23/2024 8:50	0.150	0.005	5	0
PER2 2024	5/23/2024 8:50	5/23/2024 9:00	0.150	0.006	5	0
PER2 2024	5/23/2024 9:00	5/23/2024 9:10	0.150	0.006	5	0
PER2 2024	5/23/2024 9:10	5/23/2024 9:20	0.150	0.007	5	0
PER2 2024	5/23/2024 9:20	5/23/2024 9:30	0.150	0.008	5	0
PER2 2024	5/23/2024 9:30	5/23/2024 9:40	0.150	0.008	5	0
PER2 2024	5/23/2024 9:40	5/23/2024 9:50	0.150	0.009	5	0
PER2 2024	5/23/2024 9:50	5/23/2024 10:00	0.150	0.01	5	0
PER2 2024	5/23/2024 10:00	5/23/2024 10:10	0.150	0.01	5	0
PER2 2024	5/23/2024 10:10	5/23/2024 10:20	0.150	0.01	5	0
PER2 2024	5/23/2024 10:20	5/23/2024 10:30	0.150	0.01	5	0
PER2 2024	5/23/2024 10:30	5/23/2024 10:40	0.150	0.011	5	0
PER2 2024	5/23/2024 10:40	5/23/2024 10:50	0.150	0.011	5	0
PER2 2024	5/23/2024 10:50	5/23/2024 11:00	0.150	0.011	5	0
PER2 2024	5/23/2024 11:00	5/23/2024 11:10	0.150	0.011	5	0
PER2 2024	5/23/2024 11:10	5/23/2024 11:20	0.150	0.012	5	0
PER2 2024	5/23/2024 11:20	5/23/2024 11:30	0.150	0.012	5	0
PER2 2024	5/23/2024 11:30	5/23/2024 11:40	0.150	0.013	5	0
PER2 2024	5/23/2024 11:40	5/23/2024 11:50	0.150	0.013	5	0
PER2 2024	5/23/2024 11:50	5/23/2024 12:00	0.150	0.013	5	0
PER2 2024	5/23/2024 12:00	5/23/2024 12:10	0.150	0.014	5	0
PER2 2024	5/23/2024 12:10	5/23/2024 12:20	0.150	0.014	5	0
PER2 2024	5/23/2024 12:20	5/23/2024 12:30	0.150	0.015	5	0
PER2 2024	5/23/2024 12:30	5/23/2024 12:40	0.150	0.015	5	0
PER2 2024	5/23/2024 12:40	5/23/2024 12:50	0.150	0.015	5	0
PER2 2024	5/23/2024 12:50	5/23/2024 13:00	0.150	0.016	5	0
PER2 2024	5/23/2024 13:00	5/23/2024 13:10	0.150	0.016	5	0
PER2 2024	5/23/2024 13:10	5/23/2024 13:20	0.150	0.017	5	0
PER2 2024	5/23/2024 13:20	5/23/2024 13:30	0.150	0.017	5	0
PER2 2024	5/23/2024 13:30	5/23/2024 13:40	0.150	0.018	5	0
PER2 2024	5/23/2024 13:40	5/23/2024 13:50	0.150	0.018	5	0
PER2 2024	5/23/2024 13:50	5/23/2024 14:00	0.150	0.019	5	0
PER2 2024	5/23/2024 14:00	5/23/2024 14:10	0.150	0.019	5	0
PER2 2024	5/23/2024 14:10	5/23/2024 14:20	0.150	0.02	5	0
PER2 2024	5/23/2024 14:20	5/23/2024 14:30	0.150	0.021	5	0
PER2 2024	5/23/2024 14:30	5/23/2024 14:40	0.150	0.021	5	0
PER2 2024	5/23/2024 14:40	5/23/2024 14:50	0.150	0.021	5	0
PER2 2024	5/23/2024 14:50	5/23/2024 15:00	0.150	0.021	5	0
PER2 2024	5/23/2024 15:00	5/23/2024 15:10	0.150	0.021	5	0
PER2 2024	5/23/2024 15:10	5/23/2024 15:20	0.150	0.021	5	0
PER2 2024	5/23/2024 15:20	5/23/2024 15:30	0.150	0.021	5	0
PER2 2024	5/23/2024 15:30	5/23/2024 15:40	0.150	0.021	5	0
PER2 2024	5/23/2024 15:40	5/23/2024 15:50	0.150	0.021	5	0
PER2 2024	5/23/2024 15:50	5/23/2024 16:00	0.150	0.021	5	0
PER2 2024	5/23/2024 16:00	5/23/2024 16:10	0.150	0.021	5	0
PER2 2024	5/23/2024 16:10	5/23/2024 16:20	0.150	0.021	5	0
PER2 2024	5/23/2024 16:20	5/23/2024 16:30	0.150	0.021	5	0
PER2 2024	5/23/2024 16:30	5/23/2024 16:40	0.150	0.021	5	0
PER2 2024	5/23/2024 16:40	5/23/2024 16:50	0.150	0.021	5	0
PER2 2024	5/23/2024 16:50	5/23/2024 17:00	0.150	0.021	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/23/2024 7:30	5/23/2024 7:40	0.150	0	5	0
PER1 2024	5/23/2024 7:40	5/23/2024 7:50	0.150	0	5	0
PER1 2024	5/23/2024 7:50	5/23/2024 8:00	0.150	0	5	0
PER1 2024	5/23/2024 8:00	5/23/2024 8:10	0.150	0	5	0
PER1 2024	5/23/2024 8:10	5/23/2024 8:20	0.150	0	5	0
PER1 2024	5/23/2024 8:20	5/23/2024 8:30	0.150	0	5	0
PER1 2024	5/23/2024 8:30	5/23/2024 8:40	0.150	0	5	0
PER1 2024	5/23/2024 8:40	5/23/2024 8:50	0.150	0.001	5	0
PER1 2024	5/23/2024 8:50	5/23/2024 9:00	0.150	0.001	5	0
PER1 2024	5/23/2024 9:00	5/23/2024 9:10	0.150	0.001	5	0
PER1 2024	5/23/2024 9:10	5/23/2024 9:20	0.150	0.001	5	0
PER1 2024	5/23/2024 9:20	5/23/2024 9:30	0.150	0.001	5	0
PER1 2024	5/23/2024 9:30	5/23/2024 9:40	0.150	0.001	5	0
PER1 2024	5/23/2024 9:40	5/23/2024 9:50	0.150	0.002	5	0
PER1 2024	5/23/2024 9:50	5/23/2024 10:00	0.150	0.002	5	0
PER1 2024	5/23/2024 10:00	5/23/2024 10:10	0.150	0.002	5	0
PER1 2024	5/23/2024 10:10	5/23/2024 10:20	0.150	0.002	5	0
PER1 2024	5/23/2024 10:20	5/23/2024 10:30	0.150	0.002	5	0
PER1 2024	5/23/2024 10:30	5/23/2024 10:40	0.150	0.001	5	0
PER1 2024	5/23/2024 10:40	5/23/2024 10:50	0.150	0.001	5	0
PER1 2024	5/23/2024 10:50	5/23/2024 11:00	0.150	0.001	5	0
PER1 2024	5/23/2024 11:00	5/23/2024 11:10	0.150	0.001	5	0
PER1 2024	5/23/2024 11:10	5/23/2024 11:20	0.150	0.001	5	0
PER1 2024	5/23/2024 11:20	5/23/2024 11:30	0.150	0.001	5	0
PER1 2024	5/23/2024 11:30	5/23/2024 11:40	0.150	0.002	5	0
PER1 2024	5/23/2024 11:40	5/23/2024 11:50	0.150	0.002	5	0
PER1 2024	5/23/2024 11:50	5/23/2024 12:00	0.150	0.002	5	0
PER1 2024	5/23/2024 12:00	5/23/2024 12:10	0.150	0.002	5	0
PER1 2024	5/23/2024 12:10	5/23/2024 12:20	0.150	0.002	5	0
PER1 2024	5/23/2024 12:20	5/23/2024 12:30	0.150	0.002	5	0
PER1 2024	5/23/2024 12:30	5/23/2024 12:40	0.150	0.002	5	0
PER1 2024	5/23/2024 12:40	5/23/2024 12:50	0.150	0.002	5	0
PER1 2024	5/23/2024 12:50	5/23/2024 13:00	0.150	0.002	5	0.004
PER1 2024	5/23/2024 13:00	5/23/2024 13:10	0.150	0.002	5	0.005
PER1 2024	5/23/2024 13:10	5/23/2024 13:20	0.150	0.002	5	0.033
PER1 2024	5/23/2024 13:20	5/23/2024 13:30	0.150	0.002	5	0.063
PER1 2024	5/23/2024 13:30	5/23/2024 13:40	0.150	0.002	5	0.117
PER1 2024	5/23/2024 13:40	5/23/2024 13:50	0.150	0.003	5	0.156
PER1 2024	5/23/2024 13:50	5/23/2024 14:00	0.150	0.003	5	0.238
PER1 2024	5/23/2024 14:00	5/23/2024 14:10	0.150	0.003	5	0.344
PER1 2024	5/23/2024 14:10	5/23/2024 14:20	0.150	0.003	5	0.399
PER1 2024	5/23/2024 14:20	5/23/2024 14:30	0.150	0.004	5	0.466
PER1 2024	5/23/2024 14:30	5/23/2024 14:40	0.150	0.004	5	0.574
PER1 2024	5/23/2024 14:40	5/23/2024 14:50	0.150	0.004	5	0.604
PER1 2024	5/23/2024 14:50	5/23/2024 15:00	0.150	0.004	5	0.646
PER1 2024	5/23/2024 15:00	5/23/2024 15:10	0.150	0.004	5	0.708
PER1 2024	5/23/2024 15:10	5/23/2024 15:20	0.150	0.004	5	0.784
PER1 2024	5/23/2024 15:20	5/23/2024 15:30	0.150	0.005	5	0.843
PER1 2024	5/23/2024 15:30	5/23/2024 15:40	0.150	0.005	5	0.914
PER1 2024	5/23/2024 15:40	5/23/2024 15:50	0.150	0.005	5	0
PER1 2024	5/23/2024 15:50	5/23/2024 16:00	0.150	0	5	0
PER1 2024	5/23/2024 16:00	5/23/2024 16:10	0.150	0	5	0
PER1 2024	5/23/2024 16:10	5/23/2024 16:20	0.150	0	5	0
PER1 2024	5/23/2024 16:20	5/23/2024 16:30	0.150	0	5	0
PER1 2024	5/23/2024 16:30	5/23/2024 16:40	0.150	0	5	0
PER1 2024	5/23/2024 16:40	5/23/2024 16:50	0.150	0	5	0
PER1 2024	5/23/2024 16:50	5/23/2024 17:00	0.150	0	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/24/2024 Weather: 80 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued vertical form installation for building construction. 2) ECD continues to advance the remedial excavation to the east. 3) Import of 6 loads of 3/4" stone for remedial excavation backfilling. 4) Complete additional excavation and recollect remedial excavation EP samples, see below.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): REB_MW6_BOT2_20240524, REB_MW6_SW5_20240524 and REB_MW6_SW2_20240524	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8685	1720	4140

Site Layout Map and Excavation Figures

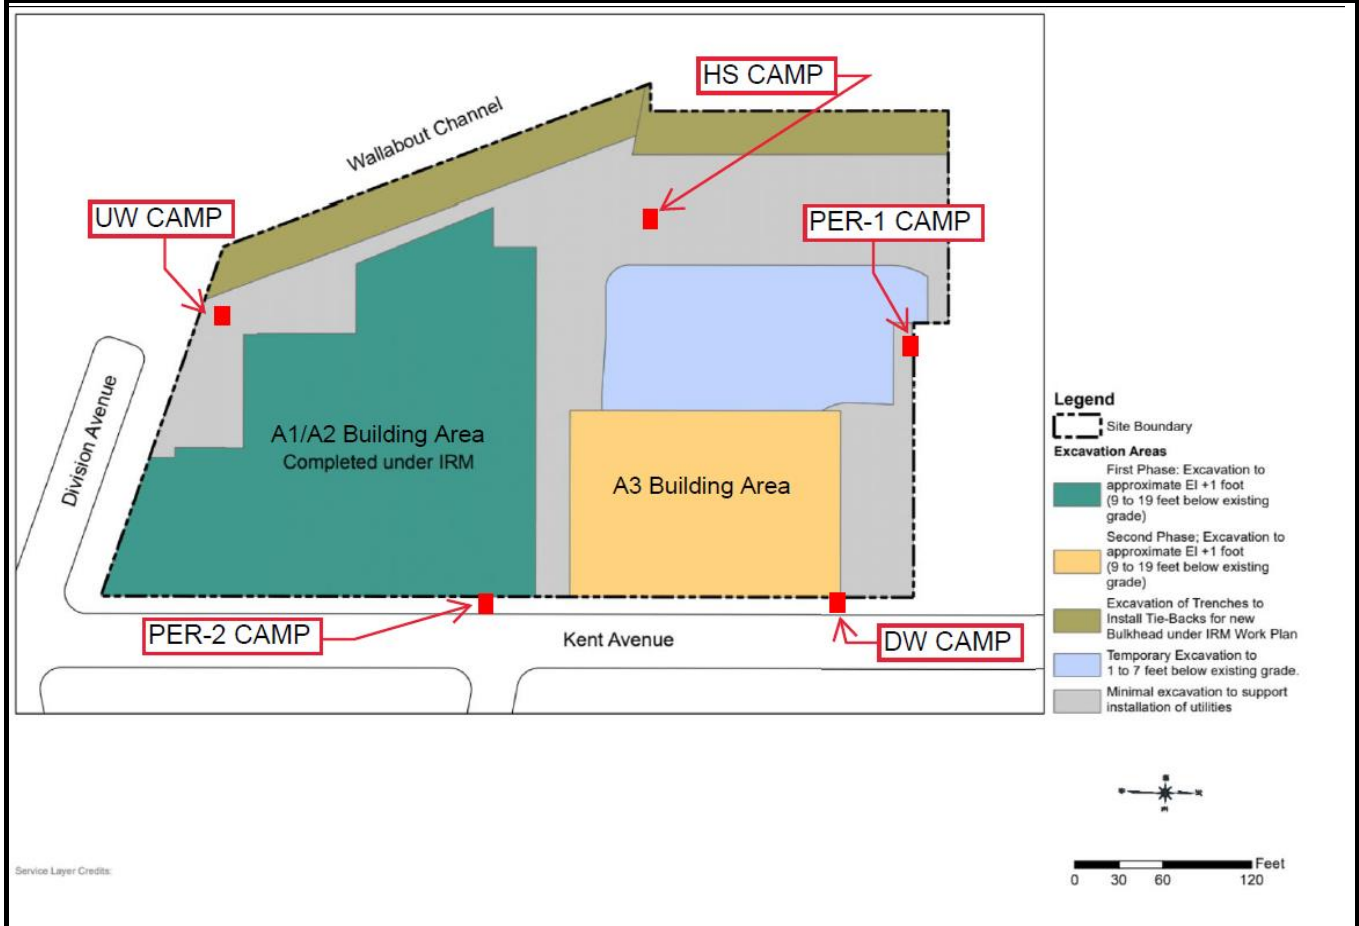

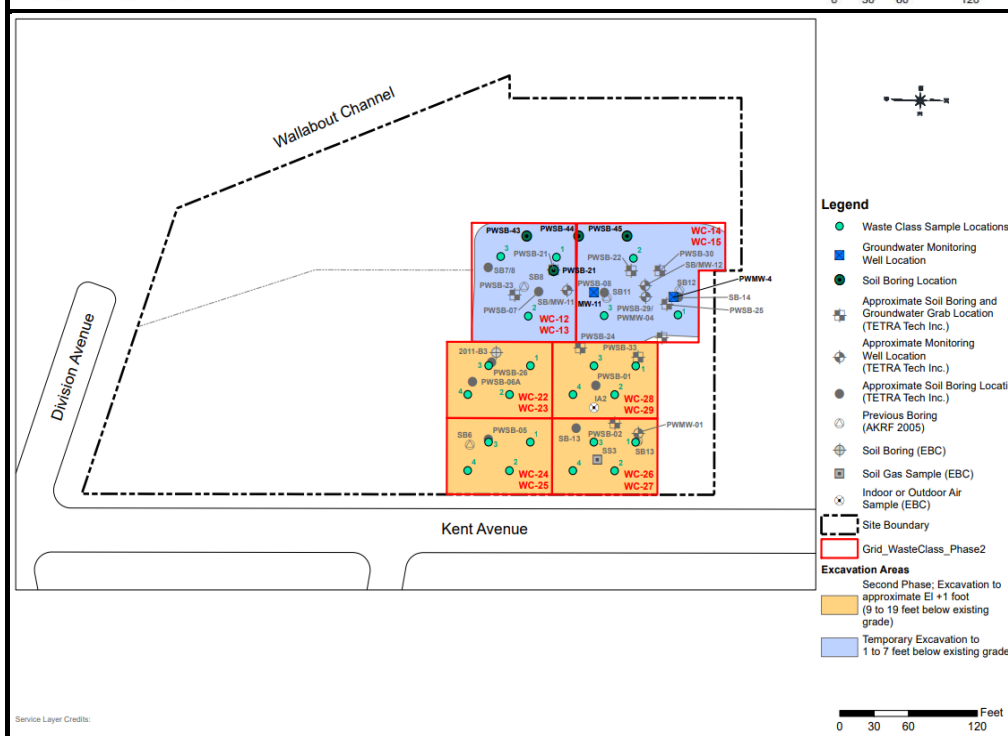
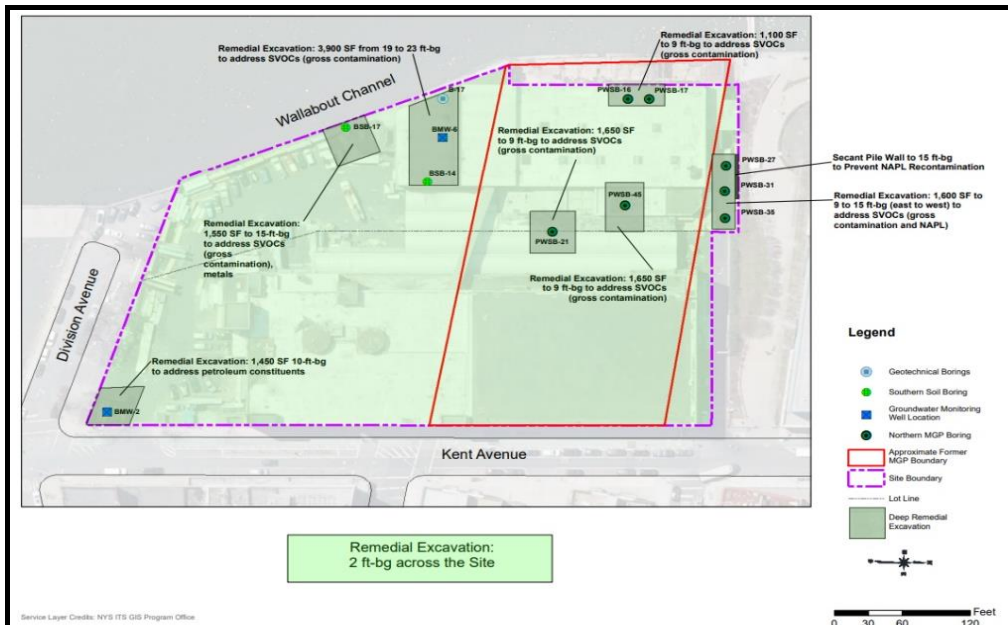


Photo 1:
View of the remedial
excavation facing north.

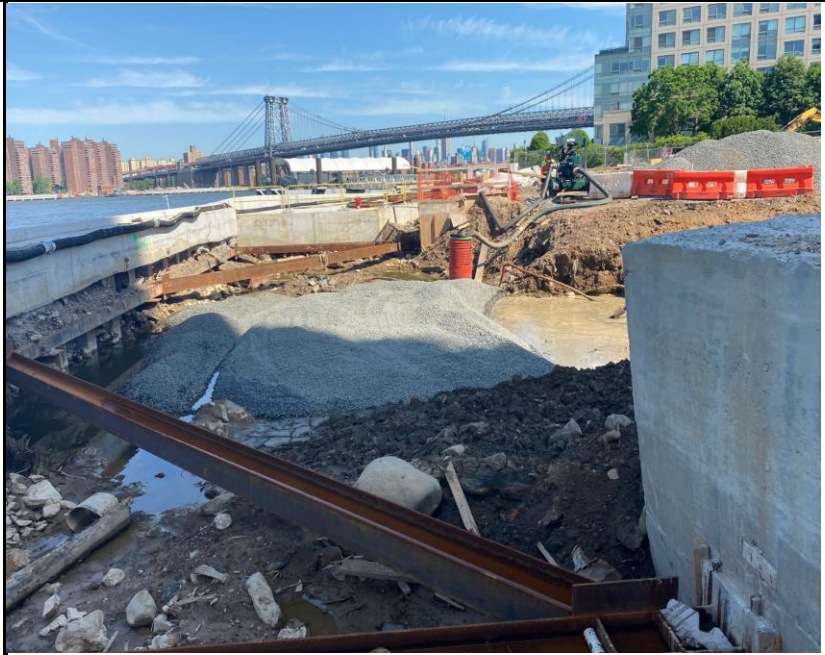


Photo 2:
View of the foundation
development facing west.



Photo 3:

View of approved backfill material stockpiled for landscaped area.



Photo 4:


View of the remedial excavation facing west.



CAMP:
Downwind
Particulates

Dust Levels


0.017 mg/m³ 0.012 mg/m³

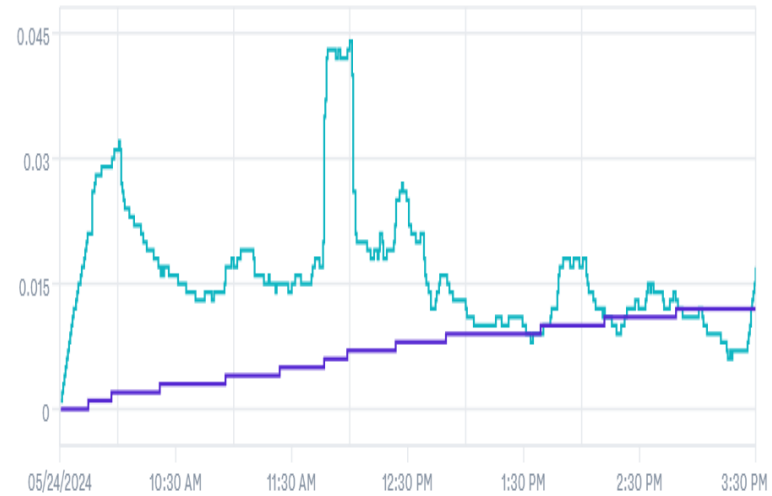

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm

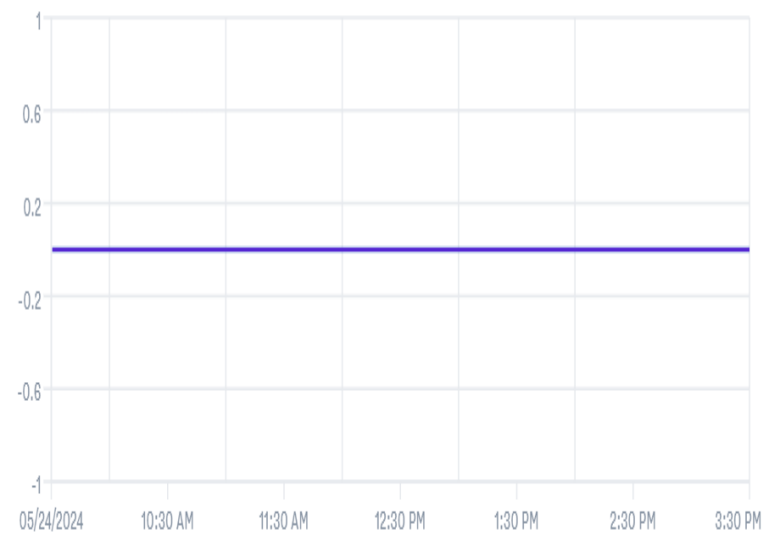

CAMP:
Upwind Particulates

Dust Levels


0.033 mg/m³ 0.027 mg/m³

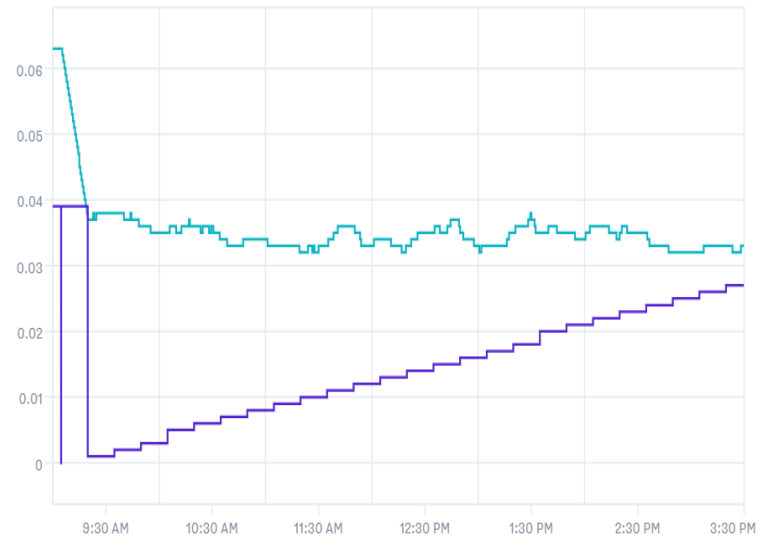

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

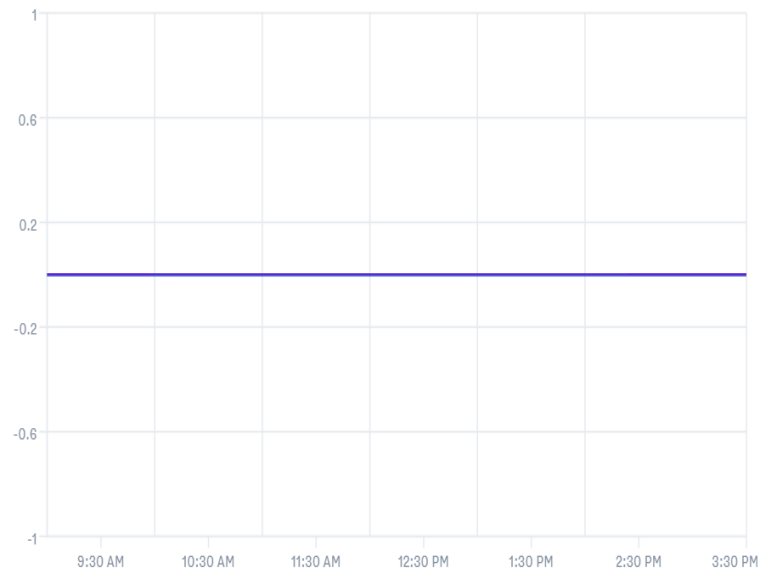

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/24/2024 9:30	5/24/2024 9:40	0.150	0	5	0
DW 2024	5/24/2024 9:40	5/24/2024 9:50	0.150	0.001	5	0
DW 2024	5/24/2024 9:50	5/24/2024 10:00	0.150	0.002	5	0
DW 2024	5/24/2024 10:00	5/24/2024 10:10	0.150	0.002	5	0
DW 2024	5/24/2024 10:10	5/24/2024 10:20	0.150	0.002	5	0
DW 2024	5/24/2024 10:20	5/24/2024 10:30	0.150	0.003	5	0
DW 2024	5/24/2024 10:30	5/24/2024 10:40	0.150	0.003	5	0
DW 2024	5/24/2024 10:40	5/24/2024 10:50	0.150	0.003	5	0
DW 2024	5/24/2024 10:50	5/24/2024 11:00	0.150	0.004	5	0
DW 2024	5/24/2024 11:00	5/24/2024 11:10	0.150	0.004	5	0
DW 2024	5/24/2024 11:10	5/24/2024 11:20	0.150	0.004	5	0
DW 2024	5/24/2024 11:20	5/24/2024 11:30	0.150	0.005	5	0
DW 2024	5/24/2024 11:30	5/24/2024 11:40	0.150	0.005	5	0
DW 2024	5/24/2024 11:40	5/24/2024 11:50	0.150	0.006	5	0
DW 2024	5/24/2024 11:50	5/24/2024 12:00	0.150	0.007	5	0
DW 2024	5/24/2024 12:00	5/24/2024 12:10	0.150	0.007	5	0
DW 2024	5/24/2024 12:10	5/24/2024 12:20	0.150	0.007	5	0
DW 2024	5/24/2024 12:20	5/24/2024 12:30	0.150	0.008	5	0
DW 2024	5/24/2024 12:30	5/24/2024 12:40	0.150	0.008	5	0
DW 2024	5/24/2024 12:40	5/24/2024 12:50	0.150	0.009	5	0
DW 2024	5/24/2024 12:50	5/24/2024 13:00	0.150	0.009	5	0
DW 2024	5/24/2024 13:00	5/24/2024 13:10	0.150	0.009	5	0
DW 2024	5/24/2024 13:10	5/24/2024 13:20	0.150	0.009	5	0
DW 2024	5/24/2024 13:20	5/24/2024 13:30	0.150	0.009	5	0
DW 2024	5/24/2024 13:30	5/24/2024 13:40	0.150	0.01	5	0
DW 2024	5/24/2024 13:40	5/24/2024 13:50	0.150	0.01	5	0
DW 2024	5/24/2024 13:50	5/24/2024 14:00	0.150	0.01	5	0
DW 2024	5/24/2024 14:00	5/24/2024 14:10	0.150	0.01	5	0
DW 2024	5/24/2024 14:10	5/24/2024 14:20	0.150	0.011	5	0
DW 2024	5/24/2024 14:20	5/24/2024 14:30	0.150	0.011	5	0
DW 2024	5/24/2024 14:30	5/24/2024 14:40	0.150	0.011	5	0
DW 2024	5/24/2024 14:40	5/24/2024 14:50	0.150	0.012	5	0
DW 2024	5/24/2024 14:50	5/24/2024 15:00	0.150	0.012	5	0
DW 2024	5/24/2024 15:00	5/24/2024 15:10	0.150	0.012	5	0
DW 2024	5/24/2024 15:10	5/24/2024 15:20	0.150	0.012	5	0
DW 2024	5/24/2024 15:20	5/24/2024 15:30	0.150	0.012	5	0
DW 2024	5/24/2024 15:30	5/24/2024 15:40	0.150	0.012	5	0
DW 2024	5/24/2024 15:40	5/24/2024 15:50	0.150	0.012	5	0
DW 2024	5/24/2024 15:50	5/24/2024 16:00	0.150	0.012	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/24/2024 9:00	5/24/2024 9:10	0.150	0.039	5	0
UW 2024	5/24/2024 9:10	5/24/2024 9:20	0.150	0.039	5	0
UW 2024	5/24/2024 9:20	5/24/2024 9:30	0.150	0.001	5	0
UW 2024	5/24/2024 9:30	5/24/2024 9:40	0.150	0.002	5	0
UW 2024	5/24/2024 9:40	5/24/2024 9:50	0.150	0.003	5	0
UW 2024	5/24/2024 9:50	5/24/2024 10:00	0.150	0.003	5	0
UW 2024	5/24/2024 10:00	5/24/2024 10:10	0.150	0.005	5	0
UW 2024	5/24/2024 10:10	5/24/2024 10:20	0.150	0.006	5	0
UW 2024	5/24/2024 10:20	5/24/2024 10:30	0.150	0.006	5	0
UW 2024	5/24/2024 10:30	5/24/2024 10:40	0.150	0.007	5	0
UW 2024	5/24/2024 10:40	5/24/2024 10:50	0.150	0.008	5	0
UW 2024	5/24/2024 10:50	5/24/2024 11:00	0.150	0.008	5	0
UW 2024	5/24/2024 11:00	5/24/2024 11:10	0.150	0.009	5	0
UW 2024	5/24/2024 11:10	5/24/2024 11:20	0.150	0.01	5	0
UW 2024	5/24/2024 11:20	5/24/2024 11:30	0.150	0.01	5	0
UW 2024	5/24/2024 11:30	5/24/2024 11:40	0.150	0.011	5	0
UW 2024	5/24/2024 11:40	5/24/2024 11:50	0.150	0.012	5	0
UW 2024	5/24/2024 11:50	5/24/2024 12:00	0.150	0.012	5	0
UW 2024	5/24/2024 12:00	5/24/2024 12:10	0.150	0.013	5	0
UW 2024	5/24/2024 12:10	5/24/2024 12:20	0.150	0.014	5	0
UW 2024	5/24/2024 12:20	5/24/2024 12:30	0.150	0.014	5	0
UW 2024	5/24/2024 12:30	5/24/2024 12:40	0.150	0.015	5	0
UW 2024	5/24/2024 12:40	5/24/2024 12:50	0.150	0.016	5	0
UW 2024	5/24/2024 12:50	5/24/2024 13:00	0.150	0.016	5	0
UW 2024	5/24/2024 13:00	5/24/2024 13:10	0.150	0.017	5	0
UW 2024	5/24/2024 13:10	5/24/2024 13:20	0.150	0.018	5	0
UW 2024	5/24/2024 13:20	5/24/2024 13:30	0.150	0.018	5	0
UW 2024	5/24/2024 13:30	5/24/2024 13:40	0.150	0.02	5	0
UW 2024	5/24/2024 13:40	5/24/2024 13:50	0.150	0.021	5	0
UW 2024	5/24/2024 13:50	5/24/2024 14:00	0.150	0.021	5	0
UW 2024	5/24/2024 14:00	5/24/2024 14:10	0.150	0.022	5	0
UW 2024	5/24/2024 14:10	5/24/2024 14:20	0.150	0.023	5	0
UW 2024	5/24/2024 14:20	5/24/2024 14:30	0.150	0.023	5	0
UW 2024	5/24/2024 14:30	5/24/2024 14:40	0.150	0.024	5	0
UW 2024	5/24/2024 14:40	5/24/2024 14:50	0.150	0.025	5	0
UW 2024	5/24/2024 14:50	5/24/2024 15:00	0.150	0.025	5	0
UW 2024	5/24/2024 15:00	5/24/2024 15:10	0.150	0.026	5	0
UW 2024	5/24/2024 15:10	5/24/2024 15:20	0.150	0.027	5	0
UW 2024	5/24/2024 15:20	5/24/2024 15:30	0.150	0.027	5	0
UW 2024	5/24/2024 15:30	5/24/2024 15:40	0.150	0.027	5	0
UW 2024	5/24/2024 15:40	5/24/2024 15:50	0.150	0	5	0
UW 2024	5/24/2024 15:50	5/24/2024 16:00	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/24/2024 9:30	5/24/2024 9:40	0.150	0	5	0
HS South	5/24/2024 9:40	5/24/2024 9:50	0.150	0	5	0
HS South	5/24/2024 9:50	5/24/2024 10:00	0.150	0.002	5	0
HS South	5/24/2024 10:00	5/24/2024 10:10	0.150	0.003	5	0
HS South	5/24/2024 10:10	5/24/2024 10:20	0.150	0.004	5	0
HS South	5/24/2024 10:20	5/24/2024 10:30	0.150	0.004	5	0
HS South	5/24/2024 10:30	5/24/2024 10:40	0.150	0.005	5	0
HS South	5/24/2024 10:40	5/24/2024 10:50	0.150	0.006	5	0
HS South	5/24/2024 10:50	5/24/2024 11:00	0.150	0.007	5	0
HS South	5/24/2024 11:00	5/24/2024 11:10	0.150	0.007	5	0
HS South	5/24/2024 11:10	5/24/2024 11:20	0.150	0.008	5	0
HS South	5/24/2024 11:20	5/24/2024 11:30	0.150	0.009	5	0
HS South	5/24/2024 11:30	5/24/2024 11:40	0.150	0.01	5	0
HS South	5/24/2024 11:40	5/24/2024 11:50	0.150	0.011	5	0
HS South	5/24/2024 11:50	5/24/2024 12:00	0.150	0.011	5	0
HS South	5/24/2024 12:00	5/24/2024 12:10	0.150	0.012	5	0
HS South	5/24/2024 12:10	5/24/2024 12:20	0.150	0.013	5	0
HS South	5/24/2024 12:20	5/24/2024 12:30	0.150	0.014	5	0
HS South	5/24/2024 12:30	5/24/2024 12:40	0.150	0.014	5	0
HS South	5/24/2024 12:40	5/24/2024 12:50	0.150	0.015	5	0
HS South	5/24/2024 12:50	5/24/2024 13:00	0.150	0.016	5	0
HS South	5/24/2024 13:00	5/24/2024 13:10	0.150	0.017	5	0
HS South	5/24/2024 13:10	5/24/2024 13:20	0.150	0.018	5	0
HS South	5/24/2024 13:20	5/24/2024 13:30	0.150	0.019	5	0
HS South	5/24/2024 13:30	5/24/2024 13:40	0.150	0.02	5	0
HS South	5/24/2024 13:40	5/24/2024 13:50	0.150	0.02	5	0
HS South	5/24/2024 13:50	5/24/2024 14:00	0.150	0.021	5	0
HS South	5/24/2024 14:00	5/24/2024 14:10	0.150	0.022	5	0
HS South	5/24/2024 14:10	5/24/2024 14:20	0.150	0.023	5	0
HS South	5/24/2024 14:20	5/24/2024 14:30	0.150	0.024	5	0
HS South	5/24/2024 14:30	5/24/2024 14:40	0.150	0.025	5	0
HS South	5/24/2024 14:40	5/24/2024 14:50	0.150	0.026	5	0
HS South	5/24/2024 14:50	5/24/2024 15:00	0.150	0.026	5	0
HS South	5/24/2024 15:00	5/24/2024 15:10	0.150	0.027	5	0
HS South	5/24/2024 15:10	5/24/2024 15:20	0.150	0.028	5	0
HS South	5/24/2024 15:20	5/24/2024 15:30	0.150	0.028	5	0
HS South	5/24/2024 15:30	5/24/2024 15:40	0.150	0.029	5	0
HS South	5/24/2024 15:40	5/24/2024 15:50	0.150	0.029	5	0
HS South	5/24/2024 15:50	5/24/2024 16:00	0.150	0.029	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/24/2024 9:00	5/24/2024 9:10	0.150	0.021	5	0
PER2 2024	5/24/2024 9:10	5/24/2024 9:20	0.150	0.021	5	0
PER2 2024	5/24/2024 9:20	5/24/2024 9:30	0.150	0.025	5	0
PER2 2024	5/24/2024 9:30	5/24/2024 9:40	0.150	0.001	5	0
PER2 2024	5/24/2024 9:40	5/24/2024 9:50	0.150	0.001	5	0
PER2 2024	5/24/2024 9:50	5/24/2024 10:00	0.150	0.001	5	0
PER2 2024	5/24/2024 10:00	5/24/2024 10:10	0.150	0.002	5	0
PER2 2024	5/24/2024 10:10	5/24/2024 10:20	0.150	0.002	5	0
PER2 2024	5/24/2024 10:20	5/24/2024 10:30	0.150	0.002	5	0
PER2 2024	5/24/2024 10:30	5/24/2024 10:40	0.150	0.003	5	0
PER2 2024	5/24/2024 10:40	5/24/2024 10:50	0.150	0.003	5	0
PER2 2024	5/24/2024 10:50	5/24/2024 11:00	0.150	0.003	5	0
PER2 2024	5/24/2024 11:00	5/24/2024 11:10	0.150	0.004	5	0
PER2 2024	5/24/2024 11:10	5/24/2024 11:20	0.150	0.004	5	0
PER2 2024	5/24/2024 11:20	5/24/2024 11:30	0.150	0.004	5	0
PER2 2024	5/24/2024 11:30	5/24/2024 11:40	0.150	0.005	5	0
PER2 2024	5/24/2024 11:40	5/24/2024 11:50	0.150	0.005	5	0
PER2 2024	5/24/2024 11:50	5/24/2024 12:00	0.150	0.005	5	0
PER2 2024	5/24/2024 12:00	5/24/2024 12:10	0.150	0.005	5	0
PER2 2024	5/24/2024 12:10	5/24/2024 12:20	0.150	0.005	5	0
PER2 2024	5/24/2024 12:20	5/24/2024 12:30	0.150	0.005	5	0
PER2 2024	5/24/2024 12:30	5/24/2024 12:40	0.150	0.005	5	0
PER2 2024	5/24/2024 12:40	5/24/2024 12:50	0.150	0.005	5	0
PER2 2024	5/24/2024 12:50	5/24/2024 13:00	0.150	0.005	5	0
PER2 2024	5/24/2024 13:00	5/24/2024 13:10	0.150	0.005	5	0
PER2 2024	5/24/2024 13:10	5/24/2024 13:20	0.150	0.005	5	0
PER2 2024	5/24/2024 13:20	5/24/2024 13:30	0.150	0.005	5	0
PER2 2024	5/24/2024 13:30	5/24/2024 13:40	0.150	0.005	5	0
PER2 2024	5/24/2024 13:40	5/24/2024 13:50	0.150	0.005	5	0
PER2 2024	5/24/2024 13:50	5/24/2024 14:00	0.150	0.005	5	0
PER2 2024	5/24/2024 14:00	5/24/2024 14:10	0.150	0.005	5	0
PER2 2024	5/24/2024 14:10	5/24/2024 14:20	0.150	0.005	5	0
PER2 2024	5/24/2024 14:20	5/24/2024 14:30	0.150	0.005	5	0
PER2 2024	5/24/2024 14:30	5/24/2024 14:40	0.150	0.005	5	0
PER2 2024	5/24/2024 14:40	5/24/2024 14:50	0.150	0.005	5	0
PER2 2024	5/24/2024 14:50	5/24/2024 15:00	0.150	0.005	5	0
PER2 2024	5/24/2024 15:00	5/24/2024 15:10	0.150	0.005	5	0
PER2 2024	5/24/2024 15:10	5/24/2024 15:20	0.150	0.005	5	0
PER2 2024	5/24/2024 15:20	5/24/2024 15:30	0.150	0.005	5	0
PER2 2024	5/24/2024 15:30	5/24/2024 15:40	0.150	0.005	5	0
PER2 2024	5/24/2024 15:40	5/24/2024 15:50	0.150	0.005	5	0
PER2 2024	5/24/2024 15:50	5/24/2024 16:00	0.150	0.005	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/24/2024 9:00	5/24/2024 9:10	0.150	0	5	0.013
PER1 2024	5/24/2024 9:10	5/24/2024 9:20	0.150	0	5	0.026
PER1 2024	5/24/2024 9:20	5/24/2024 9:30	0.150	0	5	0.082
PER1 2024	5/24/2024 9:30	5/24/2024 9:40	0.150	0	5	0.097
PER1 2024	5/24/2024 9:40	5/24/2024 9:50	0.150	0	5	0.128
PER1 2024	5/24/2024 9:50	5/24/2024 10:00	0.150	0	5	0.162
PER1 2024	5/24/2024 10:00	5/24/2024 10:10	0.150	0	5	0.199
PER1 2024	5/24/2024 10:10	5/24/2024 10:20	0.150	0	5	0.207
PER1 2024	5/24/2024 10:20	5/24/2024 10:30	0.150	0	5	0.208
PER1 2024	5/24/2024 10:30	5/24/2024 10:40	0.150	0	5	0.234
PER1 2024	5/24/2024 10:40	5/24/2024 10:50	0.150	0	5	0.245
PER1 2024	5/24/2024 10:50	5/24/2024 11:00	0.150	0.001	5	0.284
PER1 2024	5/24/2024 11:00	5/24/2024 11:10	0.150	0.001	5	0.355
PER1 2024	5/24/2024 11:10	5/24/2024 11:20	0.150	0.001	5	0.416
PER1 2024	5/24/2024 11:20	5/24/2024 11:30	0.150	0.001	5	0.424
PER1 2024	5/24/2024 11:30	5/24/2024 11:40	0.150	0.001	5	1.098
PER1 2024	5/24/2024 11:40	5/24/2024 11:50	0.150	0.001	5	1.118
PER1 2024	5/24/2024 11:50	5/24/2024 12:00	0.150	0.001	5	1.152
PER1 2024	5/24/2024 12:00	5/24/2024 12:10	0.150	0.001	5	1.161
PER1 2024	5/24/2024 12:10	5/24/2024 12:20	0.150	0.002	5	1.164
PER1 2024	5/24/2024 12:20	5/24/2024 12:30	0.150	0.002	5	1.167
PER1 2024	5/24/2024 12:30	5/24/2024 12:40	0.150	0.002	5	1.174
PER1 2024	5/24/2024 12:40	5/24/2024 12:50	0.150	0.002	5	1.183
PER1 2024	5/24/2024 12:50	5/24/2024 13:00	0.150	0.002	5	1.185
PER1 2024	5/24/2024 13:00	5/24/2024 13:10	0.150	0.003	5	1.187
PER1 2024	5/24/2024 13:10	5/24/2024 13:20	0.150	0.003	5	1.187
PER1 2024	5/24/2024 13:20	5/24/2024 13:30	0.150	0.003	5	1.187
PER1 2024	5/24/2024 13:30	5/24/2024 13:40	0.150	0.003	5	1.187
PER1 2024	5/24/2024 13:40	5/24/2024 13:50	0.150	0.003	5	1.2
PER1 2024	5/24/2024 13:50	5/24/2024 14:00	0.150	0.004	5	1.201
PER1 2024	5/24/2024 14:00	5/24/2024 14:10	0.150	0.004	5	1.208
PER1 2024	5/24/2024 14:10	5/24/2024 14:20	0.150	0.004	5	1.209
PER1 2024	5/24/2024 14:20	5/24/2024 14:30	0.150	0.004	5	1.209
PER1 2024	5/24/2024 14:30	5/24/2024 14:40	0.150	0.005	5	1.209
PER1 2024	5/24/2024 14:40	5/24/2024 14:50	0.150	0.005	5	1.209
PER1 2024	5/24/2024 14:50	5/24/2024 15:00	0.150	0.005	5	1.209
PER1 2024	5/24/2024 15:00	5/24/2024 15:10	0.150	0.005	5	1.209
PER1 2024	5/24/2024 15:10	5/24/2024 15:20	0.150	0.005	5	1.209
PER1 2024	5/24/2024 15:20	5/24/2024 15:30	0.150	0.005	5	1.209
PER1 2024	5/24/2024 15:30	5/24/2024 15:40	0.150	0.005	5	0
PER1 2024	5/24/2024 15:40	5/24/2024 15:50	0.150	0	5	0
PER1 2024	5/24/2024 15:50	5/24/2024 16:00	0.150	0	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/28/2024 Weather: 75 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued vertical form installation for building construction. 2) ECD continues to advance the remedial excavation to the east. 3) Export of 3 loads (~60 CY) of material from the remedial excavation for off-site disposal at the Bayshore Soil Management facility. 4) The dewatering system was utilized only for the duration of excavation. 5) The Site was closed the previous day, May 27th, for the Memorial Day Holiday.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	60	0
Total:(CY)	4485	0	8685	1780	4140

Site Layout Map and Excavation Figures

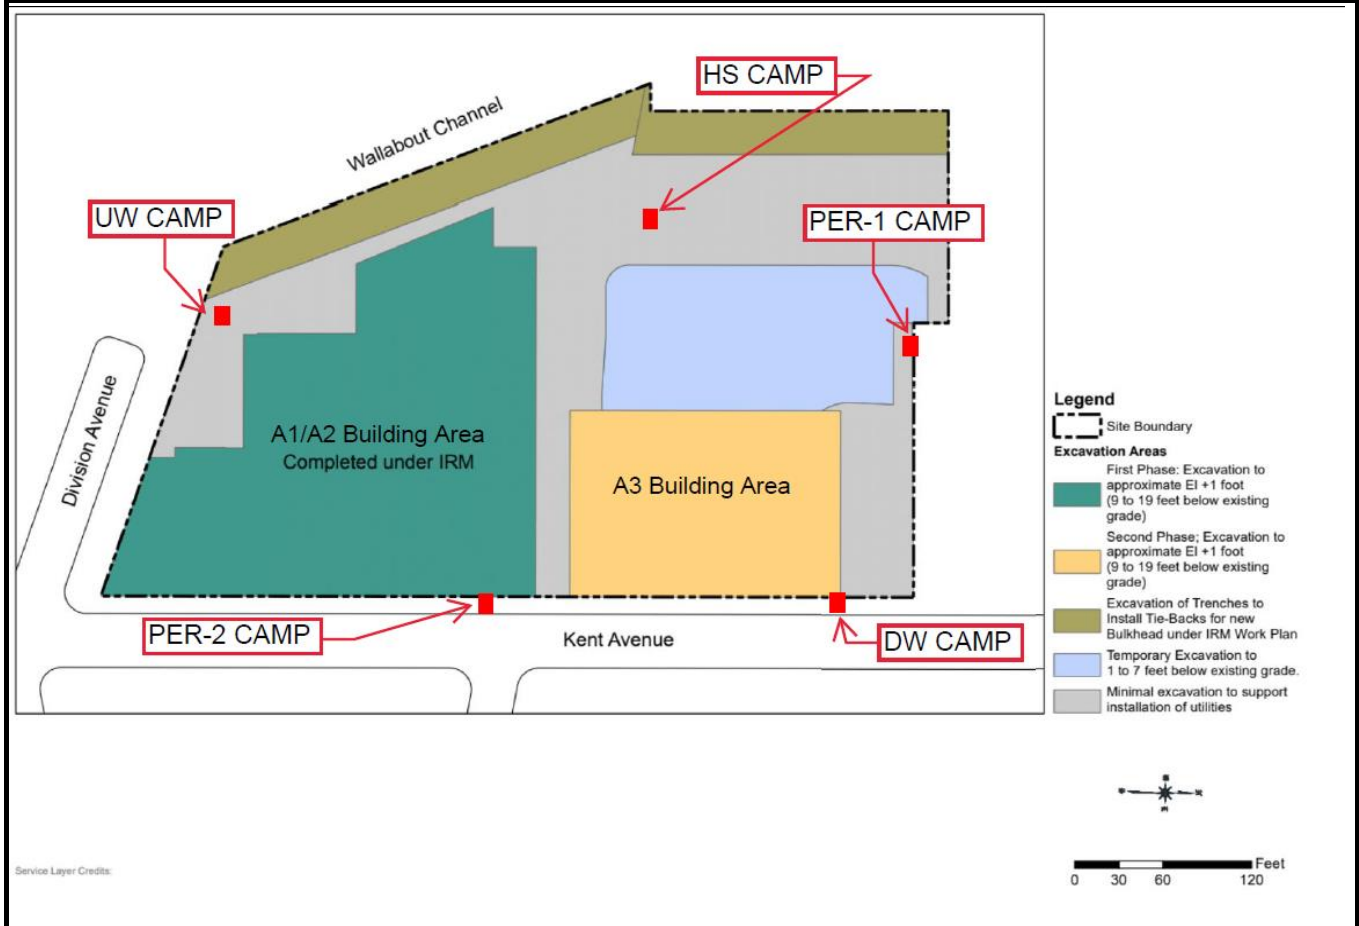

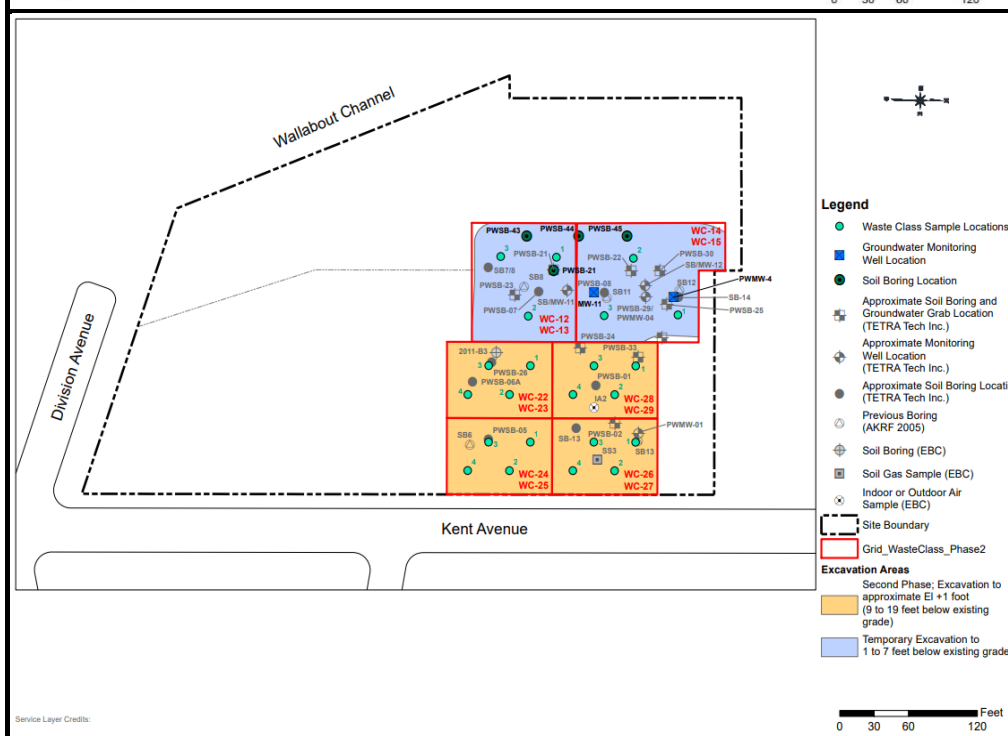
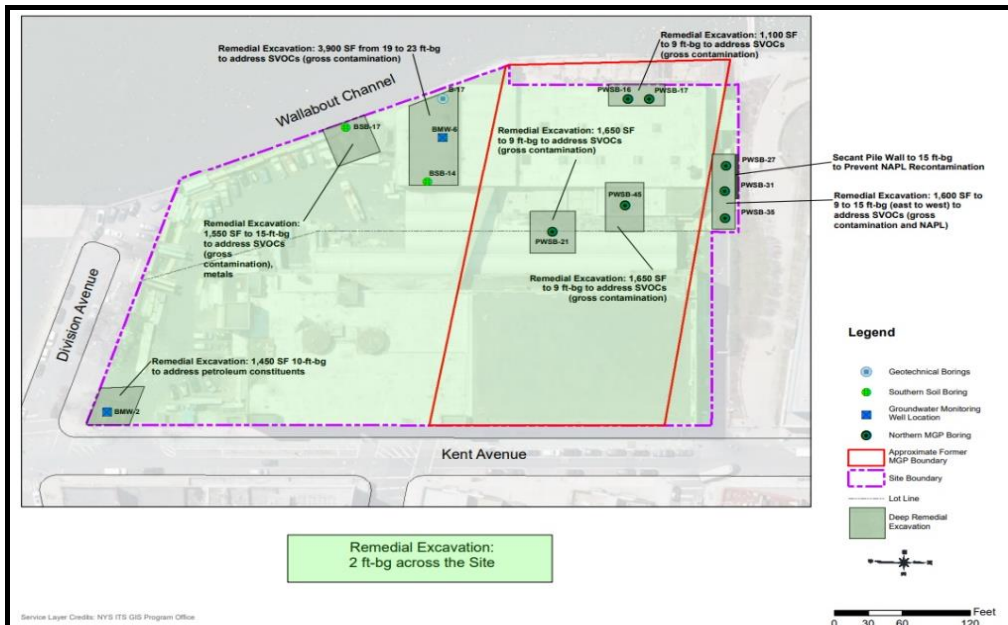


Photo 1:

View of truck loading with soil from the remedial excavation for off-site disposal to the Bayshore Soil Management facility.



Photo 2:

View of the remedial excavation facing west.



Photo 3:


View of continued excavation and concrete demolition for the remedial excavation facing west.



Photo 4:

View of truck loading with soil from the remedial excavation for off-site disposal to the Bayshore Soil Management facility




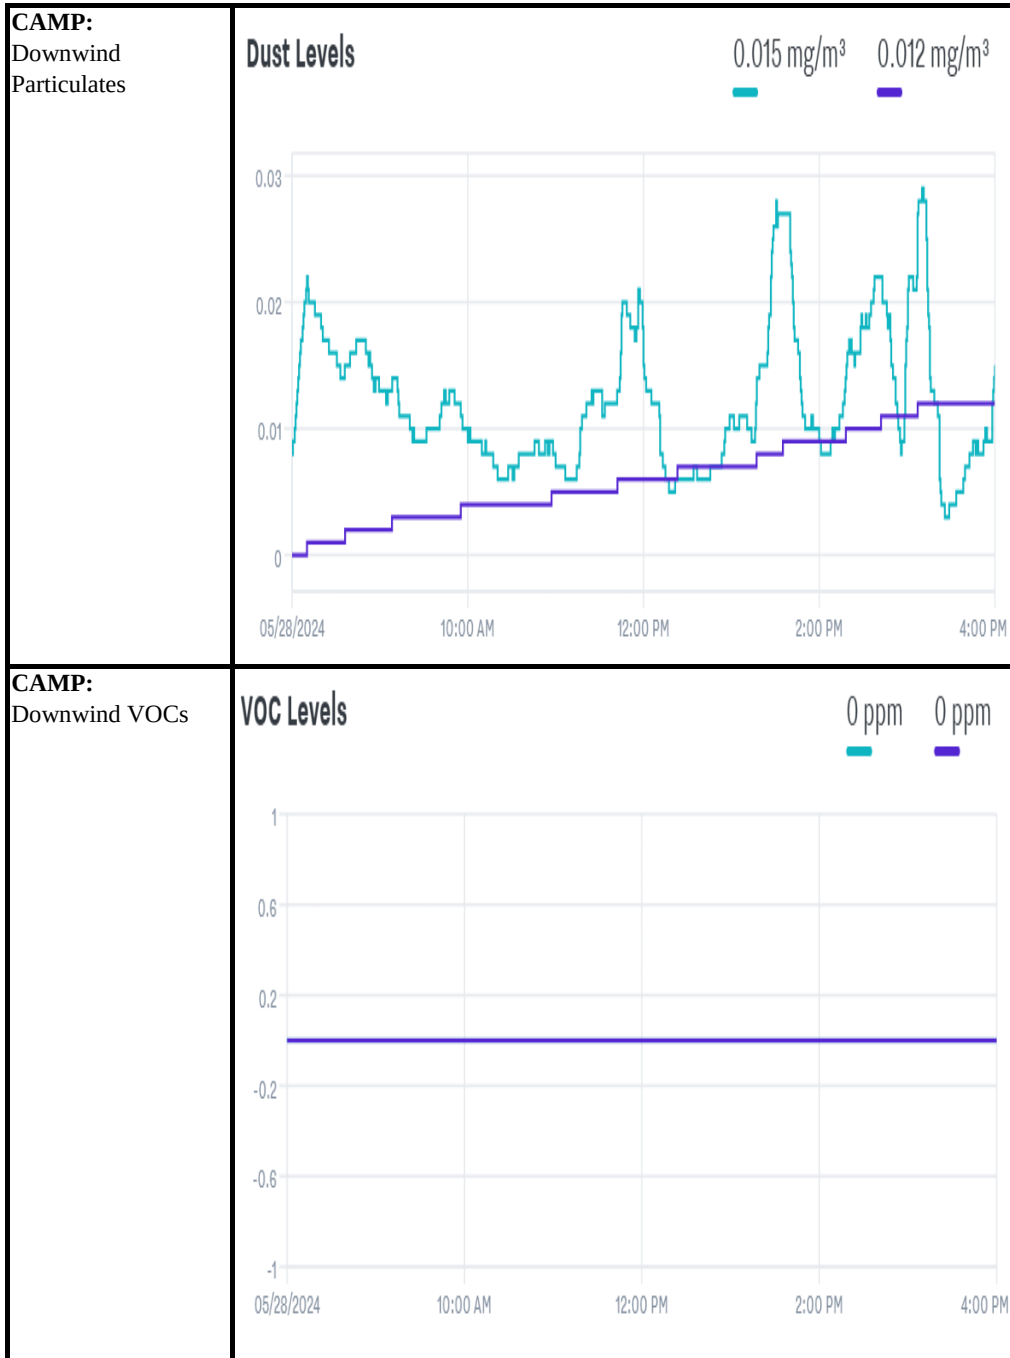

CAMP:
Upwind Particulates

Dust Levels

0.028 mg/m³ 0.038 mg/m³

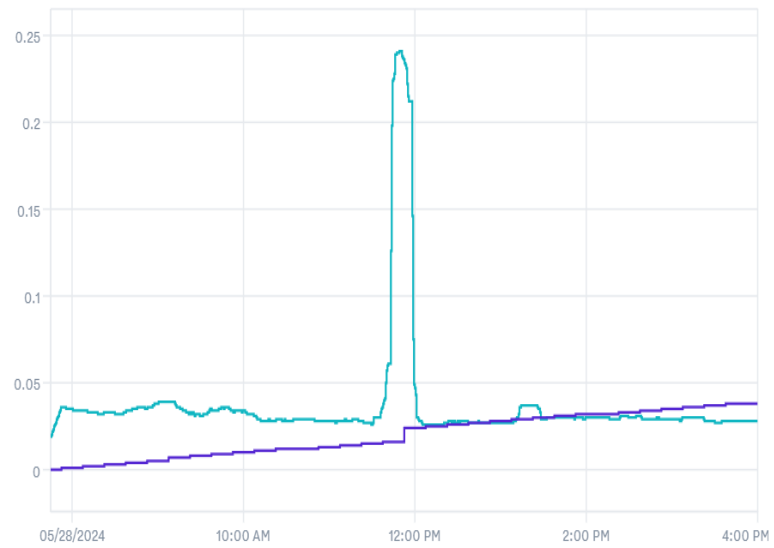

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm



Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/28/2024 8:00	5/28/2024 8:10	0.150	0	5	0
DW 2024	5/28/2024 8:10	5/28/2024 8:20	0.150	0.001	5	0
DW 2024	5/28/2024 8:20	5/28/2024 8:30	0.150	0.001	5	0
DW 2024	5/28/2024 8:30	5/28/2024 8:40	0.150	0.002	5	0
DW 2024	5/28/2024 8:40	5/28/2024 8:50	0.150	0.002	5	0
DW 2024	5/28/2024 8:50	5/28/2024 9:00	0.150	0.002	5	0
DW 2024	5/28/2024 9:00	5/28/2024 9:10	0.150	0.003	5	0
DW 2024	5/28/2024 9:10	5/28/2024 9:20	0.150	0.003	5	0
DW 2024	5/28/2024 9:20	5/28/2024 9:30	0.150	0.003	5	0
DW 2024	5/28/2024 9:30	5/28/2024 9:40	0.150	0.003	5	0
DW 2024	5/28/2024 9:40	5/28/2024 9:50	0.150	0.003	5	0
DW 2024	5/28/2024 9:50	5/28/2024 10:00	0.150	0.004	5	0
DW 2024	5/28/2024 10:00	5/28/2024 10:10	0.150	0.004	5	0
DW 2024	5/28/2024 10:10	5/28/2024 10:20	0.150	0.004	5	0
DW 2024	5/28/2024 10:20	5/28/2024 10:30	0.150	0.004	5	0
DW 2024	5/28/2024 10:30	5/28/2024 10:40	0.150	0.004	5	0
DW 2024	5/28/2024 10:40	5/28/2024 10:50	0.150	0.004	5	0
DW 2024	5/28/2024 10:50	5/28/2024 11:00	0.150	0.005	5	0
DW 2024	5/28/2024 11:00	5/28/2024 11:10	0.150	0.005	5	0
DW 2024	5/28/2024 11:10	5/28/2024 11:20	0.150	0.005	5	0
DW 2024	5/28/2024 11:20	5/28/2024 11:30	0.150	0.005	5	0
DW 2024	5/28/2024 11:30	5/28/2024 11:40	0.150	0.005	5	0
DW 2024	5/28/2024 11:40	5/28/2024 11:50	0.150	0.006	5	0
DW 2024	5/28/2024 11:50	5/28/2024 12:00	0.150	0.006	5	0
DW 2024	5/28/2024 12:00	5/28/2024 12:10	0.150	0.006	5	0
DW 2024	5/28/2024 12:10	5/28/2024 12:20	0.150	0.006	5	0
DW 2024	5/28/2024 12:20	5/28/2024 12:30	0.150	0.007	5	0
DW 2024	5/28/2024 12:30	5/28/2024 12:40	0.150	0.007	5	0
DW 2024	5/28/2024 12:40	5/28/2024 12:50	0.150	0.007	5	0
DW 2024	5/28/2024 12:50	5/28/2024 13:00	0.150	0.007	5	0
DW 2024	5/28/2024 13:00	5/28/2024 13:10	0.150	0.007	5	0
DW 2024	5/28/2024 13:10	5/28/2024 13:20	0.150	0.008	5	0
DW 2024	5/28/2024 13:20	5/28/2024 13:30	0.150	0.008	5	0
DW 2024	5/28/2024 13:30	5/28/2024 13:40	0.150	0.009	5	0
DW 2024	5/28/2024 13:40	5/28/2024 13:50	0.150	0.009	5	0
DW 2024	5/28/2024 13:50	5/28/2024 14:00	0.150	0.009	5	0
DW 2024	5/28/2024 14:00	5/28/2024 14:10	0.150	0.009	5	0
DW 2024	5/28/2024 14:10	5/28/2024 14:20	0.150	0.01	5	0
DW 2024	5/28/2024 14:20	5/28/2024 14:30	0.150	0.01	5	0
DW 2024	5/28/2024 14:30	5/28/2024 14:40	0.150	0.01	5	0
DW 2024	5/28/2024 14:40	5/28/2024 14:50	0.150	0.011	5	0
DW 2024	5/28/2024 14:50	5/28/2024 15:00	0.150	0.011	5	0
DW 2024	5/28/2024 15:00	5/28/2024 15:10	0.150	0.012	5	0
DW 2024	5/28/2024 15:10	5/28/2024 15:20	0.150	0.012	5	0
DW 2024	5/28/2024 15:20	5/28/2024 15:30	0.150	0.012	5	0
DW 2024	5/28/2024 15:30	5/28/2024 15:40	0.150	0.012	5	0
DW 2024	5/28/2024 15:40	5/28/2024 15:50	0.150	0.012	5	0
DW 2024	5/28/2024 15:50	5/28/2024 16:00	0.150	0.012	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/28/2024 8:00	5/28/2024 8:10	0.150	0.002	5	0
UW 2024	5/28/2024 8:10	5/28/2024 8:20	0.150	0.002	5	0
UW 2024	5/28/2024 8:20	5/28/2024 8:30	0.150	0.003	5	0
UW 2024	5/28/2024 8:30	5/28/2024 8:40	0.150	0.004	5	0
UW 2024	5/28/2024 8:40	5/28/2024 8:50	0.150	0.004	5	0
UW 2024	5/28/2024 8:50	5/28/2024 9:00	0.150	0.005	5	0
UW 2024	5/28/2024 9:00	5/28/2024 9:10	0.150	0.007	5	0
UW 2024	5/28/2024 9:10	5/28/2024 9:20	0.150	0.007	5	0
UW 2024	5/28/2024 9:20	5/28/2024 9:30	0.150	0.008	5	0
UW 2024	5/28/2024 9:30	5/28/2024 9:40	0.150	0.009	5	0
UW 2024	5/28/2024 9:40	5/28/2024 9:50	0.150	0.009	5	0
UW 2024	5/28/2024 9:50	5/28/2024 10:00	0.150	0.01	5	0
UW 2024	5/28/2024 10:00	5/28/2024 10:10	0.150	0.011	5	0
UW 2024	5/28/2024 10:10	5/28/2024 10:20	0.150	0.011	5	0
UW 2024	5/28/2024 10:20	5/28/2024 10:30	0.150	0.012	5	0
UW 2024	5/28/2024 10:30	5/28/2024 10:40	0.150	0.012	5	0
UW 2024	5/28/2024 10:40	5/28/2024 10:50	0.150	0.012	5	0
UW 2024	5/28/2024 10:50	5/28/2024 11:00	0.150	0.013	5	0
UW 2024	5/28/2024 11:00	5/28/2024 11:10	0.150	0.014	5	0
UW 2024	5/28/2024 11:10	5/28/2024 11:20	0.150	0.014	5	0
UW 2024	5/28/2024 11:20	5/28/2024 11:30	0.150	0.015	5	0
UW 2024	5/28/2024 11:30	5/28/2024 11:40	0.150	0.016	5	0
UW 2024	5/28/2024 11:40	5/28/2024 11:50	0.150	0.016	5	0
UW 2024	5/28/2024 11:50	5/28/2024 12:00	0.150	0.024	5	0
UW 2024	5/28/2024 12:00	5/28/2024 12:10	0.150	0.025	5	0
UW 2024	5/28/2024 12:10	5/28/2024 12:20	0.150	0.025	5	0
UW 2024	5/28/2024 12:20	5/28/2024 12:30	0.150	0.026	5	0
UW 2024	5/28/2024 12:30	5/28/2024 12:40	0.150	0.027	5	0
UW 2024	5/28/2024 12:40	5/28/2024 12:50	0.150	0.027	5	0
UW 2024	5/28/2024 12:50	5/28/2024 13:00	0.150	0.028	5	0
UW 2024	5/28/2024 13:00	5/28/2024 13:10	0.150	0.029	5	0
UW 2024	5/28/2024 13:10	5/28/2024 13:20	0.150	0.029	5	0
UW 2024	5/28/2024 13:20	5/28/2024 13:30	0.150	0.03	5	0
UW 2024	5/28/2024 13:30	5/28/2024 13:40	0.150	0.031	5	0
UW 2024	5/28/2024 13:40	5/28/2024 13:50	0.150	0.031	5	0
UW 2024	5/28/2024 13:50	5/28/2024 14:00	0.150	0.032	5	0
UW 2024	5/28/2024 14:00	5/28/2024 14:10	0.150	0.032	5	0
UW 2024	5/28/2024 14:10	5/28/2024 14:20	0.150	0.032	5	0
UW 2024	5/28/2024 14:20	5/28/2024 14:30	0.150	0.033	5	0
UW 2024	5/28/2024 14:30	5/28/2024 14:40	0.150	0.034	5	0
UW 2024	5/28/2024 14:40	5/28/2024 14:50	0.150	0.034	5	0
UW 2024	5/28/2024 14:50	5/28/2024 15:00	0.150	0.035	5	0
UW 2024	5/28/2024 15:00	5/28/2024 15:10	0.150	0.036	5	0
UW 2024	5/28/2024 15:10	5/28/2024 15:20	0.150	0.036	5	0
UW 2024	5/28/2024 15:20	5/28/2024 15:30	0.150	0.037	5	0
UW 2024	5/28/2024 15:30	5/28/2024 15:40	0.150	0.038	5	0
UW 2024	5/28/2024 15:40	5/28/2024 15:50	0.150	0.038	5	0
UW 2024	5/28/2024 15:50	5/28/2024 16:00	0.150	0.038	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/28/2024 8:00	5/28/2024 8:10	0.150	0.002	5	0
HS South	5/28/2024 8:10	5/28/2024 8:20	0.150	0.002	5	0
HS South	5/28/2024 8:20	5/28/2024 8:30	0.150	0.003	5	0
HS South	5/28/2024 8:30	5/28/2024 8:40	0.150	0.004	5	0
HS South	5/28/2024 8:40	5/28/2024 8:50	0.150	0.005	5	0
HS South	5/28/2024 8:50	5/28/2024 9:00	0.150	0.006	5	0
HS South	5/28/2024 9:00	5/28/2024 9:10	0.150	0.006	5	0
HS South	5/28/2024 9:10	5/28/2024 9:20	0.150	0.007	5	0
HS South	5/28/2024 9:20	5/28/2024 9:30	0.150	0.008	5	0
HS South	5/28/2024 9:30	5/28/2024 9:40	0.150	0.009	5	0
HS South	5/28/2024 9:40	5/28/2024 9:50	0.150	0.01	5	0
HS South	5/28/2024 9:50	5/28/2024 10:00	0.150	0.01	5	0
HS South	5/28/2024 10:00	5/28/2024 10:10	0.150	0.011	5	0
HS South	5/28/2024 10:10	5/28/2024 10:20	0.150	0.012	5	0
HS South	5/28/2024 10:20	5/28/2024 10:30	0.150	0.012	5	0
HS South	5/28/2024 10:30	5/28/2024 10:40	0.150	0.013	5	0
HS South	5/28/2024 10:40	5/28/2024 10:50	0.150	0.014	5	0
HS South	5/28/2024 10:50	5/28/2024 11:00	0.150	0.014	5	0
HS South	5/28/2024 11:00	5/28/2024 11:10	0.150	0.015	5	0
HS South	5/28/2024 11:10	5/28/2024 11:20	0.150	0.016	5	0
HS South	5/28/2024 11:20	5/28/2024 11:30	0.150	0.017	5	0
HS South	5/28/2024 11:30	5/28/2024 11:40	0.150	0.018	5	0
HS South	5/28/2024 11:40	5/28/2024 11:50	0.150	0.019	5	0
HS South	5/28/2024 11:50	5/28/2024 12:00	0.150	0.019	5	0
HS South	5/28/2024 12:00	5/28/2024 12:10	0.150	0.02	5	0
HS South	5/28/2024 12:10	5/28/2024 12:20	0.150	0.02	5	0
HS South	5/28/2024 12:20	5/28/2024 12:30	0.150	0.021	5	0
HS South	5/28/2024 12:30	5/28/2024 12:40	0.150	0.022	5	0
HS South	5/28/2024 12:40	5/28/2024 12:50	0.150	0.022	5	0
HS South	5/28/2024 12:50	5/28/2024 13:00	0.150	0.023	5	0
HS South	5/28/2024 13:00	5/28/2024 13:10	0.150	0.023	5	0
HS South	5/28/2024 13:10	5/28/2024 13:20	0.150	0.024	5	0
HS South	5/28/2024 13:20	5/28/2024 13:30	0.150	0.025	5	0
HS South	5/28/2024 13:30	5/28/2024 13:40	0.150	0.026	5	0
HS South	5/28/2024 13:40	5/28/2024 13:50	0.150	0.028	5	0
HS South	5/28/2024 13:50	5/28/2024 14:00	0.150	0.028	5	0
HS South	5/28/2024 14:00	5/28/2024 14:10	0.150	0.029	5	0
HS South	5/28/2024 14:10	5/28/2024 14:20	0.150	0.03	5	0
HS South	5/28/2024 14:20	5/28/2024 14:30	0.150	0.032	5	0
HS South	5/28/2024 14:30	5/28/2024 14:40	0.150	0.033	5	0
HS South	5/28/2024 14:40	5/28/2024 14:50	0.150	0.034	5	0
HS South	5/28/2024 14:50	5/28/2024 15:00	0.150	0.035	5	0
HS South	5/28/2024 15:00	5/28/2024 15:10	0.150	0.036	5	0
HS South	5/28/2024 15:10	5/28/2024 15:20	0.150	0.037	5	0
HS South	5/28/2024 15:20	5/28/2024 15:30	0.150	0.038	5	0
HS South	5/28/2024 15:30	5/28/2024 15:40	0.150	0.038	5	0
HS South	5/28/2024 15:40	5/28/2024 15:50	0.150	0.039	5	0
HS South	5/28/2024 15:50	5/28/2024 16:00	0.150	0.039	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/28/2024 8:00	5/28/2024 8:10	0.150	0	5	0
PER2 2024	5/28/2024 8:10	5/28/2024 8:20	0.150	0.001	5	0
PER2 2024	5/28/2024 8:20	5/28/2024 8:30	0.150	0.001	5	0
PER2 2024	5/28/2024 8:30	5/28/2024 8:40	0.150	0.001	5	0
PER2 2024	5/28/2024 8:40	5/28/2024 8:50	0.150	0.002	5	0
PER2 2024	5/28/2024 8:50	5/28/2024 9:00	0.150	0.002	5	0
PER2 2024	5/28/2024 9:00	5/28/2024 9:10	0.150	0.002	5	0
PER2 2024	5/28/2024 9:10	5/28/2024 9:20	0.150	0.003	5	0
PER2 2024	5/28/2024 9:20	5/28/2024 9:30	0.150	0.003	5	0
PER2 2024	5/28/2024 9:30	5/28/2024 9:40	0.150	0.003	5	0
PER2 2024	5/28/2024 9:40	5/28/2024 9:50	0.150	0.003	5	0
PER2 2024	5/28/2024 9:50	5/28/2024 10:00	0.150	0.003	5	0
PER2 2024	5/28/2024 10:00	5/28/2024 10:10	0.150	0.004	5	0
PER2 2024	5/28/2024 10:10	5/28/2024 10:20	0.150	0.004	5	0
PER2 2024	5/28/2024 10:20	5/28/2024 10:30	0.150	0.004	5	0
PER2 2024	5/28/2024 10:30	5/28/2024 10:40	0.150	0.004	5	0
PER2 2024	5/28/2024 10:40	5/28/2024 10:50	0.150	0.004	5	0
PER2 2024	5/28/2024 10:50	5/28/2024 11:00	0.150	0.004	5	0
PER2 2024	5/28/2024 11:00	5/28/2024 11:10	0.150	0.005	5	0
PER2 2024	5/28/2024 11:10	5/28/2024 11:20	0.150	0.005	5	0
PER2 2024	5/28/2024 11:20	5/28/2024 11:30	0.150	0.005	5	0
PER2 2024	5/28/2024 11:30	5/28/2024 11:40	0.150	0.005	5	0
PER2 2024	5/28/2024 11:40	5/28/2024 11:50	0.150	0.005	5	0
PER2 2024	5/28/2024 11:50	5/28/2024 12:00	0.150	0.006	5	0
PER2 2024	5/28/2024 12:00	5/28/2024 12:10	0.150	0.006	5	0
PER2 2024	5/28/2024 12:10	5/28/2024 12:20	0.150	0.006	5	0
PER2 2024	5/28/2024 12:20	5/28/2024 12:30	0.150	0.006	5	0
PER2 2024	5/28/2024 12:30	5/28/2024 12:40	0.150	0.007	5	0
PER2 2024	5/28/2024 12:40	5/28/2024 12:50	0.150	0.007	5	0
PER2 2024	5/28/2024 12:50	5/28/2024 13:00	0.150	0.007	5	0
PER2 2024	5/28/2024 13:00	5/28/2024 13:10	0.150	0.008	5	0
PER2 2024	5/28/2024 13:10	5/28/2024 13:20	0.150	0.008	5	0
PER2 2024	5/28/2024 13:20	5/28/2024 13:30	0.150	0.008	5	0
PER2 2024	5/28/2024 13:30	5/28/2024 13:40	0.150	0.009	5	0
PER2 2024	5/28/2024 13:40	5/28/2024 13:50	0.150	0.01	5	0
PER2 2024	5/28/2024 13:50	5/28/2024 14:00	0.150	0.01	5	0
PER2 2024	5/28/2024 14:00	5/28/2024 14:10	0.150	0.01	5	0
PER2 2024	5/28/2024 14:10	5/28/2024 14:20	0.150	0.011	5	0
PER2 2024	5/28/2024 14:20	5/28/2024 14:30	0.150	0.011	5	0
PER2 2024	5/28/2024 14:30	5/28/2024 14:40	0.150	0.012	5	0
PER2 2024	5/28/2024 14:40	5/28/2024 14:50	0.150	0.012	5	0
PER2 2024	5/28/2024 14:50	5/28/2024 15:00	0.150	0.013	5	0
PER2 2024	5/28/2024 15:00	5/28/2024 15:10	0.150	0.013	5	0
PER2 2024	5/28/2024 15:10	5/28/2024 15:20	0.150	0.014	5	0
PER2 2024	5/28/2024 15:20	5/28/2024 15:30	0.150	0.014	5	0
PER2 2024	5/28/2024 15:30	5/28/2024 15:40	0.150	0.014	5	0
PER2 2024	5/28/2024 15:40	5/28/2024 15:50	0.150	0.015	5	0
PER2 2024	5/28/2024 15:50	5/28/2024 16:00	0.150	0.015	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/28/2024 8:00	5/28/2024 8:10	0.150	0	5	0
PER1 2024	5/28/2024 8:10	5/28/2024 8:20	0.150	0	5	0
PER1 2024	5/28/2024 8:20	5/28/2024 8:30	0.150	0	5	0
PER1 2024	5/28/2024 8:30	5/28/2024 8:40	0.150	0.001	5	0
PER1 2024	5/28/2024 8:40	5/28/2024 8:50	0.150	0.001	5	0
PER1 2024	5/28/2024 8:50	5/28/2024 9:00	0.150	0.001	5	0
PER1 2024	5/28/2024 9:00	5/28/2024 9:10	0.150	0.001	5	0
PER1 2024	5/28/2024 9:10	5/28/2024 9:20	0.150	0.001	5	0
PER1 2024	5/28/2024 9:20	5/28/2024 9:30	0.150	0.001	5	0
PER1 2024	5/28/2024 9:30	5/28/2024 9:40	0.150	0.001	5	0
PER1 2024	5/28/2024 9:40	5/28/2024 9:50	0.150	0.002	5	0
PER1 2024	5/28/2024 9:50	5/28/2024 10:00	0.150	0.002	5	0
PER1 2024	5/28/2024 10:00	5/28/2024 10:10	0.150	0.002	5	0
PER1 2024	5/28/2024 10:10	5/28/2024 10:20	0.150	0.002	5	0
PER1 2024	5/28/2024 10:20	5/28/2024 10:30	0.150	0.002	5	0
PER1 2024	5/28/2024 10:30	5/28/2024 10:40	0.150	0.002	5	0
PER1 2024	5/28/2024 10:40	5/28/2024 10:50	0.150	0.002	5	0
PER1 2024	5/28/2024 10:50	5/28/2024 11:00	0.150	0.002	5	0
PER1 2024	5/28/2024 11:00	5/28/2024 11:10	0.150	0.002	5	0
PER1 2024	5/28/2024 11:10	5/28/2024 11:20	0.150	0.002	5	0
PER1 2024	5/28/2024 11:20	5/28/2024 11:30	0.150	0.002	5	0
PER1 2024	5/28/2024 11:30	5/28/2024 11:40	0.150	0.002	5	0
PER1 2024	5/28/2024 11:40	5/28/2024 11:50	0.150	0.002	5	0
PER1 2024	5/28/2024 11:50	5/28/2024 12:00	0.150	0.002	5	0
PER1 2024	5/28/2024 12:00	5/28/2024 12:10	0.150	0.002	5	0
PER1 2024	5/28/2024 12:10	5/28/2024 12:20	0.150	0.002	5	0
PER1 2024	5/28/2024 12:20	5/28/2024 12:30	0.150	0.002	5	0
PER1 2024	5/28/2024 12:30	5/28/2024 12:40	0.150	0.002	5	0
PER1 2024	5/28/2024 12:40	5/28/2024 12:50	0.150	0.002	5	0
PER1 2024	5/28/2024 12:50	5/28/2024 13:00	0.150	0.002	5	0
PER1 2024	5/28/2024 13:00	5/28/2024 13:10	0.150	0.002	5	0
PER1 2024	5/28/2024 13:10	5/28/2024 13:20	0.150	0.002	5	0
PER1 2024	5/28/2024 13:20	5/28/2024 13:30	0.150	0.002	5	0
PER1 2024	5/28/2024 13:30	5/28/2024 13:40	0.150	0.002	5	0
PER1 2024	5/28/2024 13:40	5/28/2024 13:50	0.150	0.002	5	0
PER1 2024	5/28/2024 13:50	5/28/2024 14:00	0.150	0.002	5	0
PER1 2024	5/28/2024 14:00	5/28/2024 14:10	0.150	0.002	5	0
PER1 2024	5/28/2024 14:10	5/28/2024 14:20	0.150	0.002	5	0
PER1 2024	5/28/2024 14:20	5/28/2024 14:30	0.150	0.002	5	0
PER1 2024	5/28/2024 14:30	5/28/2024 14:40	0.150	0.002	5	0
PER1 2024	5/28/2024 14:40	5/28/2024 14:50	0.150	0.002	5	0
PER1 2024	5/28/2024 14:50	5/28/2024 15:00	0.150	0.002	5	0
PER1 2024	5/28/2024 15:00	5/28/2024 15:10	0.150	0.002	5	0
PER1 2024	5/28/2024 15:10	5/28/2024 15:20	0.150	0.002	5	0
PER1 2024	5/28/2024 15:20	5/28/2024 15:30	0.150	0.002	5	0
PER1 2024	5/28/2024 15:30	5/28/2024 15:40	0.150	0.002	5	0
PER1 2024	5/28/2024 15:40	5/28/2024 15:50	0.150	0.002	5	0
PER1 2024	5/28/2024 15:50	5/28/2024 16:00	0.150	0.002	5	0

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/29/2024 Weather: 80 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued vertical form installation for building construction. 2) ECD continues to advance the remedial excavation to the east.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: The DW CAMP experienced battery issues from approximately 10:45AM to approximately 12PM.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	0	0
Total:(CY)	4485	0	8685	1780	4140

Site Layout Map and Excavation Figures

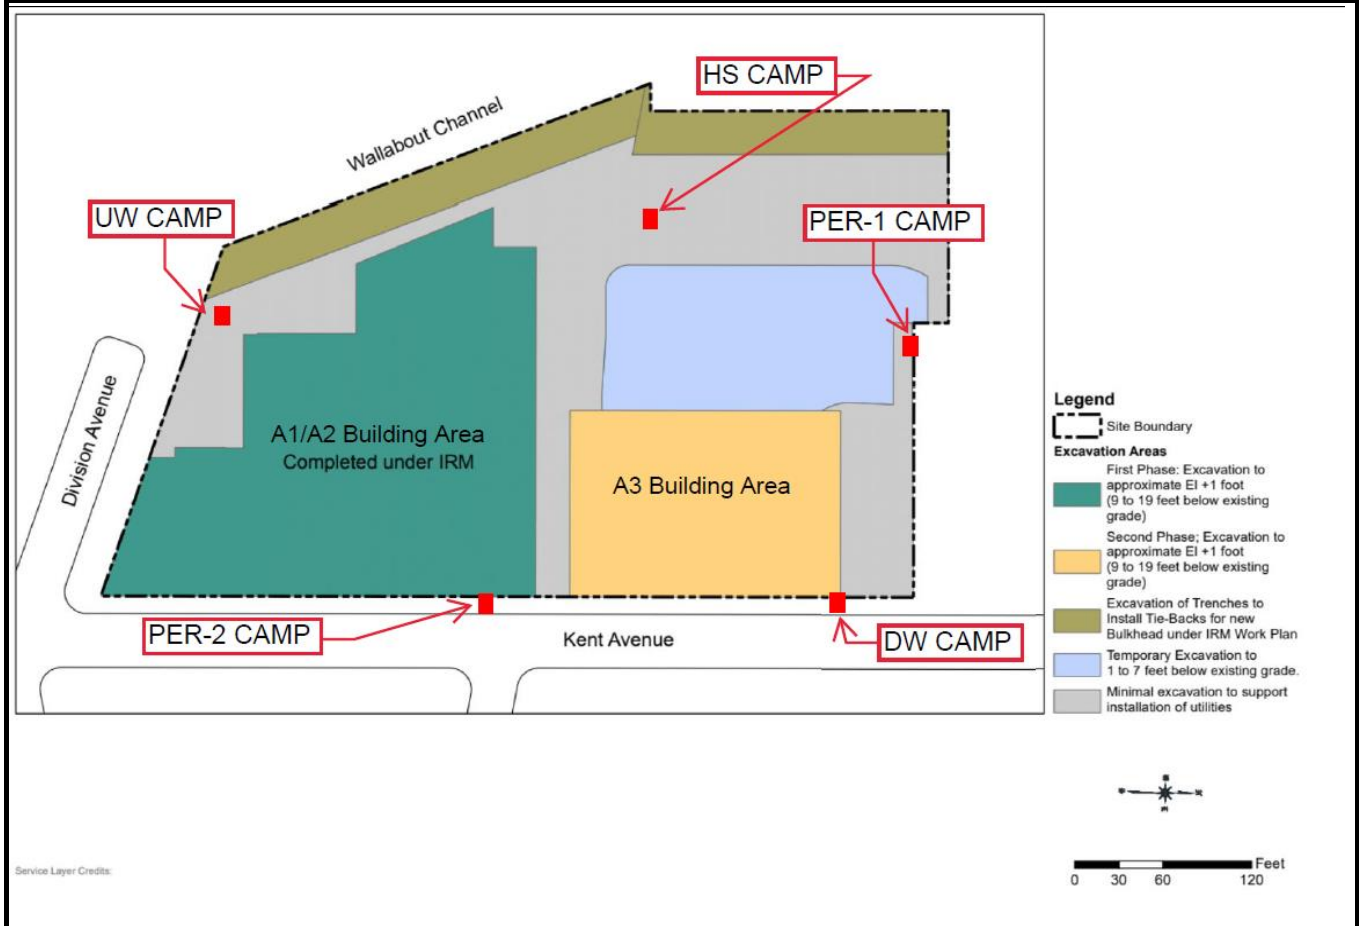

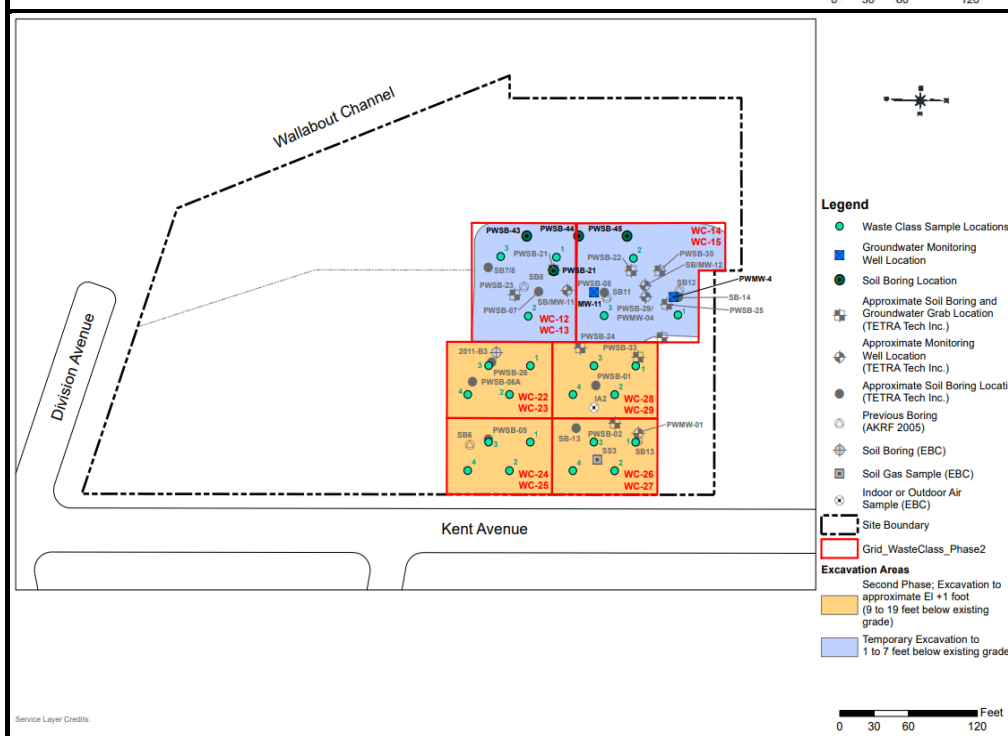
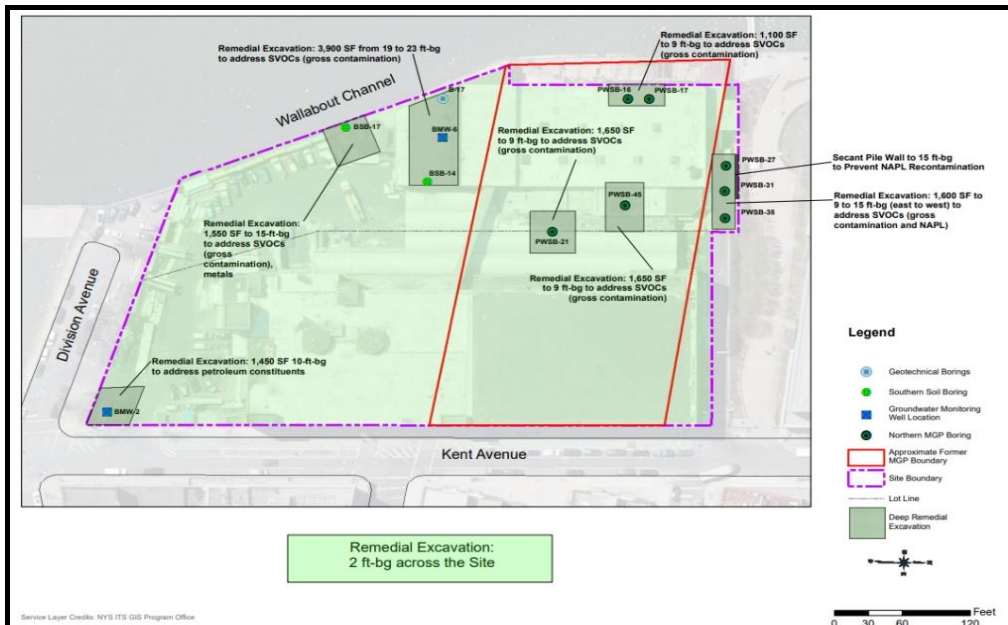


Photo 1:

View of ECD
demolishing concrete
within the remedial
excavation.



Photo 2:

View of the remedial
excavation facing west.



Photo 3:
View of the remedial
excavation facing
west.


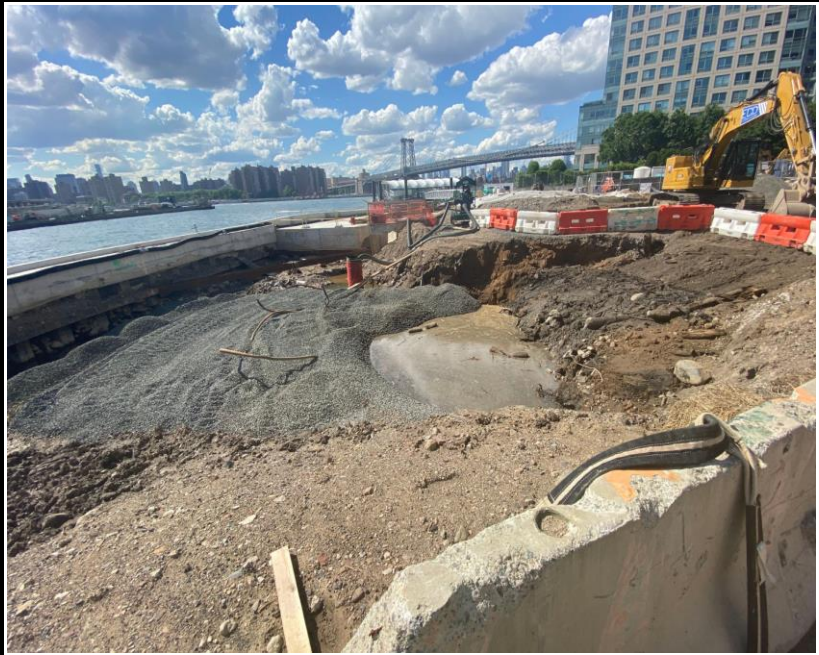


Photo 4:
View of the Site and
foundation
development facing
northwest.




CAMP:
Downwind
Particulates

Dust Levels

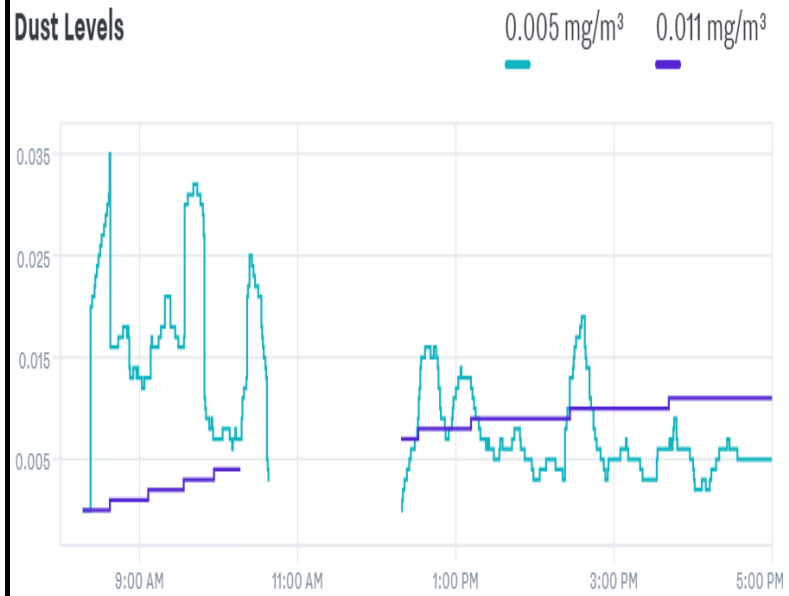


CAMP:
Downwind VOCs

VOC Levels

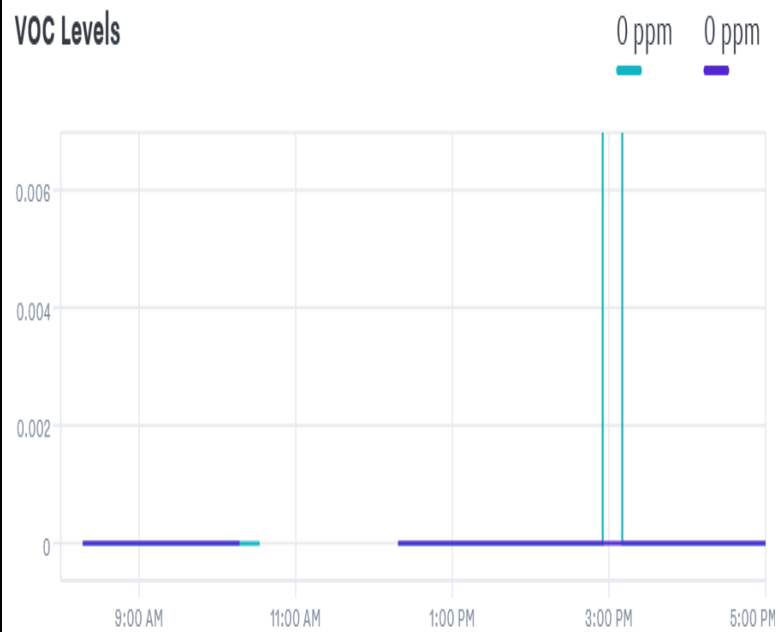


CAMP:
Upwind Particulates

Dust Levels

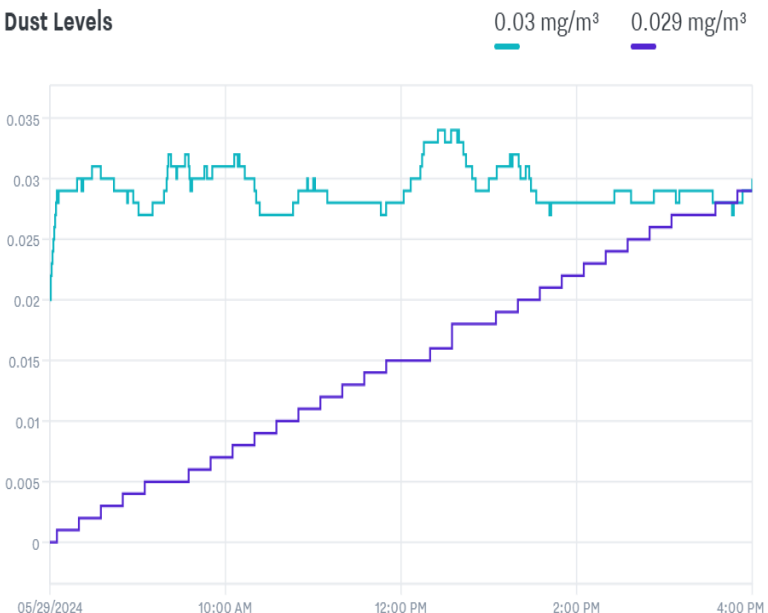

CAMP:
Upwind VOCs

VOC Levels

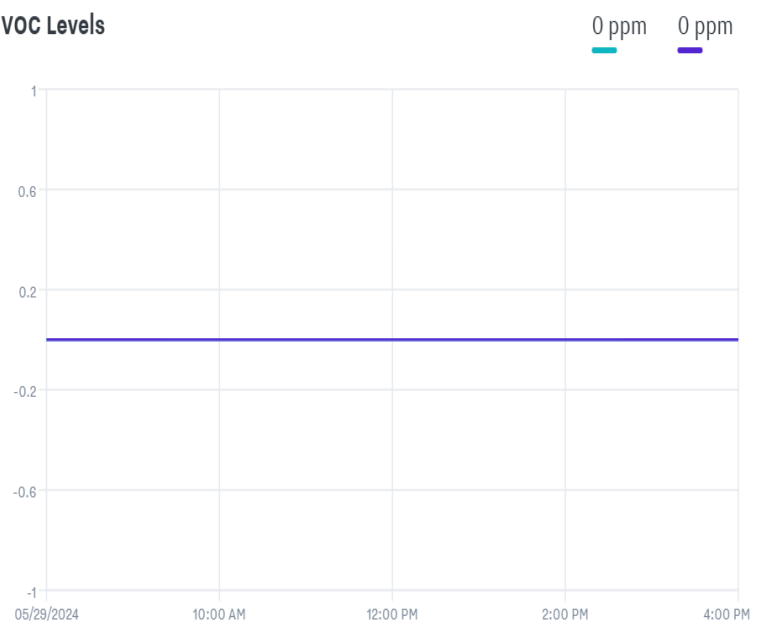

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/29/2024 8:00	5/29/2024 8:10	0.150	0	5	0
DW 2024	5/29/2024 8:10	5/29/2024 8:20	0.150	0	5	0
DW 2024	5/29/2024 8:20	5/29/2024 8:30	0.150	0	5	0
DW 2024	5/29/2024 8:30	5/29/2024 8:40	0.150	0.001	5	0
DW 2024	5/29/2024 8:40	5/29/2024 8:50	0.150	0.001	5	0
DW 2024	5/29/2024 8:50	5/29/2024 9:00	0.150	0.001	5	0
DW 2024	5/29/2024 9:00	5/29/2024 9:10	0.150	0.002	5	0
DW 2024	5/29/2024 9:10	5/29/2024 9:20	0.150	0.002	5	0
DW 2024	5/29/2024 9:20	5/29/2024 9:30	0.150	0.002	5	0
DW 2024	5/29/2024 9:30	5/29/2024 9:40	0.150	0.003	5	0
DW 2024	5/29/2024 9:40	5/29/2024 9:50	0.150	0.003	5	0
DW 2024	5/29/2024 9:50	5/29/2024 10:00	0.150	0.004	5	0
DW 2024	5/29/2024 10:00	5/29/2024 10:10	0.150	0.004	5	0
DW 2024	5/29/2024 10:10	5/29/2024 10:20	0.150	0.004	5	0
DW 2024	5/29/2024 10:20	5/29/2024 10:30	0.150	0.004	5	0
DW 2024	5/29/2024 10:30	5/29/2024 10:40	0.150	0.004	5	0
DW 2024	5/29/2024 10:40	5/29/2024 10:50	0.150	0.004	5	0
DW 2024	5/29/2024 10:50	5/29/2024 11:00	0.150	0.004	5	0
DW 2024	5/29/2024 11:00	5/29/2024 11:10	0.150	0.004	5	0
DW 2024	5/29/2024 11:10	5/29/2024 11:20	0.150	0.004	5	0
DW 2024	5/29/2024 11:20	5/29/2024 11:30	0.150	0.004	5	0
DW 2024	5/29/2024 11:30	5/29/2024 11:40	0.150	0.004	5	0
DW 2024	5/29/2024 11:40	5/29/2024 11:50	0.150	0.004	5	0
DW 2024	5/29/2024 11:50	5/29/2024 12:00	0.150	0.004	5	0
DW 2024	5/29/2024 12:00	5/29/2024 12:10	0.150	0.004	5	0
DW 2024	5/29/2024 12:10	5/29/2024 12:20	0.150	0.007	5	0.001
DW 2024	5/29/2024 12:20	5/29/2024 12:30	0.150	0.007	5	0.001
DW 2024	5/29/2024 12:30	5/29/2024 12:40	0.150	0.008	5	0.001
DW 2024	5/29/2024 12:40	5/29/2024 12:50	0.150	0.008	5	0.001
DW 2024	5/29/2024 12:50	5/29/2024 13:00	0.150	0.008	5	0.001
DW 2024	5/29/2024 13:00	5/29/2024 13:10	0.150	0.008	5	0.001
DW 2024	5/29/2024 13:10	5/29/2024 13:20	0.150	0.009	5	0.001
DW 2024	5/29/2024 13:20	5/29/2024 13:30	0.150	0.009	5	0.001
DW 2024	5/29/2024 13:30	5/29/2024 13:40	0.150	0.009	5	0.001
DW 2024	5/29/2024 13:40	5/29/2024 13:50	0.150	0.009	5	0.001
DW 2024	5/29/2024 13:50	5/29/2024 14:00	0.150	0.009	5	0.001
DW 2024	5/29/2024 14:00	5/29/2024 14:10	0.150	0.009	5	0.001
DW 2024	5/29/2024 14:10	5/29/2024 14:20	0.150	0.009	5	0.001
DW 2024	5/29/2024 14:20	5/29/2024 14:30	0.150	0.01	5	0.001
DW 2024	5/29/2024 14:30	5/29/2024 14:40	0.150	0.01	5	0.001
DW 2024	5/29/2024 14:40	5/29/2024 14:50	0.150	0.01	5	0.001
DW 2024	5/29/2024 14:50	5/29/2024 15:00	0.150	0.01	5	0.001
DW 2024	5/29/2024 15:00	5/29/2024 15:10	0.150	0.01	5	0.001
DW 2024	5/29/2024 15:10	5/29/2024 15:20	0.150	0.01	5	0.001
DW 2024	5/29/2024 15:20	5/29/2024 15:30	0.150	0.01	5	0.001
DW 2024	5/29/2024 15:30	5/29/2024 15:40	0.150	0.01	5	0.001
DW 2024	5/29/2024 15:40	5/29/2024 15:50	0.150	0.011	5	0.001
DW 2024	5/29/2024 15:50	5/29/2024 16:00	0.150	0.011	5	0.001

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/29/2024 8:00	5/29/2024 8:10	0.150	0.001	5	0
UW 2024	5/29/2024 8:10	5/29/2024 8:20	0.150	0.002	5	0
UW 2024	5/29/2024 8:20	5/29/2024 8:30	0.150	0.002	5	0
UW 2024	5/29/2024 8:30	5/29/2024 8:40	0.150	0.003	5	0
UW 2024	5/29/2024 8:40	5/29/2024 8:50	0.150	0.004	5	0
UW 2024	5/29/2024 8:50	5/29/2024 9:00	0.150	0.004	5	0
UW 2024	5/29/2024 9:00	5/29/2024 9:10	0.150	0.005	5	0
UW 2024	5/29/2024 9:10	5/29/2024 9:20	0.150	0.005	5	0
UW 2024	5/29/2024 9:20	5/29/2024 9:30	0.150	0.005	5	0
UW 2024	5/29/2024 9:30	5/29/2024 9:40	0.150	0.006	5	0
UW 2024	5/29/2024 9:40	5/29/2024 9:50	0.150	0.007	5	0
UW 2024	5/29/2024 9:50	5/29/2024 10:00	0.150	0.007	5	0
UW 2024	5/29/2024 10:00	5/29/2024 10:10	0.150	0.008	5	0
UW 2024	5/29/2024 10:10	5/29/2024 10:20	0.150	0.009	5	0
UW 2024	5/29/2024 10:20	5/29/2024 10:30	0.150	0.009	5	0
UW 2024	5/29/2024 10:30	5/29/2024 10:40	0.150	0.01	5	0
UW 2024	5/29/2024 10:40	5/29/2024 10:50	0.150	0.011	5	0
UW 2024	5/29/2024 10:50	5/29/2024 11:00	0.150	0.011	5	0
UW 2024	5/29/2024 11:00	5/29/2024 11:10	0.150	0.012	5	0
UW 2024	5/29/2024 11:10	5/29/2024 11:20	0.150	0.013	5	0
UW 2024	5/29/2024 11:20	5/29/2024 11:30	0.150	0.013	5	0
UW 2024	5/29/2024 11:30	5/29/2024 11:40	0.150	0.014	5	0
UW 2024	5/29/2024 11:40	5/29/2024 11:50	0.150	0.015	5	0
UW 2024	5/29/2024 11:50	5/29/2024 12:00	0.150	0.015	5	0
UW 2024	5/29/2024 12:00	5/29/2024 12:10	0.150	0.015	5	0
UW 2024	5/29/2024 12:10	5/29/2024 12:20	0.150	0.016	5	0
UW 2024	5/29/2024 12:20	5/29/2024 12:30	0.150	0.016	5	0
UW 2024	5/29/2024 12:30	5/29/2024 12:40	0.150	0.018	5	0
UW 2024	5/29/2024 12:40	5/29/2024 12:50	0.150	0.018	5	0
UW 2024	5/29/2024 12:50	5/29/2024 13:00	0.150	0.018	5	0
UW 2024	5/29/2024 13:00	5/29/2024 13:10	0.150	0.019	5	0
UW 2024	5/29/2024 13:10	5/29/2024 13:20	0.150	0.02	5	0
UW 2024	5/29/2024 13:20	5/29/2024 13:30	0.150	0.02	5	0
UW 2024	5/29/2024 13:30	5/29/2024 13:40	0.150	0.021	5	0
UW 2024	5/29/2024 13:40	5/29/2024 13:50	0.150	0.022	5	0
UW 2024	5/29/2024 13:50	5/29/2024 14:00	0.150	0.022	5	0
UW 2024	5/29/2024 14:00	5/29/2024 14:10	0.150	0.023	5	0
UW 2024	5/29/2024 14:10	5/29/2024 14:20	0.150	0.024	5	0
UW 2024	5/29/2024 14:20	5/29/2024 14:30	0.150	0.024	5	0
UW 2024	5/29/2024 14:30	5/29/2024 14:40	0.150	0.025	5	0
UW 2024	5/29/2024 14:40	5/29/2024 14:50	0.150	0.026	5	0
UW 2024	5/29/2024 14:50	5/29/2024 15:00	0.150	0.026	5	0
UW 2024	5/29/2024 15:00	5/29/2024 15:10	0.150	0.027	5	0
UW 2024	5/29/2024 15:10	5/29/2024 15:20	0.150	0.027	5	0
UW 2024	5/29/2024 15:20	5/29/2024 15:30	0.150	0.027	5	0
UW 2024	5/29/2024 15:30	5/29/2024 15:40	0.150	0.028	5	0
UW 2024	5/29/2024 15:40	5/29/2024 15:50	0.150	0.029	5	0
UW 2024	5/29/2024 15:50	5/29/2024 16:00	0.150	0.029	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/29/2024 8:00	5/29/2024 8:10	0.150	0	5	0
HS South	5/29/2024 8:10	5/29/2024 8:20	0.150	0	5	0
HS South	5/29/2024 8:20	5/29/2024 8:30	0.150	0.001	5	0
HS South	5/29/2024 8:30	5/29/2024 8:40	0.150	0.002	5	0
HS South	5/29/2024 8:40	5/29/2024 8:50	0.150	0.002	5	0
HS South	5/29/2024 8:50	5/29/2024 9:00	0.150	0.003	5	0
HS South	5/29/2024 9:00	5/29/2024 9:10	0.150	0.004	5	0
HS South	5/29/2024 9:10	5/29/2024 9:20	0.150	0.004	5	0
HS South	5/29/2024 9:20	5/29/2024 9:30	0.150	0.005	5	0
HS South	5/29/2024 9:30	5/29/2024 9:40	0.150	0.006	5	0
HS South	5/29/2024 9:40	5/29/2024 9:50	0.150	0.006	5	0
HS South	5/29/2024 9:50	5/29/2024 10:00	0.150	0.007	5	0
HS South	5/29/2024 10:00	5/29/2024 10:10	0.150	0.007	5	0
HS South	5/29/2024 10:10	5/29/2024 10:20	0.150	0.008	5	0
HS South	5/29/2024 10:20	5/29/2024 10:30	0.150	0.009	5	0
HS South	5/29/2024 10:30	5/29/2024 10:40	0.150	0.009	5	0
HS South	5/29/2024 10:40	5/29/2024 10:50	0.150	0.01	5	0
HS South	5/29/2024 10:50	5/29/2024 11:00	0.150	0.011	5	0
HS South	5/29/2024 11:00	5/29/2024 11:10	0.150	0.012	5	0
HS South	5/29/2024 11:10	5/29/2024 11:20	0.150	0.012	5	0
HS South	5/29/2024 11:20	5/29/2024 11:30	0.150	0.013	5	0
HS South	5/29/2024 11:30	5/29/2024 11:40	0.150	0.014	5	0
HS South	5/29/2024 11:40	5/29/2024 11:50	0.150	0.014	5	0
HS South	5/29/2024 11:50	5/29/2024 12:00	0.150	0.015	5	0
HS South	5/29/2024 12:00	5/29/2024 12:10	0.150	0.016	5	0
HS South	5/29/2024 12:10	5/29/2024 12:20	0.150	0.016	5	0
HS South	5/29/2024 12:20	5/29/2024 12:30	0.150	0.017	5	0
HS South	5/29/2024 12:30	5/29/2024 12:40	0.150	0.018	5	0
HS South	5/29/2024 12:40	5/29/2024 12:50	0.150	0.019	5	0
HS South	5/29/2024 12:50	5/29/2024 13:00	0.150	0.019	5	0
HS South	5/29/2024 13:00	5/29/2024 13:10	0.150	0.02	5	0
HS South	5/29/2024 13:10	5/29/2024 13:20	0.150	0.02	5	0
HS South	5/29/2024 13:20	5/29/2024 13:30	0.150	0.021	5	0
HS South	5/29/2024 13:30	5/29/2024 13:40	0.150	0.021	5	0
HS South	5/29/2024 13:40	5/29/2024 13:50	0.150	0.022	5	0
HS South	5/29/2024 13:50	5/29/2024 14:00	0.150	0.022	5	0
HS South	5/29/2024 14:00	5/29/2024 14:10	0.150	0.023	5	0
HS South	5/29/2024 14:10	5/29/2024 14:20	0.150	0.024	5	0
HS South	5/29/2024 14:20	5/29/2024 14:30	0.150	0.024	5	0
HS South	5/29/2024 14:30	5/29/2024 14:40	0.150	0.025	5	0
HS South	5/29/2024 14:40	5/29/2024 14:50	0.150	0.025	5	0
HS South	5/29/2024 14:50	5/29/2024 15:00	0.150	0.026	5	0
HS South	5/29/2024 15:00	5/29/2024 15:10	0.150	0.027	5	0
HS South	5/29/2024 15:10	5/29/2024 15:20	0.150	0.028	5	0
HS South	5/29/2024 15:20	5/29/2024 15:30	0.150	0.028	5	0
HS South	5/29/2024 15:30	5/29/2024 15:40	0.150	0.029	5	0
HS South	5/29/2024 15:40	5/29/2024 15:50	0.150	0.029	5	0
HS South	5/29/2024 15:50	5/29/2024 16:00	0.150	0.03	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/29/2024 8:00	5/29/2024 8:10	0.150	0.015	5	0
PER2 2024	5/29/2024 8:10	5/29/2024 8:20	0.150	0.015	5	0
PER2 2024	5/29/2024 8:20	5/29/2024 8:30	0.150	0	5	0
PER2 2024	5/29/2024 8:30	5/29/2024 8:40	0.150	0.001	5	0
PER2 2024	5/29/2024 8:40	5/29/2024 8:50	0.150	0.001	5	0
PER2 2024	5/29/2024 8:50	5/29/2024 9:00	0.150	0.001	5	0
PER2 2024	5/29/2024 9:00	5/29/2024 9:10	0.150	0.001	5	0
PER2 2024	5/29/2024 9:10	5/29/2024 9:20	0.150	0.001	5	0
PER2 2024	5/29/2024 9:20	5/29/2024 9:30	0.150	0.001	5	0
PER2 2024	5/29/2024 9:30	5/29/2024 9:40	0.150	0.002	5	0
PER2 2024	5/29/2024 9:40	5/29/2024 9:50	0.150	0.002	5	0
PER2 2024	5/29/2024 9:50	5/29/2024 10:00	0.150	0.002	5	0
PER2 2024	5/29/2024 10:00	5/29/2024 10:10	0.150	0.002	5	0
PER2 2024	5/29/2024 10:10	5/29/2024 10:20	0.150	0.002	5	0
PER2 2024	5/29/2024 10:20	5/29/2024 10:30	0.150	0.002	5	0
PER2 2024	5/29/2024 10:30	5/29/2024 10:40	0.150	0.002	5	0
PER2 2024	5/29/2024 10:40	5/29/2024 10:50	0.150	0.003	5	0
PER2 2024	5/29/2024 10:50	5/29/2024 11:00	0.150	0.003	5	0
PER2 2024	5/29/2024 11:00	5/29/2024 11:10	0.150	0.003	5	0
PER2 2024	5/29/2024 11:10	5/29/2024 11:20	0.150	0.003	5	0
PER2 2024	5/29/2024 11:20	5/29/2024 11:30	0.150	0.003	5	0
PER2 2024	5/29/2024 11:30	5/29/2024 11:40	0.150	0.003	5	0
PER2 2024	5/29/2024 11:40	5/29/2024 11:50	0.150	0.004	5	0
PER2 2024	5/29/2024 11:50	5/29/2024 12:00	0.150	0.004	5	0
PER2 2024	5/29/2024 12:00	5/29/2024 12:10	0.150	0.004	5	0
PER2 2024	5/29/2024 12:10	5/29/2024 12:20	0.150	0.004	5	0
PER2 2024	5/29/2024 12:20	5/29/2024 12:30	0.150	0.005	5	0
PER2 2024	5/29/2024 12:30	5/29/2024 12:40	0.150	0.005	5	0
PER2 2024	5/29/2024 12:40	5/29/2024 12:50	0.150	0.005	5	0
PER2 2024	5/29/2024 12:50	5/29/2024 13:00	0.150	0.005	5	0
PER2 2024	5/29/2024 13:00	5/29/2024 13:10	0.150	0.006	5	0
PER2 2024	5/29/2024 13:10	5/29/2024 13:20	0.150	0.006	5	0
PER2 2024	5/29/2024 13:20	5/29/2024 13:30	0.150	0.006	5	0
PER2 2024	5/29/2024 13:30	5/29/2024 13:40	0.150	0.006	5	0
PER2 2024	5/29/2024 13:40	5/29/2024 13:50	0.150	0.006	5	0
PER2 2024	5/29/2024 13:50	5/29/2024 14:00	0.150	0.007	5	0
PER2 2024	5/29/2024 14:00	5/29/2024 14:10	0.150	0.007	5	0
PER2 2024	5/29/2024 14:10	5/29/2024 14:20	0.150	0.007	5	0
PER2 2024	5/29/2024 14:20	5/29/2024 14:30	0.150	0.007	5	0
PER2 2024	5/29/2024 14:30	5/29/2024 14:40	0.150	0.007	5	0
PER2 2024	5/29/2024 14:40	5/29/2024 14:50	0.150	0.008	5	0
PER2 2024	5/29/2024 14:50	5/29/2024 15:00	0.150	0.008	5	0
PER2 2024	5/29/2024 15:00	5/29/2024 15:10	0.150	0.008	5	0
PER2 2024	5/29/2024 15:10	5/29/2024 15:20	0.150	0.008	5	0
PER2 2024	5/29/2024 15:20	5/29/2024 15:30	0.150	0.008	5	0
PER2 2024	5/29/2024 15:30	5/29/2024 15:40	0.150	0.009	5	0
PER2 2024	5/29/2024 15:40	5/29/2024 15:50	0.150	0.009	5	0
PER2 2024	5/29/2024 15:50	5/29/2024 16:00	0.150	0.009	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/29/2024 8:00	5/29/2024 8:10	0.150	0	5	0
PER1 2024	5/29/2024 8:10	5/29/2024 8:20	0.150	0	5	0
PER1 2024	5/29/2024 8:20	5/29/2024 8:30	0.150	0	5	0
PER1 2024	5/29/2024 8:30	5/29/2024 8:40	0.150	0	5	0
PER1 2024	5/29/2024 8:40	5/29/2024 8:50	0.150	0.001	5	0.113
PER1 2024	5/29/2024 8:50	5/29/2024 9:00	0.150	0.001	5	0.113
PER1 2024	5/29/2024 9:00	5/29/2024 9:10	0.150	0.001	5	0.113
PER1 2024	5/29/2024 9:10	5/29/2024 9:20	0.150	0.001	5	0.113
PER1 2024	5/29/2024 9:20	5/29/2024 9:30	0.150	0.001	5	0.113
PER1 2024	5/29/2024 9:30	5/29/2024 9:40	0.150	0	5	0.113
PER1 2024	5/29/2024 9:40	5/29/2024 9:50	0.150	0	5	0.113
PER1 2024	5/29/2024 9:50	5/29/2024 10:00	0.150	0.001	5	0.113
PER1 2024	5/29/2024 10:00	5/29/2024 10:10	0.150	0.002	5	0.113
PER1 2024	5/29/2024 10:10	5/29/2024 10:20	0.150	0.002	5	0.113
PER1 2024	5/29/2024 10:20	5/29/2024 10:30	0.150	0.002	5	0.113
PER1 2024	5/29/2024 10:30	5/29/2024 10:40	0.150	0.003	5	0.113
PER1 2024	5/29/2024 10:40	5/29/2024 10:50	0.150	0.003	5	0.113
PER1 2024	5/29/2024 10:50	5/29/2024 11:00	0.150	0.003	5	0.113
PER1 2024	5/29/2024 11:00	5/29/2024 11:10	0.150	0.003	5	0.113
PER1 2024	5/29/2024 11:10	5/29/2024 11:20	0.150	0.004	5	0.115
PER1 2024	5/29/2024 11:20	5/29/2024 11:30	0.150	0.004	5	0.137
PER1 2024	5/29/2024 11:30	5/29/2024 11:40	0.150	0.004	5	0.177
PER1 2024	5/29/2024 11:40	5/29/2024 11:50	0.150	0.005	5	0.183
PER1 2024	5/29/2024 11:50	5/29/2024 12:00	0.150	0.005	5	0.183
PER1 2024	5/29/2024 12:00	5/29/2024 12:10	0.150	0.005	5	0.19
PER1 2024	5/29/2024 12:10	5/29/2024 12:20	0.150	0.005	5	0.191
PER1 2024	5/29/2024 12:20	5/29/2024 12:30	0.150	0.006	5	0.191
PER1 2024	5/29/2024 12:30	5/29/2024 12:40	0.150	0.006	5	0.191
PER1 2024	5/29/2024 12:40	5/29/2024 12:50	0.150	0.006	5	0.191
PER1 2024	5/29/2024 12:50	5/29/2024 13:00	0.150	0.006	5	0.191
PER1 2024	5/29/2024 13:00	5/29/2024 13:10	0.150	0.007	5	0.191
PER1 2024	5/29/2024 13:10	5/29/2024 13:20	0.150	0.007	5	0.191
PER1 2024	5/29/2024 13:20	5/29/2024 13:30	0.150	0.007	5	0.191
PER1 2024	5/29/2024 13:30	5/29/2024 13:40	0.150	0.008	5	0.191
PER1 2024	5/29/2024 13:40	5/29/2024 13:50	0.150	0.008	5	0.191
PER1 2024	5/29/2024 13:50	5/29/2024 14:00	0.150	0.009	5	0.202
PER1 2024	5/29/2024 14:00	5/29/2024 14:10	0.150	0.009	5	0.202
PER1 2024	5/29/2024 14:10	5/29/2024 14:20	0.150	0.009	5	0.202
PER1 2024	5/29/2024 14:20	5/29/2024 14:30	0.150	0.01	5	0.202
PER1 2024	5/29/2024 14:30	5/29/2024 14:40	0.150	0.01	5	0.202
PER1 2024	5/29/2024 14:40	5/29/2024 14:50	0.150	0.011	5	0.202
PER1 2024	5/29/2024 14:50	5/29/2024 15:00	0.150	0.011	5	0.202
PER1 2024	5/29/2024 15:00	5/29/2024 15:10	0.150	0.011	5	0.202
PER1 2024	5/29/2024 15:10	5/29/2024 15:20	0.150	0.012	5	0.202
PER1 2024	5/29/2024 15:20	5/29/2024 15:30	0.150	0.012	5	0.205
PER1 2024	5/29/2024 15:30	5/29/2024 15:40	0.150	0.012	5	0.205
PER1 2024	5/29/2024 15:40	5/29/2024 15:50	0.150	0.013	5	0.205
PER1 2024	5/29/2024 15:50	5/29/2024 16:00	0.150	0.013	5	0.205

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/30/2024 Weather: 80 deg. F, Clear


Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA
Work Activities Performed: 1) Alba continued vertical form installation for building construction. 2) ECD continues to advance the remedial excavation to the east. 3) ECD exported 3 loads (~60 CY) of material from the remedial excavation for off-site disposal at the Bayshore Soil Management facility. 4) ECD imported 3 loads of 3/4" stone for backfill in the remedial excavation.	
Is the dewatering system operating: YES NO	
Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA	
Samples Collected (Since Last Report): None.	
Air Monitoring (Since Last Report): CAMP graphs and tables are included below.	
Problems Encountered: None.	
Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation development. Continue excavation for the marine front remedial excavation.	

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	60	0
Total:(CY)	4485	0	8685	1840	4140

Site Layout Map and Excavation Figures

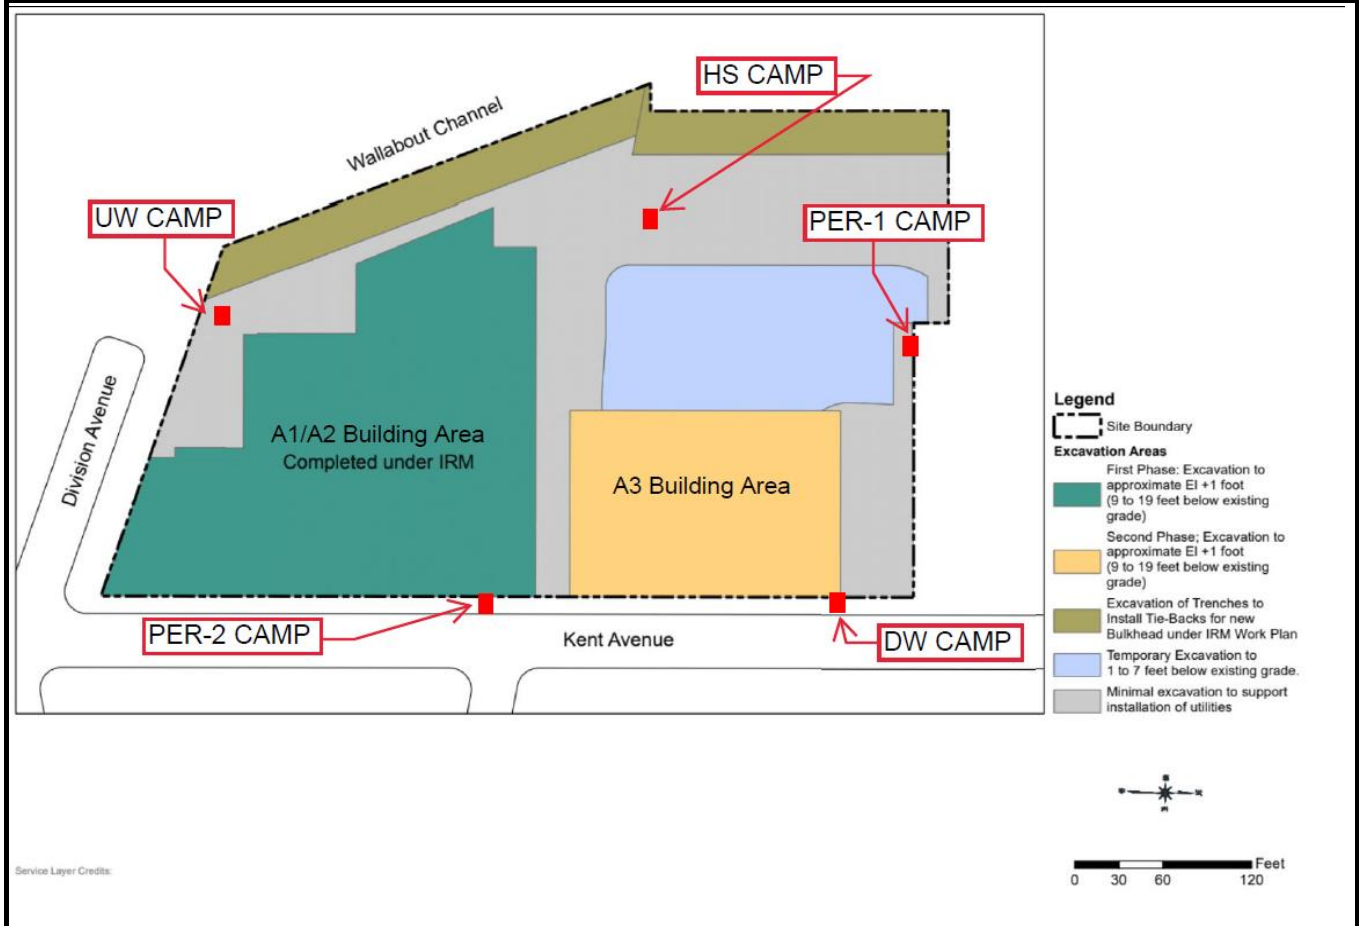

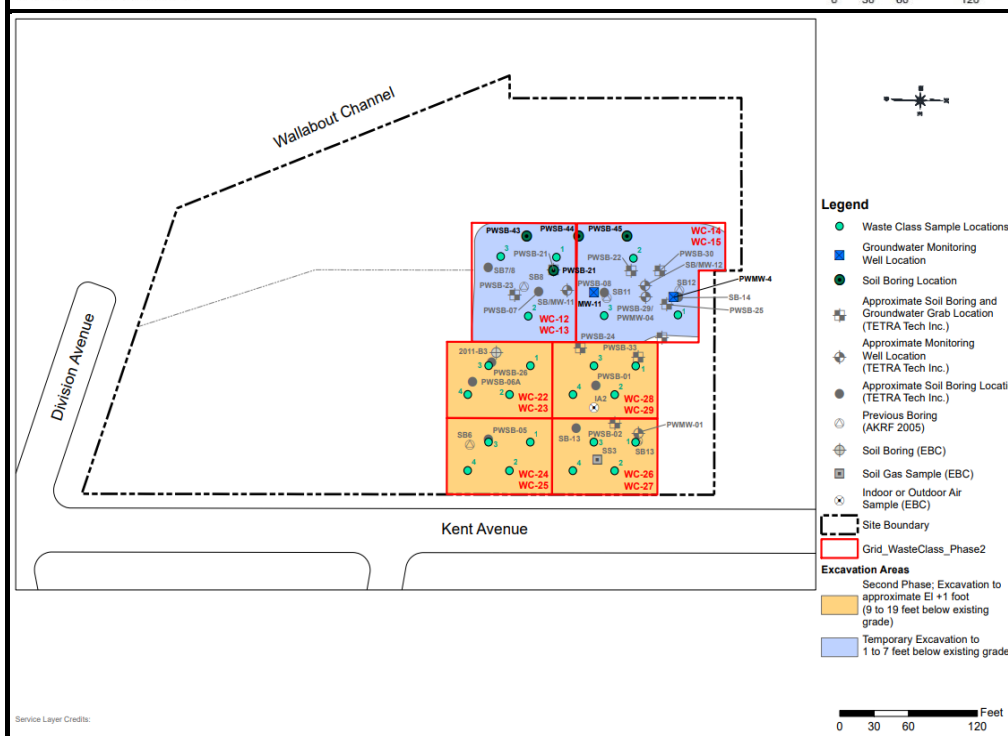
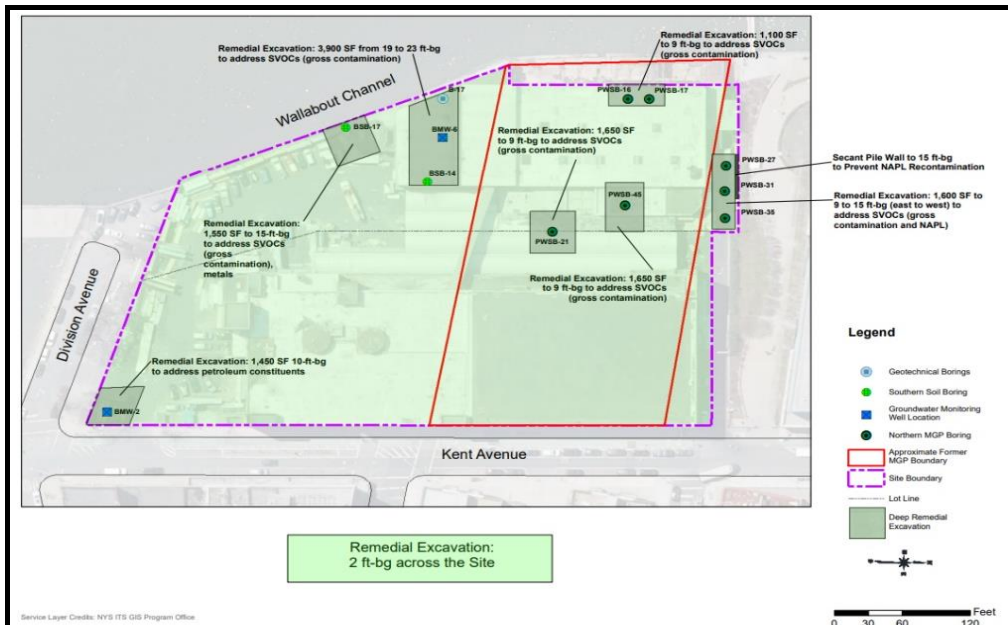


Photo 1:
View of the remedial
excavation facing west.




Photo 2:
View of stone delivery
for the remedial
excavation backfilling.



Photo 3:
View of truck loading
for off-site soil
disposal from the
remedial excavation.




Photo 4:
View of the Site and
foundation
development facing
northwest.

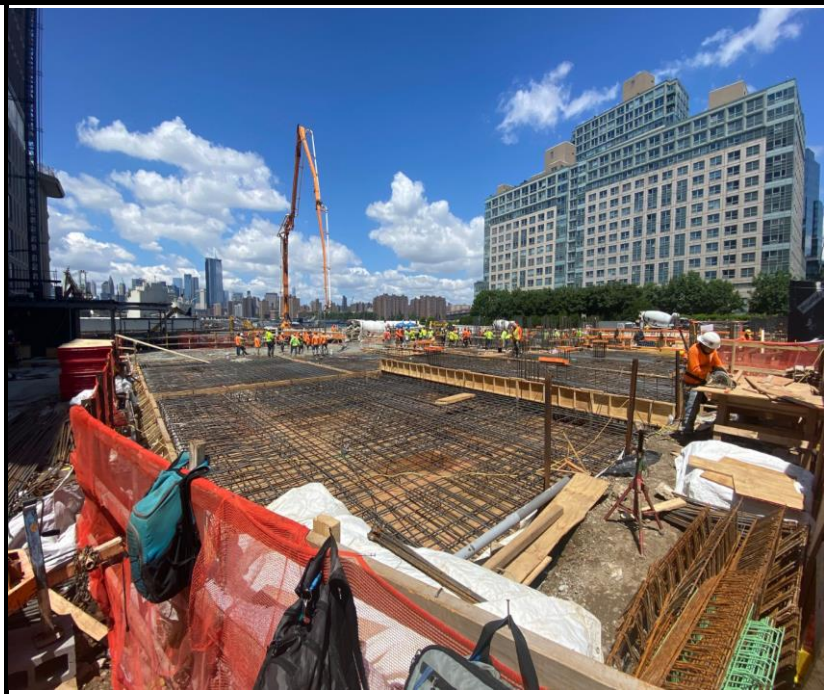

CAMP:
Downwind
Particulates

Dust Levels


0.007 mg/m³ 0.011 mg/m³

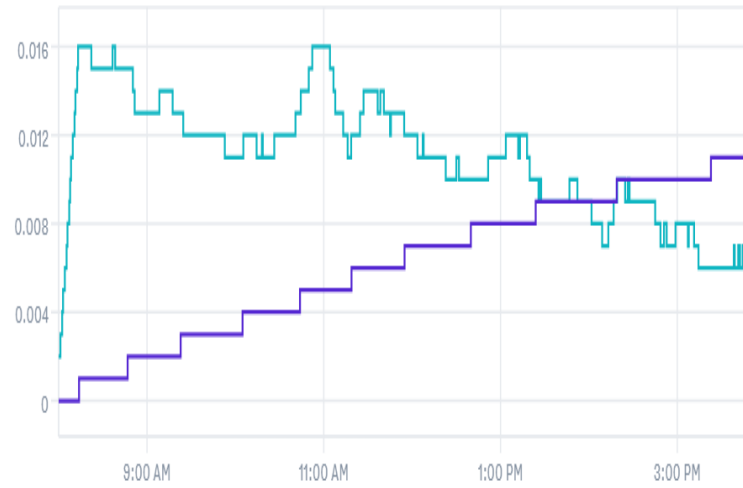

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm

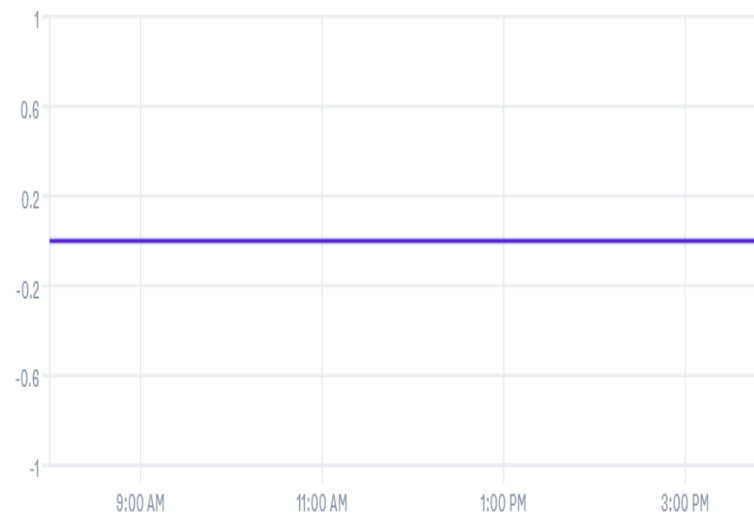

CAMP:
Upwind Particulates

Dust Levels


0.034 mg/m³ 0.033 mg/m³

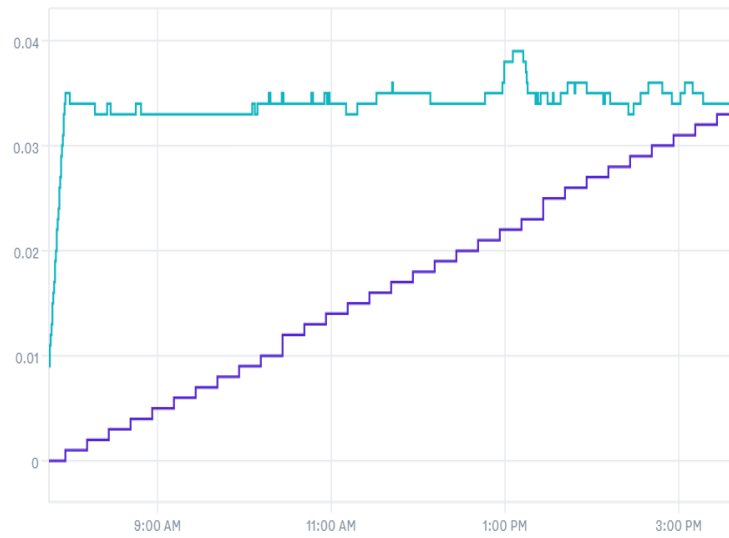

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

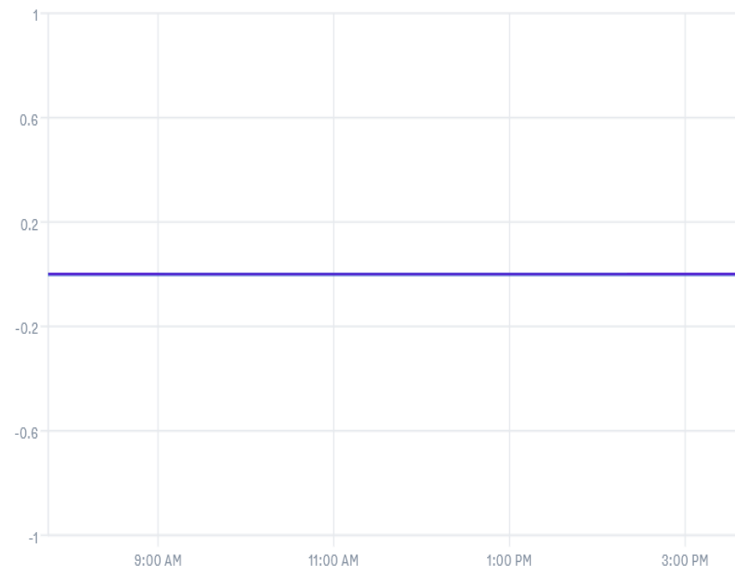

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/30/2024 7:30	5/30/2024 7:40	0.150	0	5	0
DW 2024	5/30/2024 7:40	5/30/2024 7:50	0.150	0	5	0
DW 2024	5/30/2024 7:50	5/30/2024 8:00	0.150	0	5	0
DW 2024	5/30/2024 8:00	5/30/2024 8:10	0.150	0	5	0
DW 2024	5/30/2024 8:10	5/30/2024 8:20	0.150	0.001	5	0
DW 2024	5/30/2024 8:20	5/30/2024 8:30	0.150	0.001	5	0
DW 2024	5/30/2024 8:30	5/30/2024 8:40	0.150	0.001	5	0
DW 2024	5/30/2024 8:40	5/30/2024 8:50	0.150	0.002	5	0
DW 2024	5/30/2024 8:50	5/30/2024 9:00	0.150	0.002	5	0
DW 2024	5/30/2024 9:00	5/30/2024 9:10	0.150	0.002	5	0
DW 2024	5/30/2024 9:10	5/30/2024 9:20	0.150	0.002	5	0
DW 2024	5/30/2024 9:20	5/30/2024 9:30	0.150	0.003	5	0
DW 2024	5/30/2024 9:30	5/30/2024 9:40	0.150	0.003	5	0
DW 2024	5/30/2024 9:40	5/30/2024 9:50	0.150	0.003	5	0
DW 2024	5/30/2024 9:50	5/30/2024 10:00	0.150	0.003	5	0
DW 2024	5/30/2024 10:00	5/30/2024 10:10	0.150	0.004	5	0
DW 2024	5/30/2024 10:10	5/30/2024 10:20	0.150	0.004	5	0
DW 2024	5/30/2024 10:20	5/30/2024 10:30	0.150	0.004	5	0
DW 2024	5/30/2024 10:30	5/30/2024 10:40	0.150	0.004	5	0
DW 2024	5/30/2024 10:40	5/30/2024 10:50	0.150	0.005	5	0
DW 2024	5/30/2024 10:50	5/30/2024 11:00	0.150	0.005	5	0
DW 2024	5/30/2024 11:00	5/30/2024 11:10	0.150	0.005	5	0
DW 2024	5/30/2024 11:10	5/30/2024 11:20	0.150	0.006	5	0
DW 2024	5/30/2024 11:20	5/30/2024 11:30	0.150	0.006	5	0
DW 2024	5/30/2024 11:30	5/30/2024 11:40	0.150	0.006	5	0
DW 2024	5/30/2024 11:40	5/30/2024 11:50	0.150	0.006	5	0
DW 2024	5/30/2024 11:50	5/30/2024 12:00	0.150	0.007	5	0
DW 2024	5/30/2024 12:00	5/30/2024 12:10	0.150	0.007	5	0
DW 2024	5/30/2024 12:10	5/30/2024 12:20	0.150	0.007	5	0
DW 2024	5/30/2024 12:20	5/30/2024 12:30	0.150	0.007	5	0
DW 2024	5/30/2024 12:30	5/30/2024 12:40	0.150	0.008	5	0
DW 2024	5/30/2024 12:40	5/30/2024 12:50	0.150	0.008	5	0
DW 2024	5/30/2024 12:50	5/30/2024 13:00	0.150	0.008	5	0
DW 2024	5/30/2024 13:00	5/30/2024 13:10	0.150	0.008	5	0
DW 2024	5/30/2024 13:10	5/30/2024 13:20	0.150	0.008	5	0
DW 2024	5/30/2024 13:20	5/30/2024 13:30	0.150	0.009	5	0
DW 2024	5/30/2024 13:30	5/30/2024 13:40	0.150	0.009	5	0
DW 2024	5/30/2024 13:40	5/30/2024 13:50	0.150	0.009	5	0
DW 2024	5/30/2024 13:50	5/30/2024 14:00	0.150	0.009	5	0
DW 2024	5/30/2024 14:00	5/30/2024 14:10	0.150	0.009	5	0
DW 2024	5/30/2024 14:10	5/30/2024 14:20	0.150	0.01	5	0
DW 2024	5/30/2024 14:20	5/30/2024 14:30	0.150	0.01	5	0
DW 2024	5/30/2024 14:30	5/30/2024 14:40	0.150	0.01	5	0
DW 2024	5/30/2024 14:40	5/30/2024 14:50	0.150	0.01	5	0
DW 2024	5/30/2024 14:50	5/30/2024 15:00	0.150	0.01	5	0
DW 2024	5/30/2024 15:00	5/30/2024 15:10	0.150	0.01	5	0
DW 2024	5/30/2024 15:10	5/30/2024 15:20	0.150	0.01	5	0
DW 2024	5/30/2024 15:20	5/30/2024 15:30	0.150	0.011	5	0
DW 2024	5/30/2024 15:30	5/30/2024 15:40	0.150	0.011	5	0
DW 2024	5/30/2024 15:40	5/30/2024 15:50	0.150	0.011	5	0
DW 2024	5/30/2024 15:50	5/30/2024 16:00	0.150	0.011	5	0
DW 2024	5/30/2024 16:00	5/30/2024 16:10	0.150	0.011	5	0
DW 2024	5/30/2024 16:10	5/30/2024 16:20	0.150	0.011	5	0
DW 2024	5/30/2024 16:20	5/30/2024 16:30	0.150	0.011	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/30/2024 7:30	5/30/2024 7:40	0.150	0	5	0
UW 2024	5/30/2024 7:40	5/30/2024 7:50	0.150	0	5	0
UW 2024	5/30/2024 7:50	5/30/2024 8:00	0.150	0.001	5	0
UW 2024	5/30/2024 8:00	5/30/2024 8:10	0.150	0.001	5	0
UW 2024	5/30/2024 8:10	5/30/2024 8:20	0.150	0.002	5	0
UW 2024	5/30/2024 8:20	5/30/2024 8:30	0.150	0.003	5	0
UW 2024	5/30/2024 8:30	5/30/2024 8:40	0.150	0.003	5	0
UW 2024	5/30/2024 8:40	5/30/2024 8:50	0.150	0.004	5	0
UW 2024	5/30/2024 8:50	5/30/2024 9:00	0.150	0.005	5	0
UW 2024	5/30/2024 9:00	5/30/2024 9:10	0.150	0.005	5	0
UW 2024	5/30/2024 9:10	5/30/2024 9:20	0.150	0.006	5	0
UW 2024	5/30/2024 9:20	5/30/2024 9:30	0.150	0.007	5	0
UW 2024	5/30/2024 9:30	5/30/2024 9:40	0.150	0.007	5	0
UW 2024	5/30/2024 9:40	5/30/2024 9:50	0.150	0.008	5	0
UW 2024	5/30/2024 9:50	5/30/2024 10:00	0.150	0.009	5	0
UW 2024	5/30/2024 10:00	5/30/2024 10:10	0.150	0.009	5	0
UW 2024	5/30/2024 10:10	5/30/2024 10:20	0.150	0.01	5	0
UW 2024	5/30/2024 10:20	5/30/2024 10:30	0.150	0.012	5	0
UW 2024	5/30/2024 10:30	5/30/2024 10:40	0.150	0.012	5	0
UW 2024	5/30/2024 10:40	5/30/2024 10:50	0.150	0.013	5	0
UW 2024	5/30/2024 10:50	5/30/2024 11:00	0.150	0.014	5	0
UW 2024	5/30/2024 11:00	5/30/2024 11:10	0.150	0.014	5	0
UW 2024	5/30/2024 11:10	5/30/2024 11:20	0.150	0.015	5	0
UW 2024	5/30/2024 11:20	5/30/2024 11:30	0.150	0.016	5	0
UW 2024	5/30/2024 11:30	5/30/2024 11:40	0.150	0.016	5	0
UW 2024	5/30/2024 11:40	5/30/2024 11:50	0.150	0.017	5	0
UW 2024	5/30/2024 11:50	5/30/2024 12:00	0.150	0.018	5	0
UW 2024	5/30/2024 12:00	5/30/2024 12:10	0.150	0.018	5	0
UW 2024	5/30/2024 12:10	5/30/2024 12:20	0.150	0.019	5	0
UW 2024	5/30/2024 12:20	5/30/2024 12:30	0.150	0.02	5	0
UW 2024	5/30/2024 12:30	5/30/2024 12:40	0.150	0.02	5	0
UW 2024	5/30/2024 12:40	5/30/2024 12:50	0.150	0.021	5	0
UW 2024	5/30/2024 12:50	5/30/2024 13:00	0.150	0.022	5	0
UW 2024	5/30/2024 13:00	5/30/2024 13:10	0.150	0.022	5	0
UW 2024	5/30/2024 13:10	5/30/2024 13:20	0.150	0.023	5	0
UW 2024	5/30/2024 13:20	5/30/2024 13:30	0.150	0.025	5	0
UW 2024	5/30/2024 13:30	5/30/2024 13:40	0.150	0.025	5	0
UW 2024	5/30/2024 13:40	5/30/2024 13:50	0.150	0.026	5	0
UW 2024	5/30/2024 13:50	5/30/2024 14:00	0.150	0.027	5	0
UW 2024	5/30/2024 14:00	5/30/2024 14:10	0.150	0.027	5	0
UW 2024	5/30/2024 14:10	5/30/2024 14:20	0.150	0.028	5	0
UW 2024	5/30/2024 14:20	5/30/2024 14:30	0.150	0.029	5	0
UW 2024	5/30/2024 14:30	5/30/2024 14:40	0.150	0.029	5	0
UW 2024	5/30/2024 14:40	5/30/2024 14:50	0.150	0.03	5	0
UW 2024	5/30/2024 14:50	5/30/2024 15:00	0.150	0.031	5	0
UW 2024	5/30/2024 15:00	5/30/2024 15:10	0.150	0.031	5	0
UW 2024	5/30/2024 15:10	5/30/2024 15:20	0.150	0.032	5	0
UW 2024	5/30/2024 15:20	5/30/2024 15:30	0.150	0.033	5	0
UW 2024	5/30/2024 15:30	5/30/2024 15:40	0.150	0.033	5	0
UW 2024	5/30/2024 15:40	5/30/2024 15:50	0.150	0.034	5	0
UW 2024	5/30/2024 15:50	5/30/2024 16:00	0.150	0	5	0
UW 2024	5/30/2024 16:00	5/30/2024 16:10	0.150	0	5	0
UW 2024	5/30/2024 16:10	5/30/2024 16:20	0.150	0	5	0
UW 2024	5/30/2024 16:20	5/30/2024 16:30	0.150	0	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/30/2024 7:30	5/30/2024 7:40	0.150	0	5	0
HS South	5/30/2024 7:40	5/30/2024 7:50	0.150	0	5	0
HS South	5/30/2024 7:50	5/30/2024 8:00	0.150	0	5	0
HS South	5/30/2024 8:00	5/30/2024 8:10	0.150	0.001	5	0
HS South	5/30/2024 8:10	5/30/2024 8:20	0.150	0.002	5	0
HS South	5/30/2024 8:20	5/30/2024 8:30	0.150	0.002	5	0
HS South	5/30/2024 8:30	5/30/2024 8:40	0.150	0.003	5	0
HS South	5/30/2024 8:40	5/30/2024 8:50	0.150	0.004	5	0
HS South	5/30/2024 8:50	5/30/2024 9:00	0.150	0.004	5	0
HS South	5/30/2024 9:00	5/30/2024 9:10	0.150	0.005	5	0
HS South	5/30/2024 9:10	5/30/2024 9:20	0.150	0.006	5	0
HS South	5/30/2024 9:20	5/30/2024 9:30	0.150	0.007	5	0
HS South	5/30/2024 9:30	5/30/2024 9:40	0.150	0.008	5	0
HS South	5/30/2024 9:40	5/30/2024 9:50	0.150	0.008	5	0
HS South	5/30/2024 9:50	5/30/2024 10:00	0.150	0.009	5	0
HS South	5/30/2024 10:00	5/30/2024 10:10	0.150	0.01	5	0
HS South	5/30/2024 10:10	5/30/2024 10:20	0.150	0.01	5	0
HS South	5/30/2024 10:20	5/30/2024 10:30	0.150	0.011	5	0
HS South	5/30/2024 10:30	5/30/2024 10:40	0.150	0.012	5	0
HS South	5/30/2024 10:40	5/30/2024 10:50	0.150	0.013	5	0
HS South	5/30/2024 10:50	5/30/2024 11:00	0.150	0.013	5	0
HS South	5/30/2024 11:00	5/30/2024 11:10	0.150	0.014	5	0
HS South	5/30/2024 11:10	5/30/2024 11:20	0.150	0.015	5	0
HS South	5/30/2024 11:20	5/30/2024 11:30	0.150	0.016	5	0
HS South	5/30/2024 11:30	5/30/2024 11:40	0.150	0.016	5	0
HS South	5/30/2024 11:40	5/30/2024 11:50	0.150	0.017	5	0
HS South	5/30/2024 11:50	5/30/2024 12:00	0.150	0.018	5	0
HS South	5/30/2024 12:00	5/30/2024 12:10	0.150	0.019	5	0
HS South	5/30/2024 12:10	5/30/2024 12:20	0.150	0.019	5	0
HS South	5/30/2024 12:20	5/30/2024 12:30	0.150	0.02	5	0
HS South	5/30/2024 12:30	5/30/2024 12:40	0.150	0.021	5	0
HS South	5/30/2024 12:40	5/30/2024 12:50	0.150	0.022	5	0
HS South	5/30/2024 12:50	5/30/2024 13:00	0.150	0.022	5	0
HS South	5/30/2024 13:00	5/30/2024 13:10	0.150	0.024	5	0
HS South	5/30/2024 13:10	5/30/2024 13:20	0.150	0.025	5	0
HS South	5/30/2024 13:20	5/30/2024 13:30	0.150	0.025	5	0
HS South	5/30/2024 13:30	5/30/2024 13:40	0.150	0.026	5	0
HS South	5/30/2024 13:40	5/30/2024 13:50	0.150	0.027	5	0
HS South	5/30/2024 13:50	5/30/2024 14:00	0.150	0.027	5	0
HS South	5/30/2024 14:00	5/30/2024 14:10	0.150	0.028	5	0
HS South	5/30/2024 14:10	5/30/2024 14:20	0.150	0.029	5	0
HS South	5/30/2024 14:20	5/30/2024 14:30	0.150	0.029	5	0
HS South	5/30/2024 14:30	5/30/2024 14:40	0.150	0.03	5	0
HS South	5/30/2024 14:40	5/30/2024 14:50	0.150	0.031	5	0
HS South	5/30/2024 14:50	5/30/2024 15:00	0.150	0.031	5	0
HS South	5/30/2024 15:00	5/30/2024 15:10	0.150	0.032	5	0
HS South	5/30/2024 15:10	5/30/2024 15:20	0.150	0.033	5	0
HS South	5/30/2024 15:20	5/30/2024 15:30	0.150	0.034	5	0
HS South	5/30/2024 15:30	5/30/2024 15:40	0.150	0.034	5	0
HS South	5/30/2024 15:40	5/30/2024 15:50	0.150	0.035	5	0
HS South	5/30/2024 15:50	5/30/2024 16:00	0.150	0.035	5	0
HS South	5/30/2024 16:00	5/30/2024 16:10	0.150	0.035	5	0
HS South	5/30/2024 16:10	5/30/2024 16:20	0.150	0.035	5	0
HS South	5/30/2024 16:20	5/30/2024 16:30	0.150	0.035	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/30/2024 7:30	5/30/2024 7:40	0.150	0.01	5	0
PER2 2024	5/30/2024 7:40	5/30/2024 7:50	0.150	0.01	5	0
PER2 2024	5/30/2024 7:50	5/30/2024 8:00	0.150	0.01	5	0
PER2 2024	5/30/2024 8:00	5/30/2024 8:10	0.150	0.01	5	0
PER2 2024	5/30/2024 8:10	5/30/2024 8:20	0.150	0.01	5	0
PER2 2024	5/30/2024 8:20	5/30/2024 8:30	0.150	0.01	5	0
PER2 2024	5/30/2024 8:30	5/30/2024 8:40	0.150	0.01	5	0
PER2 2024	5/30/2024 8:40	5/30/2024 8:50	0.150	0.001	5	0
PER2 2024	5/30/2024 8:50	5/30/2024 9:00	0.150	0.002	5	0
PER2 2024	5/30/2024 9:00	5/30/2024 9:10	0.150	0.002	5	0
PER2 2024	5/30/2024 9:10	5/30/2024 9:20	0.150	0.002	5	0
PER2 2024	5/30/2024 9:20	5/30/2024 9:30	0.150	0.002	5	0
PER2 2024	5/30/2024 9:30	5/30/2024 9:40	0.150	0.002	5	0
PER2 2024	5/30/2024 9:40	5/30/2024 9:50	0.150	0.003	5	0
PER2 2024	5/30/2024 9:50	5/30/2024 10:00	0.150	0.003	5	0
PER2 2024	5/30/2024 10:00	5/30/2024 10:10	0.150	0.003	5	0
PER2 2024	5/30/2024 10:10	5/30/2024 10:20	0.150	0.003	5	0
PER2 2024	5/30/2024 10:20	5/30/2024 10:30	0.150	0.004	5	0
PER2 2024	5/30/2024 10:30	5/30/2024 10:40	0.150	0.004	5	0
PER2 2024	5/30/2024 10:40	5/30/2024 10:50	0.150	0.004	5	0
PER2 2024	5/30/2024 10:50	5/30/2024 11:00	0.150	0.004	5	0
PER2 2024	5/30/2024 11:00	5/30/2024 11:10	0.150	0.004	5	0
PER2 2024	5/30/2024 11:10	5/30/2024 11:20	0.150	0.005	5	0
PER2 2024	5/30/2024 11:20	5/30/2024 11:30	0.150	0.005	5	0
PER2 2024	5/30/2024 11:30	5/30/2024 11:40	0.150	0.006	5	0
PER2 2024	5/30/2024 11:40	5/30/2024 11:50	0.150	0.006	5	0
PER2 2024	5/30/2024 11:50	5/30/2024 12:00	0.150	0.006	5	0
PER2 2024	5/30/2024 12:00	5/30/2024 12:10	0.150	0.006	5	0
PER2 2024	5/30/2024 12:10	5/30/2024 12:20	0.150	0.006	5	0
PER2 2024	5/30/2024 12:20	5/30/2024 12:30	0.150	0.007	5	0
PER2 2024	5/30/2024 12:30	5/30/2024 12:40	0.150	0.007	5	0
PER2 2024	5/30/2024 12:40	5/30/2024 12:50	0.150	0.007	5	0
PER2 2024	5/30/2024 12:50	5/30/2024 13:00	0.150	0.007	5	0
PER2 2024	5/30/2024 13:00	5/30/2024 13:10	0.150	0.007	5	0
PER2 2024	5/30/2024 13:10	5/30/2024 13:20	0.150	0.008	5	0
PER2 2024	5/30/2024 13:20	5/30/2024 13:30	0.150	0.008	5	0
PER2 2024	5/30/2024 13:30	5/30/2024 13:40	0.150	0.008	5	0
PER2 2024	5/30/2024 13:40	5/30/2024 13:50	0.150	0.008	5	0
PER2 2024	5/30/2024 13:50	5/30/2024 14:00	0.150	0.009	5	0
PER2 2024	5/30/2024 14:00	5/30/2024 14:10	0.150	0.009	5	0
PER2 2024	5/30/2024 14:10	5/30/2024 14:20	0.150	0.009	5	0
PER2 2024	5/30/2024 14:20	5/30/2024 14:30	0.150	0.009	5	0
PER2 2024	5/30/2024 14:30	5/30/2024 14:40	0.150	0.009	5	0
PER2 2024	5/30/2024 14:40	5/30/2024 14:50	0.150	0.01	5	0
PER2 2024	5/30/2024 14:50	5/30/2024 15:00	0.150	0.01	5	0
PER2 2024	5/30/2024 15:00	5/30/2024 15:10	0.150	0.01	5	0
PER2 2024	5/30/2024 15:10	5/30/2024 15:20	0.150	0.01	5	0
PER2 2024	5/30/2024 15:20	5/30/2024 15:30	0.150	0.01	5	0
PER2 2024	5/30/2024 15:30	5/30/2024 15:40	0.150	0.011	5	0
PER2 2024	5/30/2024 15:40	5/30/2024 15:50	0.150	0.011	5	0
PER2 2024	5/30/2024 15:50	5/30/2024 16:00	0.150	0.011	5	0
PER2 2024	5/30/2024 16:00	5/30/2024 16:10	0.150	0.011	5	0
PER2 2024	5/30/2024 16:10	5/30/2024 16:20	0.150	0.011	5	0
PER2 2024	5/30/2024 16:20	5/30/2024 16:30	0.150	0.011	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/30/2024 7:30	5/30/2024 7:40	0.150	0	5	0
PER1 2024	5/30/2024 7:40	5/30/2024 7:50	0.150	0	5	0
PER1 2024	5/30/2024 7:50	5/30/2024 8:00	0.150	0.001	5	0
PER1 2024	5/30/2024 8:00	5/30/2024 8:10	0.150	0.001	5	0
PER1 2024	5/30/2024 8:10	5/30/2024 8:20	0.150	0.001	5	0
PER1 2024	5/30/2024 8:20	5/30/2024 8:30	0.150	0.001	5	0
PER1 2024	5/30/2024 8:30	5/30/2024 8:40	0.150	0.001	5	0
PER1 2024	5/30/2024 8:40	5/30/2024 8:50	0.150	0.002	5	0
PER1 2024	5/30/2024 8:50	5/30/2024 9:00	0.150	0.002	5	0
PER1 2024	5/30/2024 9:00	5/30/2024 9:10	0.150	0.002	5	0
PER1 2024	5/30/2024 9:10	5/30/2024 9:20	0.150	0.002	5	0
PER1 2024	5/30/2024 9:20	5/30/2024 9:30	0.150	0.002	5	0
PER1 2024	5/30/2024 9:30	5/30/2024 9:40	0.150	0.003	5	0
PER1 2024	5/30/2024 9:40	5/30/2024 9:50	0.150	0.003	5	0
PER1 2024	5/30/2024 9:50	5/30/2024 10:00	0.150	0.003	5	0
PER1 2024	5/30/2024 10:00	5/30/2024 10:10	0.150	0.003	5	0
PER1 2024	5/30/2024 10:10	5/30/2024 10:20	0.150	0.003	5	0
PER1 2024	5/30/2024 10:20	5/30/2024 10:30	0.150	0.003	5	0
PER1 2024	5/30/2024 10:30	5/30/2024 10:40	0.150	0.004	5	0
PER1 2024	5/30/2024 10:40	5/30/2024 10:50	0.150	0.004	5	0
PER1 2024	5/30/2024 10:50	5/30/2024 11:00	0.150	0.004	5	0
PER1 2024	5/30/2024 11:00	5/30/2024 11:10	0.150	0.004	5	0
PER1 2024	5/30/2024 11:10	5/30/2024 11:20	0.150	0.005	5	0
PER1 2024	5/30/2024 11:20	5/30/2024 11:30	0.150	0.005	5	0
PER1 2024	5/30/2024 11:30	5/30/2024 11:40	0.150	0.005	5	0
PER1 2024	5/30/2024 11:40	5/30/2024 11:50	0.150	0.005	5	0
PER1 2024	5/30/2024 11:50	5/30/2024 12:00	0.150	0.006	5	0
PER1 2024	5/30/2024 12:00	5/30/2024 12:10	0.150	0.006	5	0
PER1 2024	5/30/2024 12:10	5/30/2024 12:20	0.150	0.006	5	0
PER1 2024	5/30/2024 12:20	5/30/2024 12:30	0.150	0.007	5	0
PER1 2024	5/30/2024 12:30	5/30/2024 12:40	0.150	0.007	5	0
PER1 2024	5/30/2024 12:40	5/30/2024 12:50	0.150	0.007	5	0
PER1 2024	5/30/2024 12:50	5/30/2024 13:00	0.150	0.008	5	0
PER1 2024	5/30/2024 13:00	5/30/2024 13:10	0.150	0.008	5	0
PER1 2024	5/30/2024 13:10	5/30/2024 13:20	0.150	0.009	5	0
PER1 2024	5/30/2024 13:20	5/30/2024 13:30	0.150	0.009	5	0
PER1 2024	5/30/2024 13:30	5/30/2024 13:40	0.150	0.009	5	0
PER1 2024	5/30/2024 13:40	5/30/2024 13:50	0.150	0.01	5	0
PER1 2024	5/30/2024 13:50	5/30/2024 14:00	0.150	0.01	5	0
PER1 2024	5/30/2024 14:00	5/30/2024 14:10	0.150	0.01	5	0
PER1 2024	5/30/2024 14:10	5/30/2024 14:20	0.150	0.011	5	0
PER1 2024	5/30/2024 14:20	5/30/2024 14:30	0.150	0.011	5	0.083
PER1 2024	5/30/2024 14:30	5/30/2024 14:40	0.150	0.012	5	0.083
PER1 2024	5/30/2024 14:40	5/30/2024 14:50	0.150	0.012	5	0.084
PER1 2024	5/30/2024 14:50	5/30/2024 15:00	0.150	0.012	5	0.084
PER1 2024	5/30/2024 15:00	5/30/2024 15:10	0.150	0.013	5	0.084
PER1 2024	5/30/2024 15:10	5/30/2024 15:20	0.150	0.013	5	0.084
PER1 2024	5/30/2024 15:20	5/30/2024 15:30	0.150	0.014	5	0.084
PER1 2024	5/30/2024 15:30	5/30/2024 15:40	0.150	0.014	5	0.084
PER1 2024	5/30/2024 15:40	5/30/2024 15:50	0.150	0.014	5	0.084
PER1 2024	5/30/2024 15:50	5/30/2024 16:00	0.150	0.014	5	0.084
PER1 2024	5/30/2024 16:00	5/30/2024 16:10	0.150	0.014	5	0.084
PER1 2024	5/30/2024 16:10	5/30/2024 16:20	0.150	0.014	5	0.084
PER1 2024	5/30/2024 16:20	5/30/2024 16:30	0.150	0.014	5	0.084

Daily Status Report	
Prepared by: C. Zaccheo	Date: 05/31/2024 Weather: 85 deg. F, Clear

Project: 470 Kent Avenue - Brooklyn, NY - DEC Site #s C224053 and 224053

Engineer: Matthew Carroll, P.E. Tenen Environmental, LLC	Safety Manager: Claire Zaccheo Tenen Environmental, LLC
Structural Contractor: New Line Services	Excavation Contractor: ALBA

Work Activities Performed: 1) Alba continued vertical form installation for building construction. 2) ECD continues to advance the remedial excavation to the east. 3) ECD exported 3 loads (~60 CY) of material from the remedial excavation for off-site disposal at the Bayshore Soil Management facility. 4) ECD imported 3 loads of 3/4" stone for backfill in the remedial excavation.

Is the dewatering system operating: YES NO
--

Health & Safety: (answer in red) Were there any changes to the H&S Plan? YES NO NA Were there any CAMP exceedances at the perimeter above action levels: YES NO NA Were there any dust or odor issues observed on this date? YES NO NA

Samples Collected (Since Last Report): None.

Air Monitoring (Since Last Report): CAMP graphs and tables are included below.


Problems Encountered: None.

Planned Work Activities for Next 2 Weeks: Continue superstructure development for A1 and A2 buildings; Contractor to continue A3 building foundation development. Continue excavation for the marine front remedial excavation.
--

Off-Site Material Disposal

Facility Location	Earth Efficient Harmony Foul Rift 1 Foul Rift Rd. Belvidere, NJ 07823	XRDS 190 Pompton Plains Cross Rd. Wayne, NJ 0740	Earth Efficient MSM 1080 Sand Hill Rd. E Stroudsburg, PA 18302	Bayshore Soil Management 75 Crows Mill Rd. Keasby, NJ 08832	Middlesex County Utilities Authority 2571 Main Street, Sayerville NJ 08872
Total:(CY)	0	0	0	60	0
Total:(CY)	4485	0	8685	1900	4140

Site Layout Map and Excavation Figures

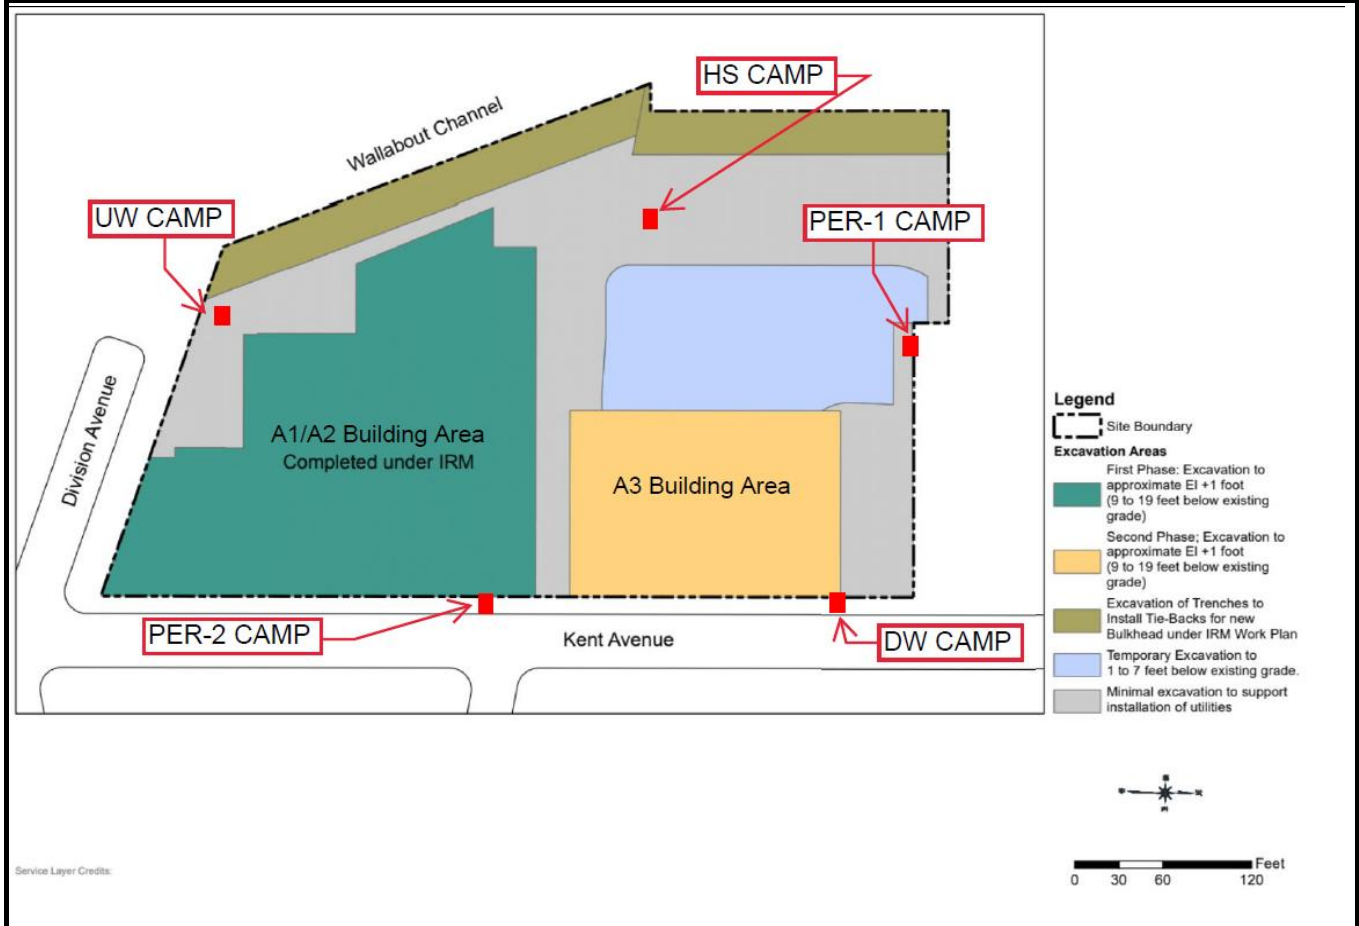

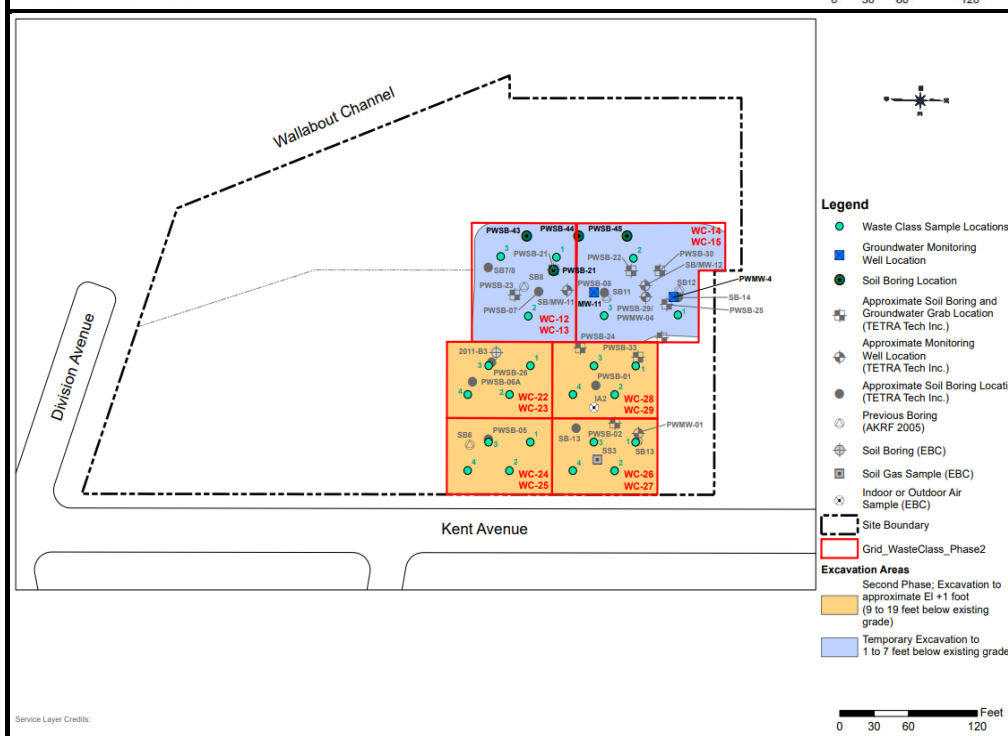
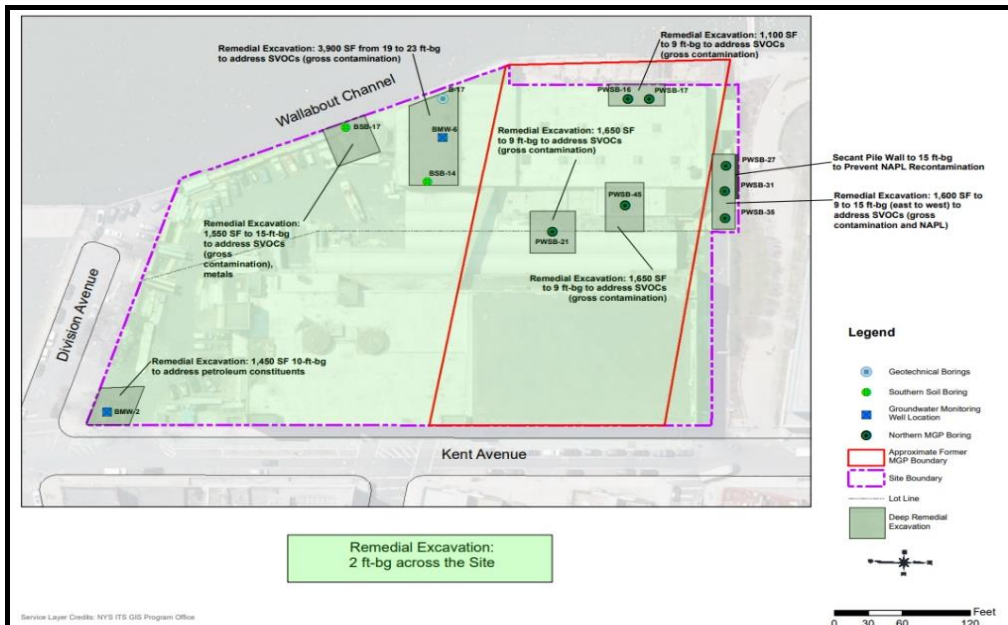


Photo 1:

View of the remedial excavation facing northwest.



Photo 2:

View of stone stockpiled for remedial excavation backfilling.



Photo 3:
View of truck loading
for off-site soil
disposal from the
remedial excavation.

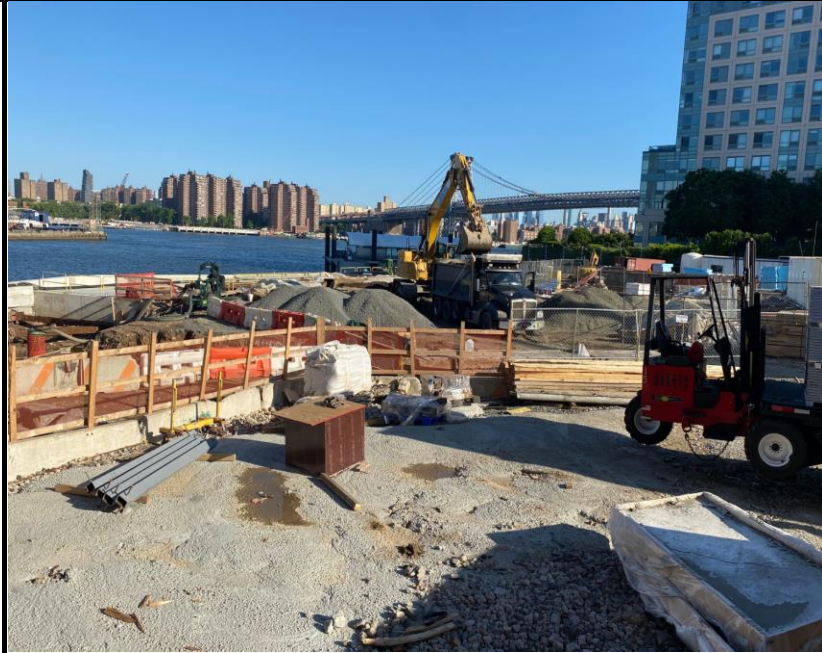



Photo 4:
View of the Site and
foundation
development facing
northeast.



CAMP:
Downwind
Particulates

Dust Levels


0.008 mg/m³ 0.013 mg/m³

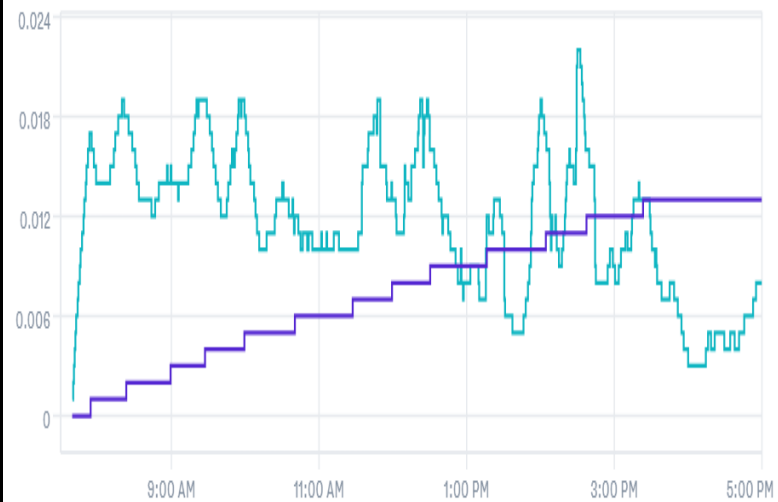

CAMP:
Downwind VOCs

VOC Levels


0 ppm 0 ppm

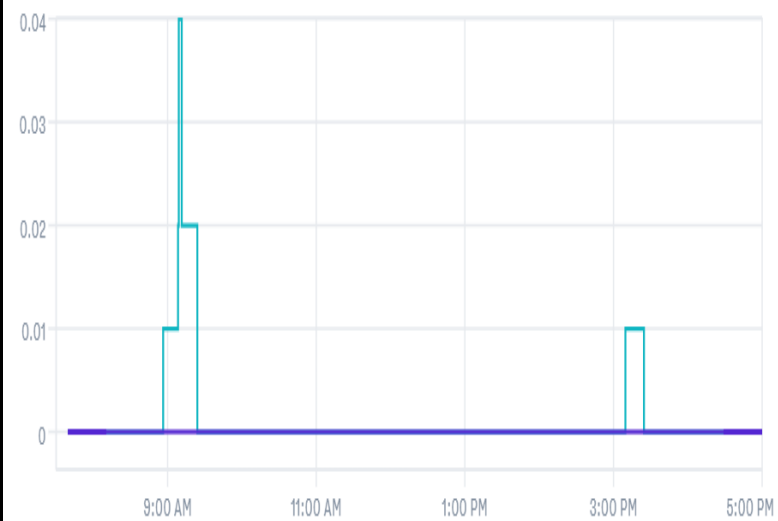

CAMP:
Upwind Particulates

Dust Levels


0.033 mg/m³ 0.035 mg/m³

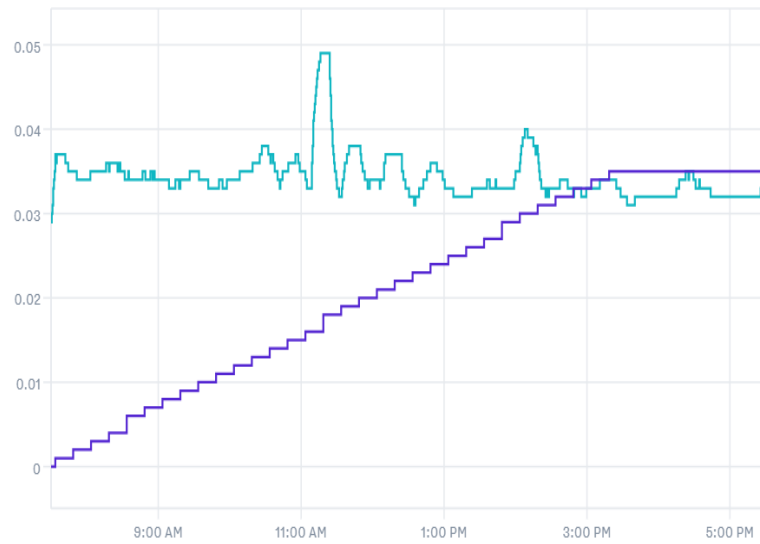

CAMP:
Upwind VOCs

VOC Levels

0 ppm 0 ppm

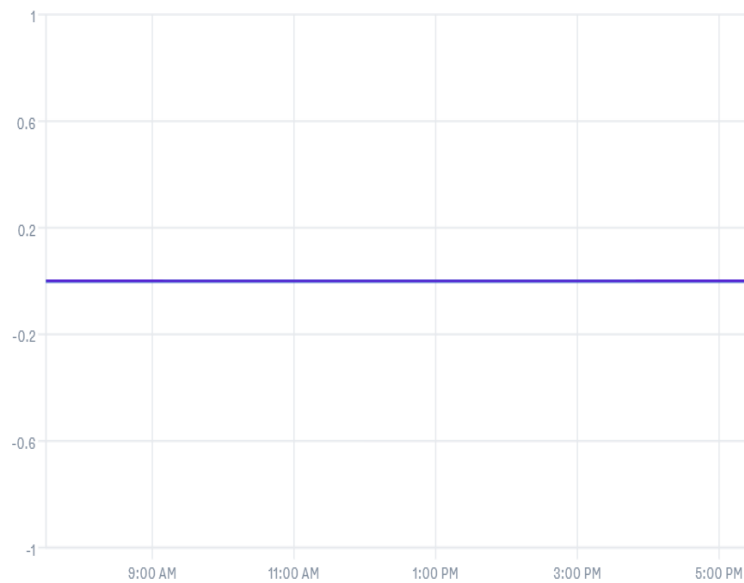

Downwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
DW 2024	5/31/2024 7:30	5/31/2024 7:40	0.150	0	5	0
DW 2024	5/31/2024 7:40	5/31/2024 7:50	0.150	0	5	0
DW 2024	5/31/2024 7:50	5/31/2024 8:00	0.150	0.001	5	0
DW 2024	5/31/2024 8:00	5/31/2024 8:10	0.150	0.001	5	0
DW 2024	5/31/2024 8:10	5/31/2024 8:20	0.150	0.001	5	0
DW 2024	5/31/2024 8:20	5/31/2024 8:30	0.150	0.002	5	0
DW 2024	5/31/2024 8:30	5/31/2024 8:40	0.150	0.002	5	0
DW 2024	5/31/2024 8:40	5/31/2024 8:50	0.150	0.002	5	0
DW 2024	5/31/2024 8:50	5/31/2024 9:00	0.150	0.003	5	0
DW 2024	5/31/2024 9:00	5/31/2024 9:10	0.150	0.003	5	0.001
DW 2024	5/31/2024 9:10	5/31/2024 9:20	0.150	0.003	5	0.001
DW 2024	5/31/2024 9:20	5/31/2024 9:30	0.150	0.004	5	0.001
DW 2024	5/31/2024 9:30	5/31/2024 9:40	0.150	0.004	5	0.001
DW 2024	5/31/2024 9:40	5/31/2024 9:50	0.150	0.004	5	0.001
DW 2024	5/31/2024 9:50	5/31/2024 10:00	0.150	0.005	5	0.001
DW 2024	5/31/2024 10:00	5/31/2024 10:10	0.150	0.005	5	0.001
DW 2024	5/31/2024 10:10	5/31/2024 10:20	0.150	0.005	5	0.001
DW 2024	5/31/2024 10:20	5/31/2024 10:30	0.150	0.005	5	0.001
DW 2024	5/31/2024 10:30	5/31/2024 10:40	0.150	0.005	5	0.001
DW 2024	5/31/2024 10:40	5/31/2024 10:50	0.150	0.006	5	0.001
DW 2024	5/31/2024 10:50	5/31/2024 11:00	0.150	0.006	5	0.001
DW 2024	5/31/2024 11:00	5/31/2024 11:10	0.150	0.006	5	0.001
DW 2024	5/31/2024 11:10	5/31/2024 11:20	0.150	0.006	5	0.001
DW 2024	5/31/2024 11:20	5/31/2024 11:30	0.150	0.007	5	0.001
DW 2024	5/31/2024 11:30	5/31/2024 11:40	0.150	0.007	5	0.001
DW 2024	5/31/2024 11:40	5/31/2024 11:50	0.150	0.007	5	0.001
DW 2024	5/31/2024 11:50	5/31/2024 12:00	0.150	0.008	5	0.001
DW 2024	5/31/2024 12:00	5/31/2024 12:10	0.150	0.008	5	0.001
DW 2024	5/31/2024 12:10	5/31/2024 12:20	0.150	0.008	5	0.001
DW 2024	5/31/2024 12:20	5/31/2024 12:30	0.150	0.008	5	0.001
DW 2024	5/31/2024 12:30	5/31/2024 12:40	0.150	0.009	5	0.001
DW 2024	5/31/2024 12:40	5/31/2024 12:50	0.150	0.009	5	0.001
DW 2024	5/31/2024 12:50	5/31/2024 13:00	0.150	0.009	5	0.001
DW 2024	5/31/2024 13:00	5/31/2024 13:10	0.150	0.009	5	0.001
DW 2024	5/31/2024 13:10	5/31/2024 13:20	0.150	0.01	5	0.001
DW 2024	5/31/2024 13:20	5/31/2024 13:30	0.150	0.01	5	0.001
DW 2024	5/31/2024 13:30	5/31/2024 13:40	0.150	0.01	5	0.001
DW 2024	5/31/2024 13:40	5/31/2024 13:50	0.150	0.01	5	0.001
DW 2024	5/31/2024 13:50	5/31/2024 14:00	0.150	0.01	5	0.001
DW 2024	5/31/2024 14:00	5/31/2024 14:10	0.150	0.011	5	0.001
DW 2024	5/31/2024 14:10	5/31/2024 14:20	0.150	0.011	5	0.001
DW 2024	5/31/2024 14:20	5/31/2024 14:30	0.150	0.011	5	0.001
DW 2024	5/31/2024 14:30	5/31/2024 14:40	0.150	0.012	5	0.001
DW 2024	5/31/2024 14:40	5/31/2024 14:50	0.150	0.012	5	0.001
DW 2024	5/31/2024 14:50	5/31/2024 15:00	0.150	0.012	5	0.001
DW 2024	5/31/2024 15:00	5/31/2024 15:10	0.150	0.012	5	0.001
DW 2024	5/31/2024 15:10	5/31/2024 15:20	0.150	0.012	5	0.001
DW 2024	5/31/2024 15:20	5/31/2024 15:30	0.150	0.013	5	0.001
DW 2024	5/31/2024 15:30	5/31/2024 15:40	0.150	0.013	5	0.001
DW 2024	5/31/2024 15:40	5/31/2024 15:50	0.150	0.013	5	0.001
DW 2024	5/31/2024 15:50	5/31/2024 16:00	0.150	0.013	5	0.001
DW 2024	5/31/2024 16:00	5/31/2024 16:10	0.150	0.013	5	0.001
DW 2024	5/31/2024 16:10	5/31/2024 16:20	0.150	0.013	5	0.001
DW 2024	5/31/2024 16:20	5/31/2024 16:30	0.150	0.013	5	0.001
DW 2024	5/31/2024 16:30	5/31/2024 16:40	0.150	0.013	5	0.001
DW 2024	5/31/2024 16:40	5/31/2024 16:50	0.150	0.013	5	0.001
DW 2024	5/31/2024 16:50	5/31/2024 17:00	0.150	0.013	5	0.001

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
UW 2024	5/31/2024 7:30	5/31/2024 7:40	0.150	0.001	5	0
UW 2024	5/31/2024 7:40	5/31/2024 7:50	0.150	0.002	5	0
UW 2024	5/31/2024 7:50	5/31/2024 8:00	0.150	0.002	5	0
UW 2024	5/31/2024 8:00	5/31/2024 8:10	0.150	0.003	5	0
UW 2024	5/31/2024 8:10	5/31/2024 8:20	0.150	0.004	5	0
UW 2024	5/31/2024 8:20	5/31/2024 8:30	0.150	0.004	5	0
UW 2024	5/31/2024 8:30	5/31/2024 8:40	0.150	0.006	5	0
UW 2024	5/31/2024 8:40	5/31/2024 8:50	0.150	0.007	5	0
UW 2024	5/31/2024 8:50	5/31/2024 9:00	0.150	0.007	5	0
UW 2024	5/31/2024 9:00	5/31/2024 9:10	0.150	0.008	5	0
UW 2024	5/31/2024 9:10	5/31/2024 9:20	0.150	0.009	5	0
UW 2024	5/31/2024 9:20	5/31/2024 9:30	0.150	0.009	5	0
UW 2024	5/31/2024 9:30	5/31/2024 9:40	0.150	0.01	5	0
UW 2024	5/31/2024 9:40	5/31/2024 9:50	0.150	0.011	5	0
UW 2024	5/31/2024 9:50	5/31/2024 10:00	0.150	0.011	5	0
UW 2024	5/31/2024 10:00	5/31/2024 10:10	0.150	0.012	5	0
UW 2024	5/31/2024 10:10	5/31/2024 10:20	0.150	0.013	5	0
UW 2024	5/31/2024 10:20	5/31/2024 10:30	0.150	0.013	5	0
UW 2024	5/31/2024 10:30	5/31/2024 10:40	0.150	0.014	5	0
UW 2024	5/31/2024 10:40	5/31/2024 10:50	0.150	0.015	5	0
UW 2024	5/31/2024 10:50	5/31/2024 11:00	0.150	0.015	5	0
UW 2024	5/31/2024 11:00	5/31/2024 11:10	0.150	0.016	5	0
UW 2024	5/31/2024 11:10	5/31/2024 11:20	0.150	0.018	5	0
UW 2024	5/31/2024 11:20	5/31/2024 11:30	0.150	0.018	5	0
UW 2024	5/31/2024 11:30	5/31/2024 11:40	0.150	0.019	5	0
UW 2024	5/31/2024 11:40	5/31/2024 11:50	0.150	0.02	5	0
UW 2024	5/31/2024 11:50	5/31/2024 12:00	0.150	0.02	5	0
UW 2024	5/31/2024 12:00	5/31/2024 12:10	0.150	0.021	5	0
UW 2024	5/31/2024 12:10	5/31/2024 12:20	0.150	0.022	5	0
UW 2024	5/31/2024 12:20	5/31/2024 12:30	0.150	0.022	5	0
UW 2024	5/31/2024 12:30	5/31/2024 12:40	0.150	0.023	5	0
UW 2024	5/31/2024 12:40	5/31/2024 12:50	0.150	0.024	5	0
UW 2024	5/31/2024 12:50	5/31/2024 13:00	0.150	0.024	5	0
UW 2024	5/31/2024 13:00	5/31/2024 13:10	0.150	0.025	5	0
UW 2024	5/31/2024 13:10	5/31/2024 13:20	0.150	0.026	5	0
UW 2024	5/31/2024 13:20	5/31/2024 13:30	0.150	0.026	5	0
UW 2024	5/31/2024 13:30	5/31/2024 13:40	0.150	0.027	5	0
UW 2024	5/31/2024 13:40	5/31/2024 13:50	0.150	0.029	5	0
UW 2024	5/31/2024 13:50	5/31/2024 14:00	0.150	0.029	5	0
UW 2024	5/31/2024 14:00	5/31/2024 14:10	0.150	0.03	5	0
UW 2024	5/31/2024 14:10	5/31/2024 14:20	0.150	0.031	5	0
UW 2024	5/31/2024 14:20	5/31/2024 14:30	0.150	0.031	5	0
UW 2024	5/31/2024 14:30	5/31/2024 14:40	0.150	0.032	5	0
UW 2024	5/31/2024 14:40	5/31/2024 14:50	0.150	0.033	5	0
UW 2024	5/31/2024 14:50	5/31/2024 15:00	0.150	0.033	5	0
UW 2024	5/31/2024 15:00	5/31/2024 15:10	0.150	0.034	5	0
UW 2024	5/31/2024 15:10	5/31/2024 15:20	0.150	0.035	5	0
UW 2024	5/31/2024 15:20	5/31/2024 15:30	0.150	0.035	5	0
UW 2024	5/31/2024 15:30	5/31/2024 15:40	0.150	0.035	5	0
UW 2024	5/31/2024 15:40	5/31/2024 15:50	0.150	0.035	5	0
UW 2024	5/31/2024 15:50	5/31/2024 16:00	0.150	0.035	5	0
UW 2024	5/31/2024 16:00	5/31/2024 16:10	0.150	0.035	5	0
UW 2024	5/31/2024 16:10	5/31/2024 16:20	0.150	0.035	5	0
UW 2024	5/31/2024 16:20	5/31/2024 16:30	0.150	0.035	5	0
UW 2024	5/31/2024 16:30	5/31/2024 16:40	0.150	0.035	5	0
UW 2024	5/31/2024 16:40	5/31/2024 16:50	0.150	0.035	5	0
UW 2024	5/31/2024 16:50	5/31/2024 17:00	0.150	0.035	5	0

Remedial Excavation CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
HS South	5/31/2024 7:30	5/31/2024 7:40	0.150	0.009	5	0
HS South	5/31/2024 7:40	5/31/2024 7:50	0.150	0.009	5	0
HS South	5/31/2024 7:50	5/31/2024 8:00	0.150	0.01	5	0
HS South	5/31/2024 8:00	5/31/2024 8:10	0.150	0.011	5	0
HS South	5/31/2024 8:10	5/31/2024 8:20	0.150	0.012	5	0
HS South	5/31/2024 8:20	5/31/2024 8:30	0.150	0.013	5	0
HS South	5/31/2024 8:30	5/31/2024 8:40	0.150	0.014	5	0
HS South	5/31/2024 8:40	5/31/2024 8:50	0.150	0.014	5	0
HS South	5/31/2024 8:50	5/31/2024 9:00	0.150	0.015	5	0
HS South	5/31/2024 9:00	5/31/2024 9:10	0.150	0.016	5	0
HS South	5/31/2024 9:10	5/31/2024 9:20	0.150	0.017	5	0
HS South	5/31/2024 9:20	5/31/2024 9:30	0.150	0.017	5	0
HS South	5/31/2024 9:30	5/31/2024 9:40	0.150	0.018	5	0
HS South	5/31/2024 9:40	5/31/2024 9:50	0.150	0.018	5	0
HS South	5/31/2024 9:50	5/31/2024 10:00	0.150	0.018	5	0
HS South	5/31/2024 10:00	5/31/2024 10:10	0.150	0.018	5	0
HS South	5/31/2024 10:10	5/31/2024 10:20	0.150	0.018	5	0
HS South	5/31/2024 10:20	5/31/2024 10:30	0.150	0.018	5	0
HS South	5/31/2024 10:30	5/31/2024 10:40	0.150	0.018	5	0
HS South	5/31/2024 10:40	5/31/2024 10:50	0.150	0.018	5	0
HS South	5/31/2024 10:50	5/31/2024 11:00	0.150	0.018	5	0
HS South	5/31/2024 11:00	5/31/2024 11:10	0.150	0.018	5	0
HS South	5/31/2024 11:10	5/31/2024 11:20	0.150	0.018	5	0
HS South	5/31/2024 11:20	5/31/2024 11:30	0.150	0.018	5	0
HS South	5/31/2024 11:30	5/31/2024 11:40	0.150	0.018	5	0
HS South	5/31/2024 11:40	5/31/2024 11:50	0.150	0.018	5	0
HS South	5/31/2024 11:50	5/31/2024 12:00	0.150	0.018	5	0
HS South	5/31/2024 12:00	5/31/2024 12:10	0.150	0.018	5	0
HS South	5/31/2024 12:10	5/31/2024 12:20	0.150	0.018	5	0
HS South	5/31/2024 12:20	5/31/2024 12:30	0.150	0.018	5	0
HS South	5/31/2024 12:30	5/31/2024 12:40	0.150	0.018	5	0
HS South	5/31/2024 12:40	5/31/2024 12:50	0.150	0.018	5	0
HS South	5/31/2024 12:50	5/31/2024 13:00	0.150	0.018	5	0
HS South	5/31/2024 13:00	5/31/2024 13:10	0.150	0.018	5	0
HS South	5/31/2024 13:10	5/31/2024 13:20	0.150	0.038	5	0
HS South	5/31/2024 13:20	5/31/2024 13:30	0.150	0.039	5	0
HS South	5/31/2024 13:30	5/31/2024 13:40	0.150	0.039	5	0
HS South	5/31/2024 13:40	5/31/2024 13:50	0.150	0.04	5	0
HS South	5/31/2024 13:50	5/31/2024 14:00	0.150	0.041	5	0
HS South	5/31/2024 14:00	5/31/2024 14:10	0.150	0.043	5	0
HS South	5/31/2024 14:10	5/31/2024 14:20	0.150	0.044	5	0
HS South	5/31/2024 14:20	5/31/2024 14:30	0.150	0.045	5	0
HS South	5/31/2024 14:30	5/31/2024 14:40	0.150	0.046	5	0
HS South	5/31/2024 14:40	5/31/2024 14:50	0.150	0.047	5	0
HS South	5/31/2024 14:50	5/31/2024 15:00	0.150	0.048	5	0
HS South	5/31/2024 15:00	5/31/2024 15:10	0.150	0.049	5	0
HS South	5/31/2024 15:10	5/31/2024 15:20	0.150	0.05	5	0
HS South	5/31/2024 15:20	5/31/2024 15:30	0.150	0.05	5	0
HS South	5/31/2024 15:30	5/31/2024 15:40	0.150	0.05	5	0
HS South	5/31/2024 15:40	5/31/2024 15:50	0.150	0.05	5	0
HS South	5/31/2024 15:50	5/31/2024 16:00	0.150	0.05	5	0
HS South	5/31/2024 16:00	5/31/2024 16:10	0.150	0.05	5	0
HS South	5/31/2024 16:10	5/31/2024 16:20	0.150	0.05	5	0
HS South	5/31/2024 16:20	5/31/2024 16:30	0.150	0.05	5	0
HS South	5/31/2024 16:30	5/31/2024 16:40	0.150	0.05	5	0
HS South	5/31/2024 16:40	5/31/2024 16:50	0.150	0	5	0
HS South	5/31/2024 16:50	5/31/2024 17:00	0.150	0	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER2 2024	5/31/2024 7:30	5/31/2024 7:40	0.150	0.011	5	0
PER2 2024	5/31/2024 7:40	5/31/2024 7:50	0.150	0	5	0
PER2 2024	5/31/2024 7:50	5/31/2024 8:00	0.150	0.001	5	0
PER2 2024	5/31/2024 8:00	5/31/2024 8:10	0.150	0.001	5	0
PER2 2024	5/31/2024 8:10	5/31/2024 8:20	0.150	0.001	5	0
PER2 2024	5/31/2024 8:20	5/31/2024 8:30	0.150	0.001	5	0
PER2 2024	5/31/2024 8:30	5/31/2024 8:40	0.150	0.002	5	0
PER2 2024	5/31/2024 8:40	5/31/2024 8:50	0.150	0.002	5	0
PER2 2024	5/31/2024 8:50	5/31/2024 9:00	0.150	0.002	5	0
PER2 2024	5/31/2024 9:00	5/31/2024 9:10	0.150	0.002	5	0
PER2 2024	5/31/2024 9:10	5/31/2024 9:20	0.150	0.002	5	0
PER2 2024	5/31/2024 9:20	5/31/2024 9:30	0.150	0.003	5	0
PER2 2024	5/31/2024 9:30	5/31/2024 9:40	0.150	0.003	5	0
PER2 2024	5/31/2024 9:40	5/31/2024 9:50	0.150	0.003	5	0
PER2 2024	5/31/2024 9:50	5/31/2024 10:00	0.150	0.003	5	0
PER2 2024	5/31/2024 10:00	5/31/2024 10:10	0.150	0.003	5	0
PER2 2024	5/31/2024 10:10	5/31/2024 10:20	0.150	0.003	5	0
PER2 2024	5/31/2024 10:20	5/31/2024 10:30	0.150	0.004	5	0
PER2 2024	5/31/2024 10:30	5/31/2024 10:40	0.150	0.004	5	0
PER2 2024	5/31/2024 10:40	5/31/2024 10:50	0.150	0.004	5	0
PER2 2024	5/31/2024 10:50	5/31/2024 11:00	0.150	0.004	5	0
PER2 2024	5/31/2024 11:00	5/31/2024 11:10	0.150	0.004	5	0
PER2 2024	5/31/2024 11:10	5/31/2024 11:20	0.150	0.004	5	0
PER2 2024	5/31/2024 11:20	5/31/2024 11:30	0.150	0.005	5	0
PER2 2024	5/31/2024 11:30	5/31/2024 11:40	0.150	0.005	5	0
PER2 2024	5/31/2024 11:40	5/31/2024 11:50	0.150	0.005	5	0
PER2 2024	5/31/2024 11:50	5/31/2024 12:00	0.150	0.005	5	0
PER2 2024	5/31/2024 12:00	5/31/2024 12:10	0.150	0.005	5	0
PER2 2024	5/31/2024 12:10	5/31/2024 12:20	0.150	0.005	5	0
PER2 2024	5/31/2024 12:20	5/31/2024 12:30	0.150	0.006	5	0
PER2 2024	5/31/2024 12:30	5/31/2024 12:40	0.150	0.006	5	0
PER2 2024	5/31/2024 12:40	5/31/2024 12:50	0.150	0.006	5	0
PER2 2024	5/31/2024 12:50	5/31/2024 13:00	0.150	0.006	5	0
PER2 2024	5/31/2024 13:00	5/31/2024 13:10	0.150	0.006	5	0
PER2 2024	5/31/2024 13:10	5/31/2024 13:20	0.150	0.006	5	0
PER2 2024	5/31/2024 13:20	5/31/2024 13:30	0.150	0.006	5	0
PER2 2024	5/31/2024 13:30	5/31/2024 13:40	0.150	0.007	5	0
PER2 2024	5/31/2024 13:40	5/31/2024 13:50	0.150	0.007	5	0
PER2 2024	5/31/2024 13:50	5/31/2024 14:00	0.150	0.007	5	0
PER2 2024	5/31/2024 14:00	5/31/2024 14:10	0.150	0.007	5	0
PER2 2024	5/31/2024 14:10	5/31/2024 14:20	0.150	0.008	5	0
PER2 2024	5/31/2024 14:20	5/31/2024 14:30	0.150	0.008	5	0
PER2 2024	5/31/2024 14:30	5/31/2024 14:40	0.150	0.008	5	0
PER2 2024	5/31/2024 14:40	5/31/2024 14:50	0.150	0.009	5	0
PER2 2024	5/31/2024 14:50	5/31/2024 15:00	0.150	0.009	5	0
PER2 2024	5/31/2024 15:00	5/31/2024 15:10	0.150	0.009	5	0
PER2 2024	5/31/2024 15:10	5/31/2024 15:20	0.150	0.009	5	0
PER2 2024	5/31/2024 15:20	5/31/2024 15:30	0.150	0.01	5	0
PER2 2024	5/31/2024 15:30	5/31/2024 15:40	0.150	0.01	5	0
PER2 2024	5/31/2024 15:40	5/31/2024 15:50	0.150	0.01	5	0
PER2 2024	5/31/2024 15:50	5/31/2024 16:00	0.150	0.01	5	0
PER2 2024	5/31/2024 16:00	5/31/2024 16:10	0.150	0.01	5	0
PER2 2024	5/31/2024 16:10	5/31/2024 16:20	0.150	0.01	5	0
PER2 2024	5/31/2024 16:20	5/31/2024 16:30	0.150	0.01	5	0
PER2 2024	5/31/2024 16:30	5/31/2024 16:40	0.150	0.01	5	0
PER2 2024	5/31/2024 16:40	5/31/2024 16:50	0.150	0.01	5	0
PER2 2024	5/31/2024 16:50	5/31/2024 17:00	0.150	0.01	5	0

Perimeter CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
PER1 2024	5/31/2024 7:30	5/31/2024 7:40	0.150	0	5	0
PER1 2024	5/31/2024 7:40	5/31/2024 7:50	0.150	0.001	5	0
PER1 2024	5/31/2024 7:50	5/31/2024 8:00	0.150	0.001	5	0
PER1 2024	5/31/2024 8:00	5/31/2024 8:10	0.150	0.001	5	0
PER1 2024	5/31/2024 8:10	5/31/2024 8:20	0.150	0.002	5	0
PER1 2024	5/31/2024 8:20	5/31/2024 8:30	0.150	0.002	5	0
PER1 2024	5/31/2024 8:30	5/31/2024 8:40	0.150	0.002	5	0
PER1 2024	5/31/2024 8:40	5/31/2024 8:50	0.150	0.002	5	0
PER1 2024	5/31/2024 8:50	5/31/2024 9:00	0.150	0.003	5	0
PER1 2024	5/31/2024 9:00	5/31/2024 9:10	0.150	0.003	5	0
PER1 2024	5/31/2024 9:10	5/31/2024 9:20	0.150	0.003	5	0
PER1 2024	5/31/2024 9:20	5/31/2024 9:30	0.150	0.004	5	0
PER1 2024	5/31/2024 9:30	5/31/2024 9:40	0.150	0.004	5	0
PER1 2024	5/31/2024 9:40	5/31/2024 9:50	0.150	0.005	5	0
PER1 2024	5/31/2024 9:50	5/31/2024 10:00	0.150	0.005	5	0
PER1 2024	5/31/2024 10:00	5/31/2024 10:10	0.150	0.005	5	0
PER1 2024	5/31/2024 10:10	5/31/2024 10:20	0.150	0.006	5	0
PER1 2024	5/31/2024 10:20	5/31/2024 10:30	0.150	0.006	5	0
PER1 2024	5/31/2024 10:30	5/31/2024 10:40	0.150	0.007	5	0
PER1 2024	5/31/2024 10:40	5/31/2024 10:50	0.150	0.007	5	0
PER1 2024	5/31/2024 10:50	5/31/2024 11:00	0.150	0.007	5	0
PER1 2024	5/31/2024 11:00	5/31/2024 11:10	0.150	0.008	5	0
PER1 2024	5/31/2024 11:10	5/31/2024 11:20	0.150	0.008	5	0
PER1 2024	5/31/2024 11:20	5/31/2024 11:30	0.150	0.009	5	0
PER1 2024	5/31/2024 11:30	5/31/2024 11:40	0.150	0.009	5	0
PER1 2024	5/31/2024 11:40	5/31/2024 11:50	0.150	0.01	5	0
PER1 2024	5/31/2024 11:50	5/31/2024 12:00	0.150	0.011	5	0
PER1 2024	5/31/2024 12:00	5/31/2024 12:10	0.150	0.011	5	0
PER1 2024	5/31/2024 12:10	5/31/2024 12:20	0.150	0.012	5	0
PER1 2024	5/31/2024 12:20	5/31/2024 12:30	0.150	0.012	5	0
PER1 2024	5/31/2024 12:30	5/31/2024 12:40	0.150	0.013	5	0
PER1 2024	5/31/2024 12:40	5/31/2024 12:50	0.150	0.014	5	0
PER1 2024	5/31/2024 12:50	5/31/2024 13:00	0.150	0.014	5	0
PER1 2024	5/31/2024 13:00	5/31/2024 13:10	0.150	0.015	5	0
PER1 2024	5/31/2024 13:10	5/31/2024 13:20	0.150	0.015	5	0
PER1 2024	5/31/2024 13:20	5/31/2024 13:30	0.150	0.016	5	0
PER1 2024	5/31/2024 13:30	5/31/2024 13:40	0.150	0.017	5	0
PER1 2024	5/31/2024 13:40	5/31/2024 13:50	0.150	0.018	5	0
PER1 2024	5/31/2024 13:50	5/31/2024 14:00	0.150	0.019	5	0
PER1 2024	5/31/2024 14:00	5/31/2024 14:10	0.150	0.021	5	0
PER1 2024	5/31/2024 14:10	5/31/2024 14:20	0.150	0.023	5	0
PER1 2024	5/31/2024 14:20	5/31/2024 14:30	0.150	0.024	5	0
PER1 2024	5/31/2024 14:30	5/31/2024 14:40	0.150	0.025	5	0
PER1 2024	5/31/2024 14:40	5/31/2024 14:50	0.150	0.025	5	0
PER1 2024	5/31/2024 14:50	5/31/2024 15:00	0.150	0.026	5	0
PER1 2024	5/31/2024 15:00	5/31/2024 15:10	0.150	0.027	5	0
PER1 2024	5/31/2024 15:10	5/31/2024 15:20	0.150	0.028	5	0
PER1 2024	5/31/2024 15:20	5/31/2024 15:30	0.150	0.028	5	0
PER1 2024	5/31/2024 15:30	5/31/2024 15:40	0.150	0.028	5	0
PER1 2024	5/31/2024 15:40	5/31/2024 15:50	0.150	0.028	5	0
PER1 2024	5/31/2024 15:50	5/31/2024 16:00	0.150	0.028	5	0
PER1 2024	5/31/2024 16:00	5/31/2024 16:10	0.150	0.028	5	0
PER1 2024	5/31/2024 16:10	5/31/2024 16:20	0.150	0.028	5	0
PER1 2024	5/31/2024 16:20	5/31/2024 16:30	0.150	0.028	5	0
PER1 2024	5/31/2024 16:30	5/31/2024 16:40	0.150	0.028	5	0
PER1 2024	5/31/2024 16:40	5/31/2024 16:50	0.150	0	5	0
PER1 2024	5/31/2024 16:50	5/31/2024 17:00	0.150	0	5	0
