

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain		Overcast		Partly Cloudy	X	Bright Sun	X
TEMP.	< 32		32-50		50-70		70-85	X	>85	

BCP Site ID #:C224267

Date: 05/01/2024

Project Name: **3901-3913 8th Avenue – Brooklyn, NY****Consultant:**Matthew Carroll, P.E.
Tenen Environmental**Safety Officer:**Claire Zaccheo
Tenen Environmental**General Contractor:**EarthTech Services, Inc.
222 William Street
Bronx, NY 10461**EarthTech Site Superintendent:**Sam Caller
(347) 907-4053**Work Activities Performed (Since Last Report):**

The contractor completed welding for support of excavation, and; began cleaning large boulders with wire brushes, brooms and air.

Working In Grid #: A1, A2 and A3**Samples Collected (Since Last Report):** None.**Air Monitoring (Since Last Report):****Background Conditions**

Upwind: Dust: 0.049 mg/m3 PID: 0.0 ppm
Downwind: Dust: 0.031 mg/m3 PID: 0.0 ppm

Daily TWA

Upwind: Dust: 0.022 mg/m3 PID: 0.006 ppm
Downwind: Dust: 0.061 mg/m3 PID: 0.061 ppm

Problems Encountered: None.**Planned Activities for the Next Day/ Week:**

The contractor will continue excavation and disposing of soil off-site.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832		Facility # Name Location	
(Trucks, CY)	Trucks	Cu. Yds.	Trucks	Cu. Yds.
Today	0	0		
Total	20	400		

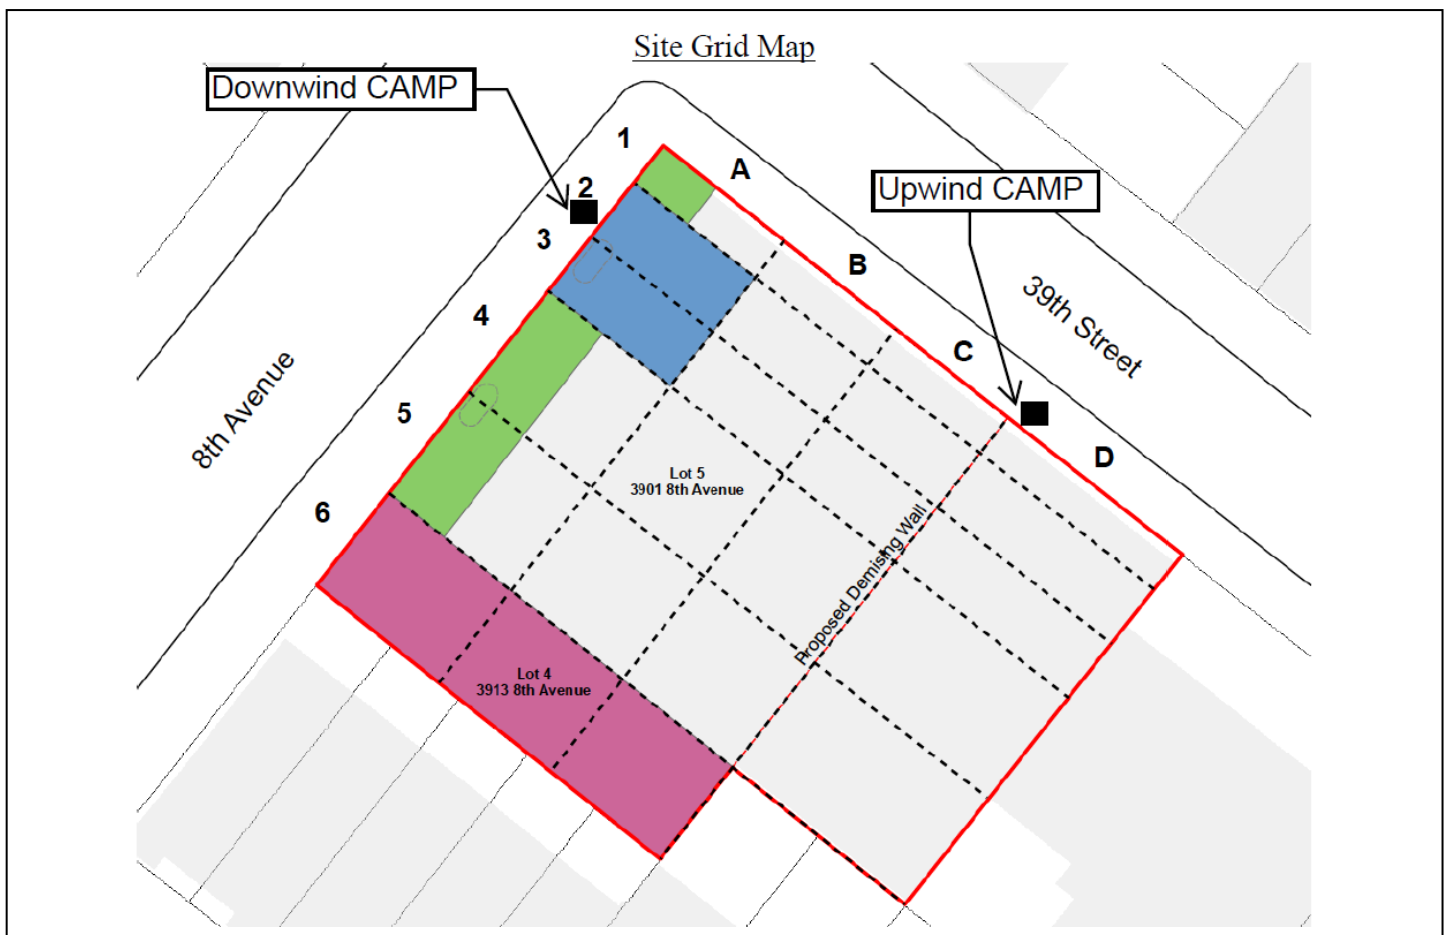


Photo Log

Photo 1 –
View of
boulder
cleaning.



Photo 2 –
View of the
excavation.



Photo 3 –
View of
soil
stockpiles.



CAMP Data


DW CAMP

Dust Levels

0.028 mg/m³

0.061 mg/m³

0.15

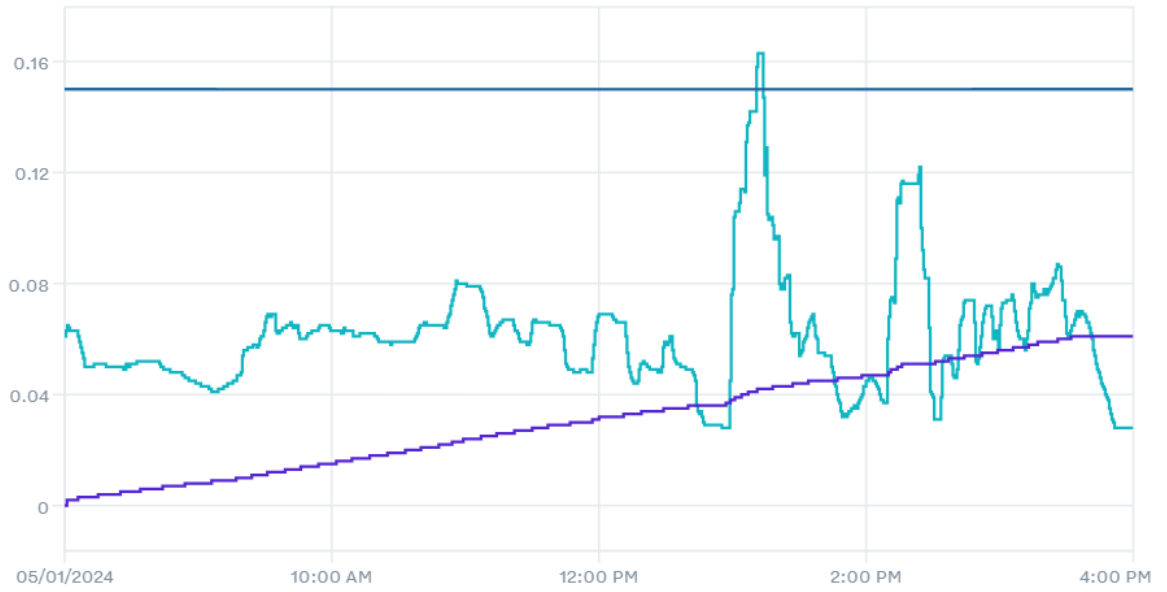


VOC Levels

0 ppm

0.061 ppm

5

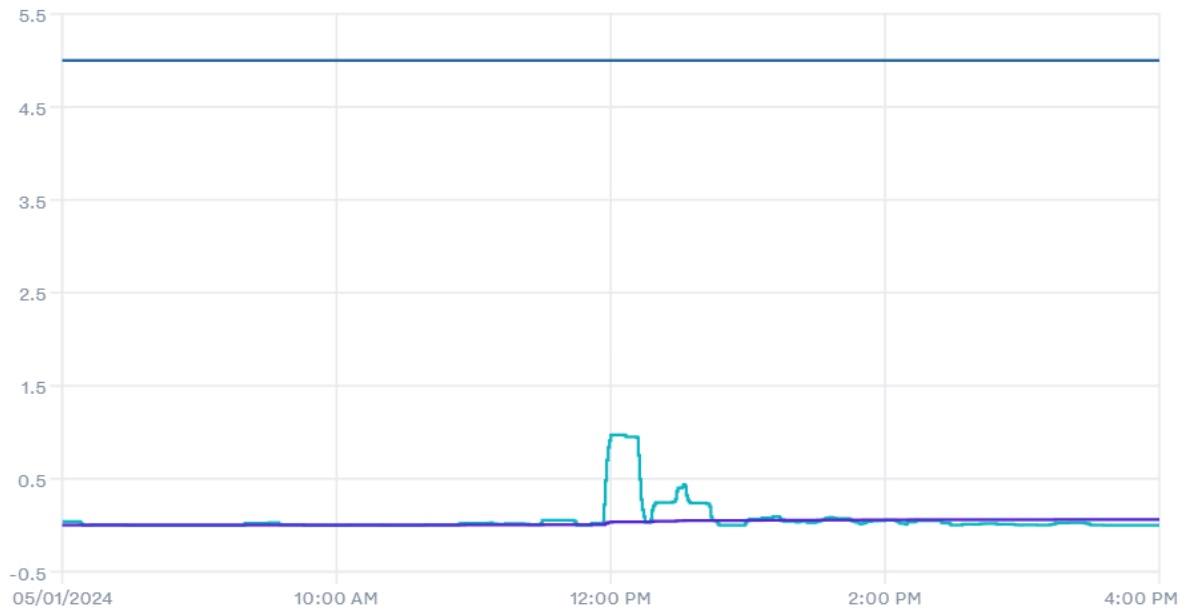


UW CAMP

Dust Levels

0.026 mg/m³

0.022 mg/m³

0.15

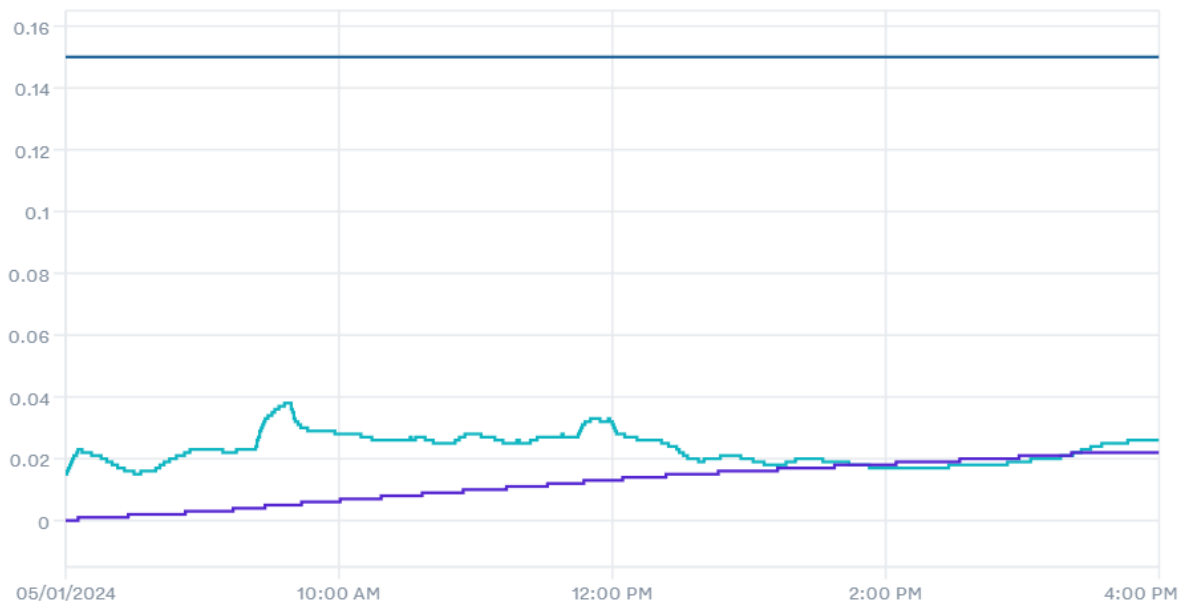


VOC Levels

0 ppm

0.006 ppm

5

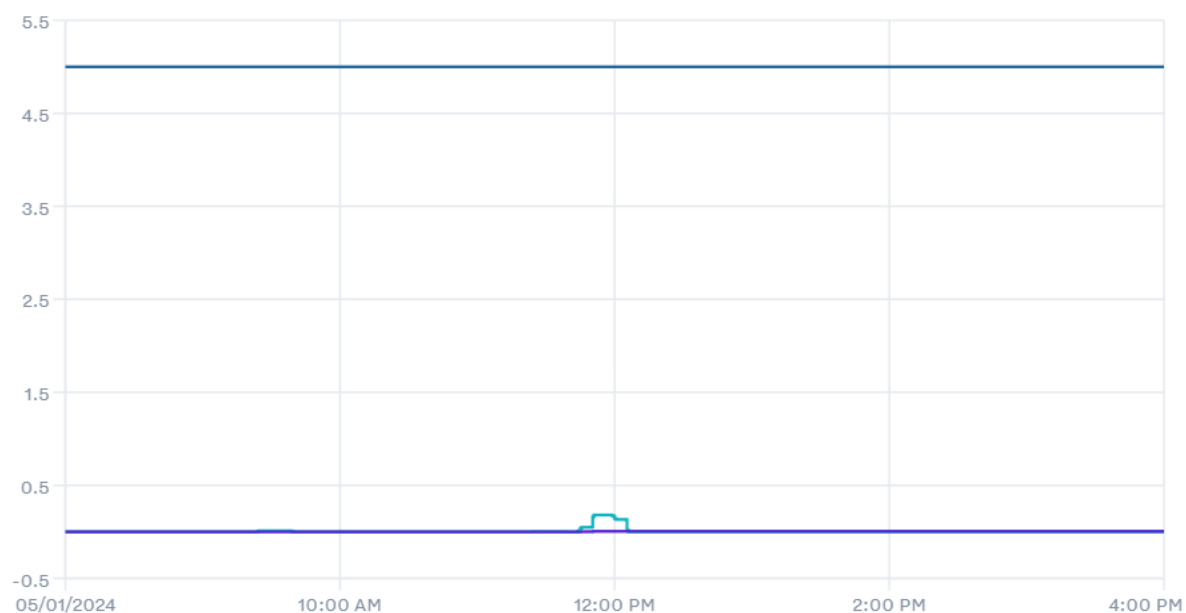

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/1/2024 8:00	5/1/2024 8:10	0.150	0.003	5	0.001
Modem 47822	5/1/2024 8:10	5/1/2024 8:20	0.150	0.004	5	0.001
Modem 47822	5/1/2024 8:20	5/1/2024 8:30	0.150	0.005	5	0.001
Modem 47822	5/1/2024 8:30	5/1/2024 8:40	0.150	0.006	5	0.001
Modem 47822	5/1/2024 8:40	5/1/2024 8:50	0.150	0.007	5	0.001
Modem 47822	5/1/2024 8:50	5/1/2024 9:00	0.150	0.008	5	0.001
Modem 47822	5/1/2024 9:00	5/1/2024 9:10	0.150	0.009	5	0.001
Modem 47822	5/1/2024 9:10	5/1/2024 9:20	0.150	0.01	5	0.001
Modem 47822	5/1/2024 9:20	5/1/2024 9:30	0.150	0.011	5	0.002
Modem 47822	5/1/2024 9:30	5/1/2024 9:40	0.150	0.013	5	0.002
Modem 47822	5/1/2024 9:40	5/1/2024 9:50	0.150	0.014	5	0.002
Modem 47822	5/1/2024 9:50	5/1/2024 10:00	0.150	0.015	5	0.002
Modem 47822	5/1/2024 10:00	5/1/2024 10:10	0.150	0.017	5	0.002
Modem 47822	5/1/2024 10:10	5/1/2024 10:20	0.150	0.018	5	0.002
Modem 47822	5/1/2024 10:20	5/1/2024 10:30	0.150	0.019	5	0.002
Modem 47822	5/1/2024 10:30	5/1/2024 10:40	0.150	0.02	5	0.002
Modem 47822	5/1/2024 10:40	5/1/2024 10:50	0.150	0.022	5	0.002
Modem 47822	5/1/2024 10:50	5/1/2024 11:00	0.150	0.024	5	0.003
Modem 47822	5/1/2024 11:00	5/1/2024 11:10	0.150	0.025	5	0.003
Modem 47822	5/1/2024 11:10	5/1/2024 11:20	0.150	0.026	5	0.003
Modem 47822	5/1/2024 11:20	5/1/2024 11:30	0.150	0.027	5	0.004
Modem 47822	5/1/2024 11:30	5/1/2024 11:40	0.150	0.029	5	0.005
Modem 47822	5/1/2024 11:40	5/1/2024 11:50	0.150	0.03	5	0.005
Modem 47822	5/1/2024 11:50	5/1/2024 12:00	0.150	0.031	5	0.033
Modem 47822	5/1/2024 12:00	5/1/2024 12:10	0.150	0.032	5	0.035
Modem 47822	5/1/2024 12:10	5/1/2024 12:20	0.150	0.034	5	0.043
Modem 47822	5/1/2024 12:20	5/1/2024 12:30	0.150	0.035	5	0.048
Modem 47822	5/1/2024 12:30	5/1/2024 12:40	0.150	0.035	5	0.05
Modem 47822	5/1/2024 12:40	5/1/2024 12:50	0.150	0.036	5	0.05
Modem 47822	5/1/2024 12:50	5/1/2024 13:00	0.150	0.038	5	0.052
Modem 47822	5/1/2024 13:00	5/1/2024 13:10	0.150	0.041	5	0.053
Modem 47822	5/1/2024 13:10	5/1/2024 13:20	0.150	0.043	5	0.053
Modem 47822	5/1/2024 13:20	5/1/2024 13:30	0.150	0.044	5	0.054
Modem 47822	5/1/2024 13:30	5/1/2024 13:40	0.150	0.045	5	0.056
Modem 47822	5/1/2024 13:40	5/1/2024 13:50	0.150	0.046	5	0.056
Modem 47822	5/1/2024 13:50	5/1/2024 14:00	0.150	0.047	5	0.058
Modem 47822	5/1/2024 14:00	5/1/2024 14:10	0.150	0.047	5	0.058
Modem 47822	5/1/2024 14:10	5/1/2024 14:20	0.150	0.051	5	0.059
Modem 47822	5/1/2024 14:20	5/1/2024 14:30	0.150	0.051	5	0.059
Modem 47822	5/1/2024 14:30	5/1/2024 14:40	0.150	0.053	5	0.06
Modem 47822	5/1/2024 14:40	5/1/2024 14:50	0.150	0.054	5	0.06
Modem 47822	5/1/2024 14:50	5/1/2024 15:00	0.150	0.056	5	0.06
Modem 47822	5/1/2024 15:00	5/1/2024 15:10	0.150	0.057	5	0.06
Modem 47822	5/1/2024 15:10	5/1/2024 15:20	0.150	0.059	5	0.061
Modem 47822	5/1/2024 15:20	5/1/2024 15:30	0.150	0.06	5	0.061
Modem 47822	5/1/2024 15:30	5/1/2024 15:40	0.150	0.061	5	0.061
Modem 47822	5/1/2024 15:40	5/1/2024 15:50	0.150	0.061	5	0.061
Modem 47822	5/1/2024 15:50	5/1/2024 16:00	0.150	0.061	5	0.061

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/1/2024 8:00	5/1/2024 8:10	0.150	0.001	5	0
Modem 50062	5/1/2024 8:10	5/1/2024 8:20	0.150	0.001	5	0
Modem 50062	5/1/2024 8:20	5/1/2024 8:30	0.150	0.002	5	0
Modem 50062	5/1/2024 8:30	5/1/2024 8:40	0.150	0.002	5	0
Modem 50062	5/1/2024 8:40	5/1/2024 8:50	0.150	0.002	5	0
Modem 50062	5/1/2024 8:50	5/1/2024 9:00	0.150	0.003	5	0
Modem 50062	5/1/2024 9:00	5/1/2024 9:10	0.150	0.003	5	0
Modem 50062	5/1/2024 9:10	5/1/2024 9:20	0.150	0.004	5	0
Modem 50062	5/1/2024 9:20	5/1/2024 9:30	0.150	0.005	5	0
Modem 50062	5/1/2024 9:30	5/1/2024 9:40	0.150	0.005	5	0
Modem 50062	5/1/2024 9:40	5/1/2024 9:50	0.150	0.006	5	0
Modem 50062	5/1/2024 9:50	5/1/2024 10:00	0.150	0.006	5	0
Modem 50062	5/1/2024 10:00	5/1/2024 10:10	0.150	0.007	5	0
Modem 50062	5/1/2024 10:10	5/1/2024 10:20	0.150	0.008	5	0
Modem 50062	5/1/2024 10:20	5/1/2024 10:30	0.150	0.008	5	0
Modem 50062	5/1/2024 10:30	5/1/2024 10:40	0.150	0.009	5	0
Modem 50062	5/1/2024 10:40	5/1/2024 10:50	0.150	0.009	5	0
Modem 50062	5/1/2024 10:50	5/1/2024 11:00	0.150	0.01	5	0
Modem 50062	5/1/2024 11:00	5/1/2024 11:10	0.150	0.01	5	0
Modem 50062	5/1/2024 11:10	5/1/2024 11:20	0.150	0.011	5	0
Modem 50062	5/1/2024 11:20	5/1/2024 11:30	0.150	0.011	5	0
Modem 50062	5/1/2024 11:30	5/1/2024 11:40	0.150	0.012	5	0
Modem 50062	5/1/2024 11:40	5/1/2024 11:50	0.150	0.013	5	0.001
Modem 50062	5/1/2024 11:50	5/1/2024 12:00	0.150	0.013	5	0.006
Modem 50062	5/1/2024 12:00	5/1/2024 12:10	0.150	0.014	5	0.006
Modem 50062	5/1/2024 12:10	5/1/2024 12:20	0.150	0.014	5	0.006
Modem 50062	5/1/2024 12:20	5/1/2024 12:30	0.150	0.015	5	0.006
Modem 50062	5/1/2024 12:30	5/1/2024 12:40	0.150	0.015	5	0.006
Modem 50062	5/1/2024 12:40	5/1/2024 12:50	0.150	0.016	5	0.006
Modem 50062	5/1/2024 12:50	5/1/2024 13:00	0.150	0.016	5	0.006
Modem 50062	5/1/2024 13:00	5/1/2024 13:10	0.150	0.016	5	0.006
Modem 50062	5/1/2024 13:10	5/1/2024 13:20	0.150	0.017	5	0.006
Modem 50062	5/1/2024 13:20	5/1/2024 13:30	0.150	0.017	5	0.006
Modem 50062	5/1/2024 13:30	5/1/2024 13:40	0.150	0.018	5	0.006
Modem 50062	5/1/2024 13:40	5/1/2024 13:50	0.150	0.018	5	0.006
Modem 50062	5/1/2024 13:50	5/1/2024 14:00	0.150	0.018	5	0.006
Modem 50062	5/1/2024 14:00	5/1/2024 14:10	0.150	0.019	5	0.006
Modem 50062	5/1/2024 14:10	5/1/2024 14:20	0.150	0.019	5	0.006
Modem 50062	5/1/2024 14:20	5/1/2024 14:30	0.150	0.019	5	0.006
Modem 50062	5/1/2024 14:30	5/1/2024 14:40	0.150	0.02	5	0.006
Modem 50062	5/1/2024 14:40	5/1/2024 14:50	0.150	0.02	5	0.006
Modem 50062	5/1/2024 14:50	5/1/2024 15:00	0.150	0.021	5	0.006
Modem 50062	5/1/2024 15:00	5/1/2024 15:10	0.150	0.021	5	0.006
Modem 50062	5/1/2024 15:10	5/1/2024 15:20	0.150	0.021	5	0.006
Modem 50062	5/1/2024 15:20	5/1/2024 15:30	0.150	0.022	5	0.006
Modem 50062	5/1/2024 15:30	5/1/2024 15:40	0.150	0.022	5	0.006
Modem 50062	5/1/2024 15:40	5/1/2024 15:50	0.150	0.022	5	0.006
Modem 50062	5/1/2024 15:50	5/1/2024 16:00	0.150	0.022	5	0.006

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	< 32		32-50		50-70		70-85	X	>85	

BCP Site ID #:C224267

Date: 05/02/2024

Project Name: **3901-3913 8th Avenue – Brooklyn, NY****Consultant:**Matthew Carroll, P.E.
Tenen Environmental**Safety Officer:**Claire Zaccheo
Tenen Environmental**General Contractor:**EarthTech Services, Inc.
222 William Street
Bronx, NY 10461**EarthTech Site Superintendent:**Sam Caller
(347) 907-4053**Work Activities Performed (Since Last Report):**

The contractor completed welding for support of excavation, and; export of 8 truck loads (approximately 160 CY) of material for off-site disposal at the Bayshore Soil Management facility.
Tenen collected six endpoint samples (EP-1 through EP-6) from the 15-ft excavation.

Working In Grid #: A1, A2 and A3**Samples Collected (Since Last Report):** EP-1, EP-2, EP-3, EP-4, EP-5 and EP-6**Air Monitoring (Since Last Report):****Background Conditions**

Upwind: Dust: 0.021 mg/m3 PID: 0.0 ppm
Downwind: Dust: 0.016 mg/m3 PID: 0.0 ppm

Daily TWA

Upwind: Dust: 0.019 mg/m3 PID: 0.0 ppm
Downwind: Dust: 0.041 mg/m3 PID: 0.028 ppm

Problems Encountered: None.**Planned Activities for the Next Day/ Week:**

The contractor will continue excavation and disposing of soil off-site.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832	
(Trucks, CY)	Trucks	Cu. Yds.
Today	8	160
Total	28	560

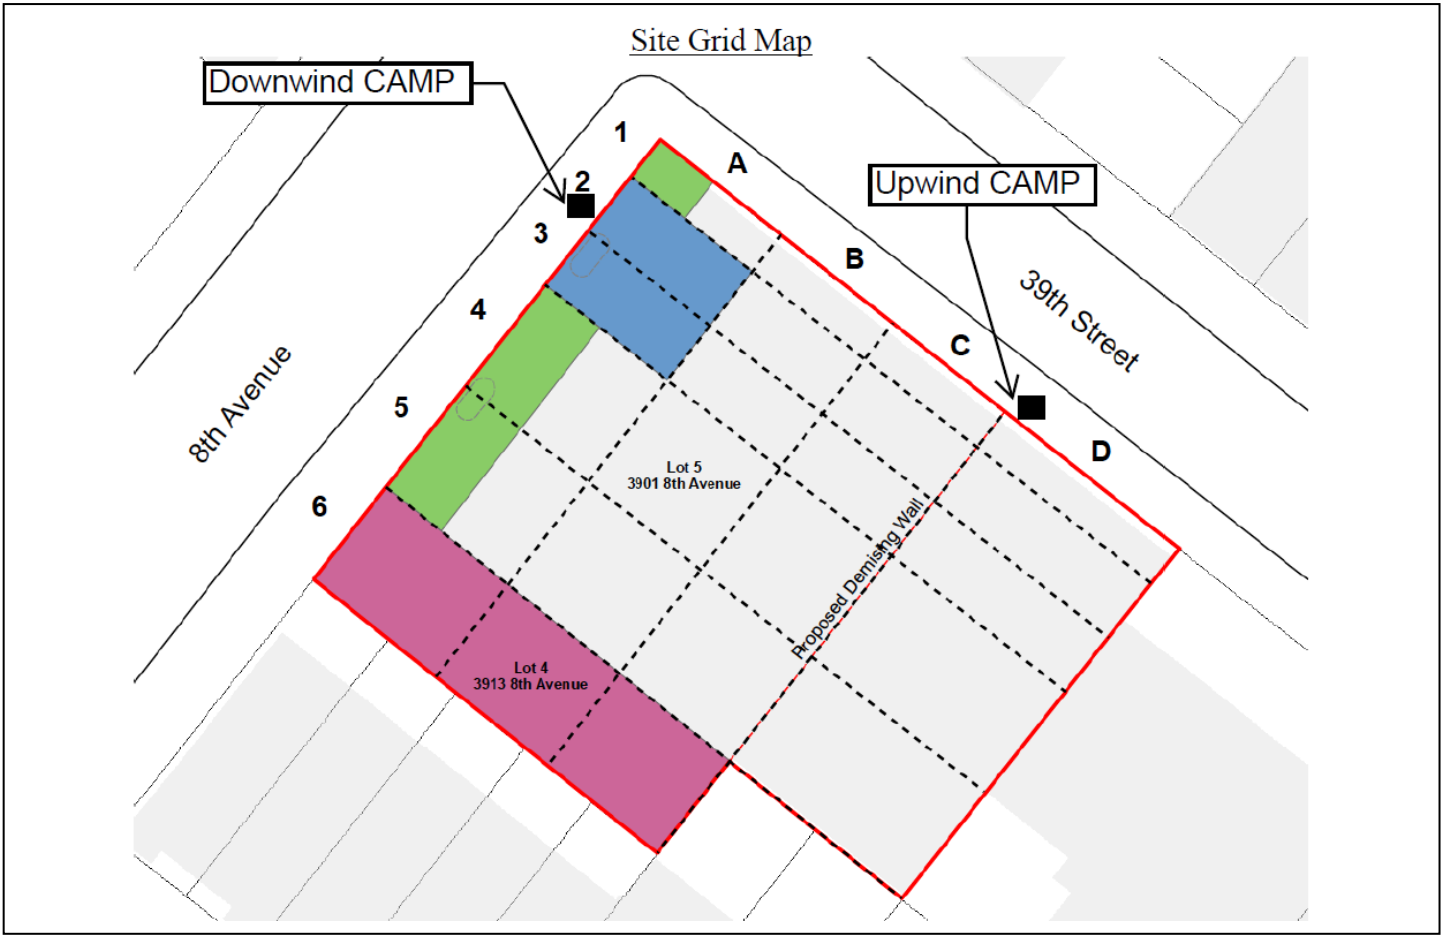


Photo Log

Photo 1 –
View of
cleaned
boulders.



Photo 2 –
View of
endpoint
sample
collection.



Photo 3 –
View of SOE
component
welding.



CAMP Data


DW CAMP

Dust Levels

0.02 mg/m³

0.041 mg/m³

0.15

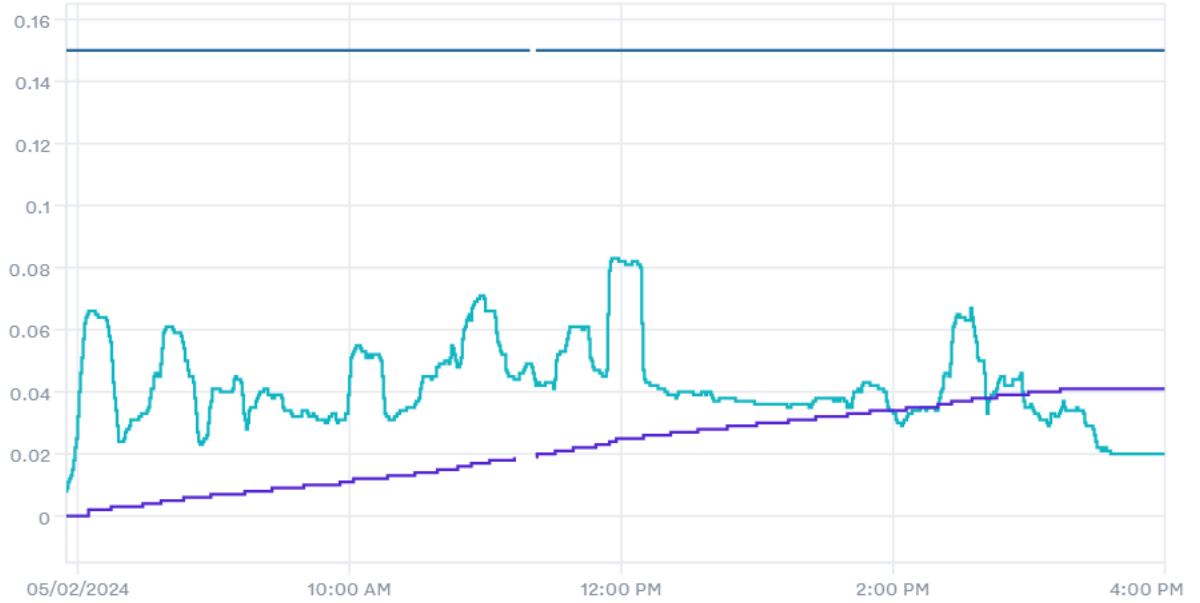


VOC Levels

0 ppm

0.028 ppm

5

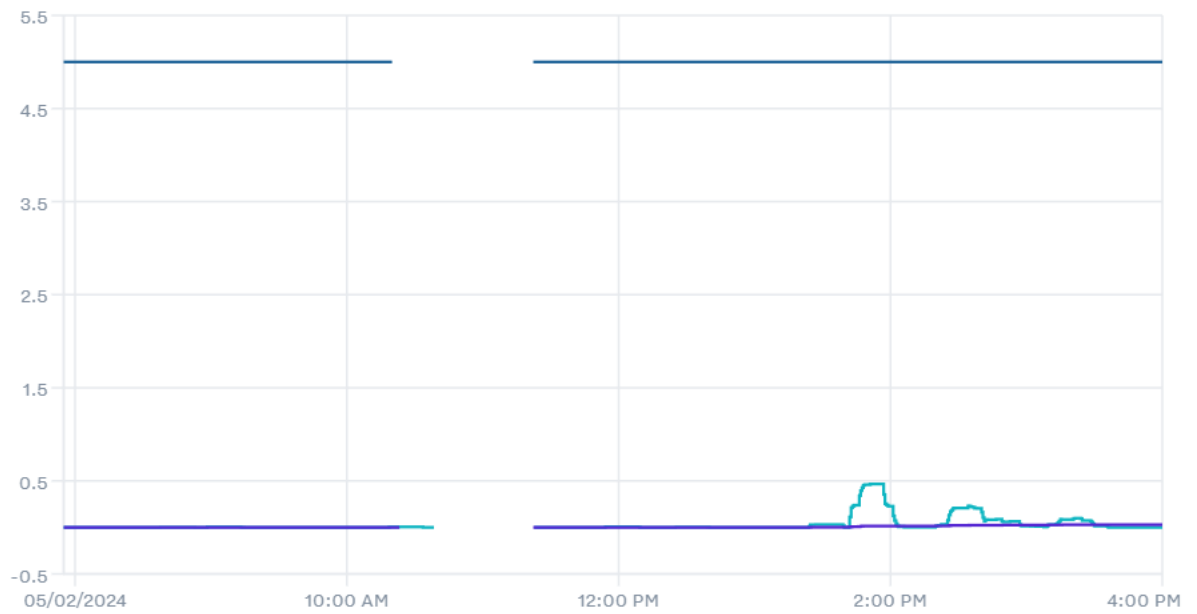


Dust Levels

0.023 mg/m³

0.019 mg/m³

0.15

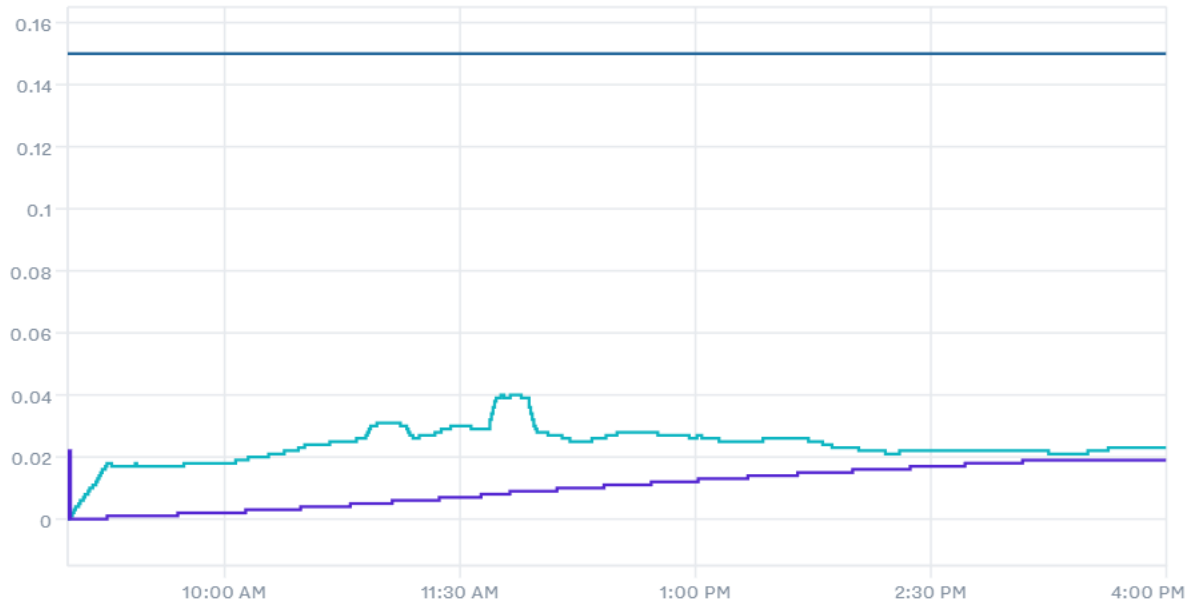


VOC Levels

0 ppm

0 ppm

5

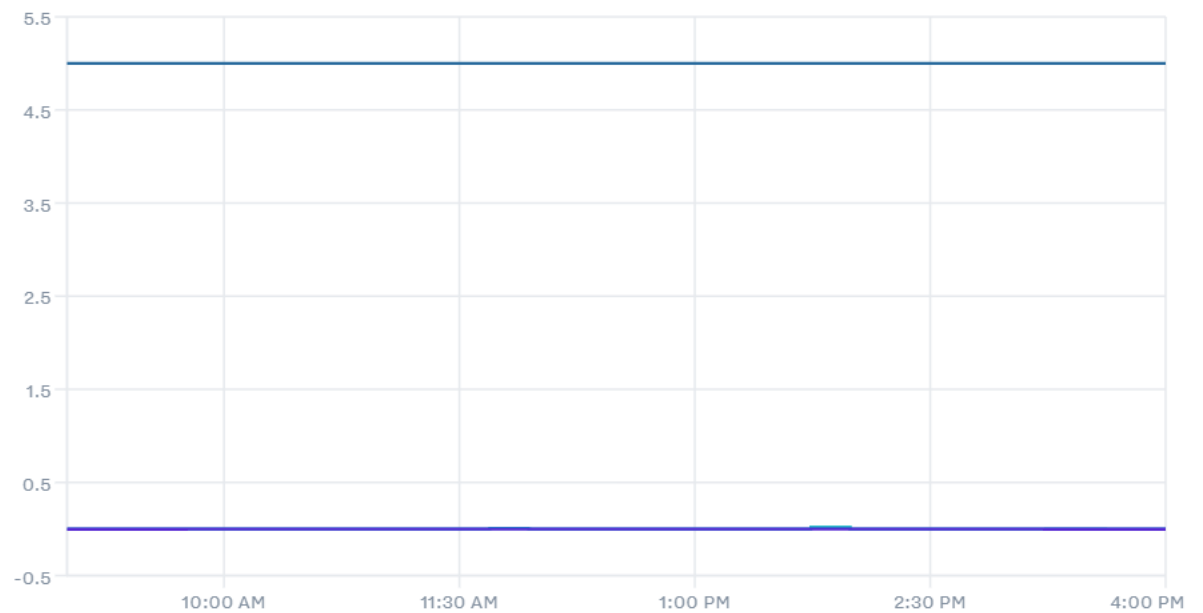

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/2/2024 7:45	5/2/2024 7:55	0.150	0	5	0
Modem 47822	5/2/2024 7:55	5/2/2024 8:05	0.150	0.002	5	0
Modem 47822	5/2/2024 8:05	5/2/2024 8:15	0.150	0.003	5	0
Modem 47822	5/2/2024 8:15	5/2/2024 8:25	0.150	0.003	5	0
Modem 47822	5/2/2024 8:25	5/2/2024 8:35	0.150	0.004	5	0
Modem 47822	5/2/2024 8:35	5/2/2024 8:45	0.150	0.005	5	0
Modem 47822	5/2/2024 8:45	5/2/2024 8:55	0.150	0.006	5	0
Modem 47822	5/2/2024 8:55	5/2/2024 9:05	0.150	0.007	5	0
Modem 47822	5/2/2024 9:05	5/2/2024 9:15	0.150	0.008	5	0
Modem 47822	5/2/2024 9:15	5/2/2024 9:25	0.150	0.008	5	0
Modem 47822	5/2/2024 9:25	5/2/2024 9:35	0.150	0.009	5	0
Modem 47822	5/2/2024 9:35	5/2/2024 9:45	0.150	0.01	5	0
Modem 47822	5/2/2024 9:45	5/2/2024 9:55	0.150	0.01	5	0
Modem 47822	5/2/2024 9:55	5/2/2024 10:05	0.150	0.012	5	0
Modem 47822	5/2/2024 10:05	5/2/2024 10:15	0.150	0.012	5	0
Modem 47822	5/2/2024 10:15	5/2/2024 10:25	0.150	0.013	5	0
Modem 47822	5/2/2024 10:25	5/2/2024 10:35	0.150	0.014	5	0
Modem 47822	5/2/2024 10:35	5/2/2024 10:45	0.150	0.015	5	0
Modem 47822	5/2/2024 10:45	5/2/2024 10:55	0.150	0.017	5	0
Modem 47822	5/2/2024 10:55	5/2/2024 11:05	0.150	0.018	5	0
Modem 47822	5/2/2024 11:05	5/2/2024 11:15	0.150	0.019	5	0
Modem 47822	5/2/2024 11:15	5/2/2024 11:25	0.150	0.02	5	0
Modem 47822	5/2/2024 11:25	5/2/2024 11:35	0.150	0.021	5	0
Modem 47822	5/2/2024 11:35	5/2/2024 11:45	0.150	0.022	5	0
Modem 47822	5/2/2024 11:45	5/2/2024 11:55	0.150	0.024	5	0
Modem 47822	5/2/2024 11:55	5/2/2024 12:05	0.150	0.025	5	0
Modem 47822	5/2/2024 12:05	5/2/2024 12:15	0.150	0.026	5	0
Modem 47822	5/2/2024 12:15	5/2/2024 12:25	0.150	0.027	5	0
Modem 47822	5/2/2024 12:25	5/2/2024 12:35	0.150	0.028	5	0
Modem 47822	5/2/2024 12:35	5/2/2024 12:45	0.150	0.028	5	0
Modem 47822	5/2/2024 12:45	5/2/2024 12:55	0.150	0.029	5	0
Modem 47822	5/2/2024 12:55	5/2/2024 13:05	0.150	0.03	5	0
Modem 47822	5/2/2024 13:05	5/2/2024 13:15	0.150	0.031	5	0
Modem 47822	5/2/2024 13:15	5/2/2024 13:25	0.150	0.031	5	0.001
Modem 47822	5/2/2024 13:25	5/2/2024 13:35	0.150	0.032	5	0.001
Modem 47822	5/2/2024 13:35	5/2/2024 13:45	0.150	0.033	5	0.008
Modem 47822	5/2/2024 13:45	5/2/2024 13:55	0.150	0.034	5	0.015
Modem 47822	5/2/2024 13:55	5/2/2024 14:05	0.150	0.034	5	0.015
Modem 47822	5/2/2024 14:05	5/2/2024 14:15	0.150	0.035	5	0.015
Modem 47822	5/2/2024 14:15	5/2/2024 14:25	0.150	0.036	5	0.016
Modem 47822	5/2/2024 14:25	5/2/2024 14:35	0.150	0.038	5	0.023
Modem 47822	5/2/2024 14:35	5/2/2024 14:45	0.150	0.038	5	0.024
Modem 47822	5/2/2024 14:45	5/2/2024 14:55	0.150	0.039	5	0.025
Modem 47822	5/2/2024 14:55	5/2/2024 15:05	0.150	0.04	5	0.025
Modem 47822	5/2/2024 15:05	5/2/2024 15:15	0.150	0.041	5	0.027
Modem 47822	5/2/2024 15:15	5/2/2024 15:25	0.150	0.041	5	0.028
Modem 47822	5/2/2024 15:25	5/2/2024 15:35	0.150	0.041	5	0.028
Modem 47822	5/2/2024 15:35	5/2/2024 15:45	0.150	0.041	5	0.028
Modem 47822	5/2/2024 15:45	5/2/2024 15:55	0.150	0.041	5	0.028
Modem 47822	5/2/2024 15:55	5/2/2024 16:00	0.150	0.041	5	0.028

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/2/2024 8:05	5/2/2024 8:15	0.150	0	5	0
Modem 50062	5/2/2024 8:15	5/2/2024 8:25	0.150	0	5	0
Modem 50062	5/2/2024 8:25	5/2/2024 8:35	0.150	0	5	0
Modem 50062	5/2/2024 8:35	5/2/2024 8:45	0.150	0	5	0
Modem 50062	5/2/2024 8:45	5/2/2024 8:55	0.150	0	5	0
Modem 50062	5/2/2024 8:55	5/2/2024 9:05	0.150	0	5	0
Modem 50062	5/2/2024 9:05	5/2/2024 9:15	0.150	0	5	0
Modem 50062	5/2/2024 9:15	5/2/2024 9:25	0.150	0.001	5	0
Modem 50062	5/2/2024 9:25	5/2/2024 9:35	0.150	0.001	5	0
Modem 50062	5/2/2024 9:35	5/2/2024 9:45	0.150	0.002	5	0
Modem 50062	5/2/2024 9:45	5/2/2024 9:55	0.150	0.002	5	0
Modem 50062	5/2/2024 9:55	5/2/2024 10:05	0.150	0.002	5	0
Modem 50062	5/2/2024 10:05	5/2/2024 10:15	0.150	0.003	5	0
Modem 50062	5/2/2024 10:15	5/2/2024 10:25	0.150	0.003	5	0
Modem 50062	5/2/2024 10:25	5/2/2024 10:35	0.150	0.004	5	0
Modem 50062	5/2/2024 10:35	5/2/2024 10:45	0.150	0.004	5	0
Modem 50062	5/2/2024 10:45	5/2/2024 10:55	0.150	0.005	5	0
Modem 50062	5/2/2024 10:55	5/2/2024 11:05	0.150	0.006	5	0
Modem 50062	5/2/2024 11:05	5/2/2024 11:15	0.150	0.006	5	0
Modem 50062	5/2/2024 11:15	5/2/2024 11:25	0.150	0.007	5	0
Modem 50062	5/2/2024 11:25	5/2/2024 11:35	0.150	0.007	5	0
Modem 50062	5/2/2024 11:35	5/2/2024 11:45	0.150	0.008	5	0
Modem 50062	5/2/2024 11:45	5/2/2024 11:55	0.150	0.009	5	0
Modem 50062	5/2/2024 11:55	5/2/2024 12:05	0.150	0.009	5	0
Modem 50062	5/2/2024 12:05	5/2/2024 12:15	0.150	0.01	5	0
Modem 50062	5/2/2024 12:15	5/2/2024 12:25	0.150	0.01	5	0
Modem 50062	5/2/2024 12:25	5/2/2024 12:35	0.150	0.011	5	0
Modem 50062	5/2/2024 12:35	5/2/2024 12:45	0.150	0.012	5	0
Modem 50062	5/2/2024 12:45	5/2/2024 12:55	0.150	0.012	5	0
Modem 50062	5/2/2024 12:55	5/2/2024 13:05	0.150	0.013	5	0
Modem 50062	5/2/2024 13:05	5/2/2024 13:15	0.150	0.013	5	0
Modem 50062	5/2/2024 13:15	5/2/2024 13:25	0.150	0.014	5	0
Modem 50062	5/2/2024 13:25	5/2/2024 13:35	0.150	0.014	5	0
Modem 50062	5/2/2024 13:35	5/2/2024 13:45	0.150	0.015	5	0
Modem 50062	5/2/2024 13:45	5/2/2024 13:55	0.150	0.015	5	0
Modem 50062	5/2/2024 13:55	5/2/2024 14:05	0.150	0.016	5	0
Modem 50062	5/2/2024 14:05	5/2/2024 14:15	0.150	0.016	5	0
Modem 50062	5/2/2024 14:15	5/2/2024 14:25	0.150	0.017	5	0
Modem 50062	5/2/2024 14:25	5/2/2024 14:35	0.150	0.017	5	0
Modem 50062	5/2/2024 14:35	5/2/2024 14:45	0.150	0.018	5	0
Modem 50062	5/2/2024 14:45	5/2/2024 14:55	0.150	0.018	5	0
Modem 50062	5/2/2024 14:55	5/2/2024 15:05	0.150	0.018	5	0
Modem 50062	5/2/2024 15:05	5/2/2024 15:15	0.150	0.019	5	0
Modem 50062	5/2/2024 15:15	5/2/2024 15:25	0.150	0.019	5	0
Modem 50062	5/2/2024 15:25	5/2/2024 15:35	0.150	0.019	5	0
Modem 50062	5/2/2024 15:35	5/2/2024 15:45	0.150	0.019	5	0
Modem 50062	5/2/2024 15:45	5/2/2024 15:55	0.150	0.019	5	0
Modem 50062	5/2/2024 15:55	5/2/2024 16:00	0.150	0.019	5	0

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	< 32		32-50		50-70	X	70-85		>85	

BCP Site ID #:C224267

Date: 05/03/2024

Project Name: **3901-3913 8th Avenue – Brooklyn, NY****Consultant:**Matthew Carroll, P.E.
Tenen Environmental**Safety Officer:**Claire Zaccheo
Tenen Environmental**General Contractor:**EarthTech Services, Inc.
222 William Street
Bronx, NY 10461**EarthTech Site Superintendent:**Sam Caller
(347) 907-4053**Work Activities Performed (Since Last Report):**

The contractor completed welding for support of excavation, and; export of 3 truckloads (approximately 60 CY) of material for off-site disposal at the Bayshore Soil Management facility.

Working In Grid #: A1, A2 and A3**Samples Collected (Since Last Report):** None.**Air Monitoring (Since Last Report):****Background Conditions**

Upwind: Dust: 0.047 mg/m3 PID: 0.6 ppm
Downwind: Dust: 0.012 mg/m3 PID: 0.0 ppm

Daily TWA

Upwind: Dust: 0.019 mg/m3 PID: 0.055 ppm
Downwind: Dust: 0.041 mg/m3 PID: 0.108 ppm

Problems Encountered: None.**Planned Activities for the Next Day/ Week:**

The contractor will continue excavation and disposing of soil off-site.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832	
(Trucks, CY)	Trucks	Cu. Yds.
Today	3	60
Total	31	620

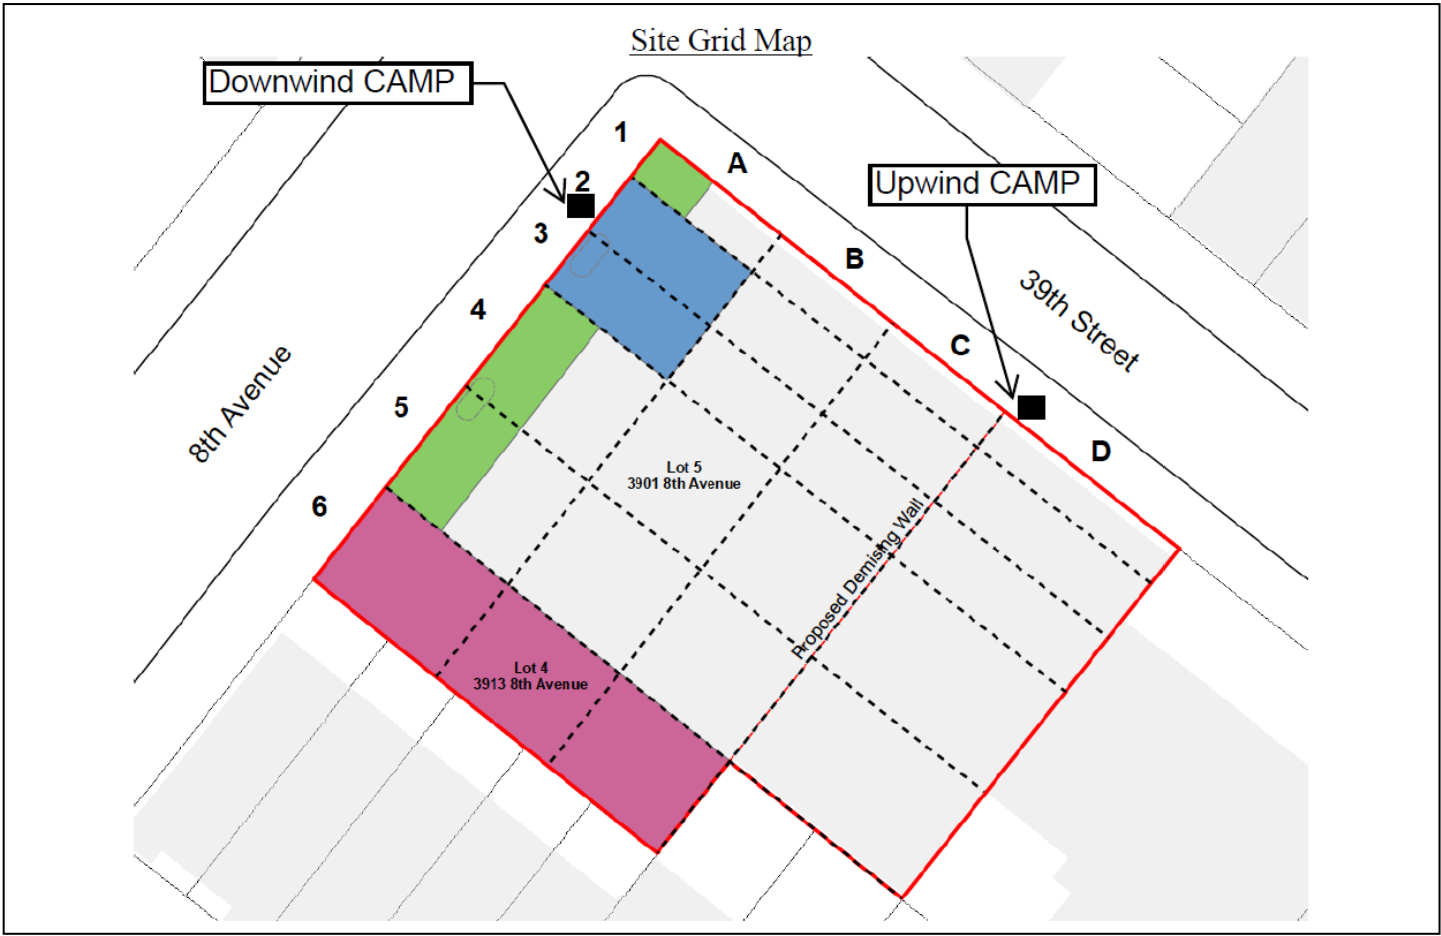


Photo Log


Photo 1 –
View of Site
conditions.



Photo 2 –
View of the
two-foot
excavation.



Photo 3 –
View of
truck loading
for off-site
soil disposal.

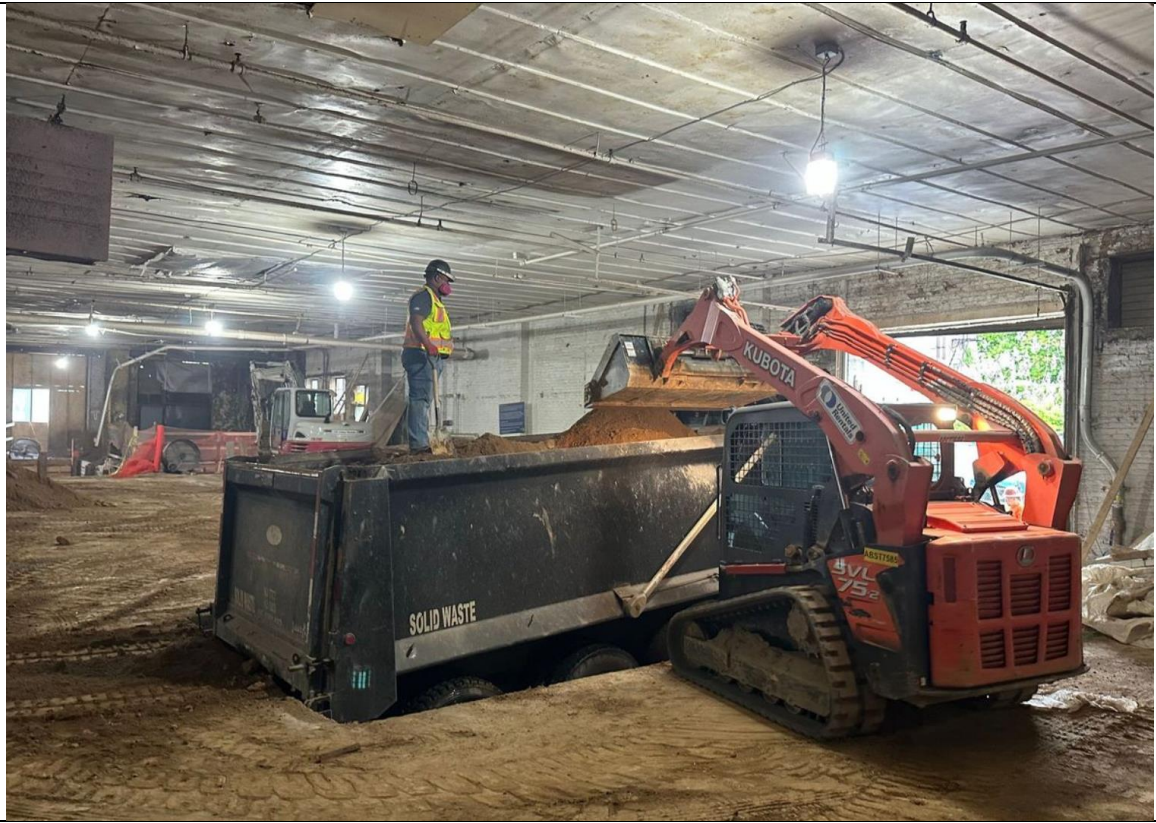

CAMP Data


DW CAMP

Dust Levels

0.135 mg/m³

0.041 mg/m³

0.15

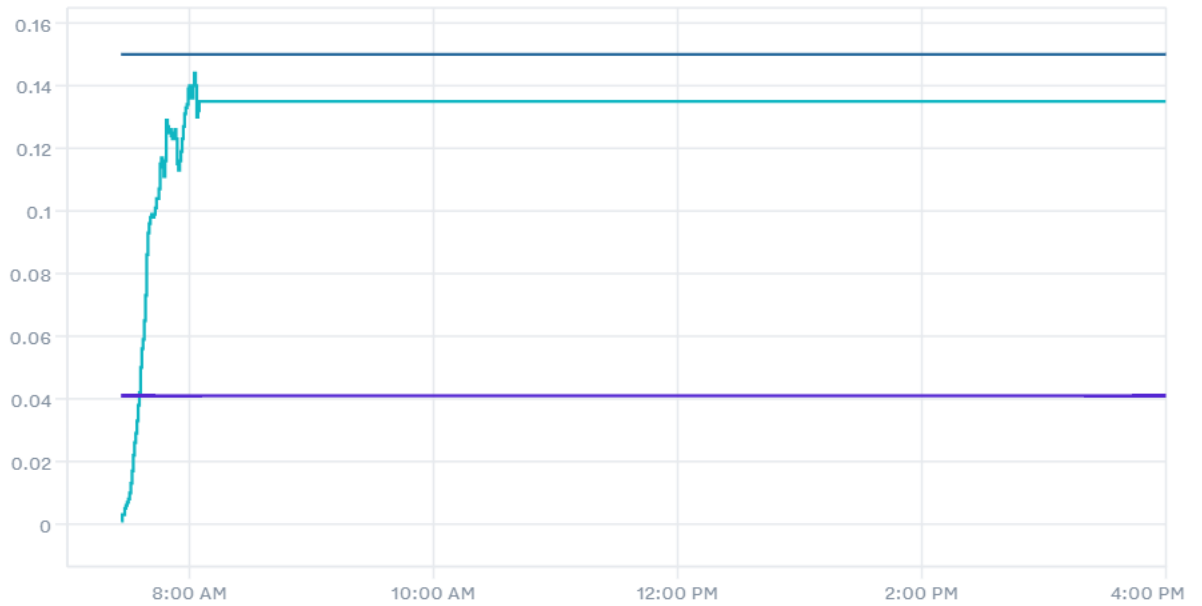


VOC Levels

0.118 ppm

0.108 ppm

5

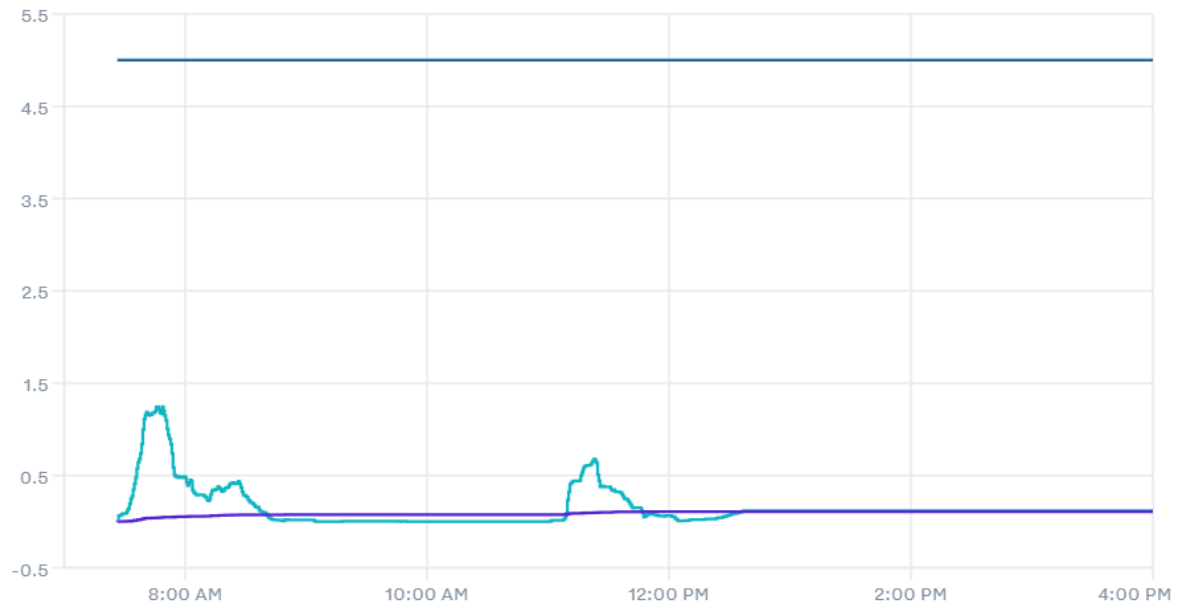


UW CAMP

Dust Levels

0.01 mg/m³

0.019 mg/m³

0.15

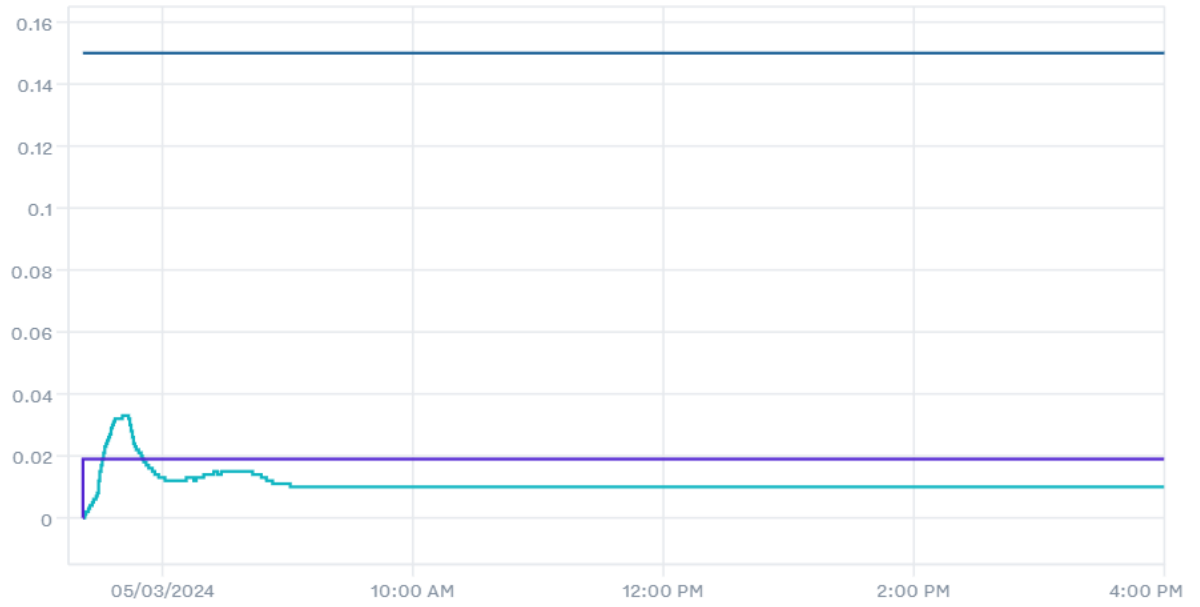


VOC Levels

0 ppm

0.055 ppm

5

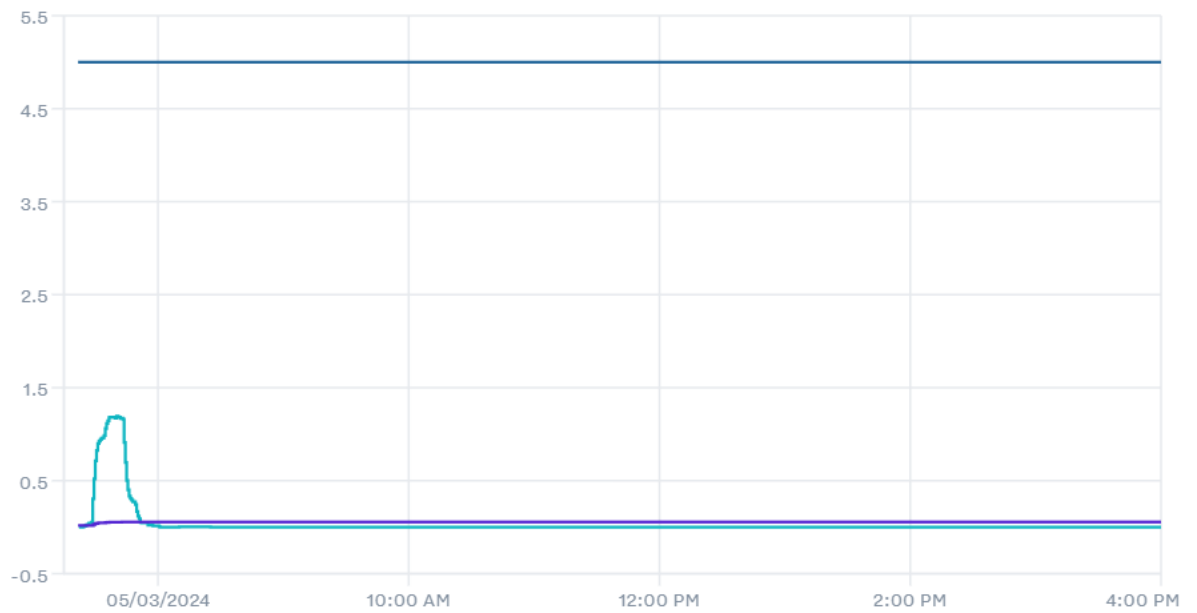

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/3/2024 8:00	5/3/2024 8:10	0.150	0.041	5	0.059
Modem 47822	5/3/2024 8:10	5/3/2024 8:20	0.150	0.041	5	0.069
Modem 47822	5/3/2024 8:20	5/3/2024 8:30	0.150	0.041	5	0.074
Modem 47822	5/3/2024 8:30	5/3/2024 8:40	0.150	0.041	5	0.074
Modem 47822	5/3/2024 8:40	5/3/2024 8:50	0.150	0.041	5	0.075
Modem 47822	5/3/2024 8:50	5/3/2024 9:00	0.150	0.041	5	0.075
Modem 47822	5/3/2024 9:00	5/3/2024 9:10	0.150	0.041	5	0.075
Modem 47822	5/3/2024 9:10	5/3/2024 9:20	0.150	0.041	5	0.075
Modem 47822	5/3/2024 9:20	5/3/2024 9:30	0.150	0.041	5	0.075
Modem 47822	5/3/2024 9:30	5/3/2024 9:40	0.150	0.041	5	0.075
Modem 47822	5/3/2024 9:40	5/3/2024 9:50	0.150	0.041	5	0.075
Modem 47822	5/3/2024 9:50	5/3/2024 10:00	0.150	0.041	5	0.075
Modem 47822	5/3/2024 10:00	5/3/2024 10:10	0.150	0.041	5	0.075
Modem 47822	5/3/2024 10:10	5/3/2024 10:20	0.150	0.041	5	0.075
Modem 47822	5/3/2024 10:20	5/3/2024 10:30	0.150	0.041	5	0.075
Modem 47822	5/3/2024 10:30	5/3/2024 10:40	0.150	0.041	5	0.075
Modem 47822	5/3/2024 10:40	5/3/2024 10:50	0.150	0.041	5	0.075
Modem 47822	5/3/2024 10:50	5/3/2024 11:00	0.150	0.041	5	0.075
Modem 47822	5/3/2024 11:00	5/3/2024 11:10	0.150	0.041	5	0.081
Modem 47822	5/3/2024 11:10	5/3/2024 11:20	0.150	0.041	5	0.095
Modem 47822	5/3/2024 11:20	5/3/2024 11:30	0.150	0.041	5	0.101
Modem 47822	5/3/2024 11:30	5/3/2024 11:40	0.150	0.041	5	0.105
Modem 47822	5/3/2024 11:40	5/3/2024 11:50	0.150	0.041	5	0.107
Modem 47822	5/3/2024 11:50	5/3/2024 12:00	0.150	0.041	5	0.108
Modem 47822	5/3/2024 12:00	5/3/2024 12:10	0.150	0.041	5	0.108
Modem 47822	5/3/2024 12:10	5/3/2024 12:20	0.150	0.041	5	0.108
Modem 47822	5/3/2024 12:20	5/3/2024 12:30	0.150	0.041	5	0.108
Modem 47822	5/3/2024 12:30	5/3/2024 12:40	0.150	0.041	5	0.108
Modem 47822	5/3/2024 12:40	5/3/2024 12:50	0.150	0.041	5	0.108
Modem 47822	5/3/2024 12:50	5/3/2024 13:00	0.150	0.041	5	0.108
Modem 47822	5/3/2024 13:00	5/3/2024 13:10	0.150	0.041	5	0.108
Modem 47822	5/3/2024 13:10	5/3/2024 13:20	0.150	0.041	5	0.108
Modem 47822	5/3/2024 13:20	5/3/2024 13:30	0.150	0.041	5	0.108
Modem 47822	5/3/2024 13:30	5/3/2024 13:40	0.150	0.041	5	0.108
Modem 47822	5/3/2024 13:40	5/3/2024 13:50	0.150	0.041	5	0.108
Modem 47822	5/3/2024 13:50	5/3/2024 14:00	0.150	0.041	5	0.108
Modem 47822	5/3/2024 14:00	5/3/2024 14:10	0.150	0.041	5	0.108
Modem 47822	5/3/2024 14:10	5/3/2024 14:20	0.150	0.041	5	0.108
Modem 47822	5/3/2024 14:20	5/3/2024 14:30	0.150	0.041	5	0.108
Modem 47822	5/3/2024 14:30	5/3/2024 14:40	0.150	0.041	5	0.108
Modem 47822	5/3/2024 14:40	5/3/2024 14:50	0.150	0.041	5	0.108
Modem 47822	5/3/2024 14:50	5/3/2024 15:00	0.150	0.041	5	0.108
Modem 47822	5/3/2024 15:00	5/3/2024 15:10	0.150	0.041	5	0.108
Modem 47822	5/3/2024 15:10	5/3/2024 15:20	0.150	0.041	5	0.108
Modem 47822	5/3/2024 15:20	5/3/2024 15:30	0.150	0.041	5	0.108
Modem 47822	5/3/2024 15:30	5/3/2024 15:40	0.150	0.041	5	0.108
Modem 47822	5/3/2024 15:40	5/3/2024 15:50	0.150	0.041	5	0.108
Modem 47822	5/3/2024 15:50	5/3/2024 16:00	0.150	0.041	5	0.108

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/3/2024 8:00	5/3/2024 8:10	0.150	0.018	5	0.054
Modem 50062	5/3/2024 8:10	5/3/2024 8:20	0.150	0.018	5	0.054
Modem 50062	5/3/2024 8:20	5/3/2024 8:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 8:30	5/3/2024 8:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 8:40	5/3/2024 8:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 8:50	5/3/2024 9:00	0.150	0.019	5	0.055
Modem 50062	5/3/2024 9:00	5/3/2024 9:10	0.150	0.019	5	0.055
Modem 50062	5/3/2024 9:10	5/3/2024 9:20	0.150	0.019	5	0.055
Modem 50062	5/3/2024 9:20	5/3/2024 9:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 9:30	5/3/2024 9:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 9:40	5/3/2024 9:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 9:50	5/3/2024 10:00	0.150	0.019	5	0.055
Modem 50062	5/3/2024 10:00	5/3/2024 10:10	0.150	0.019	5	0.055
Modem 50062	5/3/2024 10:10	5/3/2024 10:20	0.150	0.019	5	0.055
Modem 50062	5/3/2024 10:20	5/3/2024 10:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 10:30	5/3/2024 10:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 10:40	5/3/2024 10:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 10:50	5/3/2024 11:00	0.150	0.019	5	0.055
Modem 50062	5/3/2024 11:00	5/3/2024 11:10	0.150	0.019	5	0.055
Modem 50062	5/3/2024 11:10	5/3/2024 11:20	0.150	0.019	5	0.055
Modem 50062	5/3/2024 11:20	5/3/2024 11:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 11:30	5/3/2024 11:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 11:40	5/3/2024 11:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 11:50	5/3/2024 12:00	0.150	0.019	5	0.055
Modem 50062	5/3/2024 12:00	5/3/2024 12:10	0.150	0.019	5	0.055
Modem 50062	5/3/2024 12:10	5/3/2024 12:20	0.150	0.019	5	0.055
Modem 50062	5/3/2024 12:20	5/3/2024 12:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 12:30	5/3/2024 12:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 12:40	5/3/2024 12:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 12:50	5/3/2024 13:00	0.150	0.019	5	0.055
Modem 50062	5/3/2024 13:00	5/3/2024 13:10	0.150	0.019	5	0.055
Modem 50062	5/3/2024 13:10	5/3/2024 13:20	0.150	0.019	5	0.055
Modem 50062	5/3/2024 13:20	5/3/2024 13:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 13:30	5/3/2024 13:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 13:40	5/3/2024 13:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 13:50	5/3/2024 14:00	0.150	0.019	5	0.055
Modem 50062	5/3/2024 14:00	5/3/2024 14:10	0.150	0.019	5	0.055
Modem 50062	5/3/2024 14:10	5/3/2024 14:20	0.150	0.019	5	0.055
Modem 50062	5/3/2024 14:20	5/3/2024 14:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 14:30	5/3/2024 14:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 14:40	5/3/2024 14:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 14:50	5/3/2024 15:00	0.150	0.019	5	0.055
Modem 50062	5/3/2024 15:00	5/3/2024 15:10	0.150	0.019	5	0.055
Modem 50062	5/3/2024 15:10	5/3/2024 15:20	0.150	0.019	5	0.055
Modem 50062	5/3/2024 15:20	5/3/2024 15:30	0.150	0.019	5	0.055
Modem 50062	5/3/2024 15:30	5/3/2024 15:40	0.150	0.019	5	0.055
Modem 50062	5/3/2024 15:40	5/3/2024 15:50	0.150	0.019	5	0.055
Modem 50062	5/3/2024 15:50	5/3/2024 16:00	0.150	0.019	5	0.055

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	< 32		32-50		50-70	X	70-85		>85	

BCP Site ID #:C224267

Date: 05/06/2024

Project Name: **3901-3913 8th Avenue – Brooklyn, NY****Consultant:**Matthew Carroll, P.E.
Tenen Environmental**Safety Officer:**Claire Zaccheo
Tenen Environmental**General Contractor:**EarthTech Services, Inc.
222 William Street
Bronx, NY 10461**EarthTech Site Superintendent:**Sam Caller
(347) 907-4053**Work Activities Performed (Since Last Report):**

The contractor completed welding for support of excavation, and; export of 2 truckloads (approximately 40 CY) of material for off-site disposal at the Bayshore Soil Management facility.
Collected two endpoint samples (EP-7 and EP-8) from the 2-ft remedial excavation.
NYSDEC PM Erick Bower on-site for site visit.

Working In Grid #: A1, A2 and A3**Samples Collected (Since Last Report): EP-7 and EP-8****Air Monitoring (Since Last Report):****Background Conditions**

Upwind: Dust: 0.110 mg/m3 PID: 0.9 ppm
Downwind: Dust: 0.017 mg/m3 PID: 0.0 ppm

Daily TWA

Upwind: Dust: 0.041 mg/m3 PID: 0.036 ppm
Downwind: Dust: 0.132 mg/m3 PID: 0.178 ppm

Problems Encountered: Elevated downwind particulate readings were caused by the use of welding gas in the proximity of the CAMP station.

Planned Activities for the Next Day/ Week:

The contractor will continue excavation and disposing of soil off-site.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832	
(Trucks, CY)	Trucks	Cu. Yds.
Today	2	40
Total	33	660

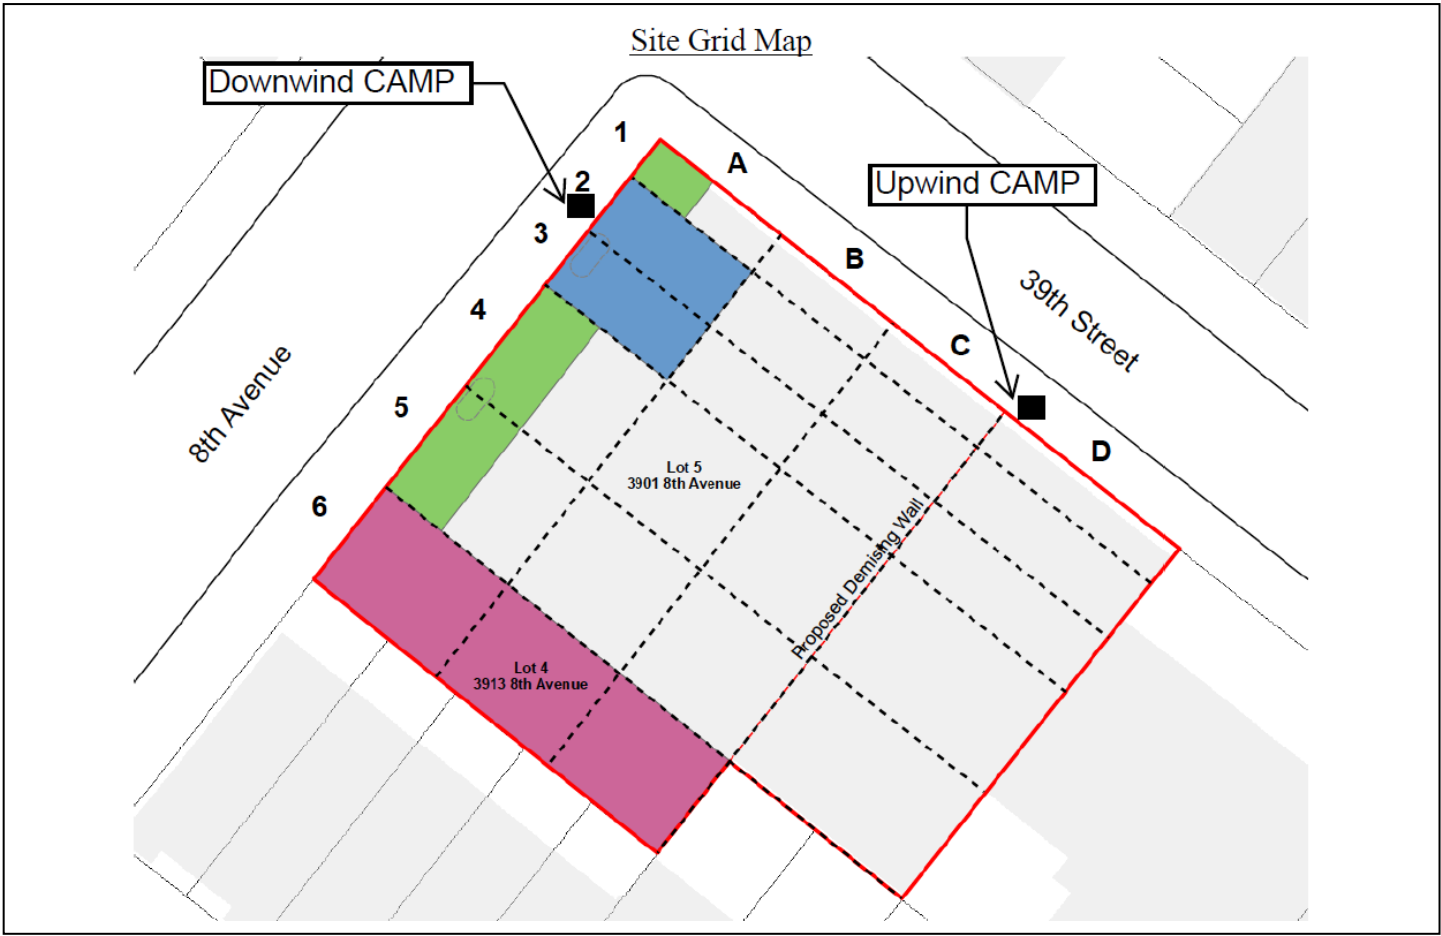


Photo Log

Photo 1 –
View of
truck loading
for off-site
soil disposal.



Photo 2 –
View of the
excavation.



Photo 3 –
View of the
excavation.



CAMP Data


DW CAMP

Dust Levels

0.188 mg/m³

0.132 mg/m³

0.15

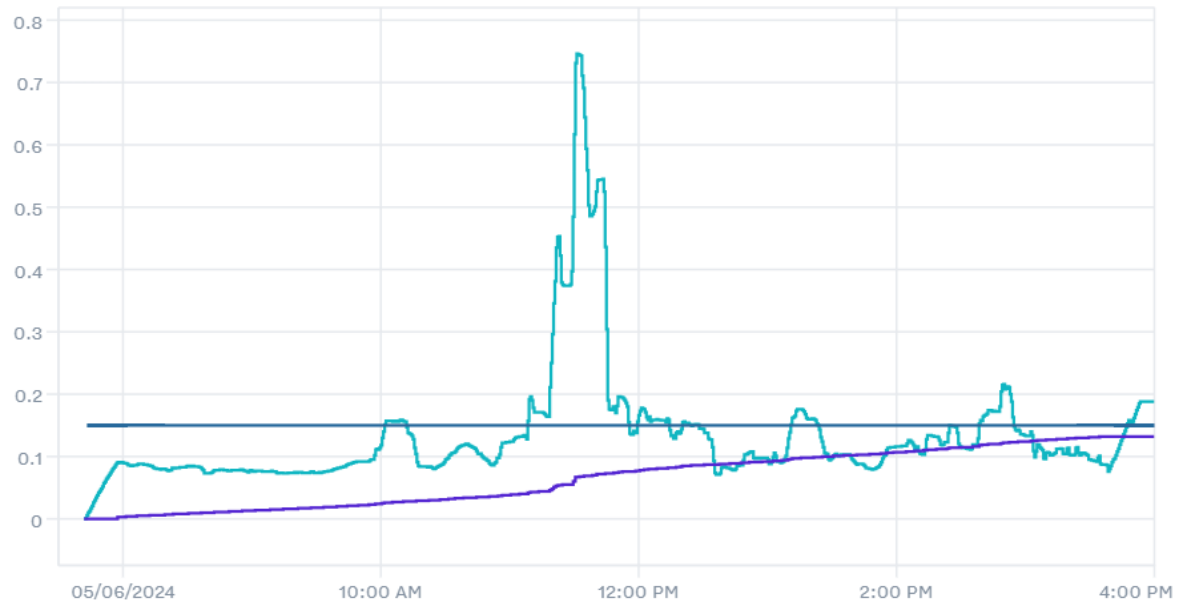


VOC Levels

0.173 ppm

0.178 ppm

5

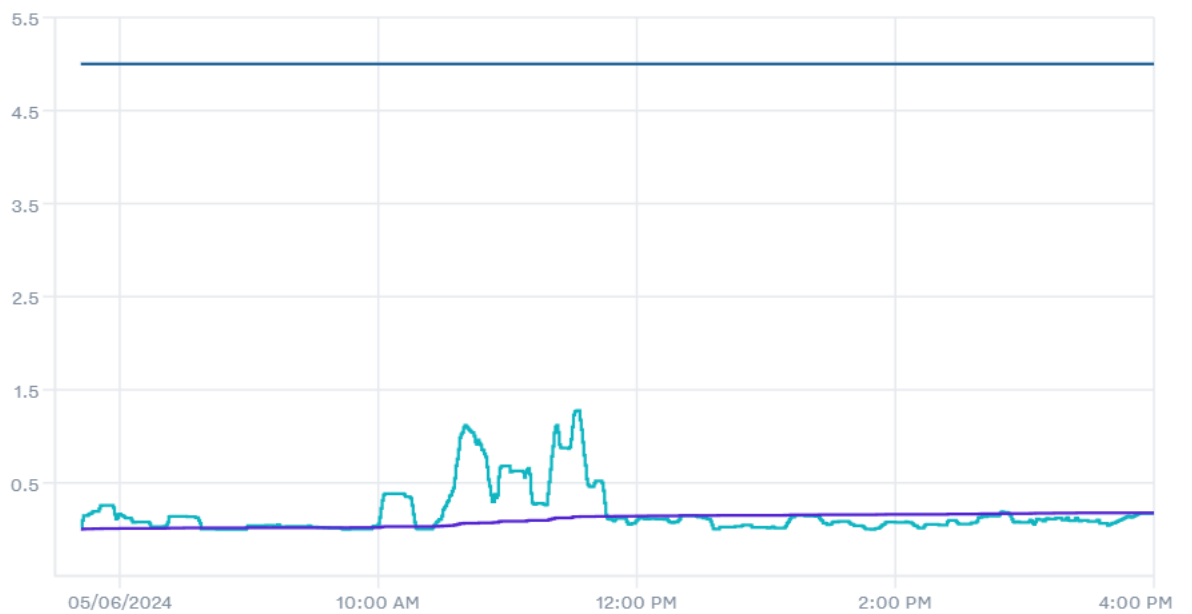


UW CAMP

Dust Levels

0.033 mg/m³

0.041 mg/m³

0.15

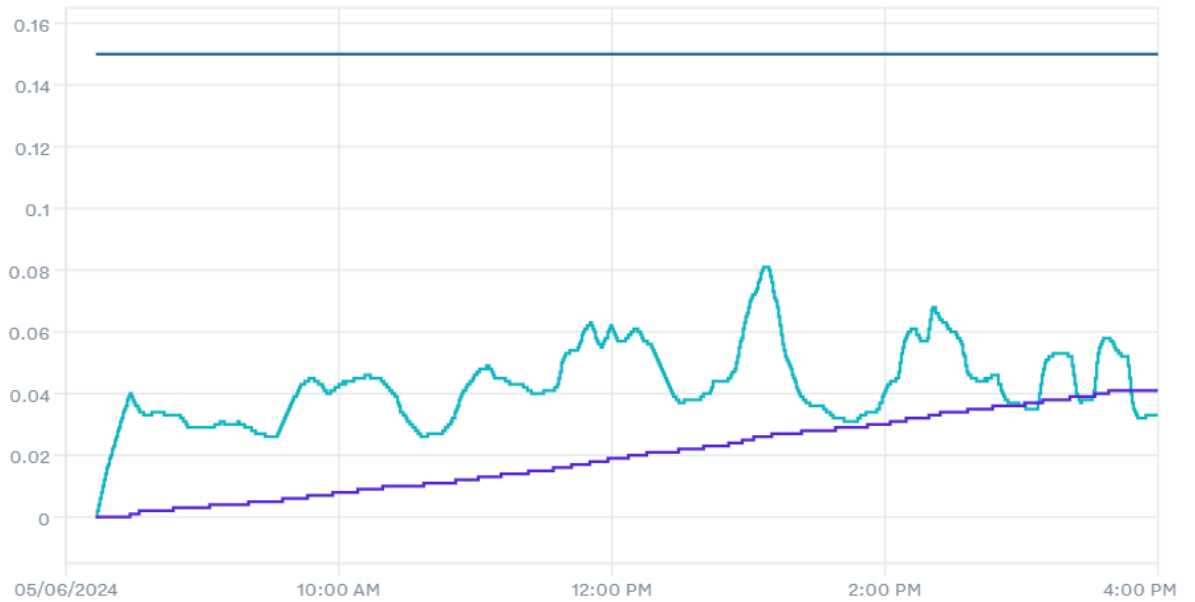


VOC Levels

0 ppm

0.036 ppm

5

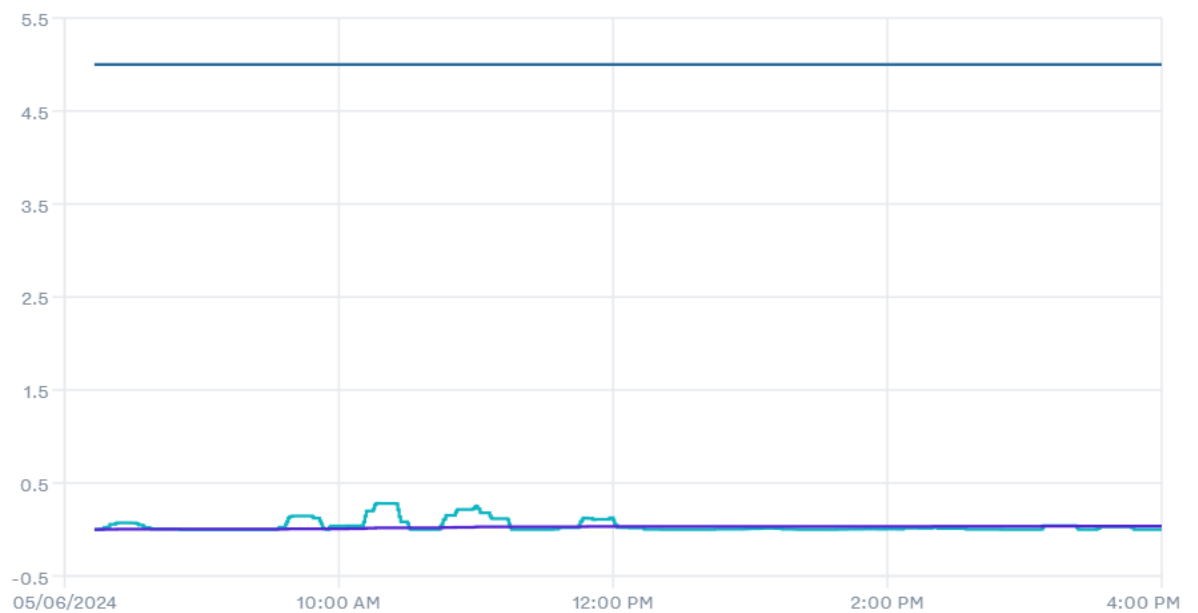

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/6/2024 8:00	5/6/2024 8:10	0.150	0.005	5	0.011
Modem 47822	5/6/2024 8:10	5/6/2024 8:20	0.150	0.007	5	0.011
Modem 47822	5/6/2024 8:20	5/6/2024 8:30	0.150	0.008	5	0.016
Modem 47822	5/6/2024 8:30	5/6/2024 8:40	0.150	0.01	5	0.016
Modem 47822	5/6/2024 8:40	5/6/2024 8:50	0.150	0.012	5	0.016
Modem 47822	5/6/2024 8:50	5/6/2024 9:00	0.150	0.013	5	0.017
Modem 47822	5/6/2024 9:00	5/6/2024 9:10	0.150	0.015	5	0.017
Modem 47822	5/6/2024 9:10	5/6/2024 9:20	0.150	0.016	5	0.018
Modem 47822	5/6/2024 9:20	5/6/2024 9:30	0.150	0.018	5	0.018
Modem 47822	5/6/2024 9:30	5/6/2024 9:40	0.150	0.02	5	0.018
Modem 47822	5/6/2024 9:40	5/6/2024 9:50	0.150	0.022	5	0.019
Modem 47822	5/6/2024 9:50	5/6/2024 10:00	0.150	0.024	5	0.02
Modem 47822	5/6/2024 10:00	5/6/2024 10:10	0.150	0.027	5	0.031
Modem 47822	5/6/2024 10:10	5/6/2024 10:20	0.150	0.029	5	0.031
Modem 47822	5/6/2024 10:20	5/6/2024 10:30	0.150	0.031	5	0.037
Modem 47822	5/6/2024 10:30	5/6/2024 10:40	0.150	0.034	5	0.066
Modem 47822	5/6/2024 10:40	5/6/2024 10:50	0.150	0.035	5	0.069
Modem 47822	5/6/2024 10:50	5/6/2024 11:00	0.150	0.038	5	0.088
Modem 47822	5/6/2024 11:00	5/6/2024 11:10	0.150	0.043	5	0.096
Modem 47822	5/6/2024 11:10	5/6/2024 11:20	0.150	0.048	5	0.109
Modem 47822	5/6/2024 11:20	5/6/2024 11:30	0.150	0.06	5	0.13
Modem 47822	5/6/2024 11:30	5/6/2024 11:40	0.150	0.07	5	0.138
Modem 47822	5/6/2024 11:40	5/6/2024 11:50	0.150	0.074	5	0.141
Modem 47822	5/6/2024 11:50	5/6/2024 12:00	0.150	0.077	5	0.143
Modem 47822	5/6/2024 12:00	5/6/2024 12:10	0.150	0.081	5	0.145
Modem 47822	5/6/2024 12:10	5/6/2024 12:20	0.150	0.084	5	0.148
Modem 47822	5/6/2024 12:20	5/6/2024 12:30	0.150	0.086	5	0.149
Modem 47822	5/6/2024 12:30	5/6/2024 12:40	0.150	0.088	5	0.15
Modem 47822	5/6/2024 12:40	5/6/2024 12:50	0.150	0.09	5	0.151
Modem 47822	5/6/2024 12:50	5/6/2024 13:00	0.150	0.092	5	0.151
Modem 47822	5/6/2024 13:00	5/6/2024 13:10	0.150	0.095	5	0.153
Modem 47822	5/6/2024 13:10	5/6/2024 13:20	0.150	0.098	5	0.156
Modem 47822	5/6/2024 13:20	5/6/2024 13:30	0.150	0.1	5	0.157
Modem 47822	5/6/2024 13:30	5/6/2024 13:40	0.150	0.102	5	0.158
Modem 47822	5/6/2024 13:40	5/6/2024 13:50	0.150	0.104	5	0.158
Modem 47822	5/6/2024 13:50	5/6/2024 14:00	0.150	0.107	5	0.161
Modem 47822	5/6/2024 14:00	5/6/2024 14:10	0.150	0.109	5	0.161
Modem 47822	5/6/2024 14:10	5/6/2024 14:20	0.150	0.112	5	0.162
Modem 47822	5/6/2024 14:20	5/6/2024 14:30	0.150	0.115	5	0.164
Modem 47822	5/6/2024 14:30	5/6/2024 14:40	0.150	0.119	5	0.168
Modem 47822	5/6/2024 14:40	5/6/2024 14:50	0.150	0.122	5	0.17
Modem 47822	5/6/2024 14:50	5/6/2024 15:00	0.150	0.124	5	0.171
Modem 47822	5/6/2024 15:00	5/6/2024 15:10	0.150	0.127	5	0.174
Modem 47822	5/6/2024 15:10	5/6/2024 15:20	0.150	0.129	5	0.176
Modem 47822	5/6/2024 15:20	5/6/2024 15:30	0.150	0.131	5	0.178
Modem 47822	5/6/2024 15:30	5/6/2024 15:40	0.150	0.132	5	0.178
Modem 47822	5/6/2024 15:40	5/6/2024 15:50	0.150	0.132	5	0.178
Modem 47822	5/6/2024 15:50	5/6/2024 16:00	0.150	0.132	5	0.178

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/6/2024 8:10	5/6/2024 8:20	0.150	0	5	0.002
Modem 50062	5/6/2024 8:20	5/6/2024 8:30	0.150	0.001	5	0.003
Modem 50062	5/6/2024 8:30	5/6/2024 8:40	0.150	0.002	5	0.003
Modem 50062	5/6/2024 8:40	5/6/2024 8:50	0.150	0.003	5	0.003
Modem 50062	5/6/2024 8:50	5/6/2024 9:00	0.150	0.003	5	0.003
Modem 50062	5/6/2024 9:00	5/6/2024 9:10	0.150	0.004	5	0.003
Modem 50062	5/6/2024 9:10	5/6/2024 9:20	0.150	0.004	5	0.003
Modem 50062	5/6/2024 9:20	5/6/2024 9:30	0.150	0.005	5	0.003
Modem 50062	5/6/2024 9:30	5/6/2024 9:40	0.150	0.006	5	0.007
Modem 50062	5/6/2024 9:40	5/6/2024 9:50	0.150	0.007	5	0.007
Modem 50062	5/6/2024 9:50	5/6/2024 10:00	0.150	0.008	5	0.008
Modem 50062	5/6/2024 10:00	5/6/2024 10:10	0.150	0.009	5	0.009
Modem 50062	5/6/2024 10:10	5/6/2024 10:20	0.150	0.01	5	0.017
Modem 50062	5/6/2024 10:20	5/6/2024 10:30	0.150	0.01	5	0.017
Modem 50062	5/6/2024 10:30	5/6/2024 10:40	0.150	0.011	5	0.017
Modem 50062	5/6/2024 10:40	5/6/2024 10:50	0.150	0.011	5	0.022
Modem 50062	5/6/2024 10:50	5/6/2024 11:00	0.150	0.012	5	0.027
Modem 50062	5/6/2024 11:00	5/6/2024 11:10	0.150	0.013	5	0.028
Modem 50062	5/6/2024 11:10	5/6/2024 11:20	0.150	0.014	5	0.028
Modem 50062	5/6/2024 11:20	5/6/2024 11:30	0.150	0.015	5	0.028
Modem 50062	5/6/2024 11:30	5/6/2024 11:40	0.150	0.016	5	0.028
Modem 50062	5/6/2024 11:40	5/6/2024 11:50	0.150	0.017	5	0.032
Modem 50062	5/6/2024 11:50	5/6/2024 12:00	0.150	0.019	5	0.032
Modem 50062	5/6/2024 12:00	5/6/2024 12:10	0.150	0.02	5	0.032
Modem 50062	5/6/2024 12:10	5/6/2024 12:20	0.150	0.021	5	0.032
Modem 50062	5/6/2024 12:20	5/6/2024 12:30	0.150	0.022	5	0.032
Modem 50062	5/6/2024 12:30	5/6/2024 12:40	0.150	0.022	5	0.032
Modem 50062	5/6/2024 12:40	5/6/2024 12:50	0.150	0.023	5	0.032
Modem 50062	5/6/2024 12:50	5/6/2024 13:00	0.150	0.025	5	0.033
Modem 50062	5/6/2024 13:00	5/6/2024 13:10	0.150	0.026	5	0.033
Modem 50062	5/6/2024 13:10	5/6/2024 13:20	0.150	0.027	5	0.033
Modem 50062	5/6/2024 13:20	5/6/2024 13:30	0.150	0.028	5	0.033
Modem 50062	5/6/2024 13:30	5/6/2024 13:40	0.150	0.029	5	0.033
Modem 50062	5/6/2024 13:40	5/6/2024 13:50	0.150	0.029	5	0.033
Modem 50062	5/6/2024 13:50	5/6/2024 14:00	0.150	0.03	5	0.033
Modem 50062	5/6/2024 14:00	5/6/2024 14:10	0.150	0.032	5	0.033
Modem 50062	5/6/2024 14:10	5/6/2024 14:20	0.150	0.033	5	0.034
Modem 50062	5/6/2024 14:20	5/6/2024 14:30	0.150	0.034	5	0.034
Modem 50062	5/6/2024 14:30	5/6/2024 14:40	0.150	0.035	5	0.034
Modem 50062	5/6/2024 14:40	5/6/2024 14:50	0.150	0.036	5	0.034
Modem 50062	5/6/2024 14:50	5/6/2024 15:00	0.150	0.036	5	0.034
Modem 50062	5/6/2024 15:00	5/6/2024 15:10	0.150	0.038	5	0.035
Modem 50062	5/6/2024 15:10	5/6/2024 15:20	0.150	0.038	5	0.035
Modem 50062	5/6/2024 15:20	5/6/2024 15:30	0.150	0.039	5	0.035
Modem 50062	5/6/2024 15:30	5/6/2024 15:40	0.150	0.041	5	0.036
Modem 50062	5/6/2024 15:40	5/6/2024 15:50	0.150	0.041	5	0.036
Modem 50062	5/6/2024 15:50	5/6/2024 16:00	0.150	0.041	5	0.036

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	< 32		32-50		50-70		70-85	X	>85	

BCP Site ID #:C224267

Date: 05/07/2024

Project Name: 3901-3913 8th Avenue – Brooklyn, NY

Consultant:

Matthew Carroll, P.E.
Tenen Environmental

Safety Officer:

Claire Zaccheo
Tenen Environmental

General Contractor:

EarthTech Services, Inc.
222 William Street
Bronx, NY 10461

EarthTech Site Superintendent:

Sam Caller
(347) 907-4053

Work Activities Performed (Since Last Report):

The contractor completed welding for support of excavation and concrete demolition.
The contractor did not complete soil movement during the workday.

Working In Grid #: A1, A2 and A3

Samples Collected (Since Last Report): None

Air Monitoring (Since Last Report):**Background Conditions**

Upwind: Dust: 0.101 mg/m3 PID: 0.8 ppm
Downwind: Dust: 0.047 mg/m3 PID: 0.1 ppm

Daily TWA

Upwind: Dust: 0.003 mg/m3 PID: 0.010 ppm*
Downwind: Dust: 0.064 mg/m3 PID: 0.018 ppm

Problems Encountered: *The upwind Dustrak experienced telemetry issues. The field personnel recorded the TWA for particulates from the Dustrak, which is depicted above.

Planned Activities for the Next Day/ Week:

The contractor will be exporting soil off-site.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832	
(Trucks, CY)	Trucks	Cu. Yds.
Today	0	0
Total	33	660

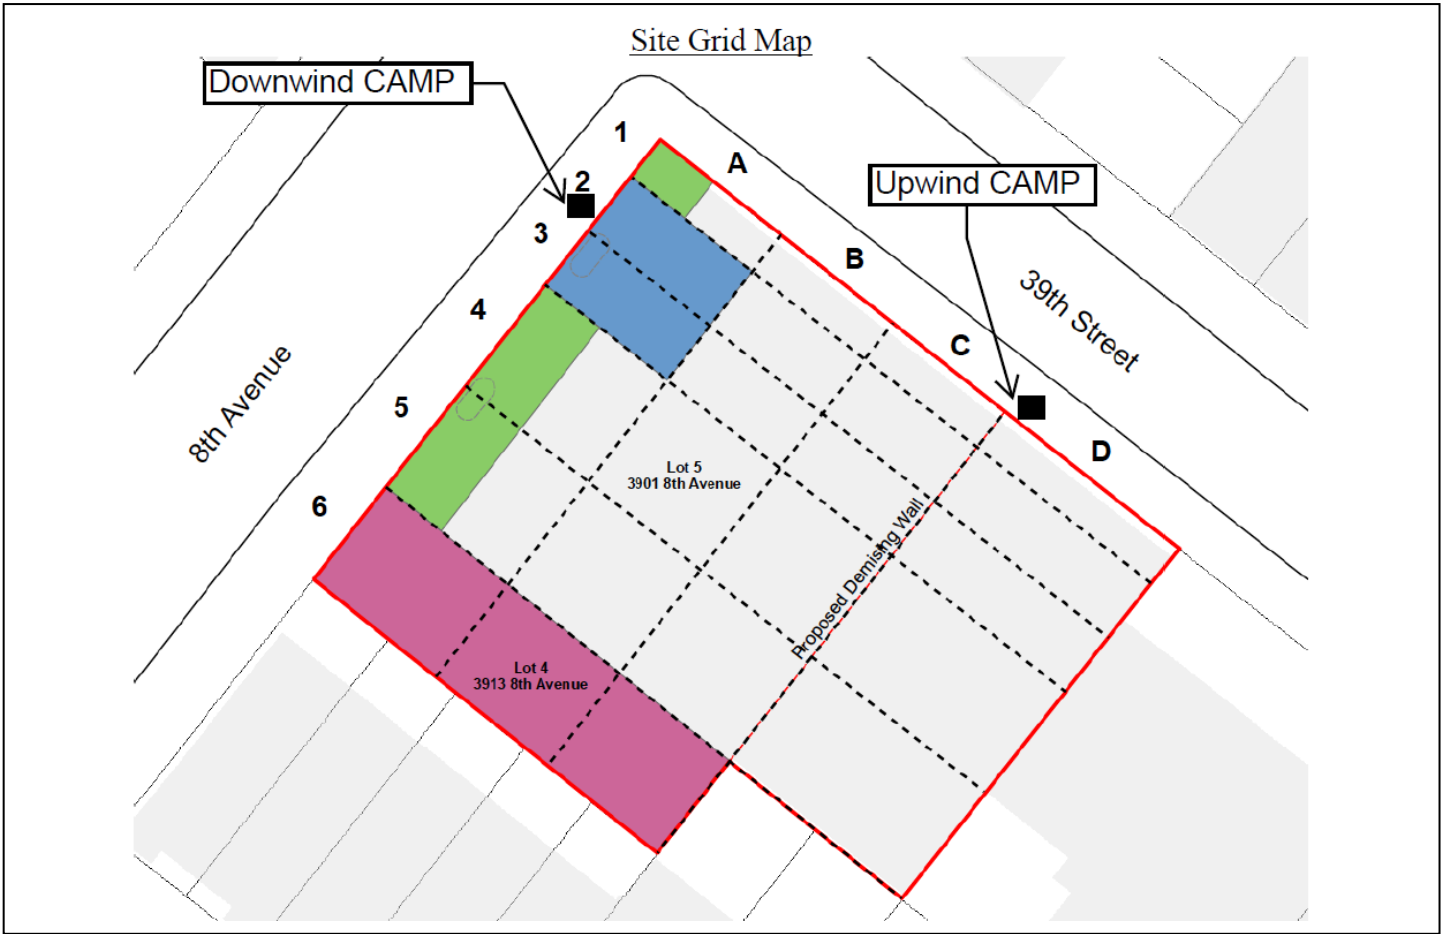


Photo Log

Photo 1 –
View of
concrete
demolition.



Photo 2 –
View of
remaining
soil for off-
site disposal.



Photo 3 –
View of Site
conditions
and boulder
cleaning.



CAMP Data


DW CAMP

Dust Levels

0.021 mg/m³

0.064 mg/m³

0.15

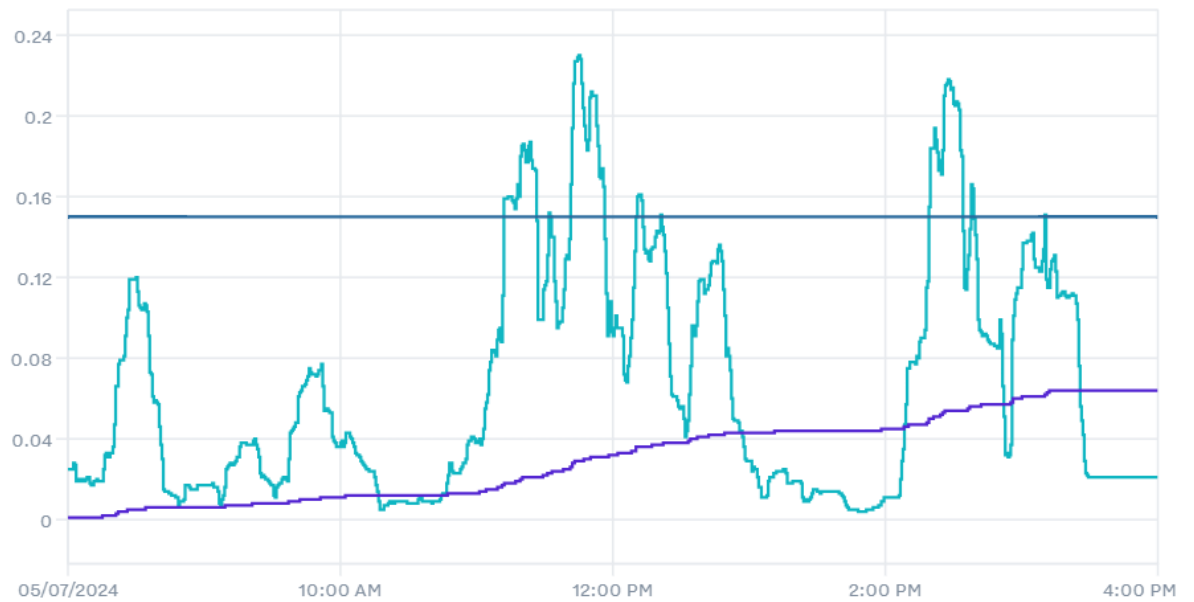


VOC Levels

0.007 ppm

0.018 ppm

5

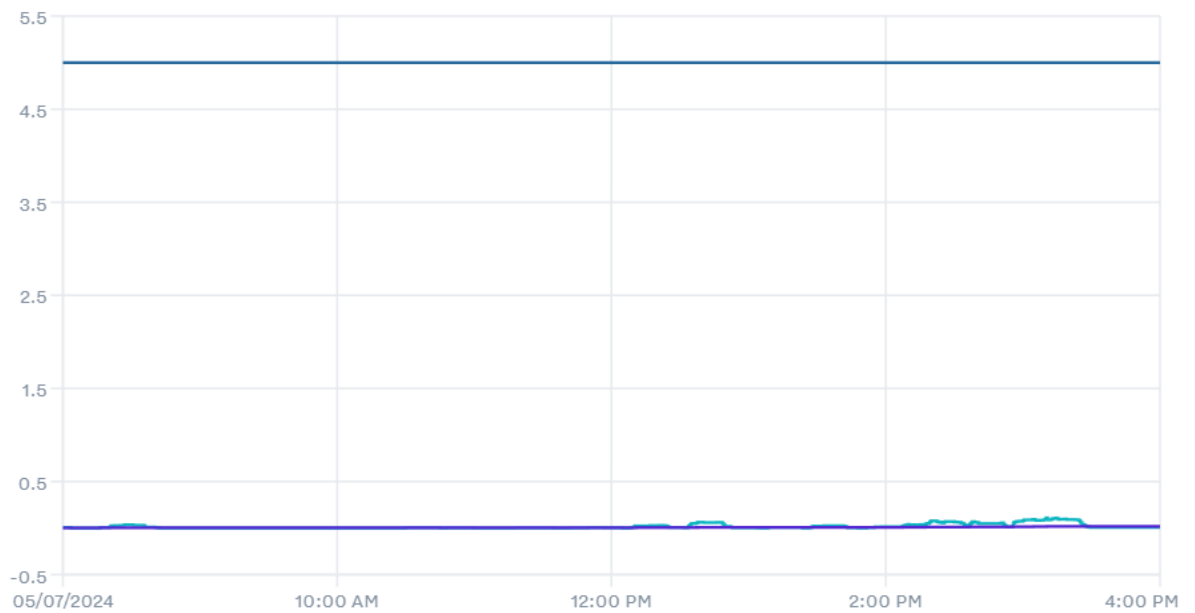


UW CAMP

VOC Levels

0 ppm

0.005 ppm

5

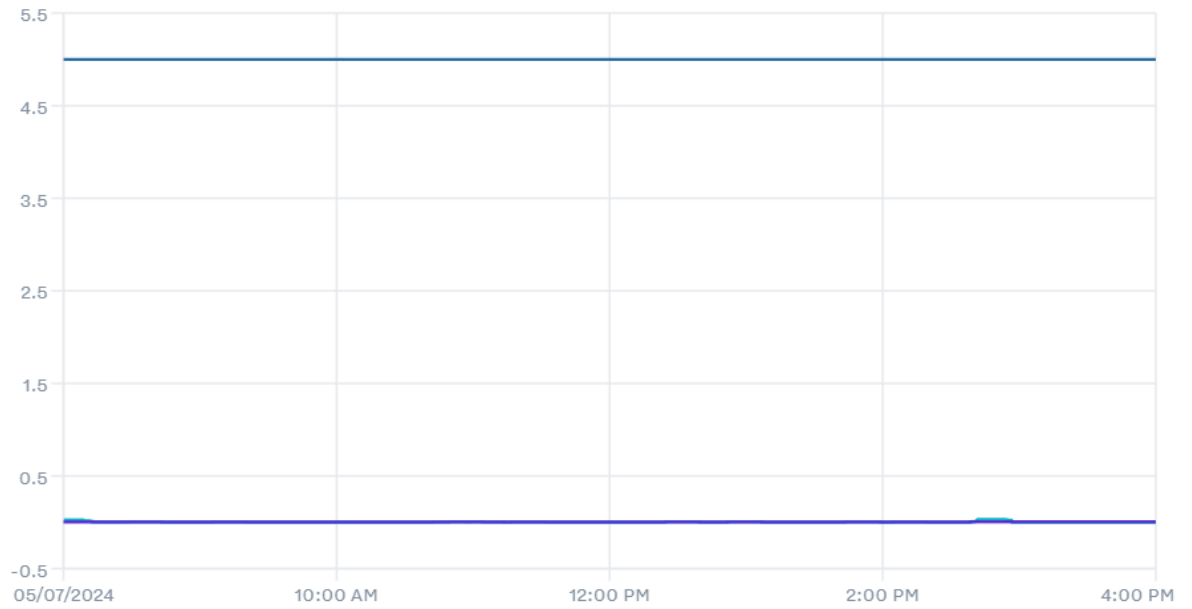

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/7/2024 7:45	5/7/2024 7:55	0.150	0	5	0.002
Modem 47822	5/7/2024 7:55	5/7/2024 8:05	0.150	0.001	5	0.002
Modem 47822	5/7/2024 8:05	5/7/2024 8:15	0.150	0.001	5	0.002
Modem 47822	5/7/2024 8:15	5/7/2024 8:25	0.150	0.004	5	0.003
Modem 47822	5/7/2024 8:25	5/7/2024 8:35	0.150	0.006	5	0.003
Modem 47822	5/7/2024 8:35	5/7/2024 8:45	0.150	0.006	5	0.003
Modem 47822	5/7/2024 8:45	5/7/2024 8:55	0.150	0.006	5	0.003
Modem 47822	5/7/2024 8:55	5/7/2024 9:05	0.150	0.006	5	0.003
Modem 47822	5/7/2024 9:05	5/7/2024 9:15	0.150	0.007	5	0.003
Modem 47822	5/7/2024 9:15	5/7/2024 9:25	0.150	0.008	5	0.003
Modem 47822	5/7/2024 9:25	5/7/2024 9:35	0.150	0.008	5	0.003
Modem 47822	5/7/2024 9:35	5/7/2024 9:45	0.150	0.01	5	0.003
Modem 47822	5/7/2024 9:45	5/7/2024 9:55	0.150	0.011	5	0.003
Modem 47822	5/7/2024 9:55	5/7/2024 10:05	0.150	0.012	5	0.003
Modem 47822	5/7/2024 10:05	5/7/2024 10:15	0.150	0.012	5	0.003
Modem 47822	5/7/2024 10:15	5/7/2024 10:25	0.150	0.012	5	0.003
Modem 47822	5/7/2024 10:25	5/7/2024 10:35	0.150	0.012	5	0.004
Modem 47822	5/7/2024 10:35	5/7/2024 10:45	0.150	0.012	5	0.004
Modem 47822	5/7/2024 10:45	5/7/2024 10:55	0.150	0.013	5	0.004
Modem 47822	5/7/2024 10:55	5/7/2024 11:05	0.150	0.015	5	0.004
Modem 47822	5/7/2024 11:05	5/7/2024 11:15	0.150	0.018	5	0.004
Modem 47822	5/7/2024 11:15	5/7/2024 11:25	0.150	0.021	5	0.004
Modem 47822	5/7/2024 11:25	5/7/2024 11:35	0.150	0.024	5	0.004
Modem 47822	5/7/2024 11:35	5/7/2024 11:45	0.150	0.029	5	0.004
Modem 47822	5/7/2024 11:45	5/7/2024 11:55	0.150	0.031	5	0.004
Modem 47822	5/7/2024 11:55	5/7/2024 12:05	0.150	0.033	5	0.004
Modem 47822	5/7/2024 12:05	5/7/2024 12:15	0.150	0.036	5	0.005
Modem 47822	5/7/2024 12:15	5/7/2024 12:25	0.150	0.038	5	0.005
Modem 47822	5/7/2024 12:25	5/7/2024 12:35	0.150	0.04	5	0.006
Modem 47822	5/7/2024 12:35	5/7/2024 12:45	0.150	0.042	5	0.007
Modem 47822	5/7/2024 12:45	5/7/2024 12:55	0.150	0.043	5	0.007
Modem 47822	5/7/2024 12:55	5/7/2024 13:05	0.150	0.043	5	0.007
Modem 47822	5/7/2024 13:05	5/7/2024 13:15	0.150	0.044	5	0.007
Modem 47822	5/7/2024 13:15	5/7/2024 13:25	0.150	0.044	5	0.007
Modem 47822	5/7/2024 13:25	5/7/2024 13:35	0.150	0.044	5	0.008
Modem 47822	5/7/2024 13:35	5/7/2024 13:45	0.150	0.044	5	0.008
Modem 47822	5/7/2024 13:45	5/7/2024 13:55	0.150	0.044	5	0.008
Modem 47822	5/7/2024 13:55	5/7/2024 14:05	0.150	0.045	5	0.008
Modem 47822	5/7/2024 14:05	5/7/2024 14:15	0.150	0.047	5	0.009
Modem 47822	5/7/2024 14:15	5/7/2024 14:25	0.150	0.052	5	0.011
Modem 47822	5/7/2024 14:25	5/7/2024 14:35	0.150	0.054	5	0.011
Modem 47822	5/7/2024 14:35	5/7/2024 14:45	0.150	0.057	5	0.013
Modem 47822	5/7/2024 14:45	5/7/2024 14:55	0.150	0.057	5	0.013
Modem 47822	5/7/2024 14:55	5/7/2024 15:05	0.150	0.061	5	0.016
Modem 47822	5/7/2024 15:05	5/7/2024 15:15	0.150	0.064	5	0.018
Modem 47822	5/7/2024 15:15	5/7/2024 15:25	0.150	0.064	5	0.018
Modem 47822	5/7/2024 15:25	5/7/2024 15:35	0.150	0.064	5	0.018
Modem 47822	5/7/2024 15:35	5/7/2024 15:45	0.150	0.064	5	0.018
Modem 47822	5/7/2024 15:45	5/7/2024 15:55	0.150	0.064	5	0.018
Modem 47822	5/7/2024 15:55	5/7/2024 16:00	0.150	0.064	5	0.018

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/7/2024 7:45	5/7/2024 7:55	0.150	NA	5	0.003
Modem 50062	5/7/2024 7:55	5/7/2024 8:05	0.150	NA	5	0.003
Modem 50062	5/7/2024 8:05	5/7/2024 8:15	0.150	NA	5	0.004
Modem 50062	5/7/2024 8:15	5/7/2024 8:25	0.150	NA	5	0.004
Modem 50062	5/7/2024 8:25	5/7/2024 8:35	0.150	NA	5	0.004
Modem 50062	5/7/2024 8:35	5/7/2024 8:45	0.150	NA	5	0.004
Modem 50062	5/7/2024 8:45	5/7/2024 8:55	0.150	NA	5	0.004
Modem 50062	5/7/2024 8:55	5/7/2024 9:05	0.150	NA	5	0.004
Modem 50062	5/7/2024 9:05	5/7/2024 9:15	0.150	NA	5	0.004
Modem 50062	5/7/2024 9:15	5/7/2024 9:25	0.150	NA	5	0.004
Modem 50062	5/7/2024 9:25	5/7/2024 9:35	0.150	NA	5	0.004
Modem 50062	5/7/2024 9:35	5/7/2024 9:45	0.150	NA	5	0.004
Modem 50062	5/7/2024 9:45	5/7/2024 9:55	0.150	NA	5	0.004
Modem 50062	5/7/2024 9:55	5/7/2024 10:05	0.150	NA	5	0.004
Modem 50062	5/7/2024 10:05	5/7/2024 10:15	0.150	NA	5	0.004
Modem 50062	5/7/2024 10:15	5/7/2024 10:25	0.150	NA	5	0.004
Modem 50062	5/7/2024 10:25	5/7/2024 10:35	0.150	NA	5	0.004
Modem 50062	5/7/2024 10:35	5/7/2024 10:45	0.150	NA	5	0.004
Modem 50062	5/7/2024 10:45	5/7/2024 10:55	0.150	NA	5	0.004
Modem 50062	5/7/2024 10:55	5/7/2024 11:05	0.150	NA	5	0.004
Modem 50062	5/7/2024 11:05	5/7/2024 11:15	0.150	NA	5	0.004
Modem 50062	5/7/2024 11:15	5/7/2024 11:25	0.150	NA	5	0.004
Modem 50062	5/7/2024 11:25	5/7/2024 11:35	0.150	NA	5	0.004
Modem 50062	5/7/2024 11:35	5/7/2024 11:45	0.150	NA	5	0.004
Modem 50062	5/7/2024 11:45	5/7/2024 11:55	0.150	NA	5	0.004
Modem 50062	5/7/2024 11:55	5/7/2024 12:05	0.150	NA	5	0.004
Modem 50062	5/7/2024 12:05	5/7/2024 12:15	0.150	NA	5	0.004
Modem 50062	5/7/2024 12:15	5/7/2024 12:25	0.150	NA	5	0.004
Modem 50062	5/7/2024 12:25	5/7/2024 12:35	0.150	NA	5	0.004
Modem 50062	5/7/2024 12:35	5/7/2024 12:45	0.150	NA	5	0.004
Modem 50062	5/7/2024 12:45	5/7/2024 12:55	0.150	NA	5	0.004
Modem 50062	5/7/2024 12:55	5/7/2024 13:05	0.150	NA	5	0.004
Modem 50062	5/7/2024 13:05	5/7/2024 13:15	0.150	NA	5	0.004
Modem 50062	5/7/2024 13:15	5/7/2024 13:25	0.150	NA	5	0.004
Modem 50062	5/7/2024 13:25	5/7/2024 13:35	0.150	NA	5	0.004
Modem 50062	5/7/2024 13:35	5/7/2024 13:45	0.150	NA	5	0.004
Modem 50062	5/7/2024 13:45	5/7/2024 13:55	0.150	NA	5	0.004
Modem 50062	5/7/2024 13:55	5/7/2024 14:05	0.150	NA	5	0.004
Modem 50062	5/7/2024 14:05	5/7/2024 14:15	0.150	NA	5	0.004
Modem 50062	5/7/2024 14:15	5/7/2024 14:25	0.150	NA	5	0.004
Modem 50062	5/7/2024 14:25	5/7/2024 14:35	0.150	NA	5	0.004
Modem 50062	5/7/2024 14:35	5/7/2024 14:45	0.150	NA	5	0.005
Modem 50062	5/7/2024 14:45	5/7/2024 14:55	0.150	NA	5	0.005
Modem 50062	5/7/2024 14:55	5/7/2024 15:05	0.150	NA	5	0.005
Modem 50062	5/7/2024 15:05	5/7/2024 15:15	0.150	NA	5	0.005
Modem 50062	5/7/2024 15:15	5/7/2024 15:25	0.150	NA	5	0.005
Modem 50062	5/7/2024 15:25	5/7/2024 15:35	0.150	NA	5	0.005
Modem 50062	5/7/2024 15:35	5/7/2024 15:45	0.150	NA	5	0.005
Modem 50062	5/7/2024 15:45	5/7/2024 15:55	0.150	NA	5	0.005
Modem 50062	5/7/2024 15:55	5/7/2024 16:00	0.150	NA	5	0.005

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy	X	Bright Sun	
TEMP.	< 32		32-50		50-70		70-85	X	>85	

BCP Site ID #:C224267

Date: 05/08/2024

Project Name: **3901-3913 8th Avenue – Brooklyn, NY****Consultant:**Matthew Carroll, P.E.
Tenen Environmental**Safety Officer:**Claire Zaccheo
Tenen Environmental**General Contractor:**EarthTech Services, Inc.
222 William Street
Bronx, NY 10461**EarthTech Site Superintendent:**Sam Caller
(347) 907-4053**Work Activities Performed (Since Last Report):**

Export of 2 truckloads (approximately 40 CY) of material for off-site disposal at the Bayshore Soil Management facility.

The workday was completed around 11:30AM following the completion of trucking for off-site soil disposal.

Working In Grid #: A1, A2 and A3**Samples Collected (Since Last Report):****Air Monitoring (Since Last Report):****Background Conditions**

Upwind: Dust: 0.047 mg/m3 PID: 0.0 ppm

Downwind: Dust: 0.024 mg/m3 PID: 0.0 ppm

Daily TWA

Upwind: Dust: 0.004 mg/m3 PID: 0.0 ppm

Downwind: Dust: 0.025 mg/m3 PID: 0.021 ppm

Problems Encountered: None**Planned Activities for the Next Day/ Week:**

The Site will be closed until backfill approval, pending the NYSDEC review and approval of endpoint sampling analytical results.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832	
(Trucks, CY)	Trucks	Cu. Yds.
Today	2	40
Total	35	700

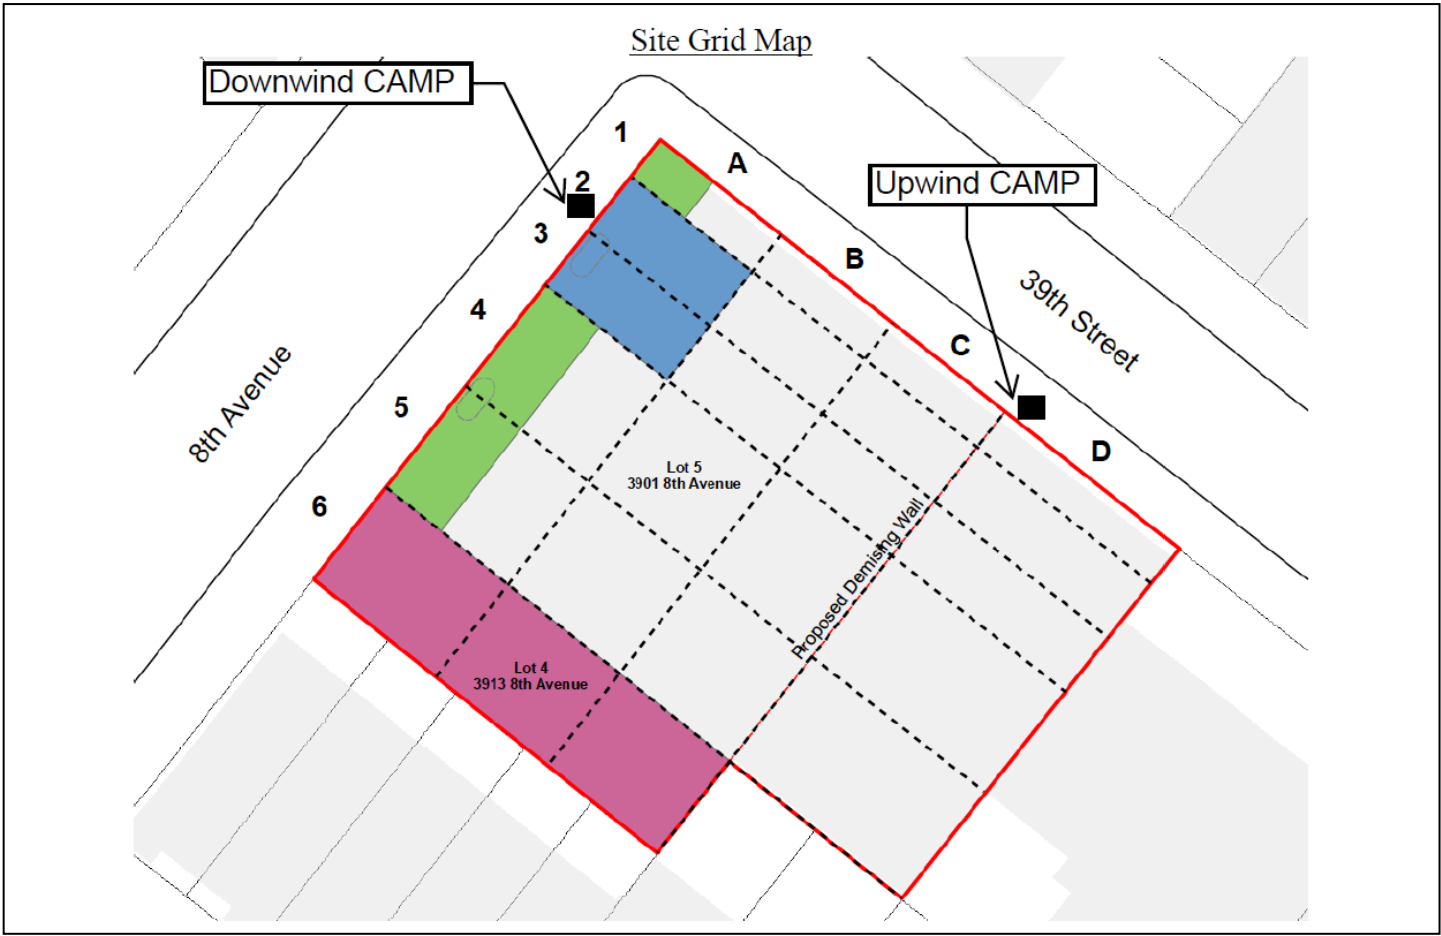


Photo Log

Photo 1 –
View of
truck loading
for off-site
soil disposal.



Photo 2 –
View of the
excavation.



Photo 3 –
View of site
conditions
and truck
loading for
off-site soil
disposal.



CAMP Data


DW CAMP

Dust Levels

0.028 mg/m³

0.004 mg/m³

0.15

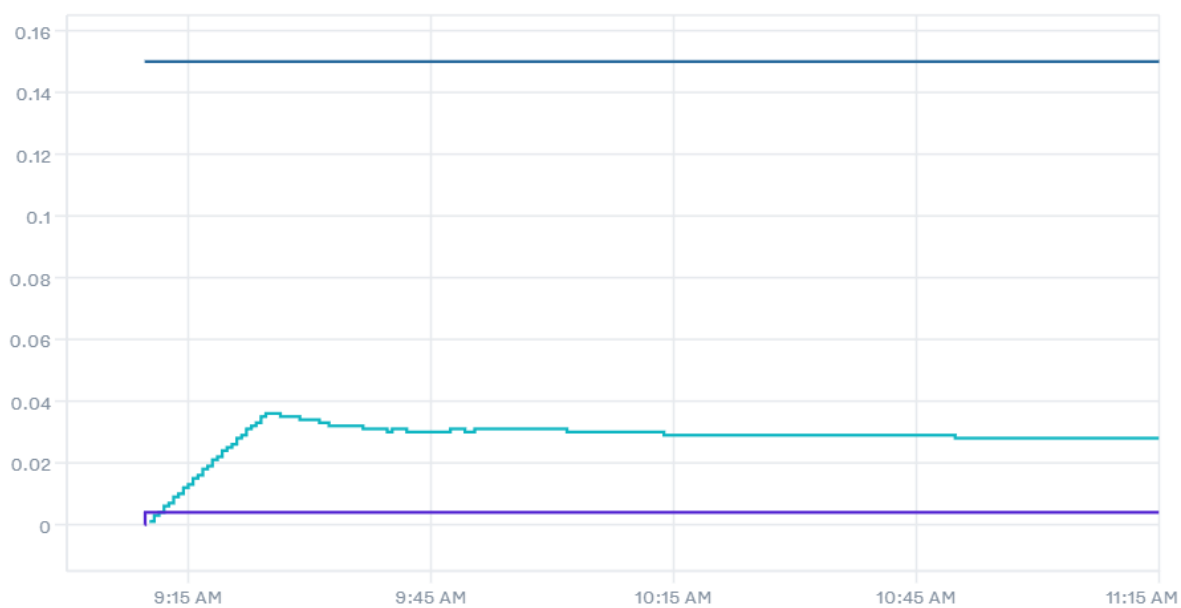


VOC Levels

0 ppm

0 ppm

5

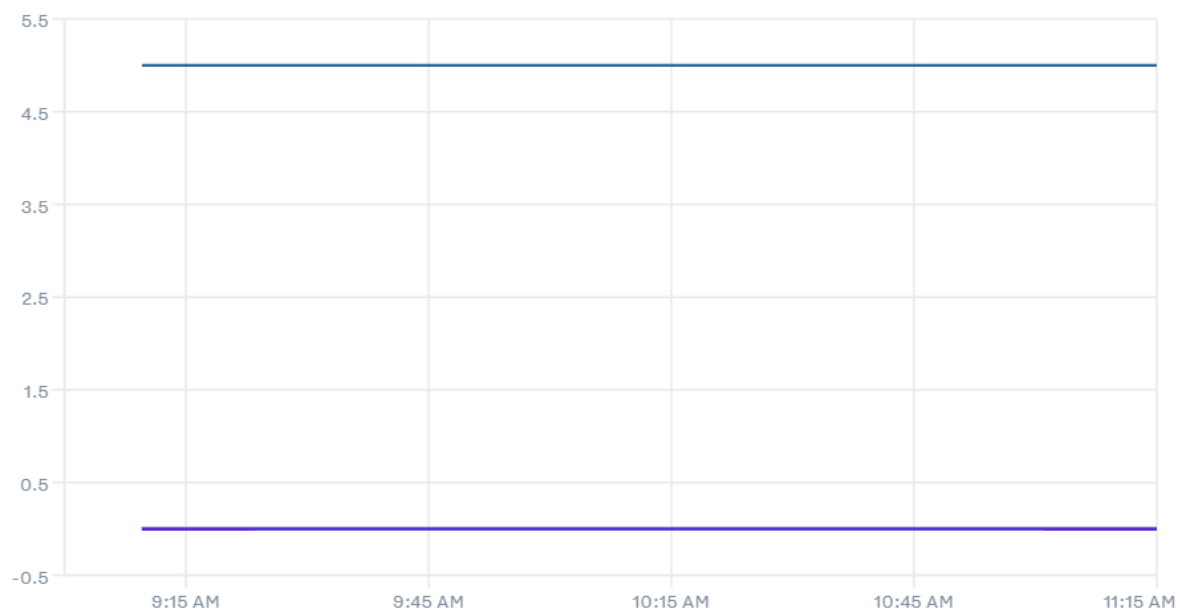


Dust Levels

0.07 mg/m³

0.025 mg/m³

0.15

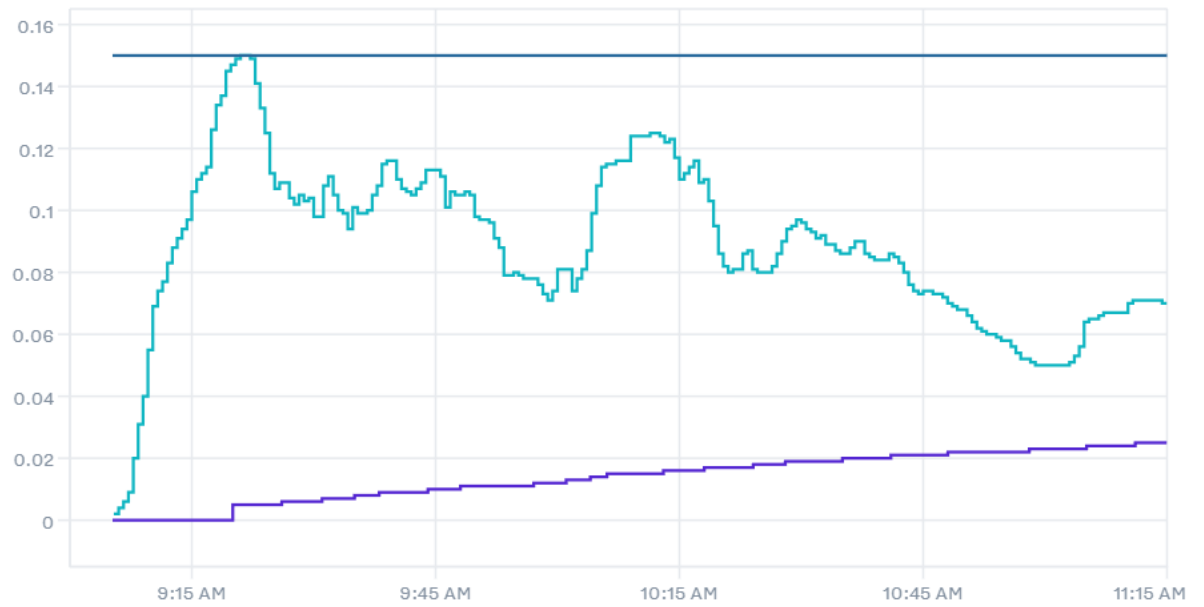


VOC Levels

0.046 ppm

0.021 ppm

5

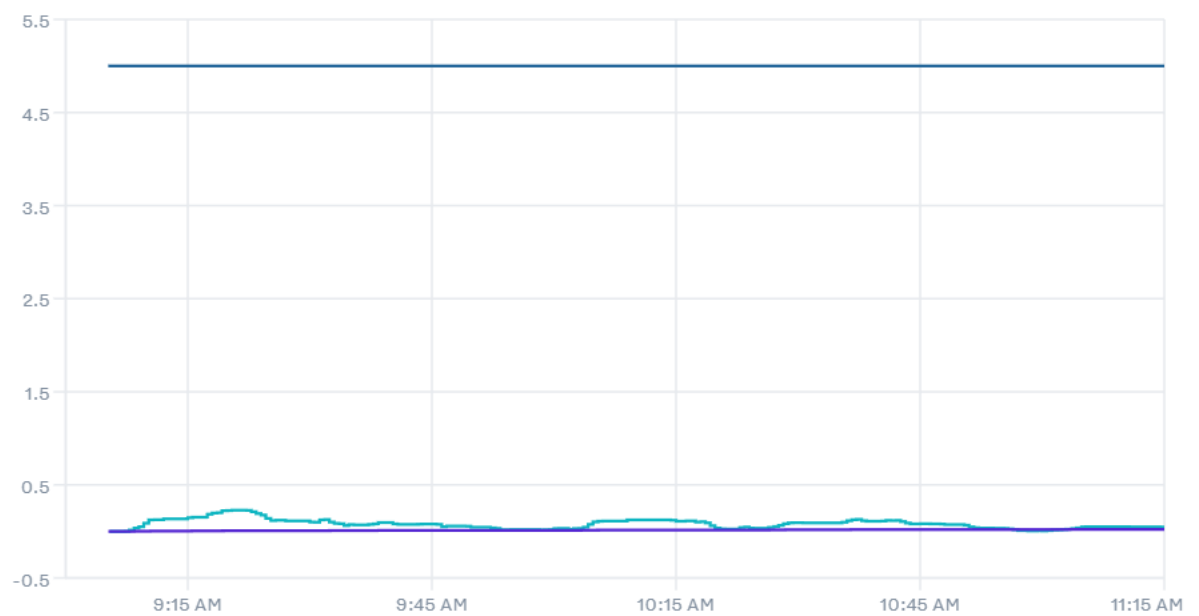

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/8/2024 9:00	5/8/2024 9:10	0.150	0	5	0.002
Modem 47822	5/8/2024 9:10	5/8/2024 9:20	0.150	0	5	0.007
Modem 47822	5/8/2024 9:20	5/8/2024 9:30	0.150	0.006	5	0.007
Modem 47822	5/8/2024 9:30	5/8/2024 9:40	0.150	0.009	5	0.01
Modem 47822	5/8/2024 9:40	5/8/2024 9:50	0.150	0.011	5	0.01
Modem 47822	5/8/2024 9:50	5/8/2024 10:00	0.150	0.012	5	0.011
Modem 47822	5/8/2024 10:00	5/8/2024 10:10	0.150	0.015	5	0.014
Modem 47822	5/8/2024 10:10	5/8/2024 10:20	0.150	0.017	5	0.015
Modem 47822	5/8/2024 10:20	5/8/2024 10:30	0.150	0.019	5	0.017
Modem 47822	5/8/2024 10:30	5/8/2024 10:40	0.150	0.02	5	0.019
Modem 47822	5/8/2024 10:40	5/8/2024 10:50	0.150	0.022	5	0.02
Modem 47822	5/8/2024 10:50	5/8/2024 11:00	0.150	0.023	5	0.02
Modem 47822	5/8/2024 11:00	5/8/2024 11:10	0.150	0.024	5	0.021
Modem 47822	5/8/2024 11:10	5/8/2024 11:15	0.150	0.025	5	0.021

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/8/2024 9:00	5/8/2024 9:10	0.150	0.004	5	0
Modem 50062	5/8/2024 9:10	5/8/2024 9:20	0.150	0.004	5	0
Modem 50062	5/8/2024 9:20	5/8/2024 9:30	0.150	0.004	5	0
Modem 50062	5/8/2024 9:30	5/8/2024 9:40	0.150	0.004	5	0
Modem 50062	5/8/2024 9:40	5/8/2024 9:50	0.150	0.004	5	0
Modem 50062	5/8/2024 9:50	5/8/2024 10:00	0.150	0.004	5	0
Modem 50062	5/8/2024 10:00	5/8/2024 10:10	0.150	0.004	5	0
Modem 50062	5/8/2024 10:10	5/8/2024 10:20	0.150	0.004	5	0
Modem 50062	5/8/2024 10:20	5/8/2024 10:30	0.150	0.004	5	0
Modem 50062	5/8/2024 10:30	5/8/2024 10:40	0.150	0.004	5	0
Modem 50062	5/8/2024 10:40	5/8/2024 10:50	0.150	0.004	5	0
Modem 50062	5/8/2024 10:50	5/8/2024 11:00	0.150	0.004	5	0
Modem 50062	5/8/2024 11:00	5/8/2024 11:10	0.150	0.004	5	0
Modem 50062	5/8/2024 11:10	5/8/2024 11:15	0.150	0.004	5	0

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain	X	Overcast		Partly Cloudy		Bright Sun	
TEMP.	< 32		32-50		50-70	X	70-85		>85	

BCP Site ID #:C224267

Date: 05/16/2024

Project Name: 3901-3913 8th Avenue – Brooklyn, NY

Consultant:

Matthew Carroll, P.E.
Tenen Environmental

Safety Officer:

Claire Zaccheo
Tenen Environmental

General Contractor:

EarthTech Services, Inc.
222 William Street
Bronx, NY 10461

EarthTech Site Superintendent:

Sam Caller
(347) 907-4053

Work Activities Performed (Since Last Report):

The contractor imported 8 (approximately 200 tons) loads of ¾” stone from the Stavola Construction Materials Bound Brook Quarry (BBQ) to backfill the remedial excavation.

Working In Grid #: A1, A2 and A3

Samples Collected (Since Last Report): None

Air Monitoring (Since Last Report):

Background Conditions

Upwind: Dust: 0.008 mg/m3 PID: 1.2 ppm
Downwind: Dust: 0.002 mg/m3 PID: 0.1 ppm

Daily TWA

Upwind: Dust: 0.019 mg/m3 PID: 0.027 ppm
Downwind: Dust: 0.003 mg/m3 PID: 0.036 ppm

*CAMP stations were placed indoors near the sidewalk exits to avoid instrument damage from high winds and rain.

Problems Encountered: None.

Planned Activities for the Next Day/ Week:

The contractor will be continuing to backfill.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832	
(Trucks, CY)	Trucks	Cu. Yds.
Today	0	0
Total	33	660

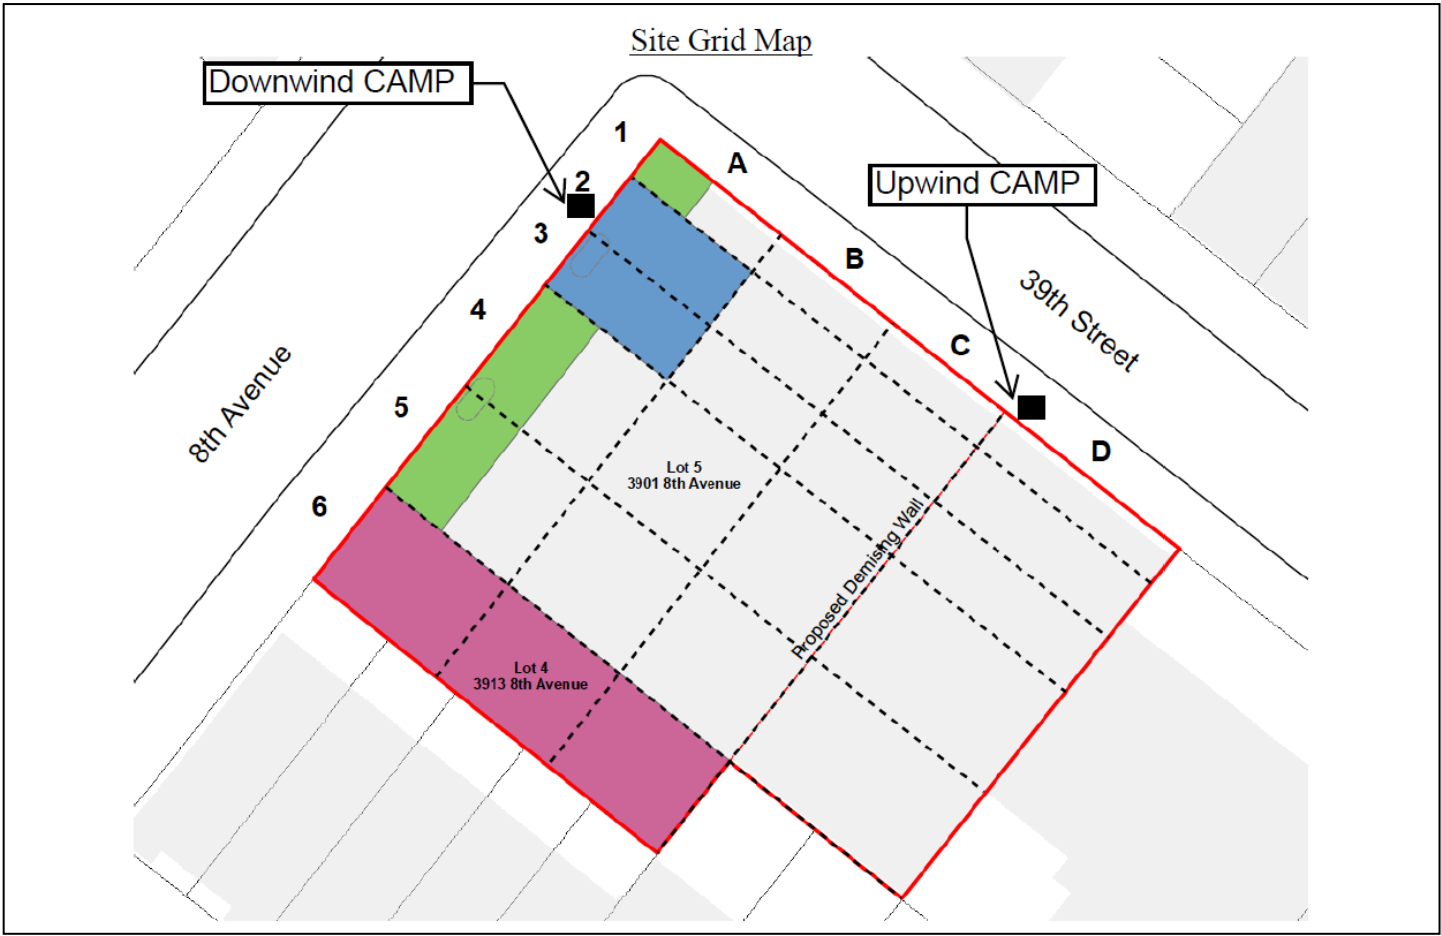


Photo Log

Photo 1 –
View of the
remedial
excavation
prior to
backfilling.



Photo 2 –
View of ¾”
stone
imported for
backfill.



Photo 3 –
View of
stone
backfilling in
the remedial
excavation.



CAMP Data


DW CAMP

Dust Levels

0.012 mg/m³

0.003 mg/m³

0.15

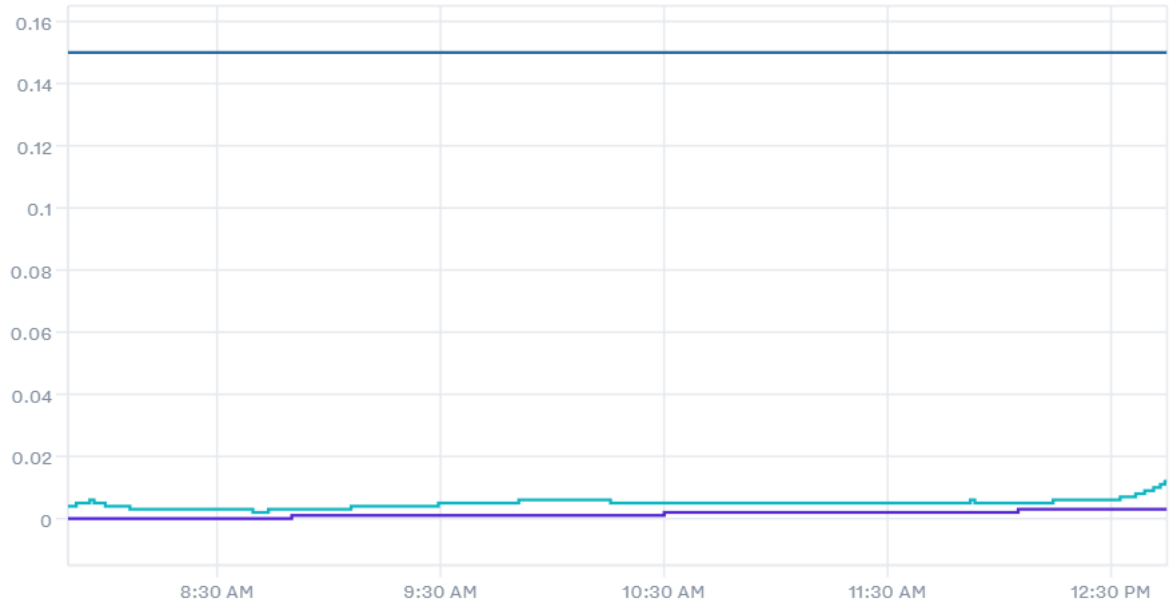


VOC Levels

0 ppm

0.036 ppm

5

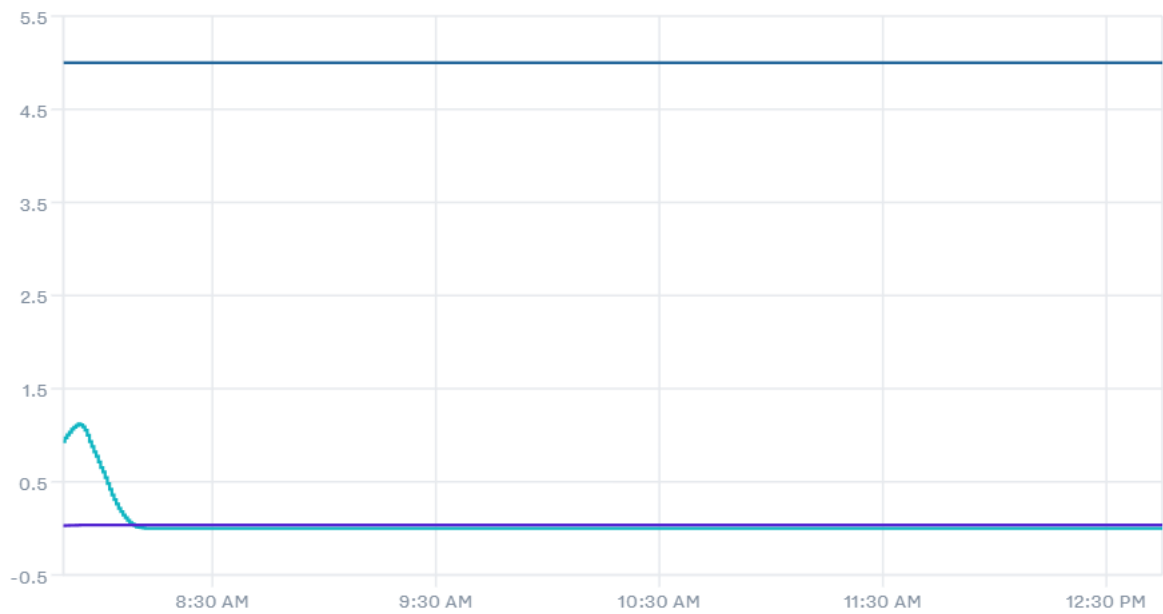


Dust Levels

0.363 mg/m³

0.019 mg/m³

0.15

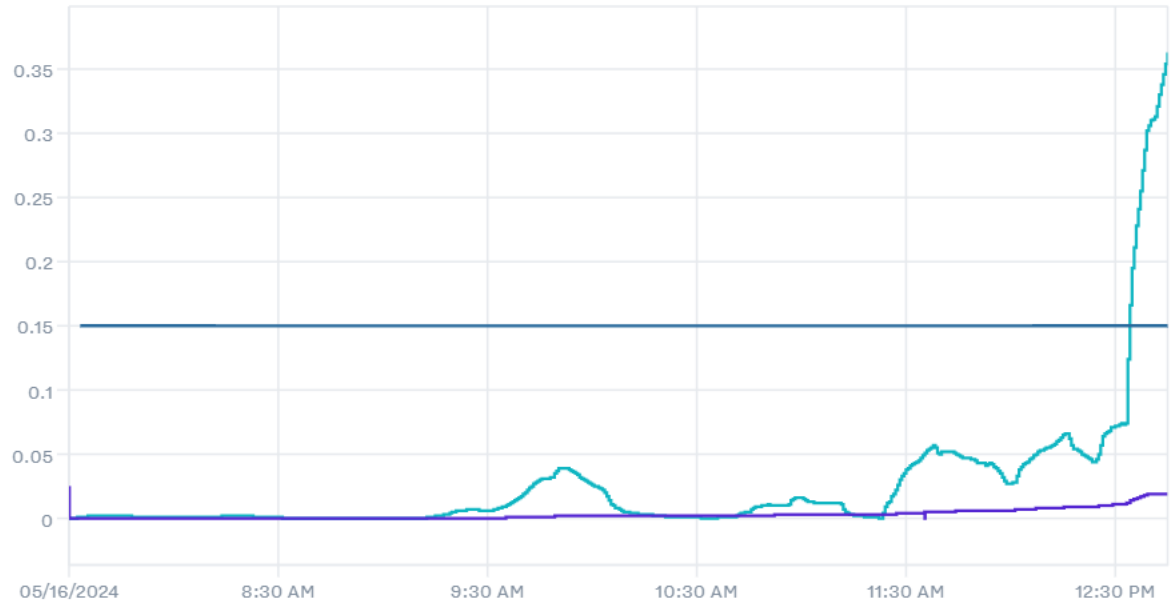


VOC Levels

0 ppm

0.027 ppm

5

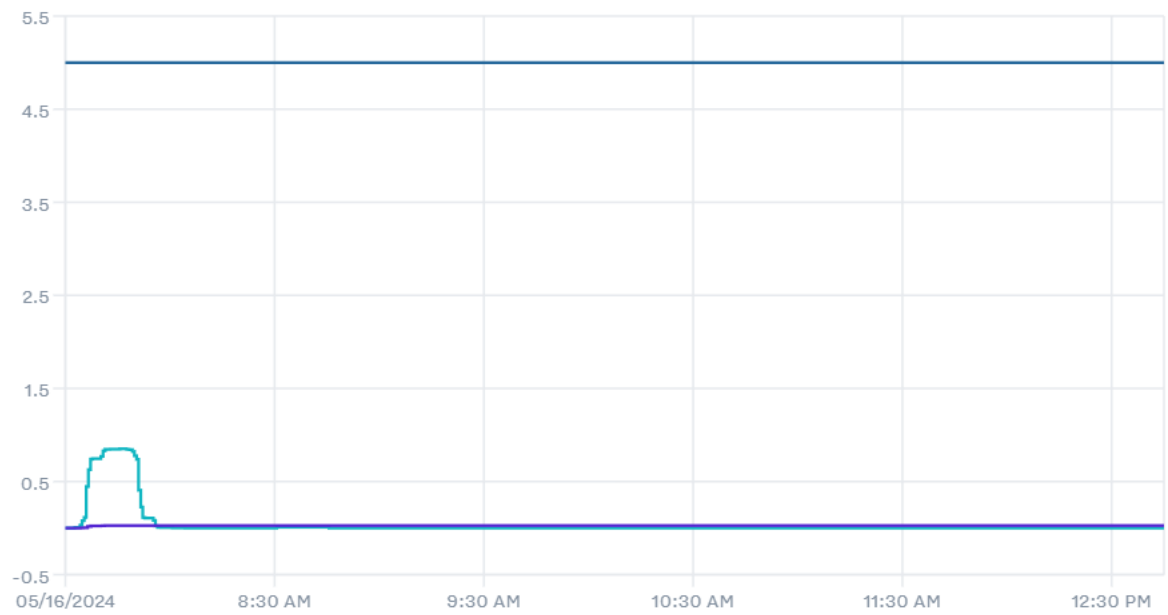

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/16/2024 7:30	5/16/2024 7:40	0.150	0	5	0.023
Modem 47822	5/16/2024 7:40	5/16/2024 7:50	0.150	0	5	0.026
Modem 47822	5/16/2024 7:50	5/16/2024 8:00	0.150	0	5	0.026
Modem 47822	5/16/2024 8:00	5/16/2024 8:10	0.150	0	5	0.026
Modem 47822	5/16/2024 8:10	5/16/2024 8:20	0.150	0	5	0.026
Modem 47822	5/16/2024 8:20	5/16/2024 8:30	0.150	0	5	0.026
Modem 47822	5/16/2024 8:30	5/16/2024 8:40	0.150	0	5	0.027
Modem 47822	5/16/2024 8:40	5/16/2024 8:50	0.150	0	5	0.027
Modem 47822	5/16/2024 8:50	5/16/2024 9:00	0.150	0	5	0.027
Modem 47822	5/16/2024 9:00	5/16/2024 9:10	0.150	0	5	0.027
Modem 47822	5/16/2024 9:10	5/16/2024 9:20	0.150	0	5	0.027
Modem 47822	5/16/2024 9:20	5/16/2024 9:30	0.150	0	5	0.027
Modem 47822	5/16/2024 9:30	5/16/2024 9:40	0.150	0.001	5	0.027
Modem 47822	5/16/2024 9:40	5/16/2024 9:50	0.150	0.002	5	0.027
Modem 47822	5/16/2024 9:50	5/16/2024 10:00	0.150	0.002	5	0.027
Modem 47822	5/16/2024 10:00	5/16/2024 10:10	0.150	0.002	5	0.027
Modem 47822	5/16/2024 10:10	5/16/2024 10:20	0.150	0.002	5	0.027
Modem 47822	5/16/2024 10:20	5/16/2024 10:30	0.150	0.002	5	0.027
Modem 47822	5/16/2024 10:30	5/16/2024 10:40	0.150	0.002	5	0.027
Modem 47822	5/16/2024 10:40	5/16/2024 10:50	0.150	0.002	5	0.027
Modem 47822	5/16/2024 10:50	5/16/2024 11:00	0.150	0.003	5	0.027
Modem 47822	5/16/2024 11:00	5/16/2024 11:10	0.150	0.003	5	0.027
Modem 47822	5/16/2024 11:10	5/16/2024 11:20	0.150	0.003	5	0.027
Modem 47822	5/16/2024 11:20	5/16/2024 11:30	0.150	0.004	5	0.027
Modem 47822	5/16/2024 11:30	5/16/2024 11:40	0.150	0.005	5	0.027
Modem 47822	5/16/2024 11:40	5/16/2024 11:50	0.150	0.006	5	0.027
Modem 47822	5/16/2024 11:50	5/16/2024 12:00	0.150	0.006	5	0.027
Modem 47822	5/16/2024 12:00	5/16/2024 12:10	0.150	0.008	5	0.027
Modem 47822	5/16/2024 12:10	5/16/2024 12:20	0.150	0.009	5	0.027
Modem 47822	5/16/2024 12:20	5/16/2024 12:30	0.150	0.011	5	0.027
Modem 47822	5/16/2024 12:30	5/16/2024 12:40	0.150	0.019	5	0.027
Modem 47822	5/16/2024 12:40	5/16/2024 12:45	0.150	0.019	5	0.027

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/16/2024 7:30	5/16/2024 7:40	0.150	0	5	0
Modem 50062	5/16/2024 7:40	5/16/2024 7:50	0.150	0	5	0.028
Modem 50062	5/16/2024 7:50	5/16/2024 8:00	0.150	0	5	0.036
Modem 50062	5/16/2024 8:00	5/16/2024 8:10	0.150	0	5	0.036
Modem 50062	5/16/2024 8:10	5/16/2024 8:20	0.150	0	5	0.036
Modem 50062	5/16/2024 8:20	5/16/2024 8:30	0.150	0	5	0.036
Modem 50062	5/16/2024 8:30	5/16/2024 8:40	0.150	0	5	0.036
Modem 50062	5/16/2024 8:40	5/16/2024 8:50	0.150	0	5	0.036
Modem 50062	5/16/2024 8:50	5/16/2024 9:00	0.150	0.001	5	0.036
Modem 50062	5/16/2024 9:00	5/16/2024 9:10	0.150	0.001	5	0.036
Modem 50062	5/16/2024 9:10	5/16/2024 9:20	0.150	0.001	5	0.036
Modem 50062	5/16/2024 9:20	5/16/2024 9:30	0.150	0.001	5	0.036
Modem 50062	5/16/2024 9:30	5/16/2024 9:40	0.150	0.001	5	0.036
Modem 50062	5/16/2024 9:40	5/16/2024 9:50	0.150	0.001	5	0.036
Modem 50062	5/16/2024 9:50	5/16/2024 10:00	0.150	0.001	5	0.036
Modem 50062	5/16/2024 10:00	5/16/2024 10:10	0.150	0.001	5	0.036
Modem 50062	5/16/2024 10:10	5/16/2024 10:20	0.150	0.001	5	0.036
Modem 50062	5/16/2024 10:20	5/16/2024 10:30	0.150	0.001	5	0.036
Modem 50062	5/16/2024 10:30	5/16/2024 10:40	0.150	0.002	5	0.036
Modem 50062	5/16/2024 10:40	5/16/2024 10:50	0.150	0.002	5	0.036
Modem 50062	5/16/2024 10:50	5/16/2024 11:00	0.150	0.002	5	0.036
Modem 50062	5/16/2024 11:00	5/16/2024 11:10	0.150	0.002	5	0.036
Modem 50062	5/16/2024 11:10	5/16/2024 11:20	0.150	0.002	5	0.036
Modem 50062	5/16/2024 11:20	5/16/2024 11:30	0.150	0.002	5	0.036
Modem 50062	5/16/2024 11:30	5/16/2024 11:40	0.150	0.002	5	0.036
Modem 50062	5/16/2024 11:40	5/16/2024 11:50	0.150	0.002	5	0.036
Modem 50062	5/16/2024 11:50	5/16/2024 12:00	0.150	0.002	5	0.036
Modem 50062	5/16/2024 12:00	5/16/2024 12:10	0.150	0.003	5	0.036
Modem 50062	5/16/2024 12:10	5/16/2024 12:20	0.150	0.003	5	0.036
Modem 50062	5/16/2024 12:20	5/16/2024 12:30	0.150	0.003	5	0.036
Modem 50062	5/16/2024 12:30	5/16/2024 12:40	0.150	0.003	5	0.036
Modem 50062	5/16/2024 12:40	5/16/2024 12:45	0.150	0.003	5	0.036

DAILY STATUS REPORT

Prepared By: C. Zaccheo

WEATHER	Snow		Rain		Overcast		Partly Cloudy		Bright Sun	X
TEMP.	< 32		32-50		50-70		70-85	X	>85	

BCP Site ID #:C224267

Date: 05/31/2024

Project Name: **3901-3913 8th Avenue – Brooklyn, NY****Consultant:**Matthew Carroll, P.E.
Tenen Environmental**Safety Officer:**Claire Zaccheo
Tenen Environmental**General Contractor:**EarthTech Services, Inc.
222 William Street
Bronx, NY 10461**EarthTech Site Superintendent:**Sam Caller
(347) 907-4053**Work Activities Performed (Since Last Report):**

The contractor imported 14 (approximately 420 tons) loads of RCA from P Park to backfill the remedial excavation.

Working In Grid #: A1, A2 and A3**Samples Collected (Since Last Report):** None**Air Monitoring (Since Last Report):****Background Conditions**

Upwind: Dust: 0.001 mg/m3 PID: 0.0 ppm
Downwind: Dust: 0.001 mg/m3 PID: 0.0 ppm

Daily TWA

Upwind: Dust: 0.009 mg/m3 PID: 0.0 ppm
Downwind: Dust: 0.005 mg/m3 PID: 0.0 ppm

Problems Encountered: None.**Planned Activities for the Next Day/ Week:**

The contractor will be continuing to backfill.

Facility # Name/ Location	Bayshore Soil Management 75 Crows Mill Road Keasby, NJ 08832	
(Trucks, CY)	Trucks	Cu. Yds.
Today	0	0
Total	33	660

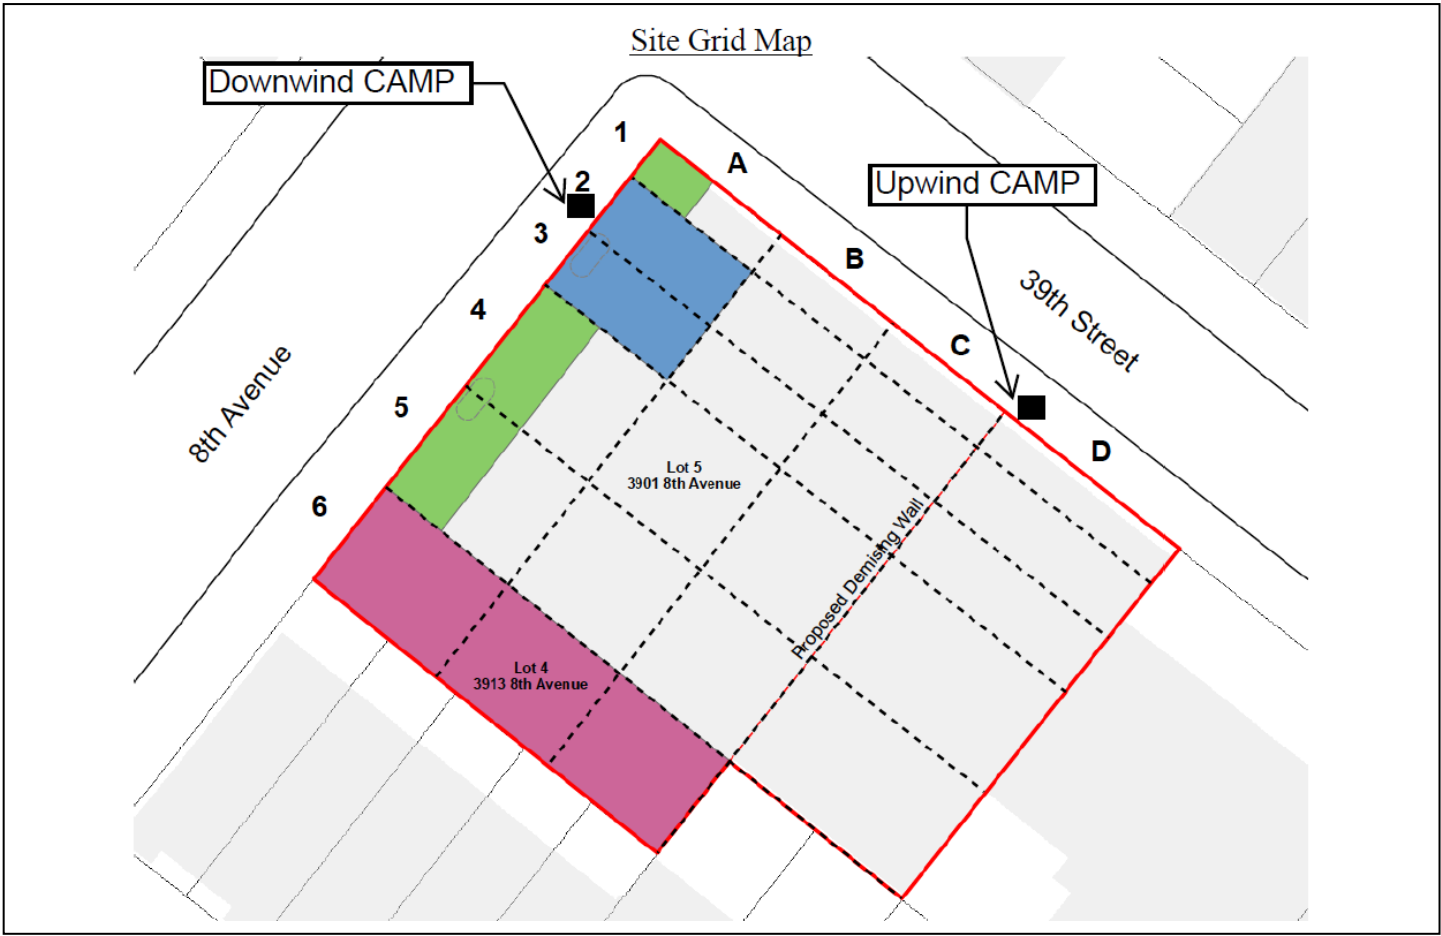


Photo Log

Photo 1 –
View of
backfilling
the remedial
excavation.



Photo 2 –
View of
RCA
imported for
backfilling.



Photo 3 –
View of
RCA
backfilling in
the remedial
excavation.



CAMP Data


DW CAMP

Dust Levels

0.011 mg/m³

0.005 mg/m³

0.15

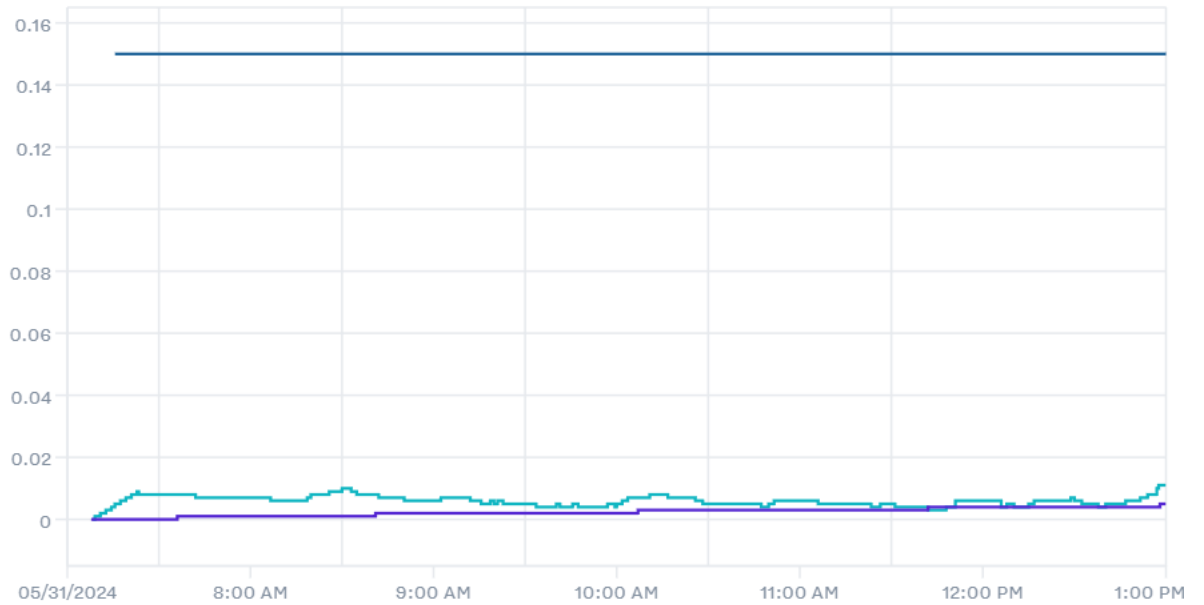


VOC Levels

0 ppm

0 ppm

5

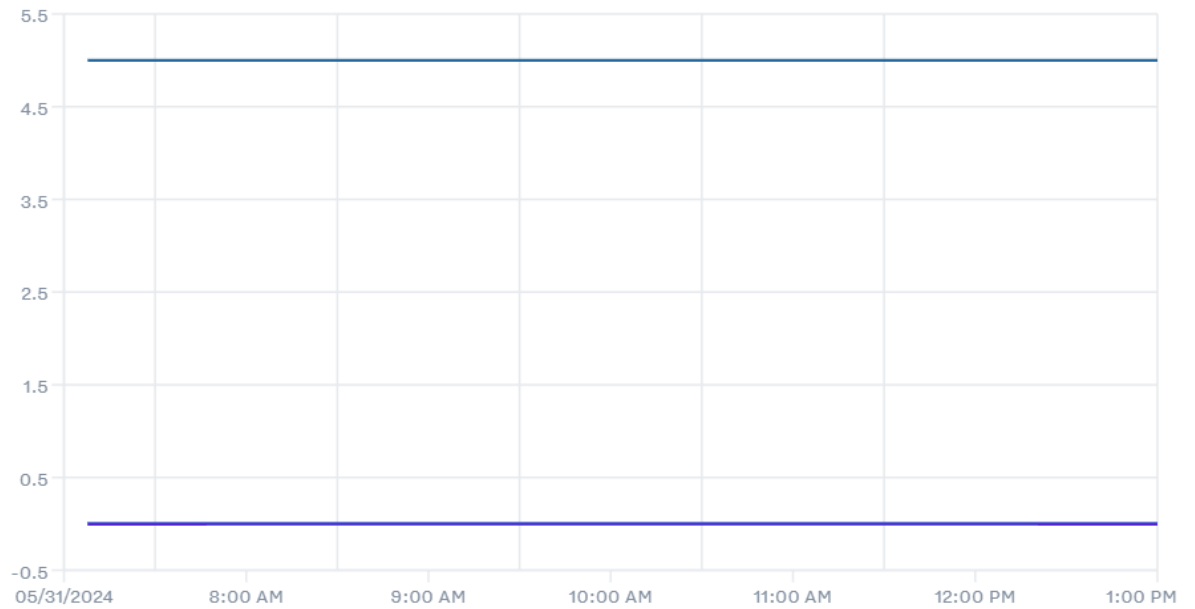


UW CAMP

Dust Levels

0.016 mg/m³

0.009 mg/m³

0.15

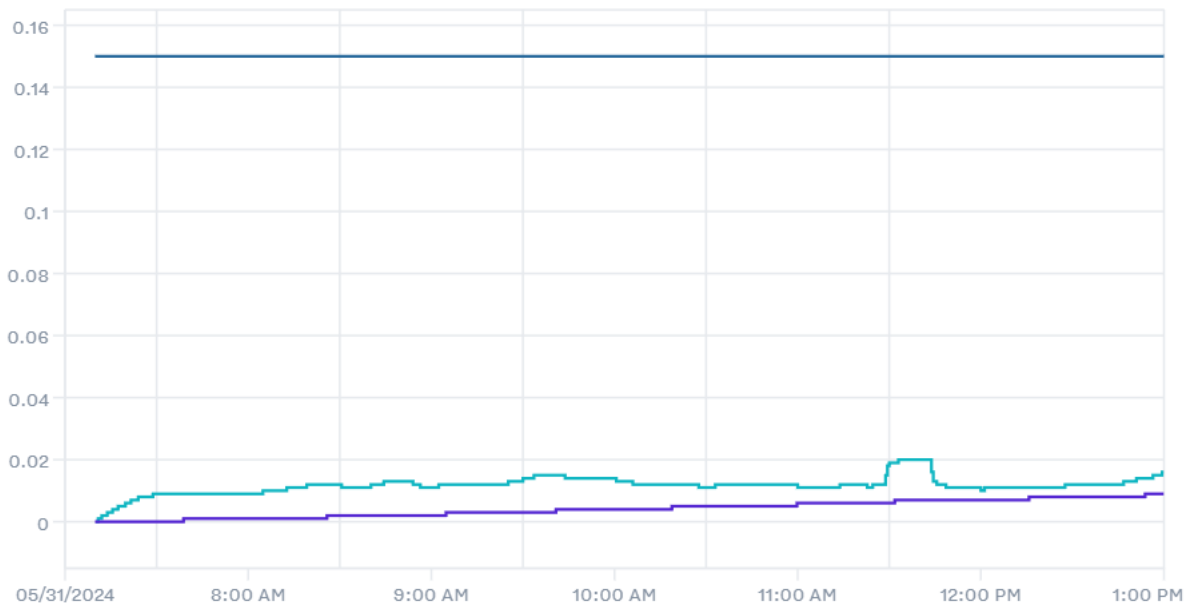


VOC Levels

0 ppm

0 ppm

5

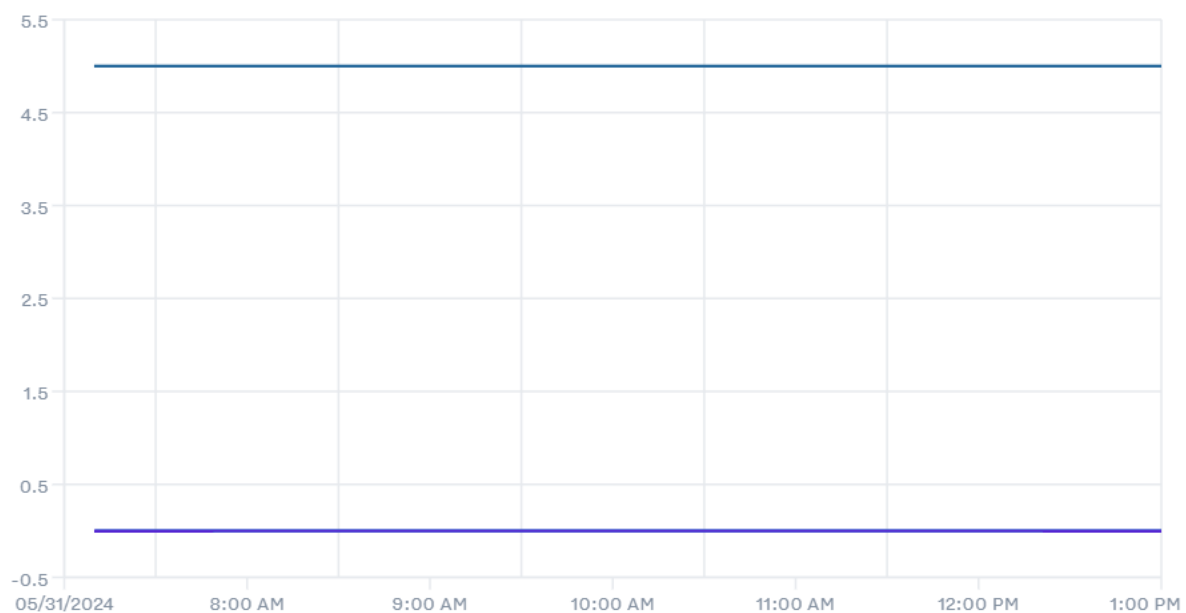

Downwind CAMP
3901-3913 8th Avenue - Brooklyn, NY
BCP Site No.: C224267

Asset Name	Start Time	End Time	Action Level (mg/m ³)	DT2 TWA (mg/m ³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 47822	5/31/2024 7:00	5/31/2024 7:10	0.150	0	5	0
Modem 47822	5/31/2024 7:10	5/31/2024 7:20	0.150	0	5	0
Modem 47822	5/31/2024 7:20	5/31/2024 7:30	0.150	0	5	0
Modem 47822	5/31/2024 7:30	5/31/2024 7:40	0.150	0.001	5	0
Modem 47822	5/31/2024 7:40	5/31/2024 7:50	0.150	0.001	5	0
Modem 47822	5/31/2024 7:50	5/31/2024 8:00	0.150	0.001	5	0
Modem 47822	5/31/2024 8:00	5/31/2024 8:10	0.150	0.001	5	0
Modem 47822	5/31/2024 8:10	5/31/2024 8:20	0.150	0.001	5	0
Modem 47822	5/31/2024 8:20	5/31/2024 8:30	0.150	0.001	5	0
Modem 47822	5/31/2024 8:30	5/31/2024 8:40	0.150	0.001	5	0
Modem 47822	5/31/2024 8:40	5/31/2024 8:50	0.150	0.002	5	0
Modem 47822	5/31/2024 8:50	5/31/2024 9:00	0.150	0.002	5	0
Modem 47822	5/31/2024 9:00	5/31/2024 9:10	0.150	0.002	5	0
Modem 47822	5/31/2024 9:10	5/31/2024 9:20	0.150	0.002	5	0
Modem 47822	5/31/2024 9:20	5/31/2024 9:30	0.150	0.002	5	0
Modem 47822	5/31/2024 9:30	5/31/2024 9:40	0.150	0.002	5	0
Modem 47822	5/31/2024 9:40	5/31/2024 9:50	0.150	0.002	5	0
Modem 47822	5/31/2024 9:50	5/31/2024 10:00	0.150	0.002	5	0
Modem 47822	5/31/2024 10:00	5/31/2024 10:10	0.150	0.003	5	0
Modem 47822	5/31/2024 10:10	5/31/2024 10:20	0.150	0.003	5	0
Modem 47822	5/31/2024 10:20	5/31/2024 10:30	0.150	0.003	5	0
Modem 47822	5/31/2024 10:30	5/31/2024 10:40	0.150	0.003	5	0
Modem 47822	5/31/2024 10:40	5/31/2024 10:50	0.150	0.003	5	0
Modem 47822	5/31/2024 10:50	5/31/2024 11:00	0.150	0.003	5	0
Modem 47822	5/31/2024 11:00	5/31/2024 11:10	0.150	0.003	5	0
Modem 47822	5/31/2024 11:10	5/31/2024 11:20	0.150	0.003	5	0
Modem 47822	5/31/2024 11:20	5/31/2024 11:30	0.150	0.003	5	0
Modem 47822	5/31/2024 11:30	5/31/2024 11:40	0.150	0.003	5	0
Modem 47822	5/31/2024 11:40	5/31/2024 11:50	0.150	0.004	5	0
Modem 47822	5/31/2024 11:50	5/31/2024 12:00	0.150	0.004	5	0
Modem 47822	5/31/2024 12:00	5/31/2024 12:10	0.150	0.004	5	0
Modem 47822	5/31/2024 12:10	5/31/2024 12:20	0.150	0.004	5	0
Modem 47822	5/31/2024 12:20	5/31/2024 12:30	0.150	0.004	5	0
Modem 47822	5/31/2024 12:30	5/31/2024 12:40	0.150	0.004	5	0
Modem 47822	5/31/2024 12:40	5/31/2024 12:50	0.150	0.004	5	0
Modem 47822	5/31/2024 12:50	5/31/2024 13:00	0.150	0.005	5	0

Upwind CAMP
470 Kent Avenue - Brooklyn, NY
BCP Site No.: C224053

Asset Name	Start Time	End Time	Action Level (mg/m³)	DT2 TWA (mg/m³)	Action Level (ppm)	MR3K TWA (ppm)
Modem 50062	5/31/2024 7:00	5/31/2024 7:10	0.150	0	5	0
Modem 50062	5/31/2024 7:10	5/31/2024 7:20	0.150	0	5	0
Modem 50062	5/31/2024 7:20	5/31/2024 7:30	0.150	0	5	0
Modem 50062	5/31/2024 7:30	5/31/2024 7:40	0.150	0.001	5	0
Modem 50062	5/31/2024 7:40	5/31/2024 7:50	0.150	0.001	5	0
Modem 50062	5/31/2024 7:50	5/31/2024 8:00	0.150	0.001	5	0
Modem 50062	5/31/2024 8:00	5/31/2024 8:10	0.150	0.001	5	0
Modem 50062	5/31/2024 8:10	5/31/2024 8:20	0.150	0.001	5	0
Modem 50062	5/31/2024 8:20	5/31/2024 8:30	0.150	0.002	5	0
Modem 50062	5/31/2024 8:30	5/31/2024 8:40	0.150	0.002	5	0
Modem 50062	5/31/2024 8:40	5/31/2024 8:50	0.150	0.002	5	0
Modem 50062	5/31/2024 8:50	5/31/2024 9:00	0.150	0.002	5	0
Modem 50062	5/31/2024 9:00	5/31/2024 9:10	0.150	0.003	5	0
Modem 50062	5/31/2024 9:10	5/31/2024 9:20	0.150	0.003	5	0
Modem 50062	5/31/2024 9:20	5/31/2024 9:30	0.150	0.003	5	0
Modem 50062	5/31/2024 9:30	5/31/2024 9:40	0.150	0.003	5	0
Modem 50062	5/31/2024 9:40	5/31/2024 9:50	0.150	0.004	5	0
Modem 50062	5/31/2024 9:50	5/31/2024 10:00	0.150	0.004	5	0
Modem 50062	5/31/2024 10:00	5/31/2024 10:10	0.150	0.004	5	0
Modem 50062	5/31/2024 10:10	5/31/2024 10:20	0.150	0.005	5	0
Modem 50062	5/31/2024 10:20	5/31/2024 10:30	0.150	0.005	5	0
Modem 50062	5/31/2024 10:30	5/31/2024 10:40	0.150	0.005	5	0
Modem 50062	5/31/2024 10:40	5/31/2024 10:50	0.150	0.005	5	0
Modem 50062	5/31/2024 10:50	5/31/2024 11:00	0.150	0.006	5	0
Modem 50062	5/31/2024 11:00	5/31/2024 11:10	0.150	0.006	5	0
Modem 50062	5/31/2024 11:10	5/31/2024 11:20	0.150	0.006	5	0
Modem 50062	5/31/2024 11:20	5/31/2024 11:30	0.150	0.006	5	0
Modem 50062	5/31/2024 11:30	5/31/2024 11:40	0.150	0.007	5	0
Modem 50062	5/31/2024 11:40	5/31/2024 11:50	0.150	0.007	5	0
Modem 50062	5/31/2024 11:50	5/31/2024 12:00	0.150	0.007	5	0
Modem 50062	5/31/2024 12:00	5/31/2024 12:10	0.150	0.007	5	0
Modem 50062	5/31/2024 12:10	5/31/2024 12:20	0.150	0.008	5	0
Modem 50062	5/31/2024 12:20	5/31/2024 12:30	0.150	0.008	5	0
Modem 50062	5/31/2024 12:30	5/31/2024 12:40	0.150	0.008	5	0
Modem 50062	5/31/2024 12:40	5/31/2024 12:50	0.150	0.008	5	0
Modem 50062	5/31/2024 12:50	5/31/2024 13:00	0.150	0.009	5	0
