**CC:** "Joe Biondolillo" <biondj@cityofrochester.gov>, "Dennis Peck (City)" <de...

**Date:** 11/9/2010 10:06 AM

**Subject:** NYSDEC Site #E828144 - Andrews St 11/06/10 and 11/8/10 demolition progress **Attachments:** Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-06-10 and 11-08-10.pdf; 11-8-10 P 002.jpg

# Charlotte,

Above grade demolition continued on 10/23/10 and 10/25/10, primarily portions of the 300 Andrews Street building that was adjacent to Andrews Street and Bristol Street. Refer to attached photo and Figure 3 depicting the area demolished to date.

Nate Simon, P.E. Day Environmental, Inc. 40 Commercial Street Rochester, New York 14614-1008 Phone: (585) 454-0210 ext:109

Fax: (585) 454-0825

<<Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-06-10 and 11-08-10.pdf>> <<11-8-10 P 002.jpg>>





CC: "Joe Biondolillo" <biondj@cityofrochester.gov>, "Dennis Peck (City)" <de...

**Date:** 11/10/2010 5:07 PM

Subject: NYSDEC Site #E828144 - Andrews St 11/9/10 demolition progress

Attachments: Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-09-10.pdf; 11-9-

10 P 001.jpg

# Charlotte,


Above grade demolition continued on 11/9/10, primarily Site cleanup on portions of 320 Andrews Street building. Refer to attached photo and Figure 3 depicting the area demolished to date.

Nate Simon, P.E. Day Environmental, Inc. 40 Commercial Street Rochester, New York 14614-1008 Phone: (585) 454-0210 ext:109

Fax: (585) 454-0825

<<Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-09-10.pdf>> <<11-9-10 P 001.jpg>>



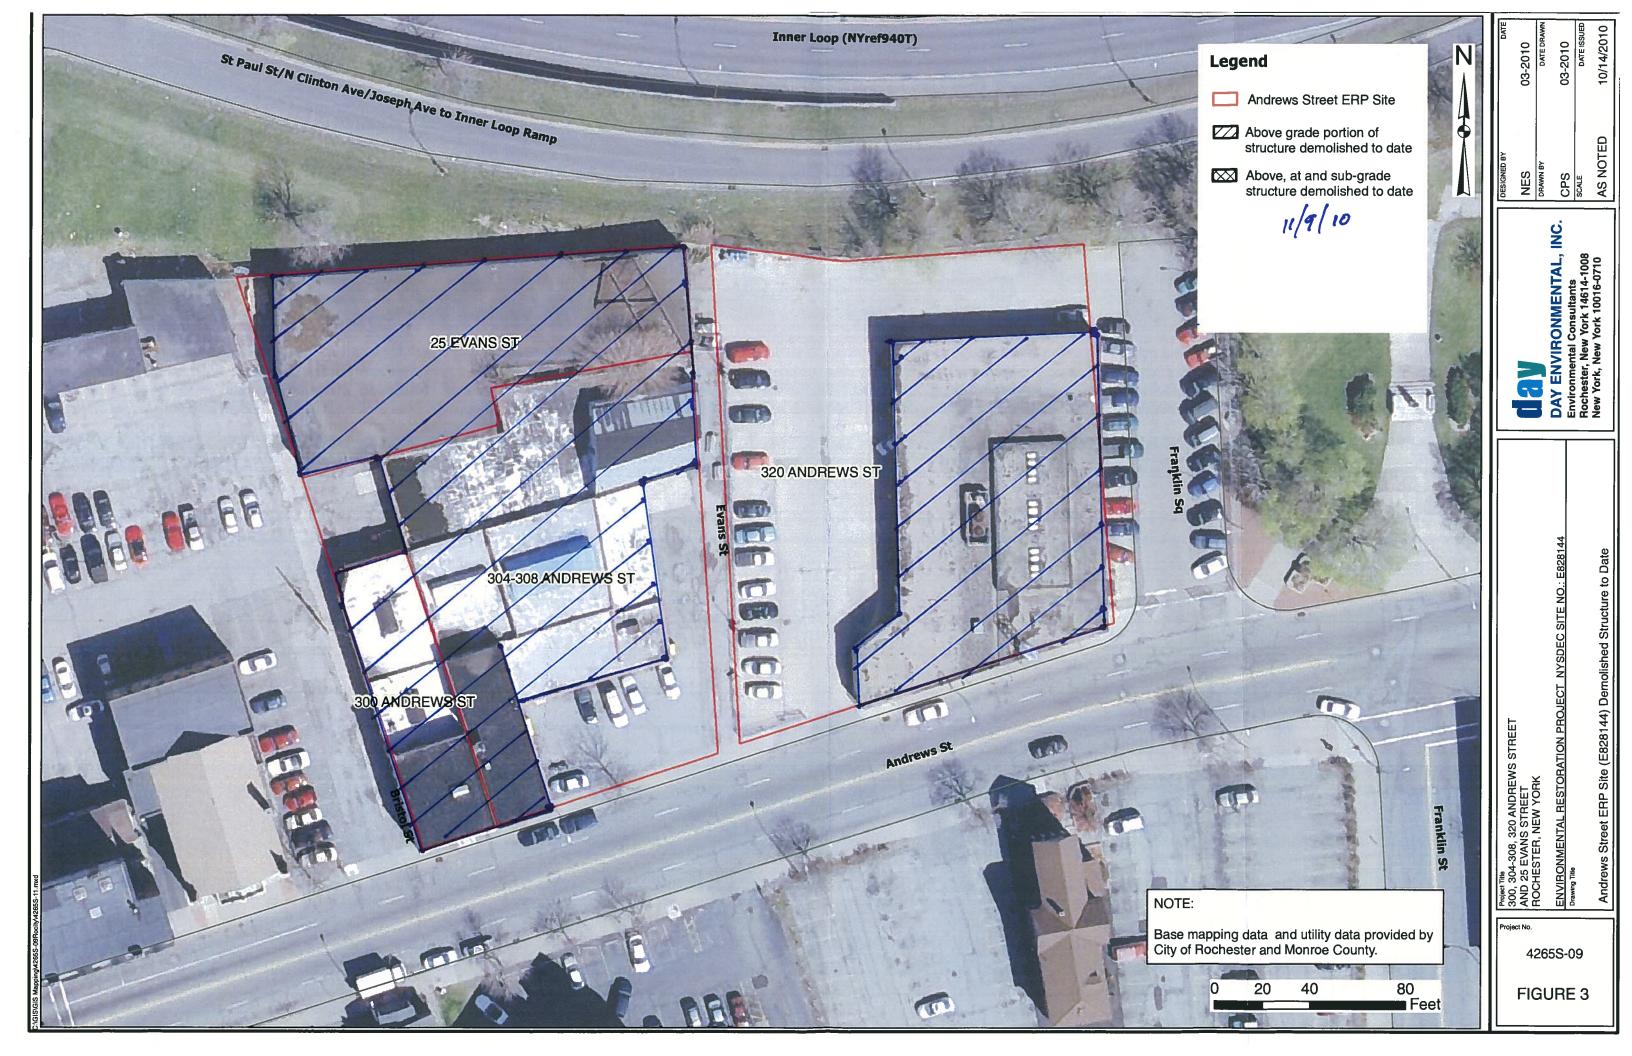

**CC:** "Joe Biondolillo" <biondj@cityofrochester.gov>, "Dennis Peck (City)" <de...

**Date:** 11/11/2010 1:44 PM

Subject: NYSDEC Site #E828144 - Andrews St 11/10/10 demolition progress

Attachments: Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-10-10.pdf; 11-

10-10 P 004.jpg


# Charlotte,

Above grade demolition continued on 11/10/10, primarily Site cleanup on portions of 300, 304-308 and 320 Andrews Street and 25 Evans Street parcels. Refer to attached photo and Figure 3 depicting the area demolished to date.

Nate Simon, P.E. Day Environmental, Inc. 40 Commercial Street Rochester, New York 14614-1008 Phone: (585) 454-0210 ext:109 Fax: (585) 454-0825

<<Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-10-10.pdf>> <<11-10-10 P 004.jpg>>



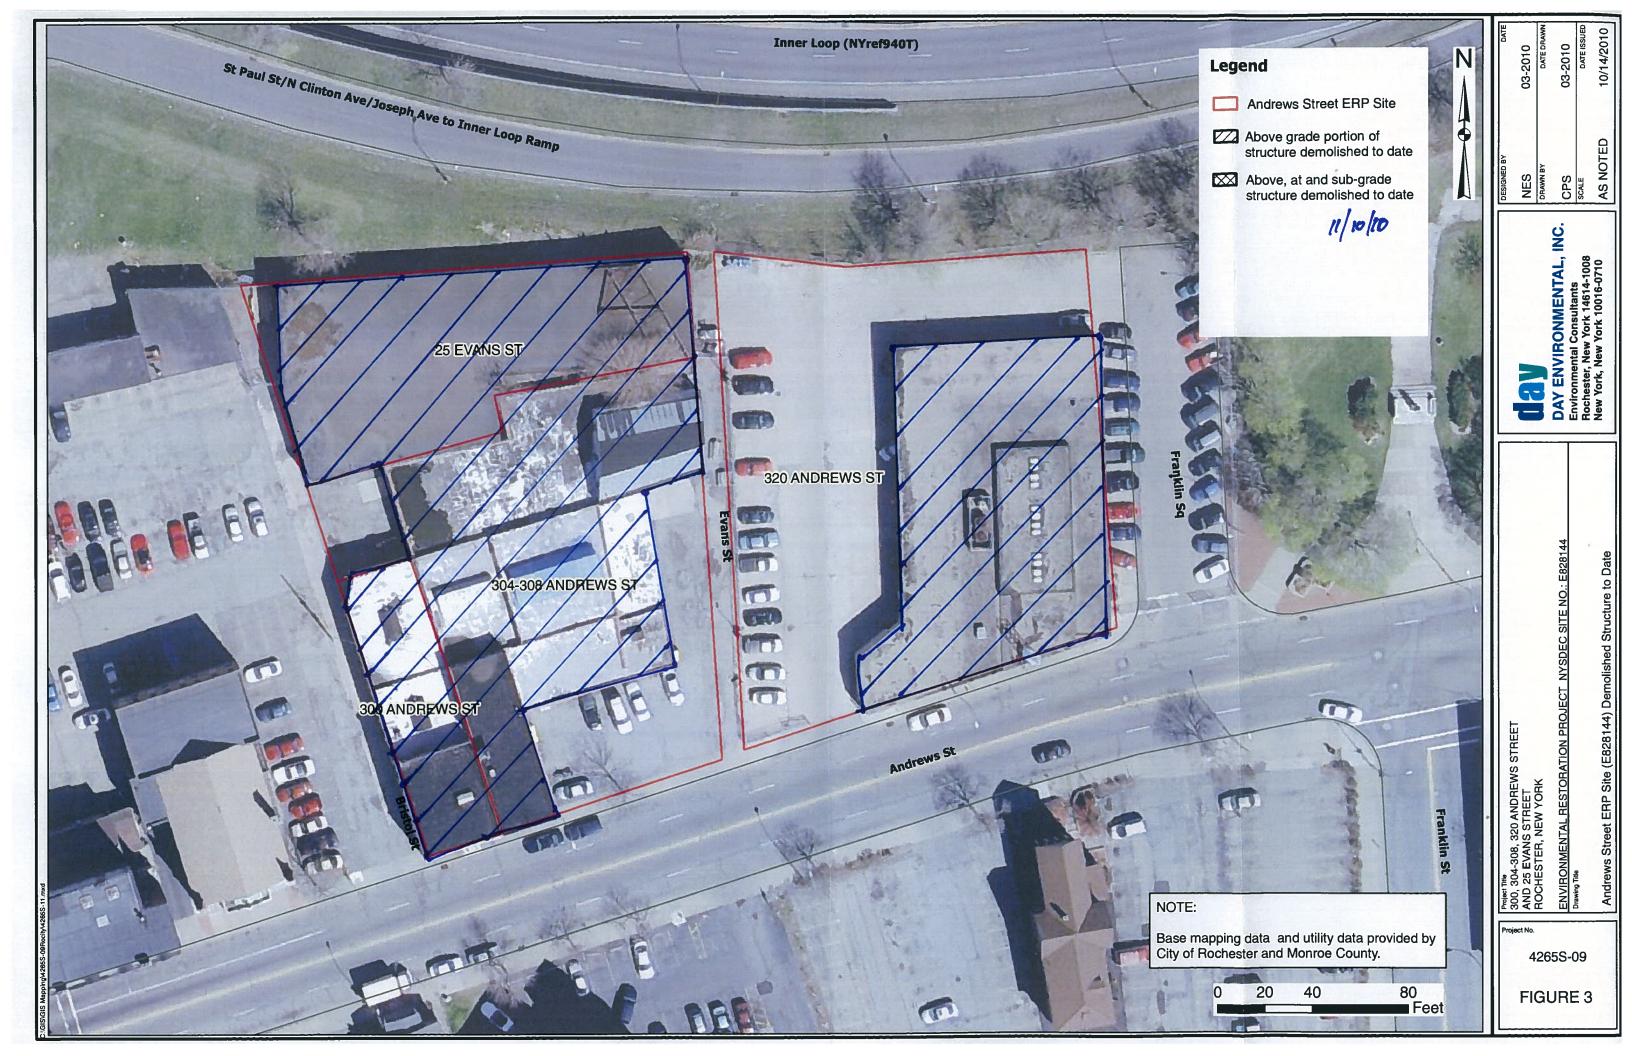

CC: "Joe Biondolillo" <biondj@cityofrochester.gov>, "Dennis Peck (City)" <de...

**Date:** 11/12/2010 9:06 AM

Subject: NYSDEC Site #E828144 - Andrews St 11/11/10 demolition progress

### Charlotte,

Due to the holiday, above grade demolition was not conducted on 11/11/10 at the 300, 304-308 and 320 Andrews Street and 25 Evans Street Site. At-grade and below grade demolition work is scheduled to begin on 11/15/10. DAY did locate select subsurface features via GPS technology in preparation for the upcoming at-grade and below grade demolition work.

Nate Simon, P.E. Day Environmental, Inc. 40 Commercial Street Rochester, New York 14614-1008 Phone: (585) 454-0210 ext:109

Fax: (585) 454-0825

**CC:** "Joe Biondolillo" <biondj@cityofrochester.gov>, "Dennis Peck (City)" <de...

**Date:** 11/15/2010 3:47 PM

**Subject:** NYSDEC Site #E828144 - Andrews St 11/12/10 through 11/15/10 demolition progress **Attachments:** Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-11-10 thorugh 11-15-10.pdf; 11-12-10 P 008.jpg; 11-12-10 P 001.jpg; 11-12-10 P 004.jpg; 11-15-10 P 010.jpg; 11-15-10 P 005.jpg

### Charlotte.

The above grade demolition continued on 11/12/10 and 11/13/10 at the 300, 304-308 and 320 Andrews Street and 25 Evans Street Site. Actives completed included site cleanup measures and the construction of the decon pad. Refer to the attached photos Figure 3.

At-grade and below grade demolition work was not conducted on 11/15/10 due to a leaking 6-inch diameter water main within the southern basement wall of the 304-308 Andrews Street building. In addition, a 3/4-inch service line within the southern basement wall of the 300 Andrews Street building is also leaking but at a much lower rate than the 6-inch water main. The water observed leaking into both 300 and 304-308 Andrews Street parcels is water from the municipal water system located in Andrews Street. Refer to the attached photos and Figure 3 for approximate locations of the 6-inch water main, the 3/4-inch service line and accumulated water within the basement of the 304-308 Andrews Street building. Following a discussion with Sean Keenan (753-7658) with the Monroe County Division of Pure Waters, it was determined that the accumulated water could be pumped from the basement to the combined sewer system without analytical laboratory testing results. Once the water lines have been addressed and are no longer leaking into the basements, the accumulated water will be discharged to the combined sewer system and the at-grade and below grade demolition work will begin at the 300 Andrews Street building. It is currently anticipated that the water main will be decommissioned on 11/16/10 and the at-grade and sub-grade demolition will begin on 11/16/10.

Accessible portions of the restricted area boundaries continue to be established in the field using spray paint. Please refer to the attached photos and Figure 3 for locations of the restricted area boundaries.

Nate Simon, P.E. Day Environmental, Inc. 40 Commercial Street Rochester, New York 14614-1008 Phone: (585) 454-0210 ext:109

Fax: (585) 454-0825

<<Figure 3, Andrews St NYSDEC Site # E828144, Demolition Progress 11-11-10 thorugh
11-15-10.pdf>> <<11-12-10 P 008.jpg>> <<11-12-10 P 001.jpg>> <<11-12-10 P 004.jpg>> <<11-15-10
P 010.jpg>> <<11-15-10 P 013.jpg>> <<11-12-10 P 005.jpg>>







