



Leak Detector			
Equipment #	Grade	Pump Type	Result
001/002	Regular	Mechanical (MLLD)	● Pass
003	Premium	Mechanical (MLLD)	● Pass

Overfill			
Equipment #	Grade	Overfill Type	Result
001	Regular	Audible External High-Level Alarm	● Pass
002	Regular	Audible External High-Level Alarm	● Pass
003	Premium	Audible External High-Level Alarm	● Pass

Precision Line Tightness Test		
Equipment #	Grade	Result
001/002	Regular	● Pass
003	Premium	● Pass

Shear Valve	
Form Name	Result
Shear Valve	● Pass

UST / AST Monitor	
Form Name	Result
UST / AST Monitor	● Pass

Justin LaComare

Justin LaComare

Dakota U

Dakota Uhler



Crompco LLC, an OWL Services Affiliated Company
1815 Gallagher Rd
Plymouth Meeting, PA 19462

7-Eleven Stores, Inc
Location #35078

40 Dennison Parkway
Corning, NY 14830
+1 607-962-4296

W-31995 Visit #33145 7/12/2023

Service Items

Item	Qty
Combos	
All Lines and Leak Detectors	2.00
Services	
Monitor System Inspection Automatic Tank Gauging System / Monitor System Inspection	1.00
All Shear Valves	2.00
Overfill Verification	1.00

APPENDIX C-9

MECHANICAL AND ELECTRONIC LINE LEAK DETECTORS PERFORMANCE TESTS

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc	
Address: 40 Dennison Parkway	Address:	
City, State, Zip Code: Corning NY 14830	City, State, Zip Code:	
Facility I.D. #: 8-390321	Phone #: 6079624296	
Testing Company: Crompco LLC	Phone #: 800-646-3161	Date: 7/12/2023

This data sheet can be used to test mechanical line leak detectors (MLLD) and electronic line leak detectors (ELLD) with submersible turbine pump (STP) systems. See PEI/RP1200 Sections 9.1 and 9.2 for test procedures.

Line Number	001/002	003				
Product Stored	Regular	Premium				
Leak Detector Manufacturer	RedJacket	RedJacket				
Leak Detector Model	FX1V	FX1V				
Type of Leak Detector	<input checked="" type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input checked="" type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input type="checkbox"/> MLLD <input type="checkbox"/> ELLD

MLLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)

STP Full Operating Pressure	25	32				
Check Valve Holding Pressure	20	32				
Line Resiliency (ml) (line bleed back volume as measured from check valve holding pressure to 0 psig)	26.5	22.71				
Step Through Time in Seconds (time the MLLD hesitates at metering pressure before going to full operating pressure as measured from 0 psig with no leak induced on the line)	1	1				
Metering Pressure (STP pressure when simulated leak rate 3 gph at 10 psig)	11	11				
Opening Time in Seconds (the time the MLLD opens to allow full pressure after simulated leak is stopped)	2	2				
Does the STP pressure remain at or below the metering pressure for at least 60 seconds when the simulated leak is induced?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Does the leak detector reset (trip) when the line pressure is bled off to zero psig?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Does the STP properly cycle on/off under normal fuel system operation conditions?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

A "No" answer to either of the above questions indicates the MLLD fails the test.

ELLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)

STP Full Operating Pressure						
How many test cycles are observed before alarm/shutdown occurs?						
Does the simulated leak cause an alarm?	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
A "No" answer to the above question indicates the ELLD fails the test.						
Does the simulated leak cause an STP shutdown?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA
Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail

Comments:

Tester's Name (print) Dakota Uhler Tester's Signature Dak U

APPENDIX C-6

**OVERFILL ALARM
OPERATION INSPECTION**

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc	
Address: 40 Dennison Parkway	Address:	
City, State, Zip Code: Corning NY 14830	City, State, Zip Code:	
Facility I.D. #: 8-390321	Phone #: 6079624296	
Testing Company: Crompco LLC	Phone #: 800-646-3161	Date: 7/12/2023

This procedure is to determine whether the high level alarm is operational and will trigger when the tank is no more than 90% full. See PEI/RP1200 Section 7.3 for the inspection procedure. This procedure is applicable to tank level monitor stems that touch the bottom of the tank when in place.

Tank Number	001	002	003	
Product Stored	Regular	Regular	Premium	
Tank Level Monitor Brand and Model	Veeder Root HLA	Veeder Root HLA	Veeder Root HLA	
1. Tank Volume, gallons	8000	8000	4000	
2. Tank Diameter, inches	92	92	92	
3. Overfill alarm activates in the test mode at the console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
4. When activated, overfill alarm can be heard or seen while delivering to the tank?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
5. After removing the probe from the tank, it has been inspected and any damaged or missing parts replaced?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
6. Float moves freely on the stem without binding?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
7. Moving product level float up the stem trigger alarm?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
8. Inch level from bottom of stem when 90% alarm is triggered.	77	77	77	
9. Tank volume at inch level in Line 8.	7200	7200	3600	
10. Calculate (Line 9 / Line 1) x 100	90	90	90	
11. Is Line 10 less than 90%?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
12. Fuel float level on the console agrees with the gauge stick reading?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
13. Overfill alarm activates at any product level above 90% tank capacity?	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

If any answers in Lines 3, 4, 5, 6, 7 or 11 are "No," or Line 13 is "Yes," the system has failed the test.

Test Results	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
---------------------	---	--	--	---

Comments:

Tester's Name (print) Dakota Uhler Tester's Signature *Dakota Uhler*

SHEAR VALVE OPERATION INSPECTION

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc
Address: 40 Dennison Parkway	Address
City, State, Zip Code: Corning NY 14830	City, State, Zip Code:
Facility I.D. #: 8-390321	Phone #: 6079624296
Testing Company: Crompco, LLC	Phone #: 610-278-7203

This data sheet is for inspecting shear valves located inside dispensers. See PEI/RP1200 Section 10 for the inspection procedure.

Product Grade	Premium	Regular	Premium	Regular					
Dispenser ID#	1/2	1/2	3/4	3/4					
Shear Valve Type (Product/Vapor)	Product	Product	Product	Product					
1. Is the shear valve rigidly anchored to the dispenser box frame or dispenser island?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
2. Is the shear section positioned between 1/2 inch above or below the top surface of the dispenser island?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
3. Is the lever arm free to move?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA
4. Does the lever arm snap shut the poppet valve?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA
5. Can any product be dispensed when the product shear valve is closed?	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA

A "No" to Lines 1-4 or a "Yes" for Line 5 indicates a test failure.

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
--------------	---	---	---	---	--	--	--	--	--

Comments:

Tester's Name (print) Dakota Uhler Tester's Signature *Dak U*

LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: 7-Eleven		Owner: 7-Eleven Stores, Inc	
Address: 40 Dennison Parkway		Address:	
City, State, Zip Code: Corning NY 14830		City, State, Zip Code:	
Facility I.D. #: 8-390321		Phone #: 6079624296	
Testing Company: Crompco LLC		Phone #: 800-646-3161	Date: 7/12/2023

This procedure is to determine whether liquid sensors located in the interstitial space of tank systems are able to detect the presence of water and fuel. See PEI/RP1200 Section 8.3 for the test procedure.

Sensor Location	001 STP Sump	002 Riser Sump	003 STP Sump				
Product Stored	Regular	Regular	Premium				
Type of Sensor	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating
Test Liquid	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product
Is the ATG console clear of any active or recurring warnings or alarms regarding the leak sensor? If the sensor is in alarm and functioning, indicate why.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Is the sensor alarm circuit operational?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Has sensor been inspected and in good operating condition?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When placed in the test liquid, does the sensor trigger an alarm?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When an alarm is triggered, is the sensor properly identified on the ATG console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

Any "No" answers indicates the sensor fails the test.

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
--------------	--	--	--	---	---	---	---

Comments:

Tester's Name (print) Dakota Uhler Tester's Signature *Dak U*

LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: 7-Eleven			Owner: 7-Eleven Stores, Inc				
Address: 40 Dennison Parkway			Address:				
City, State, Zip Code: Corning		NY	14830		City, State, Zip Code:		
Facility I.D. #: 8-390321			Phone #: 6079624296				
Testing Company: Crompco LLC			Phone #: 800-646-3161		Date: 7/12/2023		

This procedure is to determine whether liquid sensors located in the interstitial space of tank systems are able to detect the presence of water and fuel. See PEI/RP1200 Section 8.3 for the test procedure.

Sensor Location	Dispenser 1/2	Dispenser 3/4					
Product Stored	Regular, Plus, Super Premium	Regular, Plus, Super Premium					
Type of Sensor	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating
Test Liquid	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product
Is the ATG console clear of any active or recurring warnings or alarms regarding the leak sensor? If the sensor is in alarm and functioning, indicate why.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Is the sensor alarm circuit operational?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Has sensor been inspected and in good operating condition?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When placed in the test liquid, does the sensor trigger an alarm?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When an alarm is triggered, is the sensor properly identified on the ATG console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

Any "No" answers indicates the sensor fails the test.

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
---------------------	--	--	---	---	---	---	---

Comments:

Tester's Name (print) Dakota Uhler Tester's Signature *Dak U*

AUTOMATIC TANK GAUGE OPERATION INSPECTION

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc	
Address: 40 Dennison Parkway	Address:	
City, State, Zip Code: Corning NY 14830	City, State, Zip Code:	
Facility I.D. #: 8-390321	Phone #: 6079624296	
Testing Company: Crompco LLC	Phone #: 800-646-3161	Date: 7/12/2023

This procedure is to determine whether the automatic tank gauge (ATG) is operating properly. See PEI/RP1200 Section 8.2 for the inspection procedure. This procedure is applicable to tank level monitor stems that touch the bottom of the tank when in place.

Tank Number	001	002	003	
Product Stored	Regular	Regular	Premium	
ATG Brand and Model	Veeder Root TLS-350	Veeder Root TLS-350	Veeder Root TLS-350	
1. Tank Volume, gallons	8000	8000	4000	
2. Tank Diameter, inches	92	92	92	
3. After removing the ATG from the tank, it has been inspected and any damaged or missing parts replaced?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
4. Float moves freely on the stem without binding?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
5. Fuel float level agrees with the value programmed into the console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
6. Water float level agrees with the value programmed into the console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
7. Inch level from bottom of stem when 90% alarm is triggered.	77	77	77	
8. Inch level at which the overfill alarm activates corresponds with value programmed in the gauge?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
9. Inch level from the bottom when the water float first triggers an alarm.	1	1	1	
10. Inch level at which the water float alarm activates corresponds with value programmed in the gauge?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

If any answers in Lines 3, 4, 5, or 6 are "No," the system has failed the test.

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
---------------------	--	--	--	---

Comments:




Dakota Uhler



Tester's Name (print) _____ Tester's Signature _____



Diagram - Site Diagram (v10)

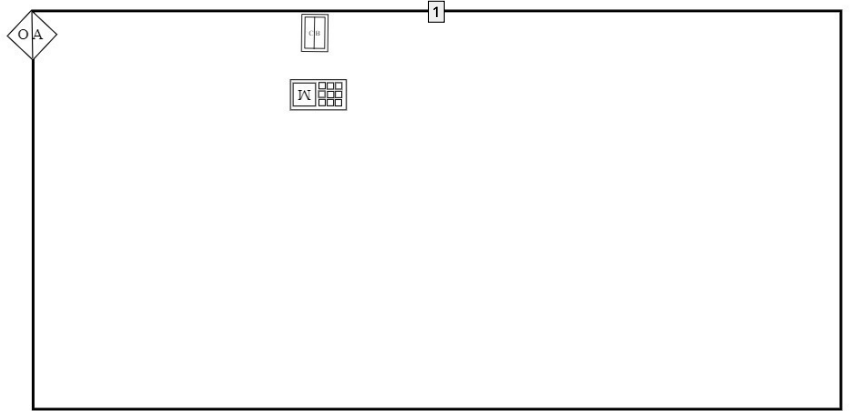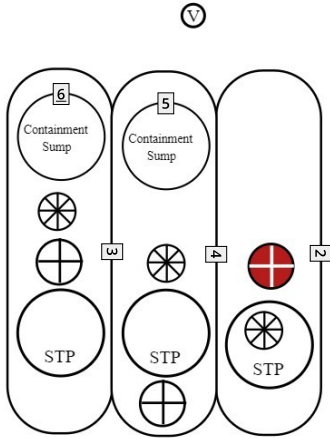

1: Rectangle - Store

2: Fiberglass Tank - Premium Tank

3: Fiberglass Tank - Regular Master Tank

4: Fiberglass Tank - Regular Siphon Tank

5: Containment Sump - Piping Sump

6: Containment Sump - Siphon Sump
