



Emergency Stop			
Equipment #	Location		Result
1	Under Counter		● Pass
2	Outside Wall of Building		
Leak Detector			
Equipment #	Grade	Pump Type	Result
007	Regular	Mechanical (MLLD)	● Pass
008	Diesel	Mechanical (MLLD)	● Pass
009	Premium	Mechanical (MLLD)	● Pass
Precision Line Tightness Test			
Equipment #	Grade		Result
007	Regular		● Pass
009	Premium		● Pass
008	Diesel		● Pass
Shear Valve			
Form Name			Result
Shear Valve			● Pass
UST / AST Monitor			
Form Name			Result
UST / AST Monitor			● Pass



Nicholas Christina



Seth Boesel

EMERGENCY STOP SWITCH OPERATION INSPECTION

Facility Name: 7-Eleven	35099	Owner: 7-Eleven Stores, Inc
Address: 51 Seneca Street		Address:
City, State, Zip Code: Hornell	NY	14843
City, State, Zip Code:		
Facility I.D. #: 8-495603		Phone #: 6073243757
Testing Company: Owl Services USA		Phone #: 610-278-7203
Date: 2/23/2026		

This procedure is to verify the operation of all emergency stop switches/buttons (E-stops). Each E-stop must disconnect power to dispensers, submersible turbine pumps (STPs) and all non-intrinsically safe electrical equipment in classified areas. Test each E-stop separately. See PEI/RP1200 Section 11 for the inspection procedure.

E-stop Number or ID	1	2				
Location	Under Counter	Outside Wall of Building				
1. E-stops labeled and located where easily accessible?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
2. System fully powered and in normal operating condition?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
3. After activating E-stop, power disconnected from:						
3a. All dispensing devices on all islands?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
3b. All STPs for all fuel grades?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
3c. All power, control and signal circuits associated with the dispensing devices and the STPs?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
3d. All other non-intrinsically safe electrical equipment in classified areas surrounding fuel dispensing devices?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
4. All intrinsically safe electrical equipment remains energized after E-stop activation?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
5. After testing, E-stop has been reset and power reestablished to normal operating condition?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
A "No" to lines 3a-3d indicates a test failure.						
Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	Pass <input type="checkbox"/> Fail	Pass <input type="checkbox"/> Fail	Pass <input type="checkbox"/> Fail	Pass <input type="checkbox"/> Fail

Comments:



Testing was conducted in accordance with PEI/RP1200

Seth Boesel



Tester's Name (print) _____ Tester's Signature _____

1 Under Counter

2 Outside Wall of Building

MECHANICAL AND ELECTRONIC LINE LEAK DETECTORS PERFORMANCE TESTS

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc	
Address: 51 Seneca Street	Address:	
City, State, Zip Code: Hornell NY 14843	City, State, Zip Code:	
Facility I.D. #: 8-495603	Phone #: 6073243757	
Testing Company: Owl Services USA	Phone #: 800-646-3161	Date: 2/23/2026

This data sheet can be used to test mechanical line leak detectors (MLLD) and electronic line leak detectors (ELLD) with submersible turbine pump (STP) systems. See PEI/RP1200 Sections 9.1 and 9.2 for test procedures.

Line Number	007	008	009			
Product Stored	Regular	Diesel	Premium			
Leak Detector Manufacturer	Veeder	Vaporless	Vaporless			
Leak Detector Model	FX1V	LD2000	LD2000			
Type of Leak Detector	<input checked="" type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input checked="" type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input checked="" type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input type="checkbox"/> MLLD <input type="checkbox"/> ELLD	<input type="checkbox"/> MLLD <input type="checkbox"/> ELLD

MLLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)

STP Full Operating Pressure	28	28	28			
Check Valve Holding Pressure	27	26	26			
Line Resiliency (ml) (line bleed back volume as measured from check valve holding pressure to 0 psig)	60.57	60.57	53			
Step Through Time in Seconds (time the MLLD hesitates at metering pressure before going to full operating pressure as measured from 0 psig with no leak induced on the line)	4	4	4			
Metering Pressure (STP pressure when simulated leak rate 3 gph at 10 psig)	14	14	14			
Opening Time in Seconds (the time the MLLD opens to allow full pressure after simulated leak is stopped)	4	4	4			
Does the STP pressure remain at or below the metering pressure for at least 60 seconds when the simulated leak is induced?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Does the leak detector reset (trip) when the line pressure is bled off to zero psig?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Does the STP properly cycle on/off under normal fuel system operation conditions?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

A "No" answer to either of the above questions indicates the MLLD fails the test.

ELLD (ALL PRESSURE MEASUREMENTS ARE MADE IN PSIG)

STP Full Operating Pressure						
How many test cycles are observed before alarm/shutdown occurs?						
Does the simulated leak cause an alarm?	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
A "No" answer to the above question indicates the ELLD fails the test.						
Does the simulated leak cause an STP shutdown?	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA
Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail

Comments: Testing was conducted in accordance with PEI/RP1200

Tester Signature: 

Tester Name: Seth Boesel

7-Eleven
 51 Seneca Street
 Hornell
 NY 14843

Purpora Engineering
 Petro-Tite Line Tightness Test Form

Work Visit # 162996
 UST Registration #
 8-495603

IDENTIFY EACH LINE AS TESTED	TIME (MILITARY)	LOG OF TEST PROCEDURES, AMBIENT TEMPERATURE, WEATHER, ETC.	PRESSURE		VOLUME			REMARKS
			PSI		READING		NET CHANGE	SIZE, LENGTH & TYPE OF LINE, #FLEX CONNECTORS, CONCLUSIONS
			BEFORE	AFTER	BEFORE	AFTER		
007	11:30	Connected line tester to: Shear						Material <u>Fiberglass</u> Wall Type <u>Double</u> Line Length (feet) <u>100</u> Diameter (inches) <u>2</u> Pressure/Suction <u>Pressure</u> Allowable Bleedback $(PL \times Ba) + (FC \times Bb(.006)) + B(.05) = N$ $(100 * 0) + (3 * 0.006) + 0.05 = 0.068$
Regular	11:45	Started line test		60		.05		
	12:00	Line Test Continued	60	60	.05	.05	0	
	12:15	Line Test Continued	60	60	.05	.05	0	
	12:30	Line Test Continued	60	60	.05	.05	0	
	12:45	Bleed Back	60	0	.05	.1	0.05	

Tests were made on the above line systems in accordance with test procedures prescribed for as detailed on attached test charts with the results as follows:

Line Identification	Meets Criteria (Yes/No)	Net Volume Change Per Hour	Date Tested
007 Regular	Yes	0	2/23/2026

CONTRACTOR CERTIFICATION

Technician:
 Seth Boesel

ab32a810

Certification # _____

Notes:

7-Eleven
 51 Seneca Street
 Hornell
 NY 14843

Purpora Engineering
 Petro-Tite Line Tightness Test Form

Work Visit # 162996
 UST Registration #
 8-495603

IDENTIFY EACH LINE AS TESTED	TIME (MILITARY)	LOG OF TEST PROCEDURES, AMBIENT TEMPERATURE, WEATHER, ETC.	PRESSURE		VOLUME			REMARKS
			PSI		READING		NET CHANGE	SIZE, LENGTH & TYPE OF LINE, #FLEX CONNECTORS, CONCLUSIONS
			BEFORE	AFTER	BEFORE	AFTER		
009	11:16	Connected line tester to: Shear						Material <u>Fiberglass</u> Wall Type <u>Double</u> Line Length (feet) <u>100</u> Diameter (inches) <u>2</u> Pressure/Suction <u>Pressure</u> Allowable Bleedback $(PL \times Ba) + (FC \times Bb(.006)) + B(.05) = N$ $(100 * 0) + (3 * 0.006) + 0.05 = 0.068$
Premium	11:31	Started line test		60		.05		
	11:46	Line Test Continued	60	60	.05	.05	0	
	12:01	Line Test Continued	60	60	.05	.05	0	
	12:16	Line Test Continued	60	60	.05	.05	0	
	12:17	Bleed Back	60	0	.05	.1	0.05	

Tests were made on the above line systems in accordance with test procedures prescribed for as detailed on attached test charts with the results as follows:

Line Identification	Meets Criteria (Yes/No)	Net Volume Change Per Hour	Date Tested
009 Premium	Yes	0	2/23/2026

CONTRACTOR CERTIFICATION

Technician:

Seth Boesel

ab32a810

Certification # _____

Notes:

SHEAR VALVE OPERATION INSPECTION

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc
Address: 51 Seneca Street	Address
City, State, Zip Code: Hornell NY 14843	City, State, Zip Code:
Facility I.D. #: 8-495603	Phone #: 6073243757
Testing Company: Owl Services USA	Phone #: 610-278-7203

This data sheet is for inspecting shear valves located inside dispensers. See PEI/RP1200 Section 10 for the inspection procedure.

Product Grade	Premium	Regular	Diesel	Premium	Regular	Kerosene			
Dispenser ID#	1/2	1/2	3/4	3/4	3/4	5			
Shear Valve Type (Product/Vapor)	Product	Product	Product	Product	Product	Product			
1. Is the shear valve rigidly anchored to the dispenser box frame or dispenser island?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
2. Is the shear section positioned between 1/2 inch above or below the top surface of the dispenser island?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
3. Is the lever arm free to move?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA
4. Does the lever arm snap shut the poppet valve?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA
5. Can any product be dispensed when the product shear valve is closed?	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA	<input type="checkbox"/> Yes <input type="checkbox"/> No <input type="checkbox"/> NA

A "No" to Lines 1-4 or a "Yes" for Line 5 indicates a test failure.

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
--------------	---	---	---	---	---	---	--	--	--

Comments:

Tester's Name (print) Seth Boesel Tester's Signature  2/23/2026

Testing was conducted in accordance with PEI/RP1200

**AUTOMATIC TANK GAUGE
OPERATION INSPECTION**

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc		
Address: 51 Seneca Street	Address:		
City, State, Zip Code: Hornell NY 14843	City, State, Zip Code:		
Facility I.D. #: 8-495603	Phone #: 6073243757		
Testing Company: Owl Services USA	Phone #: 800-646-3161	Date: 2/23/2026	

This procedure is to determine whether the automatic tank gauge (ATG) is operating properly. See PEI/RP1200 Section 8.2 for the inspection procedure. This procedure is applicable to tank level monitor probes that touch the bottom of the tank when in place.

Tank Number	007	008	009	010
Product Stored	Regular	Diesel	Premium	Kerosene
ATG Brand and Model	Veeder Root TLS-450 Plus	Veeder Root TLS-450 Plus	Veeder Root TLS-450 Plus	Veeder Root TLS-450 Plus
1. Tank Volume, gallons	8000	8000	4000	1000
2. Tank Diameter, inches	96	96	64	48
3. The ATG probe was removed from the tank and inspected for damage and residual buildup.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
4. Float moves freely on the stem without binding?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
5. Fuel float level agrees with the value programmed into the console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
6. Water float level agrees with the value programmed into the console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
7. Inch level from bottom of probe when 90% alarm is triggered.	86	86	56	38
8. Inch level at which the overfill alarm activates corresponds with value programmed in the gauge?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
9. Inch level from the bottom when the water float first triggers an alarm.	2	2	2	2
10. Inch level at which the water float alarm activates corresponds with value programmed in the gauge?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No

If any answers in Lines 3, 4, 5, or 6 are "No," the system has failed the test.

If internal ATG battery backup is present, was it functional per manufacturer's specifications. Yes No None

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail
---------------------	--	--	--	--

Comments:

Tester's Name (print) Seth Boesel

Tester's Signature



LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: 7-Eleven		Owner: 7-Eleven Stores, Inc	
Address: 51 Seneca Street		Address:	
City, State, Zip Code: Hornell NY 14843		City, State, Zip Code:	
Facility I.D. #: 8-495603		Phone #: 6073243757	
Testing Company: Owl Services USA		Phone #: 800-646-3161	Date: 2/23/2026

This procedure is to determine whether liquid sensors located in the interstitial space of UST systems are able to detect the presence of water and fuel. See PEI/ RP1200 Section 8.3 for the test procedure.

Sensor Location	007 STP Sump	008 STP Sump	009 STP Sump	010 STP Sump			
Product Stored	Regular	Diesel	Premium	Kerosene			
Type of Sensor	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating
Test Liquid	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product
Is the ATG console clear of any active alarms regarding any leak sensors? If the sensor is in alarm and functioning, indicate why.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Is the sensor alarm circuit operational?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Has sensor been inspected and in good operating condition?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When placed in the test liquid, does the sensor trigger an alarm?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When an alarm is triggered, is the sensor properly identified on the ATG console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

Any "No" answers indicates a test failure.

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
---------------------	--	--	--	--	---	---	---

Comments:

Tester's Name (print) Seth Boesel Tester's Signature 

LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: 7-Eleven		Owner: 7-Eleven Stores, Inc	
Address: 51 Seneca Street		Address:	
City, State, Zip Code: Hornell NY 14843		City, State, Zip Code:	
Facility I.D. #: 8-495603		Phone #: 6073243757	
Testing Company: Owl Services USA		Phone #: 800-646-3161	Date: 2/23/2026

This procedure is to determine whether liquid sensors located in the interstitial space of UST systems are able to detect the presence of water and fuel. See PEI/ RP1200 Section 8.3 for the test procedure.

Sensor Location	007 Tank Interstitial	008 Tank Interstitial	009 Tank Interstitial	010 Tank Interstitial			
Product Stored	Regular	Diesel	Premium	Kerosene			
Type of Sensor	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating
Test Liquid	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product
Is the ATG console clear of any active alarms regarding any leak sensors? If the sensor is in alarm and functioning, indicate why.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Is the sensor alarm circuit operational?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Has sensor been inspected and in good operating condition?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When placed in the test liquid, does the sensor trigger an alarm?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When an alarm is triggered, is the sensor properly identified on the ATG console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

Any "No" answers indicates a test failure.

Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
---------------------	--	--	--	--	---	---	---

Comments:

Tester's Name (print) Seth Boesel Tester's Signature 

LIQUID SENSOR FUNCTIONALITY TESTING

Facility Name: 7-Eleven	Owner: 7-Eleven Stores, Inc	
Address: 51 Seneca Street	Address:	
City, State, Zip Code: Hornell NY 14843	City, State, Zip Code:	
Facility I.D. #: 8-495603	Phone #: 6073243757	
Testing Company: Owl Services USA	Phone #: 800-646-3161	Date: 2/23/2026

This procedure is to determine whether liquid sensors located in the interstitial space of UST systems are able to detect the presence of water and fuel. See PEI/ RP1200 Section 8.3 for the test procedure.

Sensor Location	Dispenser 1/2	Dispenser 3/4	Dispenser 5				
Product Stored	Regular, Plus, Premium	Regular, Plus, Premium, Diesel	Kerosene				
Type of Sensor	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input checked="" type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating	<input type="checkbox"/> Discriminating <input type="checkbox"/> Non-discriminating
Test Liquid	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input checked="" type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product	<input type="checkbox"/> Water <input type="checkbox"/> Product
Is the ATG console clear of any active alarms regarding any leak sensors? If the sensor is in alarm and functioning, indicate why.	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Is the sensor alarm circuit operational?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Has sensor been inspected and in good operating condition?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When placed in the test liquid, does the sensor trigger an alarm?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
When an alarm is triggered, is the sensor properly identified on the ATG console?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No

Any "No" answers indicates a test failure.



Test Results	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail
---------------------	--	--	--	---	---	---	---

Comments:

Tester's Name (print) Seth Boesel Tester's Signature 



Diagram - Site Diagram (v1)

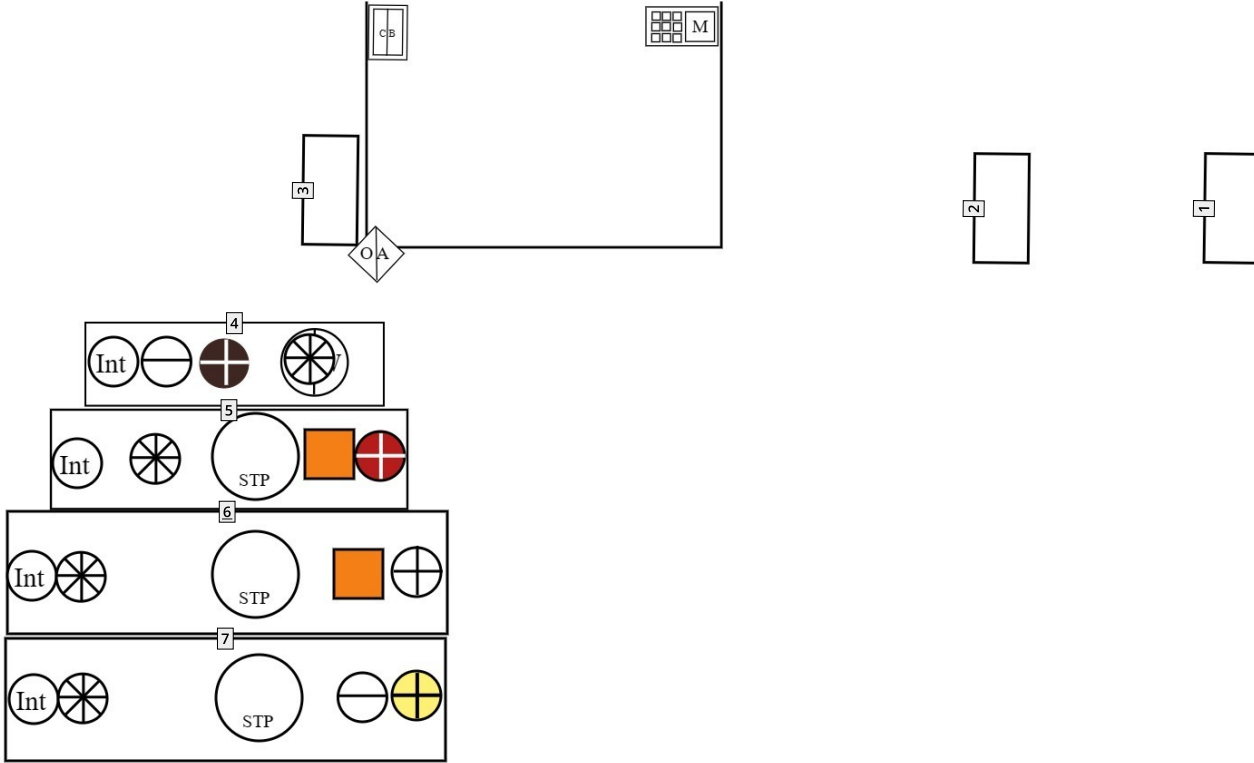

1: Dispenser - 3/4 w/ diesel

2: Dispenser - 1/2

3: Dispenser - 5 Kero

4: Steel Tank - kero

5: Steel Tank - Prem

6: Steel Tank - Reg

7: Steel Tank - Diesel



Visit Verification

CUSTOMER
 7-Eleven Stores, Inc

LOCATION
 #35099
 51 Seneca Street
 Hornell, NY 14843

CONTACT
 7-Eleven Stores, Inc

SCHEDULED
 02/23/2026 12:00am (EST)

ASSIGNED TO
 Nicholas Christina, Seth Boesel

SERVICE REASON
 Compliance

PRODUCTS & SERVICES

Item	Qty
Combos	
All Lines and Leak Detectors	3.00
Services	
Monitor System Inspection Automatic Tank Gauging System / Monitor System Inspection	1.00
All Shear Valves	3.00
Emergency Stop Inspection	1.00

CONFIRMATION

By signing this verification you are agreeing that we have performed and/or provided services and parts listed above.

Approver's Name
 Jeh

Email

Signature Status
 Captured
