

Steven Scharf - FW: NGC - OU3 RI - Progress Report for 6/1 to 6/10/05

From: "Stern, David" <DStern@arcadis-us.com>
To: "Steven Scharf" <sxscharf@gw.dec.state.ny.us>
Date: 6/20/2005 2:04 PM
Subject: FW: NGC - OU3 RI - Progress Report for 6/1 to 6/10/05
CC: "Cofman, John" <john.cofman@ngc.com>, "Leskovjan, Larry" <larry.leskovja...>
Attachments: ON-SITE VP LOCATIONS.pdf

Steve:

Attached is a summary of the work performed Week 2 (6/13 to 6/17) and plans for Week 3 (6-20 to 6-24). If you approve, we will issue this report to NYSDEC.

WORK COMPLETED (6/13 TO 6/17):

- Two drill rigs (Failing F-7) used to drill vertical profile borings (VPBs) on the Park property. 10T rig used as third crew for VPB groundwater sampling.
- John Corral (operations leader per Site Operations Plan), Melissa Saurborn, and Jennifer Cherlin are designated on-site field representatives.
- Received NYSDEC written approval of Addendum 1 to Phase 1B RI Work Plan for VP-27 and VP-28. Provided copy of plan and correspondences to Town per Site Access Agreement.
- Performed utility markout (geophysics and NYS One-Call) and cleared new VP-27 and VP-28 locations per Addendum 1 to Phase 1B RI Work Plan.
- Drilled and gamma logged VP-22, VP-23, VP-27, VP-28, VP-29 and VP-30. VP-27 had to be re-drilled due to field conditions, scheduled for Week 3.
- Groundwater sampling of VP-22, VP-23, VP-24, and VP-25.
- Received approval from Town to extend work hours from 7:30 AM to 5 PM Mon-Fri.

WORK PLANNED (6-20 to 6-24):

- Adjust proposed total depths of VPBs VP-31, and VP-32 based on nearby VOC concentration data.
- Drill and gamma log VP-27, VP-31, and VP-32.
- Groundwater sampling of VP-27, VP-28, VP-29, VP-31, and VP-32.
- Demobilize all rigs back to staging area at 5PM on 6/23.
- Restoration of our drilling locations, including borehole grouting, levelling off of ruts or depressions, repairs to asphalt and concrete, or reseeding. Site walk to remove deleterious debris related to our activities.
- Field check drilling locations for Phase 2 (Off-Site) RI.
- Prepare Phase 2 (Off-Site) RI Work Plan for vertical profile borings for NGC and NYSDEC review and approval.
- Tentative site walk with NYSDEC, NGC to off-site VPB locations on 6/22.
- Prepare Site Operations Plan for Phase 2 (Off-Site) RI.


Attached is updated site plan with VPB IDs, as they have changed per addition of VP-27 and 28.

David E. Stern, LEP
Senior Scientist
ARCADIS

88 Duryea Road
Melville, NY 11747
Tel. (631) 391-5284
Fax. (631) 249-7610
Email: <<mailto:dstern@arcadis-us.com>>
<<http://www.arcadis-us.com/>>

NOTICE OF CONFIDENTIALITY

The information contained in this e-mail message is intended only for the personal and confidential use of the recipient(s) named above. This message may be an attorney -client communication, and as such, is privileged and confidential. If the reader of this message is not the intended recipient or an agent responsible for delivering it to the intended recipient, you are hereby notified that you have received this document in error and that any review, dissemination, distribution, or copying of this message is strictly prohibited. If you have received this communication in error, please notify us immediately by e-mail, and delete the original message.

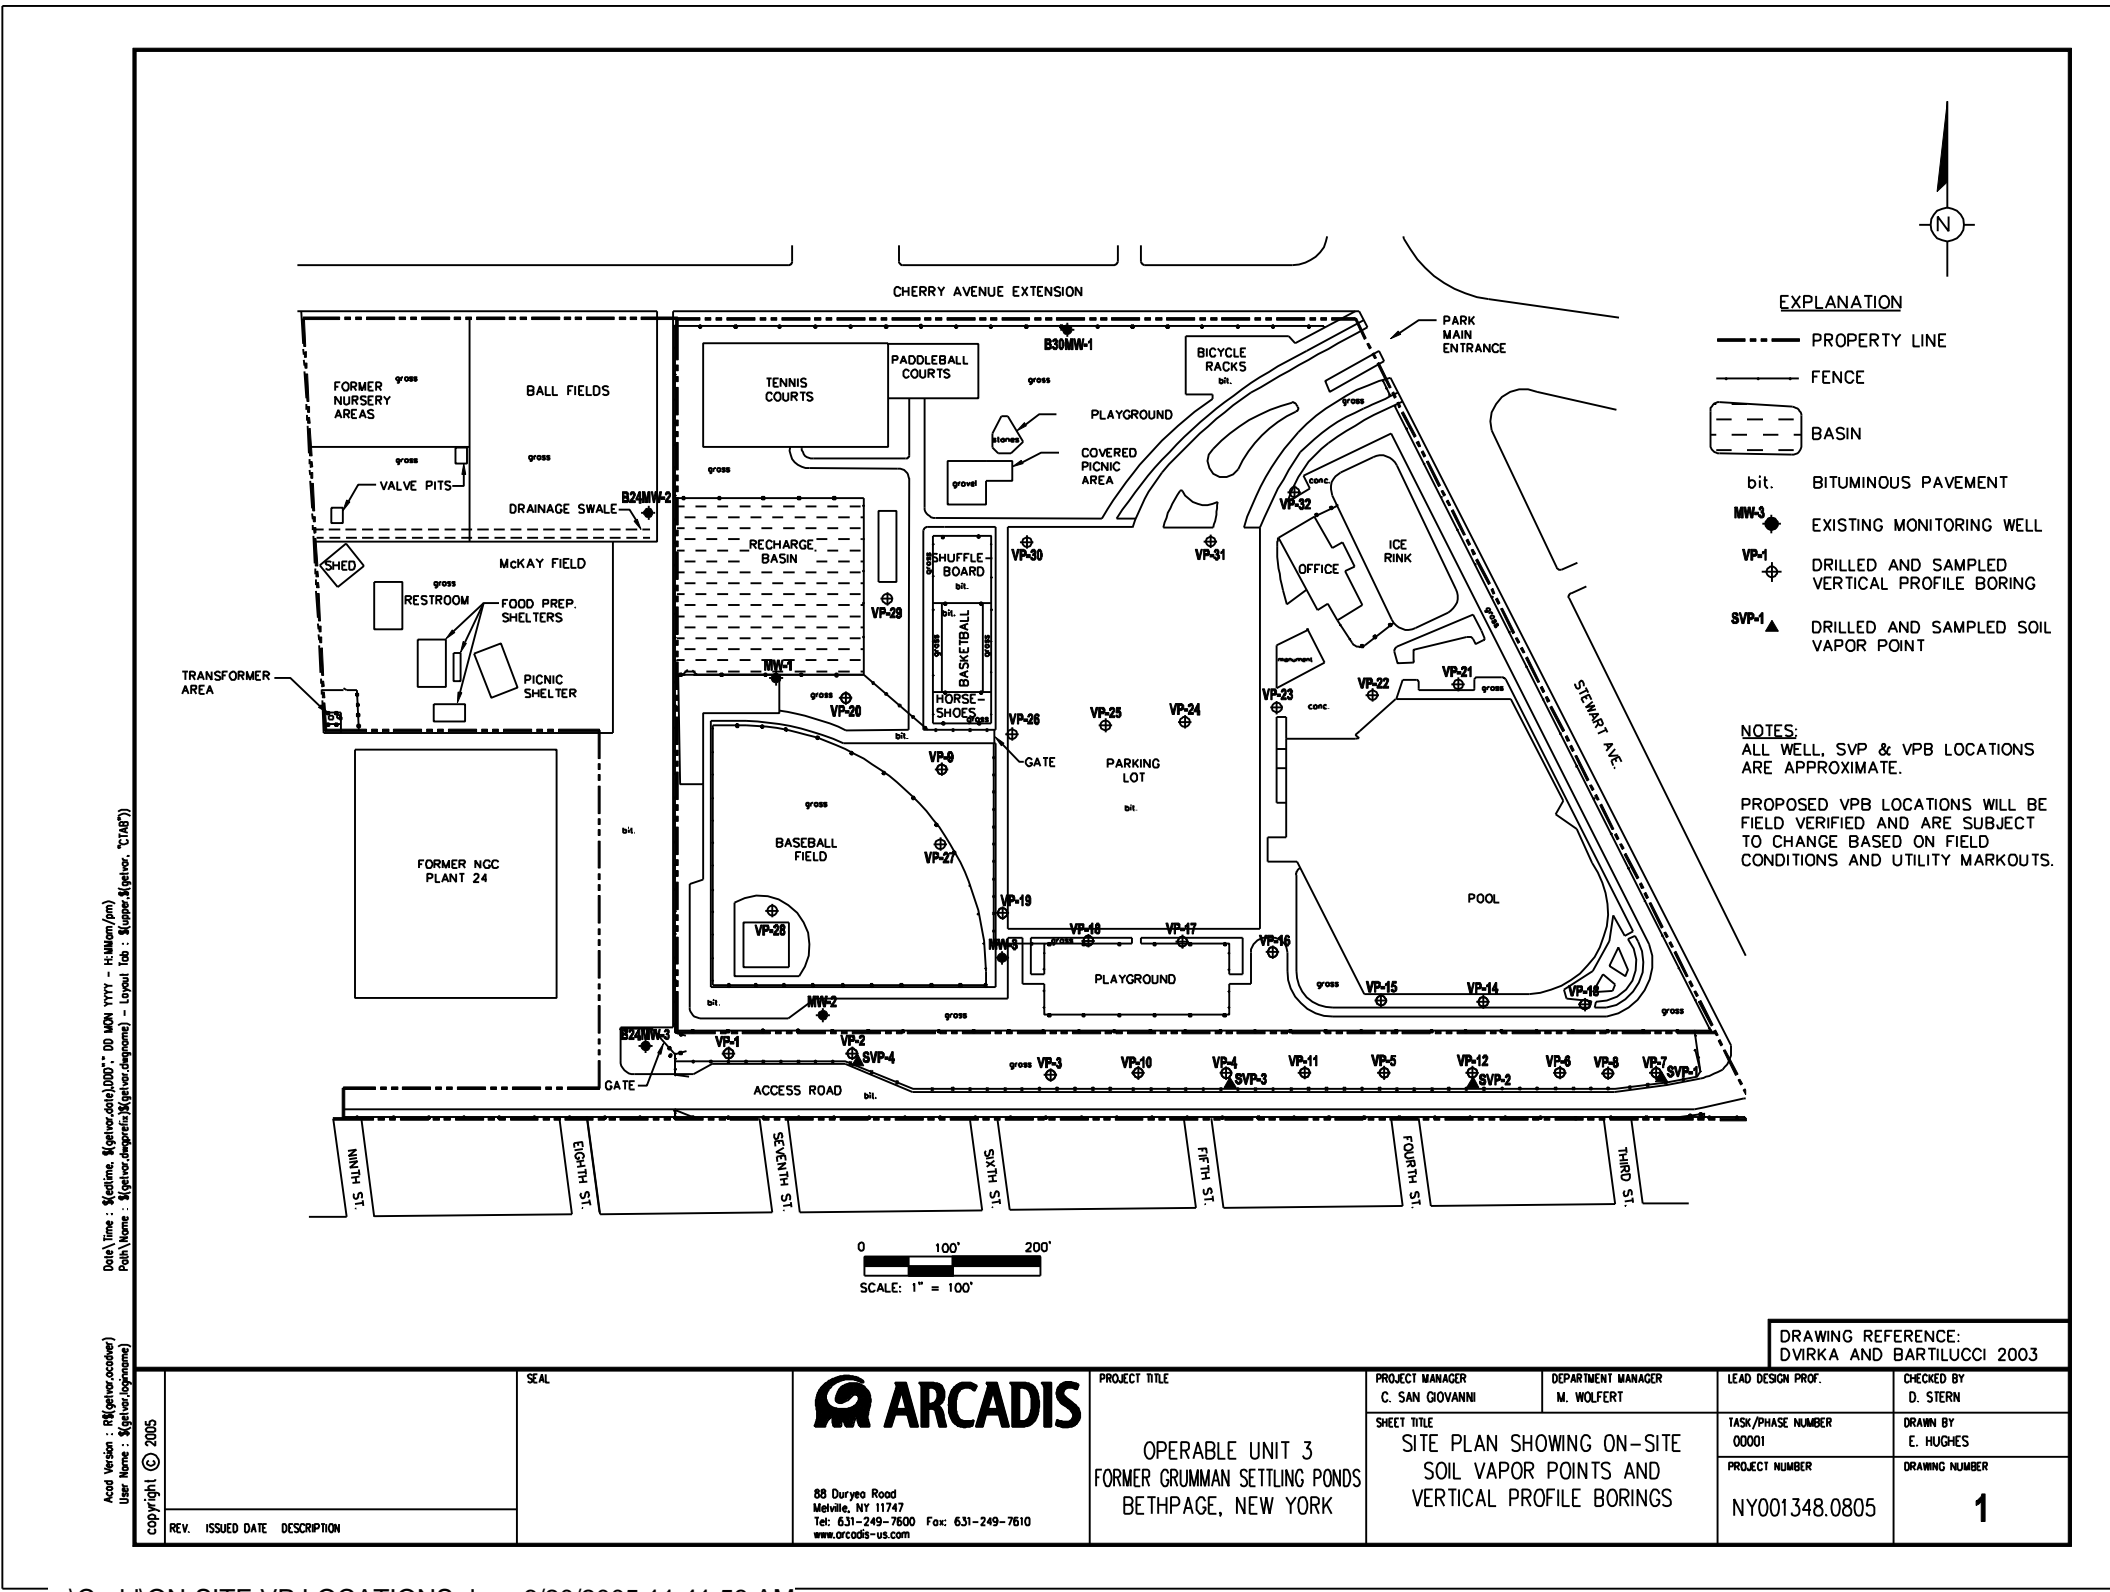

...Cadd\ON-SITE VP LOCATIONS.dwg 6/20/2005 11:41:58 AM
