



DAILY STATUS REPORT

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 14, 2023
WEATHER:	Temp: 36 – 38°F Snow/ Rain, RH: 86% Pressure: 29.54" Hg Wind: W @ 15 mph
TIME:	07:00 – 15:30

Project Team

General Contractor and Subcontractors:

- Mega Contracting Group, LLC
- Creamer Environmental, Inc. (CEI)

Engineers and Consultants:

- Roux Environmental Engineering and Geology, D.P.C.
- GZA GeoEnvironmental, Inc.

Remedial Action Work Summary

Work Activities Performed Onsite:

- Pre-trenching in preparation of installation of steel sheeting associated with support of excavation (SOE) around the former Gas Holder 4.

Contractor Work Performed Onsite:

Creamer Environmental, Inc (CEI) pre-trenched 90 linear feet along the north side of the former Gas Holder 4, adjacent to Degraw Street. CEI removed and stockpiled the former concrete building slab and sidewalk. Scrap metal and other construction debris that could have obstructed steel sheeting installation was also removed and stockpiled for future disposal. Excavated soil was placed back in the trenched area and covered with plastic liner at the end of the day. CEI conducted dust control measurements (wetting, tarping, limiting vehicle speeds, etc.) to ensure dust and odors were not impacted the neighborhood. No work was conducted inside the tension fabric structure (TFS) and the vapor managements system (VMS) was not operated.

Air Monitoring:

- No community air monitoring program (CAMP) exceedances were observed during the day.
- GZA GeoEnvironmental Inc. will provide a summary report for CAMP activities.

Erosion and Sediment Control

- Erosion and sediment controls were inspected to ensure that silt fence and filter sock were undamaged and operational.

Sampling Conducted:

- None.

Other Items of Note:

- None

Imported Material

Name - Location	Source	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
Vulcan ASTM #3 (1 ½" Stone)	Vulcan Hamburg Quarry		26.03	7	179.3
Vulcan General Fill	Vulcan Wantage Quarry		231.12	95	2417.38

**DAILY STATUS REPORT**

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 14, 2023
WEATHER:	Temp: 36 – 38°F Snow/ Rain, RH: 86% Pressure: 29.54" Hg Wind: W @ 15 mph
TIME:	07:00 – 15:30

Exported Material

Material	Facility	During This Reporting Period		Total	
		Loads	Tons	Loads	Tons
Concrete for Recycling	Bayshore			20	421.87
Concrete for Landfill	WM Fairless			37	~872.59
TCE Impacted Haz Hot Spot	CWM Emelle			7	161.72
Cd Impacted Haz Material from WC-5	CWM Emelle			3	49.45
Cd Impacted Haz Material from WC-5	Clean Earth NJ			16	397.75
Non-Haz Contaminated Urban Fill	WM Fairless			99	~2,090
MGP soil with TCE>25 ppm	Clean Earth ESMI			112	~2,472

Exported Material Truck Log

Number	Excavation Grid	Disposal Facility	Disposal Profile	Manifest Number	Trucking Company	Truck License Plate

Dewatering


Time	Totalizer Volume (gallons)*
7:10 AM	2,364,306
15:01 PM	2,364,306
Water treated and discharged since last report:	0 gallons

Anticipated Upcoming Work Activities

Pre-trenching around former Gas Holder 4 to remove obstructions for upcoming installing steel sheeting for support of excavation


PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 14, 2023
WEATHER:	Temp: 36 – 38°F Snow/ Rain, RH: 86% Pressure: 29.54" Hg Wind: W @ 15 mph
TIME:	07:00 – 15:30

Site Layout

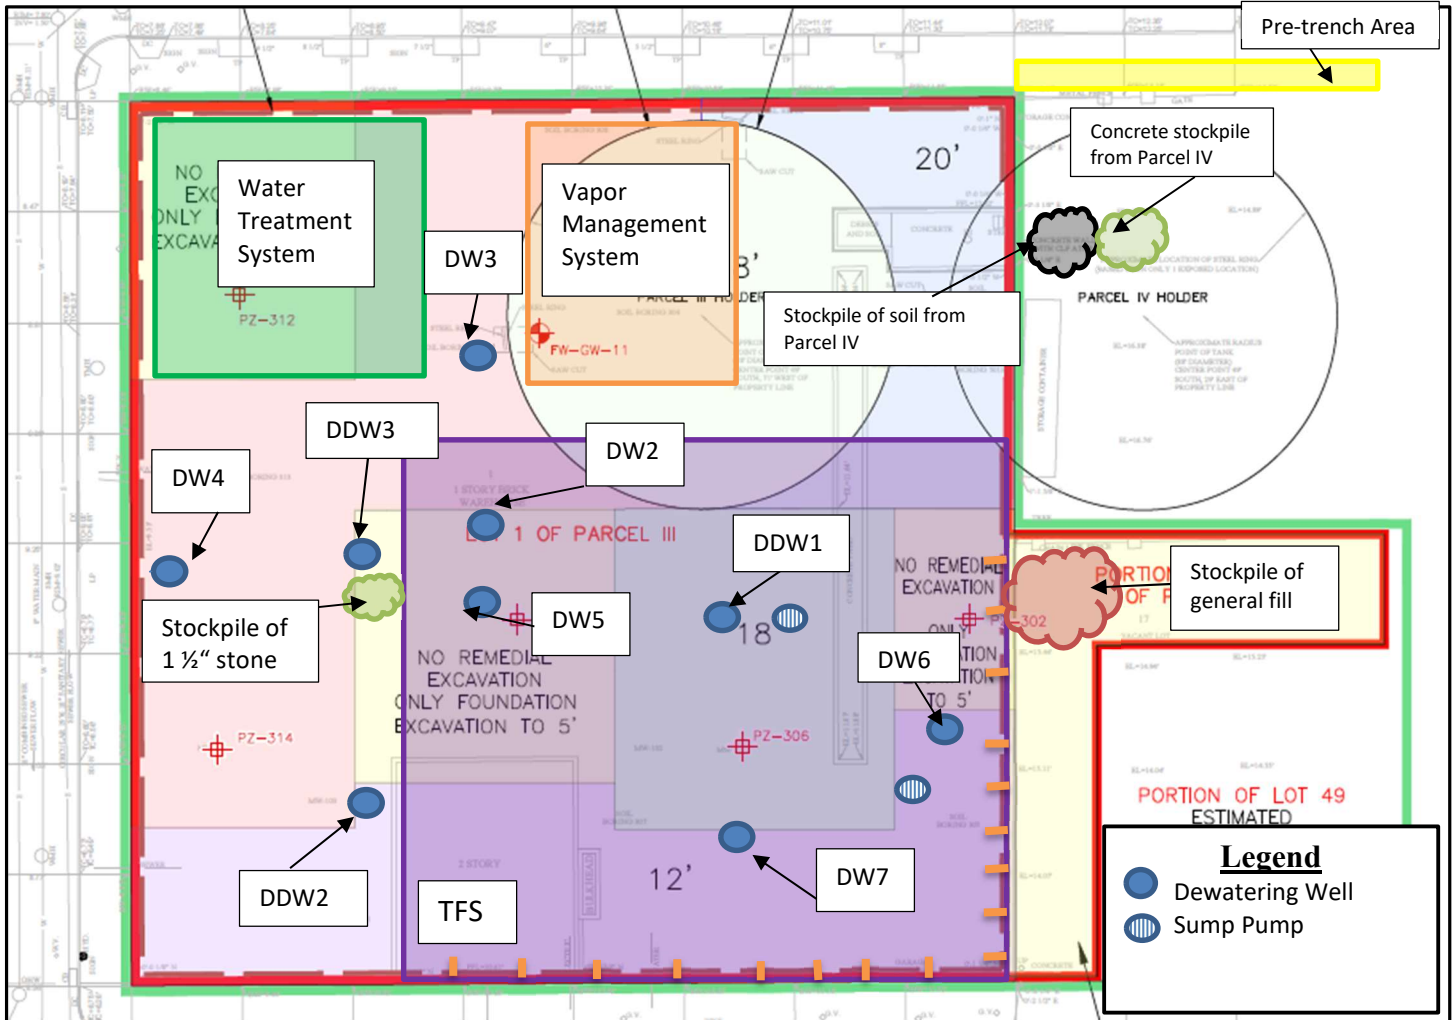

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 14, 2023
WEATHER:	Temp: 36 – 38°F Snow/ Rain, RH: 86% Pressure: 29.54" Hg Wind: W @ 15 mph
TIME:	07:00 – 15:30

Excavation Diagram

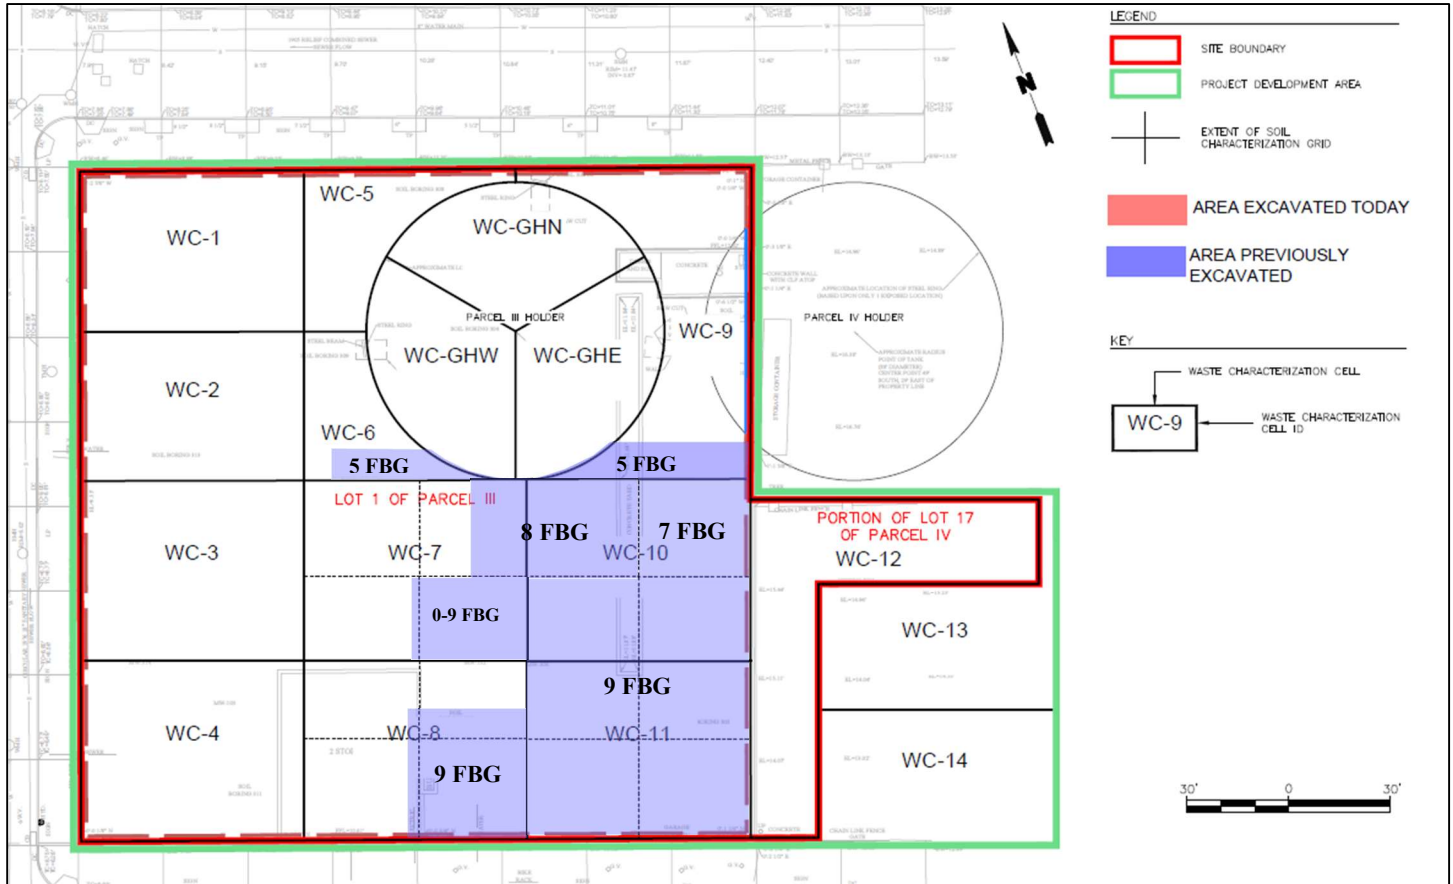

PROJECT:	Former Fulton MGP – Parcels III and IV (Site No.: 224051)
ADDRESS:	545 Sackett St., Brooklyn, NY
PREPARED BY:	Roux Environmental Engineering and Geology, D.P.C.
DATE:	March 14, 2023
WEATHER:	Temp: 36 – 38°F Snow/ Rain, RH: 86% Pressure: 29.54" Hg Wind: W @ 15 mph
TIME:	07:00 – 15:30

Photographs of Onsite Work

**Photo 1:**

CEI pre-trenching along the north side wall of former Gas Holder 4, adjacent to Degraw Street.

**Photo 2:**

Exposed soil after pre-trenching activities was covered with plastic sheeting at the end of the day.
